END OF WELL REPORT

AZADEGAN OIL FIELD

END OF WELL REPORT

AZNS – 166 (PAD #09),

KAZHDUMI WELL

Drilling Department

MAY 2026

MSA/OEOC			
	Position	**Name**	**Date & Signature**
Prepared by	Drilling Engineering Department	M.H. Haji Taleb Asgar Eyvazi	
Approved by	Project Head of Drilling Engineering	Behnam Parvaresh	
	Project Head of Drilling Operation	Piran Farzaneh	
	Project Manager	Rashid Ansari	
PPL			
	Position	**Name**	**Date & Signature**
Check & Approved by	Drilling Operation Manager	Majid Nariman	
	Subsurface Engineering Manager	Mehdi Salim Mehr	
	Head of Drilling Enginnering	Soheil Shadizadeh	
	Subsurface Project Manager	Keivan Davoodi Nejad	

TABLE OF CONTENTS

1. General Information *7*
1.1 Field Introduction 7
1.2 AZNS – 166 Well Location Map 9
2. Well History *10*
2.1 Well Informaion 10
2.2 AZNS-166 Well History 11
Drilling History 11
Operation after Completion History 12
2.3 Casing & Liner Depth 13
2.4 Summary of Workover Operation 14
Workover Summary: 14
De-Completion: 14
Completion Operation Summary: 18
2.5 AZNS-166 Well Sketch 23
2.6 Daily Time Break Down 24
2.7 Activity Breakdown Table 27
2.8 Activity Break Down Chart 30
2.9 Activity Break Down Plot 31
2.10 Bit Record Table 32
2.11 Hole Problem History 33
2.12 NPT Break-Down 34
3. Geological & Logging Reports *36*
4. Bottom Hole Assembly Record *37*
5. Casing Information *39*
.6 Cement Job Report *40*
7. Completion Report *41*
7.1 Completion Tubing Information 41
7.2 Completion Tools Specification Checklist 42
7.3 Assembling Test Report 45
7.4 Completion Operation Checklist 57
7.5 Well Head and X-mass tree Specification (installed) 61
7.6 Completion Sketch & Tally 63
7.7 Completion Tally: 64
7.8 Completion String Pressure Test 71
8. Wellhead Report *73*
8.1 Final Well Status 73
8.2 Wellhead & X-mass tree Specification 74
8.3 Wellhead Schematic 76
8.4 X-mass Tree Specification (Section D) 77
8.5 X-mass Tree Pressure Test Report (Section D – befor install) 78

8.6 X-mass Tree Pressure Test Report (Section D – after install) 79
8.7 Wellhead Related Test Reports 80
9. Drilling Fluid Information 84
9.1 Interval Remark 85
Operation Remark 85
Drilling Fluid Remark 85
9.2 Drilling Fluid type 86
9.3 Material Consumption Analysis 87
9.4 Volume Analysis 89
9.5 Daily volume Breakdown 90
9.6 Loss Distribution 92
9.7 Interval Fluid Properties Recap 94
9.8 Solid Control Disscusion 95
9.9 Inhibited CaCl2 Brine 96
10. Waste Management Service 98
10.1 Operation's Recap 98
11. Well Stimulation & Clean – Up 106
11.1 Operation Summary 106
11.2 General Information 107
11.3 Total Operation Results 108
Executed Operation Flow Chart 108
Daily Operation Summary 111
Sequence of Operation 112
Summary of Pumping Data 115
Coiled Tubing BHA Diagram 132
Slick Line BHA Diagram 133
12. List of Contractors 134
13. Appendix 135
13.1 DDR Summary 135

LIST OF TABLES

TABLE 2-1: AZNS-166 WORKOVER WELL INFORMATION 10
TABLE 2-2: AZNS-166 CASING HISTORY 13
TABLE 2-3: AZNS-166 WORKOVER INFORMATION 14
TABLE 2-4: AZNS-166 NPT TIME BREAKDOWN 35
TABLE 4-1: AZNS-166 BOTTOM HOLE ASSEMBLY 38
TABLE 5-1: AZNS-166 FINAL CASING DATA 39
TABLE 7-1: AZNS-166 TUBING DATA 41
TABLE 7-2: AZNS-166 EQUIPMENT CHECKLIST 43
TABLE 7-3: AZNS-166 EQUIPMENT CHECKLIST 44
TABLE 7-4: AZNS-166 OPERATION CHECKLIST 60
TABLE 7-5: AZNS-166 COMPLETION TALLY 70
TABLE 8-1: AZNS-166 FINAL WELL STATUS 73
TABLE 8-2: AZNS-166 EQUIPMENT SPECIFICATION 75
TABLE 8-3: AZNS-166 SECTION "D" SPECIFICATION 77
TABLE 8-4: AZNS-166 SECTION "D" TEST REPORT BEFOR INSTALLATION 78
TABLE 8-5: AZNS-166 SECTION "D" TEST REPORT AFTER INSTALLATION 79
TABLE 9-1: AZNS-166 FLUID PROPERTIES RECAP TABLE 86
TABLE 9-2: AZNS-166 MATERIAL CONSUMPTION ANALYSIS TABLE 87
TABLE 9-3: AZNS-166 VOLUME ANALYSIS TABLE 89
TABLE 9-4: AZNS-166 DAILY VOLUME BREAK DOWN TABLE 90
TABLE 9-5: AZNS-166 LOSS DISTRIBUTION 92
TABLE 9-6: AZNS-166 FLUID PROPERTIES RECAP 94
TABLE 9-7: AZNS-166 SOLID CONTROL DESSCUSION 95
TABLE 9-8: AZNS-166 INHIBITED $CaCl_2$ BRINE 96
TABLE 10-1: AZNS-166 DEWATERING/WATER TREATMENT SYSTEM 98
TABLE 10-2: AZNS-166 WATER ANALYSIS DE-COMPLETION SECTION 105
TABLE 11-1: AZNS-166 DAILY OPERATION SUMMARY 111
TABLE 11-2: AZNS-166 SEQUENCE OF OPERATION 114
TABLE 11-3: AZNS-166 TOTAL CONSUMBLE PLANNED & USED 115
TABLE 11-4: AZNS-166 SUMMARY OF PUMPING OPERATION RESULTS 116
TABLE 11-5: AZNS-166 PUMPING RETURNED OIL OPERATION REPORT 131
TABLE 11-6: AZNS-166 C.T BHA DESIGN 132
TABLE 11-7: AZNS-166 S.L BHA DESIGN 133
TABLE 12-1: AZNS-166 CONTRACTORS INVOLVED 134
TABLE 13-1: AZNS-166 DAILY DRILLING REPORT SUMMAR 138

LIST OF FIGURES

FIGURE 1-1: AZNS OILFIELD LOCATION MAP 8
FIGURE 1-2: AZNS – 166 LOCATION MAP 9
FIGURE 2-1: AZNS-166 WELL SKETCH 23
FIGURE 2-2: AZNS-166 NPT BREAK-DOWN CHART 34
FIGURE 7-1 MULE SHOE – NO-GO CONNECTION 46
FIGURE 7-2 PACKER CONNECTION 48
FIGURE 7-3 SSD CONNECTION 50
FIGURE 7-4 EXP. JOINT CONNECTION 52
FIGURE 7-5 TRSSSV CONNECTIONS 55
FIGURE 7-6 COMPLETION EQUIPMENT OFFLINE PRESSURE TEST 56
FIGURE 7-7: AZNS-166 COMPLETION SKETCH 63
FIGURE 7-8: AZNS-166 SETTING PACKER, ANNULUS & FINAL COMPLETION STRING PRESSURE TEST 72
FIGURE 8-1: AZNS-166 WELLHEAD SKETCH 76
FIGURE 8-2: AZNS-166 X-MASS TREE BODY PRESSURE TEST GRAPH BEFORE INSTALLATION 80
FIGURE 8-3: AZNS-166 X-MASS TREE BODY PRESSURE TEST GRAPH AFTER INSTALLATION 81
FIGURE 8-4: AZNS-166 WELLHEAD MOM BEFOR INSTALLATION 82
FIGURE 8-5: AZNS-166 WELLHEAD MOM AFTER INSTALLATION 83
FIGURE 9-1: AZNS-166 MUD CHEMICAL USAGE 87
FIGURE 9-2: AZNS-166 EFFECTIVE CONCENTRATION 88
FIGURE 9-3: AZNS-166 VOLUME ANALYSIS CHART 89
FIGURE 9-4: AZNS-166 DAILY VOLUME BREAK DOWN CHART 91
FIGURE 9-5: AZNS-166 LOSS ANALYSIS 93
FIGURE 9-6: AZNS-166 MUD CHEMICAL USAGE 97
FIGURE 9-7: AZNS-166 EFFECTIVE CONCENTRATION 97
FIGURE 10-1: AZNS-166 CHEMICAL CONSUMPTION AND WATER TREATMENT VOLUMES BY DATE FOR COMPLETION SECTION 99
FIGURE 10-2: AZNS-166 CHART OF LIME USAGE PER PROCESSED WATER IN COMPLETION SECTION 100
FIGURE 10-3: AZNS-166 CHART OF LIME USAGE PER DRILLED METER IN COMPLETION SECTION 100
FIGURE 10-4: AZNS-166 CHART OF PAC USAGE PER PROCESSED WATER IN COMPLETION SECTION 100
FIGURE 10-5: AZNS-166 CHART OF PAC USAGE PER DRILLED METER IN COMPLETION SECTION 101
FIGURE 10-6: AZNS-166 CHART OF POLYMER USAGE PER PROCESSED WATER IN COMPLETION SECTION 101
FIGURE 10-7: AZNS-166 CHART OF CAUSTIC USAGE PER PROCESSED WATER COMPLETION SECTION 101
FIGURE 10-8: AZNS-166 CHART OF CAUSTIC USAGE PER DRILLED METER IN COMPLETION SECTION 102
FIGURE 11-1: AZNS-166 EXECUTED OPERATION FLOW CHART 110

1. General Information

1.1 Field Introduction

Azadegan South Oil Field is situated in West Karoun, Khuzestan province on a large long – axis anticline with N – S trending with approximate dimensions about 20^{km} width and 60^{km} length near to Iran – Iraq border, It is located in The Northwest of The YADAVARAN Field and in The West of JUFEYR Field. The Average Monthly Temperature is 45$^{°c}$ in summer and Highest Temperature is 52$^{°c}$. The Lowest Temperature is -4.4$^{°c}$ in winter. Maximum Rainfall is 78^{mm} in February, Winter Season.

The trap area of the south Azadegan is limited to 43.2 * 17.2km. The Azadegan Oil field was discovered in 1999, when Well AZN-1 was drilled vertically down to the Cretaceous Fahliyan Formation with total depth of 4,643^{m}. The results of this well, revealed the reservoir characteristics of the field. Following to the result of the well no. AZN-1, another 5 exploration wells was drilled in different parts of this huge field down to Fahliyan Formation. In the later stage the well No.10 assumed as exploration well for evaluation of deeper formations. This well was drilled in 2008, down to the depth of 5340^{m} (Neyriz Fm.), mainly to evaluate the Jurassic formations.



Figure 1-1: AZNS Oilfield Location Map

1.2 AZNS – 166 Well Location Map

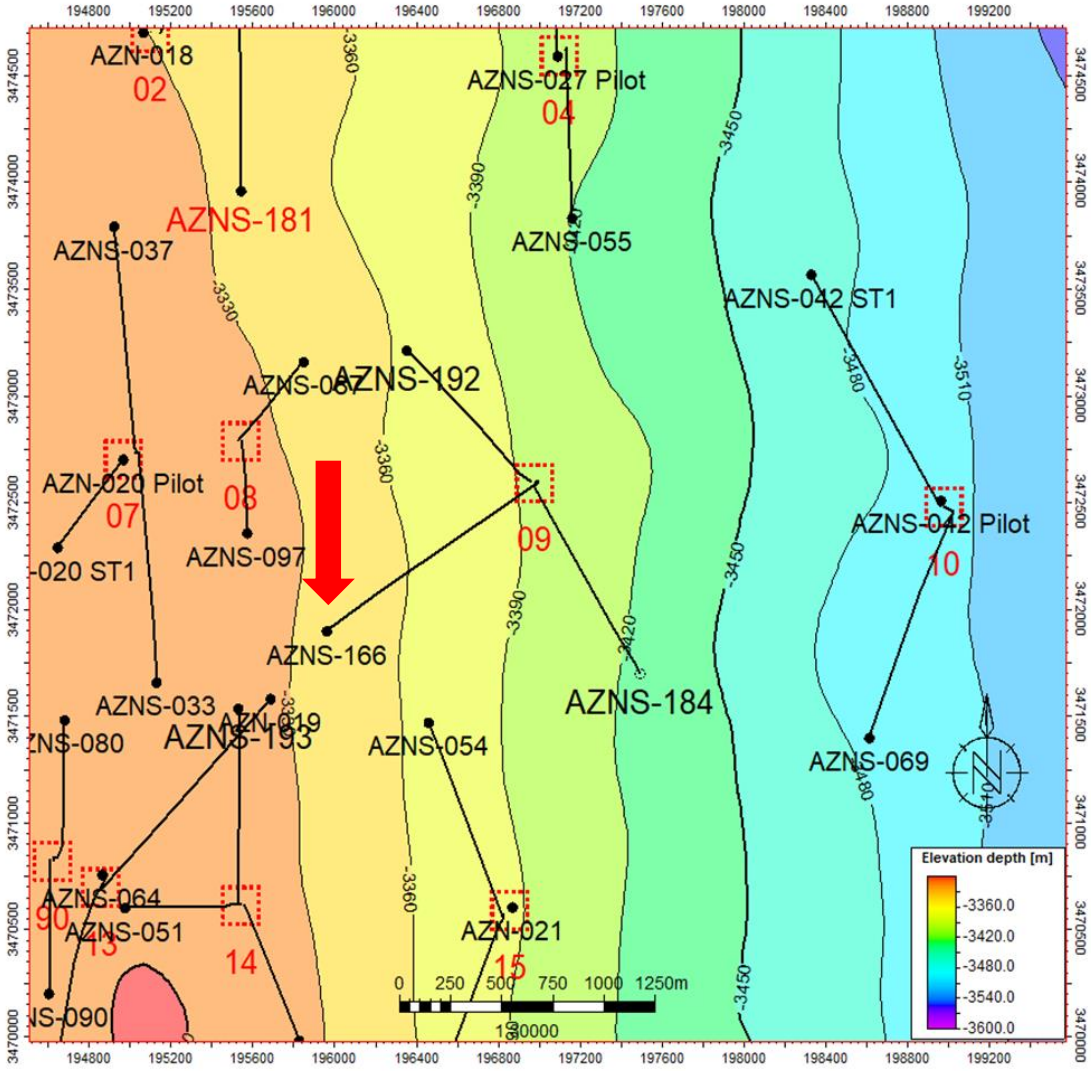


Figure 1-2: AZNS – 166 Location Map

2. Well History

2.1 Well Informaion

Rig name	OEOC 201	**Owner**	PEDEC/PPL
Rig type	Land Rig 2000HP	**Contractor**	MSA/OEOC
Well Name	AZNS – 166	**Management Contractor**	MSA
Well Type	Kazhdumi well	**Field**	South Azadegan
Completion Type	4-1/2" * 3-1/2" 7.5K	**RTE**	12.95m
Total Depth (MD)	4280 mMD	**GLE**	3.95
Surface Coordinate		N: 3,472,595 E: 196,992	
TD Coordinate		N: 3,471,897.14 E: 195,955.76	
Operation Date			
Spud Date	27 – Oct. – 2025		
Released Date	19 – Nov. – 2025		
Rig Days Plan / Actual	44.2 days (Main Plan) + 95 days (Contingency Plan) / 24 days		

Size (in)	Shoe Depth (mMD)	Specification
20	147 m	K – 55, 94#, BTC
13 – 3/8	1338 m	N – 80, 68#, BTC
9 – 5/8	1765 m	L – 80, 47#, PJE / L – 80, 47#, TPCQ
7	1608.2 – 4193 m	L – 80, 29#, TPCQ
4-1/2” Non-Slotted	4132.8 – 4199.27 m	L – 80, 13.5#, BTC
4-1/2” Slotted	4199.27 – 4269.54 m	L – 80, 13.5#, BTC
4-1/2” Non-Slotted	4269.54 – 4279.6 m	L – 80, 13.5#, TPCQ

Table 2-1: AZNS-166 Workover Well Information

2.2 AZNS-166 Well History

Drilling History

The AZNS 166- (Pad 09) was drilled by rig 28 Fath, which rig moving was spudded on 24-Janury-2019 @ 06:00.

The Well AZNS-166 was spud in with 26” bit at 06:00 on Jan 24, 2019, Drilling of this section was started from Surface on Jan 24, 2019 in Aghajari formation and ended drilling at 149m (C. Point). Install New C.H.H 20-3/4" 3K & Test P-Seals W/ 500 PSI for 15 Min.20" casing was run to 155m & cemented by inner stab-in string with slurry to surface.

Drilling of 17.5” section was started from 149 MT on Jan 31, 2019 in Aghajari formation to 1338 m (13-3/8" CSG Shoe) and Install 20-3/4"-3K * 13-5/8"-5K C.H.S (MSP DRILEX, S/N: CS1523N140058).

The 12 ¼’’ hole was started from 1338m on March 5, 2019 with 115 pcf mud weight in Gachsaran formation to 1343. then increase mud weight gradually to 124 pcf to 1765 m. observe 2-4 BPH gain and cut mud weight return to 112 PCF and increase Ca2+ ion to 6000 mg/lit. close the well and prepare 650 bbl with 130 PCF mud and kill the well and then RIH to bottom and balance mud weight at 130 PCF with no loss & no gain. Run 9 5/8” casing to 1764 MT and cementing (397 bbl 138 PCF as lead and 118 bbl 125 PCF as tail). Install 13-5/8"-5K x 11"-10K T.H.S (MSP/DRILEX).

The 8 1/2’’ hole was started from 1764m on March 26, 2019 in Gachsaran formation. With 78 PCF mud weight to 1765.5m. Continue drilling Resume Drlg Formation to 2273m. Start Dir.Drlg from kop 2735 to 4197m (7" Liner Point) While Displace Kcl-Polymer Mud (81 PCF) In Hole W/ Oil Base Mud (80 PCF).

The 6 1/8’’ hole was started from 4197m on August 31, 2020 in KAZHDUMI Formation with 82 PCF Mud W/ 6-1/8 PDC Bit & Dir. Drilling BHA to 4280m (TD). RIH W/4-1/2” Slotted Liner to 4280m Set HGR. With max inclination 63.5 and AZ 235.

Displace Mud in Well W/ Comp. Fluid (MW: 82 PCF). RIH 3-1/2" Completion String as Program to 2776mWhilePress.Test Comp. String Several Steps W/ 4500 PSI / 15 MIN, OK. cont. RIH Comp. String to 2785.2m, Land TBG HGR in 11"-10K T.H.S, Press. Test Comp. String W/ 4500 PSI / 15 MIN. Run in Comp. String W/ SB Pulling & Plug to 2770.1m Set Prong in NO-GO. Pressure test Comp. String W/4500psi for 15MIN, Ok. Close 3SV, laydown41/2"L. JT, install 4"TWCV in TBG HGR, P/T TWCV & TBG HGR W/ 4500 Psi, OK, N/D BOP Stack, Install 11"*4 1/16"-10K BTM Master Valve.

RIH W/ GS Pulling & Remove NO-GO. RIH C.T.B to 400 M, Obs. Increase Well Head Press. To 200PSI, Close The Well, Monitored Well After 3 Hr, Press: 460 PSI, Open The Well, While Flow the Well, Cont. RIH Coiled Tubing to 4280m Displace Comp. Fluid in Well W/ 240 BBL Diesel. Cont. Flow The Well W/ Chock Sizes: 54 & 48 & 32/64", Oil Weight: 54.5 LB/FT3, BS&W: 0, Ann. Press: 750 PSI, In Order to

Monitor the Well & Ann. Press., Close The WELL @ 24:00 Monitored The Well & Ann. Press., Well Head Press.: 1400 PSI, ANN. PRESS: 0 PSI.

Again RIH by Slick Line to NO-GO, Install Plug & Prong in NO-GO Landing Nipple, Test W/ 2500 PSI, AFTER 3 TIMES, Finally Ok, Again RIH by Slick Line & Install Protection Sleeve Inside The 3SV. IH Coiled Tubing to 2770m Displace Oil in Well W/ Diesel, R/U H-Lubricator Install 2-WAY Inside the Tubing HGR, L/D H-Lubricator, Close Top, Kill, Production & Chock Valve of X-Mass Tree. Release The Rig @ 24:00 on October 29, 2020 (1399/08/08).

Operation after Completion History

Well has secured with installing TWCV, plug & prong (in No-Go Landing Nipple) & closed 3SV (CL pressure: 0psi) Retrieve two way BPV, rubber packing has been damaged.

RIH to retrieve prong unsuccessful, RIH with bailer gauge to 2760m it was full of Asphaltene (2 times).

Pressurized CL with 4500psi & opened 3SV, RIH CT to depth of obstacle without pumping fluid, CT couldn't pass SSD depth @ 2740.1m.

RIH CT to 2769.9m (No-Go Depth), pumped 15bbl diesel & spotted 15bbl Xylene on obstacle, retrieve prong coated with Asphaltene.

RIH CT with GS 2.5" without pumping fluid to No-Go depth @ 2769.9m & apply 17klb over-pull to retrieve plug. CT couldn't pass 3SV, applying 4klb over-pull, plug was retrieved from fishing neck. Moreover, impression block of 3SV flapper observed on neck of plug.

SIWHP = 1700psi, flow the well (FWHP = 700psi), close 3SV flowing continued, RIH SL with LIB while 3SV flapper is closed, mark of 3SV flapper observed on LIB, flow the well towards burn pit while 3SV flapper was closed, well produce non-stop, close production valve, open 3SV flapper & RIH SL with LIB @ 102.5m, dipping valve & jar down mark on 3SV flapper observed on LIB, RIH SL with LIB while 3SV flapper was closed. Mark of 3SV flapper observed on LIB, RIH SL with 1-1/2" stem while 3SV flapper was closed. Weight dropped @ 102.5m, open 3SV flapper, RIH against SL to 102.5m & observed weight dropped.

RIH with 2.8" LIB several times while 3SV closed or open & observed mark on it but in close position pressure dropped & remained constant. (600 – 800psi)

WHP = 1500psi, RIH SL with special protection sleeve (profile: AF, ID: 2.7, OD: 3.437", modified by PED.CO). SL @ 324ft. and try to pass 3SV flapper tip of the P.S pass the flapper but not completely, effects were observed on the tip of P.S.

RIH 2.5” bailer, 2.3” LIB, 1-7/8” taper tap, couldn’t pass from 330ft., RIH with 2.320” LIB to 9090ft. (observed some drag during RIH probably due to presence of Asphaltene), observed plug impression on the LIB.

RIH SL with tubing swage 2.56”, SL @ 330ft. TOF, observed drag, jar down to pass this depth & again jar up, repeated that for several times, no success.

RIH SL with taper tap 1.5”, SL @ 9090ft. TOF & tried to catch the plug, R-pulling pin was sheared with 1200lb at the depth of 9090ft. (rope socket 1-7/8” + 3ft. stem 1-7/8” + taper tap 1.5”) were left in the well as fish. RIH SL with R-pulling 1-7/8” to 9090ft. TOF & tried to catch the fish, flow the well meanwhile trying to catch the fish, retrieved successfully.

Repeated RIH SL with taper tap 1.5”, SL @ 9090ft. TOF & tried to catch plug, R-pulling pin was sheared with 1200lb at the depth of 9090ft. (rope socket 1-7/8” + 3ft. stem 1-7/8” + taper tap 1.5”) were left in the well as fish. RIH SL with R-pulling 1-7/8” to 9090ft. TOF & tried to catch the fish, flow the well meanwhile trying to catch the fish, retrieved successfully. Secured the well.

Install WH & XMT Acc. at the presence of wellhead specialist, accessories disconnected.

2.3 Casing & Liner Depth

Casing Spec.	20"	K – 55, 94#, BTC	147^{m}
	13-3/8"	N – 80, 68#, BTC	1338^{m}
	9-5/8"	L – 80, 47#, PJE L – 80, 47#, TPCQ	1765^{m}
	7"	L – 80, 29#, TPCQ	1608.2 – 4193^{m}
	4-1/2” Non-Slotted	L – 80, 13.5#, BTC	4132.8 – 4199.27^{m}
	4-1/2” Slotted	L – 80, 13.5#, BTC	4199.27 – 4269.54^{m}
	4-1/2” Non-Slotted	L – 80, 13.5#, TPCQ	4269.54 – 4279.6^{m}

Table 2-2: AZNS-166 Casing History

2.4 Summary of Workover Operation

The AZNS-166 workover well was De-Complete by rig OEOC – 201 from "27-Oct-2025, 12:00." to "19-Nov-2025 23:59." as described in the following:

Workover Summary:

Date	27 – October – 2025
WorkOver Depth	4280 mMD
Formation	Kazhdumi
Mud Weight	83^{pcf}

Table 2-3: AZNS-166 WorkOver Information

De-Completion:

Cont. R/U, While Set & Install TDS; Spud Rig 201 as per Prespud Check List @ 1404.08.05 - 12:00 L/U 4" 10k Co-Flex Hose F/ Choke Manifold outlet To X-Mas Tree Production Valve; L/U 2" Chicksan Flowline F/ Pump Unit discharge To T.H.S side outlet; Set Storage Tank & Conn. To Burning Line; Check & Record Annulus pressures of all Wellhead sections as follows:

Section A – 0 psi / 15 min; Section B – 0 psi / 15 min; Section C – 0 psi / 15 min; All wellhead sections confirmed pressure-free and stable. Press. Test P-Seal Test of B & C Section as follows: Section B (13-3/8" P-Seal) – 1500 psi / 15 min; Section C (9-5/8" P-Seal) tested @ 2500 psi / 15 min – Press. Test between two P-Seals OK, but Press. Test between lower P-Seal & CSG HGR failed; Press. Test Chiksan Pipes & Co-Flex Hose W/ 7000psi / 15 min, Ok; P/U & M/U Wellhead Lubricator on X-Mas Tree, Press. Test the same W/ 4000psi / 15min.

Ret. TWCV W/ Wellhead Lubricator, While Record 800psi Pressure on Wellhead Lubricator Press. Gauge; L/D Wellhead Lubricator and X-Mas Tree Cap; Flush Solid Block upper valves W/ 10bbl Drill Water. R/U Slick Line BOP and install on X-Mas Tree Head; Assemble 2.75" Ring Gauge Tool Strg and Pass it Thru. Slick line Lubricator, Conn. Lubricator to Slick line BOP; Press. Test Slick Line BOP & Lubricator W/ 4000psi / 15min, Ok; RIH W/ 2.75" Ring Gauge Tool Strg To 107m, Attempt To

pass this point, No Success due to the Min ID of Protection Sleeve being 2.7" (The proper completion accessory not received from the client), Confirm Protection Sleeve is in TR3SV; POOH Slick Line Tool Strg To Surface, Flush Solid Block, L/D 2.75" Ring Gauge Tool String; P/U & Assemble 2.2" Ring Gauge Tool Strg and RIH To 3056m (No-Go Depth: 2770m), Obs. Slick Line Tension Drop due to Well Deviation, Decide To POOH Slick line Tool String To Surface; Flush Solid Block; L/D Slick Line Eqp. Prepare Rig To Kill the Well W/ Coiled Tubing; R/U Coiled Tubing Facilities as follows: M/U Coiled Tubing Riser & Conn. To Solid Block, P/U 4-1/16" 10k C.T BOP & M/U on C.T Riser, Press. Test Riser & BOP Thru. X-Mas Tree Kill Valve W/ 3000psi – OK; M/U C.T BHA (1-3/4" Wash Nozzle [5 * 1/2" Ports] + 1-3/4" Perforation Sub [12 * 1/2" Ports] + 1-3/4" Double Flapper Check Valve) and Conn. To C.T Connector; P/U C.T Injector Head & M/U on C.T BOP, Press. Test C.T Riser, BOP Rams, and Injector Head Connections Thru. C.T BHA W/ 4000psi – OK; Bleed off C.T Strg & Riser Pressure To 1000psi, then Bleed off C.T Strg To 0psi to Function Test Double Flapper Check Valve W/ 1000 psi – OK; Equalize C.T Riser, BHA & Solid Block Press. , Open Dipping & Top Master Valves. Cont. RIH W/ 1-3/4" C.T BHA, While Circ. Thru. Choke Manifold @ 0.2BPH F.R & 1100psi Back Pressure, and Take Return in Storage Tank. Kill The Well using W&W Method.

Pump Mud 83pcf @ 1BPM Flow Rate, While Maintain Const. Back Pressure via Adjustable Choke (1100psi); Confirm Stable Return & Gradually Replace Reservoir Fluid W/ 83pcf Mud; Take Returns as follows: 195bbl Reservoir Fluid & 125bbl Contaminated Mud in Storage Tank, NL-NG; At mud return MW of 71pcf, Divert Return F/ Storage Tank & L/U Choke Manifold To T.Tank; Confirm Well Dead, Bleed off Press. To 0psi. Divert Return To Active Pit; CBU Thru. C.T BHA for Two Cycle, Confirm Uniform 83 pcf In / Out MW; Obs. Well for 1Hr. , Well Static. POOH 1-3/4" C.T BHA To Surface, While Circ. Thru. C.T BHA, NL-NG; Flush C.T; Static Flow Check & Obs. The Well for 1 Hr. , Well Static; L/D C.T Eqp. ; Obs. The Well For 0.5hr Thru. Choke Manifold, Well Static; Install TWCV in TBG HGR, Perss. Test TWCV @ 4500psi, Ok. N/D X-Mas Tree.

N/U 13-5/8" 10k BOP Stack. Perform BOP Test as NIOC Policy as follow: 13-5/8" 10k Shear Ram w/ 6500psi, Ok. P/U & M/U Runing Tools HGR (ACME * TPCQ) + X.O.S (TPCQ * 4-1/2" IF) + 1Jts 5" P.Joint + 1 Jts 5" D.Pipe and Connected to TBG HGR For Continue Perform BOP Test as follow : Hydrill w/ 3000psi, Ok. Cont. Test 13-5/8" 10k BOP Stack. attempt to perform BOP test several Times No Succ, Work on fixing BOP leakages

Wait on OEOC to Cont. Test 13-5/8" 10k BOP Stack While Work on fixing BOP leakages as Below: Fix Leakage from Inner Side VLV of Top & BTM CHK Line after several times and Test W/ 4500Psi, OK.

Fixing Leakage from Top & BTM Rams & Test it W/ 4500Psi, OK.

Work on leakages between BTM Rams & Spacer Spool Connection after several times and Test W/ 4500Psi, OK. Work on Side VLV as follow : Change Outer Side VLV BTM CHK line & Fixing all side VLV inner & Outer and test all Side VLV W/ 4500Psi, OK. Test Chockmanifold & Koomy Unit, Ok.

Remove TWCV, Connect Running Tools to TBG HGR, P/U TBG HGR with max 190Klb and Unset PKR with 120Klb Over Pull step by step. Try to perform Circ Mud Thru String No Succ Due to Observe Leakage TDS Kelly Hose . Cont. Try to establish the Mud circ. as follow : Step 1 : Increased pressure step by step thru Strg. to max 480psi, no return & indicating fluid inject in formation. Step 2 : Increased pressure step by step thru Annular to max. 800psi, no return inside String to Reverse Circ. Pull out Completion string By request of Client (P.P.L) as follow: POOH & L/D 4-1/2" TBG HGR (18.9PPF, TPCQ-EX Box * Box) + 4-1/2" Double pin (18.9PPF, TPCQ-EX P*P) + 1 Jts X.O.S TPG2 + 4-1/2" Cross Over (18.9PPF, TPG2 PIN * TPCQ-EX BOX)

As Client Request (P.P.L), Cont. POOH with 2 Jts 4-1/2" TBG (18.9PPF, TPG2 BOX * PIN), OBS 15-30klb over pull @ 2759-2758.3m. Try to Cont. POOH with max 30Klb over pull step by step and several times, No Succ. Perform Circ Mud Thru String, No Return Mud and Hold Pressure in String, try again Cont POOH with max 60klb over pull step by step and several times, No Succ & Perform Circ. Mud Thru String, No Return Mud and Hold Pressure in String, try again Cont POOH with max 100klb over pull step by step and several times, Suddenly Release String & Observe U-Tube Thru String. Close the well, Circ Mud from Choke Manifold to circ. Out Cacl2 Brine as Comp. Fluid, Cont. Circ. To uniform MW to 83pcf, OBS the well Static. (Get totally 80bbl Contaminated Mud). Cont. POOH & L/D with Normal Drag to 1530m While f/u well continuously, NL-NG.

Cont. POOH & L/D Completion String to 50m While f/u well continuously, NL-NG. During Pulling out, Tubing was Observed Empty up to Around 600m. From Around 600 m, Tubing Observed Filled with Mud While Retrieving. Operation Proceeded Carefully and Under Full Safety Compliance Retrieved Tubing Joints are Being Washed and Cleaned Properly before Stacking.

Cont. POOH & L/D Completion String to Surface While f/u well continuously, NL-NG. L/D CSG Crew Equipment(OEOC) while Hight Pressure hose install on TDS.

P/U & M/U New 8-3/8" M.M.J.mill (TSK, SN: 408, 5*15/32) + Bit Sub (F.Valve in) + 9-5/8" Scraper + 1 Std 6-1/2" D.C + 6 Jts 5" H.W.D.P (Jts by Jts) Cont. Run in hole with 127 Jts 5" D.pipe (Jts by Jts) from 100 To 1360m W F/U String every 20 Jts.

Cont. RIH W/ 8-3/8" M.M.J.mill (TSK, SN: 408, 5*15/32) + Bit Sub (F.Valve in) + 9-5/8" Scraper + 1 Std 6-1/2" D.C + 6 Jts 5" H.W.D.P (Jts by Jts) Follow by 5" D.Pipe to 1609.60m While F/U String every 20 Jts , Tag 7" L.Lap @ this depth. POOH From 1609.6m to Surface and L/D 9-5/8" Scraper & 8-3/8" Junk Mill While C.W.H, NL.NG. P/U 5" DP & M/U Plug tester, Set Wear Bushing in T.H.S, Change Elevator to Suit 3-1/2" Tubular. M/U New 6" Junk Mill (T.S.E.KH) & RIH W/ 27 jts 3-1/2" HWDP (Jt by Jt) & Follow by 3-1/2" D.Pipe (Jt by Jt) to 540m for Cleaning Inside 7" liner W/ F/U String, NL-NG. Cont RIH with 6" Junk Mill (T.S.E.KH) + 27 jts 3-1/2" HWDP (Jt by Jt) & Follow by 3-1/2" D.Pipe (Jt by Jt) from 540m to 1153m for Cleaning Inside 7" liner W/ F/U String, NL-NG. Perform H2S Drill. Cont RIH with 6" Junk Mill (T.S.E.KH) + 27 jts 3-1/2" HWDP (Jt by Jt) & Follow by 3-1/2" D.Pipe (Jt by Jt) from 1153m to 2540m for Cleaning Inside 7" liner W/ F/U String, NL-NG

Cont RIH with 6" Junk Mill (T.S.E.KH) + 27 jts 3-1/2" HWDP (Jt by Jt) + 3-1/2" D.Pipe (Jt by Jt) + 4.3/4" D.PIN + 4 3/4" Bit Sub (Float In) + XOS + 5 " D.Pipe from 2540m to 4000m for Cleaning Inside 7" liner W/ F/U String, NL-NG. Observe took weight string @ 4000m and cont. Run in hole with wash down to 4015m & from 4015m with soft wash & Ream to 4133m (4-1/2" L.Lap). Circ BTM Up Till Uniform Mud weight to 83 Pcf (Min Return MW 78 PCF & Drop PH to 7.5), Flow Check the well, Static. Start POOH from 4133m (4-1/2" L.Lap) to 2820m while Circ mud Cross well head, NL.NG

Cont. POOH from 2820m to surface & L/D 6" J. Mill (T.S.E.KH, 5% Used) while Circ mud Cross well head, NL.NG. P/U & Run in hole W/ NEW 3-1/2" M.M.J.Mill (T.S.E.KH, SN : 084) + 15 Jts 3-1/8" D.C (Jt by Jt) + R/U 2-7/8 "D.Pipe handling tools and RIH W/ 6 Jts 2-7/8" (Jt by Jt) D.P to 190 m. Change Handling Tool & Cont. Run in hole by 3-1/2" D.Pipe from 190m to 2800m while break Circulate each 15 STD, NL.NG.

Run in hole by 5" D.Pipe from 2800m to 3100m while F/U string & break Circulate each 15 STD, NL.NG. Cont. RIH to 4100m; Due to severe U-Tube F/U string and break Circ. Every 5-10 Stds. Wash Dn to 4133m (4-1/2" L.Lap). Soft wash & Ream Dn to BTM and

tag the BTM & Space out to 4275.5m. Ream Dn Parameters: WOB: 1-3 Klbs, Rot: 15 RPM, TQ: 4-5.5 Klbs.ft, F.R: 65-70 GPM, SPP: 700-850 Psi.

Over Circ. Mud to uniform MW in/out to 83 pcf. Pump 20 bbl 83 pcf Filtrated CaCl2 as Non-Solid Completion Fluid & Displace to spot, OK.

Start POOH From 4275.5m to 2800m W/ Circ Mud Cross Well Head, NL.NG.

Cont POOH From 2800m to 1237m W/ Circ Mud Cross Well Head, NL.NG. Slip & Cut 97 FT DRLG LINE. Cont. POOH To 200m. Change the handling tools and Cont. POOH while L/D 2STD 2-7/8" D.Pipe & 5 STD 3-1/8" D.c (jt by jt). Check and L/D 3-1/2" J.mill (10%used). R/D 2-7/8" D.Pipe handling tools and release all the 4-1/2" LNR clean out BHA. Break out and L/D Double Pin of old completion TBG HGR carefully. M/up 6" M.M.J.mill (5% Used / T.S.E.KH) + 4 3/4" Bit Sub (F. In) + HWDP 3 1/2" & Follow by 3 1/2 DP "G" to 1350m W/ F/U String Each 15 STD , NL-NG.

Cont RIH with 6" M.M.J.mill (5% Used / T.S.E.KH) + 4 3/4" Bit Sub (F. In) + HWDP 3 1/2" & Follow by 3 1/2" DP to 1608m (7" L.Lap) Obs. Drag @ 7" L.Lap during pass 6" Mill; Smooth this interval, several times & Check w/o Rot, Ok. Cont RIH to 3925m. Cont. RIH W/ 6" M.M J.Mill and 7" Scraper to 4132m (4-1/2" L.Lap) and Pass 7" L.Lap W/ 7" Scraper Without any Drag and Scrap from 2550m to 2750m several times, F/U string and break Circ every 10 Stds. CBU W/ Hi-FR while reciprocate string; Obs. Huge amount of asphaltene pieces on shale shakers. Cont. Circ. to clean the hole and uniform MW.

Completion Operation Summary:

Displace mud In well with CaCl2 Completion Fluid Non.Solid : Pump 50BBl Hi.vis Pill, Pump & Displace the well with 680BBl CaCl2 Brine as Completion fluid (Dump 40 BBl Contaminated with mud). (Disp. Parameter : F.Rate : 180 GPm, SPP : 1250 Psi

Flow check the well, Static. Start POOH from 4132m (4-1/2" L.Lap) to 1376m while L/D 5" D.Pipe (Jt by Jt) & 3-1/2" D.Pipe (Jt by Jt) & F/U the well with CaCl2 Completion Fluid Non-Solid While POOH Check again 7" L.Lap without any Drag.

Cont. POOH 6" Clean out BHA F/ 1376m To surface On Elevator, While L/D All Tubular (Jt by Jt) & 6" Mill (10% Used, same as RIH Condition) and F/U Well w/ CaCl2 Completion Fluid Non-Solid, NL-NG. Perform BOP Test as NIOC Policy, Retrieve Wear Bushing, Set Plug Tester, Perform BOP Test as follow: 5k 13-5/8"

Annular w/ 3500psi, 15min, Ok; 10k 13-5/8" Top Ram (VBR 2-7/8" - 5") w/ 7500psi, 15min, Ok; 10k 13-5/8" BTM Ram 5" Pipe Ram w/ 7500psi, 15min, Ok; 10k 13-5/8" Shear Ram w/ 7500psi, While Press. Test All Choke Manifold Valves & Accumulator Unit Functionality, Ok; Retrieve Plug Tester; L/D Last 5" DP Std. R/U LNR Running Tools, While Circ. C.W.H, NL-NG; Held PJSM, Prepare To RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg.

RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg as follows:

3-1/2" Wireline Re-Entry Guide Shoe (10.2#, HSM3 + 3-1/2" Bottom No-Go L/N (10.2#, Seal Bore: 2.75", Xn Profile) + 3-1/2" Pup Jt TBG + 1 Jt 3-1/2" TBG + 3-1/2" Pup Jt TBG + 7" Hydraulic Set Retrievable Packer (29#) + 3-1/2" Pup Jt TBG (Check PKR Shear Pins, Ok) 1 Jt 3-1/2" TBG; Run 2.8" Gauge Ring to No-Go Depth, Ok; Cont. RIH 7" 7.5k Comp. Strg. as follows: 3-1/2" Pup Jt TBG + 3-1/2" SSD (X profile, Close position, Downward open) + 3-1/2" Pup Jt TBG 1 Jt 3-1/2" TBG + 3-1/2" Pup Jt TBG + 3-1/2" Traveling Jt (Full Open Position, Dressed w/ 3 No. Shear Pin, Splined Type) + 3-1/2" Pup Jt TBG w/ 2 Jt 3-1/2" TBG To 72m; Run 2.8" Gauge Ring to SSD Depth, Ok; While Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. Press. Test Comp. Strg against SSD Check Valve @ 72m W/ 6000 Psi / 15min, Ok; L/D Press. Test Eqps. Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 72 To 676m, While Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. R/U Slickline Tools; P/U & Assemble 2.8" Gauge Ring Tool Strg and Attempt To RIH To Top of SSD, Obs. Slickline Tension Drop @ 335m, Try To pass the same depth Sev. Times, No Success; POOH S/L Tool String To Surface; L/D Slickline Tools; Decide To POOH Comp. Strg. POOH 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 676 To 327m; Obs. 2 Jts of 3-1/2" TBG is damaged, While L/D 3-1/2" TBGs and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG; R/U Slickline Tools; P/U & Assemble 2.8" Gauge Ring Tool Strg and RIH To Top of SSD Normally; POOH S/L Tool Strg To Surface; L/D Surface Slickline Eqps. ; Prepare To Resume Comp. Strg RIH

Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 327 To 676m, While Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. Press. Test Comp. Strg against SSD Check Valve @ 676m W/ 6000 Psi / 15min, Ok; L/D Press. Test Eqps. Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 676 To 1223m, While Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor

the Well, NL-NG. Press. Test Comp. Strg against SSD Check Valve @ 1223m W/ 6000 Psi / 15min, Ok; L/D Press. Test Eqps. R/U Slickline Tools; P/U & Assemble 2.8" Gauge Ring Tool Strg and RIH To Top of SSD Normally; POOH S/L Tool Strg To Surface; L/D Surface Slickline Eqps.

Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 1223 To 1671m, While Pass 7" LNR gently, Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. Stop Op. due to bad weather @ 1671m, while Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Cont. Stop Op. due to bad weather @ 1671m, while Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 1671 To 2640m, While Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Press. Test Comp. Strg against SSD Check Valve @ 2640m W/ 6000 Psi / 15min, Ok; L/D Press. Test Eqps. Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 2640 To 2658m as follows: 4-1/2" Pup Jt (HSM3 ,18.9#, L-80, Type-1) + 4-1/2" Flow Coupling (18.9#, 9CR1MO, HSM3, 4 ft) + 4-1/2" TRSSV Tubing Retrievable Safety Valve (18.9# w/ 3.437" Seal bore, HSM3, 9CR1MO, 7.5K WP w/ AF Profile, Flapper Type) + + 4-1/2" Flow Coupling (18.9#, 9CR1MO, HSM3, 6 ft) + 4-1/2" Pup Jt (HSM3 ,18.9#, L-80, Type-1) + 1Jt 4-1/2" TBG (18.9#, L-80,HSM3) , While Clean & Wash all Connections; Use Thread Seal Compound, and JAM System, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Flush & Conn. 1/4" CL To TRSSV CL Port, Press. Test Conn. @ 6000psi / 15min, Ok, While Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. B/O All Pup Jts of Comp. Strg Facilities Ret. F/ Well AZNS#116, While Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG. Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strg against SSD Check Valve @ 2658m W/ 6000 Psi / 15min, Ok; Inflow Test, Pressure stabilized @ 1000 psi / 15 min; No pressure build-up observed. Check and test equalizing function of TR3SV; OK. Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 2658 To 2706m; P/U & M/U 4-1/2" Fluted Swage Adapter [D/P, 18.9# 9CR1MO, WEIQIXIN Co.] + TBG HANGER [MSP/Drilex, 7.5K, 11" X 4 1/2" ACME Box up X 4 1/2" Box Down L-80 18.9#, M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type "H" Two Way (Min Bore: 3.68")] + TBG HGR Running Tool + Landing Joint, While Clean & Wash all Connections; Use Thread Seal Compound, Pass Drift Thru. all Eqp. , JAM System, Secure CL using Cross Coupling Protector and Circ.

C.W.H by Trip Tank & Monitor the Well, NL-NG; Redress TBG HGR Body W/ 2No. S-Seal Gasket; Pass CL Thru. TBG HGR Slot, Cut same, and wrap on Fluted Swage below TBG HGR; Open T.H.S outlets, Clean and prepare Tubing Spool and ensure tie-down screws backed out; Cont. RIH W/ L/J to 2707.5m, While Check and Land TBG HGR in THS, Ok; Space out to 2706m (1.5m above THS). Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strg against SSD Check Valve @ 2706m W/ 6000 Psi / 15min, Ok, L/D Chiksan Pipe; P/U & M/U G.FLG + 4-1/16" 10K Gate Valve + Slickline BOP + Lubricator & BOP Panel; Test BOP, Ok; R/D Mouse Hole; R/U Surface Slickline Tools and perform Slickline Job as follows: Run#1 P/U & Assemble AF Running Tool for TRSSSV Protection Sleeve; RIH W/ 3.437" Protection Sleeve; Set in position; POOH To surface.

Run# 2 : RIH w/ 3" SB to SSD Depth; Try to engage w/ SSD WFB Check valve; No-Succ. POOH to surface; Obs. SB Steel shear pin sheared.

Run# 3 : Redress SB w/ Steel Shear Pin. RIH w/ 3" SB to SSD Depth. POOH to surface; SSD WFB Check valve retrieved.

Run# 4: P/U & Assemble Running Tool for Blanking Plug in Landing Nipple; RIH W/ 2.750" Xn Blanking Plug & Set in No-Go; POOH To Surface.

Run# 5: P/U & Assemble SB Running & Pulling for Equalizing Prong match W/ 2.750" Plug of No-Go; RIH W/ Equalizing Prong & Set in Position; POOH To Surface.

Run# 6: P/U & Assemble Shifting Tool to confirm SSD is full close; RIH W/ 2.75" Shifting Tool To SSD Depth, Confirm SSD closed; POOH To Surface; L/D Surface S/L Tools.

L/U Test Line On Strg & Press Test Same To 6000psi, Ok; Set PKR as follows:

Press. Test Surface Test Line & Chiksan Pipes @ 6,000 Psi / 5–10 Min – Ok; M/U Surface Test Line to Comp. Strg; Record Up/Dn ward Comp. Strg PKR Set: Pressurize Comp. Strg to confirm Traveling Joint Fully Open; Stepwise Pressurization to set PKR @ 2693m / 2650psi; Comp. Strg Pull Test: Over Pull String 15 klbf – PKR Pull Test Ok; Shearing Expansion Joint: Slack-Off 20 klbf – Shear Expansion Joint Ok; Observation of Back Flow confirmed; Land TBG HGR In THS: Circulate Fresh Water Through T.H.S, Ensure Tie-Down Screws Open, Drain BOP Stack Via T.H.S Gate Valves, Lower TBG HGR And Land On Load Shoulder – Verified By Wt. Indicator & L.Joint Mark; Tighten All Tie-Down Screws; Close Hydrill On L.Joint, Pressure Test TBG HGR and

All Tie-Down Screws @ 1,000 Psi / 10 Min – Ok; L/U Surf Line, Final Press. Test: Press. Test Comp. Strg @ 6,000 Psi / 15 Min – Ok; B/O Surface Line.

P/U & Assemble SB Running & Pulling for Equalizing Prong match W/ 2.750" Plug of No-Go; RIH W/ SB Pulling & Ret. Prong; POOH To Surf.;

P/U & Assemble GS Pulling and Retrieve 2.750" Blanking Plug; POOH To Surface; Press. Test PKR & HGR Seal: L/U and Conn. Chiksan Pipes To T.H.S Side outlet Valve (Ann.), Stepwise Pressurization 2,000 Psi/10 Min – HGR Seals (Bottom) & PKR Element (Top) Ok; P/U & Assemble GS Pulling Tool for TRSSSV Protection Sleeve; RIH W/ GS Pulling and Ret. TRSSV Protection Sleeve; POOH To surface. Press. Test TWCV: Back Off L.Joint From TBG HGR & L/D Same; Run 2WCV and Screw in TBG HGR; L/U and Conn. Chiksan Pipes To BOP Side outlet Valve, Stepwise Pressurization Against Shear Rams @ 6,000 Psi/15 Min – Ok; N/D BOP.

N/U XMT BTM Master Valve; Install TBG HGR M.M.Seal, N/U TBG Head Adaptor Integrated W/ One 4-1/16" Gate Valve, meanwhile Pass 1/4" CL Thru. CL; Install 4-1/16" 10k Companion FLG On Tubing Head Adaptor; L/U Chiksan pipes and Test Line on Companion FLG, Press. Test M.M.Seal @ 6,000 Psi / 15 Min – Ok; Conn. 1/4" CL to Exit Block, Press. Test 1/4" CL To BTM Section & U-Ring @ 6,000 Psi / 15 Min – Ok; Cavity Press. Test Between S – Seal, T.H.S & T.B.G Adaptor Ring Gasket, 2nd TBG O-Ring, Tie-downs Screws, and Exit Port Thru. Test port @ 6,000 Psi / 15 Min – Ok; N/U Solid Block and Tree Cap; Open All XMT Valves, Conn. 4-1/16" Companion FLG to Kill Valve, Press. Test X-Mas Tree body @ 8,000 Psi / 15 Min – Ok; Release Rig 201 @ 1404.08.28 - 23:59

2.5 AZNS-166 Well Sketch

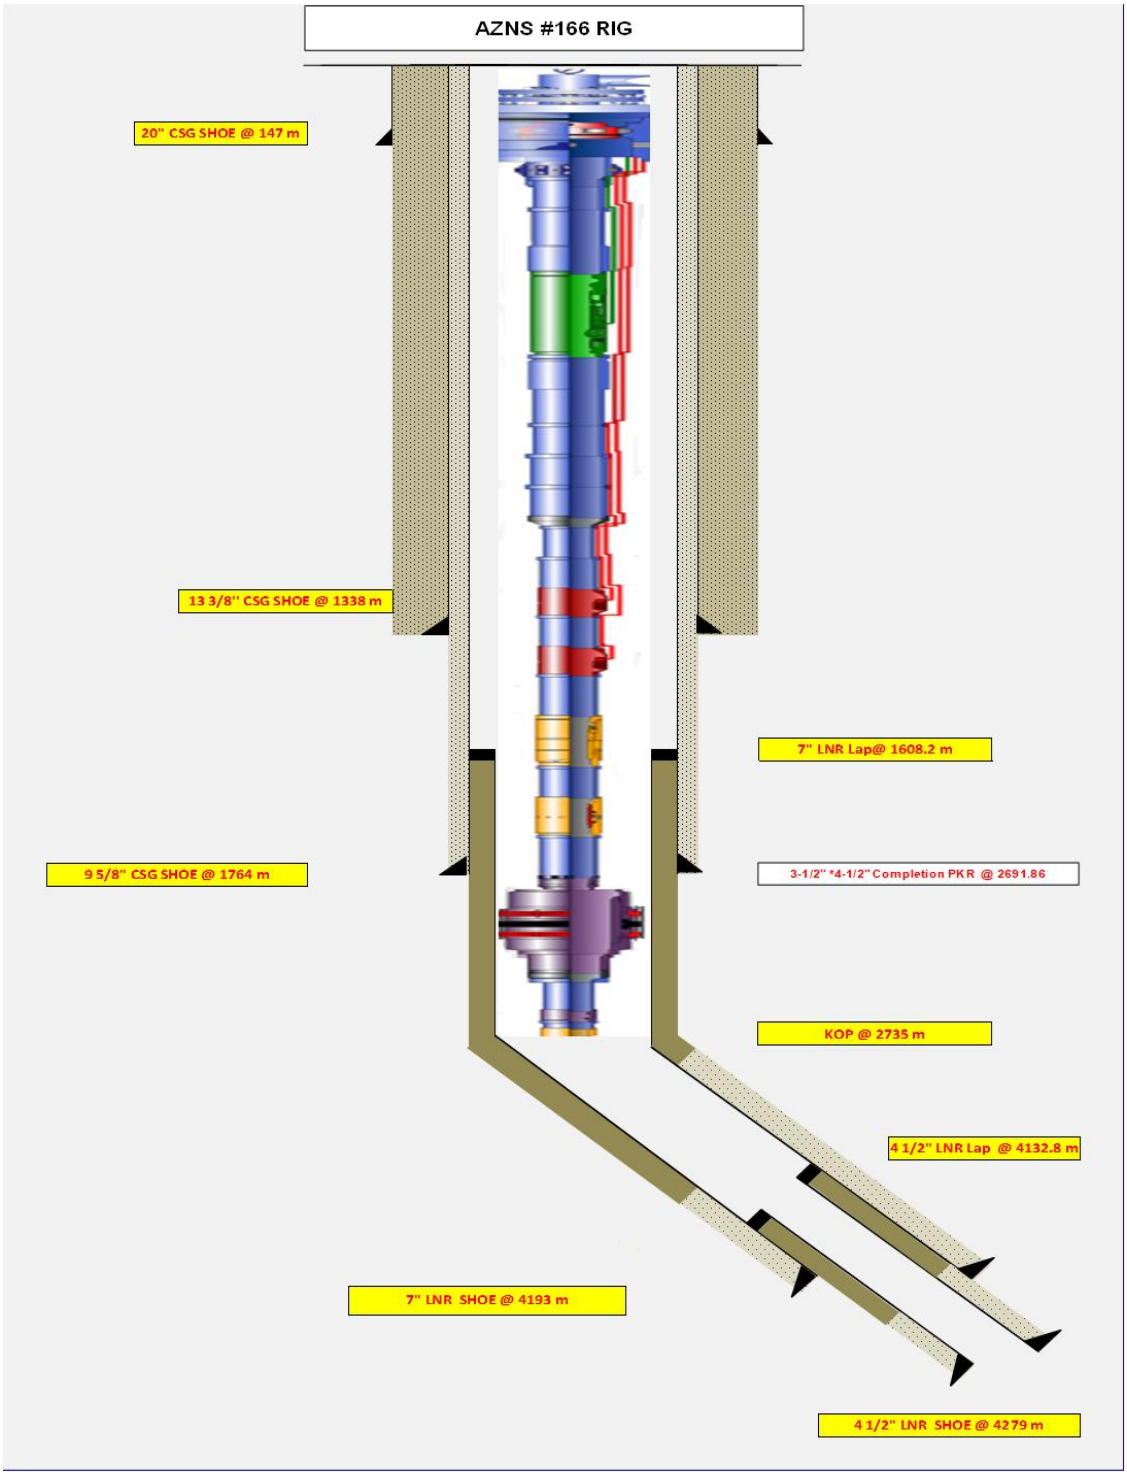


Figure 2-1: AZNS-166 Well Sketch

2.6 Daily Time Break Down

Work-Over Operation TBD of Well: AZNS-166 Work-over (Kazhdumi Producer)	IADC Code	Interval (meters)	Formation	Depth (meters)	ROP	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (%) 10	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Depth (meters)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)
			Work-over											Actual		
Check the wellhead for any damage or leakage. Record well head pressures; check all annulus pressure, Bleed off any annulus pressure to Zero.	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6	12	0.50	0.50
Retrieve BPV by lubricator and Observe well head pressure	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6	3	0.13	0.63
Close XMT valves, (Remove 7 1/16" XMT cap).	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6		0.00	0.63
R/u slick line, inspect and check the possibility of install secondary valve in SSSV. If not possible, proceed to operation by Rig	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6	3	0.13	0.75
Run lock open Tools and punch SSSV install Secondary valve and Test it. If not Successful, proceed to operation by Rig	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6		0.00	0.75
Retrieve the secondary valve then Run gauge ring to top of PLUG and retrieve Plug Note:If observe any obstruction Follow Contingency Plan#01 If successful, proceed to item 33	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6		0.00	0.75
If no success, try to retrieve by coiled tubing If successful, proceed to item 33	De-Completion		Kzh.	4279.6		Rig Less	0.00	0.0	0.0	0.0	0.00	0.0	4279.6		0.00	0.75
Held PJSM. Spud the Rig. Stand Back required 5" & 3-1/2" DPs, 5" HWDPs and 6-1/2" DC.	De-Completion		Kzh.	4279.6		0	0.00	0.0	0.0	0.0	0.00	0.0	4279.6		0.00	0.75
R/U SL,RIH & Try to open SSD,POOH to Surface.Note: If unable to open SSD Follow Contingency Plan#02	De-Completion		Kzh.	4279.6		24	1.00	1.0	1.1	26.4	1.10	1.1	4279.6		0.00	0.75
kill the well with proper Mud weight	De-Completion		Kzh.	4279.6		24	1.00	2.0	1.1	26.4	1.10	2.2	4279.6	6	0.25	1.00
Install BPV in Tubing Hanger. Note:Suitable BPV Shall be Provided by Client. Note:If Unable to set BPV Due to Damaged Profile, Install 3SV Blanking plug or Wire Line Bridge Plug	De-Completion		Kzh.	4279.6		24	1.00	3.0	1.1	26.4	1.10	3.3	4279.6	2	0.08	1.08
N/D BMW, N/U BOP, retrieve BPV Install TWCV, and perform BOP pressure test.	De-Completion		Kzh.	4279.6		60	2.50	5.5	2.8	66.0	2.75	6.1	4279.6	61.5	2.56	3.65
RIH with TBG hanger retrieving tool and engage with TBG hanger. Note:If Tubing Hanger Thread damaged follow Contingency Plan#03	De-Completion		Kzh.	4279.6		12	0.50	6.0	0.6	13.2	0.55	6.6	4279.6	1	0.04	3.69
Unlatch, Displace completion fluid & oil in hole with proper kill mud and pull completion string precautionary due to probable trapped pressure below plug & prong meanwhile POOH monitoring the well and annulus to make sure the well is safe and over balance. (from 2754m). Note:If unable to unlatch completion string due to string pack off with huge amount of debries follow contingency plan#04 Note:If unable to unlatch completion string due to string wash out follow contingency plan#05 Note: If observe any damage on THS, follow contingency plan#6	De-Completion		Kzh.	4279.6		130	5.42	11.4	6.0	143.0	5.96	12.6	4279.6	73	3.04	6.73
RIH with 8 ½" bit and clean out BHA (P/U DP's JT by JT) to 7" L.LAP (1608.2m), CBU, POOH.	Trip		Kzh.	4279.6		48	2.00	13.4	2.2	52.8	2.20	14.8	4279.6	33	1.38	8.10
RIH with 6 or 5-7/8" Mill to 2754m (P/U required DP jt by jt), Mill permanent packer, chase the packer to 4-1/2" L.L @ 4132.8m (or where ever PKR stopped), CBU, POOH.	Trip		Kzh.	4279.6		120	5.00	18.4	5.5	132.0	5.50	20.3	4279.6	69	2.88	10.98
RIH with Taper Tap and catch the packer, recover completion packer.POOH To Surface. Note:If string stuck while Recovering Completion Packer follow contingency plan#07	Trip		Kzh.	4279.6		72	3.00	21.4	3.3	79.2	3.30	23.6	4279.6		0.00	10.98

RIH with 5-7/8 Mill and clean out BHA to 4-1/2" Slotted Liner Lap @ 4132.8 m, CBU,POOH to Surface.	Trip		Kzh.	4279.6		48	2.00	23.4	2.2	52.8	2.20	25.8	4279.6		0.00	10.98
RIH with 3-1/2" Mill and clean out BHA to BTM, take care inside Slotted interval (4008m - 4068m) CBU shakers clean, POOH. Note:for Corrosion Logging inside 7" Liner follow contingency plan#8	Trip		Kzh.	4279.6		72	3.00	26.4	3.3	79.2	3.30	29.1	4279.6	55	2.29	13.27
M/U Tandem scraper BHA, RIH with tandem scrapers including 9-5/8" casing scraper & 7" liner scraper to 4130m. Scrap 9-5/8" casing and 7" liner and L/D same.	Trip		Kzh.	4279.6		0	0.00	26.4	0.0	0.0	0.00	29.1	4279.6		0.00	13.27
R/U TLC Logging, RIH & Perform Logging (Corrosion Logging) inside 7" Liner & 9-5/8" Casing,POOH to Surface.	Log		Kzh.	4279.6		0	0.00	26.4	0.0	0.0	0.00	29.1	4279.6		0.00	13.27
RIH scraper and scrape 7" production packer setting area, displace the well with completion fluid, POOH to surface.	Trip		Kzh.	4279.6		48	2.00	28.4	2.2	52.8	2.20	31.3	4279.6	73.5	3.06	16.33
RIH w/ DP's and DC's, POOH & L/D same.	Trip		Kzh.	4279.6		0	0.00	28.4	0.0	0.0	0.00	31.3	4279.6		0.00	16.33
Run 7.5K Kazhdumi completion string including CIV.	Completion		Kzh.	4279.6		168	7.00	35.4	7.7	184.8	7.70	39.0	4279.6	113.5	4.73	21.06
Set BPV inside TBH, N/D BOP's & install new XMT.	Completion		Kzh.	4279.6		48	2.00	37.4	2.2	52.8	2.20	41.2	4279.6	13.5	0.56	21.63
Retrieve BPV, install TWCV and Pressure test the XMT.	Completion		Kzh.	4279.6		18	0.75	38.2	0.8	19.8	0.83	42.0	4279.6		0.00	21.63
Secure the well by set BPV in TBG Hanger, close all X-mas Tree valves except BMV, and Release the Rig.	Completion		Kzh.	4279.6		8	0.33	38.5	0.4	8.8	0.37	42.4	4279.6	18	0.75	22.38
Retrieve BPV,R/U Slick Line, Set protection sleeve, retrieve plug & prong from NO GO landing nipple, POOH.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
RIH with CT to bottom, displace the well with diesel or nitrogen & observ well, POOH.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
R/U SL, RIH & retrieve protection sleeve, POOH, R/D SL.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
Flow the well as pre-acid clean up till acceptable BSW & reading stable flow rate on 2 different choke size for 72 hrs.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
R/U & RIH S.L, Set protection sleeve, POOH & R/D S.L RIH with C/T & perform acid wash as per program, POOH to surface. RIH w/SL and retrieve protection sleeve	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
Flow the well as post-acid clean-up till acceptable BSW & reading stable flow rate on 2 different choke size for min 96 hrs. Note 1: The time is only for flowing duration (R/U, R/D & preparation time is excluded). Note 2: Acidizing & post-acid clean-up maybe perform as rig less job upon contractor request & client approval but in case of any failure in well integrity the contractor should provide drilling rig & required services in own responsibility & fix the problem.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
RIH with S/L, set protection Sleeve, POOH & R/D SL.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
RIH with C/T to bottom & displace the well with diesel, POOH.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
RIH with S/L, install plug & prong into NO GO landing nipple, POOH.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
RIH with S/L, retrieve protection sleeve.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
Secure the well by set BPV in TBG Hanger, close all X-mas Tree valves except BMV.	Completion		Kzh.	4279.6		Rig Less	0.00	38.5	0.0	0.0	0.00	42.4	4279.6		0.00	22.38
Total Duration :							***38.5***	***38.5***			***42.4***	***42.4***				***22.4***
NOTE:																
Total Duration for Cut & Slip DL in all hole section.	Cut & Slip			3763		20	0.83	39.3	0.9	22.0	0.92	43.3	4279.6	2	0.08	22.46
Total Duration for Rig Service (Consider 0.5hr per day) in all hole section.	Rig Service			3763		21	0.88	40.2	1.0	23.3	0.97	44.2	4279.6		0.00	22.46
Total Duration of AZNS-166 Work-over Well:								40.2				44.2				***22.5***

Contingency Plans TBD of Well: AZNS-166 Work-over	IADC Code	Interval (meters)	Formation	Depth (meters)	ROP	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (%) 10	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Depth (meters)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)
Based on operation situation in each step, the following contingency plans might be followed																
Contingency plan #1: if observe any obstruction while each run w/ Gauge Cutter RIH w/CT and wash from obstruction depth to top of fish with Zylyne.	De-Completion		Kzh.	4279.6		120	5.00	5.00	5.5	132.0	5.50	5.5	4279.6	25	1.04	23.50
Contingency Plan#02 R/U & RIH W/Colliding Tools & Collide Completion String from Proper Depth,POOH & L/D, Displace well with heavy mud and try to kill the well,Circulate & Balance MW.	De-Completion		Kzh.	4279.6		240	10.00	15.00	11.0	264.0	11.00	16.5	4279.6		0.00	23.50
Contingency Plan#03 RIH w/Taper Tap & Try to tap in & engage w/Tubing Hanger	De-Completion		Kzh.	4279.6		48	2.00	17.00	2.2	52.8	2.20	18.7	4279.6		0.00	23.50
Contingency Plan#04 R/U & RIH with FPIT tools to check string free point,POOH to Surface & L/D.R/U & RIH W/Colliding Tools & Colide Completion String from Proper Depth,POOH & L/D.POOH Completion String from Colliding Depths in Several Runs.	Completion		Kzh.	4279.6		288	12.00	29.00	13.2	316.8	13.20	31.9	4279.6		0.00	23.50
Contingency Plan#05 Pull Completion String untill string will be part from weaker point then POOH & L/D String in Several attempt. It is assumed to part from 4- 1/2" expansion joint as weak point. Mill the remainder of fish & packer. Follow the rest of main plan.	Completion		Kzh.	4279.6		560	23.33	52.33	25.7	616.0	25.67	57.6	4279.6		0.00	23.50
contingency plan#06 : if observe any leakage and or failure on THS, secure the well by barriers (RTTS / CEMENT PLUG). Note:Proper Equipment shall be provided by client and install by contractor.	Trip		Kzh.	4279.6		240	10.00	62.33	11.0	264.0	11.00	68.6	4279.6		0.00	23.50
contingency plan#07 RIH w/5-7/8" or 6" Mill & Mill the Packer & Tail in Several Runs, POOH to Surface & L/D mill.	Trip		Kzh.	4279.6		240	10.00	72.33	11.0	264.0	11.00	79.6	4279.6		0.00	23.50
contingency plan#08 Perform Scraper Trip , RIH & Perform Logging (Corrosion Logging) Inside 7" Liner & 9-5/8" Casing,POOH to Surface.Stand Back required DPs, HWDPs and DC.	Trip		Kzh.	4279.6		336	14.00	86.33	15.4	369.6	15.40	95.0	4279.6		0.00	23.50
Total Duration of Contingency Plan AZNS-166 Work-over Well:								86.3				95.0				*23.5*


2.7 Activity Breakdown Table

Well Name:	AZNS-166, W.O.1	Oct-25				
CODE	Operation	27	28	29	30	31
1	Rig Up/ Tear Down / Move	12				
2	Drilling					
3	Reaming					
4	Coring					
5	Circulate & Condition					
6	Trips					
7	Service/ Maintain Rig					
8	Repair Rig					
9	Replacing Drill Line					
10	Deviation Survey					
11	Logging					
12	Run Casing/ Liner	12.00	3.00			
13	Cementing					
14	Wait on Cement					
15	Rig Up/Down BOP			6.00	12.00	
16	Test BOP				12.00	
17	Drill Stem Test					
18	Fishing					
19	Specialized Directional Work					
20	Operation Status (Waiting)					24.00
21	Safety					
22	Perforating					
23	Completion\ XMT		21.00	18.00		
24	Treating					
25	Swabbing					
26	Surface Testing					
27	Well Control					
28	Other					
29	Subsea Operation					
	Total	24.00	24.00	24.00	24.00	24.00


Well Name:	*AZNS-166, W.O.1*	*Nov-25*																	
CODE	*Operation*	*1*	*2*	*3*	*4*	*5*	*6*	*7*	*8*	*9*	*10*	*11*	*12*	*13*	*14*	*15*	*16*	*17*	*18*
1	Rig Up/ Tear Down / Move																		
2	Drilling																		
3	Reaming																		
4	Coring																		
5	Circulate & Condition							2.50				7.50	1.00						
6	Trips					21.00	21.50	21.50	24.00	24.00	22.00	14.50	23.00	18.50					
7	Service/ Maintain Rig																		
8	Repair Rig																		
9	Replacing Drill Line										2.00								
10	Deviation Survey																		
11	Logging																		
12	Run Casing/ Liner																		
13	Cementing																		
14	Wait on Cement																		
15	Rig Up/Down BOP																		7.50
16	Test BOP													4.50					
17	Drill Stem Test																		
18	Fishing																		
19	Specialized Directional Work																		
20	Operation Status (Waiting)	14.00	2.00		7.00	3.00	2.00					2.00			9.00	5.50	1.50		
21	Safety						0.50												
22	Perforating																		
23	Completion\ XMT	10.00	22.00	24.00	17.00									1.00	15.00	18.50	22.50	24.00	16.50
24	Treating																		
25	Swabbing																		
26	Surface Testing																		
27	Well Control																		
28	Other																		
29	Subsea Operation																		
	Total	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*	*24.00*

CODE	OPERATIONS	Actual Hours	Percentage
1	Rig Up/ Tear Down / Move	12.00	2.17%
2	Drilling	0.00	0.00%
3	Reaming	0.00	0.00%
4	Coring	0.00	0.00%
5	Circulate & Condition	11.00	1.99%
6	Trips	200.00	34.42%
7	Service/ Maintain Rig	0.00	0.00%
8	Repair Rig	0.00	0.00%
9	Replacing Drill Line	2.00	0.36%
10	Deviation Survey	0.00	0.00%
11	Logging	0.00	0.00%
12	Run Casing/ Liner	15.00	2.72%
13	Cementing	0.00	0.00%
14	Wait on Cement	0.00	0.00%
15	Rig Up/Down BOP	27.50	4.62%
16	Test BOP	16.50	2.99%
17	Drill Stem Test	0.00	0.00%
18	Fishing	0.00	0.00%
19	Specialized Directional Work	0.00	0.00%
20	Operation Status (Waiting)	70.00	12.68%
21	Safety	0.50	0.09%
22	Perforating	0.00	0.00%
23	Completion\ XMT	209.50	37.95%
24	Treating	0.00	0.00%
25	Swabbing	0.00	0.00%
26	Surface Testing	0.00	0.00%
27	Well Control	0.00	0.00%
28	Other	0.00	0.00%
29	Subsea Operation	0.00	0.00%
	Total	564.00	100.00%

2.8 Activity Break Down Chart

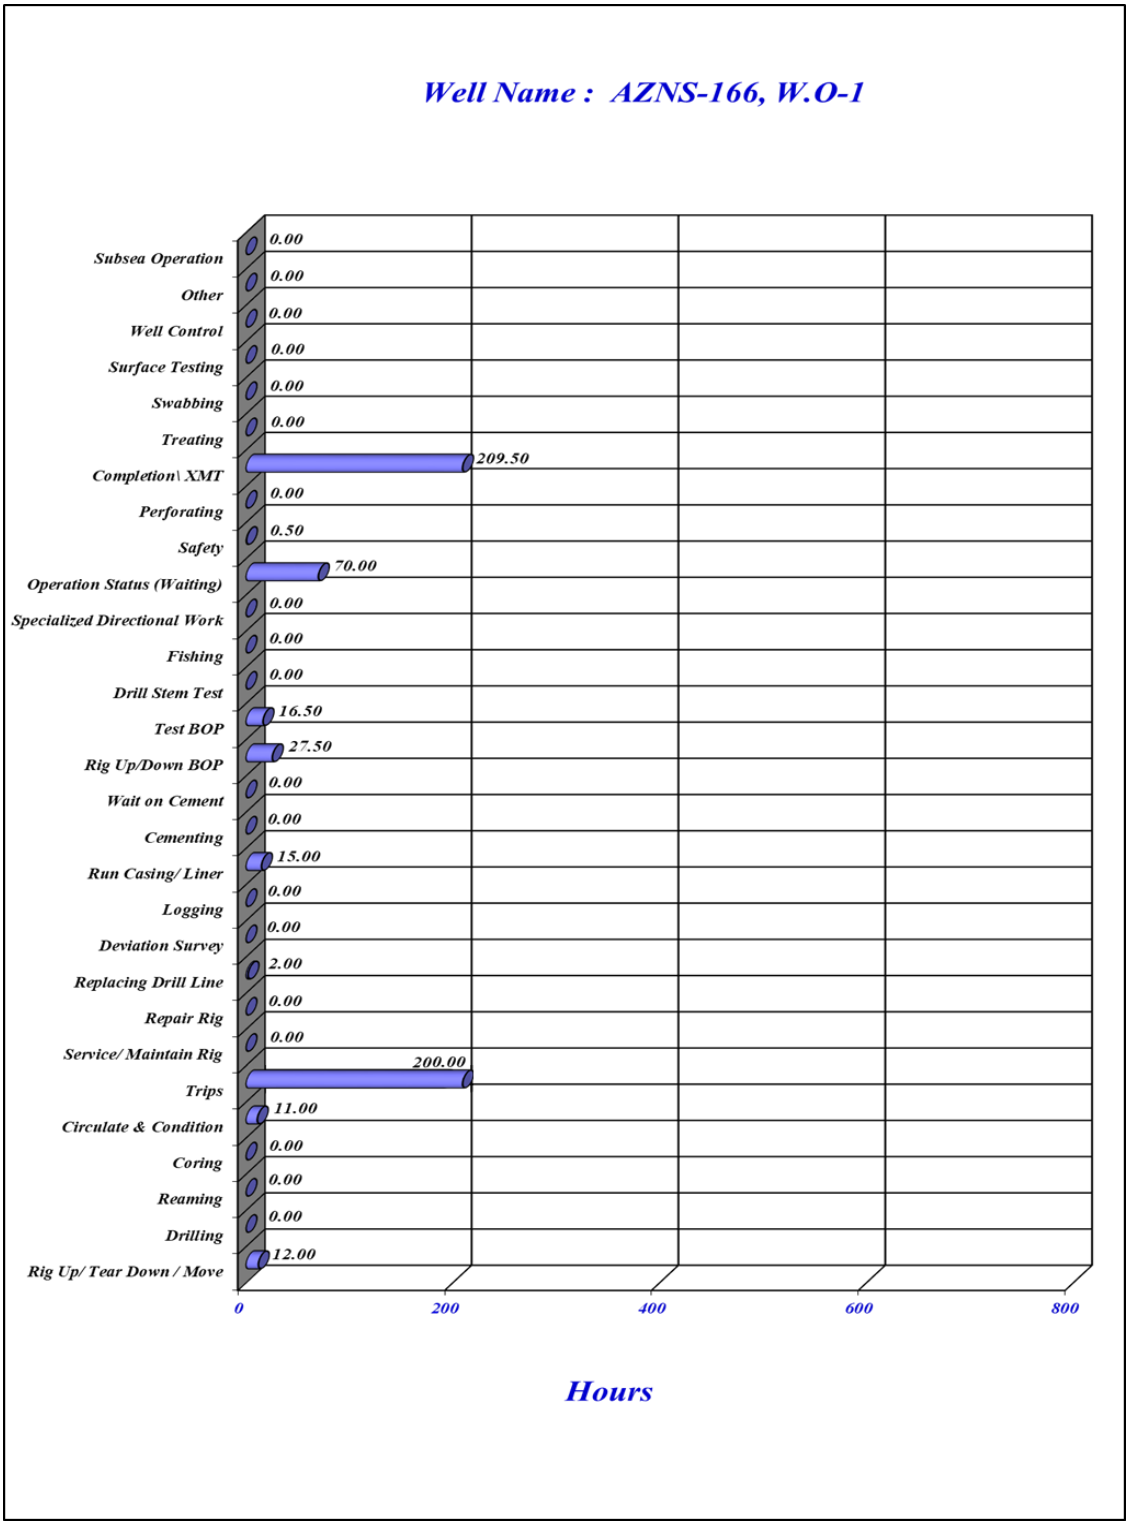

2.9 Activity Break Down Plot

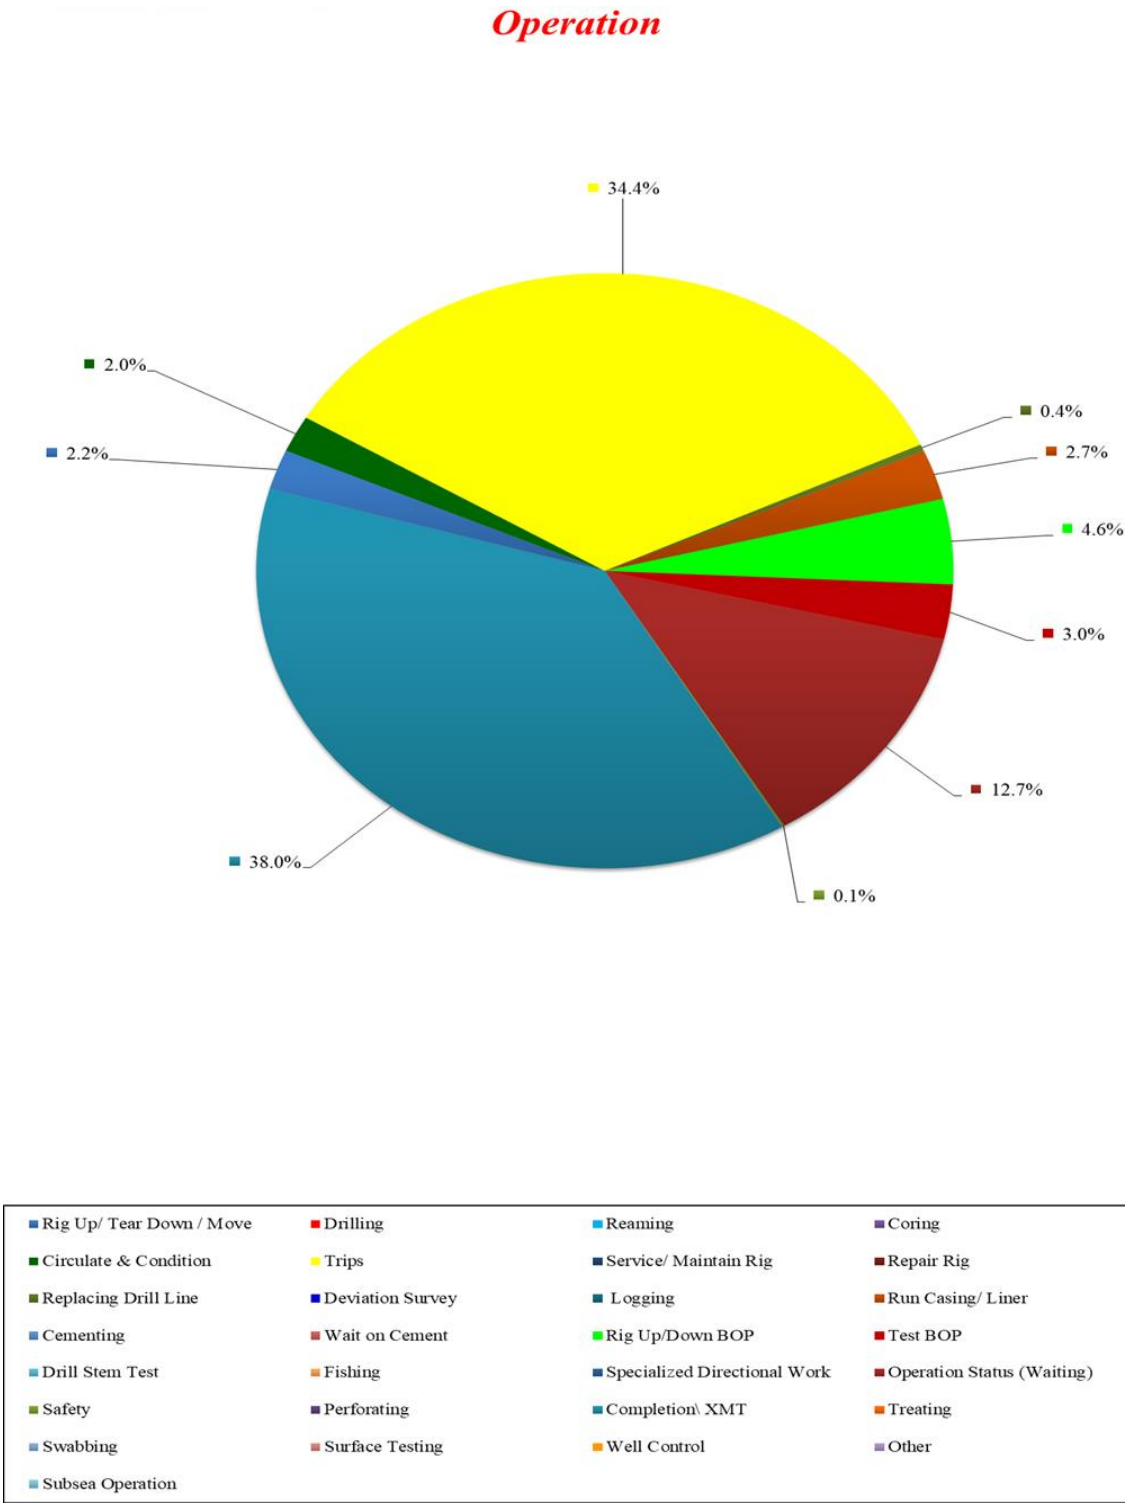

2.10 Bit Record Table

Not Applicable.

2.11 Hole Problem History

Not Applicable.

2.12 NPT Break-Down

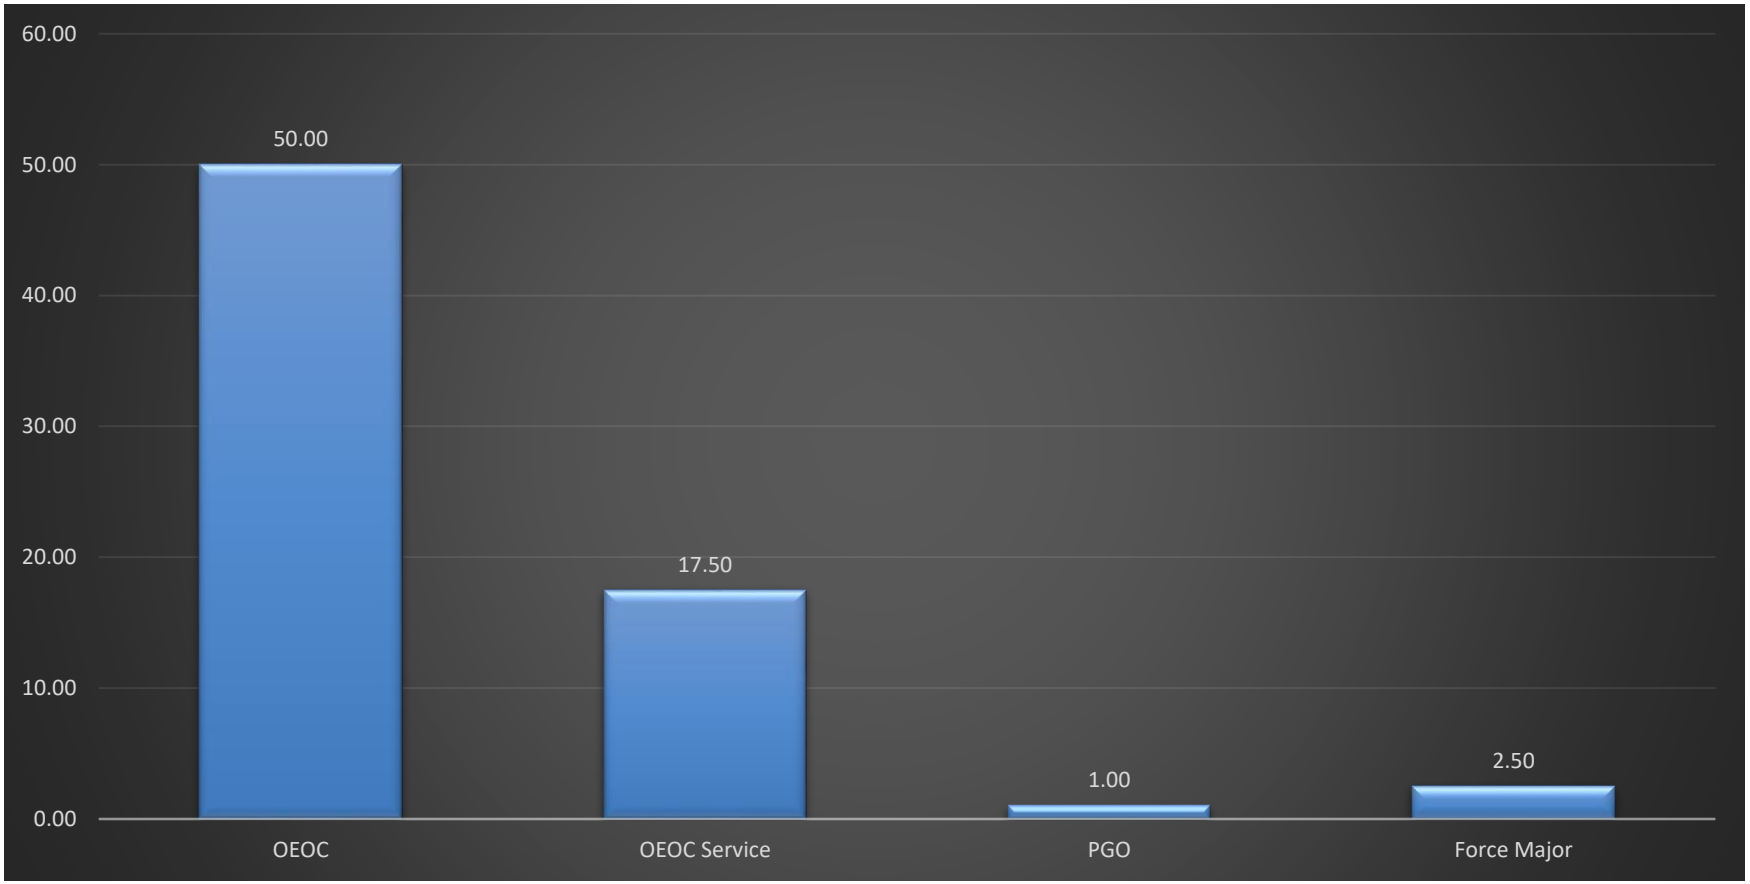


Figure 2-2: AZNS-166 NPT Break-Down Chart

Date	Start Time	End Time	NPT (hr)	DESCRIPTION	Company	Operation	Total NPT (hrs)
2025. Oct. 31	0:00	23:00	23.00	Delay in Operation	OEOC	BOP Test	23.00
	23:00	0:00	1.00	Due to failure wait indicator sensor	PGO		24.00
2025. Nov. 01	1:00	15:00	14.00	Kelly Hose Leakage	OEOC	De-Completion	38.00
2025. Nov. 02	23:00	24:00	1.00	Personnel Shortage of Drilling Fluid Crew			39.00
2025. Nov. 04	17:00	24:00	7.00	dDrilling Tools Failure		RIH	46.00
2025. Nov. 05	11:00	13:00	2.00	Delay in Operation		POOH TO SURF	48.00
	23:00	0:00	1.00	Delay in Operation		RIH to BTM	49.00
2025. Nov. 06	9:00	11:00	2.00	Delay in Operation			51.00
2025. Nov. 14	3:00	5:00	2.00	Jam system failure	OEOC Service	Completion	53.00
	15:00	0:00	9.00	Jam system failure			62.00
2025. Nov. 15	0:00	4:30	4.50	Jam system failure			66.50
	23:00	24:00	1.00	Bad Weather	-	-	67.50
2025. Nov. 16	0:00	1:30	1.50	Bad Weather	-		69.00
	19:00	21:00	2.00	Jam system failure / Delay in operation	OEOC Service	Completion	71.00

Table 2-4: AZNS-166 NPT Time BreakDown

3. Geological & Logging Reports

Not Applicable.

4. Bottom Hole Assembly Record

BHA No.				
Itme	Type	OD (in)	Length (m)	Cum. Length (m)
No. #1				
1	8-3/8" M.M.J. mill	8.375	1.14	1.14
2	Bit Sub	6.5	1.15	2.29
3	Scraper	9.625	1.63	3.92
4	D.C	6.5	26.05	29.97
5	HWDP	5	55.98	85.95

BHA No.				
Itme	Type	OD (in)	Length (m)	Cum. Length (m)
No. #2				
1	Junk Mill	6	0.93	0.93
2	Bit Sub	3.5	0.99	1.92
3	HWDP	3.5	247.67	249.59

BHA No.				
Itme	Type	OD (in)	Length (m)	Cum. Length (m)
No. #3				
1	Junk Mill	3.5	0.865	0.865
2	Bit Sub	1.125	1.23	2.095
3	D.C	1.125	139.42	141.515
4	D.P	2.875	56.725	198.24
5	X.O.S		1.17	199.41

BHA No.				
Itme	Type	OD (in)	Length (m)	Cum. Length (m)
No. #4				
1	Junk Mill	6	0.93	0.93
2	Bit Sub	3.5	0.99	1.92
3	HWDP	3.5	82.27	84.19
4	D.P	3.5	1271.505	1355.695
5	Double Pin		0.71	1356.405
6	Bit Sub		1.14	1357.545
7	Scraper	7	1	1358.545
8	X.O.S		0.25	1358.795

Table 4-1: AZNS-166 Bottom Hole Assembly

5. Casing Information

Casing Spec.	20"	K – 55, 94#, BTC	147^{m}
	13-3/8"	N – 80, 68#, BTC	1338^{m}
	9-5/8"	L – 80, 47#, PJE L – 80, 47#, TPCQ	1765^{m}
	7"	L – 80, 29#, TPCQ	1608.2 – 4193^{m}
	4-1/2" Non-Slotted	L – 80, 13.5#, BTC	4132.8 – 4199.27^{m}
	4-1/2" Slotted	L – 80, 13.5#, BTC	4199.27 – 4269.54^{m}
	4-1/2" Non-Slotted	L – 80, 13.5#, TPCQ	4269.54 – 4279.6^{m}

Table 5-1: AZNS-166 Final Casing Data

6. Cement Job Report

Not Applicable.

7. Completion Report

7.1 Completion Tubing Information

Tubing Size (in)	Weight (ppf)	Grade	Ultimate Strengths	Connection	Collapse Pressure (psi)	Burst Pressure (psi)	Interval (m)
4 – 1/2	18.9	L – 80	233^{klb}	HSM3	13830	13380	0 – 1503.299
3 – 1/2	10.2	L – 80	440^{klb}	HSM3	12120	11560	1503.29 – 2708.3

Table 7-1: AZNS-166 Tubing Data

7.2 Completion Tools Specification Checklist

Item	Equipment Description	
1	**CONTROL LINE "WEIQIXIN":**	
	THINKNESS:	0.065"
	WORK PRESSURE:	15000 PSI
	O.D.:	0.25"
	TYPE:	SEAMLESS
	MATERIAL:	INC 825
	LENGTH:	120 m/Roll
2	**UPPER FLOW COUPLING " WEIQIXIN" :**	
	OD:	**5.5"**
	ID:	3.640"
	THREADS:	4-1/2" 18.9 PPF, HSM3
	WORKING PRESSURE:	7500 PSI
	LENGTH:	6 FT
	MATERIAL:	9Cr1MO
	LOWER FLOW COUPLING " WEIQIXIN" :	
	OD:	5.550"
	ID:	3.640"
	THREADS:	4-1/2" 18.9 PPF, HSM3
	WORKING PRESSURE:	7500 PSI
	LENGTH:	4 FT
	MATERIAL:	9Cr1MO
3	**TUBING RETRIEVABL SAFETY VALVE " WEIQIXIN" :**	
	SETTING DEPTH:	61.978^{m}
	WORKING PRESSURE:	7500 PSI
	TEMPERATURE:	325 DEG F
	MAX O.D.:	7.5"
	MIN. I.D.:	3.437"
	PROFILE:	AF
	SELF-EQUALIZING FEATURE	HYDRAULIC CONTROL
	MATERIAL:	9Cr1MO
	THREADS:	4-1/2" 18.9 PPF HSM3
	PROTECTION SLEEVE	
	PROFILE	AF
	MIN ID	2.9"
4	**TRAVELING JOINT " WEIQIXIN" :**	
	STROKE LENGTH	10 FT

Item	Equipment Description	
	SHEAR PIN SET:	20000LB
	ELASTOMER:	AFLAS
	WORKING PRESSURE:	7500 psi
	TEMPERATURE:	300 DEG F
	TOOL OD:	5.315"
	TOOL ID:	2.922"
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	9Cr1MO
	TRANSFER TORQUE FEATURE	YES
5	**SLIDING SIDE DOOR " WEIQIXIN" :**	
	PROFILE:	X
	MAX.OD:	4.551"
	MIN ID:	2.750"
	PRESSURE RATING:	7500 PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	9Cr1MO
	OPEN METHOD	DOWNWARD OPEN
6	**COMPLETION PACKER " WEIQIXIN" :**	
	TYPE:	RETRIEVABLE
	CASING :	7" 29 PPF
	OD:	5.689"
	ID:	2.922"
	WORKING PRESSURE:	7500 PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	9Cr1MO
	ELEMENT MATERIAL:	AFLAS
7	**LANDING NIPPLE " WEIQIXIN" :**	
	PROFILE TYPE:	XN
	WORKING PRESSURE:	7500 PSI
	MAX O.D.:	4.5"
	SEAL BORE:	2.750”
	MIN ID:	2.441"
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	TEMPERATURE:	300 DEG F
	MATERIAL:	9Cr1MO
8	**RE-ENTRY GUIDE SHOE " WEIQIXIN" :**	
	OD:	4.5"
	MIN ID:	2.922"
	TOP CONNECTION	3-1/2" 10.20 PPF HSM3 BOX
	MATERIAL:	9Cr1MO

Table 7-2: AZNS-166 Equipment Checklist


Item	Name	Description
1	Tubing Hanger	11" BOWL x 4-1/2" 18.9 7.5K PPF & 4-1/2" 4-2G ACME WITH 4-1/2" EXTENDED NECK, WITH ONE CONTINUOUS 1/4" NPT C. LINE EXIT FOR SSSV, ONE 1/4" LINE EXIT FOR DHPG, INSTALLATION COMPLETE WITH RELATED FITTINGS AND PLUGS, C/W ALIGNMENT PREPATION FOR ESP. BPV: 4" TYPE H THREAD PREPARATION, THREE FS SEAL TO PACK OFF THE UPPER NECK AND TWO S SEAL TO PACK OFF THE BODY OF HANGER, MATERIAL: 410SS. M.C: FF-0.5 T.C: U PSL:3G PR:2 COMPANY: MSP
2	Fluted Adaptor	4 – 1/2" 18.9 PPF, L – 80 HSM3 PIN OD: 5.5'' ID: 3.64''

Table 7-3: AZNS-166 Equipment Checklist

7.3 Assembling Test Report


NOTE: Assembling & offline pressure tests of completion tools have been done on rig site in presence of client's representative.

Landing Nipple Test Report

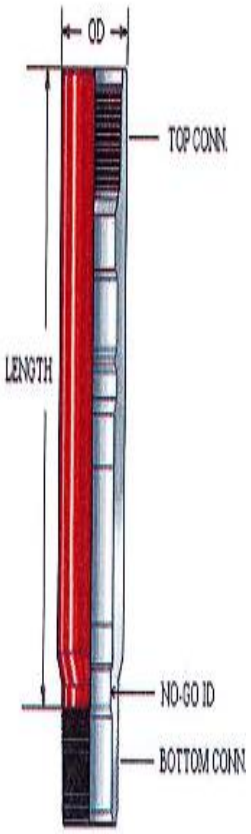

Type:	706W275-N25	
Serail Number:	2308 Y230706-01	
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX X PIN	
OD:	4.500"	
ID:	2.750"	
NO-GO ID:	2.635"	
Length:	0.374 m	
Material:	9CR1MO	
Profile:	XN	
Top Connection	Length:	1.990 m
6,000 Psi Blanking Plug Pressure No Drops in 15 Minutes	ok	
Well Name and Location:	AZNS-166	

Torque-Time Graph:

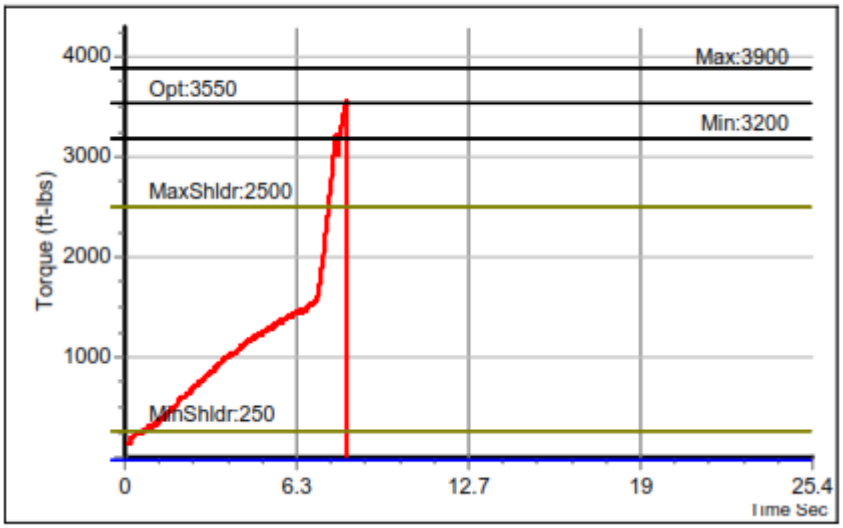

Torque-Time Graph:


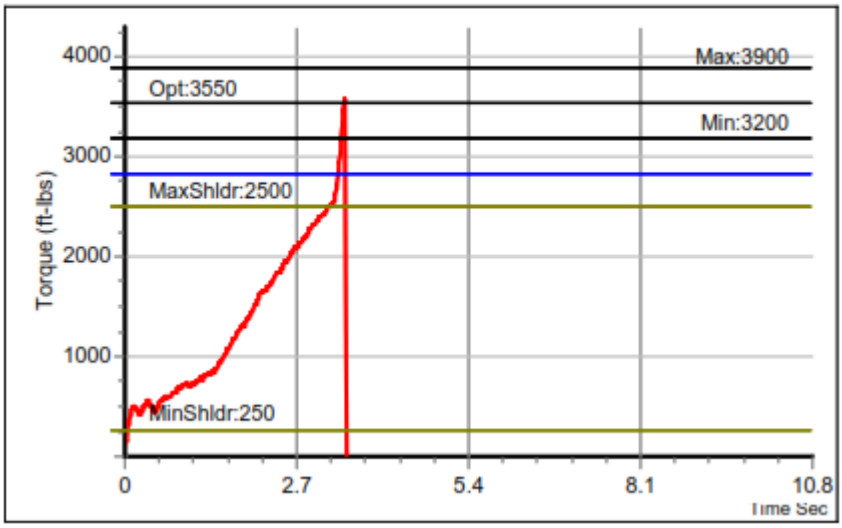



Figure 7-1 Mule Shoe – No-Go Connection

Hydraulic Set Retrievable Packer Test Report



Type:	665W150-060	
Serail Number:	2309 23087-01	
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX X PIN	
Working Pressure:	7,500 Psi	
OD:	5.910"	
ID:	2.922"	
Length:	2.679 m	
Material:	9CR1MO	
Temperature:	300 DEG F	
Element:	AFLAS	
Setting Pressure:	3,000 Psi	
Top Connection	Length:	1.905 m
Bottom Connection:	Length:	1.799 m
Well Name and Location:	AZNS-166	

Torque-Time Graph:

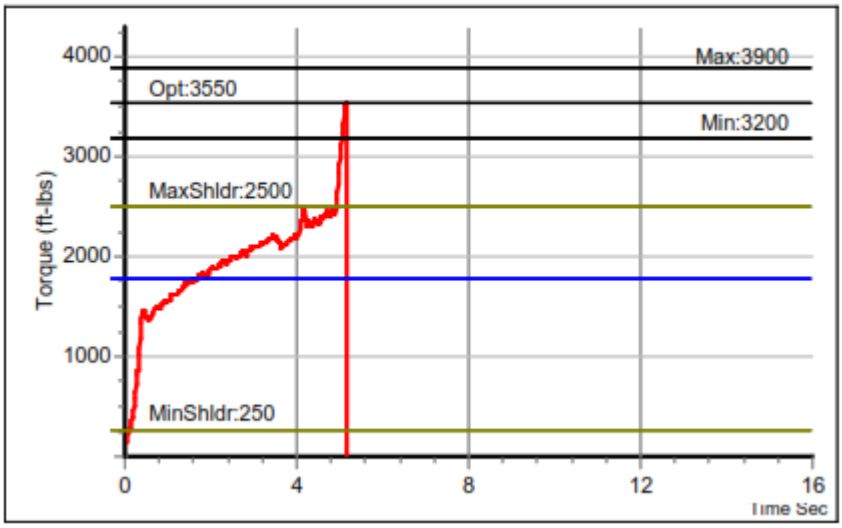

Torque-Time Graph:


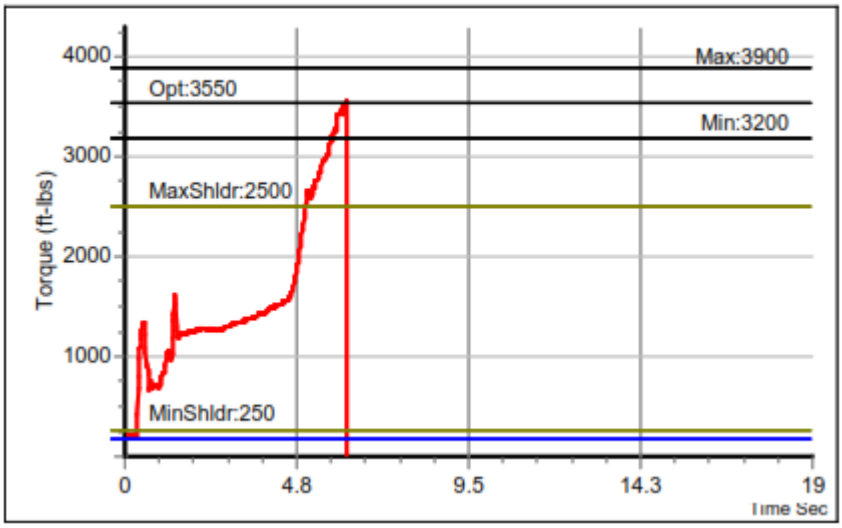



Figure 7-2 Packer Connection

Sliding Side Door Test Report

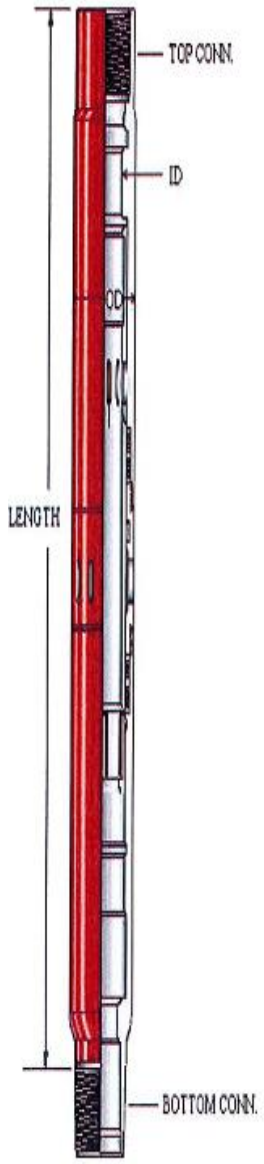

Type:	750W275-X40	
Serail Number:	2309 23090-03	
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX X PIN	
Working Pressure:	7,500 Psi	
OD:	4.551"	
ID:	2.750"	
Seal Bore ID:	2.750"	
Length:	1.195 m	
Temperature:	300 DEG F	
Material:	9CR1MO	
Profile:	X	
Shifting Direction:	DOWNWARD OPEN	
Top Connection	Length:	1.839 m
Bottom Connection:	Length:	2.174 m
6,000 Psi Pressure No Drops in 15 Minutes	ok	
6,000 Psi Check Valve Pressure No Drop in 15 Minutes	ok	
Well Name and Location:	AZNS-166	

Torque-Time Graph:

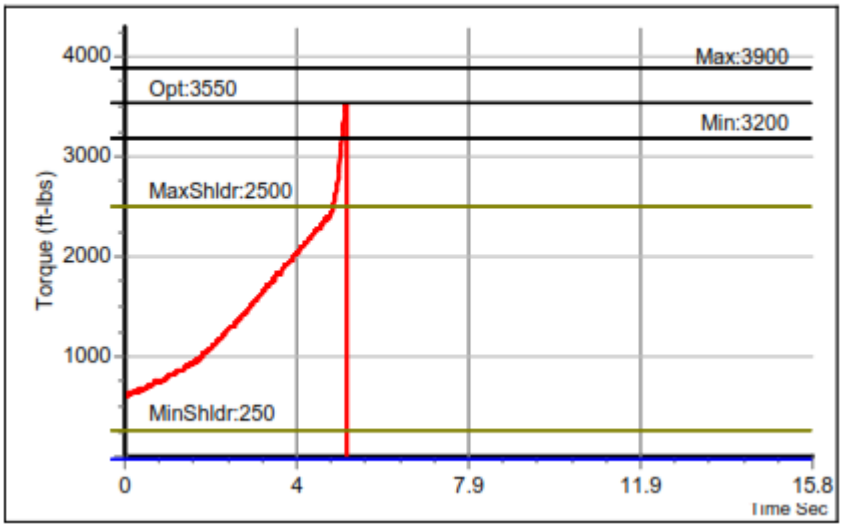

Torque-Time Graph:


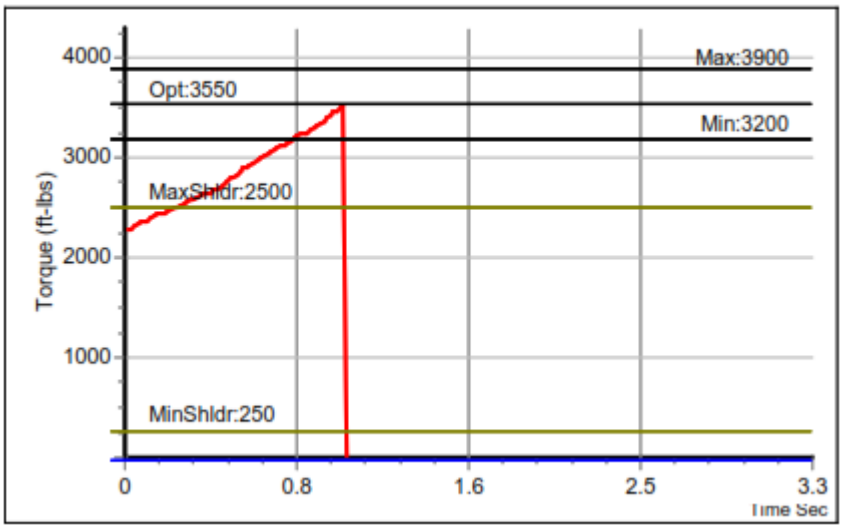



Figure 7-3 SSD Connection

Expansion Joint Test Report

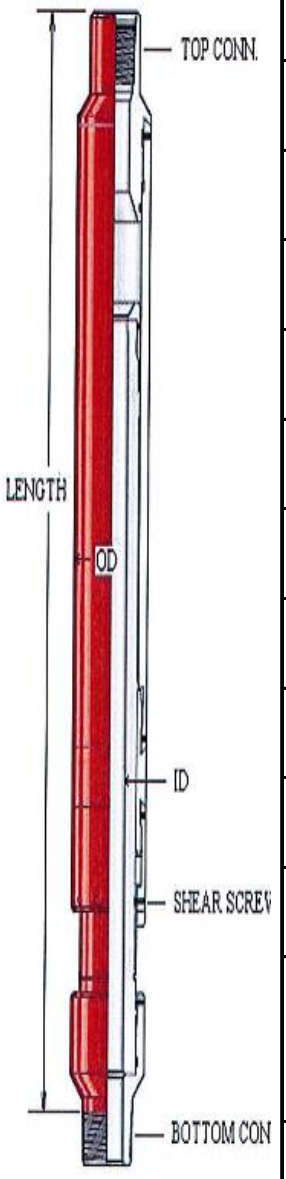

Type:	370W350-031	
Serail Number:	2308 23086-03	
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX X PIN	
Working Pressure:	7,500 Psi	
OD:	5.315"	
ID:	2.922"	
Length:	7.320 m	
Material:	9CR1MO	
Shear Screw:	3	
Top Connection	Length:	1.930 m
Bottom Connection:	Length:	1.877 m
6,000 Psi Pressure No Drops in 15 Minutes	ok	
Well Name and Location:	AZNS-166	

Torque-Time Graph:

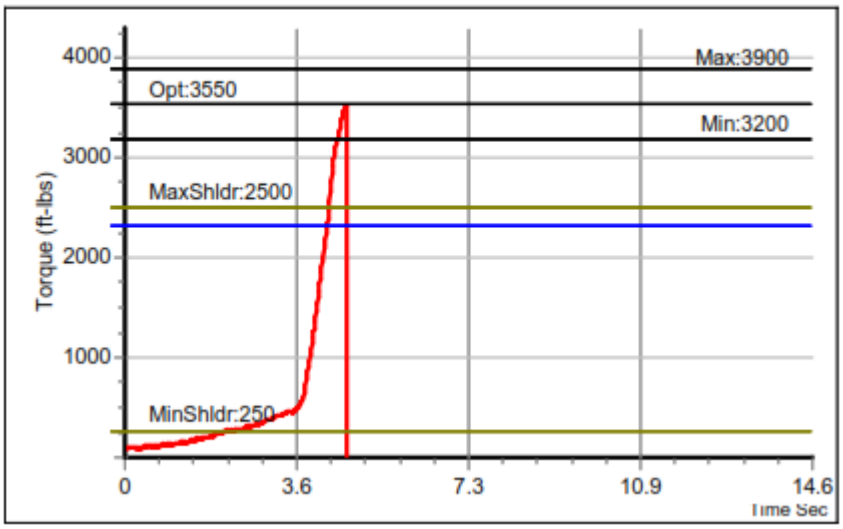

Torque-Time Graph:


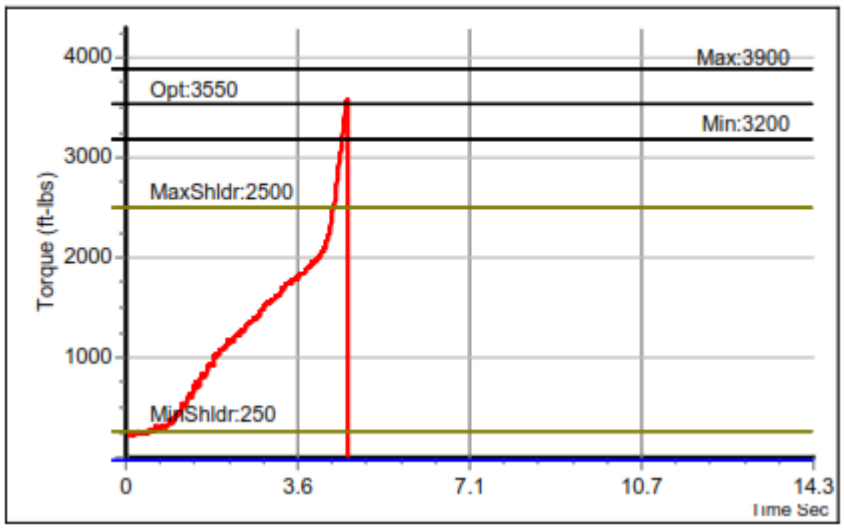



Figure 7-4 EXP. Joint Connection

SCSSV Test Report




Type:	208W343-AF03	
Serail Number:	2308 23089-03	
Connection Size:	4-1/2" 18.90 PPF HSM3 BOX X PIN	
Working Pressure:	7,500 Psi	
OD:	7.500"	
ID:	3.437"	
Length:	1.783 m	
Material:	9CR1MO	
Hydraulic Control Pressure:	Full Open	Full Close
	1800 PSI	00 Psi
6,000 Psi Hydraulic Control Pressure No Drop in 15 Minutes	ok	
6,000 Psi Pressure No Drops in 15 Minutes	ok	
6,000 Psi flapper Pressure No Drop in 15 Minutes	ok	
Top Connection	Length:	1.917 m
Flow Coupling UP:	Serial Number:	2308 Y230704-03
	Length:	1.725 m
Flow Coupling Down:	Serial Number:	2308 Y230705-02
	Length:	1.118 m
Bottom Connection:	Length:	1.996 m
Well Name and Location:	AZNS-166	


Torque-Time Graph:

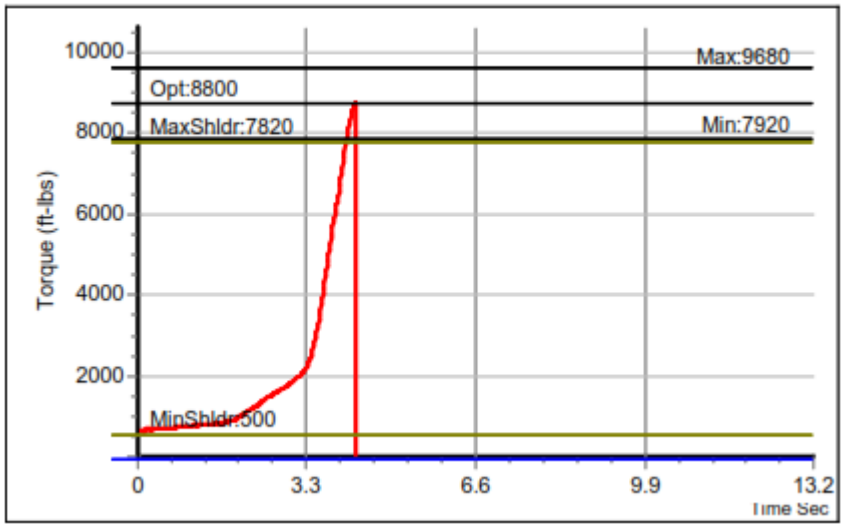

Torque-Time Graph:

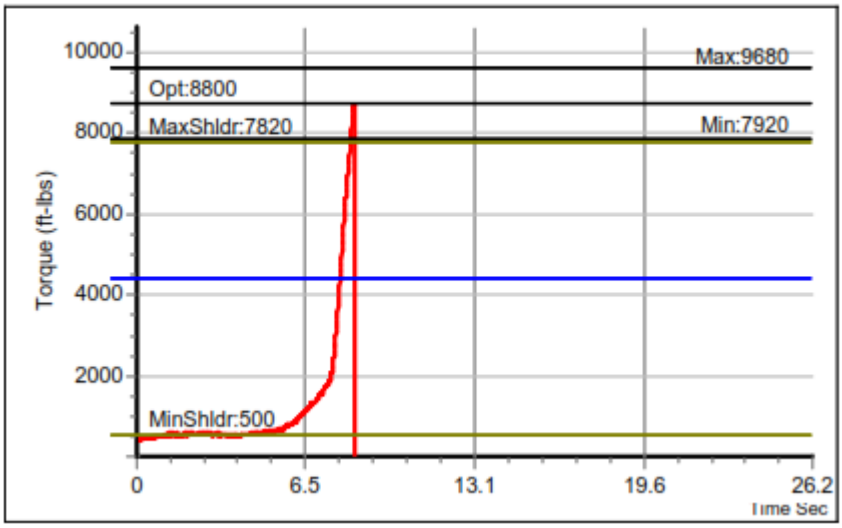

Torque-Time Graph:

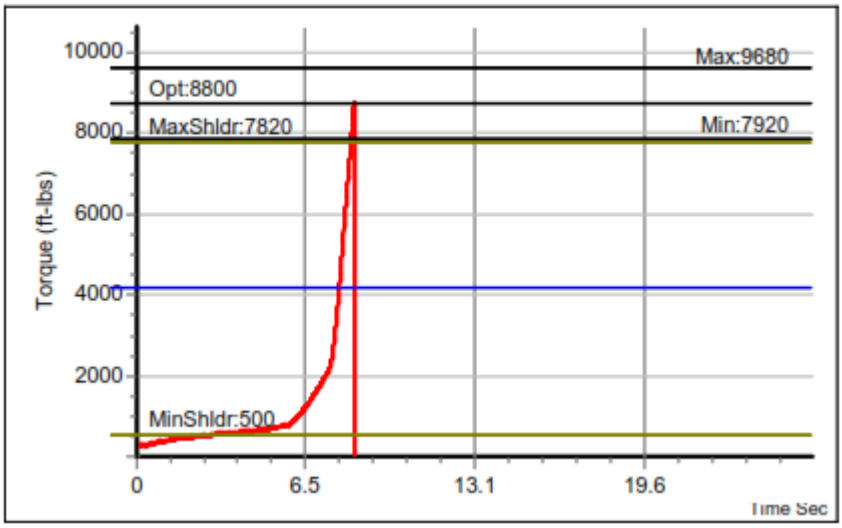

Torque-Time Graph:

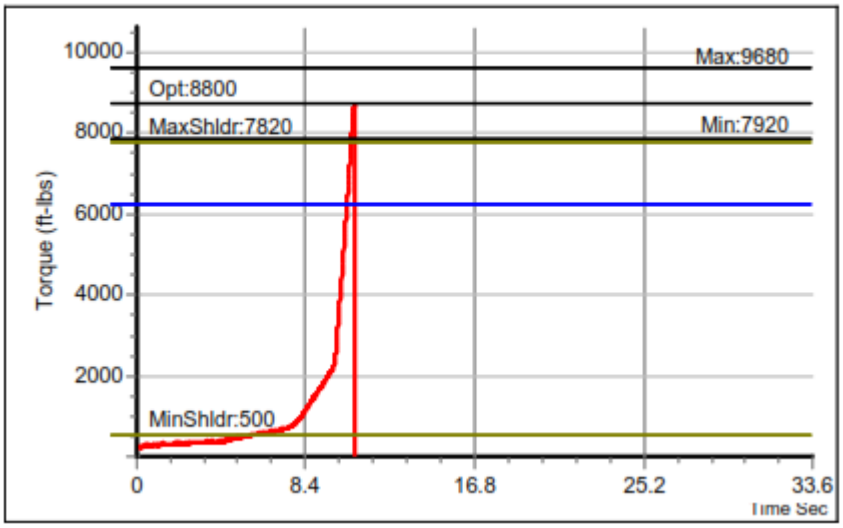


Figure 7-5 TRSSSV Connections

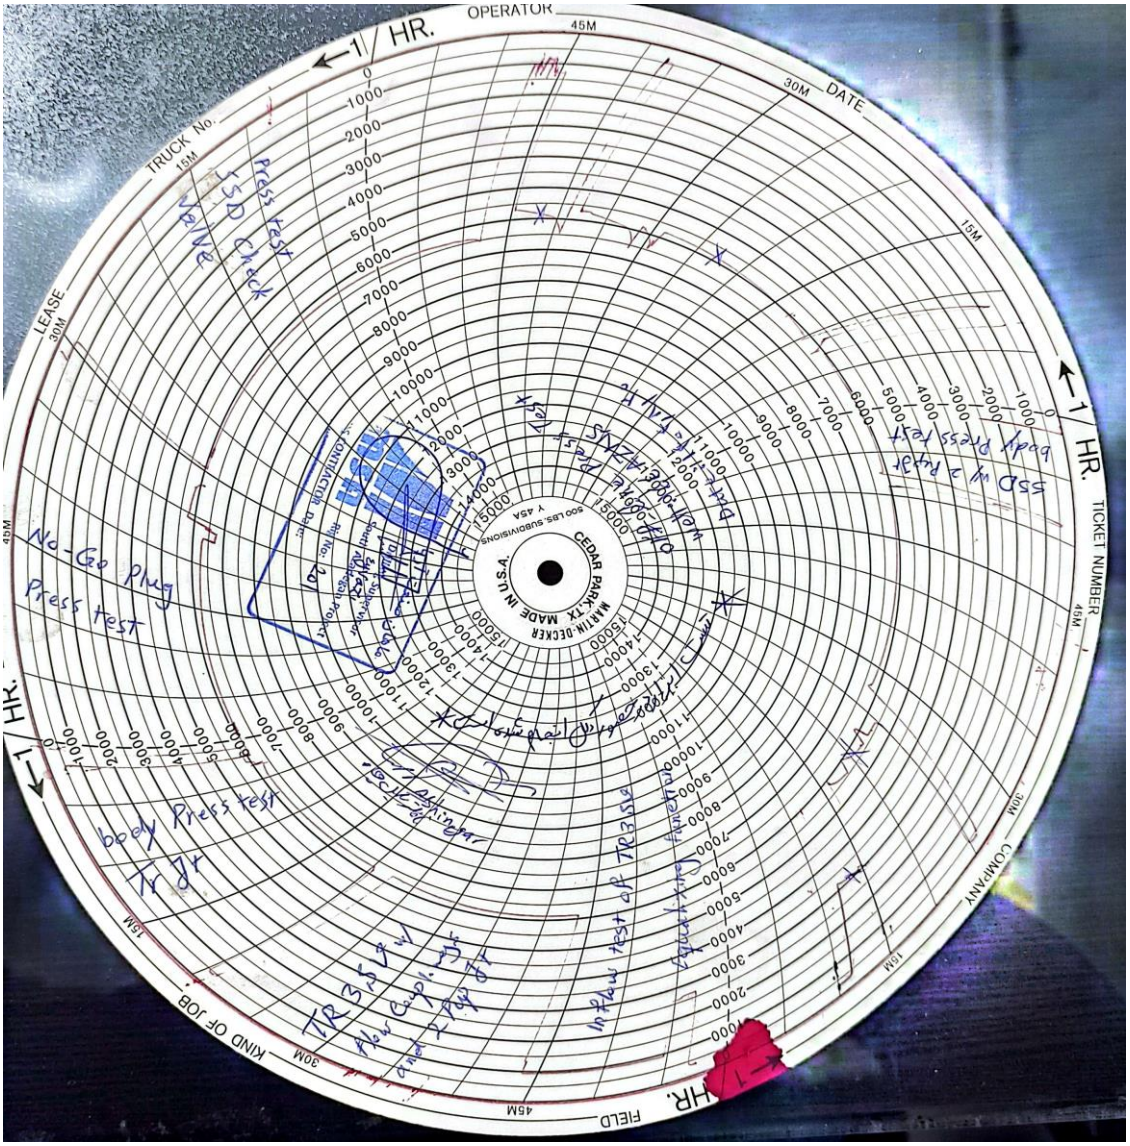


Figure 7-6 Completion Equipment Offline Pressure Test

7.4 Completion Operation Checklist

Item	Operation Name	Remark	Check Mark✓
1	Scraper Trip	Packer depth should be scraped	√
2	Pre-job preparation	Pre-connection All Down Hole Equipment With Upper & Lower Pup Joints On Confirmed Thread-makeup at Workshop, And Pressure Test Prior To Being Transported To Well Site.	X
		Retrieve Wear Bushing, M/U Jet Sub And Flush Bop Stack & Well Head With Fresh Water.	√
		All Crossovers, Pup Joints For Space Out Measured Put In Right Place.	√
		Lift Control Line And Protectors On Rig Floor.	√
		Hold A Pre-Job Safety Meeting For Running Upper Completion String.	√
3	Assembling and RIH	M/U 3-1/2" Re-entry Guide Shoe And 3-1/2" BTM No Go Landing Nipple	√
		Check The Conditions Landing Nipple To Make Sure There Is No Damage, Observe There Is No Any Trash Trapped Inside.	√
		Assemble Landing Nipple.	√
		RIH 1 Joint Tubing As Per Tally	√
		P/U And M/U Hydraulic-Set Retrievable Production Packer.	√
		Much More Care Should Be Taken When Packer Is Passing Well Head And Liner Hanger While RIH,	√
		Slack Off Packer Assembly, Double Check The Quantity Of Shear Pins, Remove The Tape On The Element, Check If Any Damages On It.	√
		RIH 1 Joint Tubing As Per Tally	√

		M/U Pup Joint And SSD (close Position) To Tubing String With check valve Inside.	√
		Pressure Test Tubing String 6000psi/15min Every 100 JTs.	√
		RIH Completion String and M/U traveling joint as per running tally.	√
		Cont. Running Tubing as per Tally.	√
		M/U TRSSSV	√
		Install control line to TRSSSV and pressure test control line 6000psi x 15mins. And then keep 3000psi pressure while running to ensure TRSSSV open. Install TRSSSV protector for the 1/4” control line. Continue to run 4-1/2” tubing as per running tally.	√
4	M/U and Space out Tubing Hanger	Pick up & M/U tubing hanger with double pin crossover. M/U landing joint. Check string weight upward and downward.	√
		Roughly cut control line about 2 meters above tubing hanger, wrap 2-3 turns and then feed through Tubing Hanger.	√
		Check string weight upward and downward and Space out Tubing Hanger 1.5 m (Half stroke) above tubing head spool	√
5	Set production packer	R/Up Slick Line. Remove Check valve inside SSD	√
		RIH and Set check valve in Landing Nipple. POOH to surface.	√
		Pressurize inside tubing to 500psi to ensure traveling joint is full open. Increase Pressure gradually to SET PACKER. Increase pressure to 6000psi to Test String.	√
6	Land Tubing	Move down completion string and apply required weight to shear traveling joint load pins and Land Tubing hanger in T.H.S. Slack off completely &	√

	hanger	Record the weight.	
		Drain the BOP stack through the gate valves of tubing head before landing hanger in THS. Leave the valves open.	√
		Tie Down Screws on THS should be fully open before Operation	√
7	N/D BOP & N/U X-mas tree	Tighten tie down screws.	√
		Test inside string w/ 6000 psi, 15 min.	√
		R/Up Slick Line. RIH with slick line and Ret. Check valve from Landing Nipple. POOH to surface.	√
		Test Annulus w/ 2000 psi 15min.	√
		Close BOP ram and test above tubing hanger (annulus between BOP and landing joint) to 1000psi.	√
		B/O & L/D landing joint.	√
		Set 4” 2Way in TBG Hanger & Test it, Back off and L/D Running Tool.	√
		N/D BOP.	√
		Feed control line, through head bonnet.	√
		Check hanger for any damage and pressure test control line to 4500psi	√
		Pressure test chemical injection line & rapture the disc after installing Bonnet.	-
		N/U x-mass tree as program.(Bottom Master)	√
		Perform required tests for X-mass tree. (Bottom Master)	√
		Connect from X-mass tree kill valve to the pump unit and test X-Mas tree body to 1000/6000 psi for 15 min against TWCV.	√
		Remove 4" two way, install 4" one way	√

		Close TRSSSV	√
		Release the rig. Clean the well site.	√

Table 7-4: AZNS-166 Operation Checklist

7.5 Well Head and X-mass tree Specification (installed)

Well Type	Specification	Check and Remark
Well Head 10000 Psi for Kazhdumi Wells	**TUBING HEAD ADAPTOR** BOTTOM STUDDED FLANGE 11", 10000 PSI, BX158 TOP STUDDED FLANGE 4-1/16" 10000 PSI BX155 FULL BORE PREPARED WITH TWO S-SEAL AND ONE METAL TO METAL SEAL TO PACK TOP NECK OF TUBING HANGER C/W RELATED TEST AND INJECTION PORTS PREPARTION. C/W TWO CONTINUOUS FEED THROUGH TYPE 1/4" NPT CONTROL LINE EXITS PREPARTION (ONE FOR 1/4" TRSSSV CL AND ONE FOR 1/4" DOWNHOLE PRESSURE GAUGE) AND TWO 3/8" NPT CONTINUOUS FEED THROUGH TYPE LINE PORTS FOR CHEMCIAL INJECTION LINE EXIT INCLUDING RELATED SWAGE LOCK FITTINGS C/WITH ONE 4-1/16", 10K WP FULL BORE MANUAL GATE VALVE FORGED BODY AND BONNET, ALLOY STAINLESS STEEL 410SS GATE & SEAT AISI 410 COATED WITH TUNGSTEN CARBIDE USING HVOF METHOD STEM: INCONEL 718 WITH BACK SEAT CAPABILITY, NON RISING STEM METAL TO METAL SEAL BETWEEN SEAT AND GATE C/W HAND WHEEL FORGED BODY ALLOY STEEL AISI 410 MAXIMUM HEIGHT: 800MM M/C: FF-0.5 T/C: U PSL:3G PR:2 CROSS T-TYPE SOLID BLOCK CROSS T-TYPE SOLID BLOCK, BOTTOM FLANGED 4-1/16" API 10000 PSI WP TOP FLANGED STUDDED 4-1/16" API 10000 PSI WP FOR TREE CAP WITH TWO STUDDED SIDE OUTLETS 4-1/16" 10000PSI WP ELEVATED AT 900 DEG AND TWO 4-1/16", 10000 PSI MANUAL GATE VALVE AT THE TOP AND BOTTOM AND ONE 4-1/16", 10000 PSI WP SAFETY VALVE EQUIPPED WITH HYDRAULIC WIRE CUT	

	ACTUATOR AS UPPER MASTER VALVE MATERIAL OF BODY, BONNET: AISI 410 SEAT, GATE: AISI 410SS HARD FACED WITH TUNGSTEN CARBIDE UASING HVOP METHOD MATERIAL OF STEM: INCONEL 718 M/C: FF-0.5 T/C: U PSL:3G PR:2G. MANUAL GATE VALVE API 4-1/16" 10000 PSI WP. FLANGED ENDS AND FULL BORE METAL TO METAL SEAL BETWEEN BODY/SEAT/GATE WITH BACK SEAT CAPABILITY, NON RISING STEM C/W HANDWHEELS MATERIAL OF BODY, BONNET, SEAT, GATE: AISI 410SS MATERIAL OF STEM: INCONEL 718 GATE&SEAT HARD FACED WITH TUNGSTEN CARBIDE BY HOVF METHOD M/C: FF-0.5 T/C: U PSL:3G PR:2 X-MAS TREE CAP 4-1/16" API 10000 PSI WP, FLANGED BOTTOM (4-1/16", BORE) 8-3/8"-4ACME-2G THREAD TOP, BLANKING PLUG TAPPED WITH 1/2" NPT THREAD, FORGED BODY, MATERIAL: STAINLESS STEEL 410 M/C:FF-0.5 T/C:U PSL:3G PR:2	

7.6 Completion Sketch & Tally

Contractor		Completion Well Schematic AZNS-166				Client				
		Liner & Tubing Data								
Field	AZADEGAN	Description	7" Liner	4.5" Liner		3 1/2" Tubing	4 1/2" Tubing	Perforation	7" Liner Lap	1608.2
Well Number:	AZNS-166	OD[in]	7	4.5		3.5	4.5			
Rig :	OEOC-201	Nominal weight [lb/ft]	29	13.5		10.2	18.9		4.5" Liner Lap	4132.8
RTE-GLE	3.95	Grade	C-75	L-80		L-80	L-80	4199.3 - 4269.54	4.5" Liner Shoe	4279
RTE-THF	12.95	Thread	TPCQ	BTC		HSM3	HSM3		Total Depth:	4279
Rig Spudded Date :	1404.08.05	Inside diameter [in]	6.184	3.92		2.92	3.64		X-mass Tree:	4-1/16"
End of Operation	1404.08.28	API Drift Diameter	6.059	3.795		2.8	3.515		Size & Rating:	10K


Schematic		Description	Max OD	Min ID	Length (m)	BTM(m)	TOP(m)
		Elevation (floor - TBG Head Flange)					
	1	TBG HANGER MSP/Drilex, 7.5K, 11" X 4 1/2" ACME Box up, L-80 18.9#, M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type "H" Two Way (Min Bore: 3.68")	11	3.68	0.531	10.608	9.847
	3	4-1/2" Fluted swage adapter D/P, 18.9# 9CR1MO, WEIQIXIN Co	5.5	3.64	1.018	11.626	10.608
	4	5 JOINTs TUBING 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	46.71	58.336	11.626
	5	Pup Jt 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	1.917	60.253	58.336
	6	4-1/2" Flow Coupling,18.9#, 9CR1MO, HSM3, 6' ft, WEIQIXIN Co	5.5	3.64	1.725	61.978	60.253
	7	4 1/2" TRSSV Tubing Retrievable Saftey Valve, 18.9# w/ 3.437" Seal bore, HSM3, 9CR1MO, 7.5K WP w/ AF Profile, Flapper Type, WEIQIXIN Co	7.5	3.437	1.783	63.761	61.978
	8	4-1/2" Flow Coupling, 18.9#, 9CR1MO, HSM3, 4' ft, WEIQIXIN Co	5.5	3.64	1.118	64.879	63.761
	9	Pup Jt 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	1.996	66.875	64.879
	10	151 JOINTs TUBING 4-1/2"HSM3 18.9#, L-80	5.118	3.64	1455.482	1503.299	66.875
	11	X-over 4-1/2"HSM3, 18.9# BOX * 3-1/2"HSM3 , 10.2# PIN,	5.25	2.922	1.124	1504.423	1503.299
	12	123 JOINTs TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	1152.059	2656.482	1504.423
	17	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.93	2658.412	2656.482
	18	3-1/2" EXP. Jt,HSM3 , 9CR1MO, 10' STK (Fully Open) Splind Rotational Lock System Any Position, Shear Pin Set 15 Klbs, WEIQIXIN Co	5	2.922	5.76	2664.172	2658.412
	19	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.877	2666.049	2664.172
	24	3-1/2" TBG, 10.2#, L-80,HSM3	4.25	2.922	9.358	2675.407	2666.049
	17	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.839	2677.246	2675.407
	18	3-1/2" Non-Elastomeric Sliding Side Door, 9CR1MO, HSM3 w/ Type X Selective profile (Profile: 2.750" X, Downward open), 7.5K	5	2.75	1.195	2678.441	2677.246
	19	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	2.174	2680.615	2678.441
	24	3-1/2" TBG, 10.2#, L-80,HSM3	4.25	2.922	9.346	2689.961	2680.615
	21	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.905	2691.866	2689.961
	22	7" 29# CSG Hydraulic set retrievable production packer to be run in 7.00" 29 PPF CSG, WEIQIXIN Co	5.315	2.922	2.679	2694.545	2691.866
	23	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.799	2696.344	2694.545
	24	3-1/2" TBG, 10.2#, L-80,HSM3	4.25	2.922	9.345	2705.689	2696.344
	25	3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.99	2707.679	2705.689
	26	3-1/2" BTM No-Go LND Nipple, HSM3, 10.2#, 9CR1MO, Seal Bore 2.750" TYPE XN, WEIQIXIN Co, 7.5K	4.551	2.75	0.374	2708.053	2707.679
	27	3-1/2" Wireline Re-Entry Guide, 10.2 #, HSM3, 9CR1MO, WEIQIXIN Co	4.25	2.922	0.247	2708.3	2708.053
		END OF COMPLETION STRING				2708.3	
Tubing Retrievable Saftey Valve						63.761	61.978
Traveling Joint						2664.172	2658.412
SSD						2678.441	2677.246
7'' HYDRAULIC SET RETRIEVABLE PRODUCTION PACKER						2694.545	2691.866
NO-GO Landing Nipple						2708.053	2707.679
Entry Guide						2708.3	2708.053

Figure 7-7: AZNS-166 Completion Sketch

7.7 Completion Tally:

MSA

Field :	S.Azadegan	Well NO:	AZNS166	Rig NO:	OEOC201	Drig CO:	OEOC
PEDEC, PPL		Completion String					

Grade	ID "	Drift "	Weight lb/ft	Burst psi	Collaspse psi	Yield klbs	Coupling "	TQ ft x lb	Nominal Dia. OD
L-80	2.922	2.797	10.2	11,560.0	12,120.0	233	3.962	3200-3550-3900	3-1/2"
L-80	3.640	3.515	18.9	13,380.0	13,820.0	440	5.137	7920-8800-9680	4-1/2"

BTM NO GO Depth:	2707.68	Formation Name :	Kazhdumi	Hook Weight :	68 k lb
BTM of String	2708.30	Formation Top :	3480	VOLUME (TOTAL)	95.76
Packer Depth :	2691.87			Mud Weight (pcf) :	84

Number on jt	Grade	Run In No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	VOL(BBL)	Remarks	
								joint no	IN / OUT
					2708.3	72.00			
3-1/2" Wireline Re-Entry Guide, 10.2 #, HSM3, 9CR1MO, WEIQIXIN Co	3-1/2" Mule Shoe		0.247	0.25	2708.053	72.01	0.01		
3-1/2" BTM No-Go LND Nipple, HSM3, 10.2#, 9CR1MO, Seal Bore 2.750" TYPE XN, WEIQIXIN Co, 7.5K	3-1/2" BTM NO GO		0.374	0.62	2707.679	72.02	0.02		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		1.990	2.61	2705.689	72.02	0.02		
1	3-1/2" TBG, 10.2#, L-80,HSM3	1	9.345	11.96	2696.344	72.28	0.27	1	
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		1.799	13.76	2694.545	72.28	0.27		
7" 29# CSG Hydraulic set retrievable production packer to be run in 7.00" 29 PPF CSG, WEIQIXIN Co	PKR		2.679	16.43	2691.866	72.35	0.34		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		1.905	18.34	2689.961	72.35	0.34		
2	3-1/2" TBG, 10.2#, L-80,HSM3	2	9.346	27.69	2680.615	72.61	0.60	2	Ring Gauge
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		2.174	29.86	2678.441	72.61	0.60		
3-1/2" Non-Elastomeric Sliding Side Door, 9CR1MO, HSM3 w/ Type X Selective profile (Profile: 2.750" X, Downward open), 7.5K	SSD		1.195	31.05	2677.246	72.64	0.63		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		1.839	32.89	2675.407	72.70	0.68		
3	3-1/2" TBG, 10.2#, L-80,HSM3	3	9.358	42.25	2666.049	72.96	0.94	3	
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		1.877	44.13	2664.172	73.01	0.99		
3-1/2" EXP. Jt,HSM3 , 9CR1MO, 10' STK (Fully Open) Splind Rotational Lock System Any Position, Shear Pin Set 15 Klbs, WEIQIXIN Co	Traveling Jt		5.760	49.89	2658.412	73.17	1.14		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	3-1/2" Pup Jt, 10.2#,HSM3		1.930	51.82	2656.482	73.22	1.20		
4	3-1/2" TBG, 10.2#, L-80,HSM3	4	9.354	61.17	2647.128	73.48	1.45	4	
6	3-1/2" TBG, 10.2#, L-80,HSM3	5	9.354	70.53	2637.774	73.74	1.71	5	Test / Ring Gauge
7	3-1/2" TBG, 10.2#, L-80,HSM3	6	9.338	79.86	2628.436	74.00	1.96	6	
8	3-1/2" TBG, 10.2#, L-80,HSM3	7	9.353	89.22	2619.083	74.26	2.21	7	
9	3-1/2" TBG, 10.2#, L-80,HSM3	8	9.353	98.57	2609.730	74.52	2.47	8	
10	3-1/2" TBG, 10.2#, L-80,HSM3	9	9.349	107.92	2600.381	74.78	2.72	9	
11	3-1/2" TBG, 10.2#, L-80,HSM3	10	9.359	117.28	2591.022	75.04	2.98	10	
12	3-1/2" TBG, 10.2#, L-80,HSM3	11	9.337	126.62	2581.685	75.30	3.23	11	
13	3-1/2" TBG, 10.2#, L-80,HSM3	12	9.332	135.95	2572.353	75.56	3.49	12	
14	3-1/2" TBG, 10.2#, L-80,HSM3	13	9.012	144.96	2563.341	75.81	3.73	13	
15	3-1/2" TBG, 10.2#, L-80,HSM3	14	9.235	154.19	2554.106	76.07	3.98	14	
16	3-1/2" TBG, 10.2#, L-80,HSM3	15	9.341	163.54	2544.765	76.33	4.24	15	
17	3-1/2" TBG, 10.2#, L-80,HSM3	16	9.469	173.00	2535.296	76.59	4.49	16	
18	3-1/2" TBG, 10.2#, L-80,HSM3	17	9.469	182.47	2525.827	76.85	4.75	17	
19	3-1/2" TBG, 10.2#, L-80,HSM3	18	9.353	191.83	2516.474	77.11	5.01	18	
20	3-1/2" TBG, 10.2#, L-80,HSM3	19	9.257	201.08	2507.217	77.37	5.26	19	
21	3-1/2" TBG, 10.2#, L-80,HSM3	20	9.472	210.56	2497.745	77.63	5.52	20	
22	3-1/2" TBG, 10.2#, L-80,HSM3	21	9.345	219.90	2488.400	77.89	5.77	21	
23	3-1/2" TBG, 10.2#, L-80,HSM3	22	9.473	229.37	2478.927	78.15	6.03	22	
24	3-1/2" TBG, 10.2#, L-80,HSM3	23	9.217	238.59	2469.710	78.41	6.28	23	
25	3-1/2" TBG, 10.2#, L-80,HSM3	24	9.261	247.85	2460.449	78.67	6.53	24	

26	3-1/2" TBG, 10.2#, L-80,HSM3	25	9.240	257.09	2451.209	78.92	6.78	25	
27	3-1/2" TBG, 10.2#, L-80,HSM3	26	9.213	266.30	2441.996	79.18	7.03	26	
28	3-1/2" TBG, 10.2#, L-80,HSM3	27	9.210	275.51	2432.786	79.44	7.28	27	
29	3-1/2" TBG, 10.2#, L-80,HSM3	28	9.343	284.86	2423.443	79.70	7.54	28	
31	3-1/2" TBG, 10.2#, L-80,HSM3	29	9.349	294.21	2414.094	79.96	7.79	29	
32	3-1/2" TBG, 10.2#, L-80,HSM3	30	9.042	303.25	2405.052	80.21	8.04	30	
33	3-1/2" TBG, 10.2#, L-80,HSM3	31	9.346	312.59	2395.706	80.47	8.29	31	
34	3-1/2" TBG, 10.2#, L-80,HSM3	32	9.350	321.94	2386.356	80.73	8.55	32	
35	3-1/2" TBG, 10.2#, L-80,HSM3	33	9.327	331.27	2377.029	80.99	8.80	33	Ring Gauge
38	3-1/2" TBG, 10.2#, L-80,HSM3	34	9.342	340.61	2367.687	81.25	9.06	34	
39	3-1/2" TBG, 10.2#, L-80,HSM3	35	9.337	349.95	2358.350	81.51	9.31	35	
40	3-1/2" TBG, 10.2#, L-80,HSM3	36	9.348	359.30	2349.002	81.76	9.56	36	
41	3-1/2" TBG, 10.2#, L-80,HSM3	37	9.337	368.64	2339.665	82.02	9.82	37	
42	3-1/2" TBG, 10.2#, L-80,HSM3	38	9.338	377.97	2330.327	82.28	10.07	38	
43	3-1/2" TBG, 10.2#, L-80,HSM3	39	9.327	387.30	2321.000	82.54	10.33	39	
44	3-1/2" TBG, 10.2#, L-80,HSM3	40	9.358	396.66	2311.642	82.80	10.58	40	
45	3-1/2" TBG, 10.2#, L-80,HSM3	41	9.335	405.99	2302.307	83.06	10.83	41	
46	3-1/2" TBG, 10.2#, L-80,HSM3	42	9.344	415.34	2292.963	83.32	11.09	42	
47	3-1/2" TBG, 10.2#, L-80,HSM3	43	9.334	424.67	2283.629	83.58	11.34	43	
48	3-1/2" TBG, 10.2#, L-80,HSM3	44	9.336	434.01	2274.293	83.84	11.60	44	
49	3-1/2" TBG, 10.2#, L-80,HSM3	45	9.348	443.36	2264.945	84.10	11.85	45	
50	3-1/2" TBG, 10.2#, L-80,HSM3	46	9.359	452.71	2255.586	84.36	12.11	46	
51	3-1/2" TBG, 10.2#, L-80,HSM3	47	9.355	462.07	2246.231	84.62	12.36	47	
52	3-1/2" TBG, 10.2#, L-80,HSM3	48	9.342	471.41	2236.889	84.88	12.61	48	
53	3-1/2" TBG, 10.2#, L-80,HSM3	49	9.341	480.75	2227.548	85.14	12.87	49	
54	3-1/2" TBG, 10.2#, L-80,HSM3	50	9.343	490.10	2218.205	85.40	13.12	50	
55	3-1/2" TBG, 10.2#, L-80,HSM3	51	9.345	499.44	2208.860	85.66	13.38	51	
56	3-1/2" TBG, 10.2#, L-80,HSM3	52	9.334	508.77	2199.526	85.92	13.63	52	
57	3-1/2" TBG, 10.2#, L-80,HSM3	53	9.348	518.12	2190.178	86.18	13.89	53	
58	3-1/2" TBG, 10.2#, L-80,HSM3	54	9.335	527.46	2180.843	86.44	14.14	54	
59	3-1/2" TBG, 10.2#, L-80,HSM3	55	9.360	536.82	2171.483	86.70	14.39	55	
60	3-1/2" TBG, 10.2#, L-80,HSM3	56	9.357	546.17	2162.126	86.96	14.65	56	
61	3-1/2" TBG, 10.2#, L-80,HSM3	57	9.361	555.54	2152.765	87.22	14.90	57	
62	3-1/2" TBG, 10.2#, L-80,HSM3	58	9.352	564.89	2143.413	87.48	15.16	58	
63	3-1/2" TBG, 10.2#, L-80,HSM3	59	9.349	574.24	2134.064	87.74	15.41	59	
64	3-1/2" TBG, 10.2#, L-80,HSM3	60	9.334	583.57	2124.730	88.00	15.67	60	
65	3-1/2" TBG, 10.2#, L-80,HSM3	61	9.361	592.93	2115.369	88.26	15.92	61	
66	3-1/2" TBG, 10.2#, L-80,HSM3	62	9.339	602.27	2106.030	88.52	16.18	62	
67	3-1/2" TBG, 10.2#, L-80,HSM3	63	9.335	611.61	2096.695	88.78	16.43	63	
68	3-1/2" TBG, 10.2#, L-80,HSM3	64	9.361	620.97	2087.334	89.04	16.68	64	
69	3-1/2" TBG, 10.2#, L-80,HSM3	65	9.352	630.32	2077.982	89.30	16.94	65	
70	3-1/2" TBG, 10.2#, L-80,HSM3	66	9.356	639.67	2068.626	89.56	17.19	66	
71	3-1/2" TBG, 10.2#, L-80,HSM3	67	9.336	649.01	2059.290	89.81	17.45	67	
72	3-1/2" TBG, 10.2#, L-80,HSM3	68	9.362	658.37	2049.928	90.07	17.70	68	
73	3-1/2" TBG, 10.2#, L-80,HSM3	69	9.362	667.73	2040.566	90.33	17.96	69	
74	3-1/2" TBG, 10.2#, L-80,HSM3	70	9.357	677.09	2031.209	90.59	18.21	70	Press tese / Ring Gauge
75	3-1/2" TBG, 10.2#, L-80,HSM3	71	9.805	686.90	2021.404	90.87	18.48	71	
76	3-1/2" TBG, 10.2#, L-80,HSM3	72	9.350	696.25	2012.054	91.13	18.73	72	

77	3-1/2" TBG, 10.2#, L-80,HSM3	73	9.358	705.60	2002.696	91.39	18.99	73
78	3-1/2" TBG, 10.2#, L-80,HSM3	74	9.358	714.96	1993.338	91.65	19.24	74
79	3-1/2" TBG, 10.2#, L-80,HSM3	75	9.361	724.32	1983.977	91.91	19.50	75
80	3-1/2" TBG, 10.2#, L-80,HSM3	76	9.263	733.59	1974.714	92.16	19.75	76
81	3-1/2" TBG, 10.2#, L-80,HSM3	77	9.334	742.92	1965.380	92.42	20.00	77
82	3-1/2" TBG, 10.2#, L-80,HSM3	78	9.364	752.28	1956.016	92.68	20.26	78
83	3-1/2" TBG, 10.2#, L-80,HSM3	79	9.298	761.58	1946.718	92.94	20.51	79
84	3-1/2" TBG, 10.2#, L-80,HSM3	80	9.359	770.94	1937.359	93.20	20.77	80
85	3-1/2" TBG, 10.2#, L-80,HSM3	81	9.339	780.28	1928.020	93.46	21.02	81
86	3-1/2" TBG, 10.2#, L-80,HSM3	82	9.467	789.75	1918.553	93.73	21.28	82
87	3-1/2" TBG, 10.2#, L-80,HSM3	83	9.468	799.22	1909.085	93.99	21.54	83
88	3-1/2" TBG, 10.2#, L-80,HSM3	84	9.469	808.68	1899.616	94.25	21.79	84
89	3-1/2" TBG, 10.2#, L-80,HSM3	85	9.468	818.15	1890.148	94.51	22.05	85
90	3-1/2" TBG, 10.2#, L-80,HSM3	86	9.470	827.62	1880.678	94.78	22.31	86
91	3-1/2" TBG, 10.2#, L-80,HSM3	87	9.338	836.96	1871.340	95.04	22.56	87
92	3-1/2" TBG, 10.2#, L-80,HSM3	88	9.467	846.43	1861.873	95.30	22.82	88
93	3-1/2" TBG, 10.2#, L-80,HSM3	89	9.464	855.89	1852.409	95.56	23.08	89
94	3-1/2" TBG, 10.2#, L-80,HSM3	90	9.468	865.36	1842.941	95.83	23.34	90
95	3-1/2" TBG, 10.2#, L-80,HSM3	91	9.467	874.83	1833.474	96.09	23.59	91
96	3-1/2" TBG, 10.2#, L-80,HSM3	92	9.351	884.18	1824.123	96.35	23.85	92
97	3-1/2" TBG, 10.2#, L-80,HSM3	93	9.469	893.65	1814.654	96.61	24.10	93
98	3-1/2" TBG, 10.2#, L-80,HSM3	94	9.468	903.11	1805.186	96.88	24.36	94
99	3-1/2" TBG, 10.2#, L-80,HSM3	95	9.349	912.46	1795.837	97.13	24.62	95
100	3-1/2" TBG, 10.2#, L-80,HSM3	96	9.344	921.81	1786.493	97.39	24.87	96
101	3-1/2" TBG, 10.2#, L-80,HSM3	97	9.335	931.14	1777.158	97.65	25.13	97
102	3-1/2" TBG, 10.2#, L-80,HSM3	98	9.351	940.49	1767.807	97.91	25.38	98
103	3-1/2" TBG, 10.2#, L-80,HSM3	99	9.351	949.84	1758.456	98.17	25.63	99
104	3-1/2" TBG, 10.2#, L-80,HSM3	100	9.349	959.19	1749.107	98.43	25.89	100
105	3-1/2" TBG, 10.2#, L-80,HSM3	101	9.331	968.52	1739.776	98.69	26.14	101
106	3-1/2" TBG, 10.2#, L-80,HSM3	102	9.341	977.87	1730.435	98.95	26.40	102
107	3-1/2" TBG, 10.2#, L-80,HSM3	103	9.349	987.21	1721.086	99.21	26.65	103
108	3-1/2" TBG, 10.2#, L-80,HSM3	104	9.349	996.56	1711.737	99.47	26.91	104
109	3-1/2" TBG, 10.2#, L-80,HSM3	105	9.349	1005.91	1702.388	99.73	27.16	105
110	3-1/2" TBG, 10.2#, L-80,HSM3	106	9.352	1015.26	1693.036	99.99	27.41	106
111	3-1/2" TBG, 10.2#, L-80,HSM3	107	9.347	1024.61	1683.689	100.25	27.67	107
112	3-1/2" TBG, 10.2#, L-80,HSM3	108	9.345	1033.96	1674.344	100.51	27.92	108
113	3-1/2" TBG, 10.2#, L-80,HSM3	109	9.512	1043.47	1664.832	100.78	28.18	109
114	3-1/2" TBG, 10.2#, L-80,HSM3	110	9.518	1052.99	1655.314	101.04	28.44	110
115	3-1/2" TBG, 10.2#, L-80,HSM3	111	9.328	1062.31	1645.986	101.30	28.69	111
116	3-1/2" TBG, 10.2#, L-80,HSM3	112	9.510	1071.82	1636.476	101.56	28.95	112
117	3-1/2" TBG, 10.2#, L-80,HSM3	113	9.527	1081.35	1626.949	101.83	29.21	113
118	3-1/2" TBG, 10.2#, L-80,HSM3	114	9.390	1090.74	1617.559	102.09	29.47	114
119	3-1/2" TBG, 10.2#, L-80,HSM3	115	9.529	1100.27	1608.030	102.35	29.73	115
120	3-1/2" TBG, 10.2#, L-80,HSM3	116	9.518	1109.79	1598.512	102.62	29.99	116

121	3-1/2" TBG, 10.2#, L-80,HSM3	117	9.232	1119.02	1589.280	102.87	30.24	117	
122	3-1/2" TBG, 10.2#, L-80,HSM3	118	9.519	1128.54	1579.761	103.14	30.50	118	
123	3-1/2" TBG, 10.2#, L-80,HSM3	119	9.518	1138.06	1570.243	103.40	30.76	119	
124	3-1/2" TBG, 10.2#, L-80,HSM3	120	9.519	1147.58	1560.724	103.67	31.02	120	
125	3-1/2" TBG, 10.2#, L-80,HSM3	121	9.378	1156.95	1551.346	103.93	31.27	121	
126	3-1/2" TBG, 10.2#, L-80,HSM3	122	8.956	1165.91	1542.390	104.18	31.51	122	
127	3-1/2" TBG, 10.2#, L-80,HSM3	123	9.514	1175.42	1532.876	104.44	31.77	123	
128	3-1/2" TBG, 10.2#, L-80,HSM3	124	9.418	1184.84	1523.458	104.70	32.03	124	
129	3-1/2" TBG, 10.2#, L-80,HSM3	125	9.526	1194.37	1513.932	104.97	32.29	125	
130	3-1/2" TBG, 10.2#, L-80,HSM3	126	9.509	1203.88	1504.423	105.23	32.55	126	
X-over 4-1/2"HSM3, 18.9# BOX * 3-1/2"HSM3 , 10.2# PIN,	4-1/2" X 3-1/2" XOS	0	1.124	1205.00	1503.299	105.29	32.59	0	
161	4-1/2" TBG, 18.9#, L-80,HSM3	127	9.523	1214.52	1493.776	105.78	33.00	127	
162	4-1/2" TBG, 18.9#, L-80,HSM3	128	9.528	1224.05	1484.248	106.27	33.40	128	Press Test / Ring Gauge
163	4-1/2" TBG, 18.9#, L-80,HSM3	129	9.525	1233.58	1474.723	106.76	33.80	129	
164	4-1/2" TBG, 18.9#, L-80,HSM3	130	9.522	1243.10	1465.201	107.25	34.20	130	
165	4-1/2" TBG, 18.9#, L-80,HSM3	131	9.524	1252.62	1455.677	107.74	34.61	131	
166	4-1/2" TBG, 18.9#, L-80,HSM3	132	9.527	1262.15	1446.150	108.23	35.01	132	
167	4-1/2" TBG, 18.9#, L-80,HSM3	133	9.524	1271.67	1436.626	108.72	35.41	133	
168	4-1/2" TBG, 18.9#, L-80,HSM3	134	9.528	1281.20	1427.098	109.21	35.81	134	
169	4-1/2" TBG, 18.9#, L-80,HSM3	135	9.53	1290.73	1417.568	109.70	36.22	135	
170	4-1/2" TBG, 18.9#, L-80,HSM3	136	9.53	1300.26	1408.038	110.19	36.62	136	
171	4-1/2" TBG, 18.9#, L-80,HSM3	137	9.527	1309.79	1398.511	110.69	37.02	137	
172	4-1/2" TBG, 18.9#, L-80,HSM3	138	9.527	1319.32	1388.984	111.18	37.42	138	
173	4-1/2" TBG, 18.9#, L-80,HSM3	139	9.529	1328.85	1379.455	111.67	37.82	139	
174	4-1/2" TBG, 18.9#, L-80,HSM3	140	9.528	1338.37	1369.927	112.16	38.23	140	
175	4-1/2" TBG, 18.9#, L-80,HSM3	141	9.533	1347.91	1360.394	112.65	38.63	141	
176	4-1/2" TBG, 18.9#, L-80,HSM3	142	9.543	1357.45	1350.851	113.14	39.03	142	
177	4-1/2" TBG, 18.9#, L-80,HSM3	143	9.553	1367.00	1341.298	113.63	39.44	143	
178	4-1/2" TBG, 18.9#, L-80,HSM3	144	9.553	1376.56	1331.745	114.12	39.84	144	
179	4-1/2" TBG, 18.9#, L-80,HSM3	145	9.551	1386.11	1322.194	114.61	40.24	145	
180	4-1/2" TBG, 18.9#, L-80,HSM3	146	9.56	1395.67	1312.634	115.11	40.65	146	
181	4-1/2" TBG, 18.9#, L-80,HSM3	147	9.553	1405.22	1303.081	115.60	41.05	147	
182	4-1/2" TBG, 18.9#, L-80,HSM3	148	9.244	1414.46	1293.837	116.07	41.44	148	
183	4-1/2" TBG, 18.9#, L-80,HSM3	149	9.534	1424.00	1284.303	116.57	41.84	149	
184	4-1/2" TBG, 18.9#, L-80,HSM3	150	9.532	1433.53	1274.771	117.06	42.25	150	
185	4-1/2" TBG, 18.9#, L-80,HSM3	151	9.534	1443.06	1265.237	117.55	42.65	151	
186	4-1/2" TBG, 18.9#, L-80,HSM3	152	9.531	1452.59	1255.706	118.04	43.05	152	
187	4-1/2" TBG, 18.9#, L-80,HSM3	153	9.531	1462.13	1246.175	118.53	43.45	153	
188	4-1/2" TBG, 18.9#, L-80,HSM3	154	9.533	1471.66	1236.642	119.02	43.86	154	
189	4-1/2" TBG, 18.9#, L-80,HSM3	155	9.534	1481.19	1227.108	119.51	44.26	155	
190	4-1/2" TBG, 18.9#, L-80,HSM3	156	9.528	1490.72	1217.580	120.00	44.66	156	
191	4-1/2" TBG, 18.9#, L-80,HSM3	157	9.532	1500.25	1208.048	120.49	45.06	157	
192	4-1/2" TBG, 18.9#, L-80,HSM3	158	9.523	1509.78	1198.525	120.98	45.47	158	
193	4-1/2" TBG, 18.9#, L-80,HSM3	159	9.526	1519.30	1188.999	121.47	45.87	159	
195	4-1/2" TBG, 18.9#, L-80,HSM3	160	9.398	1528.70	1179.601	121.96	46.26	160	
196	4-1/2" TBG, 18.9#, L-80,HSM3	161	9.531	1538.23	1170.070	122.45	46.67	161	
197	4-1/2" TBG, 18.9#, L-80,HSM3	162	9.529	1547.76	1160.541	122.94	47.07	162	
198	4-1/2" TBG, 18.9#, L-80,HSM3	163	9.529	1557.29	1151.012	123.43	47.47	163	
199	4-1/2" TBG, 18.9#, L-80,HSM3	164	9.529	1566.82	1141.483	123.92	47.87	164	
200	4-1/2" TBG, 18.9#, L-80,HSM3	165	9.532	1576.35	1131.951	124.41	48.28	165	
201	4-1/2" TBG, 18.9#, L-80,HSM3	166	9.528	1585.88	1122.423	124.90	48.68	166	
202	4-1/2" TBG, 18.9#, L-80,HSM3	167	9.528	1595.41	1112.895	125.39	49.08	167	
203	4-1/2" TBG, 18.9#, L-80,HSM3	168	9.525	1604.93	1103.370	125.88	49.48	168	
204	4-1/2" TBG, 18.9#, L-80,HSM3	169	9.551	1614.48	1093.819	126.37	49.89	169	
205	4-1/2" TBG, 18.9#, L-80,HSM3	170	9.533	1624.01	1084.286	126.86	50.29	170	


206	4-1/2" TBG, 18.9#, L-80,HSM3	171	9.523	1633.54	1074.763	127.35	50.69	171
207	4-1/2" TBG, 18.9#, L-80,HSM3	172	9.589	1643.13	1065.174	127.85	51.10	172
208	4-1/2" TBG, 18.9#, L-80,HSM3	173	9.548	1652.67	1055.626	128.34	51.50	173
209	4-1/2" TBG, 18.9#, L-80,HSM3	174	9.539	1662.21	1046.087	128.83	51.90	174
210	4-1/2" TBG, 18.9#, L-80,HSM3	175	9.552	1671.77	1036.535	129.32	52.31	175
211	4-1/2" TBG, 18.9#, L-80,HSM3	176	9.535	1681.30	1027.000	129.81	52.71	176
212	4-1/2" TBG, 18.9#, L-80,HSM3	177	9.535	1690.84	1017.465	130.30	53.11	177
213	4-1/2" TBG, 18.9#, L-80,HSM3	178	9.528	1700.36	1007.937	130.79	53.51	178
214	4-1/2" TBG, 18.9#, L-80,HSM3	179	9.535	1709.90	998.402	131.28	53.92	179
215	4-1/2" TBG, 18.9#, L-80,HSM3	180	9.407	1719.31	988.995	131.77	54.31	180
216	4-1/2" TBG, 18.9#, L-80,HSM3	181	9.534	1728.84	979.461	132.26	54.72	181
217	4-1/2" TBG, 18.9#, L-80,HSM3	182	9.533	1738.37	969.928	132.75	55.12	182
218	4-1/2" TBG, 18.9#, L-80,HSM3	183	9.525	1747.90	960.403	133.24	55.52	183
219	4-1/2" TBG, 18.9#, L-80,HSM3	184	9.523	1757.42	950.880	133.73	55.92	184
220	4-1/2" TBG, 18.9#, L-80,HSM3	185	9.522	1766.94	941.358	134.22	56.33	185
221	4-1/2" TBG, 18.9#, L-80,HSM3	186	9.527	1776.47	931.831	134.71	56.73	186
222	4-1/2" TBG, 18.9#, L-80,HSM3	187	9.527	1786.00	922.304	135.20	57.13	187
223	4-1/2" TBG, 18.9#, L-80,HSM3	188	9.527	1795.52	912.777	135.69	57.53	188
224	4-1/2" TBG, 18.9#, L-80,HSM3	189	9.528	1805.05	903.249	136.18	57.93	189
225	4-1/2" TBG, 18.9#, L-80,HSM3	190	9.552	1814.60	893.697	136.68	58.34	190
226	4-1/2" TBG, 18.9#, L-80,HSM3	191	9.533	1824.14	884.164	137.17	58.74	191
227	4-1/2" TBG, 18.9#, L-80,HSM3	192	9.527	1833.66	874.637	137.66	59.14	192
228	4-1/2" TBG, 18.9#, L-80,HSM3	193	9.552	1843.22	865.085	138.15	59.55	193
229	4-1/2" TBG, 18.9#, L-80,HSM3	194	9.533	1852.75	855.552	138.64	59.95	194
230	4-1/2" TBG, 18.9#, L-80,HSM3	195	9.413	1862.16	846.139	139.12	60.35	195
231	4-1/2" TBG, 18.9#, L-80,HSM3	196	9.528	1871.69	836.611	139.61	60.75	196
232	4-1/2" TBG, 18.9#, L-80,HSM3	197	9.531	1881.22	827.080	140.11	61.15	197
234	4-1/2" TBG, 18.9#, L-80,HSM3	198	9.528	1890.75	817.552	140.60	61.55	198
235	4-1/2" TBG, 18.9#, L-80,HSM3	199	9.524	1900.27	808.028	141.09	61.96	199
236	4-1/2" TBG, 18.9#, L-80,HSM3	200	9.53	1909.80	798.498	141.58	62.36	200
237	4-1/2" TBG, 18.9#, L-80,HSM3	201	9.527	1919.33	788.971	142.07	62.76	201
238	4-1/2" TBG, 18.9#, L-80,HSM3	202	9.524	1928.85	779.447	142.56	63.16	202
239	4-1/2" TBG, 18.9#, L-80,HSM3	203	9.526	1938.38	769.921	143.05	63.57	203
240	4-1/2" TBG, 18.9#, L-80,HSM3	204	9.532	1947.91	760.389	143.54	63.97	204
241	4-1/2" TBG, 18.9#, L-80,HSM3	205	9.529	1957.44	750.860	144.03	64.37	205
242	4-1/2" TBG, 18.9#, L-80,HSM3	206	9.533	1966.97	741.327	144.52	64.77	206
243	4-1/2" TBG, 18.9#, L-80,HSM3	207	9.527	1976.50	731.800	145.01	65.17	207
244	4-1/2" TBG, 18.9#, L-80,HSM3	208	9.528	1986.03	722.272	145.50	65.58	208
245	4-1/2" TBG, 18.9#, L-80,HSM3	209	9.528	1995.56	712.744	145.99	65.98	209
246	4-1/2" TBG, 18.9#, L-80,HSM3	210	9.534	2005.09	703.210	146.48	66.38	210
247	4-1/2" TBG, 18.9#, L-80,HSM3	211	9.536	2014.63	693.674	146.97	66.79	211
248	4-1/2" TBG, 18.9#, L-80,HSM3	212	9.533	2024.16	684.141	147.46	67.19	212
249	4-1/2" TBG, 18.9#, L-80,HSM3	213	9.529	2033.69	674.612	147.96	67.59	213
250	4-1/2" TBG, 18.9#, L-80,HSM3	214	9.524	2043.21	665.088	148.45	67.99	214
251	4-1/2" TBG, 18.9#, L-80,HSM3	215	9.531	2052.74	655.557	148.94	68.39	215
252	4-1/2" TBG, 18.9#, L-80,HSM3	216	9.532	2062.28	646.025	149.43	68.80	216
253	4-1/2" TBG, 18.9#, L-80,HSM3	217	9.535	2071.81	636.490	149.92	69.20	217
254	4-1/2" TBG, 18.9#, L-80,HSM3	218	9.535	2081.35	626.955	150.41	69.60	218
255	4-1/2" TBG, 18.9#, L-80,HSM3	219	9.53	2090.88	617.425	150.90	70.01	219
256	4-1/2" TBG, 18.9#, L-80,HSM3	220	9.535	2100.41	607.890	151.39	70.41	220
257	4-1/2" TBG, 18.9#, L-80,HSM3	221	9.53	2109.94	598.360	151.88	70.81	221
258	4-1/2" TBG, 18.9#, L-80,HSM3	222	9.526	2119.47	588.834	152.37	71.21	222
259	4-1/2" TBG, 18.9#, L-80,HSM3	223	9.53	2129.00	579.304	152.86	71.61	223

260	4-1/2" TBG, 18.9#, L-80,HSM3	224	9.529	2138.53	569.775	153.35	72.02	224	
261	4-1/2" TBG, 18.9#, L-80,HSM3	225	9.532	2148.06	560.243	153.84	72.42	225	
262	4-1/2" TBG, 18.9#, L-80,HSM3	226	9.527	2157.58	550.716	154.33	72.82	226	
263	4-1/2" TBG, 18.9#, L-80,HSM3	227	9.531	2167.12	541.185	154.82	73.22	227	
264	4-1/2" TBG, 18.9#, L-80,HSM3	228	9.529	2176.64	531.656	155.32	73.63	228	
265	4-1/2" TBG, 18.9#, L-80,HSM3	229	9.53	2186.17	522.126	155.81	74.03	229	
266	4-1/2" TBG, 18.9#, L-80,HSM3	230	9.18	2195.35	512.946	156.28	74.42	230	
267	4-1/2" TBG, 18.9#, L-80,HSM3	231	9.527	2204.88	503.419	156.77	74.82	231	
268	4-1/2" TBG, 18.9#, L-80,HSM3	232	9.545	2214.43	493.874	157.26	75.22	232	
269	4-1/2" TBG, 18.9#, L-80,HSM3	233	9.408	2223.83	484.466	157.75	75.62	233	
270	4-1/2" TBG, 18.9#, L-80,HSM3	234	9.548	2233.38	474.918	158.24	76.02	234	
271	4-1/2" TBG, 18.9#, L-80,HSM3	235	9.552	2242.93	465.366	158.73	76.43	235	
272	4-1/2" TBG, 18.9#, L-80,HSM3	236	9.56	2252.49	455.806	159.22	76.83	236	
273	4-1/2" TBG, 18.9#, L-80,HSM3	237	9.558	2262.05	446.248	159.71	77.23	237	
274	4-1/2" TBG, 18.9#, L-80,HSM3	238	9.544	2271.60	436.704	160.20	77.64	238	
275	4-1/2" TBG, 18.9#, L-80,HSM3	239	9.547	2281.14	427.157	160.70	78.04	239	
276	4-1/2" TBG, 18.9#, L-80,HSM3	240	9.525	2290.67	417.632	161.19	78.44	240	
277	4-1/2" TBG, 18.9#, L-80,HSM3	241	9.528	2300.20	408.104	161.68	78.84	241	
278	4-1/2" TBG, 18.9#, L-80,HSM3	242	9.527	2309.72	398.577	162.17	79.25	242	
279	4-1/2" TBG, 18.9#, L-80,HSM3	243	9.524	2319.25	389.053	162.66	79.65	243	
280	4-1/2" TBG, 18.9#, L-80,HSM3	244	9.524	2328.77	379.529	163.15	80.05	244	
281	4-1/2" TBG, 18.9#, L-80,HSM3	245	9.531	2338.30	369.998	163.64	80.45	245	
282	4-1/2" TBG, 18.9#, L-80,HSM3	246	9.526	2347.83	360.472	164.13	80.86	246	
283	4-1/2" TBG, 18.9#, L-80,HSM3	247	9.518	2357.35	350.954	164.62	81.26	247	
284	4-1/2" TBG, 18.9#, L-80,HSM3	248	9.529	2366.88	341.425	165.11	81.66	248	
285	4-1/2" TBG, 18.9#, L-80,HSM3	249	9.183	2376.06	332.242	165.58	82.05	249	
286	4-1/2" TBG, 18.9#, L-80,HSM3	250	9.532	2385.59	322.710	166.07	82.45	250	
287	4-1/2" TBG, 18.9#, L-80,HSM3	251	9.526	2395.12	313.184	166.56	82.85	251	
288	4-1/2" TBG, 18.9#, L-80,HSM3	252	9.521	2404.64	303.663	167.05	83.26	252	
289	4-1/2" TBG, 18.9#, L-80,HSM3	253	9.528	2414.17	294.135	167.54	83.66	253	
290	4-1/2" TBG, 18.9#, L-80,HSM3	254	9.52	2423.69	284.615	168.03	84.06	254	
291	4-1/2" TBG, 18.9#, L-80,HSM3	255	9.547	2433.23	275.068	168.53	84.46	255	
292	4-1/2" TBG, 18.9#, L-80,HSM3	256	9.13	2442.36	265.938	169.00	84.85	256	
293	4-1/2" TBG, 18.9#, L-80,HSM3	257	9.4	2451.76	256.538	169.48	85.25	257	
294	4-1/2" TBG, 18.9#, L-80,HSM3	258	9.538	2461.30	247.000	169.97	85.65	258	
295	4-1/2" TBG, 18.9#, L-80,HSM3	259	9.528	2470.83	237.472	170.46	86.05	259	
296	4-1/2" TBG, 18.9#, L-80,HSM3	260	9.52	2480.35	227.952	170.95	86.45	260	
297	4-1/2" TBG, 18.9#, L-80,HSM3	261	9.526	2489.87	218.426	171.44	86.85	261	
298	4-1/2" TBG, 18.9#, L-80,HSM3	262	9.528	2499.40	208.898	171.93	87.26	262	
299	4-1/2" TBG, 18.9#, L-80,HSM3	263	9.528	2508.93	199.370	172.42	87.66	263	
300	4-1/2" TBG, 18.9#, L-80,HSM3	264	9.529	2518.46	189.841	172.91	88.06	264	
301	4-1/2" TBG, 18.9#, L-80,HSM3	265	9.531	2527.99	180.310	173.40	88.46	265	
302	4-1/2" TBG, 18.9#, L-80,HSM3	266	9.522	2537.51	170.788	173.90	88.87	266	
303	4-1/2" TBG, 18.9#, L-80,HSM3	267	9.431	2546.94	161.357	174.38	89.26	267	
304	4-1/2" TBG, 18.9#, L-80,HSM3	268	9.35	2556.29	152.007	174.86	89.66	268	
305	4-1/2" TBG, 18.9#, L-80,HSM3	269	9.32	2565.61	142.687	175.34	90.05	269	
306	4-1/2" TBG, 18.9#, L-80,HSM3	270	9.298	2574.91	133.389	175.82	90.45	270	
307	4-1/2" TBG, 18.9#, L-80,HSM3	271	9.451	2584.36	123.938	176.31	90.84	271	
308	4-1/2" TBG, 18.9#, L-80,HSM3	272	9.448	2593.81	114.490	176.79	91.24	272	
309	4-1/2" TBG, 18.9#, L-80,HSM3	273	9.521	2603.33	104.969	177.28	91.65	273	
310	4-1/2" TBG, 18.9#, L-80,HSM3	274	9.522	2612.85	95.447	177.77	92.05	274	
311	4-1/2" TBG, 18.9#, L-80,HSM3	275	9.528	2622.38	85.919	178.26	92.45	275	
312	4-1/2" TBG, 18.9#, L-80,HSM3	276	9.521	2631.90	76.398	178.75	92.85	276	
313	4-1/2" TBG, 18.9#, L-80,HSM3	277	9.523	2641.43	66.875	179.25	93.25	277	Press Test

Pup Jt 4 1/2",HSM3 ,18.9#, L-80, Type-1	4-1/2" Pup Jt, 18.9#,HSM3	1.996	2643.42	64.879	179.35	93.25	0	
4-1/2" Flow Coupling, 18.9#, 9CR1MO, HSM3, 4' ft, WEIQIXIN Co	Short flow coupling	1.118	2644.54	63.761	179.41	93.25	0	
4 1/2" TRSSV Tubing Retrievable Saftey Valve, 18.9# w/ 3.437" Seal bore, HSM3, 9CR1MO, 7.5K WP w/ AF Profile, Flapper Type, WEIQIXIN Co	TR3SV	1.783	2646.32	61.978	179.50	93.25	0	
4-1/2" Flow Coupling,18.9#, 9CR1MO, HSM3, 6' ft, WEIQIXIN Co	Long flow coupling	1.725	2648.05	60.253	179.59	93.25	0	
Pup Jt 4 1/2",HSM3 ,18.9#, L-80, Type-1		1.917	2649.96	58.336	179.68	93.25	0	
314	4-1/2" TBG, 18.9#, L-80,HSM3	278	9.525	2659.49	48.811	180.18	93.66	278	Press Test / Inflow test
315	4-1/2" TBG, 18.9#, L-80,HSM3	279	9.528	2669.02	39.283	180.67	94.06	279	
316	4-1/2" TBG, 18.9#, L-80,HSM3	280	9.074	2678.09	30.209	181.13	94.44	280	
317	4-1/2" TBG, 18.9#, L-80,HSM3	281	9.265	2687.36	20.944	181.61	94.83	281	
318	4-1/2" TBG, 18.9#, L-80,HSM3	282	9.318	2696.67	11.626	182.09	95.23	282	
4-1/2" Fluted swage adapter D/P, 18.9# 9CR1MO, WEIQIXIN Co	Fluted Swage	0	1.018	2697.69	10.608	182.14	95.27	0	
TBG HANGER MSP/Drilex, 7.5K, 11" X 4 1/2" ACME Box up, L-80 18.9#, M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type "H" Two Way (Min Bore: 3.68")	TBG HGR	0	0.531	2698.22	10.077	182.17	95.29	0	
TBG Hanger Running Tool	TBG Hanger Running Tool	0	0.23	2698.45	9.847	182.18	95.30	0	
L/Joint	L/Joint	0	10.898	2709.35	-1.051	182.74	95.76	0	

Table 7-5: AZNS-166 Completion Tally

7.8 Completion String Pressure Test

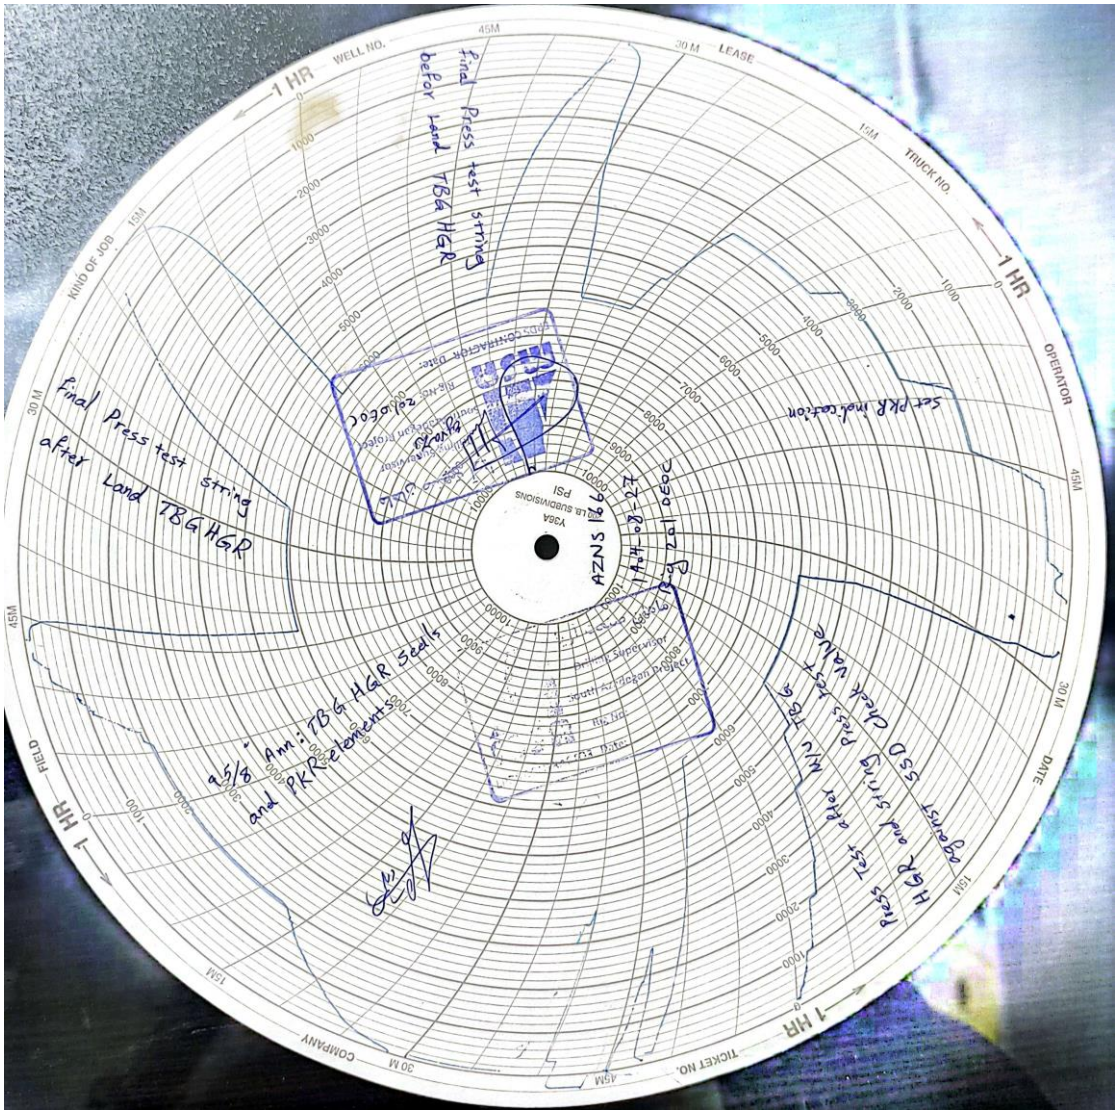

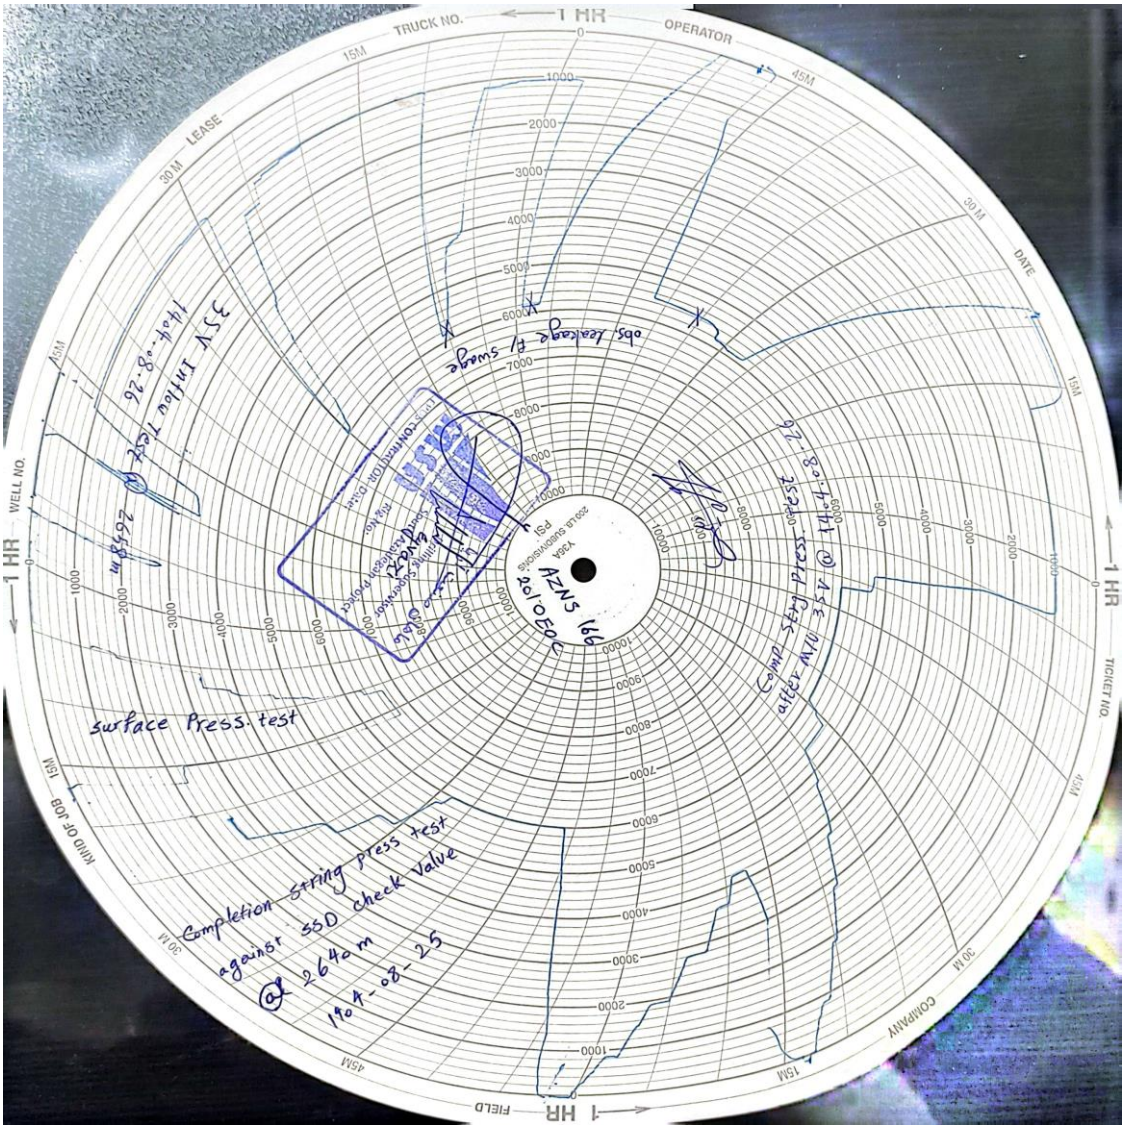


Figure 7-8: AZNS-166 Setting Packer, Annulus & Final Completion String Pressure Test

8. Wellhead Report

8.1 Final Well Status

Well Head

Item	Specification (size, pressure rating, M/C)	Test Pressure	Test Duration
C.H.H (MSP Drilex)	20-3/4'' 3K, DD-0.5 PSL1, PR1	Already Installed	-
C.H.S (MSP Drilex)	20-3/4'' 3K * 13-5/8'' 5K , DD-0.5, PSL1, PR1	Already Installed	-
T.H.S (MSP Drilex)	13-5/8'' 5K * 11''-5K, FF-0.5, PSL3, PR2	Already Installed	-
X-MASS TREE(BTM) (MSP Drilex)	4-1/16''-5K, FF-0.5, PSL3G, PR2	6,000psi	15 MIN

Wellbore Completion Fluids

Well bore	Fluid Type	Weight (pcf)
Cased Hole	$CaCL_2$	83

Well Head Pressure Record

Annulus	Pressure (psi)	Date / Time
Wellhead	0	1404. 08. 28
Tubing- 9 5/8"	0	1404. 08. 28
9 5/8" – 13 3/8"	0	1404. 08. 28
13 3/8" – 20"	0	1404. 08. 28

Barriers

Barrier Type	Depth	Pressure Test	Date Tested
Close TRSSSV	61.978m	500 psi (inflow test after finish flow the well)	1404. 08. 25

Temporary Installed Equipment:

Table 8-1: AZNS-166 Final Well Status

8.2 Wellhead & X-mass tree Specification

Well Type	Specification	Check and Remark
MSP Co. Well Head 10000 Psi for Kazhdumi Wells	**TUBING HEAD ADAPTOR** BOTTOM STUDDED FLANGE 11", 10000 PSI, BX158 TOP STUDDED FLANGE 4-1/16" 10000 PSI BX155 FULL BORE PREPARED WITH TWO S-SEAL AND ONE METAL TO METAL SEAL TO PACK TOP NECK OF TUBING HANGER C/W RELATED TEST AND INJECTION PORTS PREPARTION. C/W TWO CONTINUOUS FEED THROUGH TYPE 1/4" NPT CONTROL LINE EXITS PREPARTION (ONE FOR 1/4" TRSSSV CL AND ONE FOR 1/4" DOWNHOLE PRESSURE GAUGE) AND TWO 3/8" NPT CONTINUOUS FEED THROUGH TYPE LINE PORTS FOR CHEMCIAL INJECTION LINE EXIT INCLUDING RELATED SWAGE LOCK FITTINGS C/WITH ONE 4-1/16", 10K WP FULL BORE MANUAL GATE VALVE FORGED BODY AND BONNET, ALLOY STAINLESS STEEL 410SS GATE & SEAT AISI 410 COATED WITH TUNGSTEN CARBIDE USING HVOF METHOD STEM: INCONEL 718 WITH BACK SEAT CAPABILITY, NON RISING STEM METAL TO METAL SEAL BETWEEN SEAT AND GATE C/W HAND WHEEL FORGED BODY ALLOY STEEL AISI 410 MAXIMUM HEIGHT: 800MM M/C: FF-0.5 T/C: U PSL:3G PR:2 CROSS T-TYPE SOLID BLOCK CROSS T-TYPE SOLID BLOCK, BOTTOM FLANGED 4-1/16" API 10000 PSI WP TOP FLANGED STUDDED 4-1/16" API 10000 PSI WP FOR TREE CAP WITH TWO STUDDED SIDE OUTLETS 4-1/16" 10000PSI WP ELEVATED AT 900 DEG AND TWO 4-1/16", 10000 PSI MANUAL GATE VALVE AT THE TOP AND BOTTOM AND ONE 4-1/16", 10000 PSI WP SAFETY VALVE EQUIPPED WITH HYDRAULIC WIRE CUT	

	ACTUATOR AS UPPER MASTER VALVE MATERIAL OF BODY, BONNET: AISI 410 SEAT, GATE: AISI 410SS HARD FACED WITH TUNGSTEN CARBIDE UASING HVOP METHOD MATERIAL OF STEM: INCONEL 718 M/C: FF-0.5 T/C: U PSL:3G PR:2G. MANUAL GATE VALVE API 4-1/16" 10000 PSI WP. FLANGED ENDS AND FULL BORE METAL TO METAL SEAL BETWEEN BODY/SEAT/GATE WITH BACK SEAT CAPABILITY, NON RISING STEM C/W HANDWHEELS MATERIAL OF BODY, BONNET, SEAT, GATE: AISI 410SS MATERIAL OF STEM: INCONEL 718 GATE&SEAT HARD FACED WITH TUNGSTEN CARBIDE BY HOVF METHOD M/C: FF-0.5 T/C: U PSL:3G PR:2 X-MAS TREE CAP 4-1/16" API 10000 PSI WP, FLANGED BOTTOM (4-1/16", BORE) 8-3/8"-4ACME-2G THREAD TOP, BLANKING PLUG TAPPED WITH 1/2" NPT THREAD, FORGED BODY, MATERIAL: STAINLESS STEEL 410 M/C: FF-0.5 T/C: U PSL:3G PR:2	

Table 8-2: AZNS-166 Equipment Specification

8.3 Wellhead Schematic



Figure 8-1: AZNS-166 Wellhead Sketch

8.4 X-mass Tree Specification (Section D)

Item	Equipment	M/C	T/C	PSL	Qty
1	BTM Master Valve 11” * 4 1/16” 10K	FF-0.5	U	3G	1
2	TOP Master Valve 4 1/16” 10K	FF-0.5	U	3G	1
3	Surface Safety Valve 4 1/16” 10K	FF-0.5	U	3G	1
4	Deeping Valve 4 1/16” 10K	FF-0.5	U	3G	1
5	Wing gate valve-1 (Kill Valve) 4 1/16" 10K	FF-0.5	U	3G	1
6	Wing gate valve-2 (production valve) 10K	FF-0.5	U	3G	1
7	41/16" Choke valve 4 1/16" 10K	FF-0.5	U	3G	1
8	Christ Mas Tree	FF-0.5	U	3G	1

Table 8-3: AZNS-166 Section "D" Specification

8.5 X-mass Tree Pressure Test Report (Section D – befor install)

Item	Test	Check Mark and Result
1	Pressure test for the kill Valve W/ 1000 & 6000 Psi / 15 min	OK
2	Pressure test for the SSV W/ 1000 & 6000 Psi / 15 min	OK
3	Pressure test for the top master valve W/ 1000 & 6000 Psi / 15 min	OK
4	Pressure test for Swab valve W/ 1000 & 6000 Psi / 15 min	OK
5	Pressure test for the Production valve W/ 1000 & 6000 Psi / 15 min	OK

Table 8-4: AZNS-166 Section "D" Test Report Befor Installation

8.6 X-mass Tree Pressure Test Report (Section D – after install)

Item	Test	Check mark and Result
1	Pressure test X-MAS TREE solid block and bottom section W/1000 &6000 psi for 15min	OK
2	Pressure test for the SSV Exit block W/ 6000 Psi / 15 min	OK
3	Pressure test neck of tubing hanger metal seal W/1000 &6000 psi for 15min	OK
4	Pressure test for Swab valve W/ 6000 Psi / 15 min	-
5	Pressure test for Production valve W/6000 Psi / 15 min	-
6	Pressure test cavity of FS.seal and Ring Gasket W 6000 Psi / 15 min	OK

Table 8-5: AZNS-166 Section "D" Test Report After Installation

8.7 Wellhead Related Test Reports

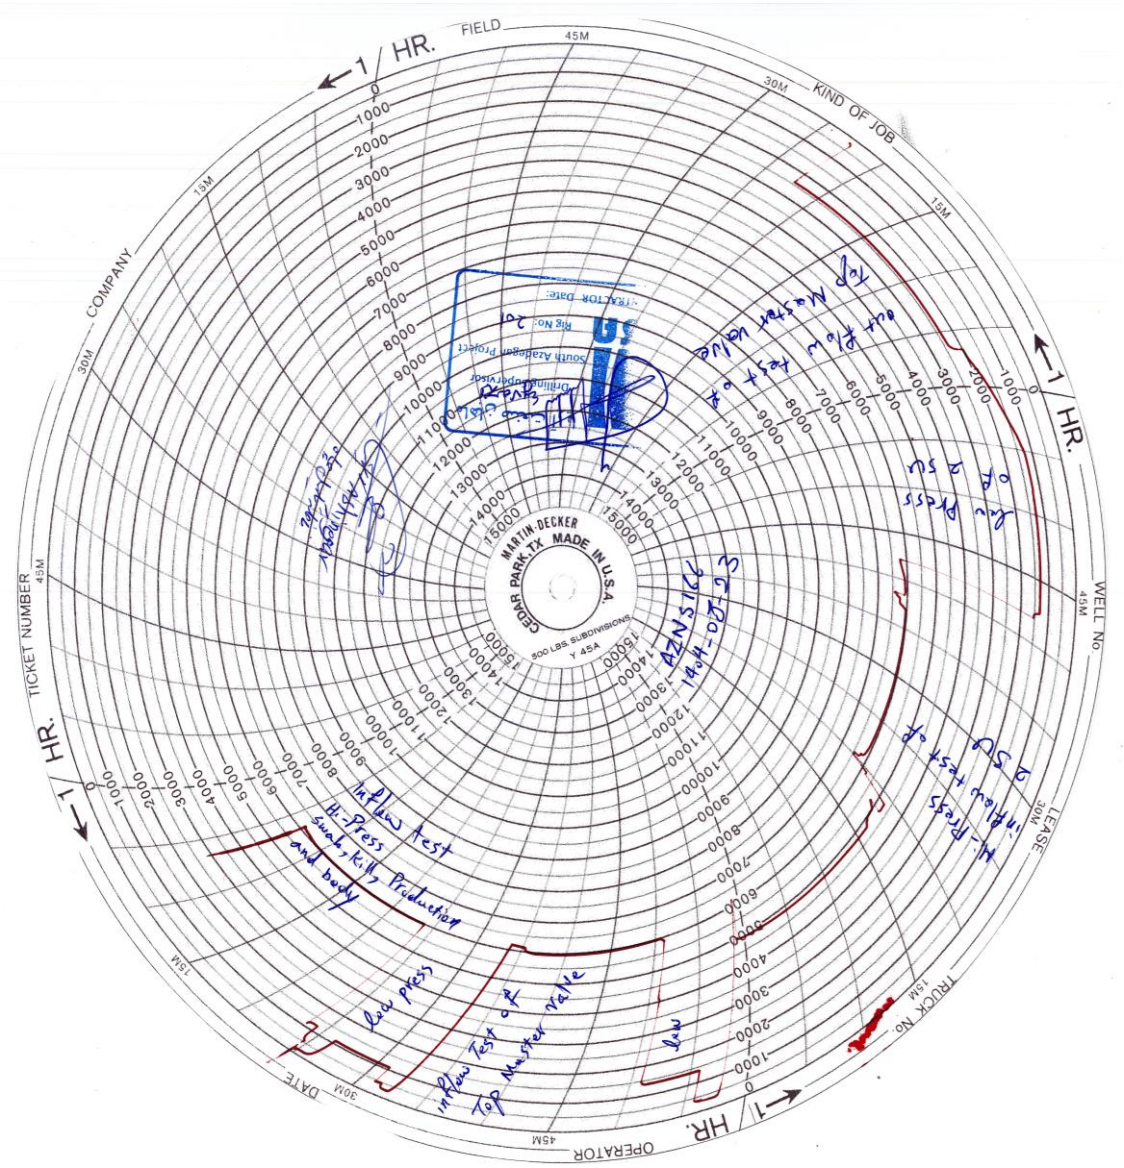


Figure 8-2: AZNS-166 X-Mass Tree Body Pressure Test Graph Before Installation


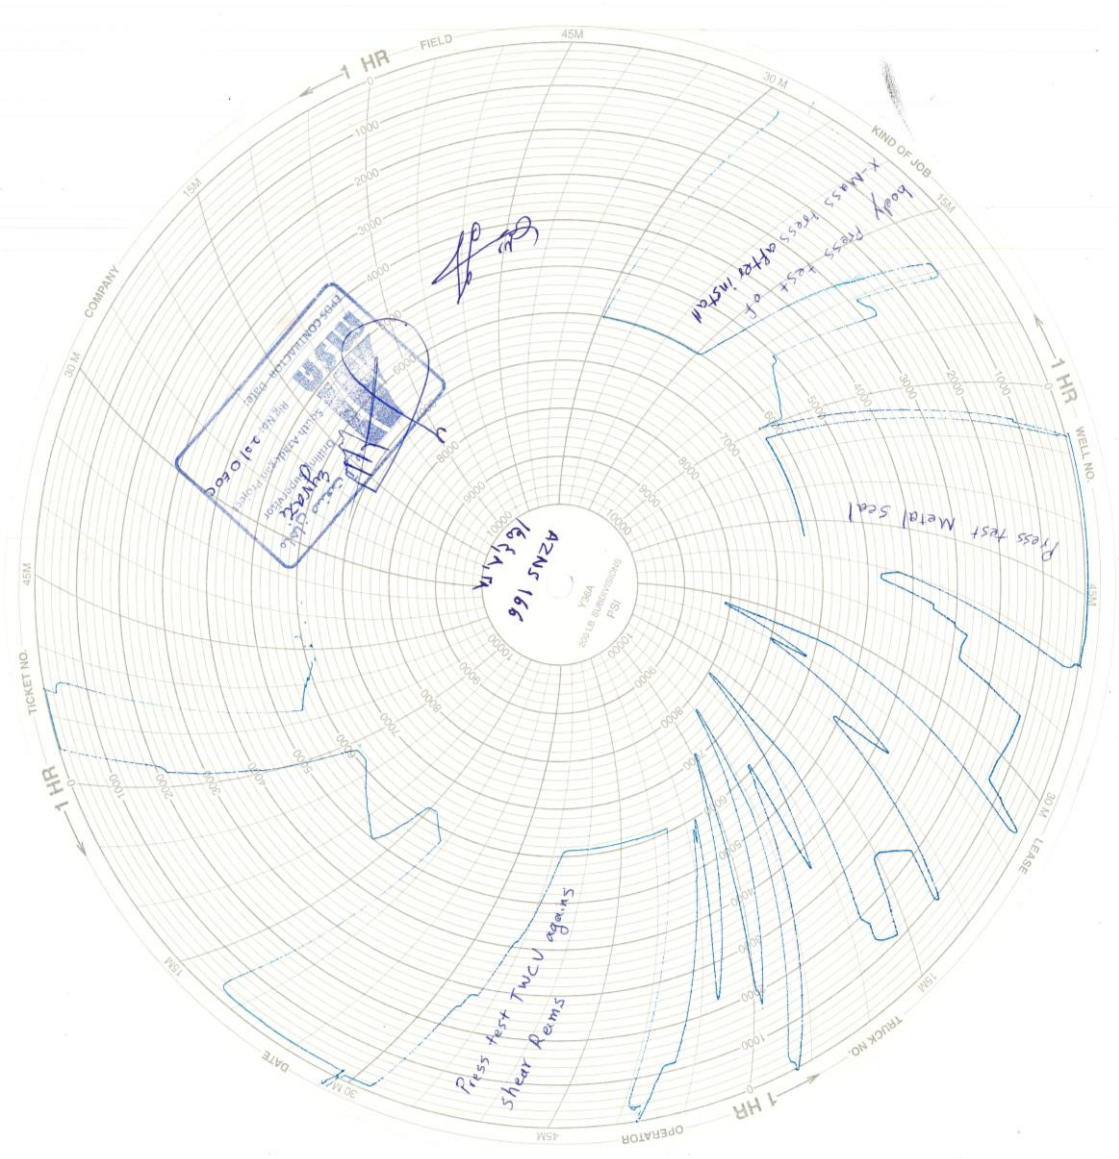


Figure 8-3: AZNS-166 X-Mass Tree Body Pressure Test Graph After Installation

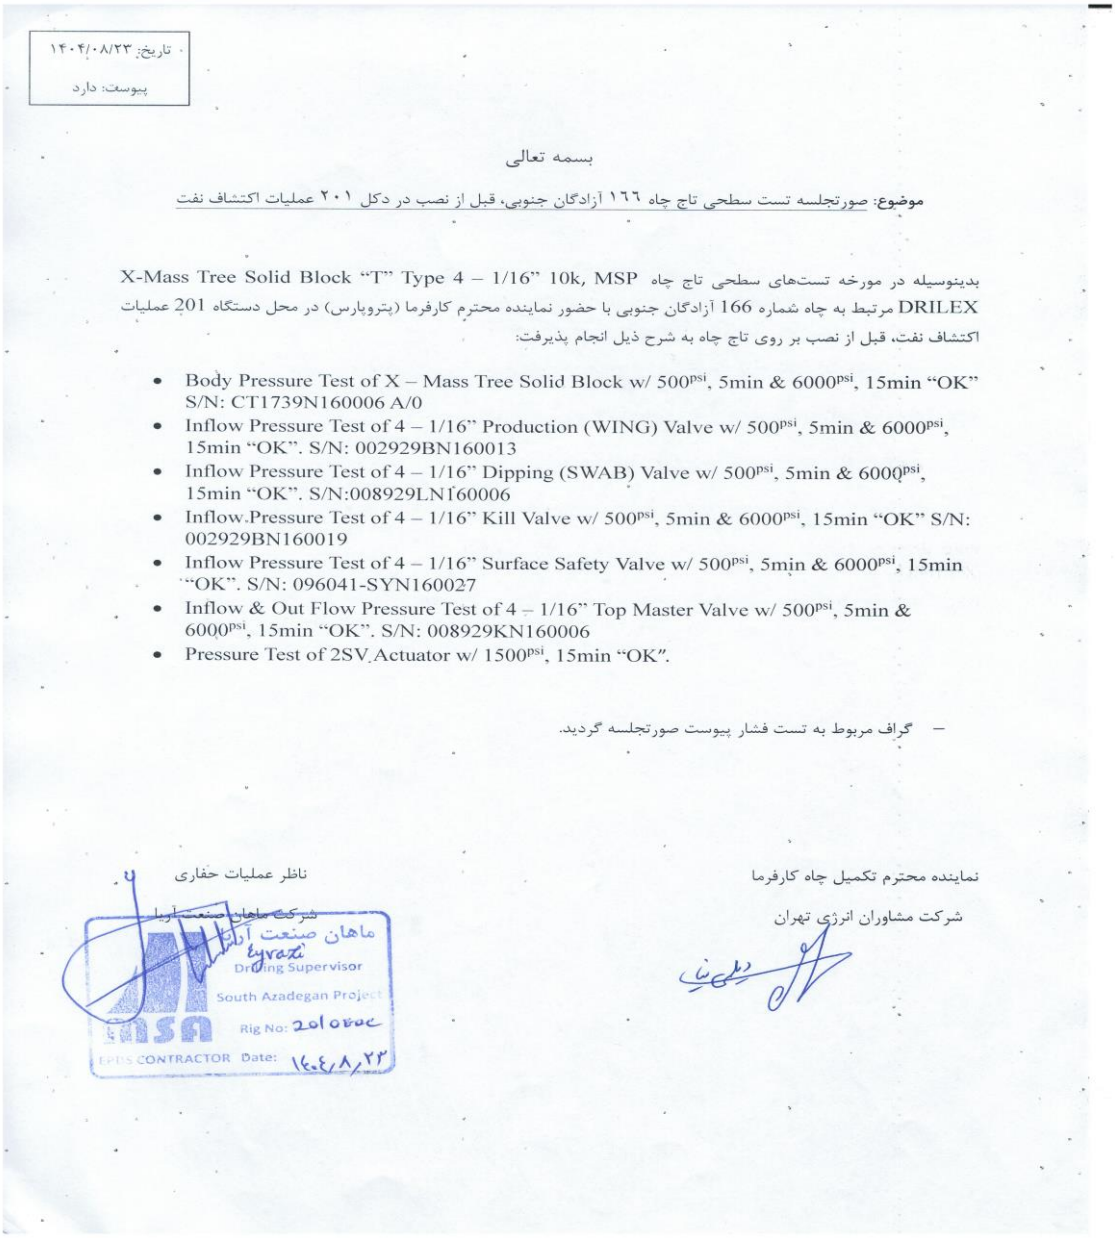

تاریخ: ۱۴۰۴/۰۸/۲۳
پیوست: دارد

بسمه تعالی

موضوع: صورتجلسه تست سطحی تاج چاه ۱۶۶ آزادگان جنوبی، قبل از نصب در دکل ۲۰۱ عملیات اکتشاف نفت

بدینوسیله در مورخه تست‌های سطحی تاج چاه X-Mass Tree Solid Block "T" Type 4 – 1/16" 10k, MSP مرتبط به چاه شماره 166 آزادگان جنوبی با حضور نماینده محترم کارفرما (پتروپارس) در محل دستگاه 201 عملیات DRILEX اکتشاف نفت، قبل از نصب بر روی تاج چاه به شرح ذیل انجام پذیرفت:

- Body Pressure Test of X – Mass Tree Solid Block w/ 500psi, 5min & 6000psi, 15min "OK" S/N: CT1739N160006 A/0
- Inflow Pressure Test of 4 – 1/16" Production (WING) Valve w/ 500psi, 5min & 6000psi, 15min "OK". S/N: 002929BN160013
- Inflow Pressure Test of 4 – 1/16" Dipping (SWAB) Valve w/ 500psi, 5min & 6000psi, 15min "OK". S/N:008929LN160006
- Inflow.Pressure Test of 4 – 1/16" Kill Valve w/ 500psi, 5min & 6000psi, 15min "OK" S/N: 002929BN160019
- Inflow Pressure Test of 4 – 1/16" Surface Safety Valve w/ 500psi, 5min & 6000psi, 15min "OK". S/N: 096041-SYN160027
- Inflow & Out Flow Pressure Test of 4 – 1/16" Top Master Valve w/ 500psi, 5min & 6000psi, 15min "OK". S/N: 008929KN160006
- Pressure Test of 2SV Actuator w/ 1500psi, 15min "OK".

– گراف مربوط به تست فشار پیوست صورتجلسه گردید.

ناظر عملیات حفاری
شرکت ماهان صنعت آرتا

نماینده محترم تکمیل چاه کارفرما
شرکت مشاوران انرژی تهران

ماهان صنعت آرتا
Eyvazi
Drilling Supervisor
South Azadegan Project
Rig No: 201 DDC
EPCIC CONTRACTOR Date: ۱۴۰۴/۸/۲۳

Figure 8-4: AZNS-166 Wellhead MOM Befor Installation



تاریخ: ۱۴۰۴/۰۸/۲۸
پیوست: دارد

بسمه تعالی

موضوع: صورتجلسه تست‌های پس از نصب تاج و ولهد چاه ۱۶۶ آزادگان جنوبی بعد از نصب در دکل ۲۰۱ عملیات اکتشاف نفت

بدینوسیله در مورخه ۱۴۰۴/۰۸/۲۸ تست‌های تاج چاه X-Mass Tree Solid Block "T" Type 4 – 1/16" 10k, MSP DRILEX و ولهد چاه شماره 166 آزادگان جنوبی با حضور نماینده محترم تکمیل چاه کارفرما و نماینده عملیات حفاری ماهان صنعت آریا در محل دستگاه حفاری ۲۰۱ عملیات اکتشاف نفت بعد از نصب بر روی چاه به شرح ذیل انجام پذیرفت:

- Body Pressure Test of X – Mass Tree Solid Block w/ 10k 11" * 4 – 1/16" 10k Tubing Head Adaptor (BTM MASTER VALVE) 10k MSP/DRILEX w/ 6000psi for 15min, "OK". S/N: 2279266A-S160003
- Pressure Test TBG HGR Metal Seal to 1000psi for 5min, 6000psi for 15min, "OK".
- Pressure Test F–Seal & Ring Gasket between T.H.S & Tubing Head Adaptor (BTM MASTER VALVE) to 6000psi for 15min, "OK".
- Pressure Test Neck of TBG HGR F-Seal to 6000psi for 15min, "OK".
- Pressure Test 1/4" Control Line (CL) to 6000psi for 15min, "OK".

– فشار تمامی دالیزها بررسی گردید که فشار آنها صفر بود.
– خروجی کنترل لاین شیر ایمنی درون چاهی در خلاف جهت شیر اصلی پایینی می‌باشد
– گراف مربوط به تست فشار پیوست صورتجلسه گردید.

ناظر عملیات حفاری
شرکت ماهان صنعت آریا

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No: 201 OEOC
EPDS CONTRACTOR Date: ۱۴۰۴/۸/۲۸

نماینده محترم تکمیل چاه کارفرما
شرکت مشاوران انرژی تهران

Figure 8-5: AZNS-166 Wellhead MOM After Installation

9. Drilling Fluid Information

Hole size (in)	Casing size (in)	CSG Depth (m MD)	Drilling Fluid system	Mud Properties
26"	20"	147 M	Already has been drilled.	
17 ½"	13 3/8"	1338 M	Already has been drilled.	
12 ¼"	9 5/8"	1764 M	Already has been drilled.	
8 ½"	7" Liner	1609 M – 4193 M	Already has been drilled.	
6 1/8"	4 1/2" Liner	4133 M- 4279 M	Already has been drilled.	

9.1 Interval Remark

Operation Remark

Spud the rig @ 27-Oct-2025 on AZN-166. Work on well head & set the protection sleeve, Kill the well by CT with 83 pcf mud, confirm uniform 83 PCF In/Out, flow check for 1 Hr "STATIC".

POOH wit CT to surface while flow check the well with Static. Unset packer, try to establish the mud circulation connection several times with "NO SUCC", POOH completion string to surface, while L/D completion string.

RIH with 8 3/8” M.M.J. MILL + 9 5/8" scraper to 1609 m (L.LAP), POOH to surface.

RIH with 6" junk mill BHA to 4133 m (4 1/2" L.LAP), Circulation bottoms up and then POOH to surface.

RIH with 3 1/2" M.M.J. MILL to 4275.5 m, circulation mud to uniform MW in/out 83 PCF, Pumped & spot 20 bbl cacl2 brine @ bottom, and POOH to surface.

Drilling Fluid Remark

Based on client decision kill the well with 83 PCF Salt/Polymer mud was used for commencing this interval. The MW increased up to by adding Limestone Powder up to 83 PCF at end of this interval.

Treated frequently with essential chemical such as caustic soda as Alkalinity controller to adjust pH, Starch LV for control FL, Soda Ash for control hardness & Xanthan gum as Viscosifier.

9.2 Drilling Fluid type

FLUID PROPERTIES RECAP					
KCL Pol Mud		Drilling start	Range		Drilling End
MW (min)	pcf	83	83	83	83
Funnel Viscosity	sec/qt	42	41	42	42
PV	cps	14	11	14	11
YP	lb/100sq.ft	12	11	12	12
pH		9.1	9.1	9.1	9.1
Cl (NaCl)	mg/L	180,000	176,000	180,000	176,000
Total Hardness	mg/L	920	920	920	920
Ca Hardness	mg/L	800	800	800	800

Table 9-1: AZNS-166 Fluid Properties Recap Table

9.3 Material Consumption Analysis

Products	Units Used	Unit wt lbs	Total wt	Effective Concentration
Bentonite	1	2,200	2,200 lbs	0.00 ppb
Caustic Soda	20	55	1,100 lbs	0.62 ppb
Limestone	91	2,200	200,200 lbs	113.21 ppb
Salt (NaCl)	76	2,200	167,200 lbs	94.55 ppb
Starch LV	116	55	6,380 lbs	3.61 ppb
Soda ASH	14	55	770 lbs	0.44 ppb
Xanthan Gum	26	55	1,430 lbs	0.81 ppb

Initial Volume	0.0 bbl
Total Volume Built	1,768.4 bbl
Volume received	0.0 bbl
Volume Returned	0.0 bbl
Total Volume Consumed	893 bbl
Volume Transfer to Next Section	875.4 bbl

Table 9-2: AZNS-166 Material Consumption Analysis Table

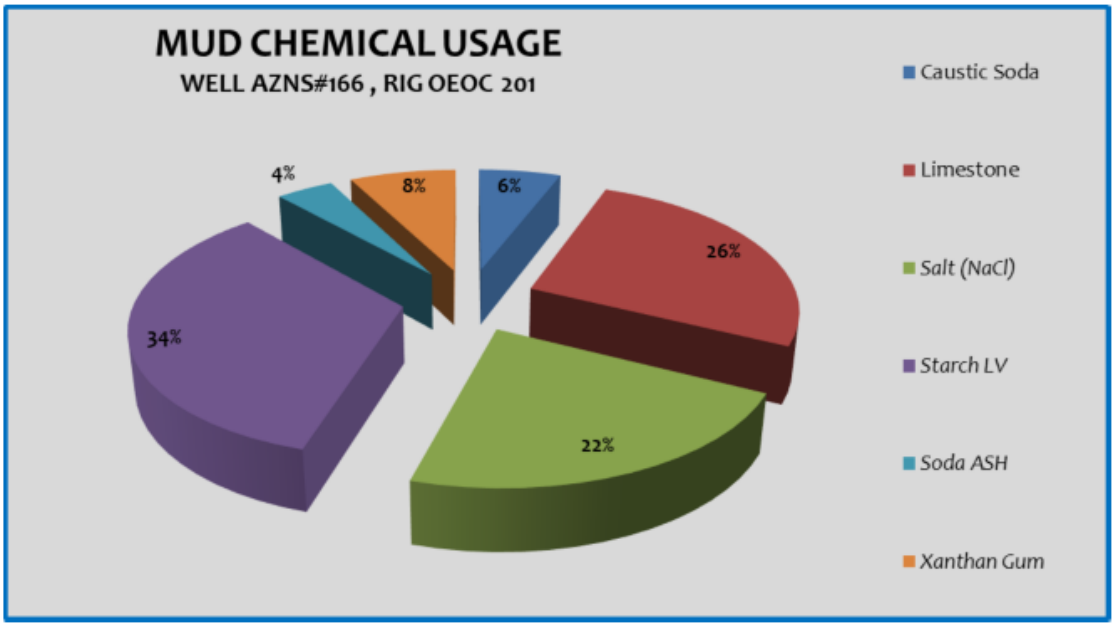


Figure 9-1: AZNS-166 Mud Chemical Usage

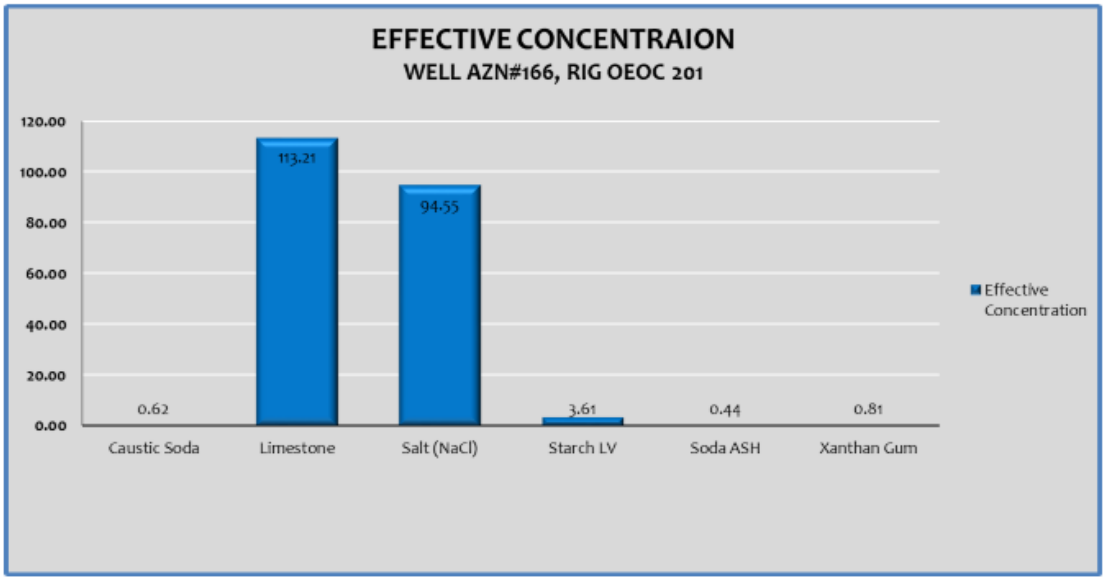


Figure 9-2: AZNS-166 Effective Concentration

9.4 Volume Analysis

WELL AZN#166, RIG OEOC 201 VOLUME ANALYSIS		
Initial Volume	bbls	0.0
Received Volume	bbls	0.0
Volume Return	bbls	0.0
Volume Built	bbls	1,768.4
Surface Losses/Dumped	bbls	893.0
Formation Losses	bbls	0.0
Total Losses	bbls	893.0
Volume Transfer Out	bbls	875

Table 9-3: AZNS-166 Volume Analysis Table

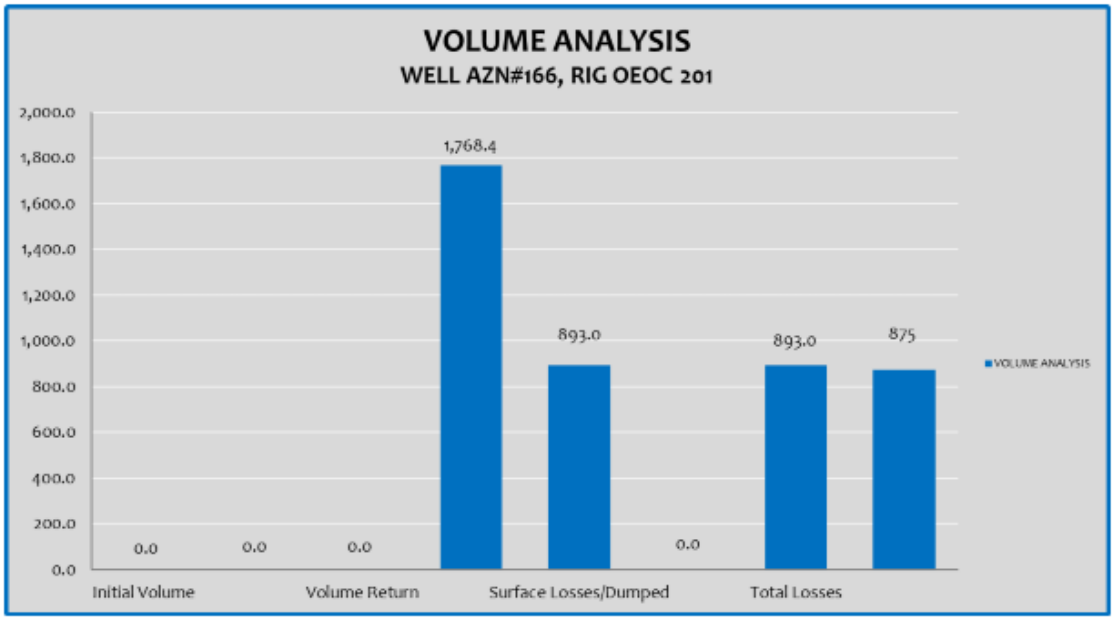


Figure 9-3: AZNS-166 Volume Analysis Chart

9.5 Daily volume Breakdown

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
27-Oct-25	01	830.1	0	0
28-Oct-25	02	208.5	0	0
29-Oct-25	03	167.3	117	0
30-Oct-25	04	150.6	16	0
31-Oct-25	05	0.0	0	0
1-Nov-25	06	0.0	0	0
2-Nov-25	07	134.4	103	0
3-Nov-25	08	0.0	15	0
4-Nov-25	09	0.5	147	0
5-Nov-25	10	0.0	50	0
6-Nov-25	11	250.5	0	0
7-Nov-25	12	19.1	75	0
8-Nov-25	13	0.0	65	0
9-Nov-25	14	7.4	65	0
10-Nov-25	15	0.0	240	0
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		1,768.4	893	0

Table 9-4: AZNS-166 Daily Volume Break Down Table

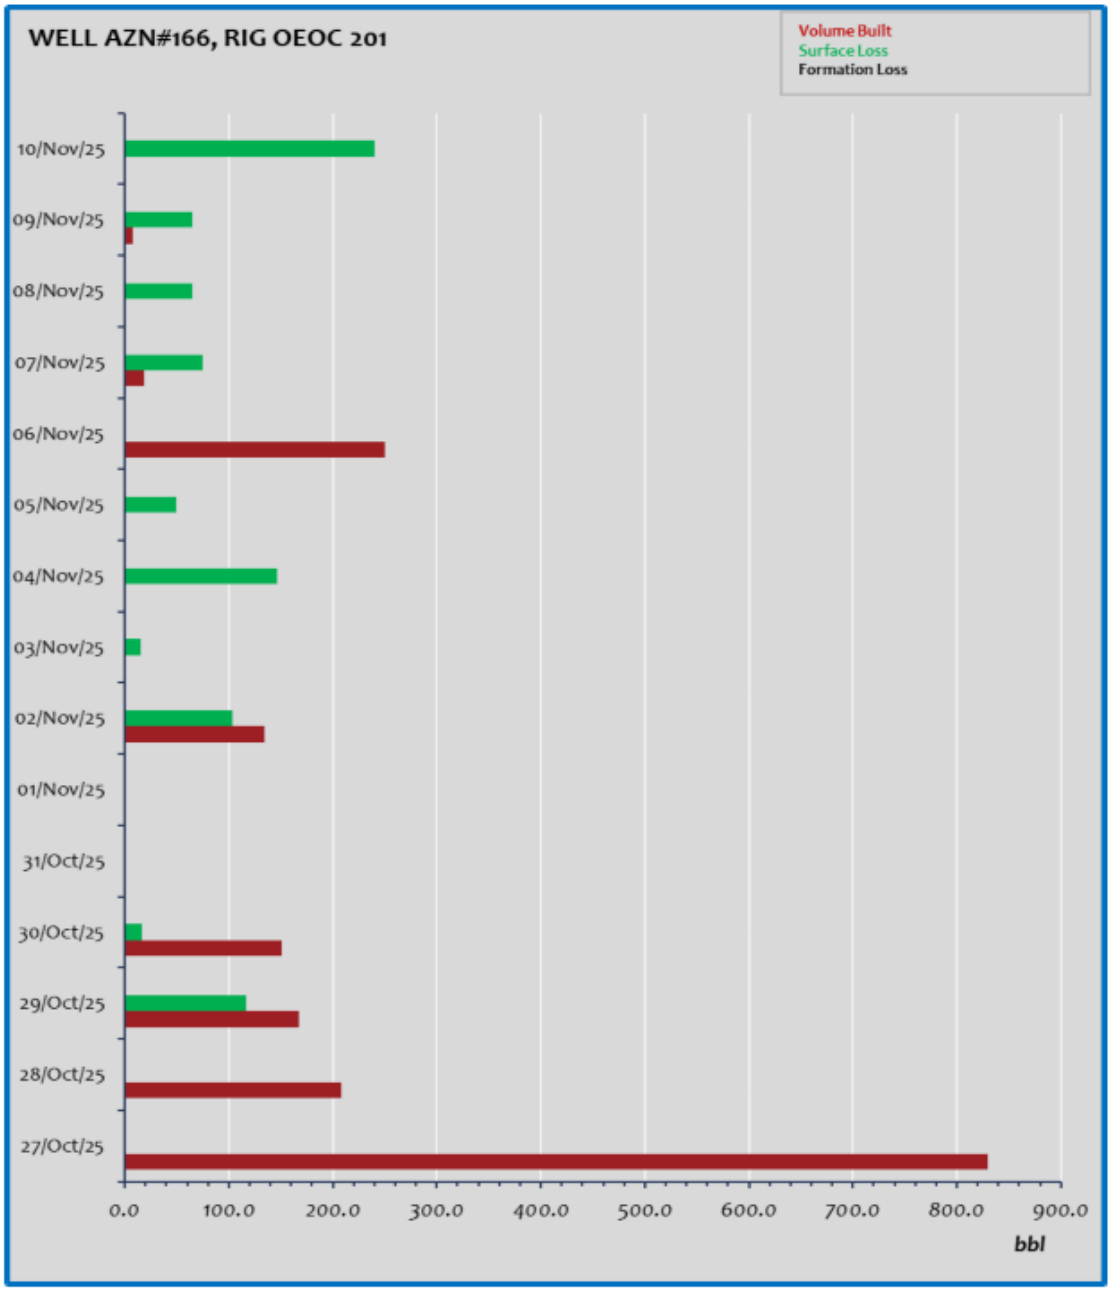


Figure 9-4: AZNS-166 Daily Volume Break Down Chart

9.6 Loss Distribution

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
27-Oct-25	01	830.1	0	0	0	0	0	0	0	0	0
28-Oct-25	02	208.5	0	0	0	0	0	0	0	0	0
29-Oct-25	03	167.3	0	0	0	0	0	0	0	0	117
30-Oct-25	04	150.6	0	0	0	0	0	0	0	0	16
31-Oct-25	05	0.0	0	0	0	0	0	0	0	0	0
1-Nov-25	06	0.0	0	0	0	0	0	0	0	0	0
2-Nov-25	07	134.4	0	0	0	0	10	0	0	0	93
3-Nov-25	08	0.0	0	0	0	0	15	0	0	0	0
4-Nov-25	09	0.5	0	0	0	0	0	0	0	0	147
5-Nov-25	10	0.0	0	0	0	0	30	0	20	0	0
6-Nov-25	11	250.5	0	0	0	0	0	0	0	0	0
7-Nov-25	12	19.1	0	0	0	0	45	0	20	0	10
8-Nov-25	13	0.0	0	0	0	0	45	0	20	0	0
9-Nov-25	14	7.4	35	0	0	0	30	0	0	0	0
10-Nov-25	15	0.0	70	0	0	0	100	0	70	0	0
Total (bbl)		Volume of Built	Dump/Contaminate	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
		1,768.4	105	0	0	0	275	0	130	0	383.0
Note: Prepared 1217.8 Cacl2 brine r (DMR#10,11,12,13,14,15) that is consider in next section.											

Table 9-5: AZNS-166 Loss Distribution

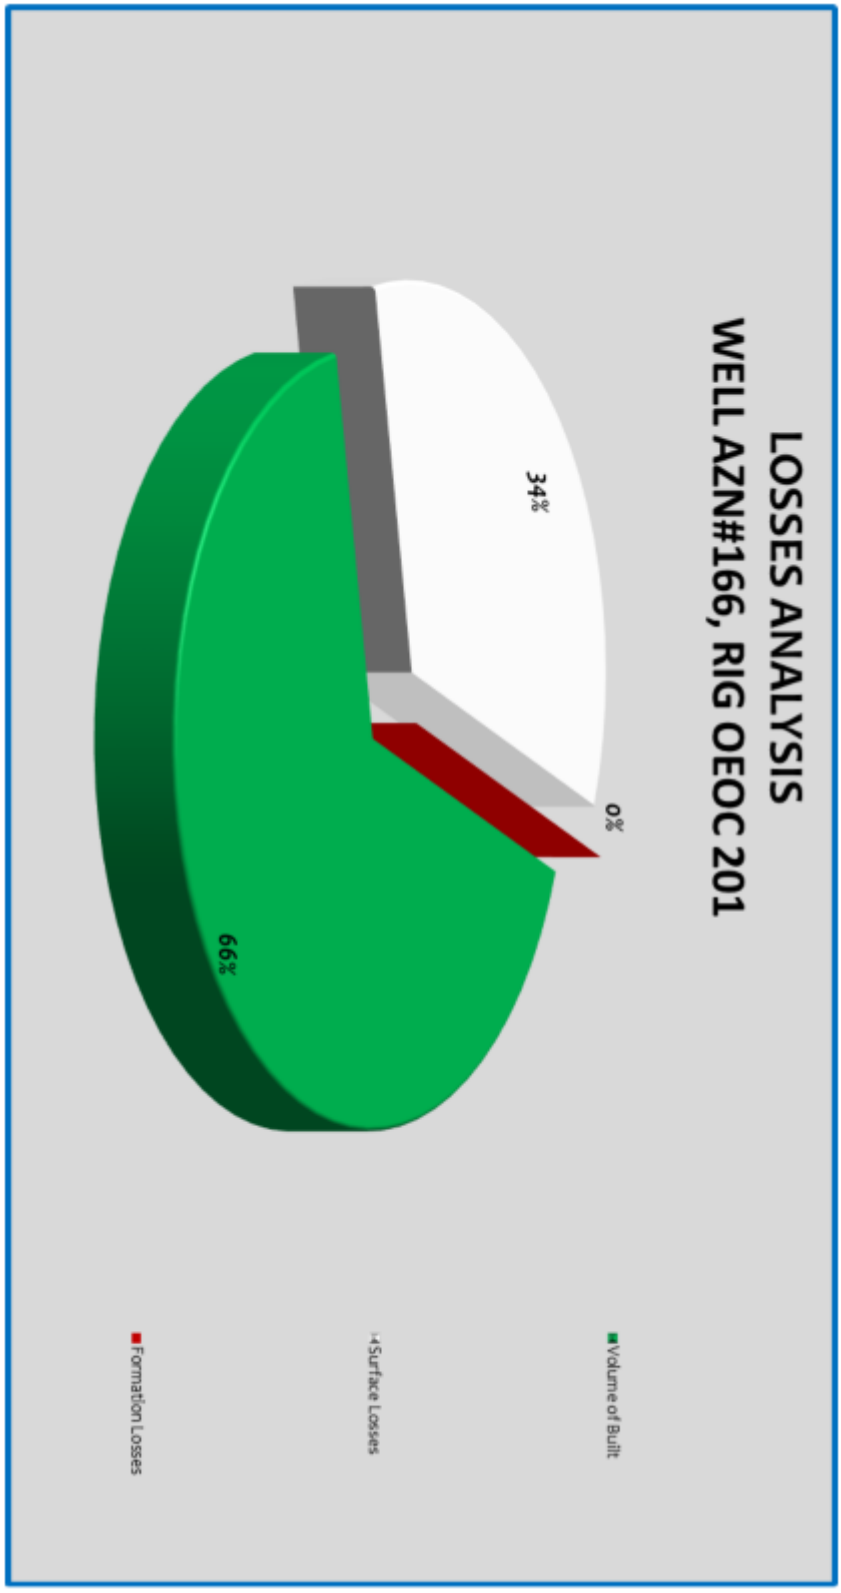


Figure 9-5: AZNS-166 Loss Analysis

9.7 Interval Fluid Properties Recap

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	Chloride	Calcium	Total Hardness	Mud Type
27-Oct-25	4279	83	42	14	12	12	9.1	180,000	800	920	Salt/Poly Mud
28-Oct-25	4279	83	42	14	12	12	9.1	180,000	800	920	Salt/Poly Mud
29-Oct-25	4279	83	42	14	12	12	9.1	180,000	800	920	Salt/Poly Mud
30-Oct-25	4279	83	42	14	12	12	9.1	180,000	800	920	Salt/Poly Mud
31-Oct-25	4279	83	42	14	12	12	9.1	180,000	800	920	Salt/Poly Mud
1-Nov-25	4279	83	42	14	12	12	9.1	180,000	800	920	Salt/Poly Mud
2-Nov-25	4279	83	41	12	11	10	9.1	180,000	800	920	Salt/Poly Mud
3-Nov-25	4279	83	41	12	11	10	9.1	180,000	800	920	Salt/Poly Mud
4-Nov-25	4279	83	42	11	12	9	9.1	176,000	800	920	Salt/Poly Mud
5-Nov-25	4279	83	42	11	12	9	9.1	176,000	800	920	Salt/Poly Mud
6-Nov-25	4279	83	42	11	12	9	9.1	176,000	800	920	Salt/Poly Mud
7-Nov-25	4279	83	42	11	12	14	9.1	176,000	800	920	Salt/Poly Mud
8-Nov-25	4279	83	42	11	12	14	9.1	176,000	800	920	Salt/Poly Mud
9-Nov-25	4279	83	42	11	12	14	9.1	176,000	800	920	Salt/Poly Mud
10-Nov-25	4279	83	42	11	12	14	9.1	176,000	800	920	Salt/Poly Mud

Table 9-6: AZNS-166 Fluid Properties Recap

9.8 Solid Control Disscusion

Rig OEOC 201 has 3 shale shakers were dressed with:

Shaker#1: 120 – 140 Mesh Screen

Shaker#2: 120 – 140 Mesh Screen

Shaker#3: 120 – 140 Mesh Screen

WELL AZN#166, RIG OEOC 201	
Solid Control Equipment Working Hr.s	
Shaker # 01	0
Shaker # 02	96
Shaker # 03	48

Table 9-7: AZNS-166 Solid Control Desscusion

9.9 Inhibited CaCl2 Brine

$CaCL_2$ BRINE

This fluid is recommended to make from fresh water or is solutions made with water and the addition of one or more electrolytes. These fluids do not contain either suspended particles or viscosifiers, which mean neither filtration control or viscosity control, are provided.

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Lime	112	55	6,160	lbs	4.4	ppb
Corrosion Inhibitor	8	55	440	gals	0.4	gpb
H_2S Scavenger	5	55	275	gals	0.3	gpb
O_2 Scavenger	4	55	220	gals	0.2	gpb
Xan.Gum	5	55	275	lbs	2.8	ppb
Cacl2 95% Purity	39	2,200	85,800	lbs	60.7	ppb
Salt	5	2,200	11,000	lbs	110.0	ppb
Cacl2 85% Purity	87	2,200	191,400	lbs	135.5	ppb

Corrosion Inhibitor 0.4 gpb	= 1%vol
H_2S Scavenger 0.2 gpb	= 0.5%vol
O_2 Scavenger 0.2 gpb	= 0.5%vol

Hi-Vis Pill Vol.	100 bbl
Total Volume Built (Completion Fluid)	1,412.8 bbl
Prepared 100 bbls Nacl Brine Hi-vis & Pumped 50 bbls as spacer	

Table 9-8: AZNS-166 Inhibited $CaCl_2$ Brine

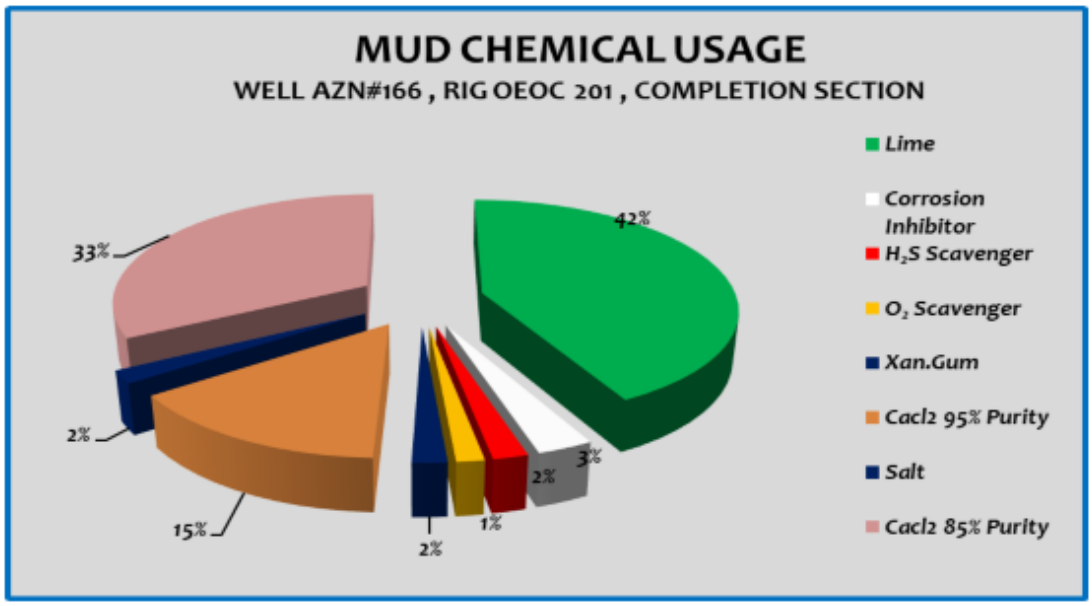


Figure 9-6: AZNS-166 Mud Chemical Usage

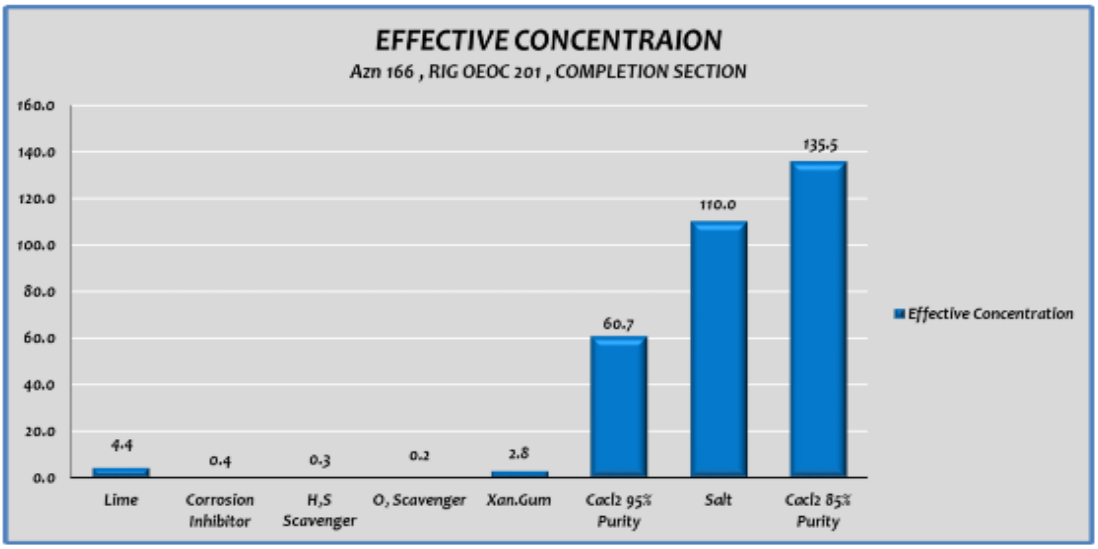


Figure 9-7: AZNS-166 Effective Concentration

10. Waste Management Service

10.1 Operation's Recap

Dewatering system was run totally for 63 hrs. Processing 475^{m3} fluid by using 49^{kg} Poly Aluminum Chloride (PAC), 18^{kg} Poly Electrolyte (Polymer) 350^{kg} Lime & 100^{kg} Soda, 25^{kg} Caustic during the interval.

Dewatering/Water Treatment System	
PROCESSED VOLUME (m3)	475
D-WATERING RUNNING Hrs.	63
COAGULANT (PAC) (kg)	49
FLOCCULANT (POLYMER) (kg)	18
LIME (kg)	350
SODA ASH (kg)	100
CAUSTIC	25

Table 10-1: AZNS-166 Dewatering/Water Treatment System

Date	Treated water (M³)	Cum. Treated Water (M3)	PAC (Kg)	POLYMER (Kg)	LIME (Kg)	CAUSTIC (Kg)	SODA ASH (Kg)
05.Nov.2025	30	30	3	1	0	0	25
06.Nov.2025	0	30	0	0	0	0	0
07.Nov.2025	30	60	3	1	0	0	25
08.Nov.2025	40	100	5	2	0	25	0
09.Nov.2025	0	0	0	0	0	0	0
10.Nov.2025	20	120	5	2	25	0	0
11.Nov.2025	30	150	5	2	50	0	0
12.Nov.2025	60	210	10	3	75	0	0
13.Nov.2025	40	250	0	0	0	0	0
14.Nov.2025	0	0	0	0	0	0	0
15.Nov.2025	0	0	0	0	0	0	0
16.Nov.2025	70	320	0	0	0	0	0
17.Nov.2025	0	0	0	0	0	0	0
18.Nov.2025	85	405	0	0	0	0	0
19.Nov.2025	95	475	0	0	0	0	0
20.Nov.2025	0	0	0	0	0	0	0
21.Nov.2025	0	0	0	0	0	0	0
22.Nov.2025	0	0	0	0	0	0	0
23.Nov.2025	0	0	0	0	0	0	0
24.Nov.2025	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0
	0	0	0	0	0	0	0

Figure 10-1: AZNS-166 chemical consumption and water treatment volumes by date for Completion section

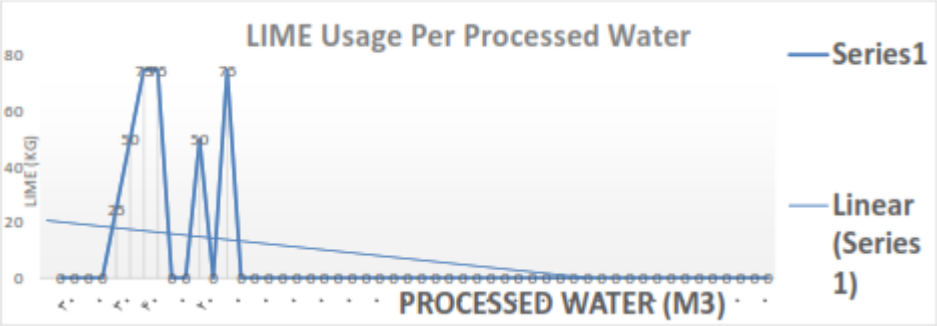


Figure 10-2: AZNS-166 Chart of LIME usage per processed water in Completion section

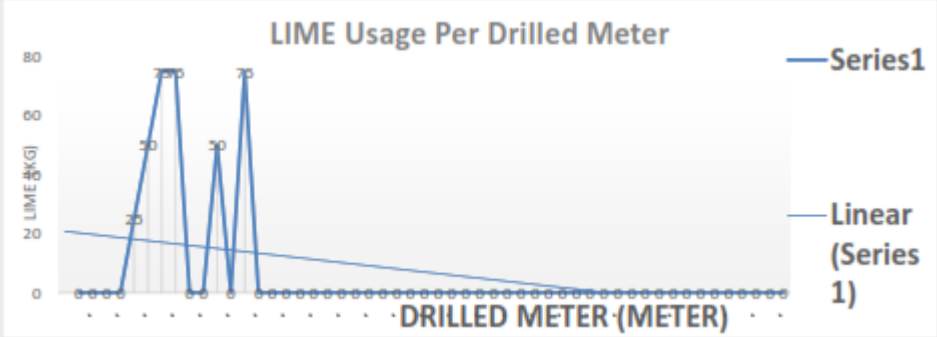


Figure 10-3: AZNS-166 Chart of LIME usage per Drilled Meter in Completion section

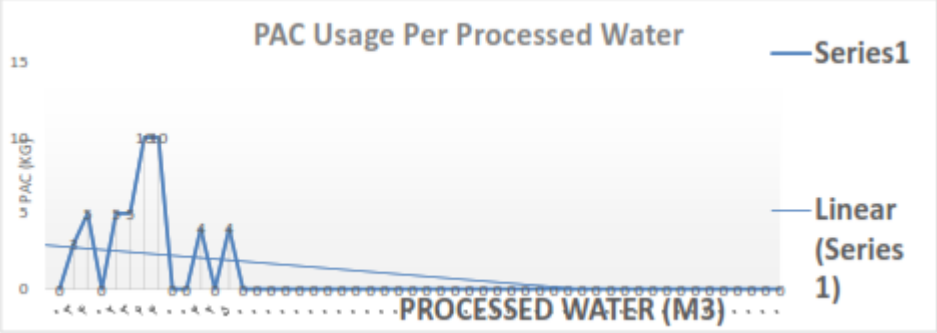


Figure 10-4: AZNS-166 Chart of PAC usage per processed water in Completion section

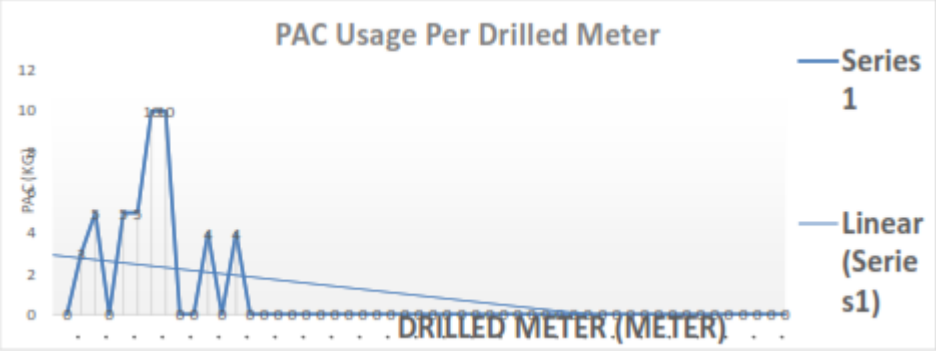


Figure 10-5: AZNS-166 Chart of PAC usage per Drilled Meter in Completion section

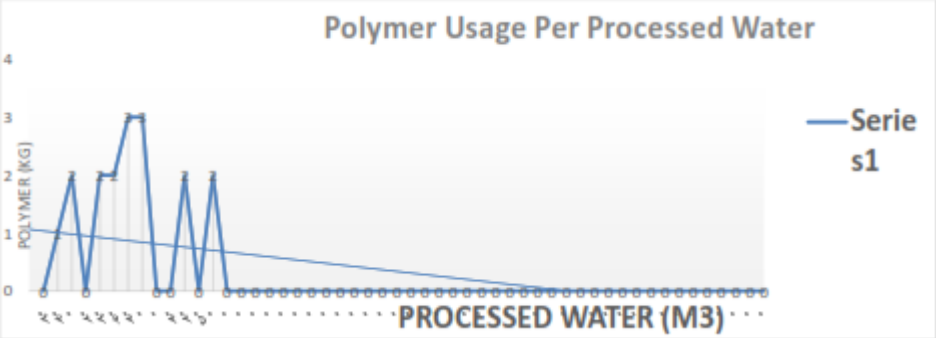


Figure 10-6: AZNS-166 Chart of Polymer usage per processed water in Completion section

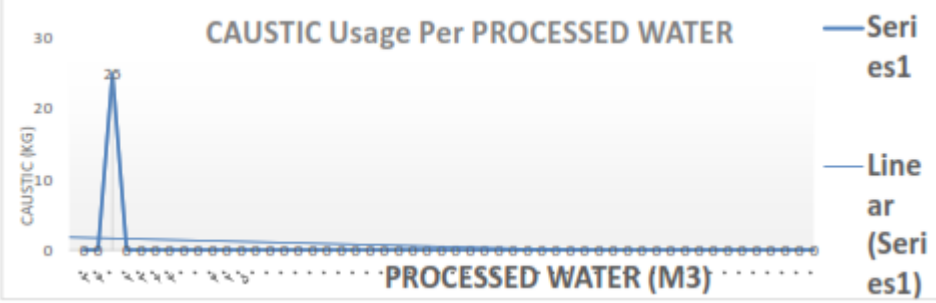


Figure 10-7: AZNS-166 Chart of caustic usage per processed water Completion section

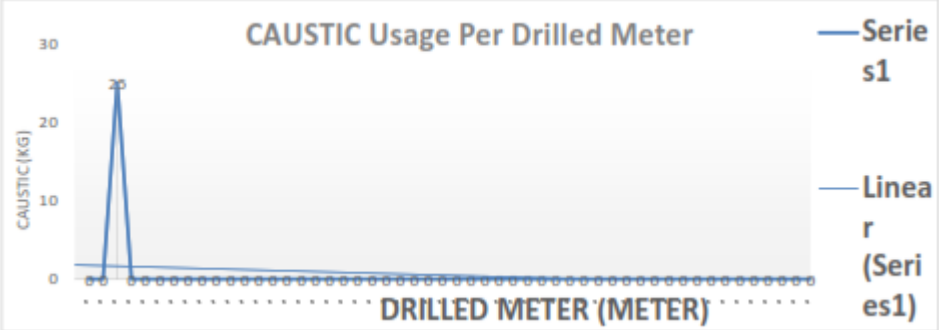


Figure 10-8: AZNS-166 Chart of caustic usage per Drilled Meter in Completion section

REP	Date	Water Properties				
		pH	Total Hardness	Calcium	TSS	Turbidity
Unit		7 - 9	Mg/Lit	Mg/Lit	Mg/lit	mg/Lit

1	05. Nov .2025	Received	7	600	400	Over range	Over range
		Send	7	600	360	33	22
2	06. Nov .2025	Received	7	600	400	Over range	Over range
		Send	7	600	360	33	22
3	07. Nov .2025	Received	7	600	400	Over range	Over range
		Send	7	560	320	32	21
4	08. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	540	320	31	20
5	09. Nov .2025	Received	7	600	400	Over range	Over range
		Send					
6	10. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	540	320	31	20
7	11. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	540	320	50	25
8	12. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	560	320	65	32
9	13. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	560	320	60	29
10	14.	Received	7	600	400	Over ran	Over rang

	Nov .2025					ge	e
		Send	8	560	320	60	29
11	15. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	560	320	60	29
12	16. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	560	360	48	22
13	17. Nov .2025	Received	7	600	400	Over range	Over range
		Send	8	560	360	48	22
14	18. Nov .2025	Received	7	720	560	Over range	Over range
		Send	8	640	400	45	21
15	19. Nov .2025	Received	7	720	560	Over range	Over range
		Send	8	640	400	45	21
16	20. Nov .2025	Received	7	680	440	Over range	Over range
		Send					
17	21. Nov .2025	Received	7	680	440	Over range	Over range
		Send					
18	22. Nov .2025	Received	7	680	440	Over range	Over range
		Send					
19	23. Nov .2025	Received	7	680	440	Over range	Over range
		Send					

20	24.Nov.2025	Received	7	680	440	Over range	Over range
		Send					
21	25.Nov.2025	Received	7	680	440	Over range	Over range
		Send					
22	26.Nov.2025	Received	7	680	440	Over range	Over range
		Send					
23	27.Nov.2025	Received	7	680	440	Over range	Over range
		Send					
24		Received	7	680	440	Over range	Over range
		Send					

Table 10-2: AZNS-166 Water Analysis De-Completion section

11. Well Stimulation & Clean – Up

11.1 Operation Summary

The primary objective of the planned operation on Well-51 is to restore well accessibility, confirm well integrity. The operation commenced with rig-up of slickline equipment followed by successful pressure testing of the surface pressure control system to ensure operational integrity and safe execution throughout the intervention campaign. Following pressure verification, the TMV was opened under zero shut-in wellhead pressure conditions, and slickline was RIH to set the P.S at a depth of 63.7^{m} in order to protect the completion components during the upcoming coiled tubing operations.

Subsequently, a tubing drift and depth verification was performed utilizing a gauge bailer assembly. The SL reached an accessible depth of 2950 mMD, confirming partial well accessibility prior to pulling out of hole to surface. Following completion of SL activities, CT equipment was rigged up and pressure tested according to operational and safety requirements. The initial N2 kick-off operation was then performed by running coiled tubing in hole to 2300 mMD while continuously pumping approximately 2430 gal of N_2 to initiate well unloading and improve fluid mobility inside the wellbore. During the operation, the well remained under continuous monitoring conditions with casing pressure recorded at 32/64 choke setting, wellhead pressure at 0^{psi} and no observable returns at surface.

In order to further condition the wellbore and improve accessibility, CTU was run in hole while pumping approximately 530^{bbl} of returned oil as displacement fluid. During the operation, an obstruction was encountered between 4148 m MD and 4205 m MD. Several attempts were made to remove the obstruction while pumping oil at an estimated rate of 1 bpm and surface pressures ranging between 3500 to 4000^{psi}; however, no significant progress was achieved in passing the restriction. A secondary N2 kick-off operation was subsequently initiated with coiled tubing positioned at approximately 1000 mMD and then run back to 2300 m MD while pumping N_2. Nitrogen returns observed at surface. The CTU string was then POOH to surface with a total N_2 volume of approximately 2235^{gal} pumped during the operation.

Following completion of the CTU activities, slickline operations were resumed using a 3.5” gauge scraper assembly to retrieve the previously installed protection sleeve. The P.S was successfully recovered and a flapper valve functionality test was performed to verify completion barrier integrity. The well was then flowed and continuously monitored to evaluate overall well condition and pressure behavior. During the

monitoring period, annulus pressure was gradually bled down from 1000^{psi} to 100^{psi} under controlled conditions to ensure stable well status. Upon completion of all operational objectives, the well was secured safely for future intervention and production – related activities.


11.2 General Information

Service:	Well testing, Acidizing, Coiled Tubing, S/L, Oil transfer
Operation Date:	23/ January /2026 – 02/ February /2026
Well Type:	Kazhdumi Deviated Well
Fluid Type:	OIL AND GAS
Casing Size:	20", 13 – 3/8", 9 – 5/8, 7", 4 – 1/2"
Tubing Size:	4 1/2" 18.9^{ppf}, L-80 (0 – 1,503.299 mMD); 31/2" 10.2^{ppf} , L-80 (1,503.299 – 2,708.3 mMD)
Producing Interval:	3733 – 3752.95 mMD
Well Objective:	Restore well accessibility, Confirm well integrity
Targer Formation:	kazhdumi
Oil Density (API):	0.30 psi/ft.
Minimum ID:	2.562" @3345.589 mMD, 3 – 1/2" B. NoGo LN
Producing Formation:	Kaz – 2
H_2S Content (%):	Null
CO_2 (mole %):	2.6111
Surface Temperature:	About 70 ^oF
Reservoir Temperature:	238 ^oF @3480 mss (oil datum depth)
Formation Pressure:	Kaz – 2: 4094^{psi}, Kaz – 2-2: 4069^{psi}, Kaz – 4: 4195^{psi}
GOR (scf/stb):	N/A
Formation Fracture Gradiant (psi/ft.):	0.83 ~ 0.84

11.3 Total Operation Results

Executed Operation Flow Chart

Execution Plan	Required Material	Notes
Start		
L/U & Pressure Test		Line/Up and pressure test the equipment incloud SWT , LPU.
R/U SL & Pressure Test		Line/Up pressure test S/L
Set Protection Sleeve		Open TMV[SIWHP :0 psi]and RIH SL for setting protection sleeve at 63.7 m SL BHA: Rope socket 1-7/8" + 11 ft stem 1-7/8" + 4 ft M.jar 1-7/8" + PS 3.437
TD Check via Gauge Bailer		S/L Arrived at2950 m last accessble depth & start POOH SL to surface SL (0.125") BHA: Rope Socket 1.7/8" ,11ft Stem 1.7/8", M.J 5 ft 1.7/8", H.J 3ft 1.7/8", Gauge Bailer 3ft 1.7/8"

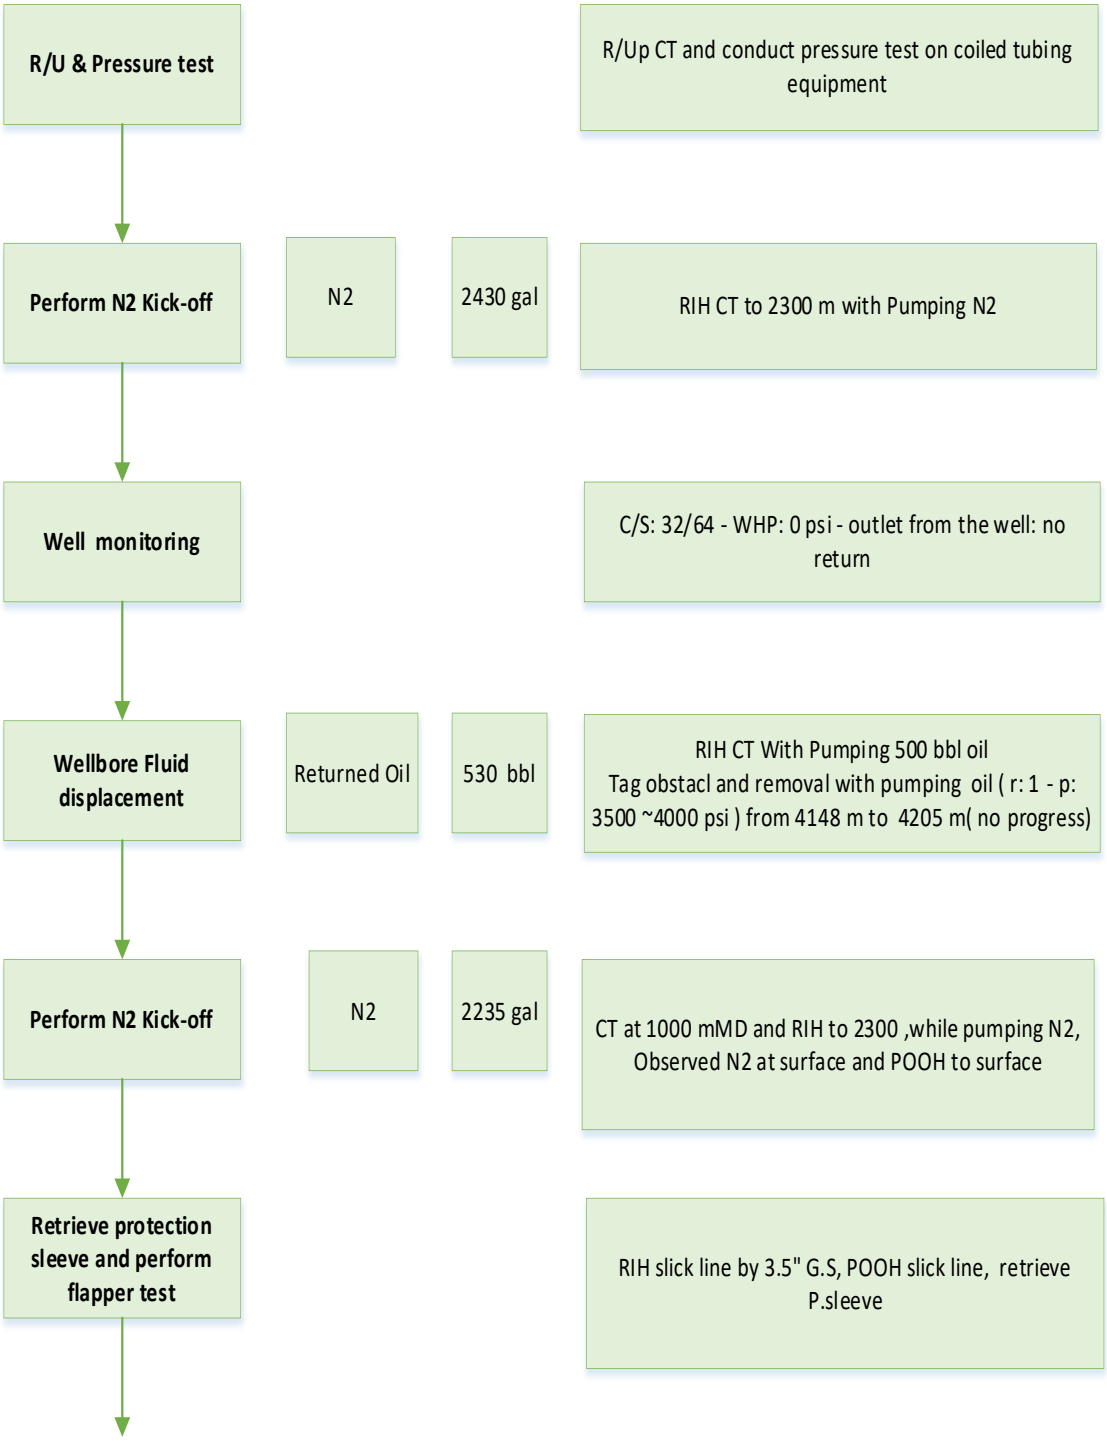
R/U & Pressure test
R/Up CT and conduct pressure test on coiled tubing equipment
Perform N2 Kick-off
N2
2430 gal
RIH CT to 2300 m with Pumping N2
Well monitoring
C/S: 32/64 - WHP: 0 psi - outlet from the well: no return
Wellbore Fluid displacement
Returned Oil
530 bbl
RIH CT With Pumping 500 bbl oil
Tag obstacl and removal with pumping oil (r: 1 - p: 3500 ~4000 psi) from 4148 m to 4205 m(no progress)
Perform N2 Kick-off
N2
2235 gal
CT at 1000 mMD and RIH to 2300 ,while pumping N2, Observed N2 at surface and POOH to surface
Retrieve protection sleeve and perform flapper test
RIH slick line by 3.5" G.S, POOH slick line, retrieve P.sleeve

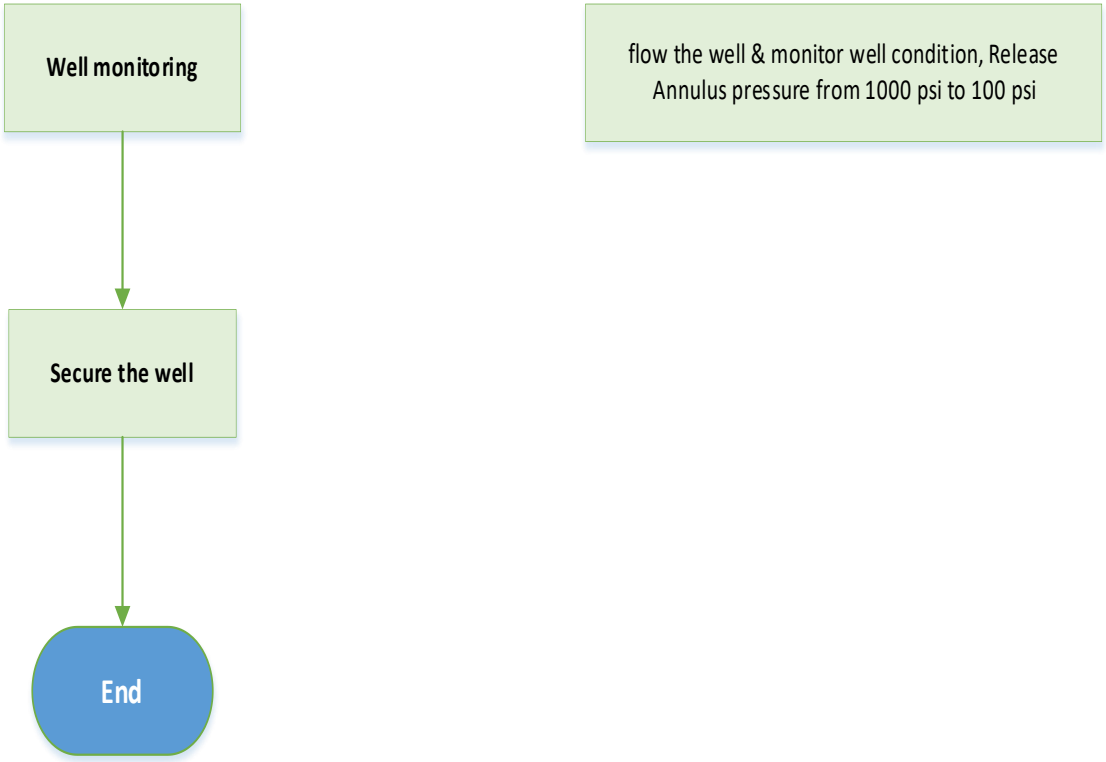


Figure 11-1: AZNS-166 Executed Operation Flow Chart

Daily Operation Summary

Date	Operation Summary
23 – Jan – 2026	Moving equipment, R/U equipment (S/L), set P.S at 63.7^{m}, Open TMV, SIWHP: 0^{psi}, RIH S/L to Max accessible TD (2950^{m})
24 – Jan – 2026	Line Up CT & N_2 Track, Perform N_2 lifting (T.V: 2430 gal)
25 – Jan – 2026	Well head pressure monitoring (C/S: closed - WHP: 0 psi - outlet from the well: no return)
26 – Jan – 2026	with on reserved 400 bbl oil from CETEP
27 – Jan – 2026	PT of CTU
28 – Jan – 2026	RIH CT With Pumping 500^{bbl} oil, Tag obstacle and removal with pumping oil (r: 1 - p: 3500 ~ 4000 psi) from 4148^{m} to 4205^{m}, no progress
29 – Jan – 2026	Finish pumping return oil and perform N_2 lifting (RIH from 1000^{m} to 2300^{m} while pumping 2235 – gal N_2) and POOH to surface, R/U and pressure testing SL, RIH slick line by 3.5" G.S in order to retrieve P.S, flow the well & monitor well condition, SIWHP: 800^{psi}.
30 – Jan – 2026	flowing the well & monitor well condition
31 – Jan – 2026	flowing the well & monitor well condition
01 – Fab – 2026	flowing the well & monitor well condition, All personnel and equipment released

Table 11-1: AZNS-166 Daily Operation Summary

Sequence of Operation

Date	Time	Sequence
23 – Jan – 2026	17:00	Moving equipment and material to pad 9 (Recieved CTU & Pump truck& N2 truck)
23 – Jan – 2026	17:30	Start R/U equipment (S/L)
23 – Jan – 2026	18:30	Performed Wrap test @ OK
23 – Jan – 2026	19:00	Performed S/L pull test 1100 lb,OK
23 – Jan – 2026	20:00	R/U S/L PCE (BOP& Lubricator
23 – Jan – 2026	20:30	Performed S/L BOP function Test
23 – Jan – 2026	21:00	Performed P/T S/L Lubricator & BOP , 300/5500 psi, 5/15min , Against TMV, OK
23 – Jan – 2026	21:45	Open TMV (SIWHP:0 psi)
23 – Jan – 2026	21:50	Start RIH S/L to set P.S
23 – Jan – 2026	22:00	S/L Set P.S @ 63.7m & POOH
23 – Jan – 2026	22:10	Close TMV
23 – Jan – 2026	22:10	N/D Lubricator, S/L changed BH @ S/L(0.125") BHA: Rope Socket 1.7/8" ,11ft Stem 1.7/8", M.J 5 ft 1.7/8", GS Running Tools , P.Sleeve 3.437" AF , ID : 2.9"
23 – Jan – 2026	22:30	N/U Lubricator ,P/T 300/5500psi ,5/15min Against TMV. Open TMV (SIWHP:0 psi)@ Start RIH S/L to Max acceseble TD
23 – Jan – 2026	23:30	S/L Arrived at 2950m last accessble depth
23 – Jan – 2026	24:00	S/L at surface close TMV&DPV @ S/L(0.125") BHA: Rope Socket 1.7/8" ,11ft Stem 1.7/8", M.J 5 ft 1.7/8", H.J 3ft 1.7/8", Gauge Bailer 3ft 1.7/8"
24 – Jan – 2026	00:30	R/D S/L PCE
24 – Jan – 2026	00:30	Perform Connector Pull test w/ 19Klb
24 – Jan – 2026	02:30	N/U CT BOP
24 – Jan – 2026	03:00	Perform BOP Ram function Open/Close test, OK
24 – Jan – 2026	03:30	Perform Blind Ram P/T , 300/5500psi, 5/15min, 03:30 OK

24 – Jan – 2026	04:30	CT(1.5", 0.125") BHA : Roll on Connector, DFCV, Nozzle 5 port @ R/U INJ.H.
24 – Jan – 2026	05:30	Perform DFCV differential P/T w/ 1500 psi, OK
24 – Jan – 2026	06:30	Perform Pipe Ram test ,OK
24 – Jan – 2026	07:30	Start Line Up & Transfer N2 Tank to N2 Pump
24 – Jan – 2026	08:30	Finished Cool Down
24 – Jan – 2026	09:00	Start RIH CT With Pumping N2 @ BHA: Roll On Connector +Doul Flapper Check Valve +Wash Nozzle 5 port
24 – Jan – 2026	14:30	CTU Arrived at 2300m depth
24 – Jan – 2026	16:50	Finished Pumping N2 @ (T.V: 2430 gl) (outlet from the well: N2)
24 – Jan – 2026	23:55	Well head pressure monitoring @ 16:50 to 23:55 (C/S: 32/64 - WHP: 0 psi - outlet from the well: no return)
24 – Jan – 2026	24:00	Close the well from adj chock
25 – Jan – 2026	00:00	CTU POOH from 2300m depth to surface
25 – Jan – 2026	02:30	CTU Arrived surface
25 – Jan – 2026	02:35	Well head pressure monitoring (C/S: closed - WHP: 0 psi - outlet from the well: no return)
25 – Jan – 2026	11:30	Well head pressure monitoring (C/S: closed - WHP: 0 psi - outlet from the well: no return) R/D the injector CTU
27 – Jan – 2026	14:15	filled up the CT reel with 25 bbl water
27 – Jan – 2026	14:40	Rig up the injector CTU
27 – Jan – 2026	14:50	perform pressure test the rubber striper and injector and BOP with(5500 psi)(ok)
28 – Jan – 2026	05:15	displacement CT reel with 30 bbl Oil at (r: 1 - P: 2000 ~2300)
28 – Jan – 2026	05:45	wait on LPU Run Data acquisition
28 – Jan – 2026	08:00	Opened TMV
28 – Jan – 2026	08:05	Start RIH CT With Pumping 500 bbl oil @ (C/S: 36/64)
28 – Jan – 2026	14:40	Tag obstacle and removal with pumping oil (r: 1 - p: 3500 ~4000 psi) from(4148 m) to (4205 m) @ 14:40 to 23:15 #(no progress)
28 – Jan – 2026	20:00	Received 1 Load (150 bbl) oil on the location

28 – Jan – 2026	23:15	Start POOH CT from 4205 m to 1000 m with pumping oil
29 – Jan – 2026	03:00	Start cool down N2
29 – Jan – 2026	03:30	CT at 1000 mMD, stop pumping crude oil (T.V: 50 bbl) and start pumping N2
29 – Jan – 2026	03:45	Increase C/S from 32 to 64/64" adj
29 – Jan – 2026	05:00	Observed N2 at surface
29 – Jan – 2026	05:15	RIH CT from 1000 to 2300 mMD
29 – Jan – 2026	07:15	CT reached to 2300 mMD, continue N2 lift
29 – Jan – 2026	11:00	Finished Pumping N2 @ 11:00 (T.V: 2235 gl) (outlet from the well: N2) @ CTU POOH from 2300m depth to surface
29 – Jan – 2026	13:50	CTU Arrived surface
29 – Jan – 2026	13:55	Closed TMV
29 – Jan – 2026	14:00	Start R/D CT
29 – Jan – 2026	15:30	Finished R/D CT
29 – Jan – 2026	16:00	R/U slick line (SIWHP: 800 psi).
29 – Jan – 2026	16:30	Pressure test up to 5000 psi, ok
29 – Jan – 2026	16:45	Start RIH slick line by 3.5" G.S
29 – Jan – 2026	17:00	POOH slick line , retrieve P.s successfully @ Slick line BHA: Rope Socket 1.7/8" ,11ft Stem 1.7/8", M.J 5 Ft 1.7/8", 3.5 " GS tool. P.S spec: 3.437" AF , ID : 2.9".
29 – Jan – 2026	17:00	flow the well & monitor well condition
30 – Jan – 2026	00:00	flow the well & monitor well condition.
31 – Jan – 2026	00:00	flow the well & monitor well condition.
01 – Feb – 2026	00:00	flow the well & monitor well condition.
01 – Feb – 2026	11:30	All personnel and equipment released.
End Of Job		

Table 11-2: AZNS-166 Sequence of Operation

Summary of Pumping Data

Item	Pumped Material	Planned	Total used	Unit
1	Diesel	1,376	0	BBL
2	HCL 32%	129	0	BBL
3	Fresh Water	318	35	BBL
4	Returned oil	0	530	BBL
5	Surfactant	307	0	USG
6	Mutual Solvent	598	0	USG
7	Iron Reducing Agent (WA-iRED 457)	307	0	USG
8	Iron Control Agent (WA-450N)	81	0	USG
9	Corrosion Inhibitor Aid	458	0	USG
10	Anti-sludge Agent	352	0	USG
11	Non-Emulsifier Agent	352	0	USG
12	Corrosion Inhibitor	311	0	USG
13	Clay Stabilizer	255	0	USG
14	Asphaltene Solvent	2,310	0	
15	Liquid Nitrogen	14,000	4660	USG
16	Ammonium Bifluoride (ABF)	28	0	Sacks
17	Caustic Soda	8	0	Sacks

Table 11-3: AZNS-166 Total Consumble Planned & Used

11.3.1.1 Summary of Pumping Operation Results

Summary Of Pumping Operation Results					
Operation	Start Date and time DD/MM/YYYY, HH:MM	End Date and time DD/MM/YYYY, HH:MM	Volume		Unit
			USED	PLANNED	
N_2 Lifting	24 – January – 2026, 09:00	24 – January – 2026, 14:30	2430	2430	GAL
Pumping Returned Oil	28 – January – 2026, 05:15	29 – January – 2026, 03:15	530	0	BBL
N_2 Lifting	29 – January – 2026, 03:30	29 – January – 2026, 11:00	2230	2235	GAL

Table 11-4: AZNS-166 Summary of Pumping Operation Results

11.3.1.2 Pumping Operation Results & Plots

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	8:29	Returned Oil	36	N/A	204	805	0.2	0.3
28 – Jan – 2026	8:33	Returned Oil	36	N/A	254	1550	0.4	1.7
28 – Jan – 2026	8:37	Returned Oil	36	N/A	308	7	0.0	2.1
28 – Jan – 2026	8:41	Returned Oil	36	N/A	367	6	0.0	2.1
28 – Jan – 2026	8:45	Returned Oil	36	N/A	432	5	0.0	2.1
28 – Jan – 2026	8:50	Returned Oil	36	N/A	506	7	0.0	2.1
28 – Jan – 2026	8:54	Returned Oil	36	N/A	510	805	0.2	2.7
28 – Jan – 2026	8:58	Returned Oil	36	N/A	590	1179	0.3	3.8
28 – Jan – 2026	9:02	Returned Oil	36	N/A	611	11	0.0	4.2
28 – Jan – 2026	9:06	Returned Oil	36	N/A	666	7	0.0	4.2
28 – Jan – 2026	9:10	Returned Oil	36	N/A	720	8	0.0	4.2
28 – Jan – 2026	9:15	Returned Oil	36	N/A	793	873	0.2	4.3
28 – Jan – 2026	9:19	Returned Oil	36	N/A	852	43	0.0	5.0
28 – Jan – 2026	9:23	Returned Oil	36	N/A	921	10	0.0	5.0
28 – Jan – 2026	9:27	Returned Oil	36	N/A	981	10	0.0	5.0
28 – Jan – 2026	9:31	Returned Oil	36	N/A	1001	7	0.0	5.0
28 – Jan – 2026	9:35	Returned Oil	36	N/A	1057	1319	0.3	5.8

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	9:40	Returned Oil	36	N/A	1141	12	0.0	6.1
28 – Jan – 2026	9:44	Returned Oil	36	N/A	1214	8	0.0	6.1
28 – Jan – 2026	9:48	Returned Oil	36	N/A	1272	7	0.0	6.1
28 – Jan – 2026	9:52	Returned Oil	36	N/A	1343	1377	0.3	6.7
28 – Jan – 2026	9:56	Returned Oil	36	N/A	1404	12	0.0	7.0
28 – Jan – 2026	10:00	Returned Oil	36	N/A	1449	9	0.0	7.0
28 – Jan – 2026	10:05	Returned Oil	36	N/A	1516	9	0.0	7.0
28 – Jan – 2026	10:09	Returned Oil	36	N/A	1505	7	0.0	7.0
28 – Jan – 2026	10:13	Returned Oil	36	N/A	1523	10	0.0	7.0
28 – Jan – 2026	10:17	Returned Oil	36	N/A	1582	1235	0.3	7.3
28 – Jan – 2026	10:21	Returned Oil	36	N/A	1648	1357	0.3	8.6
28 – Jan – 2026	10:25	Returned Oil	36	N/A	1708	12	0.0	9.0
28 – Jan – 2026	10:30	Returned Oil	36	N/A	1776	10	0.0	9.0
28 – Jan – 2026	10:34	Returned Oil	36	N/A	1829	10	0.0	9.0
28 – Jan – 2026	10:38	Returned Oil	36	N/A	1882	11	0.0	9.0
28 – Jan – 2026	10:42	Returned Oil	36	N/A	1936	8	0.0	9.0
28 – Jan – 2026	10:46	Returned Oil	36	N/A	1992	10	0.0	9.0
28 – Jan – 2026	10:50	Returned Oil	36	N/A	2004	11	0.0	9.0
28 – Jan – 2026	10:55	Returned Oil	36	N/A	2070	853	0.2	9.7

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	10:59	Returned Oil	36	N/A	2138	932	0.3	10.7
28 – Jan – 2026	11:03	Returned Oil	36	N/A	2199	12	0.0	11.0
28 – Jan – 2026	11:07	Returned Oil	36	N/A	2269	10	0.0	11.0
28 – Jan – 2026	11:11	Returned Oil	36	N/A	2322	11	0.0	11.0
28 – Jan – 2026	11:15	Returned Oil	36	N/A	2394	11	0.0	11.0
28 – Jan – 2026	11:20	Returned Oil	36	N/A	2460	856	0.3	12.1
28 – Jan – 2026	11:24	Returned Oil	36	N/A	2516	17	0.0	13.0
28 – Jan – 2026	11:28	Returned Oil	36	N/A	2522	10	0.0	13.0
28 – Jan – 2026	11:32	Returned Oil	36	N/A	2581	865	0.3	13.8
28 – Jan – 2026	11:36	Returned Oil	36	N/A	2588	1351	0.4	15.1
28 – Jan – 2026	11:40	Returned Oil	36	N/A	2601	2580	0.7	17.3
28 – Jan – 2026	11:45	Returned Oil	36	N/A	2599	3379	0.8	20.6
28 – Jan – 2026	11:49	Returned Oil	36	N/A	2617	3738	0.8	24.0
28 – Jan – 2026	11:53	Returned Oil	36	N/A	2627	2931	0.7	27.1
28 – Jan – 2026	11:57	Returned Oil	36	N/A	2672	2894	0.7	30.1
28 – Jan – 2026	12:01	Returned Oil	36	N/A	2696	1644	0.5	32.4
28 – Jan – 2026	12:05	Returned Oil	36	N/A	2733	1614	0.5	34.6
28 – Jan – 2026	12:10	Returned Oil	36	N/A	2772	1722	0.5	36.8
28 – Jan – 2026	12:14	Returned Oil	36	N/A	2808	1731	0.5	38.8

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	12:22	Returned Oil	36	N/A	2851	1846	0.5	42.4
28 – Jan – 2026	12:26	Returned Oil	36	N/A	2875	1866	0.5	44.2
28 – Jan – 2026	12:30	Returned Oil	36	N/A	2922	1902	0.4	46.0
28 – Jan – 2026	12:35	Returned Oil	36	N/A	2969	1925	0.4	47.8
28 – Jan – 2026	12:39	Returned Oil	36	N/A	3010	1993	0.4	49.5
28 – Jan – 2026	12:43	Returned Oil	36	N/A	3013	2030	0.4	51.2
28 – Jan – 2026	12:47	Returned Oil	36	N/A	3060	2102	0.4	52.9
28 – Jan – 2026	12:51	Returned Oil	36	N/A	3111	2139	0.4	54.5
28 – Jan – 2026	12:55	Returned Oil	36	N/A	3142	2143	0.4	56.0
28 – Jan – 2026	13:00	Returned Oil	36	N/A	3193	2178	0.4	57.5
28 – Jan – 2026	13:04	Returned Oil	36	N/A	3243	2201	0.4	59.0
28 – Jan – 2026	13:08	Returned Oil	36	N/A	3294	2201	0.4	60.5
28 – Jan – 2026	13:12	Returned Oil	36	N/A	3345	2201	0.4	62.0
28 – Jan – 2026	13:16	Returned Oil	36	N/A	3404	2188	0.4	63.5
28 – Jan – 2026	13:20	Returned Oil	36	N/A	3466	2190	0.3	65.0
28 – Jan – 2026	13:25	Returned Oil	36	N/A	3503	2181	0.4	66.4
28 – Jan – 2026	13:29	Returned Oil	36	N/A	3534	2224	0.3	67.9
28 – Jan – 2026	13:33	Returned Oil	36	N/A	3597	2243	0.3	69.4
28 – Jan – 2026	13:37	Returned Oil	36	N/A	3659	2214	0.4	70.8

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	13:41	Returned Oil	36	N/A	3722	2227	0.4	72.3
28 – Jan – 2026	13:45	Returned Oil	36	N/A	3784	2216	0.4	73.7
28 – Jan – 2026	13:50	Returned Oil	36	N/A	3846	2238	0.4	75.2
28 – Jan – 2026	13:54	Returned Oil	36	N/A	3909	2217	0.4	76.7
28 – Jan – 2026	13:58	Returned Oil	36	N/A	3971	2215	0.4	78.1
28 – Jan – 2026	14:02	Returned Oil	36	N/A	4004	2216	0.4	79.6
28 – Jan – 2026	14:06	Returned Oil	36	N/A	4037	2219	0.3	81.1
28 – Jan – 2026	14:10	Returned Oil	36	N/A	4089	2229	0.4	82.5
28 – Jan – 2026	14:15	Returned Oil	36	N/A	4142	2210	0.4	84.0
28 – Jan – 2026	14:19	Returned Oil	36	N/A	4139	2238	0.3	85.5
28 – Jan – 2026	14:23	Returned Oil	36	N/A	4146	2224	0.3	86.9
28 – Jan – 2026	14:27	Returned Oil	36	N/A	4150	2241	0.3	88.3
28 – Jan – 2026	14:31	Returned Oil	36	N/A	4146	3694	0.7	90.0
28 – Jan – 2026	14:35	Returned Oil	36	N/A	4154	3311	0.6	92.4
28 – Jan – 2026	14:40	Returned Oil	36	N/A	4146	3493	0.6	95.0
28 – Jan – 2026	14:44	Returned Oil	36	N/A	4155	3490	0.6	97.4
28 – Jan – 2026	14:48	Returned Oil	36	N/A	4158	3001	0.5	99.7
28 – Jan – 2026	14:52	Returned Oil	36	N/A	4137	4163	0.7	102.2
28 – Jan – 2026	14:56	Returned Oil	36	N/A	4157	2999	0.5	104.6

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	15:00	Returned Oil	36	N/A	4158	3555	0.6	106.9
28 – Jan – 2026	15:05	Returned Oil	36	N/A	4158	2526	0.4	109.3
28 – Jan – 2026	15:09	Returned Oil	36	N/A	4158	2457	0.4	110.9
28 – Jan – 2026	15:13	Returned Oil	36	N/A	4159	2447	0.4	112.5
28 – Jan – 2026	15:17	Returned Oil	36	N/A	4159	3453	0.6	114.3
28 – Jan – 2026	15:21	Returned Oil	36	N/A	4159	3527	0.6	116.8
28 – Jan – 2026	15:25	Returned Oil	36	N/A	4159	3436	0.6	119.2
28 – Jan – 2026	15:30	Returned Oil	36	N/A	4160	2439	0.4	121.3
28 – Jan – 2026	15:34	Returned Oil	36	N/A	4160	3440	0.6	123.7
28 – Jan – 2026	15:38	Returned Oil	36	N/A	4161	3406	0.6	126.2
28 – Jan – 2026	15:42	Returned Oil	36	N/A	4161	3425	0.6	128.8
28 – Jan – 2026	15:46	Returned Oil	36	N/A	4162	3435	0.6	131.3
28 – Jan – 2026	15:50	Returned Oil	36	N/A	4162	3482	0.6	133.9
28 – Jan – 2026	15:55	Returned Oil	36	N/A	4158	3412	0.6	136.5
28 – Jan – 2026	15:59	Returned Oil	36	N/A	4160	3511	0.6	139.2
28 – Jan – 2026	16:03	Returned Oil	36	N/A	4160	3420	0.6	141.7
28 – Jan – 2026	16:07	Returned Oil	36	N/A	4146	3432	0.6	144.3
28 – Jan – 2026	16:11	Returned Oil	36	N/A	4146	3429	0.6	146.9
28 – Jan – 2026	16:15	Returned Oil	36	N/A	4146	3436	0.6	149.5

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	16:20	Returned Oil	36	N/A	4146	2789	0.4	152.1
28 – Jan – 2026	16:24	Returned Oil	36	N/A	4146	2711	0.4	153.8
28 – Jan – 2026	16:28	Returned Oil	36	N/A	4146	2467	0.0	154.4
28 – Jan – 2026	16:32	Returned Oil	36	N/A	4146	3142	0.0	155.1
28 – Jan – 2026	16:36	Returned Oil	36	N/A	4146	3072	0.0	155.1
28 – Jan – 2026	16:40	Returned Oil	36	N/A	4146	3069	0.0	155.1
28 – Jan – 2026	16:45	Returned Oil	36	N/A	4148	3066	0.0	155.1
28 – Jan – 2026	16:49	Returned Oil	36	N/A	4161	3060	0.0	155.1
28 – Jan – 2026	16:53	Returned Oil	36	N/A	4161	3055	0.0	155.1
28 – Jan – 2026	16:57	Returned Oil	36	N/A	4162	3048	0.0	155.1
28 – Jan – 2026	17:01	Returned Oil	36	N/A	4162	3033	0.0	155.1
28 – Jan – 2026	17:05	Returned Oil	36	N/A	4162	1150	0.0	155.1
28 – Jan – 2026	17:10	Returned Oil	36	N/A	4151	1046	0.0	155.1
28 – Jan – 2026	17:14	Returned Oil	36	N/A	4151	2041	0.4	155.5
28 – Jan – 2026	17:18	Returned Oil	36	N/A	4159	2025	0.4	156.9
28 – Jan – 2026	17:22	Returned Oil	36	N/A	4150	2092	0.4	158.4
28 – Jan – 2026	17:26	Returned Oil	36	N/A	4150	3717	0.7	160.5
28 – Jan – 2026	17:30	Returned Oil	36	N/A	4156	4580	0.8	163.9
28 – Jan – 2026	17:35	Returned Oil	36	N/A	4162	4679	0.9	167.5

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	17:39	Returned Oil	36	N/A	4163	4513	0.9	171.2
28 – Jan – 2026	17:43	Returned Oil	36	N/A	4163	746	0.0	174.4
28 – Jan – 2026	17:47	Returned Oil	36	N/A	4164	752	0.0	174.4
28 – Jan – 2026	17:51	Returned Oil	36	N/A	4164	2711	0.4	175.9
28 – Jan – 2026	17:55	Returned Oil	36	N/A	4165	2553	0.0	176.6
28 – Jan – 2026	18:00	Returned Oil	36	N/A	4165	1427	0.4	176.7
28 – Jan – 2026	18:04	Returned Oil	36	N/A	4166	1615	0.3	177.9
28 – Jan – 2026	18:08	Returned Oil	36	N/A	4166	1619	0.4	179.3
28 – Jan – 2026	18:12	Returned Oil	36	N/A	4169	2141	0.5	180.6
28 – Jan – 2026	18:16	Returned Oil	36	N/A	4194	4726	0.9	184.0
28 – Jan – 2026	18:20	Returned Oil	36	N/A	4196	4651	0.9	187.5
28 – Jan – 2026	18:25	Returned Oil	36	N/A	4168	4604	0.9	191.1
28 – Jan – 2026	18:29	Returned Oil	36	N/A	4185	4482	0.9	194.8
28 – Jan – 2026	18:33	Returned Oil	36	N/A	4206	4443	0.9	198.5
28 – Jan – 2026	18:37	Returned Oil	36	N/A	4198	4672	0.9	202.2
28 – Jan – 2026	18:41	Returned Oil	36	N/A	4204	4644	0.9	205.8
28 – Jan – 2026	18:45	Returned Oil	36	N/A	4205	4692	0.9	209.5
28 – Jan – 2026	18:50	Returned Oil	36	N/A	4206	4478	0.9	213.1
28 – Jan – 2026	18:54	Returned Oil	36	N/A	4202	4570	0.9	216.8

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	18:58	Returned Oil	36	N/A	4206	4539	0.9	220.4
28 – Jan – 2026	19:02	Returned Oil	36	N/A	4200	2482	0.6	223.7
28 – Jan – 2026	19:06	Returned Oil	36	N/A	4204	2466	0.6	226.2
28 – Jan – 2026	19:10	Returned Oil	36	N/A	4203	2840	0.7	228.7
28 – Jan – 2026	19:15	Returned Oil	36	N/A	4203	4424	0.8	232.1
28 – Jan – 2026	19:19	Returned Oil	36	N/A	4205	2486	0.6	235.4
28 – Jan – 2026	19:23	Returned Oil	36	N/A	4205	4065	0.9	238.3
28 – Jan – 2026	19:27	Returned Oil	36	N/A	4205	4146	0.9	241.9
28 – Jan – 2026	19:31	Returned Oil	36	N/A	4205	4133	0.9	245.4
28 – Jan – 2026	19:35	Returned Oil	36	N/A	4205	4125	0.9	248.9
28 – Jan – 2026	19:40	Returned Oil	36	N/A	4205	4142	0.8	252.5
28 – Jan – 2026	19:44	Returned Oil	36	N/A	4205	4207	0.8	256.0
28 – Jan – 2026	19:48	Returned Oil	36	N/A	4205	4176	0.9	259.5
28 – Jan – 2026	19:52	Returned Oil	36	N/A	4205	4212	0.8	263.0
28 – Jan – 2026	19:56	Returned Oil	36	N/A	4205	4231	0.9	266.5
28 – Jan – 2026	20:00	Returned Oil	36	N/A	4205	4243	0.9	270.0
28 – Jan – 2026	20:05	Returned Oil	36	N/A	4205	4082	0.9	273.5
28 – Jan – 2026	20:09	Returned Oil	36	N/A	4196	4155	0.8	277.1
28 – Jan – 2026	20:13	Returned Oil	36	N/A	4204	4205	0.8	280.5

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	20:17	Returned Oil	36	N/A	4205	3980	0.8	283.8
28 – Jan – 2026	20:21	Returned Oil	36	N/A	4205	4031	0.8	287.1
28 – Jan – 2026	20:25	Returned Oil	36	N/A	4205	3920	0.8	290.2
28 – Jan – 2026	20:30	Returned Oil	36	N/A	4205	3906	0.8	293.5
28 – Jan – 2026	20:34	Returned Oil	36	N/A	4205	3738	0.9	297.0
28 – Jan – 2026	20:38	Returned Oil	36	N/A	4205	3623	0.8	300.4
28 – Jan – 2026	20:42	Returned Oil	36	N/A	4205	3698	0.8	303.8
28 – Jan – 2026	20:46	Returned Oil	36	N/A	4205	3648	0.8	307.2
28 – Jan – 2026	20:50	Returned Oil	36	N/A	4205	3723	0.8	310.6
28 – Jan – 2026	20:55	Returned Oil	36	N/A	4205	3772	0.8	313.9
28 – Jan – 2026	20:59	Returned Oil	36	N/A	4205	3872	0.8	317.2
28 – Jan – 2026	21:03	Returned Oil	36	N/A	4205	3704	0.8	320.6
28 – Jan – 2026	21:07	Returned Oil	36	N/A	4205	3675	0.8	324.0
28 – Jan – 2026	21:11	Returned Oil	36	N/A	4205	3754	0.8	327.4
28 – Jan – 2026	21:15	Returned Oil	36	N/A	4205	3738	0.8	330.8
28 – Jan – 2026	21:20	Returned Oil	36	N/A	4205	3746	0.8	334.2
28 – Jan – 2026	21:24	Returned Oil	36	N/A	4205	3666	0.8	337.5
28 – Jan – 2026	21:28	Returned Oil	36	N/A	4205	3581	0.8	341.0
28 – Jan – 2026	21:32	Returned Oil	36	N/A	4205	3497	0.8	344.5

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	21:36	Returned Oil	36	N/A	4201	3538	0.9	348.0
28 – Jan – 2026	21:40	Returned Oil	36	N/A	4205	3588	0.8	351.5
28 – Jan – 2026	21:45	Returned Oil	36	N/A	4205	3568	0.9	354.9
28 – Jan – 2026	21:49	Returned Oil	36	N/A	4206	3746	0.8	358.4
28 – Jan – 2026	21:53	Returned Oil	36	N/A	4206	3820	0.8	361.7
28 – Jan – 2026	21:57	Returned Oil	36	N/A	4206	3696	0.8	365.0
28 – Jan – 2026	22:01	Returned Oil	36	N/A	4206	3644	0.8	368.5
28 – Jan – 2026	22:05	Returned Oil	36	N/A	4202	3618	0.8	371.9
28 – Jan – 2026	22:10	Returned Oil	36	N/A	4200	3616	0.8	375.4
28 – Jan – 2026	22:14	Returned Oil	36	N/A	4200	3641	0.8	378.8
28 – Jan – 2026	22:18	Returned Oil	36	N/A	4179	3515	0.9	382.2
28 – Jan – 2026	22:22	Returned Oil	36	N/A	4132	3561	0.9	385.7
28 – Jan – 2026	22:26	Returned Oil	36	N/A	4205	3603	0.8	389.2
28 – Jan – 2026	22:30	Returned Oil	36	N/A	4205	3638	0.8	392.6
28 – Jan – 2026	22:35	Returned Oil	36	N/A	4205	3527	0.9	396.1
28 – Jan – 2026	22:39	Returned Oil	36	N/A	4201	3533	0.9	399.6
28 – Jan – 2026	22:43	Returned Oil	36	N/A	4205	3290	0.9	403.2
28 – Jan – 2026	22:47	Returned Oil	36	N/A	4205	3249	0.9	406.9
28 – Jan – 2026	22:51	Returned Oil	36	N/A	4206	3553	0.8	410.4

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
28 – Jan – 2026	22:55	Returned Oil	36	N/A	4206	3563	0.8	413.9
28 – Jan – 2026	23:00	Returned Oil	36	N/A	4206	3447	0.9	417.3
28 – Jan – 2026	23:04	Returned Oil	36	N/A	4206	3511	0.9	420.9
28 – Jan – 2026	23:08	Returned Oil	36	N/A	4202	3732	0.8	424.3
28 – Jan – 2026	23:12	Returned Oil	36	N/A	4200	3803	0.8	427.7
28 – Jan – 2026	23:16	Returned Oil	36	N/A	4200	3793	0.8	431.0
28 – Jan – 2026	23:20	Returned Oil	36	N/A	4179	3797	0.8	434.3
28 – Jan – 2026	23:25	Returned Oil	36	N/A	4132	322	0.0	437.1
28 – Jan – 2026	23:29	Returned Oil	36	N/A	4083	295	0.0	437.1
28 – Jan – 2026	23:33	Returned Oil	36	N/A	4032	290	0.0	437.1
28 – Jan – 2026	23:37	Returned Oil	36	N/A	3981	285	0.0	437.1
28 – Jan – 2026	23:41	Returned Oil	36	N/A	3925	285	0.0	437.1
28 – Jan – 2026	23:45	Returned Oil	36	N/A	3868	252	0.0	437.1
28 – Jan – 2026	23:50	Returned Oil	36	N/A	3809	209	0.0	437.1
28 – Jan – 2026	23:54	Returned Oil	36	N/A	3747	152	0.0	437.1
28 – Jan – 2026	23:58	Returned Oil	36	N/A	3716	91	0.0	437.1
29 – Jan – 2026	0:02	Returned Oil	36	N/A	3680	36	0.0	437.1
29 – Jan – 2026	0:06	Returned Oil	36	N/A	3663	7	0.0	437.1
29 – Jan – 2026	0:10	Returned Oil	36	N/A	3599	7	0.0	437.1

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
29 – Jan – 2026	0:15	Returned Oil	36	N/A	3530	7	0.0	437.1
29 – Jan – 2026	0:19	Returned Oil	36	N/A	3458	7	0.0	437.1
29 – Jan – 2026	0:23	Returned Oil	36	N/A	3385	1074	0.4	437.7
29 – Jan – 2026	0:27	Returned Oil	36	N/A	3319	171	0.0	439.1
29 – Jan – 2026	0:31	Returned Oil	36	N/A	3262	140	0.0	439.1
29 – Jan – 2026	0:35	Returned Oil	36	N/A	3195	106	0.0	439.1
29 – Jan – 2026	0:40	Returned Oil	36	N/A	3136	74	0.0	439.1
29 – Jan – 2026	0:44	Returned Oil	36	N/A	3078	53	0.0	439.1
29 – Jan – 2026	0:48	Returned Oil	36	N/A	3020	40	0.0	439.1
29 – Jan – 2026	0:52	Returned Oil	36	N/A	2962	1003	0.4	439.2
29 – Jan – 2026	0:56	Returned Oil	36	N/A	2898	1580	0.4	440.9
29 – Jan – 2026	1:00	Returned Oil	36	N/A	2833	63	0.0	441.0
29 – Jan – 2026	1:05	Returned Oil	36	N/A	2773	52	0.0	441.0
29 – Jan – 2026	1:09	Returned Oil	36	N/A	2719	42	0.0	441.0
29 – Jan – 2026	1:13	Returned Oil	36	N/A	2666	27	0.0	441.0
29 – Jan – 2026	1:17	Returned Oil	36	N/A	2596	14	0.0	441.0
29 – Jan – 2026	1:21	Returned Oil	36	N/A	2521	7	0.0	441.0
29 – Jan – 2026	1:25	Returned Oil	36	N/A	2449	3	0.0	441.0
29 – Jan – 2026	1:30	Returned Oil	36	N/A	2381	1798	0.5	442.6

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
29 – Jan – 2026	1:34	Returned Oil	36	N/A	2324	30	0.0	443.0
29 – Jan – 2026	1:38	Returned Oil	36	N/A	2279	14	0.0	443.0
29 – Jan – 2026	1:42	Returned Oil	36	N/A	2230	1544	0.4	443.7
29 – Jan – 2026	1:46	Returned Oil	36	N/A	2181	2370	0.5	445.7
29 – Jan – 2026	1:50	Returned Oil	36	N/A	2210	2644	0.5	447.8
29 – Jan – 2026	1:55	Returned Oil	36	N/A	2254	2775	0.6	450.0
29 – Jan – 2026	1:59	Returned Oil	36	N/A	2268	2934	0.6	452.3
29 – Jan – 2026	2:03	Returned Oil	36	N/A	2310	2952	0.6	454.6
29 – Jan – 2026	2:07	Returned Oil	36	N/A	2356	2894	0.6	457.0
29 – Jan – 2026	2:11	Returned Oil	36	N/A	2385	2954	0.6	459.4
29 – Jan – 2026	2:15	Returned Oil	36	N/A	2410	2866	0.6	461.7
29 – Jan – 2026	2:20	Returned Oil	36	N/A	2424	2848	0.6	464.1
29 – Jan – 2026	2:24	Returned Oil	36	N/A	2402	2901	0.6	466.6
29 – Jan – 2026	2:28	Returned Oil	36	N/A	2386	955	0.3	467.1
29 – Jan – 2026	2:32	Returned Oil	36	N/A	2258	445	0.0	468.7
29 – Jan – 2026	2:36	Returned Oil	36	N/A	2118	2699	0.6	471.1
29 – Jan – 2026	2:40	Returned Oil	36	N/A	2076	2831	0.6	473.5
29 – Jan – 2026	2:45	Returned Oil	36	N/A	1949	11	0.0	475.0
29 – Jan – 2026	2:49	Returned Oil	36	N/A	1838	10	0.0	477.6

Returned Oil Operation Report								
Date (DD-MM-YYYY)	Time (HH:MM)	P. fluid Type	CS (1/64 in)	WHP (PSI)	CT Depth (m)	Pumping pressure (PSI)	Pump Rate (BPM)	Volume total (BBL)
29 – Jan – 2026	2:53	Returned Oil	36	N/A	1734	1306	0.4	478.1
29 – Jan – 2026	2:57	Returned Oil	36	N/A	1620	1984	0.5	480.1
29 – Jan – 2026	3:01	Returned Oil	36	N/A	1568	113	0.0	481.9
29 – Jan – 2026	3:05	Returned Oil	36	N/A	1498	440	0.5	482.0
29 – Jan – 2026	3:10	Returned Oil	36	N/A	1412	1879	1.0	484.7

Table 11-5: AZNS-166 Pumping Returned Oil Operation Report

Coiled Tubing BHA Diagram

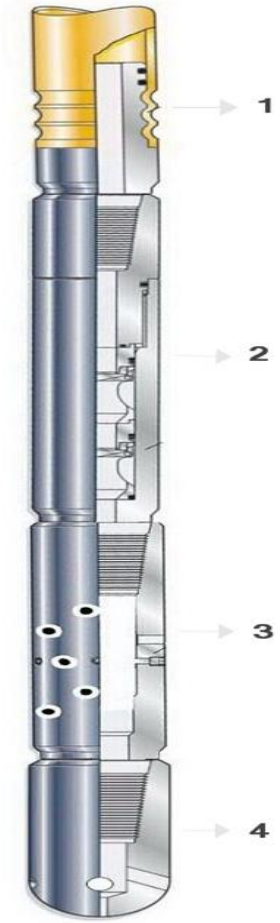
Row	BHA	Length (in)	OD size (in)	Schematic
1	Roll On Connector	3.3	1 3/4	
2	Two Check valves (Flapper Type)	8.3		
3	Perforation Sub (75 mm holes)	6.3		
4	Wash Nozzle (8 mm holes)	5		

Table 11-6: AZNS-166 C.T BHA Design

Slick Line BHA Diagram


OD size (in)	Tools	Length (ft)	schematic
1 7/8	Rope socket	0.5	
1 7/8	Stem	75	
1 7/8	Mechanical Jar	4 (closed) & 6 (fully open)	
1 7/8	Hydraulic Jar	2	
3.49	Gauge Cutter or GS Pulling or Memory Gauge	1	 

Table 11-7: AZNS-166 S.L BHA Design

12. List of Contractors

Item	Service Item	Contractor
1	Drilling Rig, Mobilization and Demobilization the Rig, Rig Move Between Well Pads	OEOC
2	Drilling Fluids and Completion Fluids	VIRA
3	Waste Management	Behsan
4	Mud Logging	Pars Geo Data
5	H2S Monitoring and Control	PSAJ
6	Casing and Tubing Running	OEOC
7	Cementing	Spud Energy
8	Slick Line	OEOC
9	Stimulation (Coiled Tubing and Acidizing and Nitrogen Lifting)	OEOC
10	Surface Well Testing	OEOC
11	Well Head	OEOC

Table 12-1: AZNS-166 Contractors Involved

13. Appendix

13.1 DDR Summary

Item	Date	Remark
1	27 – Oct – 25	Cont. R/U; Spud Rig 201; L/U 4" 10k psi Co-Flex Hose F/ Choke Manifold outlet To X-Mas Tree Productio Valve; L/U 2" Chicksan Flowline F/ Pump Unit discharge To T.H.S side outlet; Set Storgae Tank & Conn. To Burning Line; Check & Record Annulus pressures of all Wellhead sections; Press. Test P-Seal Test of B & C Section; Press. Test Chiksan Pipes W/ 3000psi / 15 min, Ok; P/U & M/U Wellhead Lubricator on X-Mas Tree, Press. Test the same W/ 4000psi / 15min, Ok.
2	28 – Oct – 25	Ret. TWCV W/ Wellhead Lubricator, Record 800psi Press. on Lubricator Press. Gauge, L/D Wellhead Lubricator; Assemble 2.75" Ring Gauge Tool Strg, RIH W/ 2.75" Ring Gauge Tool Strg To 107m, Attempt To pass this point, No Success due to the Min ID of Protection Sleeve being 2.7", POOH Slick Line Tool Strg To Surface; P/U & Assemble 2.2" Ring Gauge Tool Strg and RIH To 3056m, POOH Slick line Tool Strg To surf. ; R/U Coiled TBG Facilities; Cont. RIH W/ 1-3/4" C.T BHA, While Circ. Thru. Choke Manifold @ 0.2BPH F.R & 1100psi Back Pressure; Start Kill The Well.
3	29 – Oct – 25	Cont. Kill The Well using W&W Method, Confirm Uniform 83 pcf In / Out MW; Obs. Well for 1Hr. , Well Static; POOH 1-3/4" C.T BHA To Surface, While Circ. Thru. C.T BHA, NL-NG; Flush C.T; Static Flow Check & Obs. The Well for 1 Hr. , Well Static; L/D C.T Eqp. ; Obs. The Well For 0.5hr Thru. Choke Manifold, Well Static; Install TWCV in TBG HGR, Perss. Test @ 4500psi, Ok; N/D X-Mas Tree; N/U BOP
4	30 – Oct – 25	Cont. N/U 13-5/8" 10k BOP Stack. Perform BOP Test as NIOC Policy
5	31 – Oct – 25	Cont. N/U 13-5/8" 10k BOP Stack. Perform BOP Test as NIOC Policy

6	01 – Nov – 25	Remove TWCV, Unset PKR, try to establish the Mud circulation Thru Strg. & ann. Several times, No Succ. Pull out Completion string By request of Client (P.P.L).
7	02 – Nov – 25	Cont. POOH while L/D Completion String .
8	03 – Nov – 25	Cont. POOH while L/D Completion String .
9	04 – Nov – 25	Cont POOH to surf and L/D Completion String. Run in hole with 8-3/8" M.M.J.Mill + 9-5/8" Scraper to 1360m
10	05 – Nov – 25	Cont RIH to 1609.60m While F/U String every 20 Jts , Tag 7" L.Lap @ this depth. POOH to Surf. M/U & Run in hole with 6" Junk Mill + BHA to 540m
11	06 – Nov – 25	Cont RIH with 6" Junk Mill (T.S.E.KH) + 27 jts 3-1/2" HWDP (Jt by Jt) & Follow by 3-1/2" D.Pipe (Jt by Jt) to 2540m for Cleaning Inside 7" liner W/ F/U String, NL-NG.
12	07 – Nov – 25	Cont RIH with 6" Junk Mill to 4133m (4-1/2" L.Lap) Circ BTm Up, POOH from 4133 to 2820m
13	08 – Nov – 25	POOH to Surface & L/D 6" J. Mill (T.S.E.KH, 5% Used). P/U & Run in hole W/ NEW 3-1/2" M.M.J.Mill (T.S.E.KH, SN : 084) + 15 Jts 3-1/8" D.C (Jt by Jt) + 6 Jts 2-7/8" (Jt by Jt) & follow by 3-1/2" D.Pipe from 190m to 2800m while break Circulate each 15 STD, NL.NG.
14	09 – Nov – 25	Cint RIH to 4275.5m, Over Circ. Mud to uniform MW in/out to 83 pcf. Pump 20 bbl 83 pcf CaCl2 as Non-Solid Completion Fluid & Displace to spot, OK. Start POOH From 4275.5m to 2800m W/ Circ Mud Cross Well Head, NL.NG
15	10 – Nov – 25	POOH To 1237m. Slip & Cut Drlg Line. Cont POOH to Surface. M/U & RIH with 6" M.M.J.mill (5% Used / T.S.E.KH) + 4 3/4" Bit Sub (F. In) + HWDP 3 1/2" & Follow by 3 1/2 DP "G" to 1350m
16	11 – Nov – 25	Cont RIH to 4132m while Scrap 7" PKR Depth, Several Time. Circ Btm Up. Displace mud In well with CaCl2 Completion Fluid Non.Solid : Pump 50BBl Hi.vis Pill, Pump & Displace the well

		with 680BBl CaCl2 Brine as Completion fluid (Dump 40 BBl Contaminated with mud).
17	12 – Nov – 25	Start POOH from 4132m to 1376m while L/D 5" D.Pipe (Jt by Jt) & 3-1/2" D.Pipe (Jt by Jt) & F/U the well with CaCl2 Completion Fluid Non-Solid
18	13 – Nov – 25	Cont. POOH 6" Clean out BHA F/ 1376m To Surface On Elevator, While L/D All Tubular (Jt by Jt) & 6" Mill and F/U Well w/ CaCl2 Completion Fluid Non-Solid, NL-NG; BOP Test; Prepare Rig & R/U CSG Running Eqp. To Run 7.5K 3-1/2" * 4-1/2" Comp. Strg
19	14 – Nov – 25	RIH 7.5K 3-1/2" * 4-1/2" Comp. Strg as per tally To 676m; R/U S/L Tools, P/U & Assemble 2.8" Gauge Ring and Attempt To RIH To Top of SSD, Obs. S/L Tension Drop @ 335m, Try To pass same depth Sev. Times, No Success; POOH S/L Tool String To Surface; L/D Slickline Tools; Decide To POOH Comp. Strg; POOH 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 676 To 327m; Obs. 2 Jts of 3-1/2" TBG is damaged; P/U & Assemble 2.8" Gauge Ring and RIH To Top of SSD Normally; POOH S/L Tool Strg To Surface; L/D Surface Slickline Eqps. ; Prepare To RIH Comp. Strg
20	15 – Nov – 25	Cont. RIH 7.5K 3-1/2" * 4-1/2" Comp. Strg as per tally F/ 327 To 676m; Press. Test Comp. Strg @ 676m W/ 6000 Psi / 15min, Ok; Cont. RIH 7.5K 3-1/2" * 4-1/2" Comp. Strg as per tally F/ 676 To 1223m; Press. Test Comp. Strg @ 1223m W/ 6000 Psi / 15min, Ok; P/U & Assemble 2.8" Gauge Ring and RIH To Top of SSD Normally; L/D S/L Surface Eqp. ; Cont. RIH 7.5K 3-1/2" * 4-1/2" Comp. Strg as per tally F/ 1223 To 1671m; Stop Op. due to bad weather, NL-NG.
21	16 – Nov – 25	Cont. Stop Op. due to bad weather, @ 1671m, while Circ. C.W.H by Trip Tank; Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 1671 To 2640m; Press. Test Comp. Strg against SSD Check Valve @ 2640m W/ 6000 Psi / 15min, Ok; Cont. RIH W/ 3-1/2" * 4-1/2" 7.5k Comp. Strg F/ 2640 To 2658m as follows: 4-1/2" Pup Jt + 4-1/2" Short Flow Coupling + 4-1/2" TRSSV Tubing Retrievable Safety Valve + 4-1/2" Long Flow Coupling + 4-1/2" Pup Jt, NL-NG.

22	17 – Nov – 25	Flush & Conn. 1/4" CL To TRSSV CL Port, Press. Test Conn. @ 6000psi / 15min, Ok; B/O All Pup Jts of Comp. Strg Facilities Ret. F/ Well AZNS#116; Press. Test Comp. Strg against SSD Check Valve @ 2658m W/ 6000 Psi / 15min, Ok; Inflow Test, Pressure stabilized @ 1000 psi / 15 min, Ok; M/U Fluted Swage + TBG HGR + Running Tool + L.J; Space out to 2706m (1.5m above THS); Press. Test Comp. Strg against SSD Check Valve @ 2706m W/ 6000 Psi / 15min, Ok; P/U & M/U G.FLG + 4-1/16" 10K Gate Valve + Slickline BOP + Lubricator & BOP Panel; S/L Op. is in progress, NL-NG.
23	18 – Nov – 25	RIH W/ 2.750" Xn Blanking Plug & Set Plug in No-Go; RIH W/ Equalizing Prong & Set in Position; RIH W/ 2.75" Shifting Tool To SSD Depth, Confirm SSD closed; Set PKR; PKR Pull Test Ok; Shear Expansion Joint Ok; Land TBG HGR In THS; Pressure Test TBG HGR and All Tie-Down Screws, Ok; Final Press. Test: Press. Test Comp. Strg @ 6,000 Psi / 15 Min – Ok; RIH W/ SB Pulling & Ret. Prong; Retrieve 2.750" Blanking Plug; Press. Test PKR & HGR Seal; Ret. TRSSV Protection Sleeve; Press. Test TWCV, Ok; N/D BOP
24	1 9 – Nov – 25	Cont. N/D BOP; Install TBG HGR M.M.Seal, N/U TBG Head Adaptor; Pass 1/4" CL Thru. CL; Install 4-1/16" 10k Companion FLG On Tubing Head Adaptor; Press. Test M.M.Seal @ 6,000 Psi / 15 Min – Ok; Cavity Press. Test Between S – Seal, T.H.S & T.B.G Adaptor Ring Gasket, 2nd TBG O-Ring, Tie-downs Screws, and Exit Port Thru. Test port @ 6,000 Psi / 15 Min – Ok; N/U Solid Block and Tree Cap; Open All XMT Valves, Conn. 4-1/16" Companion FLG to Kill Valve, Press. Test X-Mas Tree body @ 8,000 Psi / 15 Min – Ok; Release Rig 201 @ 1404.08.28 - 23:59 p.m.

Table 13-1: AZNS-166 Daily Drilling Report Summar
