END OF WELL REPORT

AZADEGAN OIL FIELD

END OF WELL REPORT

AZNS – 075 – ST1 (PAD #80)

GADVAN WELL

Drilling Department

MAY 2026

MSA/OEOC			
	Position	**Name**	**Date & Signature**
Prepared by	Drilling Engineering Department	M.H.Haji Taleb Asgar Eyvazi	
Approved by	Project Head of Drilling Engineering	Behnam Parvaresh	
	Project Head of Drilling Operation	Piran Farzaneh	
	Project Manager	Rashid Ansari	
PPL			
	Position	**Name**	**Date & Signature**
Check & Approved by	Drilling Operation Manager	Majid Nariman	
	Subsurface Engineering Manager	Mehdi Salim Mehr	
	Project Manager	Soheil Shadizadeh	
	Subsurface Project Manager	Keivan Davoodi Nejad	

TABLE OF CONTENTS

1. General Information 10
1.1 Field Introduction 10
1.2 AZNS – 075 Well Location Map 11
2. Well History 12
2.1 Well Informaion 12
2.2 AZNS – 075 Well History 14
2.3 AZNS – 075 – ST1 Well Sketch 65
2.4 AZNS – 075 – ST1 Bit Data Chart 66
2.5 Bit Record Table 67
3. Time Analysis Report 68
3.1 Time vs. Depth Chart 68
3.2 Total Time Break-Down of Operation 69
3.3 NPT Break-Down 75
4. Dry Test Report 79
4.1 7” L.Lap dry test 79
4.2 5” L.Lap Dry test 81
5. Geological & Logging Reports 85
5.1 Stratigraphy 85
5.2 Logging and Testing Reports 92
5.3 Perforation Reports 92
5.4 Directional Drilling Report 93
6. Bottom Hole Assembly Record 109
7. Casing Information 132
8. Cement Job Report 133
8.1 7” Liner Cementing Operation Information 133
8.2 Engineering Data 133
8.3 Operation Sequence 134
8.4 Mixing Sequence 135
8.5 Job Graph 136
8.6 Timing Schedule 137
8.7 Amount of Material & Used in Operation 138
8.8 7” Liner Tie-Back Cementing Operation Information 139
8.9 Engineering Data 139
8.10 Operation Sequence 140
8.11 Pumping Schedule 141
8.12 Amount of Material & Used in Operation 141
8.13 5” Liner Cementing Operation Information 141
8.14 Engineering Data 142
8.15 Operation Sequence 143

8.16 Pumping Schedule 144
8.17 Amount of Material & Used in Operation 144
9. Completion Report 145
9.1 Completion Tubing Information 145
9.2 Completion Tools Specification Checklist 145
9.3 Assembling Test Report 149
9.4 Completion Operation Checklist 155
9.5 Completion Sketch & Tally 159
9.6 Completion String Pressure Test 166
10. Wellhead Report 170
10.1 Final Well Status 170
10.2 Wellhead & X-mass tree Specification 171
10.3 Wellhead Schematic 173
10.4 X-mass Tree Specification (Section D) 174
10.5 X-mass Tree Pressure Test Report (Section D – befor install) 175
10.6 X-mass Tree Pressure Test Report (Section D – after install) 176
10.7 Wellhead Related Test Reports 177
11. Drilling Fluid Information 181
11.1 Summary 181
11.2 Interval Remark 182
11.2.1 WorkOver & 8 3/8" Hole Section 182
11.2.2 6 – 1/8" Hole Section Drilling Fluid Types 200
11.2.3 Interval Completion Section 218
12. Waste Management Report 220
12.1 De – Completion Section 220
12.1.1 Operation's Recap 220
12.1.2 Dewatering's Recap 225
12.1.3 Chemical 230
12.2 8 – 3/8" Hole Section 232
12.2.1 Operation's Recap 232
12.2.2 Dewatering's Recap 238
12.2.3 Chemical 244
12.3 6 – 1/8" Hole Section 247
12.3.1 Operation's Recap 247
12.3.2 Dewatering's Recap 251
12.3.1 Chemical 255
12.4 Completion Section 257
12.4.1 Operation's Recap 257
12.4.2 Dewatering's Recap 265
12.4.1 Chemical 278

13. List of Contractors 286
14. Appendix 287
14.1 DDR Summary 287

LIST OF TABLES

TABLE 2-1: AZNS-075-ST1 WORKOVER WELL INFORMATION 13
TABLE 2-2: AZNS-075-ST1 BIT RECORD TABLE 67
TABLE 3-1: AZNS-075-ST1 WORKOVER TIME BREAKDOWN 74
TABLE 3-2: AZNS-075-ST.1 NPT TIME BREAKDOWN (BASED ON CLIENT'S ORDER & INFORMATION) 78
TABLE 4-1: AZNS-75 7" LINER INFORMATION 79
TABLE 4-2: AZNS-075-ST1 DRY TEST INFORMATION 79
TABLE 4-3: AZNS-075-ST1 DOWNHOLE TEST RESULT DATA 81
TABLE 4-4: AZNS-075-ST1 5" LINER INFORMATION 82
TABLE 4-5: AZNS-075-ST1 5" DRY TEST INFORMATION 82
TABLE 5-1: AZNS-075-ST1 FORMATION & RESERVOIR SUB LAYERS TOP 88
TABLE 5-2: AZNS-075-ST1 WELL DATA SUMMARY 89
TABLE 5-3: AZNS-075-ST1 MUD LOSS & GAIN 90
TABLE 5-4: AZNS-075-ST1 HYDROCARBON SHOWS 91
TABLE 5-5: AZNS-075-ST1 LOGGING INFORMATION 92
TABLE 5-6: AZNS-075-ST1 PERFORATION DATA 92
TABLE 5-7: AZNS-075-ST1 DIRECTIONAL DRILLING SURVEY 97
TABLE 5-8: AZNS-075-ST1 SAMPLE INTERVAL & QUALITY (CUTTING COLLECTION) 106
TABLE 7-1: AZNS-075-ST1 FINAL CASING DATA 132
TABLE 8-1: AZNS-075-ST1 ENGINEERING DATA 133
TABLE 8-2: AZNS-075-ST1 TIMING SCHEDULE 137
TABLE 8-3: AZNS-075-ST1 MATERIAL USED TABLE 138
TABLE 8-4: AZNS-075-ST1 ENGINEERING DATA 139
TABLE 8-5: AZNS-075-ST1 PUMPING SCHEDULE 141
TABLE 8-6: AZNS-075-ST1 MATERIAL USED TABLE 141
TABLE 8-7: AZNS-075-ST1 ENGINEERING DATA 142
TABLE 8-8: AZNS-075-ST1 PUMPING SCHEDULE 144
TABLE 8-9: AZNS-075-ST1 MATERIAL USED TABLE 144
TABLE 9-1: AZNS-075-ST1 TUBING DATA 145
TABLE 9-2: AZNS-075-ST1 COMPLETION EQUIPMENT CHECKLIST 148
TABLE 9-3: AZNS-075-ST1 OPERATION CHECKLIST 158
TABLE 9-4: AZNS-075-ST1 COMPLETION TALLY 165
TABLE 10-1: AZNS-075-ST1 FINAL WELL STATUS 170
TABLE 10-2: AZNS-075-ST1 WELLHEAD EQUIPMENT SPECIFICATION 172
TABLE 10-3: AZNS-075-ST1 SECTION "D" SPECIFICATION 174
TABLE 10-4: AZNS-075-ST1 SECTION "D" TEST REPORT BEFOR INSTALLATION 175
TABLE 10-5: AZNS-075-ST1 SECTION "D" TEST REPORT AFTER INSTALLATION 176
TABLE 11-1: AZNS-075-ST1 SUMMARY OF FLUID 181
TABLE 11-2: AZNS-075-ST1 FLUID PROPERTIES RECAP TABLE 184
TABLE 11-3: AZNS-075-ST1 MATERIAL CONSUMPTION ANALYSIS TABLE 185
TABLE 11-4: AZNS-075-ST1 VOLUME ANALYSIS TABLE 187
TABLE 11-5: AZNS-075-ST1 DAILY VOLUME BREAK DOWN TABLE 189
TABLE 11-6: AZNS-075-ST1 LOSS DISTRIBUTION 192
TABLE 11-7: AZNS-075-ST1 FLUID PROPERTIES RECAP 195
TABLE 11-8: AZNS-075-ST1 8-1/2" SOLID CONTROL DESSCUSION 199
TABLE 11-9: AZNS-075-ST1 6-1/8" FLUID PROPERTIES RECAP TABLE 200
TABLE 11-10: AZNS-075-ST1 6-1/8" INTERVAL MATERIAL CONSUMPTION ANALYSIS 200
TABLE 11-11: AZNS-075-ST1 6-1/8" INTERVAL VOLUME ANALYSIS 202
TABLE 11-12: AZNS-075-ST1 6-1/8" INTERVAL DAILY VOLUME BREAKDOWN 204
TABLE 11-13: AZNS-075-ST1 6-1/8" INTERVAL LOSS DISTRIBUTION 208
TABLE 11-14: AZNS-075-ST1 6-1/8" INTERVAL FLUID PROPERTIES 211
TABLE 11-15: AZNS-075-ST1 6-1/8" SOLID CONTROL DESSCUSION 217

TABLE 11-16: AZNS-075-ST1 COMPLETION MATERIAL CONCENTRATION 218
TABLE 12-1: AZNS-075-ST1 DE-COMPLETION SECTION SOLID HANDLING SYSTEM 222
TABLE 12-2: AZNS-075-ST1 DE-COMPLETION SECTION FIXATION ANALYSIS TABLE 224
TABLE 12-3: AZNS-075-ST1 DE-COMPLETION SECTION DEWATERING DATA TABLE 227
TABLE 12-4: AZNS-075-ST1 DE-COMPLETION SECTION DEWATERING ANALYSIS TABLE 229
TABLE 12-5: AZNS-075-ST1 8-3/8" SECTION SOLID HANDLING SYSTEM 234
TABLE 12-6: AZNS-075-ST1 8-3/8" SECTION FIXATION ANALYSIS TABLE 237
TABLE 12-7: AZNS-075-ST1 8-3/8" SECTION DEWATERING DATA TABLE 240
TABLE 12-8: AZNS-075-ST1 8-3/8" SECTION DEWATERING ANALYSIS TABLE 243
TABLE 12-9: AZNS-075-ST1 6-1/8" SECTION SOLID HANDLING SYSTEM 248
TABLE 12-10: AZNS-075-ST1 6-1/8" SECTION FIXATION ANALYSIS TABLE 250
TABLE 12-11: AZNS-075-ST1 6-1/8" SECTION DEWATERING DATA TABLE 252
TABLE 12-12: AZNS-075-ST1 6-1/8" SECTION DEWATERING ANALYSIS TABLE 254
TABLE 12-13: AZNS-075-ST1 COMPLETION SECTION SOLID HANDLING SYSTEM 260
TABLE 12-14: AZNS-075-ST1 COMPLETION SECTION FIXATION ANALYSIS TABLE 264
TABLE 12-15: AZNS-075-ST1 COMPLETION SECTION DEWATERING DATA TABLE 273
TABLE 12-16: AZNS-075-ST1 COMPLETION SECTION DEWATERING ANALYSIS TABLE 277
TABLE 13-1: AZNS-075-ST1 CONTRACTORS INVOLVED 286
TABLE 14-1: AZNS-075-ST1 DAILY DRILLING REPORT SUMMARY 304

LIST OF FIGURES

FIGURE 1-1: AZNS OILFIELD LOCATION MAP 10
FIGURE 1-2: AZNS-075 WELL LOCATION MAP 11
FIGURE 2-1: AZNS-075-ST1 WELL SKETCH 65
FIGURE 2-2: AZNS-075-ST1 BIT DATA CHART 66
FIGURE 3-1: AZNS-075-ST1 WORKOVER WELL TIME VS. DEPTH AFTER SIDE TRACK 68
FIGURE 4-1: AZNS-075-ST1 DRY TEST EVENT 80
FIGURE 4-2: AZNS-075-ST1 7" L.LAP DRY TEST RESULT – MIDDLE BT 81
FIGURE 4-3: AZNS-075-ST1 5" L.LAP DRY TEST RESULT – MIDDLE BT 84
FIGURE 5-1: AZNS-075-ST1 CROSS SECTION 107
FIGURE 5-2: AZNS-075-ST1 PLAN VIEW 108
FIGURE 8-1: AZNS-075-ST1 7" LINER JOB GRAPH 137
FIGURE 9-1: AZNS-075-ST1 RETRIEVABLE PACKER CONNECTION 149
FIGURE 9-2: AZNS-075-ST1 SSD CONNECTIONS 150
FIGURE 9-3: AZNS-075-ST1 EX JT CONNECTIONS 151
FIGURE 9-4: AZNS-075-ST1 LANDING NIPPLE CONNECTIONS 152
FIGURE 9-5: AZNS-075-ST1 FIRST CIM CONNECTIONS 153
FIGURE 9-6: AZNS-075-ST1 SECOND CIM CONNECTIONS 154
FIGURE 9-7: AZNS-075-ST1 COMPLETION SKETCH 159
FIGURE 9-8: AZNS-075-ST1 ANNULUS PRESSURE TEST, STRING PRESSURE TEST AFTER PACKER SETTING GRAPH 166
FIGURE 9-9: AZNS-075-ST1 PACKER SETTING, TRSSSV INFLOW TEST & STRING PRESSURE TEST AFTER M/H TBG HGR GRAPH 167
FIGURE 9-10: AZNS-075-ST1 COMPLETION STRING PRESSURE TEST 168
FIGURE 9-11: AZNS-075-ST1 COMPLETION TRSSSV PRESSURE TEST 169
FIGURE 10-1: AZNS-075-ST1 WELLHEAD SKETCH 173
FIGURE 10-2: AZNS-075-ST1 X-MASS TREE BODY PRESSURE TEST GRAPH BEFORE INSTALLATION 177
FIGURE 10-3: AZNS-075-ST1 X-MASS TREE BODY PRESSURE TEST GRAPH AFTER INSTALLATION 178
FIGURE 10-4: AZNS-075-ST1 WELLHEAD MOM BEFOR INSTALLATION 179
FIGURE 10-5: AZNS-075-ST1 WELLHEAD MOM AFTER INSTALLATION 180
FIGURE 11-1: AZNS-075-ST1 MUD CHEMICAL USAGE 186
FIGURE 11-2: AZNS-075-ST1 EFFECTIVE CONCENTRATION 186
FIGURE 11-3: AZNS-075-ST1 VOLUME ANALYSIS CHART 187
FIGURE 11-4: AZNS-075-ST1 DAILY VOLUME BREAK DOWN CHART 190
FIGURE 11-5: AZNS-075-ST1 LOSS ANALYSIS 193
FIGURE 11-6: AZNS-075-ST1 8-1/2" DENSITY GRAPH 196
FIGURE 11-7: AZNS-075-ST1 8-1/2" VISCOSITY GRAPH 196
FIGURE 11-8: AZNS-075-ST1 8-1/2" PV & YP GRAPH 196
FIGURE 11-9: AZNS-075-ST1 8-1/2" PH GRAPH 197
FIGURE 11-10: AZNS-075-ST1 8-1/2" CALCIUM GRAPH 197
FIGURE 11-11: AZNS-075-ST1 8-1/2" TOTAL HARDNESS GRAPH 197
FIGURE 11-12: AZNS-075-ST1 8-1/2" SOLID% GRAPH 198
FIGURE 11-13: AZNS-075-ST1 8-1/2" CHLORIDE GRAPH 198
FIGURE 11-14: AZNS-075-ST1 8-1/2" WATER LOSS GRAPH 198
FIGURE 11-15: AZNS-075-ST1 8-1/2" KCL % WT GRAPH 199
FIGURE 11-16: AZNS-075-ST1 6-1/8" EFFECTIVE CONCENTRATION 201
FIGURE 11-17: AZNS-075-ST1 6-1/8" MUD CHEMICAL USAGE 201
FIGURE 11-18: AZNS-075-ST1 6-1/8" INTERVAL VOLUME ANALYSIS 202
FIGURE 11-19: AZNS-075-ST1 6-1/8" INTERVAL DAILY VOLUME BREAKDOWN 205
FIGURE 11-20: AZNS-075-ST1 6-1/8" LOSSES ANALYSIS 206
FIGURE 11-21: AZNS-075-ST1 6-1/8" LOSSES ANALYSIS 209
FIGURE 11-22: AZNS-075-ST1 6-1/8" DENSITY GRAPH 212
FIGURE 11-23: AZNS-075-ST1 6-1/8" VISCOSITY GRAPH 212
FIGURE 11-24: AZNS-075-ST1 6-1/8" PV & YP GRAPH 213
FIGURE 11-25: AZNS-075-ST1 6-1/8" PH GRAPH 213
FIGURE 11-26: AZNS-075-ST1 6-1/8" CALCIUM GRAPH 214
FIGURE 11-27: AZNS-075-ST1 6-1/8" TOTAL HARDNESS GRAPH 214

FIGURE 11-28: AZNS-075-ST1 6-1/8" SOLID% GRAPH 215
FIGURE 11-29: AZNS-075-ST1 6-1/8" WATER LOSS% GRAPH 215
FIGURE 11-30: AZNS-075-ST1 6-1/8" CHLORIDE GRAPH 216
FIGURE 11-31: AZNS-075-ST1 6-1/8" KCL % WT GRAPH 216
FIGURE 11-32: AZNS-075-ST1 COMPLETION SECTION MUD CHEMICAL USAGE 219
FIGURE 11-33: AZNS-075-ST1 COMPLETION SECTION EFFECTIVE CONCENTRATION 219

1. General Information

1.1 Field Introduction

Azadegan South Oil Field is situated in West Karoun, Khuzestan province on a large long – axis anticline with N – S trending with approximate dimensions about 20^{km} width and 60^{km} length near to Iran – Iraq border, It is located in The Northwest of The YADAVARAN Field and in The West of JUFEYR Field. The Average Monthly Temperature is 45$^{°c}$ in summer and Highest Temperature is 52$^{°c}$. The Lowest Temperature is -4.4$^{°c}$ in winter. Maximum Rainfall is 78^{mm} in February, Winter Season.

The trap area of the south Azadegan is limited to 43.2x17.2km. The Azadegan Oil field was discovered in 1999, when Well AZN-1 was drilled vertically down to the Cretaceous Fahliyan Formation with total depth of 4,643m. The results of this well, revealed the reservoir characteristics of the field. Following to the result of the well no. AZN-1, another 5 exploration wells was drilled in different parts of this huge field down to Fahliyan Formation. In the later stage the well No.10 assumed as exploration well for evaluation of deeper formations. This well was drilled in 2008, down to the depth of 5340m (Neyriz Fm.), mainly to evaluate the Jurassic formations.

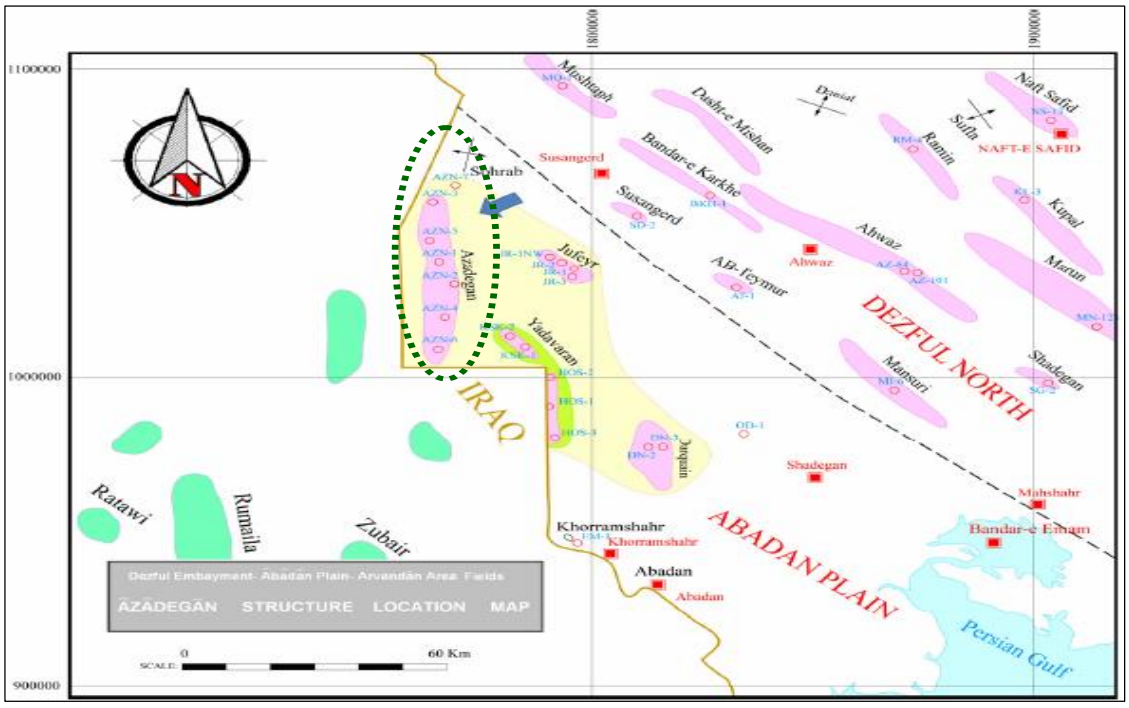


Figure 1-1: AZNS Oilfield Location Map

1.2 AZNS – 075 Well Location Map

This well is located on "Pad – 80" of South Azadegan Oil field in Block – III.

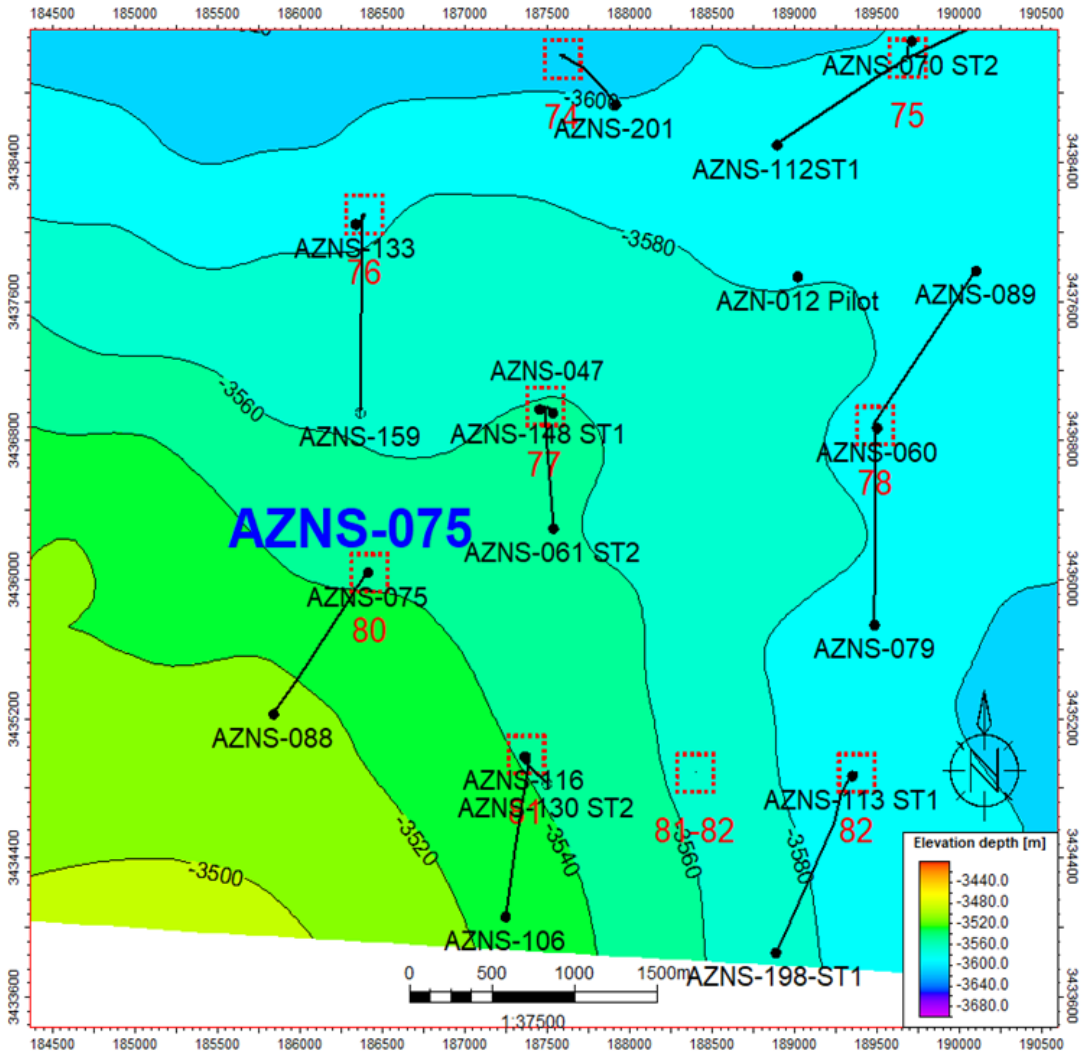


Figure 1-2: AZNS-075 Well Location Map

2. Well History

2.1 Well Informaion

Rig name	201	Owner	PEDEC/PPL
Rig type	Land Rig 2000HP	Contractor	MSA/OEOC
Well Name	AZNS – 075	Management Contractor	MSA
Well Type	Side Track I / Area III	Field	South Azadegan
Completion Type	4-1/2" * 3-1/2" 7.5K	RTE	12.95
Actual TD	3888^{m}	GLE	3.95
Surface Coordinate		N: 3,436,066 – E: 186,427	
Target Coordinate		N: 3,436,065.94 – E: 187,145.01	
Operation Date			
Spud Date	20 – March – 2025		
Released Date	01 – Sep – 2025		
Rig Days Plan / Actual	145.7 days (Main Plan) + 149.2 Days (with Contingency Plan) / 166 days		

Size (in)	Shoe Depth (mMD)	Specification
20	151.5	K – 55, 94^{ppf}, BTC
13 – 3/8	1155.5	N – 80, 68^{ppf}, BTC
9 – 5/8	2477.5	L – 80, 47^{ppf}, PJE
7 (side track)	2167.5 – 3692	L – 80, 29^{ppf}, TPCQ
7 SN PKR	2167.5	-
7 (tie back)	2034 – 2165	L – 80, 29^{ppf}, TPCQ

5 (side track)	3593.5 – 3888	L – 80, 18^{ppf}, HSG3 – FJTHD
5 SN PKR	3593.5	-

Table 2-1: AZNS-075-ST1 Workover Well Information

2.2 AZNS – 075 Well History

This well was drilled on 13 Jun 2015 by rig FATH-33 to produce oil from GADVAN formation as below operation summary:

1. 26” Hole was drilled, Ran & Cemented 20” Surface Casing. 20" CSG was run & cemented by inner stab-in stringer with slurry to surface.

2. N/U CHH and BOP Stack, Performed Pressure Test, Drilled out float shoe.

3. 17-1/2" hole was drilled. Run and cement 13-3/8” casing @ 1155.5m.

4. N/U CHS and BOP, Performed Pressure Test, drilled out float shoe.

5. 12 1/4" Hole was drilled. Run and cement 9 5/8" casing @ 2477.5m.

6. N/U THS and BOP Stack, performed pressure tests, drilled out float shoe.

7. 8 1/2" hole was drilled, 7" Liner was run & cemented from 2356m to 3799.5m. 7" L. Lap dry test was performed, no bubble was observed, 920 psi pressure build up was observed in the closing period.

8. Set two cement plugs & Rig was released on 30-Aug-2015.

9. Rig FATH-65 was spudded on 17 Jan 2017.

10. D/O Two cement plugs.

11. 7" Liner lap dry test was performed, no bubble was observed, 113 psi pressure build up was observed in closing period.

12. Perforation was performed inside of 7” liner, Perforation interval: 3659-3666 m & 3669-3678 m

13. Completion string was run and packer was set at 3575.34m.

14. Rig FATH-65 was released on 17-Feb-2017.

15. Acidizing was performed after releasing the rig. 30 bbls of 28% HCl was spotted by CT on perforation zone and then bullheaded into formation.

16. After unloading the well with diesel and nitrogen, it was observed the well was not flowing but annulus between production casing and tubing got pressure.

17. To check the status of reservoir interval tried to run Temperature, Pressure and Caliper logs in static and injection mode, but the operation of injection mode was not successful due to leakage in completion string and annulus pressure.

18. To test completion string and verify the leak point, plug & prong were set in SSD and string was tested by pressurizing, there was no leakage. The plug & prong were set in NO-GO landing nipple and tried to pressurize the string, pressure test was failed and it was confirmed that leak point is in interval between SSD and production packer.

19. It has been supposed water entry from Gadvan or even Kazhdumi formation into well is the main reason which has prevented the well flowing.

Summary of Workover Operation

The AZNS – 075 workover well was De-Complete by rig OEOC – 201 on Pad 80, from "20 – March – 2025" to "01 – September – 2025" as described in the following:

De – Completion Summary:
Prepare, arrange and started M/U totally 26 STDs (78 Jts) 5" DP jt by jt.

Install 4-1/16" C.Flange and autoclave on XMT kill valve then connected to top kill line. Install Coflex on XMT production valve and line up to Ch. manifold. removed XMT cap. meanwhile monitor annular pressure thru THS. Install lubricator, Press. Tested XMT valves, Coflex and connections w/5000 psi; "OK". Press. tested kill line w/2000 psi; "OK". Attempt to retrieve TWCV Obs. No TWCV existing. L/D Lubricator.

R/U slick line. Connected hand pump to TRSSV control line and apply pressure to operate same. RIHw/ protection sleeve on SL, installed in TRSSV. RIH w/ 2.8" gauge ring to 3562m (SSD depth). RIH w/ shifting tools Attempt to Open SSD Several Times, No. Succ. Pull out & R/D Slick line. Connected THS side outlet to Ch. Manifold. Apply pressure f/ top kill line in order to check tubing isolation. Obs pressure gradually decrease while get return f/ annulus. Try to stablish break circ. Circ. With 82 pcf fresh poly mud thru Ch. Manifold while apply 400psi back pressure, Inc. FR to 300 gpm step by step make which indicates that string is wash out. Cont. circ. Till balance MW (82pcf) in/out. Recognize that tubing is wash out f/ above the SSD. Cont. circ. And obs the pit levels. Prepare kill mud in order to inc. MW to 84 pcf. In progress. Cont. circ. And obs the pit levels. Prepared kill mud, added to active system and inc. MW to 84 pcf.

R/U SL. BOP & lubricator. Retrieve protection sleeve. Close TRSSV. Install TWCV. Press. Tested w/ 5000psi; OK. B/O XMT Kill & Choke lines. N/D XMT 4-1/16"10k, N/U 13-5/8" 10k BOP Stack is in Progress. Cont. N/U 13-5/8" 10k BOP Stack. attempt to perform BOP test several Time No Succ, Work on fixing BOP leakages.

P/U & M/U 4-1/2" TBG HGR Running-Retrieving Tool (TPCQ * ACME) + X.O. S (4-1/2" IF * 4-1/2" TPCQ) + 1Jt 5" DP + Pup Joint, RIH W/ Same and Screw Onto TBG HGR, Record Upward & Dnward String Weight, P/U TBH from THS (Hook load: 230 Klb), Release Completion String w/ 27 Turns Forward Without TQ, Cut 1/4" CL f/ TBG HGR Slots, R/D Retrieving String Including: P.Joint, L.Joint, X.O.S, HGR Running Tools, B/O & L/D TBG HGR + FLUTED SWAGE ADAPTER.

Mud Circulate meanwhile R/U Casing Running Equipment. Continue Retrieving Comp. Strg As Follow: B/O & L/D 9 Jts 4-1/2" TBG (TPCQ) + 1 Jt TRSSV & L/D 1 Jts 4-1/2" TBG (TPCQ) Totally: 10 Jts) while Circ Mud Cross Well Head NL.NG. Continue Retrieving Comp. Strg As Follow: B/O & L/D 4-1/2" TBG (TPCQ) Totally 115 Jts while Circ Mud Cross Well Head w/ NL.NG. Continue Retrieving Comp. Strg As Follow: B/O & L/D 4-1/2" TBG (TPCQ-EX, 18.9#) Totally 236 Jts & Cross Over (4-1/2", 18.9#, TPCQ-EX BOX * 3-1/2", 10.2#, TPCQ-EX PIN) & 3-1/2" TBG (TPCQ-EX, 10.2#) Totally 30 Jts while Circ Mud Cross Well Head w/ NL.NG. Continue Retrieving Comp. Strg As Follow while Circ Mud Cross Well Head w/ NL.NG. B/O & L/D 3-1/2" TBG (TPCQ-EX, 10.2#) Totally 136 Jts + 5 Jts 3 1/2" P.Joint (TPCQ-EX, 10.2#) + Expansion Jt + SSD (Close Position) + Anchor Seal (w/ Good Condition).

P/U & M/U 6" B.Bit#1 (Used, Open) + 7" Scraper and Followed by 12 Jts 3 1/2" HWDP + 48 Joints 3 1/2" D.Pipe "G" (Jts By Jts) + 14 STD's 3-1/2" D.Pipe "S" + 12 Jts 3-1/2" D.Pipe "S" (Jts By Jts) To 1093m While Pass Rabbit thru All tubular & Fill Up String Every 15 STD's. NL.NG. Continue Run in hole with 6" B.Bit#1 (Used, Open) To 1230m, P/U & M/U XOS + 9 5/8" Scraper & Follow By 5" D.Pipe to 3283m While Fill Up String Every 15 STD's. NL.NG. Till R.T. Continue Run in hole with 6" B.Bit#1 (Used, Open) By 5" D.Pipe from 3283m to 3575m (Jts By Jts) , Tag PKR @ 3575m, While Fill Up String Every 15 STD's. NL.NG. Circ BTM'S Up, Observe the well, Static.

Start POOH from 3575m to 900m While Flow Check the well @ 7" L.Lap NL.NG . Continue pull out of hole from 900m to Surface While Flow Check the well on BHA, NL.NG & L/D Mouse Hole, Pick up shoting nipple. R/U Wireline logging Equipment (SEALAND Co.). Perform Log according program in the hole:

Run#1: CBIL-CDR-GR-CCL (7in Liner) : Run Sealand Co CBIL/CDR/GR/CCL logging Tools to 3555m, Start logging up to 2356m (7" L.Lap), Cont POOH logging Tools to Surf. while Circ X-Wellhead W/ NL-NG.

Run#2: CBIL-CDR-GR-CCL (9 5/8in Casing) Run Sealand Co CBIL/CDR/GR/CCL logging Tools to 2356m (7" L.Lap), Start logging up to 790m while Circ X-Wellhead W/ NL-NG, Cont log up to Surface while Circ X-Wellhead W/ NL-NG. R/D Wireline logging Equipment (SEALAND Co.). Prepare Rig Floor (L/D shooting nipple, Pick up Mouse Hole) ،Till R.T.

P/U & M/U and R/B 9 Jts 6-1/2" D.Pipe, Install Wearbushing. P/U & M/U Open-End DPs including: 23 STD's 3-1/2" D.P "G" + 39 Jts 3-1/2" D.Pipe "S" (Jts by Jts) & Follow By 5" D.Pipe to 3290m While Circ Mud Cross Well Head , NL.NG.

Held Pre-job safety meeting, Rig up cement unit and Line up to the rig floor, Test CMT lines W/500psi 5 min. And 3000 psi for 15 min, OK. Fill Pump Truck tanks with fresh Water for mixing fluids. Start mixing cement additives and preparing mixing fluids according Program. Start pumping 10 bbl (62.4 pcf) Ahead spacer, Mix & Pump 23 bbl Cement slurry (118 PCF) with rate 4 bpm. Pump 3 bbl (62.4 PCF) Spacer Behind, Displace mud With 143 BBl (1 BBL Short). Pull out the drill pipe above the top of Cement, 10 Std's. Flush The String. POOH 6 Std's and Circ BTM's UP. Cont POOH To 2550 m. Cont. POOH 3-1/2" & 5" OEDP F/ 2550 to 2320m On Elevator, While Circ. C.W.H, W/ NL-NG. Cont. POOH 3-1/2" & 5" OEDP F/ 2320m to surface On Elevator, While Circ. C.W.H, W/ NL-NG.

P/U & M/U 6-1/8" D/O BHA including: 6-1/8" Tri-Cone Bit (Open, K.Dream, Used, S/N: 2304674JH, Dull Condition: 2-2-WT-A-E-I-BT-DTF, IADC: 537) + 4-3/4" B.Sub + 9Stds 3-1/2" HWDP and RIH W/ Same To 249m, F/U BHA & Break Circ. , W/ NL-NG. Cont. RIH W/ 6-1/8" D/O BHA F/ 249 To 3107m Followed by 3-1/2" & 5" DPs On Elevator, While F/U Strg & Break Circ, Every 15Stds, W/ NL-NG.

Held up Strg Wt. @ 3107m, Conn. TDS and attempt to Cont. RIH W/ Wash Dn, No Success, Start D/O Medium to Hard CMT Inside 7"LNR W/ 6-1/8" D/O BHA F/ 3107 To 3156m W/ Applying Parameters: Rotation: 60RPM, TQ: 3-4klbs.ft, F.R: 350GPM, SPP: 1900-2000psi, WOB: 5-12klbs, ROP: 7-8mph, While Reciprocate Every Drilled out Jt, W/ NL-NG. Cont. D/O Medium to Hard CMT Inside 7"LNR W/ 6-1/8" D/O BHA F/ 3156 To 3165m W/ Applying Parameters: Rotation: 60RPM, TQ: 3-4klbs.ft, F.R: 350GPM, SPP: 1900-2000psi, WOB: 5-12klbs, ROP: 7-8mph, While Reciprocate Every Drilled out Jt, W/ NL-NG. Pump 40bbl Hi-Vis Pill @ 3165m, then Circ. Till Shakering out the pumped Hi-Vis Pill, W/ Nl-NG. POOH 6-1/8" D/O BHA F/ 3165m To surface On Elevator and L/D BHA & 6-1/8" T.Cone Bit W/ Same Condition, While Circ. C.W.H, W/ NL-NG.

P/U & M/U 7"DST Tool Srting including: Bottom B.T (First Memory Gauge) + Anchor pipe + X.O.S 3 1/2" EUE Box x 3 1/2" FH Pin + Middle Packer element + 7" Above Packer + X.O.S 3-1/2" FH *3-1/2" IF PIN + RH Release Safety Joint + Hydraulic JAR + Middle B.T (Second Memory Gauge) + Hydrospring + D.C.I.P + X.O.S 4-1/2" IF Box x 3-1/2" IF Pin + 1 Jt 3-1/2" Drill Pipe + Reverse Sub and RIH to 22m, While Monitor the Well, W/ NL-NG. Cont. RIH W/ 7" DST Tool String F/ 22 To 865m On Elevator Followed by 6Stds 4-3/4" DC + 9 Stds 3-1/2" HWDP + 12 Stds 3-1/2" DP + 4 Stds 5" DP W/ Speed Control at the request of OEOC DST Supervisor, While Pass Rabbit Thru. all Tubular and F/U Strg W/ Drill water as a Water Cushion at 5-Std intervals, W/ NL-

NG. Cont. RIH W/ 7" Dry Test Tool String F/ 865 To 3061m On Elevator Followed by 5" DP W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 2265m of Strg W/ Drill water as a Water Cushion at 5-Std intervals, W/ NL-NG.

Dry Test Summary:
Perform Dry Test Op. as follow:

R/U and prepare surface lines and DST choke manifold, Pressure test lines to 3000 psi for 15 minutes, test confirmed OK, Record Strg Wt. in both upward and downward directions. Setting PKR and Opening Hydro-Spring Valve: Rotate Strg 6 full turns clockwise, Apply set-down Wt. of 20klbf to set the 7" Dry Test PKR at 3057m, Obs. Hydro-Spring Valve opening indication on M/D. Open Period Monitoring: Maintain open condition for 3 Hrs. , Log start time of Opened period, Monitor for any bubbles at the surface, no bubbles observed, Confirm Annulus fluid level is Static during observation. Close Period Monitoring: S/O Strg Weight, Rotate Strg 11 full turns forward to close the DCIP Dry Test Assy Valve, Log start time of Closed period, Closed period Monitoring for 6 Hrs. in progress at M.N for ongoing monitoring, Confirm Annulus fluid level is Static during observation. Cont. Close Period Monitoring, Confirm Annulus fluid level is Static and stable during observation. Open Circulation Valve: Drop Bar to open Circ. valve, No Success, Open DCIP Circ. Port and Establish Reverse Circulation, confirm balance mud is observed at the surface and the water cushion is the same as the F/U Volume. Prepare to POOH: Unset the 7" Dry Test PKR using normal P/U Weight, B/O & L/D Dry Test Surface Equipment. POOH 7" Dry Test Tool String F/ 3059 To 348m On Elvevator W/ Speed Control at the request of OEOC Dry Test supervisor, While Circ. C.W.H, W/ NL-NG. POOH 7" Dry Test Tool String F/ 348m To Surface On Elvevator W/ Speed Control at the request of OEOC Dry Test supervisor, B/O & L/D Dry Test Tool String, Read Middle & BTM B.T, 6Hrs. Close-Period Monitoring Results: [Middle B.T: 3264 - 3358psi, BTM B.T: 3280-3374psi], Check Sample Properties of flowing sample between DCIP & Hydrospring [MW: 80pcf, PH: 11.4 , Cl: 172000, Ca+: 1400 , PV: 8, YP:5], While Circ. C.W.H, W/ NL-NG.

Ret. Wear Bushing, P/U & M/U 9-5/8" Dry Test Tool String including: Bottom B.T (First Memory Gauge) + Anchor pipe + X.O.S 3 1/2" EUE Box x 3 1/2" FH Pin +Middle Packer element + 9-5/8" Above Packer + X.O.S 3-1/2" FH *3-1/2" IF PIN + RH Release Safety Joint + Hydraulic JAR + Middle B.T (Second Memory Gauge) + Hydrospring + D.C.I.P + X.O.S 4-1/2" IF Box x 3-1/2" IF Pin + 1 Jt 5" Drill Pipe + Reverse Sub and RIH W/ Same, While Pass Rabbit Thru. all Tubular and Circ. C,W,H, W/NL-NG. Cont.

RIH W/ 9-5/8" Dry Test Tool String To 2130m On Elevator Followed by 3Stds 6-1/2" DC & 5" DPs W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 1285m of Strg W/ Drill water as a Water Cushion at 5-Std intervals, and Circ. C,W,H, W/ NL-NG.

Cont. RIH W/ 9-5/8" Dry Test Tool String F/ 2130 To 2315m On Elevator Followed by 5" DP W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 1285m of Strg W/ Drill water as a Water Cushion at 5-Std intervals , and Circ. C,W,H, W/ NL-NG.

R/U and prepare surface lines and Dry Test choke manifold, Pressure test lines to 3000 psi for 15 minutes, test confirmed OK, Record Strg Wt. in both upward and downward directions. Setting PKR and Opening Hydro-Spring Valve: Rotate Strg 6 full turns clockwise, Apply set-down Wt. of 25klbf to set the 9-5/8" Dry Test PKR at 2314m, Obs. Hydro-Spring Valve opening indication on M/D. Open Period Monitoring: Maintain open condition for 3 Hrs. , Log start time of Opened period (03:15), Monitor for any bubbles at the surface, no bubbles observed, Confirm Annulus fluid level is Static during observation. Close Period Monitoring: S/O Strg Weight, Rotate Strg 11 full turns forward to close the DCIP Dry Test Assy Valve, Log start time of Closed period (06:35), Maintain open condition for 6 Hrs. , Confirm Annulus fluid level is Static and stable during observation. Open Circulation Valve: Drop Bar to open Circ. valve, Establish Reverse Circulation, confirm balance mud is observed at the surface and the water cushion is the same as the F/U Volume. Prepare to POOH: Unset the 9-5/8" Dry Test PKR using normal P/U Weight, B/O & L/D Dry Test Surface Equipment. POOH 9-5/8" Dry Test Tool String F/ 2319 To 820m On Elvevator W/ Speed Control at the request of OEOC Dry Test supervisor, While Circ. C.W.H, W/ NL-NG.

POOH 9-5/8" Dry Test Tool String F/ 820m To Surface On Elvevator W/ Speed Control at the request of OEOC Dry Test supervisor, B/O & L/D Dry Test Tool String, Read Middle & BTM B.T Memory Data, 6Hrs. Close-Period Monitoring Results: [Middle B.T: 1889 - 2189psi, BTM B.T: 1926-2226psi], Check Sample Properties of flowing sample between DCIP & Hydrospring [PH: 11.2 , Chloride: 170000 mg/lit, Ca++: 1200 mg/lit , Total Hardness: 1360 mg/lit], While Circ. C.W.H, W/ NL-NG. Perform BOP Test as NIOC Policy.

RIH W/ 3-1/2" OEDP To 278m, While Circ. C.W.H, W/ NL-NG. Resume RIH W/ 3-1/2" & 5" OEDP 278 To 2300m, While Circ. C.W.H, W/ NL-NG. Conn. TDS & CBU @ 2300m, Meanwhile Prepare Rig Floor and R/U CMT Job Eqp., While Monitor the

Well & Circ. C.W.H, W/ NL-NG. Cont. CBU @ 2300m, Meanwhile Prepare Rig Floor and R/U CMT Job Eqp. , While Monitor the Well & Circ. C.W.H, W/ NL-NG.

RIH W/ 3-1/2 & 5" OEDP F/ 2300 To 2358m, Held PJSM, Press. Test Chiksan Pipes & CMT Valves W/ 500/ 3000psi Stepwise, Ok, Perform Ongoing CMT Plug as follow:

Pump 15bbl Spacer Ahead (MW: 62.4pcf) + Prepare CMT Solution and Mix W/ CMT Class G and Pump 35bbl CMT Slurry (Slurry Density: 118pcf) + Pump 1.8bbl Spacer Behind (MW: 62.4pcf) Disp. Pumped Spacer Ahead, CMT Slurry, and Spacer behind W/ 75bbl Mud (MW: 84pcf), While Monitor the Well, W/ NL-NG. B/O Chiksan Pipes, POOH 3-1/2" & 5" OEDP F/ 2358 To 2100m, Flush String, Cont. POOH 3-1/2" & 5" OEDP F/ 2100 To 1979m, Circ. As Cycle @ 1979m, While Monitor the Well & Circ. C.W.H, W/ NL-NG. POOH 3-1/2" & 5" OEDP F/ 2100m To Surface, While Circ. C.W.H, W/ NL-NG.

P/U & M/U 8-1/2" D/O BHA including: [8-1/2" Tri-Cone Bit (Used, K.Dream, Open, S/N: 2304674JH, IADC: 537, Dull: 2-2-WT-A-E-I-BT-DTF)+ Bit Sub (Float-In) + 3Stds 6-1/2" DC] and RIH To 82m, F/U BHA and Break Circ. , W/ NL-NG. Cont. RIH W/ 8-1/2" D/O BHA F/ 82 To 338m Followed By 5" DPs On Elevator, While F/U Strg & Break Circ. at 10-Std intervals, W/ NL-NG. Cont. RIH W/ 8-1/2" D/O BHA F/ 338 To 1989m Followed By 5" DPs On Elevator, While F/U Strg & Break Circ. at 10-Std intervals, W/ NL-NG. Cont. RIH W/ 8-1/2" D/O BHA F/ 1989 To 2134m Followed By 5" DPs On Elevator, While F/U Strg & Break Circ. At 10-Std intervals, W/ NL-NG. Conn. TDS and RIH W/ 8-1/2" D/O BHA W/ Wash Dn F/ 2134 To 2174m, Held up Strg Wt. & Tag TOC @ 2174m, W/ NL-NG. CBU @ 2174m W/ 8-1/2" D/O BHA, W/ NL-NG.

D/O CMT W/ 8-1/2" D/O BHA F/ 2174 To 2270m W/ Applying Parameters [WOB: 3-12klbs, Rotation: 30-60RPM, Tq: 1-5klbs.ft, F.R: 400-450GPM, SPP: 550-650psi, ROP: 5-6mph], While Reciprocate Every Drilled out Std before each Conn. & Pump Hi-Vis Pill Periodically, W/ NL-NG. Pump 40bbl Hi-Vis Pill, CBU @ 2270m to sweep the well W/ 8-1/2" D/O BHA till Shakering out Hi-Vis Pill, W/ NL-NG. POOH 8-1/2" D/O BHA F/ 2270m To Surface On Elevator, B/O 8-1/2" Tri-Cone Bit W/ Same Conditon & rest of BHA, While Circ. C.W.H, W/ NL-NG.

P/U & M/U 9-5/8" Scraper BHA including: [8-1/2" Tri-Cone Bit (Used, K.Dream, Open, S/N: 2304674JH, IADC: 537, Dull: 2-2-WT-A-E-I-BT-BHA)+ Bit Sub + 9-5/8" Scraper + 1 Std 6-1/2" DC] and RIH To 27m, F/U BHA & Break Circ. , W/ NL-NG. Cont. RIH W/ 9-5/8" Scraper BHA F/ 27 To 2252m Followed by 5" DPs On Elevator, While F/U

Strg & Break Circ. At 10-Std Intervals, W/ NL-NG. Conn. TDS and RIH W/ 9-5/8" Scraper BHA F/ 2252 To 2270m W/ Wash Dn, Pump 30 bbl Hi-Vis Pill, CBU @ 2270m, While Perform Mud Treatment to optimize Rheological properties, Reduce MW F/ 84 pcf To 80 pcf, and Sev. Times Scrape Interval 2170 to 2270m, Prpbable Set Point of 9-5/8" Hyd. Whipstock Sys. PKR , W/ NL-NG. POOH 9-5/8" Scraper BHA F/ 2270To 829m On Elevator, While Circ. C.W.H, W/ NL-NG. POOH 9-5/8" Scraper BHA F/ 829m To Surface On Elevator, B/O 8-1/2" Tri-Cone Bit W/ Same Conditon & rest of BHA, While Circ. C.W.H, W/ NL-NG.

P/U & M/U 9-5/8" Cased-Hole Sidetrack BHA including: 9-5/8" Hyd. Whipstock System (Hyd. PKR + Hyd. Whipface) + 8-3/8" Lead Mill +6-1/2" Running Tool + 1 Jt 5" DP; Conn. CL to Hyd. PKR Port, Pass & Secure in Whipface Slot; Conn. same CL to 8-3/8" Lead Mill Nozzle;Gauge Lead Mill w/ 8-3/8" Ring Gauge, Ok; B/O 5" DP & F/U Hyd. Whipstock Assy. w/ Oil, Let Oil Settle in all CL and System to releaseany entrapped air; M/U 5" DP & UBHO Sub (Gyro sub); Align Whipface; M/U 1st 6-1/2" DC & RIH To 46m; F/U 6-1/2" DC w/ Fresh Hi-Vis Pill, While Circ. C.W.H, NL-NG. Cont. RIH W/ 9-5/8" Cased-Hole Sidetrack BHA F/ 46 To 1634m W/ Speed Control at the request of HPOGC supervisor followed by3Stds 6-1/2" DC and 5" DPs, While F/U String W/ F/U Hose at 10-std interval and Monitor the Well, W/ NL-NG.

Cont. RIH W/ 9-5/8" Cased-Hole Sidetrack BHA F/ 1634 To 2260m W/ Speed Control at the request of HPOGC supervisor followed by5" DPs, While F/U String W/ F/U Hose at 10-std interval and Monitor the Well, W/ NL-NG.R/U Surface Logging Eqp. ; P/U & Assemble Wire Line Tools as Gyro Tool String including: [Cable head + Telemetry + CCL + Temp. Sensor + Pres. Sensor + Gyro + Mule Shoe] - (Max OD: 2", Total Length: 3.4m, Total Weight: 65lb);RIH To 2257m (Gyro Sub Depth);Latch Gyro Tool String into Gyro Sub, Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success; POOH 2" GyroTool String to Surface; While Monitor the Well, W/ NL-NG., Wait on Receive Back up Gyro Tool String; P/U & Assemble Received Wire Line Tools as Gyro Tool String including: [Cable head + Telemetry + CCL + Temp. Sensor + Pres. Sensor + Gyro + Mule Shoe] - (Max OD: 2", Total Length: 3.4m, Total Weight: 65lb); RIH To 2257m (Gyro Sub Depth); Latch Gyro Tool String into Gyro Sub, Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success; While Monitor the Well, W/ NL-NG.

Cont. Attempt to get Gyro data; Latch Gyro Tool String into Gyro Sub,Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success; POOH 2" Gyro Tool String to Surface; Change Mule Shoe,Assemble Wire Line Tools as Gyro Tool String

including: [Cable head + Telemetry + CCL + Temp. Sensor + Pres. Sensor + Gyro +6Hrs. NPT For Paniz Energy Co. due to too malfunction, Cont. Attempt to get Gyro data; Latch Gyro Tool String into Gyro Sub,Mule Shoe] -(Max OD: 2", Total Length: 3.4m, Total Weight: 65lb); RIH To 2257m (Gyro Sub Depth); Latch Gyro Tool String into Gyro Sub,Attempt to get Gyro data, Ok, repeat latch/unlatch cycles multiple times to verify tool functionality and data accuracy – confirmed data OK, While Monitor the Well, W/ NL-NG.Set Whipface orientation to planned Azimuth (Az. :90deg) based on Gyro Data reading; POOH 2" Gyro Tool String to surface, L/D Wireline Tools, While Monitor the Well, W/ NL-NG.Record Up/Dn Strg Wt, Set Whipstock PKR @ 2265m (Whipstock Top Depth: 2257.9m, Whipstock BTM Depth: 2265m)W/ apply pressure at 3000psi & hold for 10min (Hook Load drop confirmed PKR set), Perform 20klbf Push/Pull Test, then Return Hook Load to neutral & bleed off Press. to 0psi; Apply 80klbf Overpull to shear 8-3/8" Lead Mill shear screw; Apply and hold pressureat 2000psi, Rotate Strg at 20RPM to break knock-off plugs, take Mud return, Bleed off Press. to 0psi, While Monitor the Well, W/ NL-NG.CBU @ 2265m to Shear In/Out Mud, While Monitor the Well, W/ NL-NG.Window Milling W/ 8-3/8" Cased-hole sidetrack BHA F/ 2257.9 To 2259.2m W/ Applying Parameters: [WOB: 2-14klbs, Rotation: 50-60RPM,Tq: 2-7klbs.ft, F.R: 250-320GPM, SPP: 430-450psi], While Pump Hi-Vis Pill periodically & check Ditch magnet ,and Monitor the Well,W/ NL-NG.Cont. Window Milling W/ 8-3/8" Cased-hole sidetrack BHA F/ 2259.2 To 2262.5m W/ Applying Parameters: [WOB: 2-14klbs,Rotation: 50-60RPM, Tq: 2-7klbs.ft, F.R: 250-320GPM, SPP: 430-450psi], While Pump Hi-Vis Pill periodically, check Ditch magnet,Sh.Shakers Sample (50% Formation & 20% CMT at last sample), and Monitor the Well, W/ NL-NG.Pump 40bbl Hi-Vis Pill, CBU @ 2262.5m Till Shakering out pumped Hi-Vis Pill, While Monitor the Well, W/ NL-NG.POOH 8-3/8" Cased-hole sidetrack BHA F/ 2262.5m To Surface On Elevator, B/O & L/D 8-3/8" Lead Mill (Full Gauge, 20% Used), UBHO,and rest of BHA, While Circ. C.W.H, W/ NL-NG.P/U & M/U 8-1/2" Window Dressing BHA including: [8-1/2" Tri-Mill (Lead Mill + Follow Mill + Watermelon -- S/N: 4005, New) +6-1/2" Running Tool + 1 Jt 5" DP + 4 Stds 6-1/2" DC] and RIH to 123m, F/U BHA & Break Circ, W/ NL-NG.Cont. RIH W/ Window Dressing BHA F/ 123 To 922m On Elevator Followed by 5" DPs, While F/U Strg at 15-Std Intervals, W/ NL-NG.

RIH W/8-1/2" Milling & Dressing BHA to 2259.4m, String Took Weight, Circ. Mud, W/ NL-NG.Start Window Milling & Dressing W/8-1/2" Tri-Mill to 2266m. Pump Hi-Vis Pill to Clean the Hole while Dec. Mwt to 76pcf & Work on Mud Rheology, Check Window Clear by Lowering The Mill Through it Without Rotating Several times.POOH

to Surface and L/D Tri Mill (10% Used).P/U 6-3/4" PDM (AKO: 1.5°, Stabilizer: 8-1/8", S.R: 0.36, Lobe: 5/6, Stage: 6) & Prepare To Suface Test .

Directional Drilling Summary:

Cont. P/U 6-3/4" PDM (Lang Fang,AKO: 1.5°, Stabilizer: 8-1/8",S.R: 0.36,Lobe: 5/6, Stage: 6), Perform test W/ F.rate: 400gpm, Press: M.L: 450psiM/U 6-3/4" Float Sub + 6-1/2" UBHO + 6-3/8" NMDC, Set MWD , M/U 8-3/8" New TCI Bit (537, 3*16/32, Kingdream)M/U Jyro Sub (Paniz) / Align the Key of UBHO Sleeve & Jyro Sub With the Bent Sub-Scribe line, Perform Shallow test :W/ F.rate: 400gpm, Press: M.L: 850-910psi. Cont. RIH W/ 24 Jts 5" H.W.D.P (Jt By Jt & Pass Rabit thru Each Joint) + 6 1/2" FLEX JOINT + 6 1/2" D.JAR + 6 Jts 5" H.W.D.P (Jt By Jt & Pass Rabit thru Each Joint) to 305 W/NL-NG.Cont. RIH W/ 5" Drill Pipe to 2260m(BTM) While Perform Shallow Test @ 500m & 1650m, Ok.R/U & Assemble Wire Line Tools as Gyro Tool String including: [Cable head + Telemetry + CCL + Temp. Sensor + Pres. Sensor + Gyro + Mule Shoe] - (Max OD: 1-11/16", Total Length: 3.3m), Check Surface Gyro Data, RIH To 2247m (Gyro Sub Depth); Latch Gyro Tool String into Gyro Sub, Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success; POOH Gyro Tool String to 1000m While Monitor the Well, W/ NL-NG. .

Cont. POOH Gyro Tool to Surface and R/D Wire Line Tools While Monitor the Well, W/ NL-NG.POOH D.D BHA to Surface, L/D Gyro Sub, Change Key of Sleeve, M/U & Align Key of Sleeve Gyro Sub With the Bent Sub-ScribeRIH W/D.D BHA to 330m, R/U Wire line Tools As Gyro, Run Gyro Tool String, Latch in Gyro Sub, Check Gyro Data Several Times, OK.Pull out Gyro Tool to Surface & R/D it. Cont. RIH W/ D.D BHA to 2262.5m While Perform shallow test @ 504m,1387m, OK. F/U String W/NL-NG.R/U & Assemble Wire Line Tools as Gyro Tool including: [Cable head + Telemetry + CCL + Temp. Sensor + Pres. Sensor + Gyro + Mule Shoe] - (Max OD: 1-11/16", Total Length: 3.3m), RIH To 680m .

Cont RIH with Gyro Tool To 2247m (Gyro Sub Depth).Latch in Gyro Sub, repeat latch/unlatch cycles multiple times to verify tool functionality and data accuracy – confirmed data OK. Adjust Toolface Orientation , POOH Gyro Tool String to Surface While Monitor the Well, W/ NL-NG.Strat D.DRLF 8-3/8" Hole section As Below :D.DRLG As Sliding Mode F/2266.10m to 2278m(DRLG Parameter : WOB: 6-10Klb, F.Rate: 450 GPM ,SPP: 1560-1650 Psi)D.DRLG As Rot. Mode F/2278m to 2293.5m(DRLG Parameter : WOB: 8-15Klb, ,F.Rate: 450 GPM SPP: 1560-1680 Psi, Rot: 35 RPM , TQ: 3-7 Klb.f)While Take Survey & Monitor the Well, W/ NL-NG .

Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/2293.5m To 2310m While Take Survey & Monitor the Well, W/ NL-NG.(DRLG Parameter: WOB: 12-18Klb, Rot: M + 35rpm, SPP: 1580-1680 Psi, F.Rate: 450GPM,TQ: 2-7klb.ft)Pump Hi Vis Pill to Clean the Hole, POOH to Surface, L/D Gyro Sub (Paniz Co.) & 8-3/8" Tri Cone No#1 (B.Bit, king Dream, S/N: 2417584JH, IADC: HJT537G, Nozzle: 3*16/32")(Bit Dull Condition: 1.1.WT.A.E.I.NO.BHA)Check PDM & MWD Tools (Change Battery), M/U & RIH W/ 8-3/8" New PDC Bit No#2 (Best, Nozzles: 7*14/32, S/N : 220793, IADC: M1375) + 6-3/4" PDM (AKO : 1.5)(LANG FANG, Run 2, S/N: ORT-572151490-3, R/S: 5/6, Stage: 6, Rev/Gal: 0.36), Conn To TDS and Perform Surface test,Ok. P/U & M/U D.D BHA Including :(6-3/4" Float Sub + 6-3/4" UBHO + 6-3/4" NMDC + 24 Jts 5" HWDP + 6-1/2" Flex Joint + 6-1/2" DERLG Jar +6 Jts 5" HWDP) and follow by 5" D.Pipe to 1250m While Perform Shallow test @ 500m and fill up string every 15 Stands W/ NL.NG .

Cont. RIH W/ D.D BHA to 2310m While Perform Shallow test @ 1500m and fill up string every 15 Stands.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2310m To 2329.29m. Take SurveyPump Hi Vis Pill & B/R and R/D Each STD.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2329.29m To 2330.80m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2330.80m To 2333.94m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2333.94m To 2349.80m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2349.80m To 2354.14m.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2354.14m To 2357.96m.Pump Hi Vis Pill & B/R and R/D Each STD.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2357.96m To 2359.84m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2359.84m To 2364m.While Monitor the Well, W/ 1.5-2.5 BPH Loss. .Rotating Mode DRLG Parameter: WOB: 12-18Klb, Rot: M + 35rpm, SPP: 1300-1450 Psi, F.Rate: 450GPM,TQ: 2-5klb.ft.Sliding Mode DRLG Parameter: WOB: 5-11Klb, Rot: M , SPP: 1300-1450 Psi, F.Rate: 450GPM.

Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2364m To 2369m.Take SurveyCont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2369m To 2375m.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2375m To 2378m.Take SurveyCont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2378m To 2379m.Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2379m To 2385m.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2385m To 2386.5m.Take Survey Pump Hi Vis Pill & B/R and R/D Each STD.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2386.5m

To 2388m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2388m To 2393m.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2393m To 2398m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2398m To 2402m.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2402m To 2407m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Sliding Mode F/ 2407m To 2411m.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2411m To 2415m.Pump Hi Vis Pill & B/R and R/D Each STD.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2415m To 2416.8m.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2416.8m To 2425.5m.While Monitor the Well, W/ 0.5-1 BPH Loss. .Rotating Mode DRLG Parameter: WOB: 12-18Klb, Rot: M + 35rpm, SPP: 1200-1600 Psi, F.Rate: 400-450GPM, TQ: 2-5klb.ft.Sliding Mode DRLG Parameter: WOB: 5-11Klb, Rot: M , SPP: 1200-1600 Psi, F.Rate: 400-450GPM.

Cont. Directional Drilling 8-3/8" Hole Section F/ 2425.5m To 2617.34m W/ Pump 25 BBL LCM Pill (10#, Limestone chips F) W/ 8-10 BPH loss.Take Survey Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 2617.34m To 2620m W/ Low ROP w/ 8-10 BPH loss.Try to Cont. D.DRLG, No. Succ. Due to Low ROP. And Pressure Up PDM In Slide mode Drilling.Circ BTM's Up Till Clean the well, Spot 100 BBL LCM Pill (10#, Limestone chips F).Try to POOH on elevator, observe 30-40 klb drag, POOH pump out to 2530m, cont. POOH to 2262m on elevetor w/0-10 klb drag.Pump & spot 100 bbl LCM Pill (20#, lst chips F+ M), POOH to 800m While Circ. Mud Cross Wellhead W/ 5 BPH loss.Slip & Cut 97ft of DRLG Line @ 800m. Circ. Mud Cross Wellhead W/5 BPH loss.Cont. POOH From 800m To On BHA.B/O and L/D 6 3/8" NMDC + 6 1/2" UBHO + 6 3/4" float sub + 6 3/4" PDM + 8 3/8" PDC Bit No#2 (Best, Nozzles: 7*14/32,S/N : 220793, IADC: M1375) Bit Dull Condition : (0.1.BT.S.X.I.NO.DMF)P/U & RIH W/ 5" D.Pipe (Jts By Jts)(Totally 5 Jts) To 46 m (Wash and pass Rabbit thru All 5" D.Pipe) .

Cont. P/U & RIH W/ 5" D.Pipe (Jts By Jts)(Totally 75 Jts) To 710 m (Wash and pass Rabbit thru All 5" D.Pipe) Circ Mud Hi-Rate Inside all Tubular For Clean it W/ 5-6 BPH loss.POOH to Surface, Rack back Tot. 25 STD 5" DP.P/U 6-3/4" PDM (AKO : 1.22)(LANG FANG, NEW, S/N: ORT-572150642-1, R/S: 5/6, Stage: 6, Rev/Gal: 0.36), Conn To TDS and Perform, Ok.P/U & M/U 8-3/8" Uesd PDC Bit No#2 (RR, Beste, Nozzles: 7*14/32, S/N : 220793, IADC: M1375) + D.D BHA Including : (6-3/4" Float Sub + 6-3/4"UBHO + 6-3/4" NMDC + 24 Jts 5" HWDP + 6-1/2" Flex Joint + 6-1/2" DRLG Jar + 6 Jts 5" HWDP) and follow by 5" D.Pipe to 300m.Cont. RIH with 5" D.Pipe

to 2500m While Perform Shallow test @ 500m and fill up string every 15 Stands W/ 5-6 BPH loss.Cont. RIH Pump Down with Mediume Wash & Ream To 2620m (TD) .

Cont. Directional Drilling 8-3/8" Hole Section F/ 2620.13m to 2884m W/ Apply Params [WOB: 2-4klbf, Rotation: 35RPM, TQ: 5-7klb.ft, F.R: 470gpm, SPP: 1550-1800psi]. POOH 8-3/8" Dir. Drlg BHA F/ 2884 To 2538m W/ Pump out and B/Ream in some intervals due to PDM life time, While monitor the well, W/ 5-6BPH Loss.Cont. POOH 8-3/8" Dir. Drlg BHA F/ 2538 To 155m On Elevator, While Circ. C.W.H, W/ 5-6BPH Loss.Stop Op. at the request of OEOC Rig 201 HSE Officer due to windy weather @ 155m, While Circ. C.W.H, periodically slow & break Circ. Thru. Strg, W/ 5-6BPH Loss.

Cont. Stop Op. at the request of OEOC Rig 201 HSE Officer due to windy weather @ 155m, While Circ. C.W.H, periodically slow & break Circ. Thru. Strg, W/ 3-4BPH Loss.Resume POOH 8-3/8" Dir. Drlg BHA F/ 155m To surface, L/D 8-3/8" Bit (Dull Grade: 2-3-WT-A-X-I-NO-BHA) & Rest of BHA, While Circ. C.W.H, W/ 3-4BPH Loss.Perform BOP Test as NIOC Policy, Retrieve Wear Bushing, Set Plug Tester, Perform BOP Test as follow:5k 13-5/8" Annular w/ 3500psi, 15min, Ok, 10k 13-5/8" Top Ram (VBR 2-7/8" - 5") w/ 7500psi, 15min, Ok, 10k 13-5/8" BTM Ram5" Pipe Ramw/ 7500psi, 15min, Ok, 10k 13-5/8" Shear Ram w/ 7500psi, While Press. Test All Choke Manifold Valves & Accumulator Unit Functionality,Ok, Retrieve Plug Tester, Install Wear Bushing.P/U & M/U 5" DPs Jt by Jt and RIH to 257m, While Pass Rabbit Thru. All Tubular and Circ. C.W.H; Conn. TDS, Flush & Circ. Thru. Strg for a while; POOH 5" OEDP & Rack Back all made up 5"Stds (Totally 10Stds) in derrick, While Circ. C.W.H, W/ 5-6BPH Loss. Prepare to P/U & M/U 8-3/8" Dir. Drlg, P/U 6-3/4" DHM (PDM, Lang Fang, S/N: 572151510-A, Rtr-Stat: 5-6, Stage: 6, Rev/Gal: 0.36, Bent sub: 1.2), Perform Shallow Test w/ 450gpm, got 320psi Diff. Pressure (M.L), Set DHM AKO to 1.22Deg. ; P/U & M/U 8-3/8" PDC Bit (Used, BESTE, Nozzle Size: 7*14/32", S/N: 220852, IADC: M1375, Dull Grade: 2-3-WT-A-X-I-NO-BHA) + 6-3/4" F.Sub + 6-3/4" UBHO + 6-3/4" NFMDC and MWD Tools, Perform Shallow Test w/ 450gpm, got 600-690psi Diff. Pressure (M.L); P/U & M/U Rest of BHA including 6Stds 5" HWDP + 6-1/2" Flex Jt + 6-1/2" Jar + 6Stds 5" HWDP and RIH to 305m, F/U BHA & Break Circ. , W/ 3-4BPH Loss.Cont. RIH w/ 8-3/8" Dir. Drlg BHA F/ 305 To 2260m Followed by 5"DPs On Elevator, While F/U String and Break Circ. Every 15Stds, and Perform DHM Functional Tests during RIH [Depth: 500m, F.R: 450gpm, SPP: 980psi ; Depth: 1500m, F.R: 450gpm, SPP: 1140-1180psi],W/ 3-4BPH Loss.

Cont. RIH W/ 8-3/8" Dir. Drlg BHA F/ 2260 To 2521m Followed by 5"DPs On Elevator, While F/U String and Break Circ. Every 10Stds, W/ 3-4BPH Loss.Hold Up Strg Wt. @

2521m; Conn. TDS & F/U Strg; Cont. RIH W/ 8-3/8" Dir. Drlg W/ Wash Dn F/ 2521 To 2575m, Pressure up & Hold Up Strg Wt. @ 2575m, Attempt to pass this point Sev. Times W/ Pump out, No Success, W/ 3-4BPH Loss.Cont. RIH W/ 8-3/8" Dir. Drlg BHA F/ 2575 To 2884m W/ Soft to Medium Wash & Ream Dn, W/ 2-3BPH Loss.Resume Dir. Drlg 8-3/8" Hole Section F/ 2884 to 2979.7m W/ Param [WOB:10-15klbf, F.R: 520gpm, SPP: 2100-2200psi, ROP: 1mph]. Pump 40 bbl Hi-Vis Pill, CBU @ 2979.7m till shakering out pumped Hi-Vis Pill, W/ 1-2BPH Loss. POOH 8-3/8" Dir. Drlg BHA F/ 2979.7 To 2870m On Elevator, Overpull encountered @ 2870m, While monitor the well & Circ. Thru. Trip Tank, W/ 1-2BPH Loss.Conn. TDS & Cont. POOH 8-3/8" Dir. Drlg BHA F/ 2870 To Surf. On Elevator.

L/D 8-3/8" Bit W/ Same Condition (D.G: 2-3-WT-A-X-I-NO-BHA) & BHA, While monitor the well & Circ. Thru. Trip Tank, W/ 1-2BPH Loss.P/U & M/U 6-3/4" DHM & 5"DP, Unable to B/O 6-3/4" DHM Stab. W/ Rig Tongs after multiple attempts; P/U & M/U Back up 6-3/4" DHM, Stab. still not released; Decided to change BHA at request of Hana Energy Co. Supervisor, While monitor the well & Circ. C.W.H, W/ 1-2BPH Loss.P/U 6-3/4" DHM (PDM, Lang Fang, S/N: ORT772160006-A, Rtr-Stat: 7-8, Stage: 6, Rev/Gal: 0.29, Bent sub: 1.5), Perform Shallow Test w/ 450gpm, got 400-480psi Diff. Pressure (M.L), Set DHM AKO to 1.5Deg. ; P/U & M/U 8-3/8" PDC Bit (Used, BESTE, Nozzle Size: 7*14/32", S/N: 220852, IADC: M1375, Dull Grade: 2-3-WT-A-X-I-NO-DMF) + 6-3/4" F.Sub + 8" Stabilizer + 6-3/4" UBHO + 6-3/4" NFMDC and MWD Tools, Perform Shallow Test w/ 490gpm, got 890-950psi Diff. Pressure (M.L); P/U & M/U Rest of BHA including 6Stds 5" HWDP + 6-1/2" Flex Jt + 6-1/2" Jar + 6Stds 5" HWDP and RIH to 307.2m, F/U BHA & Break Circ. , W/ 1-2BPH Loss.Cont. RIH w/ 8-3/8" Dir. Drlg BHA F/ 307.2 To 2620m Followed by 5"DPs On Elevator, While F/U String and Break Circ. at 15-Std intervals, and Perform DHM Functional Tests during RIH W/ 1-2BPH Loss.Hold Up Strg Wt. @ 2620m; Conn. TDS & F/U Strg; Cont. RIH W/ 8-3/8" Dir. Drlg W/ Wash Dn F/ 2620 To 2800m, Hold Up Strg Wt. @ 2800m, Attempt to pass this point W/ Pump out,No Success, W/ 1-2BPH Loss.Cont. RIH W/ 8-3/8" Dir. Drlg BHA F/ 2800 To 2874m W/ Soft Wash & Ream Dn, W/ 1-2BPH Loss.

Cont. RIH W/ 8-3/8" Dir. Drlg BHA F/ 2874 To 2979.6m W/ Soft Wash & Ream Dn, W/ 1-2BPH Loss.Tag BTM @ 2979.6m, Resume Dir. Drlg 8-3/8" Hole Section F/ 2979.6 to 3068.4m W/ Applying Params [WOB:20-25klbf, F.R: 500gpm, SPP: 2000-2200psi, ROP: 1.4mph], W/ 1-2BPH Loss.Take Survey Attempt to Cont. Dir. Drlg 8-3/8" Hole Section As Slide Mode @ 3068.4 W/ Applying Params [WOB:20-25klbf, F.R: 500gpm, SPP: 2000-2200psi], No Progress, W/ 1-2BPH Loss.Cont. Dir. Drlg 8-3/8" Hole Section F/ 3068.4 to 3304m W/ Applying Params [WOB: 10-15klbf, Rotation:

40RPM, TQ: 2-7klbf.ft, F.R: 510gpm, SPP: 2600-2750psi, ROP: 2.5mph], W/ 3-4BPH Loss.Pump 40bbl Hi-Vis Pill @ 3304m, CBU till Shakering out the pumped Hi-Vis Pill, W/ 3-4BPH Loss.

POOH 8-3/8" Dir. Drlg BHA F/ 3304 to 2670m W/ Pump out and Cont. POOH with Normal Trip to surface W/2-3BPH Loss.L/D 6-3/4" PDM (S/N: ORT772160006-A) & MWD-Gr Tools, 8-3/8" PDC Bit Best , Dull Grading: (3-5-BT-A-X-I-BU(5%)-BHA) 1 Hrs Waiting for OEOC Due to Change TDS Saver Sub W/2-3BPH Loss.P/U & Run in hole with 15 Jts 5" D.P "S" (Jts By Jts) and Flush it with Hi-Rate Circ mud, POOH & Rack Back on Derrick. Prepare to P/U & M/U 8-3/8" D.DRLG, P/U 6-3/4" PDM (Lang Fang, S/N: 772151489-1, Rtr-Stat: 7/8, Stage: 6, Rev/Gal: 0.29, Bent sub: 1.5).

Perform Shallow Test w/ F.Rate 450 GPM, Press: 250 psi (M.L), Set PDM AKO to 1.5Deg. ; P/U & M/U 8-3/8" PDC Bit (Used RR , BEST, Nozzle Size: 7*14/32") + 6-3/4" F.Sub + 8" S.Stablizer + 6-3/4" UBHO + 6-3/4" NMDC and MWD Tools, Make Aline, Perform Shallow Test w/ F.Rate 450 GPM, Press: 650psi (M.L). POH and L/D 8-3/8" PDC Bit (Used RR , BEST) and P/U & M/U 8-3/8" PDC Bit (New , BEST, Nozzle Size: 7*14/32", S/N: 220793, IADC: M1375ss). RIH with Same D.DRLG BHA Including : (8 STD 5" H.W.D.P + 6-1/2" Flex Jt + 6-1/2" Jar + 2 Stds 5" HWDP) & Follow by 5" D.Pipe to 3304m with Good Hole Condition and F/U String Every 15Stds & 2-3 BPH LossPerform PDM Functional Tests during RIH [Depth: 500m, F.R: 440gpm, SPP: 850psi , Depth: 1500m, F.R: 442gpm, SPP: 1150psi]Circulate mud while take survey.

Resume Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 3304m To 3594m. Pump Hi Vis Pill to Clean the Hole, POOH with Good Hole Condition to 3580m, Cont. POOH with Pump Out to 3480m & Continut Pull out of hole with Good Hole Condition To 249m While Monitor the Well, W/ 2-4 BPH Loss.

Cont POOH to Surface & L/D 6-3/4" PDM (Lang Fang, S/N: 772151489-1, Rtr-Stat: 7/8, Stage: 6, Rev/Gal: 0.29, Bent sub: 1.5), 6-3/4" F.Sub + 8" S.Stablizer + 6-3/4" UBHO + 6-3/4" NMDC and MWD Tools & 8-3/8" PDC Bit (BEST, Nozzle Size: 7*14/32", S/N: 220793, IADC: M1375ss)(Bit Dull Condition: 1.1.WT.A.X.I.NO.BHA)Perform BOP Test as NIOC Policy, Retrieve Wear Bushing, Set Plug Tester, Perform BOP Test as follow:5k 13-5/8" Annular w/ 3500psi, 15min, Ok, 10k 13-5/8" Top Ram (VBR 2-7/8" - 5") w/ 7500psi, 15min, Ok, 10k 13-5/8" BTM Ram 5" Pipe Ramw/ 7500psi, 15min, Ok, 10k 13-5/8" Shear Ram w/ 7500psi, While Press. Test All Choke Manifold Valves & Accumulator Unit Functionality,Ok, Retrieve Plug Tester, Install

Wear Bushing.Perform Shallow Test w/ F.Rate 450 GPM, Press: 400 psi (M.L), Set PDM AKO to 1.22Deg. P/U & M/U 8-3/8" PDC Bit No#7 (Used RR , BEST, P/U & M/U 8-3/8" D.DRLG, P/U 6-3/4" PDM (Lang Fang, S/N: 772160803, Rtr-Stat: 7/8, Stage: 6, Rev/Gal: 0.29, Bent sub: 1.22),Nozzle Size: 7*14/32", S/N : 220793) + 6-3/4" F.Sub + 6-3/4" UBHO + 6-3/4" NMDC and MWD Tools (Change Battery), Make Aline, Perform Shallow Test w/ F.Rate 450 GPM, Press: 840psi (M.L). Cont. RIH with Same D.DRLG BHA Including: (8 STD 5" H.W.D.P + 6-1/2" Flex Jt + 6-1/2" Jar + 2 Stds 5" HWDP) & Follow by 5" D.Pipe to 3443m with Good hole Condition While F/U String and Break Circ. Every 15Stds.

Continue Run in hole to 3594m (Tag BTM), with Good hole Condition While F/U String and Break Circ. Every 15Stds. Pump Hi-Vis pillWith Take Survey.Cont. Directional Drilling 8-3/8" Hole Section As Rotating Mode F/ 3594m To 3675 m while take survey.While Monitor the Well, W/ 2-4 BPH Loss.

Cont. Directional Drilling 8-3/8" Hole Section F/ 3675m To 3692 m while take survey.With Monitor the Well, W/ 2-4 BPH Loss.Rotating Mode DRLG Parameter: WOB: 3-10Klb, Rot: M + 40rpm, SPP: 2450-2650 Psi, F.Rate: 480-500GPM, TQ: 5-10klb.ft, ROP: 4-5 MPH Stop Drilling & Circ BTm's Up as Requested by Geologist to get sample to Confirm LNR Point.Pull out of hole to 3299m (Top of Kazhdumi formation) With tight spot @ several point (3638, 3639, 3594 m)Run in hole with wash & ream to 3692m (BTM).Circ Mud to clean the hole, Spot 90 BBL Hi.Vis Pill.POOH on Elevator from 3692m (BTM) to 1954m W/ 2-4 BPH Loss.

Cont POOH from 1954m to Surface & L/D 6-3/4" PDM (Lang Fang, S/N: 772160803, Rtr-Stat: 7/8, Stage: 6, Rev/Gal: 0.29, Bent sub: 1.22) +8-3/8" PDC Bit No#7 (Used RR , BEST, Nozzle Size: 7*14/32", S/N : 220793) Dull Grading: (1.1.WT.A.X.I.NO.TD) + 6-3/4" F.Sub + 6-3/4" UBHO + 6-3/4" NMDC and MWD-Gr Tools While Obs. Well on BHA W/ 3-4 BPH Loss.Slip & Cut 100Ft DRLG Line.

R/U Casing Running Tools While Change Top Ram's To 4-1/2" * 7" Var. Held PJSM with all crew. P/U & Run in hole with 7" LNR As Below :7" F.Shoe (29#,TPCQ, L-80,PPA) + 2 jts 7" Liner (29#, TPCQ,L-80) + 7" F. Collar (29#,TPCQ, L-80,PPA) + 1 jts 7" Liner (29#, TPCQ,L-80) + 7" LDC (29#,TPCQ, L-80,PPA) + 1 jts 7" Liner (29#, TPCQ,L-80) & Function Test F.Shoe & F.Collar, Use Thread Lock Compound in Shoe Track Connections and Break Circ. Thru. Shoe Track, Ok. Cont. Run 7" LNR (29#, TPCQ,L-80) to 1056m (Totally : 94 Jts) & Install Spirolizer and fill up string According Program W/2-3BPH Loss.

Cont. Run 7" LNR (29#, TPCQ,L-80) to 1518m (Totally : 135 Jts) & Install Spirolizer and fill up string According Program W/2-3BPH Loss.P/U & M/U 7" LNR R.HGR assembly with top PKR (29#, L80, TPCQ, PPA), LWP is shear pinned to the bottom of running tools,Check setting tools and all connection. record up and down string weight. R/D LNR running equipment (OEOC Co.). Follow by 5" Drill pipe to 3692m (Tag Bottom, Picked up off Bottom).Drop Ball, Pumping Until it Land on the Seat in the LDC, Set the Hanger as per Setting Procedure (1800psi), Cont. Pump to the Setting Ball Was Blown out by Increase Pressure (2700psi) to Shear the Pin in the Seat. Circulation was Reestablished.Liner Setting Tool Release By Rotating the String to the Right 26 Turns Right Hand, Sting out 1m W/ 2-3 BPH Loss.R/U Cement Line.PJSM Held With Key Personnel, Test CMT line W/3000Psi, OK. PUMP 20bbls Chemical Wash (62.4 Pcf), Pump 50bbl as Spacer Wash (85Pcf) By Rig Pump, Pump 86bbl Lead Slurry CMT (98Pcf), PUMP 74bbl Tail Slurry CMT (118Pcf), Release PDP, Disp. Cement with 306 BBL Mud (Obs. Shear off Wiper plug after Pump 124bbl Mud and Obs. Bump Plug W/2000Psi, Perform Integrity Test ,Ok).Bleed of Pressure, Check Back Flow, Ok. Sting Out and Set Packer, Ok. 8 bbl Loss During Cement Job. .

Start POOH 10 STD Flush The String, Cont. POOH 8 STD, C.B.U. Cont. POOH to Surface & L/D LNR Running tools.P/U & M/U 8-3/8" Used TCI Bit (RR, 537, 3*16/32, Kingdream, S/N: 2417584JH) + Bit sub 6 1/2" + 7 STD'S 5" H.W.D.P & Follow by 5" D.POn Elevator 1816m.Circ. BTM's UP.Cont. Run in hole with Wash down from 1816m to 2134m, Tag TOC.Start D/O Med To Hard CMT F/ 2134 To 2167.5m (New 7" L.Lap).Circ. BTM's UP.

Start POOH 10 STD Flush The String, Cont. POOH 8 STD, C.B.U. Cont. POOH to Surface & L/D LNR Running tools.P/U & M/U 8-3/8" Used TCI Bit (RR, 537, 3*16/32, Kingdream, S/N: 2417584JH) + Bit sub 6 1/2" + 7 STD'S 5" H.W.D.P & Follow by 5" D.POn Elevator 1816m.Circ. BTM's UP.Cont. Run in hole with Wash down from 1816m to 2134m, Tag TOC.Start D/O Med To Hard CMT F/ 2134 To 2167.5m (New 7" L.Lap).Circ. BTM's UP.

Dry Test Operation Summary:

P/U & M/U 9-5/8"Dry Test Tool String including: Bottom B.T (First Memory Gauge) + Anchor pipe + X.O.S 4-1/2" IF Box x 3 1/2" FH Pin +Middle Packer element + 9-5/8" Above Packer + X.O.S 3-1/2" IF Box *4-1/2" IF PIN + X.O.S 3-1/2" FH Box *3-1/2" IF PIN + RH Release Safety Joint + Hydraulic JAR + Middle B.T (Second Memory Gauge) + Hydro-spring + D.C.I.P + X.O.S 4-1/2" IF Box x 3-1/2" IF Pin + 1 Jt 5" Drill

Pipe + Reverse Sub and RIH to 23m, While Monitor the Well, W/ NL-NG.Cont. RIH W/ 9-5/8"Dry Test Tool String F/ 23 To 2142m On Elevator Followed by 7 Stds 5" HWDP & 5"DPs W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 886m of Strg W/ Drill water (62.4 pcf) as a Water Cushion at 5-Std intervals, W/ NL-NG.Prepare Rig Floor, Change TDS Links & Perform Dry Test Op. as follows:R/U and prepare Chicksan pipes and DST choke manifold, Pressure test lines to 3000 psi for 15 minutes, test confirmed OK, Record Strg Wt. in both upward and downward directions.Setting PKR and Opening Hydro-Spring Valve: Rotate Strg 6 full turns clockwise, Apply set-down Wt. to set the 9-5/8" Dry Test PKR at 2138m, Obs. Hydro-Spring Valve opening indication on M/D; Well opened Thru. Hydro-Spring Valve.Open Period Monitoring: Log start time of Opened period (23:05), Maintain open condition and monitor for any bubbles at the surface is in progress at M.N for ongoing monitoring, Bubbles observed; Confirm Annulus fluid level is Static during observation.

Cont. Open Period Monitoring and maintain for totally 1.5 Hrs. , While monitor for any bubbles at the surface, Bubbles observed; Confirm Annulus fluid level is Static during observation; Decide to Start Close Period Monitoring.Close Period Monitoring: S/O Strg Weight, Rotate Strg clockwise to close the DCIP Dry Test Assy. Valve to Close the Well, Log start time of Closed period (00:45a.m) and monitor for 6 Hrs. ,Confirm Annulus fluid level is Static during observation.Open Circulation Valve: Drop Bar to open Circ. valve, Establish Reverse Circulation, confirm balance mud is observed at the surface and the water cushion is the same as the F/U Volume; Unset the 9-5/8" Dry Test PKR using normal P/U Weight, B/O & L/D Dry Test Surface Equipment, W/ NL-NG.CBU and Flow Check @ 2142m, Well Static, W/ NL-NG.POOH 9-5/8" Dry Test Tool String F/ 2142m To Surface On Elevator W/ Speed Control at the request of OEOC Dry Test supervisor, B/O & L/D BHA & Dry Test Tool String; Read Middle & BTM B.T, 1.5Hrs. Open-Period Monitoring Results: [Middle B.T: 1455 - 2336psi, BTM B.T: 1480-2350psi], 6Hrs. Close-Period Monitoring Results: [Middle B.T: 2336 - 3352psi, BTM B.T: 2350-3370psi]; Check Sample Properties of flowing sample between DCIP & Hydrospring [MW: 71pcf, PH: 6.8 , Cl: 130000, Ca+: 4800], While Circ. C.W.H, W/ NL-NG.

P/U & M/U 6-1/8" D/O BHA including: [6-1/8" Tri-Cone Bit (K.Dream, IADC: 537, S/N: 2304674JH, Used, D.G: 2-2-WT-A-E-I-BT-DTF, Open, Cum. Drilled: 58m CMT D/O +10m Formation, Cum. Hrs on BTM: 31.5) + 4-3/4" Bit sub (float-in) + 9Stds 3-1/2" HWDP] and RIH to 249.5m,F/U BHA & Break Circ. , NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 249.5 To 2167m On Elevator Followed by 3-1/2" & 5" DPs, While

F/U Strg & Break Circ. at 15-Std intervals, NL-NG; Obs. Leakage on TDS Drlg Fluid Hose @ 2167m, POOH 6-1/8" D/O BHA To 2152m.Stop RIH Op. & Change TDS Drlg Fluid Hose, While Monitor the Well & Slow Circ. Thru. Strg @ 2152m, NL-NG.Resume RIH W/ 6-1/8" D/O BHA F/ 2152 To 2171m W/ Wash & Ream Dn, Held up Strg Wt. & Tag Pack of Bushing @ 2171m; D/O P.O.B W/ Applying Parameters: [WOB: 1-7klbf, Rot. : 40 RPM, TQ: 1-2klbf.ft, F.R: 260gpm, SPP: 1350psi] & Dress its interval Sev. Times, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 2171.5 To 2730m On Elevator Followed by 5" DPs, While F/U Strg & Break Hi-Rate Circ. at 10-Std intervals,NL-NG; Obs. Negligible Drag @ 2730m.Cont. RIH W/ 6-1/8" D/O BHA F/ 2730 To 2852m W/ Soft Wash & Ream Dn W/ Applying Parameters: [WOB: 0.5-1klbf, Rot. : 30-40RPM,TQ: 1-2klbf.ft, F.R: 280gpm, SPP: 1500-1550psi], NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 2852 To 3020m On Elevator Followed by 5" DPs, While F/U Strg & Break Hi-Rate Circ. at 6-Std intervals for a while, NL-NG.

Cont. RIH W/ 6-1/8" D/O BHA F/ 3020 To 3563m On Elevator Followed by 5" DPs, While F/U Strg & Break Hi-Rate Circ. at 6-Std intervals for a while, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3563 To 3617m W/ Soft Wash & Ream Dn W/ Applying Parameters: [WOB: 0.5-1klbf, Rot. : 30-40RPM,TQ: 1-2klbf.ft, F.R: 280gpm, SPP: 1500-1550psi], NL-NG.D/O Soft to Medium CMT W/ 6-1/8" D/O BHA F/ 3617 To 3656m W/ Applying Parameters: [WOB: 5-20klbf, Rot. : 30-50RPM, TQ: 1-5klbf.ft,F.R: 340gpm, SPP: 2500-2570psi], While pump Hi-Vis Pill & Reciprocate Strg before each connection, NL-NG.Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3656 To 3658.7m W/ Applying Parameters: [WOB: 6-24klbf, Rot. : 30-50RPM, TQ: 2-6klbf.ft, F.R: 340gpm, SPP: 2500-2570psi], While D/O LDC, Pump Down Plug, and Wiper Plug @ 3657m, Dress & Smooth LDC, Pump Down Plug, and Wiper Plug position Sev. Times, pump Hi-Vis Pill ,and Reciprocate Strg periodically, NL-NG.

Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3658.7 To 3672m W/ Applying Parameters: [WOB: 10-15klbf, Rot. : 30-50RPM, TQ: 2-6klbf.ft, F.R: 340gpm, SPP: 2500-2570psi], While D/O F.Collar @ 3668m, Dress & Smooth F.Collar position Sev. Times, pump Hi-Vis Pill ,and Reciprocate Strg periodically, NL-NG.Pump 30bbl Hi-Vis Pill, CBU @ 3672m till Shakering out Hi-Vis Pill, NL-NG.POOH 6-1/8" D/O BHA F/ 3672 To 2150m On Elevator, While Perform Positive Test Monitor the well and Circ. C.W.H, NL-NG.Conduct 7" L.Lap Positive Pressure Test at 2150m by gradually applying 1500psi, while pumping 2.5 bbl of mud; Maintain Stable Pressure W/ No Drop Observed, and Confirm Full Return of Pumped Mud upon Pressure Release.Cont. POOH 6-1/8" D/O BHA F/ 2150 To 1230m On Elevator, While Perform Positive Test Monitor the well and Circ. C.W.H, NL-NG.Due to Windy weather, Stop POOH Op. @ 1230m,

While Slow Circ. Thru. Strg, NL-NG.Cont. POOH 6-1/8" D/O BHA F/ 1230m To Surface On Elevator, L/D BHA & 6-1/8" Tri-cone Bit W/ Same Dull Grade (2-2-WT-A-E-I-BT-BHA), While Monitor the well and Circ. C.W.H, NL-NG.Retrieve Wear Bushing, Change Top Rams Form 4-1/2" × 7" VBR To 2-7/8" × 5" VBR is in progress @ M.N, While Monitor the well and Circ. C.W.H, NL-NG.

Cont. Change Top Rams Form 4-1/2" × 7" VBR To 2-7/8" × 5" VBR, Set Plug Tester, Press. Test the Same W/ 7500psi,15min, Ok,Retrieve Plug Tester; Prepare Rig Floor to RIH W/ 9-5/8" ×7" Tandem Scraper BHA, While Monitor the well and Circ. C.W.H, NL-NG.P/U & M/U 9-5/8" ×7" Tandem Scraper BHA including: [6-1/8" Tri-Cone Bit (K.Dream, IADC: 537, S/N: 2304674JH, Used, Open,Dull Grade: 2-2-WT-A-E-I-BT-BHA, Cum. Drilled: 114.3m CMT D/O +10m Formation, Cum. Hrs on BTM: 55) + 7" Scraper + 4-3/4" Bit sub (float-in) + 9Stds 3-1/2" HWDP] and RIH to 250.5m, F/U BHA & Break Circ. , NL-NG.Cont. RIH W/ 9-5/8" ×7" Tandem Scraper BHA F/ 250.5 To 2276m On Elevator Followed by 43 Stds + 1 Jt 3-1/2" DPs + X.O.S +9-5/8" Scraper and 5"DPs, While F/U Strg & Break Circ. At 15-Std intervals, NL-NG.Due to Windy weather, Stop RIH Op. @ 2276m at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg, NL-NG.Cont. RIH W/ 9-5/8" ×7" Tandem Scraper BHA F/ 2276 To 3612m On Elevator Followed by 5" DPs, While F/U Strg & Break Circ. At 15-Std intervals, NL-NG.Conn. TDS & Cont. RIH W/ 9-5/8" ×7" Tandem Scraper BHA F/ 3612 To 3671m W/ Wash Dn, Tag 7" L.Lap W/ 9-5/8" Scraper, NL-NG.

Conduct Multiple Scraping Passes On 7" S.N PKR Setting Interval; Achieve Full ID Contact W/ Scraper Blades, NL/NG.Pump 40bbl Hi-Vis Pill, CBU; Shakering out Pumped Hi-Vis Pill confirmed; Static Flow check for 30min, Well Static, NL-NG.POOH 9-5/8" ×7" Tandem Scraper BHA F/ 3671 To 1532m On Elevator, While Circ. C.W.H, NL-NG.Due to Windy weather, Stop POOH Op. @ 1532m at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg, NL-NG.Cont. POOH 9-5/8" ×7" Tandem Scraper BHA F/ 1532 To 893m On Elevator, While Circ. C.W.H, NL-NG.Due to Windy weather, Stop POOH Op. @ 893m at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg, NL-NG.Cont. POOH 9-5/8" ×7" Tandem Scraper BHA F/ 893m To Surface On Elevator, L/D BHA & Bit W/ Same Condition, While F/U the Well & Circ. C.W.H, NL-NG.Prepare Rig Floor to perform Wire Line Logging Op. as Plan; Change 13-5/8" 10K Top Rams F/ 2-7/8" × 5" VBR To 4-1/2" × 7" VBR;Pressure Test on Changed Rams, OK; L/D Mousehole & R/U and Set 7" Shooting Nipple; P/U & Make Up Wireline BOP on Shooting Nipple, Perform Wireline BOP Test, OK; PJSM Conducted; R/U Surface Wireline Tools, P/U & Ass. Wireline Logging Tool Stringas SBT-VDL-GR-CCL (Total Length: 16.42m, Total Weight: 364 kg, Max OD: 89mm)

For Cement Bond Evaluation of 7" LNR, While Circ. C.W.H, NL-NG.Start RIH W/ Same Wireline Logging Tool String F/ Surface To 2050m, While Record Normal Tension Every 500m, While Monitorthe Well, NL-NG.

Cont. RIH W/ Wireline Logging Tool String F/ 2050 To 3670m, While Record Normal Tension Every 500m.Commence Data Acquisition Logging Up F/ 3670 To 2160m to Fully Cover Logging Interval; Logging Up in Interval 2550 To 2450m was repeated based on Client's Request for Verification; L/D Wireline Logging Tool String and Surface Eqp.Prepare Rig Floor to P/U & M/U 6-1/8" D/O BHA; Change 13-5/8" 10K Top Rams F/ 4-1/2" × 7" VBR To 2-7/8" × 5" VBR;Pressure Test on Changed Rams, OK; Install Wear Bushing; R/U Mousehole, While Circ. C.W.H, NL-NG.P/U & M/U 6-1/8" D/O BHA including: [6-1/8" Tri-Cone Bit (K.Dream, IADC: 537, S/N: 2304674JH, Used, D.G: 2-2-WT-A-E-I-BT-BHA, Open, 114.3m CMT D/O +10m Formation, Cum. Hrs on BTM: 55) + 4-3/4" Bit sub (float-in) + 9Stds 3-1/2" HWDP] and RIH to 249.5m,F/U BHA & Break Circ. , NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 249.5 To 3652m On Elevator Followed by 3-1/2" & 5" DPs, While M/U Additional 3-1/2" DPs required for Drlg6-1/8" Hole Section Jt by Jt, and F/U Strg & Break Circ. at 10-Std intervals, NL-NG.Conn. TDS & Cont. RIH W/ 6-1/8" D/O BHA F/ 3652 To 3660m W/ Wash Dn, NL-NG.

Cont. RIH W/ 6-1/8" D/O BHA F/ 3660 To 3672m W/ Wash Dn, Tag BTM @ 3672m, NL-NG.D/O Medium to Hard CMT W/ 6-1/8" D/O BHA F/ 3672 To 3692m W/ Applying Parameters: [WOB: 6-25klbf, Rot. : 40-50RPM, TQ: 2-6klbf.ft, F.R: 50-300gpm, SPP: 210-2350psi], While D/O F.Shoe @ 3791.5, Dress & Smooth F.Shoe position Sev. Times, pump Hi-Vis Pill Periodically, NL-NG.Pump 40bbl Hi-Vis Pill & CBU @ 3693m, While optimize Drilling Fluid Parameters & Increase MW F/ 76 To 78pcf, NL-NG.Commence Drilling 6-1/8" Hole Section W/ 6-1/8" D/O BHA F/ 3692 To 3697m W/ Applying Parameters: [WOB: 15-20klbf, Rot. : 40-60RPM, TQ: 2-5klbf.ft, F.R: 200-300gpm, SPP: 2100-2350psi], NL-NG.Pump 40bbl Hi-Vis Pill & CBU @ 3697m till Shakering out the pumped Hi-Vis Pill; Static Flow Check @ 3697m, Well Static, NL-NG.POOH 6-1/8" D/O BHA F/ 3697 To 2095m On Elevator, While Monitor the well and Circ. C.W.H, NL-NGSlip & Cut 100ft of Drlg Line, While Slow Circ. Thru. Strg & Monitor the Well, NL-NG.Cont. POOH 6-1/8" D/O BHA F/ 2095 To 1663m On Elevator, While Monitor the well and Circ. C.W.H, NL-NG

Cont. POOH 6-1/8" D/O BHA F/ 1663m To Surface On Elevator, L/D 6-1/8" Tri-Cone Bit (2-3-WT-A-E-I-BT-BHA) and rest of BHA, While Monitor The Well and Circ. C.W.H, NL-NGPrepare Rig Floor to P/U & M/U 6-1/8" Dir. Drlg BHA; P/U 4-3/4"

DHM (PDM, Lang Fang, S/N: 120140608, Rtr-Stat: 5-6, Stage: 6, Rev/Gal: 0.8, Bent sub: 1.5m), Perform Shallow Test w/ 250gpm, got 700psi (M.L), Set DHM AKO to 1.5Deg;P/U & M/U 6-1/8" PDC Bit (Used, BEST, S/N: 255421, IADC: M1665, Nozzle Size: 3*22/32" NZL Port, Dull Grade: 1-1-WT-A-X-I-NO-TD, TFA: 1.1") + 5-7/8" String Stab. + 4-3/4" F.Sub + 4-3/4" MWD Sub + 4-3/4" NMDC and MWD Tool; Perform Shallow Test w/ 250gpm, got 1000-1150psi Diff. Pressure (M.L); P/U & M/U Rest of BHA including 8Stds 3-1/2" HWDP + D.Pin + 4-3/4" Jar + 1Stds 3-1/2" HWDP and RIH to 274m, F/U BHA & Break Circ. , NL-NG.Cont. RIH w/ 6-1/8" Dir. Drlg BHA F/ 274 To 3665m Followed by 3-1/2" & 5"DPs On Elevator, While F/U String and Break Circ. at 15-Std intervals, and Perform DHM Functional Tests during RIH [Depth: 500m, F.R: 200gpm, SPP: 1030-1140psi; Depth: 1500m, F.R: 200gpm, SPP: 1400-1480psi; Depth: 3000m, F.R: 200gpm, SPP: 1850-1940psi], NL-NG.

Conn. TDS & F/U Strg; Cont. RIH W/ 6-1/8" Dir. Drlg W/ Wash Dn F/ 3665 To 3697m, Hold Up Strg Wt. @ 3697m, NL-NG.Attempt to Cont. Dri. Drlg 6-1/8" Hole Section as Slide Mode, No Success; Cont. Dir. Drlg 6-1/8" Hole Section As Rotating Mode F/ 3697 to 3699m W/ Applying Params [WOB: 5-6klbf, Rotation: 40RPM,TQ: 3-5klbf.ft, F.R: 220gpm, SPP: 2150-2250psi, ROP: 4mph], NL-NG.Cont. Dir. Drlg 6-1/8" Hole Section F/ 3699 to 3760m W/ Applying Params [WOB: 6-8klbf, Rotation: 40RPM,TQ: 3-5klbf.ft, F.R: 200gpm, 1950-2100psi, ROP: 4mph], While Take Survey, NL-NG.A 350 psi pressure rise occurred; POOH to 3,723 m; Pipe screen and surface lines inspected & found intact; Troubleshooting continued W/ No MWD signal observed;Decided to POOH the 6-1/8" Dir. Drlg BHA To Surf. for inspection of the Strg and BHA, NL-NG.POOH 6-1/8" Dir. Drlg BHA F/ 3723To 705m On Elevator, While Monitor the Well & Circ. C.W.H, NL-NG.Due To Windy Weather, Stop POOH Op. @ 705m at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg & Monitor the Well, NL-NG.Cont. POOH 6-1/8" Dir. Drlg BHA F/ 705m To Surface On Elevator, L/D 6-1/8" PDC Bit & Rest of BHA is in progress, While Monitor the Well & Circ. C.W.H, NL-NG.

Cont. L/D 6-1/8" PDC Bit & Rest of BHA; Conduct Shallow Test W/ 250gpm, Got SPP: 720psi (M.L); Obs. Damage to the pulser poppet valve; While Circ. C.W.H, NL-NG.Perform BOP Test as NIOC Policy, Retrieve Wear Bushing, Set Plug Tester, Perform BOP Test as follow:5k 13-5/8" Annular w/ 3500psi, 15min, Ok, 10k 13-5/8" Top Ram (VBR 2-7/8" - 5") w/ 7500psi, 15min, Ok, 10k 13-5/8" BTM Ram 5" Pipe Ramw/ 7500psi, 15min, Ok, 10k 13-5/8" Shear Ram w/ 7500psi, While Press. Test All Choke Manifold Valves & Accumulator Unit Functionality,Ok, Retrieve Plug Tester, Install Wear Bushing.Prepare Rig Floor to P/U & M/U 6-1/8" Dir. Drlg BHA; P/U 4-

3/4" DHM (PDM, Lang Fang, S/N: 120140608, Rtr-Stat: 5-6, Stage: 6, Rev/Gal: 0.8, Bent sub: 1.5m) Set DHM AKO to 1.22Deg; M/U 6-1/8" PDC Bit (Used, BEST, S/N: 255421, IADC: M1665, Nozzle Size: 3*22/32" NZL Port, Dull Grade: 1-1-WT-A-X-I-NO-TD, TFA: 1.1") + 4-3/4" F.Sub + 4-3/4" MWD Sub + 4-3/4" NMDC and MWD Tool; Perform Shallow Test w/ 250gpm, got 970-1080psi Diff. Pressure (M.L); P/U & M/U Rest of BHA including 8Stds 3-1/2" HWDP + D.Pin + 4-3/4" Jar + 1Stds 3-1/2" HWDP and RIH To 272m, F/U BHA & Break Circ. ,NL-NGCont. RIH w/ 6-1/8" Dir. Drlg BHA F/ 272 To 1513.6m Followed by 3-1/2" DPs On Elevator, While F/U String and Break Circ. at 15-Std intervals, and Perform DHM Functional Tests during RIH [Depth: 500m, F.R: 200gpm, SPP: 1050-1120psi; Depth: 1500m, F.R: 200gpm, SPP: 1400-1480psi], NL-NG.Due To Windy Weather,Stop RIH Op. @ 1513.6m at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg & Monitor the Well, NL-NG.Cont. RIH w/ 6-1/8" Dir. Drlg BHA F/ 1513.6 To 3658m Followed by 3-1/2" & 5" DPs On Elevator, While F/U String and Break Circ. at 15-Std intervals, and Perform DHM Functional Tests during RIH [Depth: 3000m, F.R: 200gpm, SPP: 1690-1770psi], NL-NG.

RIH W/ 6-1/8" Dir. Drlg BHA F/ 3695 To 3760m Followed by 5" DPs W/ Soft Wash & Ream Dn, Tag BTM @ 3760m, NL-NG.Resume Dir. Drlg 6-1/8" Hole Section As Rotating Mode F/ 3760 to 3771.4m W/ Applying Params [WOB: 6-8klbf, Rotation: 40RPM, TQ: 3-5klbf.ft, F.R: 200gpm, SPP: 1850-2050psi, ROP: 4mph], While take Survey, Reciprocate the drilled Std & M/U Next Std, Pump Hi-Vis Pill, NL-NG.Cont. Dir. Drlg 6-1/8" Hole Section F/ 3771.4 to 3888m (TD) W/ Applying Params [WOB: 3-5klbf, Rotation: 40RPM, TQ: 3-6klbf.ft, F.R: 200gpm, SPP: 1900-2150psi, ROP: 4-5mph], NL-NG.Circ BTM'S Up Till Clean the hole.

POOH with B.Ream & Pump on to 3692m (7" Shoe) with normal Hole Condition, Run in hole without RRM & GPM to 3888m withNormal hole Condition.POOH from 3888m to 3692m (7" Shoe), OBS. The well with 5BPH Gain, Obs. Dec. Mw To 74pcf, Close The Well, Press. Zero, Circ. Mud Throu Ch.Manifold To Balance MW to 78PCF, Flow Check, "Static".

RIH to 3888m (BTM) While Wash & Ream (3792-3794, 3814-3817, 3881-3886).Inc. MW to 80pcf & Work on Mud Rheology.POOH to 3857 While Ream & Back Ream Several times Interval Depth: 3888- 3881m, Cont. POOH To 3847m, String Stuck.Work on Stuck with Downward and Apply max. 100klb weight Finally String got free.Cont. Back Ream to 3692m (7" shoe), Flow Check the well, "Static".

RIH w/ Wash & Ream to 3888m. With normal hole condition.Inc. MW to 81pcf, Spot 50BBL Hi.Vis Pill.Pull out of hole for Checking hole condition W/ Pump on & B.Ream From 3888m to 3684m. While Flow check @ 3692m (7"Shoe) "Static"Cont POOH on Elevator from 3684m to 2433m.Run in hole for Checking hole condition on Elevator From 2430m to 3692m (7" Shoe). W/NL.NG.Cont Run in hole with Wash Dn & Ream to 3888m (BTM), Check Hole Condition as below While Inc. Mw to 82 PCF.

Cont Run in hole for Checking hole condition W/ Wash Dn From 3713m to 3796m W/Max 5Klb Drag.Cont Run in hole for Checking hole condition W/ Wash Dn & Ream From 3796m to 3870m W/Max 10-20Klb Drag after Wash & Ream CheckInterval Several Time. Obs. Change Mud Properties (Ca++ 2700, F.L : 4) while Inc. Mw to 83 PCF Work on Mud Rheology.Cont RIH from 3870m to 3888m (BTM) W/Max 20-30Klb Drag. Pumping 30BBL Hi.Vis Pill.POOH from 3888m to 3800m with B.Ream & Cont POOH from 3800m to 3750m with Pumping & Cont POOH on Elevator from 3750m To 1398m and Flow Check the well @ 3692m (7" Shoe) " Static " .1 HRS Waiting For OEOC 201 Rig Due to Delay in POOH Operation.

Cont POOH on Elevator from 1398m To 1150m & Run in Hole with 15 Jts 3-1/2" D.P and Make Stand in Derrick, Cont POOH to Surface &L/D 6-1/8" Dir. Drlg BHA (4-3/4" PDM, Lang Fang, S/N: 120140608) + 6-1/8" PDC Bit (Used, BEST, S/N: 255421, IADC: M1665, Nozzle Size: 3*22/32", Dull Grade: 1-2-BT-T-X-I-WT-BHA) + 4-3/4" F.Sub + 4-3/4" MWD Sub + 4-3/4" NMDC and MWD Tool + 4-3/4" D.Jar.P/U & M/U BHA including 6-1/8" Tci.cone Bit (Used, K.Dream, S/N: 2304674JH, IADC: 537, Nozzle: Open) + 4-3/4 B.Sub + 1 STD 4-3/4" D.C +8 Stds 3-1/2" HWDP + D.Pin + 4-3/4" D.Jar + 1 Stds 3-1/2" HWDP & Follow by 3-1/2" D.Pipe to 1870m. Cont RIH by 5" D.Pipe to 3665m &Cont RIH With Wash Dn to 3723m, Continue Run in hole on Elevator from 3723m to 3752m W/NL.NG .

Cont RIH With Normal Trip to 3888m W/ Max 1-3 Klb Drag. Circ Mud To Clean the holeAttemp To POOH from 3888m, Obs. Max. 30klb Overpull, Apply Pumping , POOH to 3810 With Pumping, Cont POOH on Elevator from 3810m to 3692m.Run in hole with Normal Trip from 3692m to 3888m.Circ Btm's up while Inc Mw to 84 PCF & work on mud Rheology.POOH from 3887m to 3838m.Run in hole again to 3888m.Pull out of hole on Elevator from 3888m to 3800m.Run in hole again to 3888m, Spot 50 BBL Hi-Vis Pill.POOH on Elevator to 1466m W/ NL.NG.

Cont POOH on Elevator to Surface & L/D 6-1/8" Tci.cone Bit (Used, K.Dream, S/N: 2304674JH, IADC: 537, Nozzle: Open, Bit Dull Condition : 2.2.WT.A.E.I.BT.LOG) +

4-3/4" D.Jar. Retrive Wear Bushing.Prepare & RIH with Full Suite Logging Tools (SEALAND Co.) on 3-1/2" D.Pipe to 60 m White pass Rabit thru all tubular .Stop Operation due to bad Weather .Cont RIH with Full Suite Logging Tools (SEALAND Co.) on 3-1/2" D.Pipe to 1045 m White pass Rabit thru all tubular & Fill Up string every10 Stand's W/NL.NG.

Cont RIH with Full Suite Logging Tools (SEALAND Co.) on 3-1/2" & 5" D.Pipe to 3450m White pass Rabit thru all tubular & Fill Up string every 10 Stand's W/NL.NG.Circ. Mud 1.5 Cap String Vol. R/U Shaves, Install C.S.E.S On DP, Run Wirline Logging in String W/PWCH to 50 Above Latch Point, Circ. Mud W/ Max.Apply 1000psi in String, Cont. Run PWCH & Connected to Latch Point, Ok.Cont. RIH W/5" DP & Wireline Logging on String While Take Log Down to 3788m,Wait on client Due to Stop Operation By Clinet order To secure and suspend the well. POOH to 3450m, Disconnected C.S.E.S &R/D Shaves .*Logging BHA*Total Length: 36.899m, Max. Outside: 5-1/8", HRDA-Sonic Sonde, HRDA- Sonic Cartridge, DLL- Resistivity Sonde, DLL- Resistivity Cartridge LDS- Density Sonde, NDES- Neutron Density Cartridge, CNL- Neutron Sonde, NGS- Gamma, HDT - Telemetry, TTRM

Wait on client Due to Stop Operation By Clinet order To secure and suspend the well. Cont POOH with Full Suite Logging Tools (SEALAND Co.) To surface & L/D Full Suite Logging Tools.1730m For CMT Plug .Slip & Cut 102FT DRLG Line.Wait on client Due to Stop Operation By Clinet order To secure and suspend the well and P/U & RIH with 3-1/2" & 5" D.Pipe OEDP to *Logging BHA*Total Length: 36.899m, Max. Outside: 5-1/8", HRDA-Sonic Sonde, HRDA- Sonic Cartridge, DLL- Resistivity Sonde, DLL- Resistivity Cartridge LDS- Density Sonde, NDES- Neutron Density Cartridge, CNL- Neutron Sonde, NGS- Gamma, HDT - Telemetry, TTRM

Wait on client Due to Stop Operation By Clinet order To secure and suspend the well and P/U & RIH with 3-1/2" & 5" D.Pipe OEDP to 3299m For CMT Plug, Circ mud Till R.T.Additives and preparing mixing fluidsaccording to Program. Start to pumping 3.5 bbl (75 pcf) Ahead spacer.Wait on Recived Pump Truck OEOC.R/U Cement Line. Test the lines W/3000 psi for 10 min, Fill tanks with fresh water (8 bbl) for mixing fluids. Start mixing cement Mix & Pump 15 bbl (62 sxs Cmt) Cement slurry (118 PCF). Pump 1 bbl (75 PCF) Spacer Behind. Displace CMT With 126 BBL Mud. POOH 9 Std's to 3040m (4 STD's Wet D.Pipe), Flush the string. .

Cont. POOH To 2167m (7" L.Lap), Circ Mud.R/U Cement Line. Test the lines W/3000 psi for 10 min, Fill tanks with fresh water (8 bbl) for mixing fluids. Start mixing cement

Additives and preparing mixing fluidsaccording to Program. Start to pumping 8 bbl (75 pcf) Ahead spacer.Mix & Pump 24 bbl (100 sxs Cmt) Cement slurry (118 PCF). Pump 1 bbl (75 PCF) Spacer Behind. Displace CMT With 61 BBL Mud.(1 BBl Short), POOH 9 Std's To 2018.76m ,Flush the string. Cont POOH to 1932.63m, Circ. BTM's Up.Close The Well .Cont POOH To Surface.

Stop Operation Due to Special war conditions By Client Request. Close The Well.

Stop Operation Due to Special war conditions By Client Request. Close The Well.Stop Operation Due to windy weather (dust strom) by request Rig 201 OEOC HES Officer .P/U & RIH with 8-3/8" Tri.cone Bit NO#4 (RR3, 537, Open, Kingdream, S/N: 2417584JH) + Bit sub 6 1/2" + 2 STD 6-1/2" D.C + 3 STD 5" H.W.D.P & Follow By 5" D.Pipe to 995m W/NL.NG .

Cont Run In hole on elevator to 1960m and Cont. RIH with Pump on to 2103m, Took Weight (64m above 7" L.Lap)Start D/O CMT Plug from 2103m to 2167.5m (7" L.Lap)(D/O Parameters: WOB: 5-15 Klb, Rot: 40-50 RPM, F.R: 320-350 GPM, SPP: 370-420 PSI).Circ BTM's Up .start POOH on Elevator from 2167.5m to 423m .Work on Drawworks.

Cont. POOH 8-3/8" D/O BHA on Elevator F/ 423m To Surface; L/D 8-3/8" Tri. Cone Bit NO#4 (RR3, 537, Open, K.Dream, S/N: 2417584JH, Dull Grade: 1.1.WT.A.E.I.NO.BHA), While Circ. C.W.H, NL-NGP/U & M/U BHA including 6-1/8" Tricone Bit (Used, K.Dream, S/N: 2304674JH, IADC: 537, Nozzle: Open) + 4-3/4 B.Sub + 1 STD 4-3/4" D.C +8 Stds 3-1/2" HWDP + 4-5/8" D.Jar + 1 Stds 3-1/2" HWDP and RIH To 282.4m, F/U BHA and Break Circ. , W/ NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 282.4 To 3139.6m Followed By 3-1/2" & 5" DPs On Elevator, While F/U Strg & Break Circ. At 15-Std intervals, Obs. Drag @ 3139.6m, W/ NL-NG.Conn. TDS and Cont. RIH W/ 6-1/8" D/O BHA F/ 3139.6 To 3170m W/ Soft Wash & Ream Dn W/ Applying Parameters [WOB: 2-3klbs, Rotation: 30RPM, Tq: 2-3klbs.ft, F.R: 270GPM, SPP: 1700-1750psi], Held up Stg Wt. & Tag TOC @ 3170m, While Reciprocate Strg before Conn. , W/ NL-NG.D/O CMT W/ 6-1/8" D/O BHA F/ 3170 To 3211.6m W/ Applying Parameters [WOB: 5-10klbs, Rotation: 30-40RPM, Tq: 2-4klbs.ft,F.R: 220-300GPM, SPP: 1700-2200psi, ROP: 7-8mph], While Reciprocate Every Drilled out Std before each Conn. & Pump Hi-Vis Pill Periodically, W/ NL-NG.

Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3211.6 To 3280m W/ Applying Parameters [WOB: 10-15klbs, Rotation: 30-50RPM, Tq: 2-4klbs.ft,F.R: 220-300GPM, SPP: 1700-2200psi, ROP: 9-10mph], While Reciprocate Every Drilled out Std before each Conn.

& Pump Hi-Vis Pill Periodically, W/ NL-NG.Pump 40Hi-Vis Pill, CBU @ 3280m To Sweep the Well and Shaker out the pumped Hi-Vis Pill, While optimize mud properties, NL-NG.Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3280 To 3300m W/ Applying Parameters [WOB: 10-15klbs, Rotation: 30-50RPM, Tq: 2-4klbs.ft,F.R: 220-300GPM, SPP: 1700-2200psi, ROP: 9-10mph], While Reciprocate Every Drilled out interval & Pump Hi-Vis Pill, W/ NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3300 To 3322m W/ Wash & Ream Dn W/ Applying Parameters [WOB: 1-2klbs, Rotation: 30-50RPM, Tq: 2-3klbs.ft, F.R: 220-300GPM, SPP: 1700-2200psi], NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3322 To 3664m Followed by 5" DPs On Elevator, While Circ. C.W.H, NL-NG.Pump 40Hi-Vis Pill, CBU @ 3664m To Sweep the Well and Shaker out the pumped Hi-Vis Pill, While optimize Mud properties, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3664 To 3693.5m Followed by 5" DPs On Elevator, While Circ. C.W.H, NL-NG.Conn. TDS and Cont. RIH W/ 6-1/8" D/O BHA F/ 3693.5 To 3740m W/ Wash Dn, Obs. Drag @ 3740m, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3740 To 3780m W/ Medium To Hard Wash & Ream Dn [WOB: 1-4klbs, Rotation: 30-50RPM, Tq: 3-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2300psi],, While Reciprocate and Back Ream Each Std Sev. Times, NL-NG.

Encounter Tight Hole Condition @ Interval 3750-3888m (TD); Conduct Hard Wash & Ream Dn W/ 6-1/8” D/O BHA W/ Applying Parameters [WOB: 3-8klbs, Rotation: 60-80RPM, Tq: 3-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi]; Apply Continuous Reciprocation & Back Ream to manage drag and Condition the Hole; Note TQ increase through Tight spots, While Pump Hi-Vis pill periodically, NL-NG.Pump 40bbl Hi-Vis Pill @ 3888m (TD), CBU & Shaker out the pumped Hi-Vis Pill, NL-NG.POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3689m (3m above 7" Shoe Depth) W/ Applying Parameters[Rotation: 20-30RPM, Tq: 2-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.RIH W/ 6-1/8" D/O BHA F/ 3689 To 3791 W/ Wash & Ream Dn W/ Applying Parameters [WOB: 3-8klbs, Rotation: 60-80RPM, Tq: 3-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.

Encounter Tight Hole Condition @ 3791m; Conduct Hard Wash & Ream Dn W/ 6-1/8” D/O BHA W/ Applying Parameters [WOB: 3-12klbs, Rotation: 60-80RPM, Tq: 3-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi]; Apply Continuous Reciprocation & Back Ream to manage drag and Condition the Hole and Attempt to Pass the same point, No Success; Note TQ increase through Tight spots, While Pump Hi-Vis pill periodically, NL-NG. POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3791 To 3670m (above 7" Shoe Depth) W/ Applying Parameters [Rotation: 20-30RPM, Tq: 2-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi],, NL-NG.RIH W/ 6-1/8" D/O BHA F/ 3670 To 3791 W/

Wash & Ream Dn W/ Applying Parameters [WOB: 3-10klbs, Rotation: 40-60RPM, Tq: 3-5.5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.Encounter Tight Hole Condition @ Interval 3791-3798m; Conduct Hard Wash & Ream Dn W/ 6-1/8" D/O BHA W/ Applying Parameters[WOB: 3-18klbs, Rotation: 60-80RPM, Tq: 3-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi]; Apply Continuous Reciprocation & Back Ream to manage drag and Condition the Hol; Note TQ increase through Tight spots, While Pump Hi-Vis pill periodically, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3798 To 3802.5m W/ Wash & Ream Dn W/ Applying Parameters [WOB: 3-10klbs, Rotation: 40-60RPM,Tq: 3-5.5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.

Encounter Tight Hole Condition @ 3802.5-3808m; Conduct Hard Wash & Ream Dn W/ 6-1/8" D/O BHA W/ Applying Parameters [WOB: 3-12klbs, Rotation: 60-80RPM, Tq: 3-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi]; Apply Continuous Reciprocation & Back Ream to manage drag and Condition the Hole; Note TQ increase through Tight spots, While Pump Hi-Vis pill periodically, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3808 To 3888 W/ Wash & Ream Dn W/ Applying Parameters [WOB: 3-10klbs, Rotation: 40-60RPM,Tq: 3-5.5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3682m (above 7" Shoe Depth) W/ Applying Parameters [Rotation: 20-30RPM, Tq: 2-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi],, NL-NG.While Slow Circ. @ 3682m Thru Strg & Monitor the Well, NL-NG.RIH W/ 6-1/8" D/O BHA F/ 3682 To 3808 W/ Wash Dn W/ Applying Parameters [WOB: 3-5klbs, F.R: 70-75GPM, SPP: 250-270psi], NL-NG.

Cont. RIH W/ 6-1/8" D/O BHA F/ 3808 To 3870m W/ Wash Dn W/ Applying Parameters [WOB: 3-5klbs, F.R: 70-75GPM, SPP: 250-270psi], NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3870 To 3888m W/ Wash & Ream Dn W/ Applying Parameters W/ Applying Parameters [WOB: 3-10klbs, Rotation: 40-60RPM, Tq: 3-5.5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3664m W/ Applying Parameters [Rotation: 10-90RPM, Tq: 2-5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.While Slow Circ. @ 3664m Thru Strg & Monitorthe Well, NL-NG.Stop Op. @ 3664m at request of OEOC Rig 201 HSE Officer Due To Windy Weather, While Slow Circ. Thru. Strg, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3664 To 3779m W/ Wash Dn W/ Applying Parameters [WOB: 3-5klbs, F.R: 70-75GPM, SPP: 250-270psi], NL-NG.While Slow Circ. @ 3779m Thru. Strg & Monitorthe Well, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3779 To 3888m W/ Wash Dn W/ Applying Parameters [WOB: 3-5klbs, F.R: 70-75GPM, SPP: 250-270psi], NL-NG.While Slow Circ. @ 3882m Thru. Strg & Monitorthe Well, NL-NG.Pump 40bbl

Hi-Vis Pill @ 3888m, CBU & Shaker out Hi-Vis Pill is in progress @ M.N, While Reciprocate Strg, NL-NG.

Cont. CBU & Shaker out Hi-Vis Pill @ 3888m, While Reciprocate Strg, Then Spot 40bbl Hi-Vis Pill @ 3888m, NL-NG.While Circ. @ 3886m Thru. Strg & Monitor the Well, NL-NG.Attempt To Start POOH 6-1/8” D/O BHA To Surface, Strg got Stuck @ 3880m, Work on Stuck Strg & Make it free; POOH 6-1/8” D/O BHAW/ Back Ream & Pump Out F/ 3888 To 3690m W/ Applying Parameters [Rotation: 70-80RPM, Tq: 2-6klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.RIH W/ 6-1/8" D/O BHA F/ 3690 To 3808m W/ Wash & Ream Dn W/ Applying Parameters W/ Applying Parameters [WOB: 3-10klbs,Rotation: 40-60RPM, Tq: 3-5.5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NGWhile Circ. @ 3808m Thru. Strg & Monitor the Well, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 3808 To 3888m W/ Wash & Ream Dn W/ Applying Parameters W/ Applying Parameters [WOB: 3-10klbs,Rotation: 40-60RPM, Tq: 3-5.5klbs.ft, F.R: 250-300GPM, SPP: 2100-2450psi], NL-NG.Pump 40bbl Hi-Vis Pill @ 3888m, CBU & Shaker out Hi-Vis Pill, While Reciprocate Strg, Then Spot 40bbl Hi-Vis Pill @ 3888m, NL-NG.POOH 6-1/8" D/O BHA F/ 3888 To 3664m On Elevator W/ Normal Hole Condition, While Circ. C.W.H, NL-NG.Cont. POOH 6-1/8" D/O BHA F/ 3664 To 338m On Elevator, While Circ. C.W.H, NL-NG.

Cont. POOH 6-1/8" D/O BHA F/ 338m To Surface On Elevator, L/D 6-1/8" Tricone Bit (2-2-WT-A-E-I-BT-LOG) & Rest of BHA, While Circ. C.W.H, NL-NG.Prepare Rig Floor For Logging, R/D Mouse Hole, Retrieve 11"Wear Bushing, P/U & Set 7" Shooting Nipple and Wire Line BOP; Perform Pressure Test, Ok; R/U SeaLand Wire Line Eqp. , P/U & Assemble Wireline Tool String including: Bridle for DLL +Tension Temperature Mud Resistivity + High Speed Digital Transmission/GR + Isolated Sub + Dual Lateral Log Tool Electronic Sub + Dual Lateral Log Tool Mandrel Sub + High Resolution Digital Acoustic + High Resolution Digital Acoustic Probe + Tool Bottom(Total Length: 32.24 m, Total Weight : 964.5 lb, Max OD:3.642 in) As Full Suite Logging (Resistivity-Sonic-CDR-GR) and RIH W/ the same To 3800m; Obs. Wireline Cable Tension Drop @ 3800m, Decided To POOH Wireline Logging Tool String; Commence Data Acquisition Logging Up F/ 3800 To 3692m to Fully Cover Logging Interval; POOH Wireline Logging Tool String To Surface, L/D Wireline Tool String, R/D Surface SeaLand Wireline Tools Eqp. & 7" Shooting Nipple; R/U Mouse Hole, Set 11" Wear Bushing, While Circ. C.W.H & Monitorthe Well, NL-NG.P/U & M/U 6-1/8" Condition BHA including: [6-1/8" PDC Bit (Used, BEST, S/N: 255421, IADC: M1665, Nozzle Size: 3*22/32", Dull Grade: 1-2-BT-T-X-I-WT-BHA) + 4-3/4" B.Sub + 2Jts 4-3/4" DC + 5-7/8" Stabilizer + 1Jt 4-3/4" DC + 8Stds 3-1/2" HWDP + 4-5/8" Drlg Jar

+1Std 3-1/2" HWDP] and RIH To 283.7m, F/U BHA & Break Circ. , NL-NG.Cont. RIH W/ 6-1/8" Condition BHA F/ 283.7 To 3692m On Elevator Followed by 3-1/2" & 5" DPs, While F/U Strg & Break Circ.at 15-Std intervals, NL-NG.Conn. TDS & F/U Strg, Cont. RIH W/ 6-1/8" Condition BHA F/ 3692 To 3752m W/ Wash & Ream Dn W/ Applying Parameters[WOB: 1-5klbs, Rotation: 155-160RPM, Tq: 3-6klbs.ft, F.R: 270GPM, SPP: 2660psi], NL-NG.

Cont. RIH W/ 6-1/8" Condition BHA F/ 3752 To 3888m W/ Wash & Ream Dn W/ Applying Parameters[WOB: 1-5klbs,Rotation: 155-160RPM, Tq: 3-6klbs.ft, F.R: 270GPM, SPP: 2660psi], While Back Ream & Ream Dn Each Std Before Connection, NL-NG.POOH 6-1/8" Condition BHA F/ 3888 To 3692m W/ Applying Parameters [Rotation: 15-160RPM, Tq: 2-6klbs.ft, F.R: 270GPM, SPP: 2660psi],While Hard To Med. Back Ream & Ream Dn Interval 3800 To 3888m Sev. Times, NL-NG.RIH W/ 6-1/8" Condition BHA F/ 3692 To 3888m W/ Wash & Ream Dn W/ Applying Parameters [WOB: 3-5klbs, Rotation: 155-160RPM, Tq: 3-6klbs.ft, F.R: 270GPM, SPP: 2660psi], While Conduct Back Ream & Ream Dn Interval 3800-3888m Sev. Times, Normal Hole Condition confirmed, NL-NG.Pump 50bbl Hi-Vis Pill @ 3888m, CBU & Shaker out Hi-Vis Pill, While Reciprocate Strg, NL-NG.POOH 6-1/8" Condition BHA F/ 3888 To 3800m W/ Pump out, Normal Hole Condition confirmed; Cont. POOH The same BHA F/ 3800 To3692m On Elevator, Normal Hole Condition confirmed, While Circ. C.W.H, NL-NG.Stop POOH Operation @ 3692m Due to Windy Weather at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg, NL-NG.Cont. POOH 6-1/8" Condition BHA F/ 3692 To 1292m On Elevator, While Circ. C.W.H, NL-NG.

Cont. POOH 6-1/8" Condition BHA F/ 1292m To Surface, L/D 6-1/8" Bit (1-2-BT-T-X-I-WT-LOG) & Rest of BHA, While Circ. C.W.H, NL-NG.M/U Additional 3-1/2" Tubular needed for TLC Job Jt by Jt, Flush Tubular; Stand Back The same Tubular in the Derrick, NL-NG.P/U & Assemble Wireline Logging Tool String For TLC Logging including: [Downhole Wet Connector Head + Flexibly Sub + N Hard Electrode System + Tension Temperature Mud Resistivity + High Speed Digital Transmission/GR + Natural Gamma Spectrum + Isolated Sub + E-Dual Lateral Log Tool Electronic Sub + S-Dual Lateral Log Tool Mandrel Sub + E-High Resolution Digital Acoustic + S-High Resolution Digital Acoustic Probe + Tool Bottom (Total Length : 27.244 m, Total Weight : 1545.940 lb, Max Outside Diameter : 3.642 in)] and RIH To 27m; Tool String Function Test performed; Signal reception confirmed, While Circ. C.W.H, NL-NG.Cont. RIH W/ Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole F/ 27 To 314m Followed by 3-1/2" On Elevator, While F/U Strg at 10-Std Interval.Stop RIH Operation @ 314m Due to Windy Weather at the request of OEOC Rig 201 HSE

Officer, While Slow Circ. Thru. Strg, NL-NG.Cont. RIH W/ Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole F/ 314 To 1556m Followed by 3-1/2" & 5"DPs On Elevator, While F/U Strg at 10-Std Interval.

Cont. RIH W/ Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole F/ 1556 To 3614m Followed by 3-1/2" & 5"DPs On Elevator, While F/U Strg at 10-Std Interval, NL-NG.CBU 1.5 Strg Cap @ 3614m to clean Latching Position & remove debris, While R/U Surface Wireline Eqp. , NL-NG.Hold CSES suspended above Drill Floor, RIH W/ PWCH On Wireline 50m into the Well, M/U CSES to Drill String, Lowered CSES belowDrill Floor; RIH W/ PWCH On Wireline, While Circ. above Latch Depth & Build up SPP To 1000 psi To Assist PWCH RIH; Attempt latching, latching confirmed Mechanically/Electricall, But No Data received; POOH PWCH On Wireline To Surface, POOH CSES above Drill Floor, Then Replace PWCH W/ Back up PWCH; Prepare Tools and Cont. Operations as per previous procedure, RIH & Re-latched, But still No Data observed; Decided To POOH Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole To Surface; L/D PWCH, B/O CSES,

R/D Surface Wireline Eqp. , NL-NG.POOH Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole F/ 3614 To 2788m On Elevator, While Circ. C.W.H, NL-NG.

The well was conditioned to ensure stability and optimal fluid properties while waiting on SeaLand Co. operations Cont. POOH Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole-TLC F/ 2788m To Surface On Elevator, L/D SLD Wireline Logging Tool String; Obs. N Bridle (DLL Deep, SeaLand Co.) damaged and failed; R/D Wireline Logging Surface Tools, While Circ. C.W.H, NL-NG.The well was conditioned to ensure stability and optimal fluid properties while waiting on SeaLand Co. P/U & M/U 6-1/8" Condition BHA including: [6-1/8" PDC Bit (Used, BEST, S/N: 255421, IADC: M1665, Nozzle Size: 3*22/32",Dull Grade: 1-2-BT-T-X-I-WT-LOG) + 4-3/4" B.Sub + 2Jts 4-3/4" DC + 5-7/8" Stabilizer + 1Jt 4-3/4" DC + 8Stds 3-1/2" HWDP + 4-5/8" Drlg Jar +1Std 3-1/2" HWDP] and RIH To 283.7m, NL-NG. While wait on seaLand Co. Cont. RIH W/ 6-1/8" Condition BHA F/ 283.7 To 3692m On Elevator Followed by 3-1/2" & 5" DPs, NL-NG.Conn. TDS & F/U Strg, Cont. RIH W/ 6-1/8" Condition BHA F/ 3692 To 3877m W/ Wash Dn [F.R: 50GPM, SPP: 155psi];Cont. RIH W/ 6-1/8" Condition BHA F/ 3877 To 3888m W/ Wash & Ream Dn W/ Applying Parameters [WOB: 1-7klbs, Rotation: 155-160RPM, Tq: 3-6klbs.ft, F.R: 255GPM, SPP: 2550psi], Normal Hole Condition confirmed, NL-NG.

CBU @ 3888m, While Back Ream & Ream Dn Interval 3866-3888m, NL-NG.Cont. POOH 6-1/8" Condition BHA Pump out F/ 3888 To 3780m, NL-NG.Cont. POOH 6-1/8" Condition BHA F/ 3780m To Surface On Elevator, L/D Bit W/ Same Condtion and Rest of BHA, While Circ. C.W.H, NL-NG.Prepare Rig Floor For Logging, R/D Mouse Hole, Retrieve 11"Wear Bushing, P/U & Set 7" Shooting Nipple and Wire Line BOP; Perform Pressure Test, Ok; R/U SeaLand Wire Line Eqp. , P/U & Assemble Wireline Tool String including: Bridle for DLL +Tension Temperature Mud Resistivity + High Speed Digital Transmission/GR + Isolated Sub + Dual Lateral Log Tool Electronic Sub + Dual Lateral Log Tool Mandrel Sub + High Resolution Digital Acoustic + High Resolution Digital Acoustic Probe + Tool Bottom (Total Length: 32.24 m, Total Weight : 964.5 lb, Max OD:3.642 in) As Full Suite Logging (Resistivity-Sonic-CDR-GR) and RIH W/ the same To 3885m; Commence Data Acquisition Logging Up F/ 3885 To 3800m to Fully Cover Logging Interval, While Circ. C.W.H, NL-NG.Cont. Commence Data Acquisition Logging Up F/ 3800 To 3692m to Fully Cover Logging Interval; Logging Up in Interval 3700 To 3780m was repeated based on Client's Request for Verification; POOH Wireline Logging Tool String To Surface, L/D Wireline Tool String, R/D Surface SeaLand Wireline Tools Eqp. & 7" Shooting Nipple; R/U Mouse Hole, Set11" Wear Bushing, While Circ. C.W.H & Monitor the Well, NL-NG.Slip & Cut 100ft Drlg Line, While Circ. C.W.H, NL-NG.P/U & M/U 6-1/8" Condition BHA including: [6-1/8" PDC Bit (Used, BEST, S/N: 255421, IADC: M1665, Nozzle Size: 3*22/32",Dull Grade: 1-2-BT-T-X-I-WT-LOG) + 4-3/4" B.Sub + 2Jts 4-3/4" DC + 5-7/8" Stabilizer + 1Jt 4-3/4" DC + 8Stds 3-1/2" HWDP + 4-5/8" Drlg Jar +1Std 3-1/2" HWDP] and RIH To 283.7m, F/U BHA & Break Circ. , NL-NG.

Cont. RIH W/ 6-1/8" Condition BHA F/ 283.7 To 3692m On Elevator Followed by 3-1/2" & 5" DPs, While F/U Strg & Break Circ.at 15-Std intervals, NL-NG.Conn. TDS & F/U Strg, Cont. RIH W/ 6-1/8" Condition BHA F/ 3692 To 3888m W/ Wash Dn [F.R: 50GPM, SPP: 155psi], Normal Hole Condition confirmed, NL-NG.Pump 50bbl Hi-Vis Pill @ 3888m, CBU till Shaker out the pumped Hi-Vis Pill, NL-NG.Cont. POOH 6-1/8" Condition BHA F/ 3888 To 110m On Elevator, While Circ. C.W.H, NL-NG.

Cont. POOH 6-1/8" Condition BHA F/ 110m To Surface On Elevator, L/D 6-1/8" PDC Bit (1-2-BT-T-X-I-WT-TD) & Rest of BHA, While Circ. C.W.H, NL-NG.Held PJSM, R/U Casing Running Tools, P/U & M/U 5" F.Shoe (18#, L-80, HSG3-FJ THD, PPA) + 1 Jt 5" LNR (18#, L-80, HSG3-FJ THD) +5" F.Collar (18#, L-80, HSG3-FJ THD, PPA) + 1 Jt 5" LNR (18#, L-80, HSG3-FJ THD) + 5"LDC (18#, L-80, HSG3-FJ THD, PPA) + 1 Jt 5" LNR (18#, L-80, HSG3-FJ THD) and RIH to 36.97m, While Function Test F.Shoe & F.Collar, Use Thread Lock Compound in Shoe Track Connections, and

Break Circ. Thru. Shoe Track, NL-NG.Cont. RIH W/ 5" LNR Assy. F/ 36.97 To 295m Followed By 21 Jts 5" LNR (18#, L-80, HSG3-FJ THD) (Totally : 24 Jts 5" LNR) While Use Thread Seal Compound, Torque Turn Monitoring System, Spirolizer as per plan, NL-NG.P/U & M/U Liner Hanger Assy. With Top PKR to 5" LNR, L.W.P Pinned to Bottom Running tools, Check Setting tools & All Connection, Record Up & Downward String weight, Cont. RIH with 3-1/2" & 5" D.P to 3450m while Pass Rabbit thru All D.Pipe & fill up string W/NL.NG..

Cont. Run 5" LNR with Follow by 5" D.P to 3692m (7" Shoe) & Break Circ Mud while Pass Rabbit thru All D.Pipe & fill up string W/NL.NG.Cont RIH with 5" D.P to 3888m (TD) & while Pass Rabbit thru All D.Pipe & fill up string. Record Up & Downward String weight, Pick up string 1^{m} off Btm (3887m), Drop Ball and Set LNR HGR with 2000Psi @ 3598.5m, Ok. Increase Press. To 2500Psi to shear LDC,Release Setting tools & Check String Weight, Ok.HPJSM, PUMP 15bbls Chemical Wash (62.4 Pcf), Pump 20bbl as Spacer Wash (90Pcf) By Rig Pump, Pump 30.72bbl Slurry CMT (118Pcf), Release PDP, Disp. Cement with 166 BBL Mud (Obs. Shear off Wiper plug after Pump 150bbl Mud and Obs. Bump Plug W/2000Psi, Perform Integrity Test ,Ok). Bleed of Pressure, Check Back Flow, Ok. Sting Out and Set Packer, Ok. NL-NG During Cement Job. POOH 10 STD, Flush The String, Cont. POOH 8STD.Circ. BTM's UP .Cont. POOH to Surface & L/D Setting Tools LNR HGR. P/U & M/U 6-1/8" BHA including: 6-1/8" Tri-Cone Bit, K.Dream, IADC: 537, S/N: 2304674JH, Used, D.G: 2-2-WT-A-E-I-BT-BHA, Open) + 4-3/4" Bit sub (float-in) + 3 Stds 4-3/4" D.C + 6 Stds 3 1/2"HWDP & Follow by 3-1/2" D.P to 390m.

Cont Run in hole with 6-1/8" BHA including: 6-1/8" Tri-Cone Bit, K.Dream, IADC: 537, S/N: 2304674JH, Used, Open) + 4-3/4" Bit sub (float-in) + 3 Stds 4-3/4" D.C + 6 Stds 3 1/2"HWDP & Follow by 3-1/2" & 5" D.P to 3596m and Confirm 5" L.Lap @ 3596m.Circ Mud till clean Shaker.POOH While L/D 83 Joint's extra 5" D.Pipe to 2132m.

Cont. POOH While L/D Extra 5" D.Pipe to 1835m (Totally : 111 Jts),Cont POOH by Stands from 1835m to 448m.Cont POOH from 448m to 274m while L/D Totally 21 Jts Extra 3-1/2" D.P (Jts by Jts),Cont POOH from 274m to surface and L/D 6-1/8" Tri-Cone Bit, K.Dream, IADC: 537, S/N: 2304674JH, Used, Open, D.C: 2-2-WT-A-E-I-BT-BHA.Install G-Monkey board, Wash and SLM & Pass Rabbit DPs, Change Handling Tools, P/U & Run in hole with 4-1/8" M.M Junk Mill (New,T.S.E.KH, Nozzle Port : 5*10/32", S/N 944) + 16 Jts 3-1/8" D.C(Jts by Jts) to 142m.

Cont Run in hole with 4-1/8" D/O BHA 5 Jts 3-1/8" D.C (Jts by Jts) + 15 Jts 2-7/8" D.P (Jts by Jts) & Follow by 3-1/2" D.Pipe to 3601.4m.Tag P.O.B.Strat D/Out P.O.B to 3601.8m suddenly drop weight. Continue run in Hole with wash & ream to 3604m. Took weight. Continue D/Out to 3604.8m, drop weight. Continue run in Hole with wash Down to 3612.46m W/NL.NG.

Continue run in Hole with wash Down to 3864.13m, Took weight, Continue D/O P.D.P & L.W.P & LDC to 3864.5m, try to continue, No Progress. D/Out Parameters: WOB: 5-8 Klb, ROT: 30-40 RPM, F.Rate: 30-65 GPM, SPP: 260-850 PSI, TQ: 3-5 KLB.Ft Circ BTm's Up. POOH with 4-1/8" D/O BHA From 3864.5m to 3467m while Circ Mud Cross Well Head & NL.NG. .

Cont POOH with 4-1/8" D/O BHA From 3467m to Surf and L/D 4-1/8" M.M.J.M (Mill condition : 10% used)while Circ Mud Cross Well Head & NL.NG.Perform BOP Test as NIOC Policy, Retrieve Wear Bushing, Set Plug Tester, Perform BOP Test as follow:5k 13-5/8" Annular w/ 3500psi, 15min, Ok, 10k 13-5/8" Top Ram (VBR 2-7/8" - 5") w/ 7500psi, 15min, Ok, 10k 13-5/8" BTM Ram 5" Pipe Ramw/ 7500psi, 15min, Ok, 10k 13-5/8" Shear Ram w/ 7500psi, While Press. Test All Choke Manifold Valves & Accumulator Unit Functionality,Ok, Retrieve Plug Tester, Install Wear Bushing.P/U & RIH With 3-3/4" M.M.J.Mill (New. T.S.E.KH, NZL Port : 5*10/32", S/N: 101) + 3 1/8" B.sub + 7 STDs 3 1/8" DC + 5 STDs 2-7/8" DP & Follow by 3 1/2" DP to 740m While Break Circ Mud W/NL.NG. .

Cont RIH With 3-3/4" M.M.J.Mill & Same BHA Follow by 3 1/2" DP to 1898m While Break Circ Mud, Change Elavator & Handling tool.Cont RIH With 5" DP to 3596m (5" L.Lap) While Break Circ Mud. W/NL.NG.4 Hrs Waiting for Rig 201 Duo to Delay in Run in hole Operation.Cont Run in hole with Pumping from 3596m (5" L.Lap) to 3864.5m.1 Hrs Waiting for Rig 201 Duo to Work on Drawworks.Commence D/Out LDC to 3864.8m and D/Out Soft to Med CMT Below LDC from 3864.8 to 3868m and Med to Hard from 3868 to 3876.2m.D/Out Soft to Med CMT Parameters: (WOB: 1-3 Klb, ROT: 30 RPM, F.Rate: 60-65 GPM, SPP: 800-1000 PSI, TQ: 3-5 KLb.ft, ROP: 15 MPH)D/Out Med to Hard CMT Parameters: (WOB: 3-5 Klb, ROT: 30 RPM, F.Rate: 60-65 GPM, SPP: 800-1000 PSI, TQ: 3-5 KLb.ft, ROP: 5 MPH)

Commence D/Out Med to Hard from 3876.2 to 3876.7m (F.Coller Depth), Work on D/OUT interval for Smooth it Several timesCirc BTM's UP With Pump 20BBL Hi.Vis Pill While Work on reduce mud weight 1 PCF (from 87 to 86). Balance Mw In/Out (

86 Pcf)Start POOH from 3876.7m to 2379m .2 Hrs Wait on operation due to bad weather.Cont. POOH From 2379m to Surface & L/D 3-3/4" M.M.J.Mill (10% Used). L/D Mouse Hole, P/U & install Shooting Nipple.2 Hrs Waiting for Rig 201 Due to Delay in POOH Operation.R/U Wireline logging Equipment (SeaLand Co.) .

Cont R/U Wireline logging Equipment including (CCL - GR - SBT - VDL) (Total Length: 16.66m, Max OD : 3.62") Run in Hole with Logging Tools Run#1 (CCL - GR - SBT - VDL) to 3874.7m, Take Log up from 3874.7m to 3560m and Cont POOH to Surface & L/D Logging Tools (CCL - GR - SBT - VDL) W/NL.NG.R/U & Run in Hole with Logging Tools Run#2 (CNT - GR) to 3874m, Take Log up from 3874m to 3596m (5" L.Lap) and Cont. POOH to Surface meanwhile Obs. drag during Logging operation at three point inside 5" LNR.L/D Logging Tools (CNT - GR) & R/D logging Equipment.P/U & M\U 9-5/8" CSG Scraper BHA including : (5-7/8" Center Cut Bit + Bit Sub + 1 STD 3 1/2" DP + X.O.S + 9 5/8" Scraper) and follow by5" D.Pipe to 2167m (7" L.Lap) while Scrap PKR depth Interval several time, Pump 30BBL Hi.Vis Pill .

Cont work on Scrap PKR Interval while Circ Btm's Up & Shaker Out Hi.Vis Pill.POOH From 2167m to Surf & L/D 5-7/8" Center Cut Bit & 9-5/8" CSG Scraper while Circ mud Cross well head.Slip & Cut 97Ft DRLG Line.P/U & RIH with 7-5/16" Polish Mill (NZL Port : 4*10/32") + 5 STD 5" H.W.D.P & Follow by 5" D.Pipe to 220m W/NL.NG.Stop operation due to bad weather.Cont RIH with 7-5/16" Polish Mill + 5 STD 5" H.W.D.P & Follow by 5" D.Pipe to 2167m (7" L.Lap) W/NL.NG.Work on Polish inside 7" PBR Several times.Pump 30BBl Hi.vis Pill, Circ Btm's up and Shaker out Hi.Vis Pill.POOH from 2167m to 1421m while Circ mud Cross well head .

Cont POOH From 1421m to Surf & L/D 7-5/16" Polish Mill (NZL Port : 4*10/32") while Circ mud Cross well head.P/U & M/U 7" S.N PKR (29#, L-80, ACME, PPA) + 4 STD 6-1/2" D.C + 6 STD 5" H.W.D.P to 276m.Cont RIH with 7" S.N PKR BHA From 276m to 2167m (7" L.Lap) W/NL.NG.Connect Top Drive and establish Circulate while records all required parameters. Set 7" S.N PKR as procedure, Succ.POOH from 2165m (New 7" L.Lap) to Surface and L/D Setting Tools while Circ mud Cross well head.P/U & M/U 5-1/8" Polish Mill + 4-3/4" Double Pine + 4-3/4" Bit Sub + 9 Stds 3-1/2 H.W.D.P to 250m.Cont RIH with 5-1/8" Polish Mill BHA to 450m W/NL.NG. .

Cont RIH with 5-1/8" Polish Mill BHA with 3-1/2" & 5" D.Pipe from 450m to 3596m (5" L.Lap) W/NL.NG.Meanwhile Polish inside 5" PBR Several times, Work on Dec. mud weight 1 PCF (from 86 to 85). Balance Mw In/Out (85 Pcf) &Take " LG " Mark several Time. Check 5" L.Lap Depth carefully, Observe 5" L.Lap Depth to aproximatly

4m Deeper (5" L.Lap : 3600m)Start POOH From 3600m to Surf. while Circ mud Cross well head.1 Hrs Waiting for Rig 201 Duo to Delay in POOH Operation.P/U & RIH with 5-1/8" Polish Mill + 4-3/4" Double Pin + 7" Scraper + 4-3/4" Bit Sub + 1 Stds 3-1/2 H.W.D.P to 30m. .

Cont RIH with 5-1/8" Polish Mill + 4-3/4" Double Pin + 7" Scraper + 4-3/4" Bit Sub + 9 Stds 3-1/2 H.W.D.P & Follow by 3-1/2" & 5" D.Pipe To 3596m (5" L.Lap) While Break Circ Each 20 Stds.Meanwhile Scrap 5" S.N PKR depth Interval, Pump 25BBL Hi.Vis Pill, Circ Btm's Up & Shaker Out Hi.Vis Pill and Work on Dec. mud5-1/8" Polish mill + 7" Scraper While Circ Mud cross well head .Weight 1 PCF (from 85 to 84). Balance Mw In/Out (84 Pcf).POOH with 7" Scraper from 3596m to 3570m (Dry test PKR Depth) and scrap Dry test PKR Depth Several time, Cont POOH to Surf & L/D.

P/U & RIH W/ 5" Tie-Back Packer Assy. + 6 STD 4-3/4" D.C + 9 STD 3-1/2" H.W.D.P Followed by 3-1/2" & 5" DPs To 3596m (5" L.Lap), While Break Circ. At 20-Stds Interval, NL-NG.Record Upward & DownwardStrg Weight; Sting in Seal Nipple into 5" LNR PBR W/ 20 Klbs, Accompany by an increase in SPP pressure;Apply 50 Klbs Slack-off To Set PKR Via Collect Lock Mechanism, Indication observed on Weight Indicator; Confirmed New 5"L.Lap @ 3593.5m;Perform 10 Klbs Pull Test – Test result OK; Release Setting Tool W/ 26 Turns, NL-NG.POOH 5" Tie-Back Packer Assy. Setting Tool F/ 3593.5 To 2231m, While Circ. C.W.H, NL-NG.

Cont. POOH 5" Tie-Back Packer Assy. Setting Tool F/ 106m To Surface, R/D Eqp. & Prepare to RIH W/ Dry Test Tool String, While Circ. C.W.H, NL-NG.P/U & M/U 7"Dry Test Tool String including: Bottom B.T (First Memory Gauge) + Anchor pipe + X.O.S 3 1/2" FH Pin x 3-1/2" IF Box +X.O.S 3 1/2" IF Pin x 4-1/2" IF Box + Middle Packer element + 7" Above Packer + X.O.S 3-1/2" IF Box *4-1/2" EUE PIN +X.O.S 3-1/2" FH Box *3-1/2" IF PIN + RH Release Safety Joint + Hydraulic JAR + Middle B.T (Second Memory Gauge) + Hydro-spring + D.C.I.P + 1 Jt 3-1/2" Drill Pipe + Reverse Sub and RIH to 23m, While Monitor the Well, W/ NL-NG.Cont. RIH W/ 7"Dry Test Tool String F/ 23 To 1797m On Elevator Followed by 6 Stds 4-3/4" DC, 46 Stds 3-1/2" DPs and 5"DPs W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U Strg W/ Drill water (62.4 pcf) as a Cushion at 5-Std intervals, W/ NL-NG.

Cont. RIH W/ 7"Dry Test Tool String F/ 1797 To 3572m On Elevator Followed by 5"DPs 'W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 2541m of Strg W/ Drill water (62.4 pcf) as a Cushionat

5-Std intervals, NL-NG.Prepare Rig Floor, Change TDS Links & Perform Dry Test Op. as follows:R/U and prepare Chicksan pipes and DST choke manifold, Pressure test lines to 3000 psi for 15 minutes, test confirmed OK, Record Strg Wt. in both upward and downward directions.Setting PKR and Opening Hydro-Spring Valve: Rotate Strg 6 full turns clockwise, Apply set-down Wt. to set the 7" Dry Test PKR at 3570m, Obs. Hydro-Spring Valve opening indication on M/D; Well opened Thru. Hydro-Spring Valve.Open Period Monitoring: Log start time of Opened period (17:30), Maintain open condition and monitor for totally 3Hrs.for any bubbles at the surface for ongoing monitoring, No Bubbles observed; Confirm Annulus fluid level is Static during observation.Close Period Monitoring: S/O Strg Weight, Rotate Strg clockwise to close the DCIP Dry Test Assy. Valve to Close the Well, Log start time of Closed period (20:30) and monitor for 3.5 Hrs.is in progress at M.N, Confirm Annulus fluid level is Staticduring observation, NL-NG.

Cont. Close Period Monitoring and maintain for totally 6 Hrs, Confirm Annulus fluid level is Static during observation.Open Circulation Valve: Drop Bar to open Circ. valve, Establish Reverse Circulation, confirm balance mud is observed at the surface andthe water cushion is the same as the F/U Volume; Unset the 7" Dry Test PKR using normal P/U Weight stepwise, B/O & L/D Dry Test Surface Equipment, NL-NG.CBU Thru. Strg Till Uniform In/Out MW @ 3563m; Static Flow Check, Well Static, NL-NG.POOH 7" Dry Test Tool String F/ 3563 To 560m On Elevator W/ Speed Control (5 Std/Hr. in 7" LNR; 8 Std/Hr. in 9-5/8" CSG) at the request of OEOC Dry Test supervisor, While Circ. C.W.H, NL-NG.

POOH 7" Dry Test Tool String F/ 560m To Surface On Elevator W/ Speed Control (5 Std/Hr. in 7" LNR; 8 Std/Hr. in 9-5/8" CSG) at the request of OEOC Dry Test supervisor, B/O & L/D BHA & Dry Test Tool String; Read Middle & BTM B.T:3Hrs. Open-Period Monitoring Results: [Middle B.T: 3572 - 3572psi, BTM B.T: 3588-3588psi];6Hrs. Close-Period Monitoring Results: [Middle B.T: 3572 - 3798psi, BTM B.T: 3588-3814psi]; Check Properties of flowing sample between DCIP & Hydrospring [MW: 74pcf, PH: 7.5 , Cl: 180000, Ca+: 2400];While Circ. C.W.H, NL-NG.Slip & Cut of 100ft Drlg Line, While Circ. C.W.H, NL-NG.P/U & M/U 9-5/8"Dry Test Tool String including: Bottom B.T (First Memory Gauge) + Anchor pipe + X.O.S 3 1/2" IF Box x 3 1/2" FH Pin + X.O.S 4-1/2" IF Box x 3 1/2" IF Pin + Middle Packer element + 9-5/8" Above Packer + X.O.S 3-1/2" IF Box *4-1/2" IF PIN + X.O.S 3-1/2" FH Box x 3-1/2" IF PIN + RH Release Safety Joint + Hydraulic JAR + Middle B.T (Second Memory Gauge) + Hydro-spring + D.C.I.P + X.O.S 4-1/2" IF Box x 3-1/2" IF Pin +1 Jt 5" Drill Pipe + Reverse Sub and RIH to 23.5m, While Monitor the Well, W/ NL-NG.Cont. RIH

W/ 9-5/8"Dry Test Tool String F/ 23.5 To 1950m On Elevator Followed by 4 Stds 6-1/2 DCs + 2Stds 5" HWDP & 5"DPs W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 678m of Strg W/ Drill water (62.4 pcf) as a Cushion at 5-Std intervals, NL-NG.

Cont. RIH W/ 9-5/8"Dry Test Tool String F/ 1950 To 2148m On Elevator Followed by 5"DPs W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular, NL-NG.Prepare Rig Floor, Change TDS Links & Perform Dry Test Op. as follows:R/U and prepare Chicksan pipes and DST choke manifold, Pressure test lines to 3000 psi for 15 minutes, test confirmed OK, Record StrgWt. in both upward and downward directions.Setting PKR and Opening Hydro-Spring Valve: Rotate Strg 6 full turns clockwise, Apply set-down Wt. to set the 9-5/8" Dry TestPKR at 2145m, Obs. Hydro-Spring Valve opening indication on M/D; Well opened Thru. Hydro-Spring Valve.Open Period Monitoring: Log start time of Opened period (03:00 a.m), Maintain open condition and monitor for any bubbles at the surfacefor ongoing monitoring, No Bubbles observed during the first hour of monitoring period, Bubbles observed afterward; Confirm Annulus fluid level is Static during observation, NL-NG.Close Period Monitoring: S/O Strg Weight, Rotate Strg clockwise to close the DCIP Dry Test Assy. Valve to Close the Well,Log start time of Closed period (06:00 a.m) and monitor for 6 Hrs. , Bubbles continuously observed Thru. Strg & Annulus during Monitoring, Annulus fluid level exhibited fluctuations & Not remain Static throughout Observation.Open Circulation Valve: Drop Bar to open Circ. valve, Establish Reverse Circulation, confirm balance mud is observed at the surface; Recovered approximately 20 bbl of Mud-contaminated fluid, 30 bbl of Drill water, and 10 bbl of Mud-contaminated fluid; Unset the 9-5/8" Dry Test PKR using normal P/U Weight stepwise, B/O & L/D Dry Test Surface Equipment, NL-NG.CBU Thru. Strg Till Uniform In/Out MW @ 2140m; Static Flow Check, Well Static, NL-NG.POOH 9-5/8" Dry Test Tool String F/ 2140 To 945m On Elevator W/ Speed Control (8 Std/Hr.) at the request of OEOC Dry Test supervisor,While Circ. C.W.H, NL-NG.

Cont. POOH 9-5/8" Dry Test Tool String F/ 945m To Surface On Elevator W/ Speed Control (8 Std/Hr.) at the request of OEOC Dry Test supervisor, B/O & L/D BHA & Dry Test Tool String; Read Middle & BTM B.T:3Hrs. Open-Period Monitoring Results: [Middle B.T: 1062 - 1541psi, BTM B.T: 1081-1556psi];6Hrs. Close-Period Monitoring Results: [Middle B.T: 1541 - 3369psi, BTM B.T: 1556-3381psi]; While Circ. C.W.H, NL-NG.Perform BOP Test as NIOC Policy, Retrieve Wear Bushing, Set Plug Tester, Perform BOP Test as follow:5k 13-5/8" Annular w/ 3500psi, 15min, Ok, 10k 13-5/8" Top Ram (VBR 2-7/8" - 5") w/ 7500psi, 15min, Ok, 10k 13-5/8" BTM Ram 5" Pipe

Ramw/ 7500psi, 15min, Ok, 10k 13-5/8" Shear Ram w/ 7500psi, While Press. Test All Choke Manifold Valves & Accumulator Unit Functionality,Stop RIH Operation Due to Windy Weather at the request of OEOC Rig 201 HSE Officer, While Circ. C.W.H, NL-NG.Ok, Retrieve Plug Tester.P/U & M/U 7-5/16" Polish BHA including: [7-5/16" Polish Mill & 5 Stds 5" HWDP] and RIH To 137.5m, F/U BHA and Break Circ. , NL-NG.Cont. RIH W/ 7-5/16" Polish BHA F/ 137.5 To 850m On Elevator, While F/U Strg & Break Circ. At 10-Stds interval, NL-NG.Stop RIH Operation @ 850m Due to Windy Weather at the request of OEOC Rig 201 HSE Officer, While Slow Circ. Thru. Strg, NL-NG.Cont. RIH W/ 7-5/16" Polish BHA F/ 850 To 2165m On Elevator, While F/U Strg & Break Circ. At 10-Stds interval, NL-NG.Conn. TDS and Circ. For a while On Top of 7" LNR; Cont. RIH W/ 7-5/16" Polish Mill W/ Wash Dn To 2167.5m & Tag L.G,Work on making L.G mark on Polish Mill Nose W/ Applying parameters: [WOB: 10klbf, Rotation: 35RPM, Tq: 1-3klbf.ft]; Polish Inside Tie-Back Sleeve W/ Pump out Sev. Times; Circ. BTMs Up, While Reciprocate Strg periodically, NL-NG.POOH 7-5/16" Polish BHA F/ 2167 To 1707m, While Circ. C.W.H, NL-NG.

POOH 7-5/16" Polish BHA F/ 1707m To Surface, L/D 7-5/16" Polish Mill & Rest of BHA, Obs. L.G Mark on Polish Mill Nose, While Circ. C.W.H, NL-NG.Prepare Rig Floor To RIH 7" Tie-Back Assy, R/U CSG Running Tools;Seal Nipple (29#,L-80, TPCQ THD,PPA) + 2Jts 7" LNR (29#,L-80, TPCQ THD) + LDC (29#,L-80, TPCQ THD,PPA) + 10Jts 7" LNR (29#,L-80, TPCQ THD) + LG + 7" T.B.Sleeve + Setting Tool and RIH To 133m, While Clean & Wash All Threads, using Thread Seal Compound, Thread Lock Compound For Seal Nipple & LDC, Torque and Turn Monitorng System ; Record Strg Wt. in Both Upward & Dnward Directions; Conduct Rotational Functionality Test on Setting Tools, Ok; While Circ. C.W.H, NL-NG.Cont. RIH W/ 7" Tie-Back Assy F/ 133 To 2160 m, While Drift All Tubular, NL-NG.Conn. TDS & Circ. On 7" TOL For a while; R/U & L/U Chiksan Pipes & CMT Manifold; Conduct Press. Test on Chiksan Pipes andCMT Manifold W/ 3000psi, 15min, Ok; Load Pump Down Plug; NL-NG.

Hold PJSM; Record Strg Wt. in Both Upward & Dnward Directions; Sting in 7" Tie-Back Assy W/ 100 psi To 2165.5m, Note 200 psi pressure rise and hold; Sting out 7" Tie-Back Assy to 2165.3m, Note Pressure return to Normal; Slow Circ. On 7" TOL fora while; Pump 20 bbl 62.4 pcf Drill Water by Rig Pump as Spacer; Mix and Pump CMT "G" blended Silica Flour(S.V: 30 bbl, S.W: 118 pcf) using SPAD Energy Co. Pump Truck @ F.L: 4–5 bpm & SPP: 80 psi; Release Pump Down Plug and displaceW/ 125 bbl 84 pcf Mud, While Shear Wiper Plug Pins after 114 bbl displacement @ 750 psi; Sting in Seal Nipple inside Tie-Back Sleeve , Note Hook Load reduction equivalent to

7" Tie-Back Assy Weight; POOH to 1825 m to avoid being stuck in CMT, Flush Strg; Cont. POOH W/ Setting Tools to 1730 m, Circ. BTM's up, L/D CMT Manifold & Other Eqp. , NL-NG.To 2166.5m; Release Setting Tools and POOH to 2032m (2 m above New 7" L.LAP) to confirm Dogs are clear F/ Tie-Back Sleeve.Cont. POOH W/ Setting Tools 1730 To 1241m, While L/D 5 Stds Extra 5" DPs, L/D CMT Manifold and Circ. C.W.H, NL-NG.Set Wear Bushing; P/U & M/U 8-3/8" D/O BHA including: [8-3/8" Tri-Cone Bit (K.Dream, IADC: 537, S/N: 2417584JH, Used,1.1.WT.A.E.I.NO.BHA, 3*18/32") + 4-3/4" Bit sub (float-in) + 2 Stds 6-1/2" DC + 10 Stds 5" HWDP] and RIH to 332m, F/U BHA & Break Circ. NL-NG.Cont. RIH W/ 8-3/8" D/O BHA F/ 332 To 1845m On Elevator Followed by 5" DPs, While F/U Strg & Break Circ. at 10-Std intervals, NL-NG.Conn. TDS & Cont. RIH W/ 8-3/8" D/O BHA F/ 1845 To1990m W/ Wash Dn, NL-NG.CBU @ 1990m To Condition Mud, NL-NG.Cont. RIH W/ 8-3/8" D/O BHA F/ 1990 To 2007m W/ Wash Dn W/ Applying Parameters: [WOB: 10klbf, F.R: 350GPM, SPP: 750psi] to conduct CMT Hardness Test; CMT confirmed Hard @ 2007m per criteria W/ No Bit/Nozzle Penetration and Stable Parameters, NL-NG.

D/O Medium to Hard CMT W/ 8-3/8" D/O BHA F/ 2007 To 2034.5m W/ Applying Parameters: [WOB: 5-10 klbf, Rot. : 30 RPM, TQ: 1-3 klbf.ft, F.R: 350GPM, SPP: 900psi], NL-NG.Pump 40bbl Hi-Vis Pill and CBU @ 2034.5m till Shakering out the pumped Hi-Vis Pill, Confirm Sh.Shaker cleaning, NL-NG.POOH 8-3/8" D/O BHA F/ 2034.5m To Surface On Elevator, L/D 8-3/8" Bit W/ Same Condition & Rest of BHA, While Circ. C.W.H, NL-NG.P/U & M/U 6-1/8" D/O BHA including: [6-1/8" Tri-Cone Bit (K.Dream, IADC: 537, S/N: 2304674JH, Used, Open, 2.3.WT.A.E.I.BT.BHA)Cont. RIH W/ 6-1/8" D/O BHA F/ 249 To 1970m On Elevator Followed by 3-1/2 & 5" DPs, While F/U Strg & Break Circ. at 10-Std intervals, NL-NG. + 4-3/4" Bit sub (float-in) + 9 Stds 3-1/2" HWDP] and RIH to 249m, F/U BHA & Break Circ. , NL-NG.Conn. TDS & Cont. RIH W/ 6-1/8" D/O BHA F/1970 To 2034.5m W/ Wash Dn, Tag P.O.B @ 2036.5m, NL-NG.D/O P.O.B F/ 2036.5 To 2038.10m W/ Applying Parameters: [WOB: 6-15klbf, Rot. : 30-50RPM, TQ: 2-5klbf.ft, F.R: 100-300gpm, SPP: 250-1360psi], While D/O CMT Inside 7" Tie-Back PBR and Pack of Bushing is in progress, NL-NG.

Cont. D/O Pack of Bushing W/ 6-1/8" D/O BHA To 2038.28m W/ Applying Parameters: [WOB: 6-15klbf, Rot. : 30-50RPM, TQ: 1-3klbf.ft, F.R: 100-300gpm, SPP: 250-1360psi], While Dress & Smooth Pack of Bushing Interval, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 2038.28 To 2123m W/ Wash Dn, NL-NG.D/O Medium to Hard CMT W/ 6-1/8" D/O BHA F/ 2123 To 2178m W/ Applying Parameters: [WOB: 6-17klbf, Rot. : 30-70RPM, TQ: 2-5klbf.ft, F.R: 100-300gpm, SPP: 250-1360psi], While D/O CMT Inside 7" Tie-Back LNR, Wiper Plug & Pump Down Plug, LDC, Dress & Smooth LDC

Interval, NL-NG.Pump 30bbl Hi-Vis Pill & CBU @ 2178m Till Shakering out the pumped Hi-Vis Pill, NL-NG.Cont. RIH W/ 6-1/8" D/O BHA F/ 2178 To 2637m On Elevator Followed By 5" DPs, While F/U Strg & Break Circ. At 10-Std Interval, NL-NG.

Cont. RIH W/ 6-1/8" D/O BHA F/ 2673 To 3593m (5" L.Lap) On Elevator Followed By 5" DPs, While F/U Strg & Break Circ. At 10-Std Interval, NL-NG.Pump 40bbl Hi-Vis Pill & CBU @ 3593m Till Shakering out the pumped Hi-Vis Pill, NL-NG.POOH 6-1/8" D/O BHA F/ 3593m To Surface On Elevator, L/D 6-1/8" Tri-Cone Bit [2.3.WT.A.E.I.BT.BHA] & Rest of BHA, While Circ. C.W.H, NL-NG.P/U & M/U 3-3/4" Clean out BHA including: [3-3/4" Mill (T.S.E.KH, 5*10/32" NZL Port, New) + 3-1/8" Bit Sub + 7 Stds 3-1/8" DCs +5 Stds 2-7/8" DPs] and RIH To 336m, F/U BHA & Break Circ. , NL-NG.Cont. RIH W/ 3-3/4" Clean out BHA F/ 336 To 1028m Followed by 3-1/2" DPs On Elevator, While F/U Strg & Break Circ.

Cont. RIH W/ 3-3/4" Clean out BHA F/ 1028 To 3593.5m (5" L.Lap) Followed by 3-1/2" & 5" DPsOn Elevator, While F/U Strg & Break Circ. At 10-Stds Interval, NL-NG.Conn. TDS & Cont. RIH W/ 3-3/4" Clean out BHA W/ Wash Dn F/ 3593.5 To 3876m, NL-NG.Pump 40bbl Hi-Vis Pill & CBU @ 3876m (5" F.Collar Depth) Till Shakering out the pumped Hi-Vis Pill, NL-NG.POOH 3-3/4" Clean out BHA F/ 3876 To 1320m On Elevator, While Circ. C.W.H, NL-NG.

Cont. POOH 3-3/4" Clean out BHA F/ 1320m To Surface On Elevator, While Circ. C.W.H, NL-NG.Retrieve 11" Wear Bushing; Change 13-5/8" 10K Top Rams F/ 2-7/8" × 5" VBR To 4-1/2" × 7" VBR; Pressure Test on Changed Rams, OK;L/D Mousehole & R/U and Set 7" Shooting Nipple; P/U & Make Up Wireline BOP on Shooting Nipple, Perform Wireline BOP Test, OK; PJSM Conducted; R/U Surface Wireline Tools, P/U & Ass. Wireline Logging Tool String as SBT-VDL-GR-CCL (Total Length: 16.42 m, Total Weight: 236.5 kg, Max OD: 92 mm) For Cement Bond Evaluation of 5" LNR and RIH W/ Wireline Logging Tool String To 3880 m, While Record Normal Tension Every 500m, While Circ. C.W.H, NL-NG.Commence Data Acquisition Logging Up F/ 3875 To 3545m to Fully Cover Logging Interval; Logging Up in Interval 3850 To 3745mwas repeated based on Client’s Request for Verification; POOH Wireline Logging Tool String To Surface, R/D Surface SeaLand Wireline Tools Eqp. & 5" Shooting Nipple; R/U Mouse Hole, Set 11" Wear Bushing, While Circ. C.W.H & Monitor the Well, NL-NG.P/U & M/U 9-5/8" Scraper BHA including: [8-3/8" TCI Bit (K.Dream, IADC: 537, S/N: 2417584JH, Used, Open, D.G: 1.1.WT.A.E.I.NO.BHA) 6-1/2" Bit sub (float-in) + 9-5/8" Scraper + 1Std 6-1/2" DC + 2Stds 5" HWDP] and RIH to 86m, F/U BHA & Break

Circ. , NL-NG.Cont. RIH W/ 9-5/8" Scraper BHA F/ 86 To 2034m Followed 5" DPs, While F/U Strg & Break Circ. At 10-Std intervals, NL-NG.Scraping Passes On 9-5/8" Dry Test PKR Setting Interval (1980-2034m); Achieve Full ID Contact W/ Scraper Blades, NL/NG.Pump 40bbl Hi-Vis Pill @ 2021m, CBU; Shakering out Pumped Hi-Vis Pill confirmed, NL-NG.

POOH 9-5/8"Scraper BHA F/ 2021 To Surf. L/D 9-5/8" Scraper & 8-3/8" Insert Bit W/Same Cond. While Circ. C.W.H, NL-NG.Remove W.Bushing, Bit Dull Cond. (1.1.WT.A.E.I.NO.BHA).P/U & M/U 9-5/8"Dry Test Tool String including: Bottom B.T (First Memory Gauge) + Anchor pipe + X.O.S 3 1/2" IF Box x 3 1/2" FH Pin + X.O.S 4-1/2" IF Box x 3 1/2" IF Pin + Middle Packer element + 9-5/8" Above Packer + X.O.S 3-1/2" IF Box *4-1/2" IF PIN + X.O.S 3-1/2" FH Box x 3-1/2" IF PIN + RH Release Safety Joint + Hydraulic JAR + Middle B.T (Second Memory Gauge) + Hydro-spring + D.C.I.P + X.O.S 4-1/2" IF Box x 3-1/2" IF Pin +1 Jt 5" Drill Pipe + Reverse Sub and RIH to 23.5m, While Monitor the Well, W/ NL-NG.Cont. RIH W/ 9-5/8"Dry Test Tool String On Elevator Followed by 4 Stds 6-1/2 DCs + 2Stds 5" HWDP & 5"DPs To 2015m.W/ Speed Control at the request of OEOC Dry Test Supervisor, While Pass Rabbit Thru. all Tubular and F/U 732.7m of Strg W/ Drill water R/U and prepare Chicksan pipes and DST choke manifold, Pressure test lines to 2500 psi for 15 minutes, Ok. Record Strg upward and (62.4 pcf) as a water Cushion at 5-Std intervals, Change TDS Links, NL-NG.Downward. Set PKR and Open Hydro-Spring Valve: Rotate Strg 8 full turns clockwise, Apply set-down Wt. to set the 9-5/8" Dry TestPKR at 2015m, Obs. Hydro-Spring Valve opening indication and Well opened Thru. Hydro-Spring Valve. .

Open Period Monitoring: start time of Open period from 00:00 AM to 03:00 AM, No Bubbles observed during the monitoring period.Confirm Annulus fluid level is Static during observation, NL-NG.Close DCIP and monitor the well for 6 hrs, No Bubbles observed during the monitoring period & Annulus fluid level is Static.Drop bar, Revers Circ Mud and Get 42 BBL D.Water , Unset PKR, Direct Circ Mud to Balance MW (84PCF).Start POOH 9-5/8" Dry Test Tool String To Surface On Elevator W/ Speed Control at the request of OEOC Dry Test supervisor .

L/D Dry Test Tool String3Hrs. Open-Period Monitoring Results: [Middle B.T: 1132 - 1139psi, BTM B.T: 1158-1161psi];6Hrs. Close-Period Monitoring Results: [Middle B.T: 1140-1321psi, BTM B.T: 1162-1344psi]; While Circ. C.W.H, NL-NG.P/U & RIH With 3-3/4" M.M.J.Mill (T.S.E.KH, NZL Port : 5*10/32") + 3 1/8" B.sub + 7 STDs 3 1/8" DC + 5 STDs 2-7/8" DP & Follow by 3 1/2" & 5" DP to 3876m (5" F.Coller) While Break Circ Mud W/NL.NG.Circ BTM's Up .Spot 26BBL Brine.

Cont Spot 26BBL Brine (CaCl2, 84pcf)Strat POOH from 3876m to 2240 m While Circ. C.W.H, NL-NG.Slip & Cut DRLG Line.Cont POOH from 2240 to 1895mWait on Client to Receive Explosive Material while Slow Circ mud.Cont. Wait on Client to Receive Explosive Material while Cont POOH from 1895m to 595m W/NL.NG .

Cont. Wait on Client to Receive Explosive Material while Cont POOH from 595m to Surf W/NL.NG.Cont. Wait on Client to Receive Explosive Material while Slow Circ C.W.H .

Cont. Wait on OEOC to Receive TDS while Slow Circ C.W.H , Recived TDS @ 15:00 O'Clock, R/U & Install TDS.R/U Wireline as program:Run#1 (Dummy Run) : 2 No. 2-7/8" B.Gun + CCL to 3872m, POOH to Surface & L/D Wrieline Tools.Wait on Daylight.

Wait on Daylight.R/U Wireline, Held PJSM For All Crew & Perforating Operation as program:Run#1 (Perforation Run) : Armed Gun W/ 119 Bullets (Net Length: 6m) & RIH with wireline tool (CCL + Loaded Gun) To Shoot Pisition (3859~3865m) and Shoot bullet, OK. POOH to surface.Run#2 (Perforation Run) : Armed Gun W/ 119 Bullets (Net Length: 6m) & RIH with wireline tool (CCL + Loaded Gun) To Shoot Run#3 (Perforation Run) : Armed Gun W/ 60 Bullets (Net Length: 3m) & RIH with wireline tool (CCL + Loaded Gun) To Shoot Pisition (3849~3852m) and Shoot bullet, OK. POOH to surface.Pisition (3853~3859m) and Shoot bullet, OK. POOH to surface.Wait on Daylight.

Wait on Daylight.R/U Wireline, Held PJSM For All Crew & Perforating Operation as program:Run#4 (Perforation Run) : Armed Gun W/ 85 Bullets (Net Length: 4.30m) & RIH with wireline tool (CCL + Loaded Gun) To Shoot Pisition (3842~3846.3m) and Shoot bullet, OK. POOH to surface & R/D Wireline Tools.L/D Shooting Nipple, Install Mouse Hole,M/U 3-1/2" P.J On Completion Tools/ Change Top Rams to 2-78" * 5" variable & Test it , OK.P/U & RIH with 3-3/4" Clean out BHA including : (3-3/4" M.M.J.Mill + 7 STD 3-1/8" D.C + 5 STD 2-7/8" D.P) to 338m .Install Wear bushing.

Cont RIH with 3-3/4" Clean out BHA including : (3-3/4" M.M.J.Mill + 7 STD 3-1/8" D.C + 5 STD 2-7/8" D.P) & Follow by 3-1/2" & 5" D.P To 3593m (5" L.Lap) With Break Circ Each 15 STD W/Nl.NG.4 Hrs Waiting For OEOC Rig 201 Duo to Delay in RIH Operation.Cont. RIH from 3593m to 3876m (5" F.Coller) with Pump Down & RPM and Check String Upward & Downward, OK.Circ. BTM's UP .

Cont. Circ BTM's UP & Spot 20 BBL Non Solid (Cacl2, 84 PCF).POOH On Elavator from 3876m to 335m while fill up the well W/NL.NG.Cont POOH from 335 to 35m

while L/D 5 STD's 2-7/8" D.P & 6 STD's 3-1/8" D.C (Jts by Jts) and fill up the well, NL.NG. .

Cont POOH from 35 to Surface while L/D 3-3/4" M.M.J.Mill & 1 Stand's 3-1/8" D.C (Jts by Jts) and fill up the well, NL.NG.RIH with 8-3/8" Bit + Bit Sub + 5 STD 6-1/2" D.C + 5 STD 5" H.W.D.P to 264m For L/D Useless Tubular in Derrick.POOH On Elavator from 264m to 100m while L/D 5 STD 5" H.W.D.P & 5 STD 6-1/2" D.C (Jts by Jts) and fill up the well, NL.NG.RIH with 6 STD 4-3/4" D.C + 7 STD 3-1/2" H.W.D.P to 346m For L/D Useless Tubular in Derrick.POOH On Elavator from 346m to Surface while L/D 6 STD 4-3/4" D.C + 7 STD 3-1/2" H.W.D.P (Jts by Jts) and fill up the well, NL.NG.Retrieve Wear Bushing & Change Elevator.P/U and Run in hole with 7" Scraper BHA including : 5-7/8" B.Bit + 7" Scraper + Bit Sub (Float in) + 2 STD 3 1/2" HWDP & Follow by3 1/2" D.P to 1240m While fill Up string Each 15 STD, W/NL.NG. .

Cont. Run in hole on Elevator with 7" Scraper BHA & Follow by 3-1/2" & 5" D.P to 2330m While fill Up string Each 15 STD, W/NL.NG.Perform Scrap PKR Depth from 2330m to 2450m Each STD Several time.Cont Run in hole on Elevator from 2450m to 3562m While fill Up string Each 15 STD & Cont RIH from 3562m to 3592m with Wash downPumping 30BBL Hi.Vis Pill, Circ Btm's up and Shaker out Hi.Vis Pill. Pump 50BBL Hi.Vis Pill as Spacer. Disp whole well With 650BBl (84Pcf , Non solid Comp. Fluid) and Got 50BBL contaminated with mud Close IBOP and Flow Check the well for 1hrs, Static.Start POOH with 7" Scraper from 3592m to 2932m while L/D 5" D.P (Jts by Jts) .

Cont POOH with 7" Scraper to Surf meanwhile L/D All Tublur in Derrick in Progress (Jts by Jts) .R/U NDCO LNR Running Equip.Held PJSM, Run in hole w/ 7" Comp. Strg as Below:P/U & M/U 3 1/2" Wireline Re-Entry Guide Shoe (10.2#,, ID: 2.922") + 3 1/2" BTM NO-GO L/N (10.2#, Seal Bore: 2.75", XN Profile) + 1 Jt3 1/2" TBG. P/U & M/U 7" Hydraulic Set Retrievable PKR (Min ID: 2.922", 29#) + 1 Jt 3 1/2" TBG. Run 2.8" Gauge Ring to NO-GO Depth, OK. Cont. RIH w/ 3 1/2" Pup Jt + 3 1/2" SSD (S.Bore: 2.75", X profile, Close position, Downward open) + 3 1/2" Pup Jt + 1 Jt 3 1/2" TBG + 3 1/2" Pup Jt + 3 1/2" Traveling Jt (full open position, Dressed w/ 3 No. Shear Pin, Splined Type) + 3 1/2" Pup Jt + 1 Jt 3 1/2" TBG + 3 1/2" Pup Jt + 3 1/2" CIV#1 & Tubing retrievable CIM (10 2#, Dual Check Valve, WP: 15K psi) + 3 1/2" Pup Jt + 1 Jt 3 1/2" TBG + P/U & Install CIL #1,2 in spooler machine & Install Pulley in monkey board. Pass CILs f/ pulley. 3 1/2" Pup Jt + 3 1/2" CIV#2 & Tubing retrievable CIM (10 2#, Dual Check Valve, WP: 15K psi) + 3 1/2" Pup Jt + 1 Jt 3-1/2" TBG.R/U Slick Line

equipment. Run 2.8" Gauge Ring to top of SSD: OK. R/D Slick line tools. Press test, surface test line w/ 7500 psi, Ok. Line up surface test Line to string. Perform Press test Comp. String for SSD Check valve @ 85m w/ 6000 psi, OK.Connected CIL 1#2 to CIM1#2 and Perssure test same with 2000Psi and Hold Preesure 800-1000Psi during Run In Hole.Cont Run in hole with 5 Jts 3 1/2" TBG (10.2#, L-80, HSM3)(Totally 11 Jts) to 130m and used 3-1/2" Cross Coupling as Per Program. .

Cont. RIH Comp. Strg W/ 29Jts 3-1/2" TBG [10.2#, L-80,HSM3] & 1Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 47Jts) F/ 130 To 474m, While Clean & Wash all Connections; use Thread Seal Compound, and Torque/Turn Monitoring System; secure CILs UsingCross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.R/U Slick Line Tools, P/U & Assemble 2.80" Guage Ring, RIH W/ Same Tool String to Top of SSD (Max ID: 2.750"), Ok;POOH to surface and R/D Slick Line Eqp. , While Circ. C.W.H by Trip Tank, NL-NG.R/U CMT Unit and Connect Chiksan pipes to Circ. Swage, Perform Comp. Strg Press. Test at 474m W/ 6000psi, 15min, Ok. Cont. RIH Comp. Strg W/ 88 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 135Jts) F/ 474 To 1300m, While Clean & Wash all Connections; use Thread Seal Compound, and Torque/Turn Monitoring System; secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Cont. RIH Comp. Strg W/ 11Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 146Jts) F/ 1300 To 1413m, While Clean & Wash all Connections; use Thread Seal Compound, and Torque/Turn Monitoring System; secure CILs Using Cross Coupling Cable Protectors & Hold Pressurein both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.R/U CMT Unit and Connect Chiksan pipes to Circ. Swage, Perform Comp. Strg Press. Test at 1413m W/ 6000psi, 15min, Ok. Cont. RIH W/ 7"Comp. Strg W/ 167 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 213 Jts) F/ 1413 To 2050m; Obs. Hold up Comp. Strg Weight@ 2050m, Attempt to Pass This Point, No Success, Decide to POOH Comp. Strg to surface and Check the same, While Clean & Wash Connections; use Thread Seal Compound, and Torque/Turn Monitoring System; secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.by Trip Tank & Monitor the Well, NL-NG.R/U Slickline Eqp. , RIH W/ 2.750" SB To 2025m; Retrieve Check Valve, POOH Slickline Tool String, L/D Slickline Eqp. , While Circ. C.W.H POOH Comp. Strg F/ 2050 To 2004m, While L/D TBGs Jt by Jt & Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Cont. POOH Comp. Strg F/ 2004 To 340m, While L/D TBGs Jt by Jt & Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Cont. POOH Comp. Strg F/ 340m To Surface, While L/D TBGs Jt by Jt & Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.R/U Surface Slickline Tools, Install 7" Shooting Nipple; P/U & Assemble 6.100" Gauge Ring Tool String and RIH To 7" L.Lap Depth,Attempt to Pass 7" L.Lap, No Success; POOH Slickline Tool String To Surface; R/D Slickline Tools & Shooting Nipple, NL-NG.P/U & M/U 6-1/8" Clean out BHA including: [6-1/8 Concave Junk Mill (New, T.S.E.K.C, S/N: 763, 4No. NZL Port) + 4-3/4" B.Sub + 9Stds 3-1/2" HWDP] and RIH W/ Same BHA Followed by 3-1/2" & 5" DPs Jt by Jt To 941m, While Break Circ. At 700m-intervals, NL-NG.

Cont. RIH W/ 6-1/8" Clean out BHA F/ 941 To 2600m Followed by 3-1/2" & 5" DPs Jt by Jt To 941m, While Smooth Interval 2037-2038m (7" Tie-Back L.Lap); Check 7" LDC Interval & Previous 7" L.Lap W/ & W/O Parameters; Break Circ. At 700m-intervals, NL-NG.POOH 6-1/8" Clean out BHA F/ 2600 To 2177m On Elevator, While L/D All Extra Tubular Jt by Jt and Circ. C.W.H Thru. T.Tank, NL-NG.

Cont. POOH 6-1/8" Clean out BHA F/ 2177m To Surface On Elevator, While L/D6-1/8" Concave Junk Mill & All Extra Tubular Jt by Jt and Circ. C.W.H Thru. T.Tank, NL-NG.Ret. Wear Bushing and Prepare Rig Floor To Run 7.5k Comp. Strg; R/U NDCO LNR Running Equip. , While C.W.H Thru. T.Tank, NL-NG.Held PJSM, RIH W/ 7" 7.5k Comp. Strg as follows:3-1/2" Wireline Re-Entry Guide Shoe (10.2#, Id: 2.922") + 3-1/2" Bottom No-Go L/N (10.2#, Seal Bore: 2.75", Xn Profile) + 1 Joint 3-1/2" TBG,7" Hydraulic Set Retrievable Packer (Min Id: 2.922", 29#) + 1 Joint 3-1/2" TBG + 3-1/2" Pup Jt + 3-1/2" SSD (S.Bore: 2.75", X profile, Close position, Downward open) + 3-1/2" Pup Jt; Run 2.8" Gauge Ring to No-Go Depth, Ok; Cont. RIH 7.5k Comp. Strg. as follows:1 Jt 3-1/2" TBG + 3-1/2" Pup Jt + 3-1/2" Traveling Jt (Full Open Position, Dressed w/ 3 No. Shear Pin, Splined Type) + 3-1/2" Pup Jt + 1 Jt 3-1/2" TBG + 3-1/2" Pup Jt + 3-1/2" CIV#1 & Tubing Retrievable CIM (10 2#, Dual Check Valve, WP: 15K psi) + 3-1/2" Pup Jt + 1 Jt 3-1/2" TBG + 3-1/2" Pup Jt + 3-1/2" CIV#2 & Tubing Retrievable CIM (10 2#, Dual Check Valve, WP: 15K psi) + 3-1/2" Pup Jt , While C.W.H Thru. T.Tank, NL-NG.

R/U Slickline Equipment. Run 2.8" Gauge Ring to Top of SSD: Ok. R/D Slickline Tools.Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strgagainst SSD Check Valve @ 85m W/ 6000 Psi, Ok, L/D Chicksan Pipe.Install Pulley in Monkey Board, Pass CILs F/ Pulley; Connect

CIL #1,2 to CIM #1,2 and Press. Test Same W/ 2000 Psi, Both Ok.Cont. RIH 7.5k Comp. Strg W/ 39Jts 3-1/2" TBG [10.2#, L-80,HSM3] & 2 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 52 Jts) F/ 85 To 455m, Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. StrgWhile Clean & Wash all Connections; Use Thread Seal Compound, and Torque/Turn Monitoring System; Secure CILs Usingagainst SSD Check Valve @ 455m W/ 6000 Psi, Ok, L/D Chicksan Pipe.Cont. RIH 7.5k Comp. Strg W/ 67 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 111 Jts) F/ 455 To 1070m, While Clean & Wash all Connections; Use Thread Seal Compound, and Torque/Turn Monitoring System; Secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strgagainst SSD Check Valve @ 1070m W/ 6000 Psi, Ok, L/D Chicksan Pipe.Cont. RIH 7.5k Comp. Strg W/ 5 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally:116 Jts) F/ 1070 To 1138m, While Clean & Wash all Connections; Use Thread Seal Compound, and Torque/Turn Monitoring System; Secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Cont. RIH 7.5k Comp. Strg W/ 59 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 175 Jts) F/ 1138 To 1689m, While Clean & Wash all Connections; Use Thread Seal Compound, and Torque/Turn Monitoring System; Secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strgagainst SSD Check Valve @ 1689m W/ 6000 Psi / 15min, Ok, L/D Chiksan Pipe.Cont. RIH 7.5k Comp. Strg W/ 65 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 240 Jts) F/ 1689 To 2308m, While Clean & Wash all Connections; Use Thread Seal Compound, and Torque/Turn Monitoring System; Secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strgagainst SSD Check Valve @ 2308m W/ 6000 Psi / 15min, Ok, L/D Chiksan Pipe.Cont. RIH 7.5k Comp. Strg W/ 4-1/2" Pup Jt [HSM3 ,18.9#, L-80, Type-1] + 4-1/2" Flow Coupling [18.9#, 9CR1MO, HSM3, 4 ft, WEIQIXIN Co.] +4-1/2" TRSSV Tubing Retrievable Safety Valve [18.9# w/ 3.437" Seal bore, HSM3, 9CR1MO, 7.5K WP w/ AF Profile, Flapper Type] +4-1/2" Flow Coupling [18.9#, 9CR1MO, HSM3, 6 ft, WEIQIXIN Co.] + 4-1/2" Pup Jt [HSM3 ,18.9#, L-80, Type-1] +1 Jt 4-1/2" TBG

[18.9#, L-80,HSM3] To 2325m, While Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.Flush & Conn. 1/4" CL To TRSSV CL Port, Press. Test Conn. @ 6000psi / 15min, Ok, While Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.

Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strgagainst SSD Check Valve @ 2325m W/ 6000 Psi / 15min, Ok; TRSSV closed; Comp. Strg bled down to 1000 psi for Inflow Test; Pressure stabilized @ 1000 psi / 15 min; No pressure build-up observed.Cont. RIH 7.5k Comp. Strg W/ 4 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 245 Jts) F/ 2325 To 2363m, While Clean & Wash all Connections; Use Thread Seal Compound, and Torque/Turn Monitoring System; Secure CILs Using Cross Coupling Cable Protectors & Hold Pressure in both CILs, and Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.P/U & M/U 4-1/2" Fluted Swage Adapter [D/P, 18.9# TPCQ-EX Pin on top X HSM3 Pin on down, 9CR1MO, WEIQIXIN Co.] + TBG HGR [MSP/Drilex, 7.5K, 11" X 4 1/2" ACME Box up X 4 1/2" TPCQ-EX Box Down L-80 18.9#, M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type "H" Two Way (Min Bore: 3.68")] + TBG HGR Running Tool + Landing Joint, While Pass Drift Thru. all Eqp.Pressure Test Surface Test Line & Chiksan Pipes, Ok; L/U Surface Test Line to Strg; Perform Press. Test Comp. Strgagainst SSD Check Valve @ 2374m W/ 6000 Psi / 15min, Ok, L/D Chiksan Pipe; Pressure Test 1/4" CL & 3/8" CILs; Pressure up CILs to rupture CIV disk @ 6000-8000psi; Bleed off CL & CILs; Cut lines to Rig Floor and wrap on Fluted Swage below TBG HGR; Route Lines Thru. TBG HGR; Install plugs on CL & CILs; Tag 1st & 2nd CILs; Secure and mark lines on Landing Joint;Verify TBG HGR orientation with X-Tree; Clean and prepare Tubing Spool; Open T.H.S outlets and ensure tie-down screws backed out.P/U & M/U G.FLG + 4-1/16" 10K Gate Valve + Slickline BOP + Lubricator & BOP Panel; Test BOP, Ok; R/D Mouse Hole; R/U Surface Slickline Tools and perform Slickline Job as follows:Run#1 P/U & Assemble AF Running Tool for TRSSSV Protection Sleeve; RIH W/ 3.437" Protection Sleeve; Set in position; POOH To surface.Cont. Slickline Job as follows:Run#2 P/U & Assemble SB Running & Pulling; RIH W/ Same Tool String and Ret. Check valve F/ SSD; POOH To Surface, Run#3 P/U & Assemble Running Tool for Blanking Plug in Landing Nipple; RIH W/ 2.750" Blanking Plug To 2375m, While Work on Setting Plug in Landing Nipple, Slickline Tension got dropped; POOH To Surface, Obs. 2.75" Plug + SB Running + Mechanical Jar +1-7/8" Rope socket + 1280ft Slickline left in the Comp. Strg.Run#4 P/U & M/U 2.6" Impression Block and RIH To 2375m (No-Go Depth); Attempt To make Impression, POOH To surface, Obs. Impression of Fish.Run#5 P/U & M/U Slickline Grapple Assembly and RIH W/ 2.75" Grapple To 2375m; Engage Fish; POOH To surface, Fish not recovered.Run#6 P/U & Assemble GS Pulling and Retrieve 3.437" Protection Sleeve F/ TRSSV; POOH To Surface.Run#7 P/U

& Assemble 3.3" Gauge Ring To 3-1/2" * 4-1/2" X.O.S, Ok; POOH To Surface.Run#8 P/U & M/U Slickline Grapple Assembly and RIH W/ 2.8" Grapple To 2375m; Engage Fish; POOH To surface To Check, Fish not recovered.Run#9 P/U & M/U Slickline Grapple Assembly and RIH W/ 2.9" Grapple To 2375m; Engage Fish; POOH To surface To Checkin progress @ M.N.

Cont. Slickline Job as follows:Cont. POOH Slickline Grapple Assembly To Surface, All Slickline Assy recovered successfully but 2.750" Blanking Plug,L/D Slickline Tools Strg; Cut 600ft of Slickline; Cont. Slickline Job as follows:P/U & Assemble AF Running Tool for TRSSSV Protection Sleeve; RIH W/ 3.437" Protection Sleeve; Set in position; POOH To surface.P/U & Assemble GS Pulling and Retrieve 2.750" Blanking Plug To Check that; POOH To Surface.P/U & Assemble Running Tool for Blanking Plug in Landing Nipple; RIH W/ 2.750" Blanking Plug & Set in No-Go; POOH To Surface.P/U & Assemble SB Running & Pulling for Equalizing Prong match W/ 2.750" Plug of No-Go; RIH W/ Equalizing Prong & Set in Position; P/U & Assemble 2.8" Gauge Ring To Top of SSD, Ok; POOH To Surface.P/U & Assemble Shifting Tool to confirm SSD is full close; RIH W/ 2.75" Shifting Tool To SSD Depth (2349.2M), Confirm SSD closed; POOH To Surface.L/U Test Line On Strg & Press Test Same To 6000psi, Ok; Set PKR as follows:Press. Test Surface Test Line & Chiksan Pipes @ 6,000 Psi / 5–10 Min – Ok; L/U Surface Test Line to Comp. Strg;PKR Set: Pressurize Comp. Strg to confirm Traveling Joint Fully Open; Stepwise Pressurization to set PKR @ 2362m; Press. Test Comp. Strg: Increase To 6,000 Psi – Test Comp. String Ok; Comp. Strg Pull Test: Over Pull String 15 klbf – PKR Pull Test Ok; Shearing Expansion Joint: Slack-Off 20 klbf – Shear Expansion Joint Ok;Land TBG HGR In THS: Circulate Fresh Water Through T.H.S, Ensure Tie-Down Screws Open, Drain BOP Stack Via THS Gate Valves,Lower TBG HGR And Land On Load Shoulder – Verified By Wt. Indicator & L.Joint Mark; Tighten All Tie-Down Screws; Close Hydrill On L.Joint, Pressure Test TBG HGR and All Tie-Down Screws @ 1,000 Psi / 10 Min – Ok; L/U Surf Line,Final Press. Test: Press. Test Comp. Strg @ 6,000 Psi / 15 Min – Ok; R/D Same.P/U & Assemble AF Running Tool for TRSSSV Protection Sleeve; RIH W/ 3.437" Protection Sleeve; Set in position; POOH To surface.P/U & Assemble SB Running & Pulling for Equalizing Prong match W/ 2.750" Plug of No-Go; RIH W/ SB Pulling & Ret. Prong; POOH To Surf. ; P/U & Assemble GS Pulling and Retrieve 2.750" Blanking Plug; POOH To Surface.Press. Test PKR & HGR Seal: L/U and Conn. Chiksan Pipes To T.H.S Side outlet Valve (Ann.), Stepwise Pressurization 2,000 Psi/10 Min – HGR Seals (Bottom) & PKR Element (Top) Ok;P/U & Assemble GS Pulling Tool for TRSSSV Protection Sleeve; RIH W/ GS Pulling and Ret. TRSSV Protection Sleeve; POOH To surface.Press. Test TWCV: L/U and Conn. Chiksan Pipes To BOP Side outlet Valve, Back Off L.Joint On TH & L/D

Same; Run 2WCV and Screwin TBG HGR; Stepwise Pressurization Against Shear Rams @ 6,000 Psi/15 Min – Ok.

N/D BOP.Install TBG HGR M.M.Seal, N/U TBG Head Adaptor Integrated W/ One 4-1/16" Gate Valve, meanwhile Pass 1/4" CL & 3/8" CILs .Thru. CL & CIL Ports; Install 4-1/16" 10k Companion FLG On Tubing Head Adaptor, L/U Chiksan pipes and Test Line on Companion FLG, Press. Test M.M.Seal @ 6,000 Psi / 15 Min – Ok; Conn. 1/4" CL to Exit Block, Press. Test 1/4" CL @ 6,000 Psi / 15 Min – Ok; Press. Test Both CILs @ 2000 Psi / 15 Min – Ok; Press. Test Between Lower S – Seal & Cavity Thru. Test port @ 6,000 Psi / 15 Min – Ok; Press. Test Between Neck of HGR S – Seal & Cavity Thru. Test port @ 6,000 Psi / 15 Min – Ok;

N/UP S.block & Press. Test X-Mas Tree body @ 8,000 Psi / 15 Min – Ok; Release Rig 201 @ 1404.06.10 - 6:00 a.m.

2.3 AZNS – 075 – ST1 Well Sketch

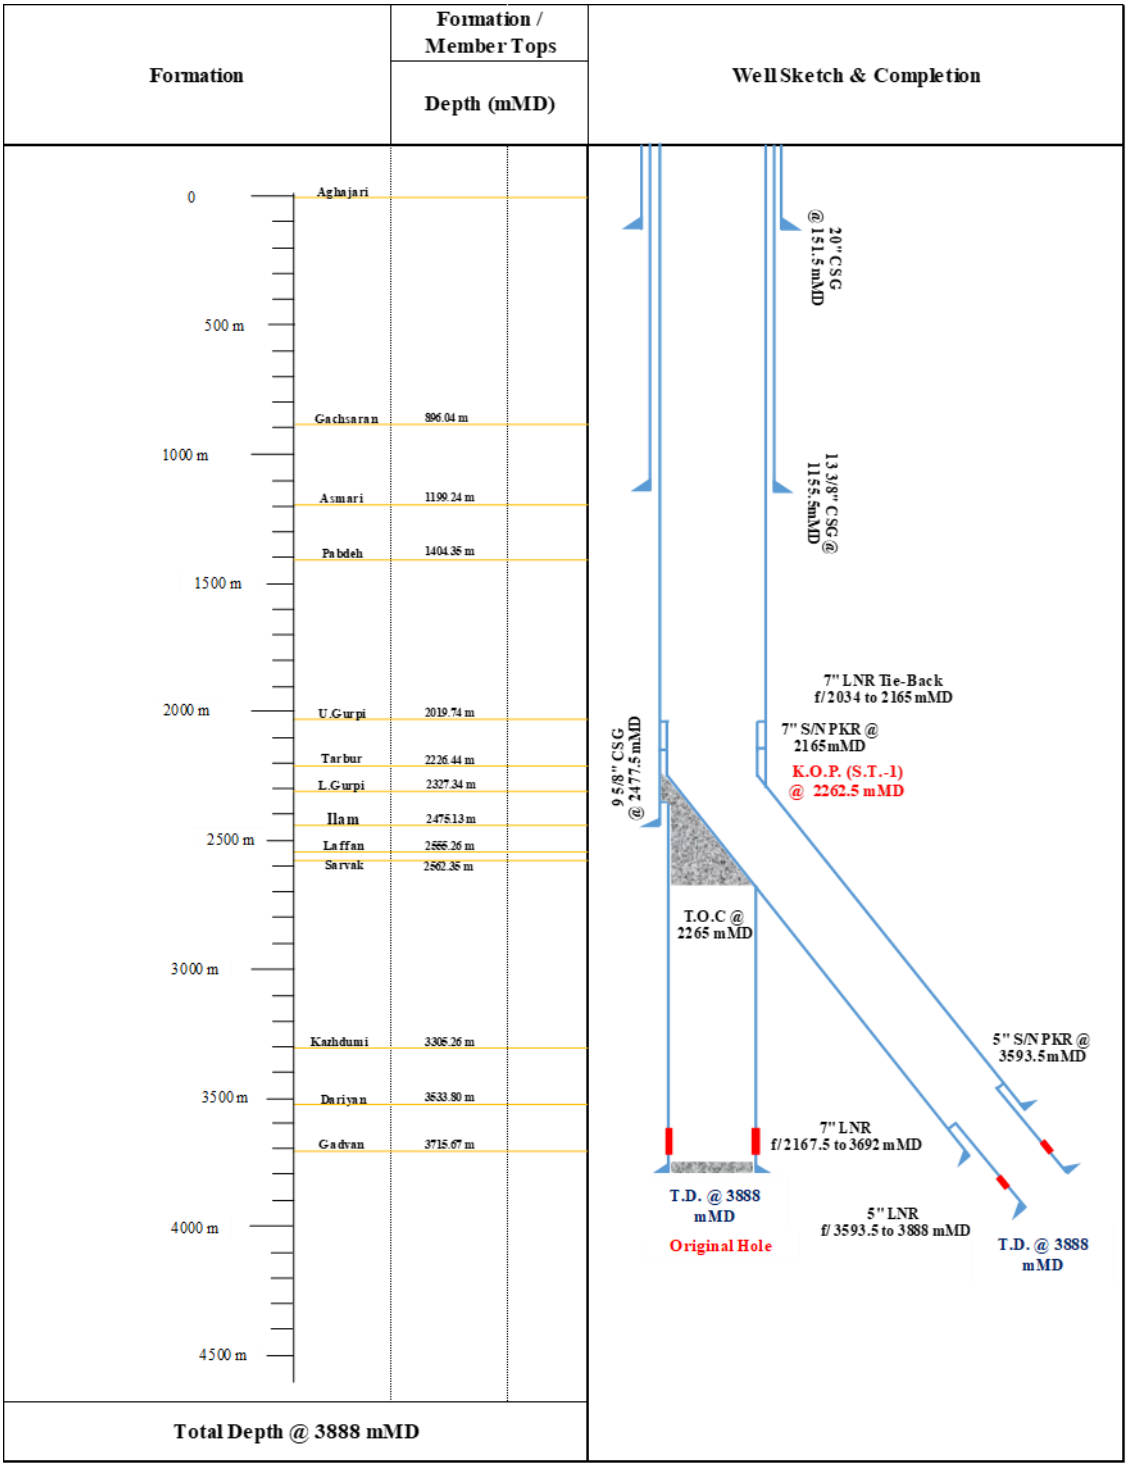


Figure 2-1: AZNS-075-ST1 Well Sketch

2.4 AZNS – 075 – ST1 Bit Data Chart

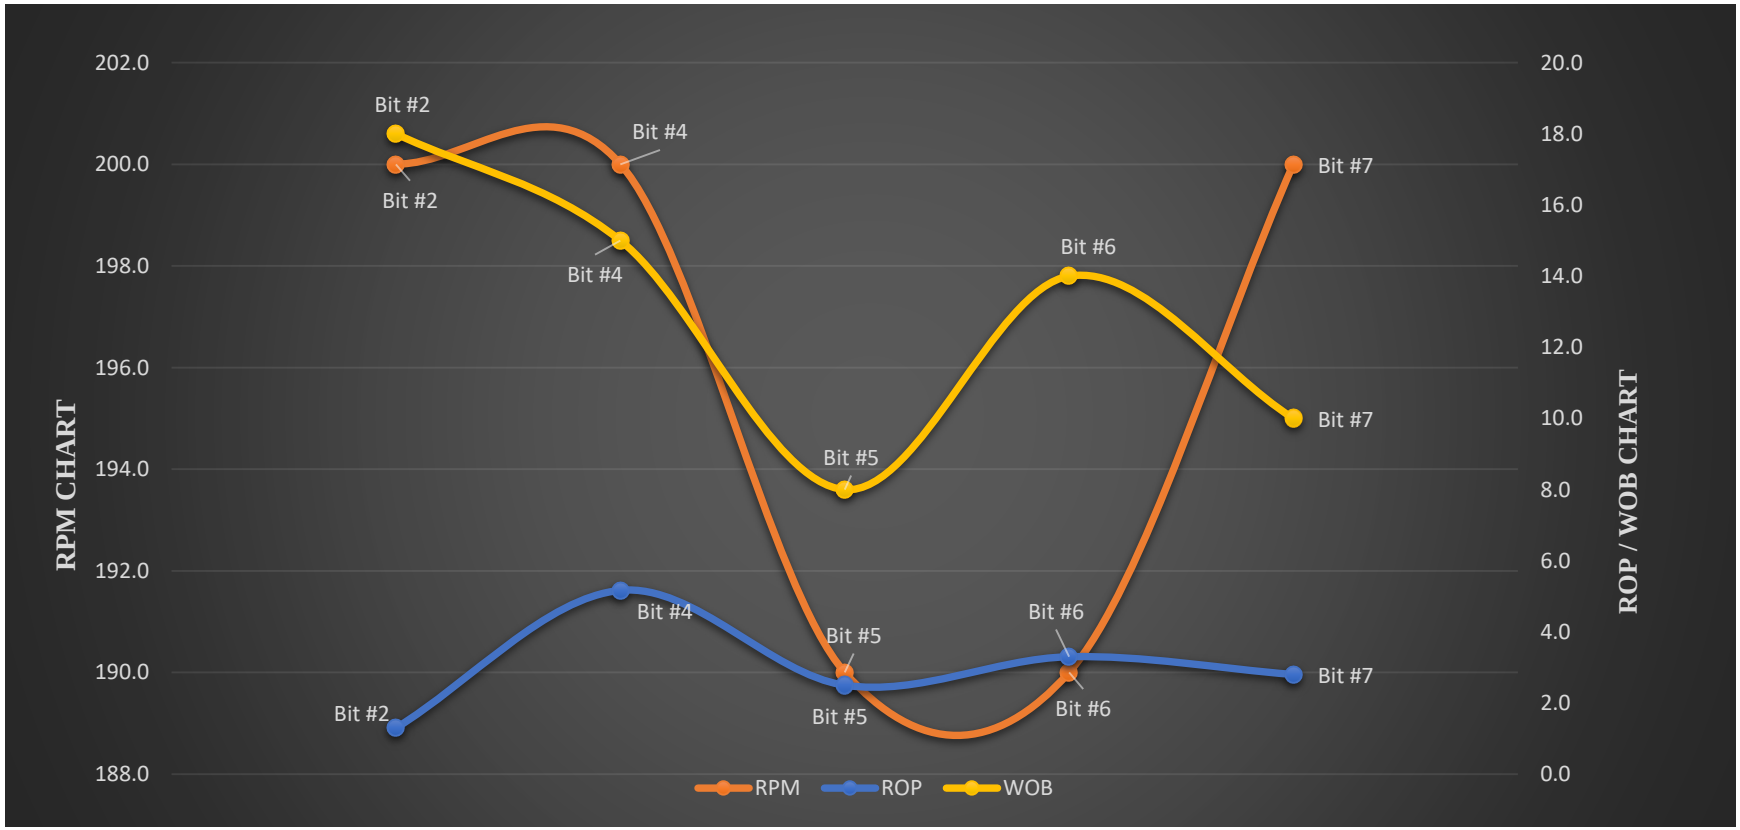


Figure 2-2: AZNS-075-ST1 Bit Data Chart

2.5 Bit Record Table

						BIT PERFORMANCE BY FORMATION								DRILLING PARAMETERS						HYDRAULICS		Dull Grading									Remarks
Bit No	Size	Bit Manufacture	Type	IADC Code	Serial No	Jets			CMT	Depth		Depth		Metres	Hrs	ROP	WOB (klb)	Surf RPM		Pump Press	GPM		Mud Weight pcf		IR	OR	DC	Loc	B/S	G/16	OC	R Pulled	
						No	x	Size		In	Out	In	Out																			
1	6"	-	B. Bit	-	-	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	84	84	-	-	-	-	-	-	-	-	Run as Scraper trip.
2	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			Yes	3107	3165	-	-	58	6.5	-	5 - 12	60	60	1900 - 2000	350	350	84	84	2	2	WT	A	E	I	BT	DTF	CMT D/O
3	8-1/2"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			Yes	2174	2270	-	-	96	13.5	-	3 - 12	30	60	550 - 650	400	450	84	84	2	2	WT	A	E	I	BT	BHA	CMT D/O
3 RR1	8-1/2"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	80	80	2	2	WT	A	E	I	BT	BHA	Run as Scraper trip.
4	8-3/8"	Kingdream	Tri-Cone Bit (HJT537G)	537	2417584JH	3	x	16	NO	-	-	2266.1	2310	43.9	8.5	5.2	12 - 18	165 PDM	35	1650 - 1680	450	450	76	76	1	1	WT	A	E	I	NO	BHA	RIH w/ Directional BHA f/ 2266.1 to 2310
5	8-3/8"	Beste	PDC(M1375)	M1375	220793	7	x	14	NO	-	-	2310	2620	310	99	3.1	6 - 18	162 PDM	35	1200 - 1500	450	450	76	76	0	1	BT	S	X	I	NO	DMF	RIH w/ Directional BHA f/ 2310 to 2620
5 RR1	8-3/8"	Beste	PDC(M1375)	M1375	220793	7	x	14	NO	-	-	2620	2884	264	108	2.4	2 - 4	0.36 PDM	35	1550 - 1800	450	450	76	76	1	1	WT	A	X	I	NO	BHA	RIH w/ Directional BHA f/ 2620 to 2884
6	8-3/8"	Beste	PDC(M1375)	M1375	220852	7	x	14	NO	-	-	2884	2979.7	95.7	31.3	3.1	1 - 15	0.36 PDM	35	2100 - 2200	500	530	76	76	2	3	WT	A	X	I	NO	BHA	RIH w/ Directional BHA f/ 2884 to 2979.7
6 RR1	8-3/8"	Beste	PDC(M1375)	M1375	220852	7	x	14	NO	-	-	2979.7	3304	324.3	93.5	3.5	10 - 28	0.29 PDM	35	2450 - 2650	480	510	76	76	3	5	BT	A	X	I	BU(5%)	BHA	RIH w/ Directional BHA f/ 2979.7 to 3304
5 RR2	8-3/8"	Beste	PDC(M1375)	M1375	220793	7	x	14	NO	-	-	3304	3594	290	117	2.5	5 - 15	0.29 PDM	40	1880 - 2500	450	500	76	76	1	1	WT	A	X	I	NO	BHA	RIH w/ Directional BHA f/ 3304 to 3594
5 RR3	8-3/8"	Beste	PDC(M1375)	M1375	220793	7	x	14	NO	-	-	3594	3692	98	48	2.0	3 - 10	0.29 PDM	40	2450 - 2650	480	500	76	76	1	1	WT	A	X	I	NO	TD	Drlg formation f/ 3594 to 3692m ad as TD.
4 RR1	8-3/8"	Kingdream	Tri-Cone Bit (HJT537G)	537	2417584JH	3	X	16	Yes	2134	2167.5	-	-	33.5	4	-	-	-	-	-	-	-	76	76	1	1	WT	A	E	I	NO	BHA	CMT D/O
4 RR2	8-3/8"	Kingdream	Tri-Cone Bit (HJT537G)	537	2417584JH	3	X	16	NO	-	-	-	-	-	-	-	-	-	-	-	-	-	76	76	1	1	WT	A	E	I	NO	BHA	Run as Scraper trip.
2 RR1	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			Yes	3617	3672	-	-	55	20.5	-	10 - 15	30	50	2500 - 2570	340	340	76	76	2	2	WT	A	E	I	BT	BHA	CMT D/O
2 RR2	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	76	76	2	2	WT	A	E	I	BT	BHA	Run as Scraper trip.
2 RR3	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			Yes	3672	3692	3692	3697	5	4	1.3	15 - 20	0.8 PDM	40	2100 - 2350	200	300	78	78	2	3	WT	A	E	I	BT	BHA	CMT D/O & Drlg formation f/ 3692 to 3697m
7	6-1/8"	Beste	PDC(M1665)	M1665	255421	3	X	22	NO	-	-	3697	3760	63	24.8	2.5	6 - 8	0.8 PDM	40	1950 - 2100	200	200	78	78	1	1	WT	A	X	I	NO	TD	Drlg formation f/ 3697 to 3760m
7 RR1	6-1/8"	Beste	PDC(M1665)	M1665	255421	3	X	22	NO	-	-	3760	3888	128	40.5	3.2	3 - 5	0.8 PDM	40	1900 - 2150	200	200	78	78	1	2	BT	T	X	I	WT	BHA	Drlg formation f/ 3760 to 3888m as TD.
2 RR4	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	84	84	2	2	WT	A	E	I	BT	LOG	Run as Condition trip
4 RR3	8-3/8"	Kingdream	Tri-Cone Bit (HJT537G)	537	2417584JH	Open			Yes	2103	2167.5	-	-	64.5	11	-	5 - 15	40	50	370 - 420	320	350	84	84	1	1	WT	A	E	I	NO	BHA	CMT D/O
2 RR5	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			Yes	3170	3300	-	-	130	16.5	-	10 - 15	30	50	1700 - 2200	220	300	84	84	2	2	WT	A	E	I	BT	LOG	CMT D/O & Condition trip
7 RR2	6-1/8"	Beste	PDC(M1665)	M1665	255421	3	X	22	NO	-	-	-	-	-	-	-	3 - 5	155	160	2660	270	270	85	85	1	2	BT	T	X	I	WT	LOG	Run as Condition trip
7 RR3	6-1/8"	Beste	PDC(M1665)	M1665	255421	3	X	22	NO	-	-	-	-	-	-	-	-	-	-	155	50	50	85	85	1	2	BT	T	X	I	WT	LOG	Run as Condition trip
7 RR4	6-1/8"	Beste	PDC(M1665)	M1665	255421	3	X	22	NO	-	-	-	-	-	-	-	-	-	-	155	50	50	87	87	1	2	BT	T	X	I	WT	TD	Run as Condition trip
2 RR6	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	2	2	WT	A	E	I	BT	BHA	Run as Condition trip
4 RR4	8-3/8"	Kingdream	Tri-Cone Bit (HJT537G)	537	2417584JH	3	X	18	Yes	2007	2034.5	-	-	27.5	4	-	5 - 10	30	30	900	350	350	84	84	1	1	WT	A	E	I	NO	BHA	CMT D/O
2 RR7	6-1/8"	Kingdream	Tri-Cone Bit	537	2304674JH	Open			Yes	2123	2178	-	-	55	15	-	6 - 17	30	70	250 - 1360	100	300	84	84	2	3	WT	A	E	I	BT	BHA	CMT D/O
4 RR5	8-3/8"	Kingdream	Tri-Cone Bit (HJT537G)	537	2417584JH	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	84	84	1	1	WT	A	E	I	NO	BHA	Run as Scraper trip.
8	5-7/8"	Kingdream	B. Bit	-	-	Open			NO	-	-	-	-	-	-	-	-	-	-	-	-	-	84	84	-	-	-	-	-	-	-	-	Run as Scraper trip.

Table 2-2: AZNS-075-ST1 Bit Record Table

3. Time Analysis Report

3.1 Time vs. Depth Chart

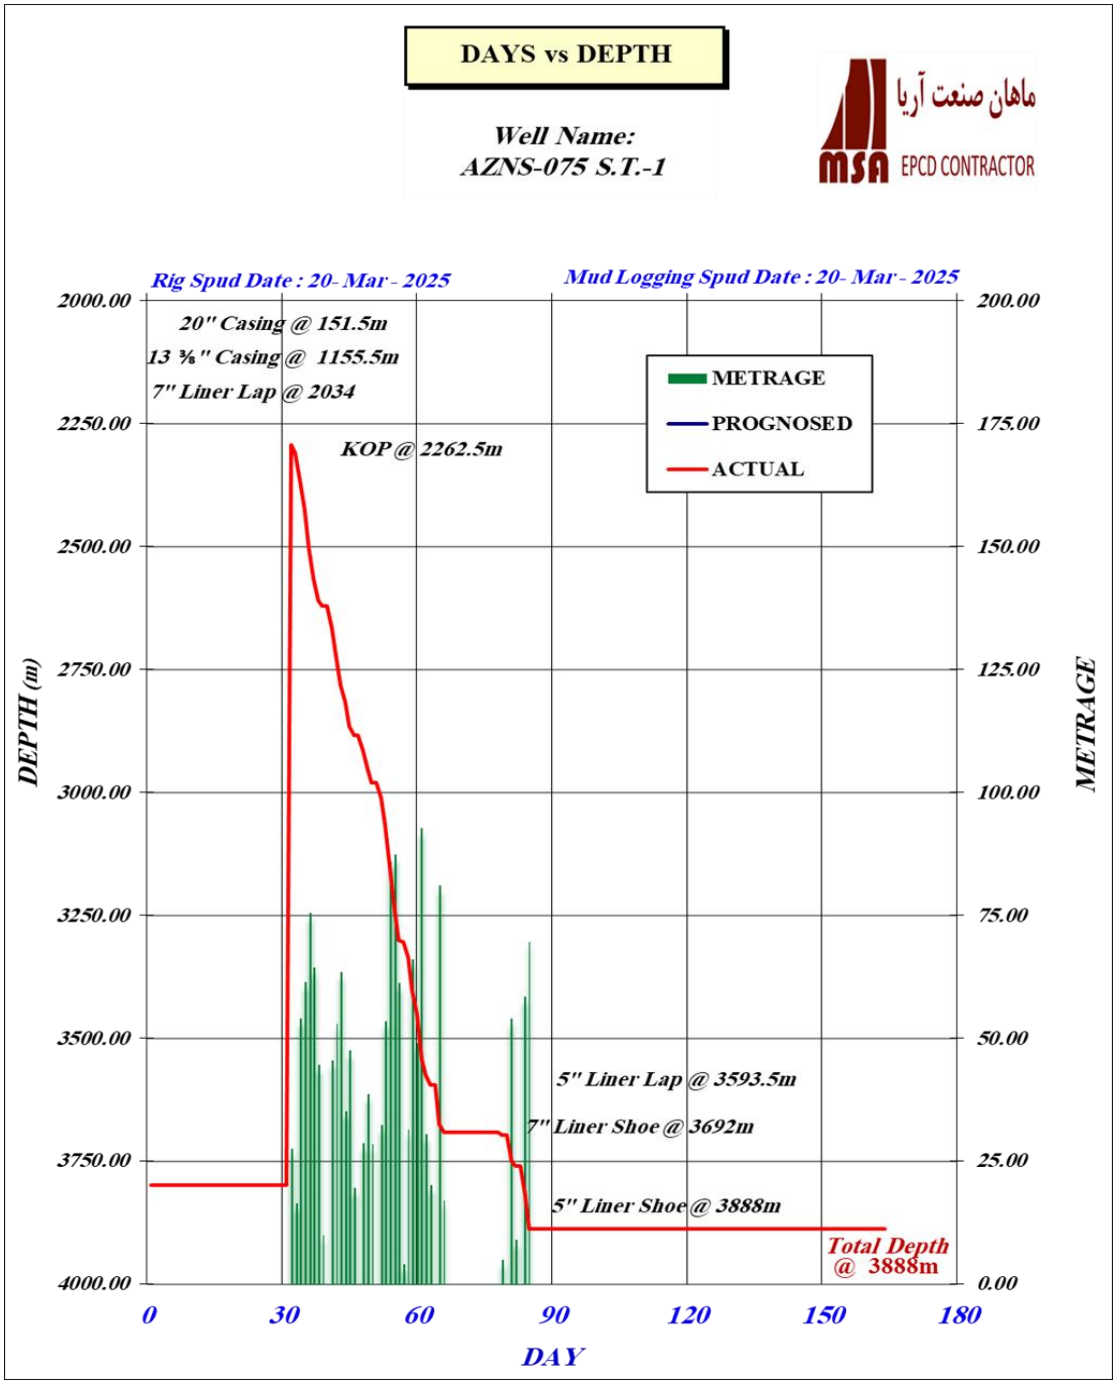


Figure 3-1: AZNS-075-ST1 Workover Well Time vs. Depth After Side Track

3.2 Total Time Break-Down of Operation

Well Name:	AZNS-075, W.O.1 , ST-1	Mar-25											
CODE	Operation	20	21	22	23	24	25	26	27	28	29	30	31
1	Rig Up/ Tear Down / Move												
2	Drilling												
3	Reaming												
4	Coring												
5	Circulate & Condition								2.00			2.50	
6	Trips	10.00										19.50	4.00
7	Service/ Maintain Rig												
8	Repair Rig								1.00				
9	Replacing Drill Line												
10	Deviation Survey												
11	Logging												20.00
12	Run Casing/ Liner												
13	Cementing												
14	Wait on Cement												
15	Rig Up/Down BOP				18.00	24.00							
16	Test BOP												
17	Drill Stem Test												
18	Fishing												
19	Specialized Directional Work												
20	Operation Status (Waiting)		20.00	14.00			24.00	24.00	14.00	1.00	5.50	2.00	
21	Safety												
22	Perforating												
23	Completion\ XMT	14.00	4.00		2.00				7.00	23.00	18.50		
24	Treating												
25	Swabbing												
26	Surface Testing												
27	Well Control			10.00	4.00								
28	Other												
29	Subsea Operation												
	Total	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00

Well Name:	AZNS-075, W.O.1 , ST-1	Apr-25																												
CODE	Operation	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
1	Rig Up/ Tear Down/ Move																														
2	Drilling																				15.50	8.50	18.00	19.50	20.50	18.50	20.75	4.00		21.00	21.50
3	Reaming			6.00	1.00							18.00											1.50	1.50	1.50	3.00	1.50			1.00	1.00
4	Coring																														
5	Circulate & Condition	3.50			1.50					3.00	3.00	1.00	5.50			2.00	2.00	4.00										7.50			
6	Trips	15.50	1.50	16.50	9.50					7.00	17.00	0.50	18.50	2.50			9.50	8.00	18.00			15.50	4.50					10.00	24.00		
7	Service/ Maintain Rig																														
8	Repair Rig																														
9	Replacing Drill Line									1.50																		2.00			
10	Deviation Survey															8.50								3.00	2.00	2.50	1.75	0.50		1.00	1.50
11	Logging	5.00																													
12	Run Casing/ Liner																														
13	Cementing		10.50								2.50																				
14	Wait on Cement																														
15	Rig Up/Down BOP																														
16	Test BOP									4.50																					
17	Drill Stem Test				12.00	24.00	24.00	24.00	24.00	8.00																					
18	Fishing																														
19	Specialized Directional Work													21.50	10.00	13.50	12.50	12.00													
20	Operation Status (Waiting)		12.00	1.50							1.50	4.50			14.00				6.00	24.00	8.50									1.00	
21	Safety																														
22	Perforating																														
23	Completion\ XMT																														
24	Treating																														
25	Swabbing																														
26	Surface Testing																														
27	Well Control																														
28	Other																														
29	Subsea Operation																														
	Total	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00

Well Name:	AZNS-075, W.O.1 , ST-1	May-25																												
CODE	Operation	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
1	Rig Up/ Tear Down / Move																1															
2	Drilling	20.75	23.25	22.75	9.50		12.75	23.00	11.50		20.50	22.75	21.75	24.00	24.00	1.50	9.50	24.00	23.00	24.00	23.00	13.50		21.00	6.00							
3	Reaming						8.50																					5.00				6.50
4	Coring																															
5	Circulate & Condition															1.50						1.00			3.00			2.00			1.50	
6	Trips				12.50	16.50	2.50									20.00	13.50					9.50	20.00	3.00	15.00	7.00		9.00	7.00		0.50	14.50
7	Service/ Maintain Rig																															
8	Repair Rig																															
9	Replacing Drill Line																									2.00						
10	Deviation Survey	3.25	0.75	1.25	0.50		0.25	1.00	0.50		0.50	1.25	2.25																			
11	Logging																															
12	Run Casing/ Liner																									15.00	19.50	8.00				
13	Cementing																										4.50					
14	Wait on Cement																															
15	Rig Up/Down BOP																															
16	Test BOP					4.00																	4.00									
17	Drill Stem Test																												17.00	24.00	22.00	
18	Fishing																															
19	Specialized Directional Work																															
20	Operation Status (Waiting)				1.50	3.50			12.00	24.00	3.00					1.00			1.00		1.00											3.00
21	Safety																															
22	Perforating																															
23	Completion\ XMT																															
24	Treating																															
25	Swabbing																															
26	Surface Testing																															
27	Well Control																															
28	Other																															
29	Subsea Operation																															
	Total	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00

Well Name:	AZNS-075, W.O.1 , ST-1	Jun-25																												
CODE	Operation	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
1	Rig Up/ Tear Down/ Move																														
2	Drilling						4.00		23.50	8.00		22.00	21.50																		
3	Reaming	17.50	4.50			1.00	6.00		0.50					9.00	17.00	11.50															
4	Coring																														
5	Circulate & Condition		1.00		2.00		5.50						2.50	2.00	2.00			1.00													
6	Trips	6.50	12.50		17.00	14.00	5.75	24.00		16.00				10.00	5.00	12.50	24.00	23.00	5.50						5.00						
7	Service/ Maintain Rig																														
8	Repair Rig																														
9	Replacing Drill Line						2.75														2.00										
10	Deviation Survey																														
11	Logging					7.00													10.50	24.00											
12	Run Casing/ Liner																														
13	Cementing																														
14	Wait on Cement																														
15	Rig Up/Down BOP																														
16	Test BOP		2.00	1.50		2.00					3.00																				
17	Drill Stem Test			13.00																											
18	Fishing													3.00																	
19	Specialized Directional Work																														
20	Operation Status (Waiting)		4.00	9.50	5.00						21.00	2.00							8.00		22.00	24.00	24.00	24.00	24.00	19.00	24.00	24.00	24.00	24.00	24.00
21	Safety																														
22	Perforating																														
23	Completion\ XMT																														
24	Treating																														
25	Swabbing																														
26	Surface Testing																														
27	Well Control																														
28	Other																														
29	Subsea Operation																														
	Total	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00

Well Name:	AZNS-075, W.O.1 , ST-1	Jul-25																												
CODE	Operation	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
1	Rig Up/ Tear Down/ Move																															
2	Drilling																															
3	Reaming								3.50						9.00	22.50		11.00	1.00													
4	Coring																															
5	Circulate & Condition									3.00		1.00		5.50					6.00		2.00											
6	Trips									21.00	0.50	11.00	24.00	17.50	15.00	1.50	18.00	8.00	12.00	10.00	16.50	24.00	22.00	24.00	23.00	7.00					6.50	4.00
7	Service/ Maintain Rig																															
8	Repair Rig																															
9	Replacing Drill Line																				2.00								2.00			
10	Deviation Survey																															
11	Logging								4.00										1.00	14.00												
12	Run Casing/ Liner										23.50	6.00													1.00						2.00	20.00
13	Cementing											6.00																				
14	Wait on Cement																															
15	Rig Up Down BOP																															
16	Test BOP																6.00														3.00	
17	Drill Stem Test																									17.00	24.00	24.00	22.00	24.00	8.00	
18	Fishing																															
19	Specialized Directional Work																															
20	Operation Status (Waiting)	24.00	24.00	24.00	24.00	24.00	24.00	24.00	16.50					1.00				5.00	4.00		3.50		2.00								4.50	
21	Safety																															
22	Perforating																															
23	Completion\ XMT																															
24	Treating																															
25	Swabbing																															
26	Surface Testing																															
27	Well Control																															
28	Other																															
29	Subsea Operation																															
	Total	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00

Well Name:	AZNS-075, W.O.1 , ST-1	Aug-25																													
CODE	Operation	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30
1	Rig Up/ Tear Down/ Move																														
2	Drilling																														
3	Reaming	3.00	6.00	21.50		4.50																									
4	Coring																														
5	Circulate & Condition	0.50	1.50	1.00	2.50	5.00	1.00			5.50	1.00					6.00	4.50														
6	Trips	9.00	16.50	1.50	21.50	14.50	13.50	5.00		16.50	6.00				11.00	12.00	14.50	24.00	18.00	24.00	8.50				15.00	24.00	20.50				
7	Service/ Maintain Rig																														
8	Repair Rig																														
9	Replacing Drill Line										2.00																				
10	Deviation Survey																														
11	Logging						9.50														2.00										
12	Run Casing/ Liner	11.50																			15.50										
13	Cementing																														
14	Wait on Cement																														
15	Rig UpDown BOP																														
16	Test BOP																														
17	Drill Stem Test							19.00	24.00	2.00																					
18	Fishing																														
19	Specialized Directional Work																														
20	Operation Status (Waiting)										15.00	24.00	17.00	11.00	6.00	6.00	5.00													11.00	12.00
21	Safety																														
22	Perforating												7.00	13.00	7.00																
23	Completion\ XMT																		5.00			24.00	24.00	24.00	9.00		1.50	24.00	24.00	13.00	12.00
24	Treating																														
25	Swabbing																														
26	Surface Testing																														
27	Well Control																		1.00												
28	Other																														
29	Subsea Operation																														
	Total	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00	24.00

Table 3-1: AZNS-075-ST1 WorkOver Time Breakdown

3.3 NPT Break-Down

Section	Op.	Co.	NPT (hr)	Date
Workover	WAITING	OEOC	14	1404.01.01
	WAITING	OEOC	13	1404.01.01
	WAITING	OEOC	3	1404.01.04
	WAITING	OEOC	24	1404.01.05
	WAITING	OEOC	24	1404.01.06
	WAITING	OEOC	14	1404.01.07
	WAITING	OEOC	1	1404.01.08
	LOGGING, TRIP IN, CIRC. FOR CMT PLUG	OEOC	4	1404.01.12
	CIRC. CMT PLUG JOB	OEOC	12	1404.01.13
	RIH D/OT BHA	OEOC	1	1404.01.21
	RIH D/OT BHA	OEOC	0.5	1404.01.21
	RIH D/OT BHA	OEOC	4.5	1404.01.22
	SET WHIPSTOCK	OEOC	14	1404.01.25
	SET WHIPSTOCK	OEOC	6	1404.01.26
	ALIGN TOOL FACE OF PDM	OEOC	6	1404.01.29
	ALIGN TOOL FACE OF PDM	OEOC	24	1404.01.30
	TAKE SURVEY, SIDE TRACK	OEOC	8.5	1404.01.31
	SIDE TRACK	OEOC	16	1404.02.07
	ROUND TRIP	OEOC	24	1404.02.08
	TRIP	OEOC	1.5	1404.02.14
	TRIP	OEOC	3.5	1404.02.15
	DIR.DRLG	OEOC	12	1404.02.18
	DIR.DRLG	OEOC	24	1404.02.19
	DIR.DRLG	OEOC	3	1404.02.20
	TRIP	OEOC	1	1404.02.25
	D.DRLG	OEOC	1	1404.02.30
	D.DRLG/TRIP OUT	OEOC	10.5	1404.02.31
	ROUND TRIP/BOP TEST	OEOC	20	1404.03.01

	TRIP IN/D.DRLG	OEOC	3	1404.03.02
	TRIP IN/D/OUT	OEOC	3	1404.03.10
	TRIP	OEOC	3	1404.03.12
	TRIP	OEOC	1	1404.03.12
	SCRAPER TRIP	OEOC	9.5	1404.03.13
	SCRAPER TRIP	OEOC	3	1404.03.14
	SCRAPER TRIP	OEOC	2	1404.03.14
	TRIP	OEOC	2	1404.03.16
	DIR.DRLG	OEOC	18.5	1404.03.19
	DIR.DRLG	OEOC	24	1404.03.20
	DIR.DRLG	OEOC	2	1404.03.21
	HOLE CONDITIONING	OEOC	12	1404.03.25
	HOLE CONDITIONING	OEOC	24	1404.03.26
	HOLE CONDITIONING	OEOC	24	1404.03.27
	HOLE CONDITIONING/LOG	OEOC	6	1404.03.28
	F.SUITE LOG	OEOC	8	1404.03.28
	TRIP IN AS OPEN END DPS	OEOC	8.5	1404.03.30
	TRIP IN & PERFORM CMT PLUG	OEOC	24	1404.03.31
	PERFORM CMT PLUG/SHUT IN WELL	OEOC	24	1404.04.01
	SHUT IN AS SECURE WELL/WAIT ON DECISION	OEOC	24	1404.04.02
	SHUT IN AS SECURE WELL/WAIT ON DECISION	OEOC	9	1404.04.03
	WAIT ON WIND SPEED	OEOC	10	1404.04.03
	TRIP IN AS CLEAN OUT ASSY. TO D/O CMT PLUGS	OEOC	5	1404.04.03
	TRIP IN /D/O CMT PLUG#1/POOH	OEOC	24	1404.04.04
	ROUND TRIP /D/O CMT PLUG#2	OEOC	11	1404.04.05
	D/O CMT PLUG#2	OEOC	13	1404.04.06
	HOLE CONDITION	OEOC	10	1404.04.07
	HOLE CONDITION	OEOC	10	1404.04.08
	HOLE CONDITION	OEOC	10	1404.04.09
	HOLE CONDITION	OEOC	13.5	1404.04.10
	HOLE CONDITION	OEOC	10.5	1404.04.10
	HOLE CONDITION	OEOC	24	1404.04.11
	LOGGING	OEOC	8.5	1404.04.12
	HOLE CONDITION	OEOC	15.5	1404.04.12
	HOLE CONDITION	OEOC	24	1404.04.13
	HOLE CONDITION	OEOC	4	1404.04.14

	LOGGING	OEOC	9	1404.04.14
	LOGGING	OEOC	24	1404.04.15
	LOGGING	OEOC	10.5	1404.04.16
	HOLE CONDITIONING	OEOC	13.5	1404.04.16
	LOGGING	OEOC	16.5	1404.04.17
	HOLE CONDITIONING	OEOC	2	1404.04.17
	CLEAN OUT/TRIP OUT	OEOC	2	1404.04.27
	LOGGING/SCRAPPING	OEOC	10	1404.04.28
	SCRAPPING/POLISH MILL/TRIP	OEOC	24	1404.04.29
	POLISH MILL TRIP/SET 7"SN PKR	OEOC	24	1404.04.30
	5"POLISH MILL TRIP/7"SCRAP TRIP	OEOC	23	1404.04.31
	SET 5" SN PKR	OEOC	24	1404.05.02
	SET 5" SN PKR/RUN 5" DRY TEST ASSY.	OEOC	7	1404.05.03
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	16.5	1404.05.06
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.07
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.08
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.09
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.10
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.11
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.12
	24 HRs / DUE TO REMEDY 7" L.LAP LEAKAGE	OEOC	24	1404.05.13
	24 HRs / DUE TO REPEAT SBT LOG	OEOC	24	1404.05.14
	24 HRs / DUE TO REPEAT 7" L.LAP DRY TEST	OEOC	24	1404.05.15
	24 HRs / DUE TO REPEAT 7" L.LAP DRY TEST	OEOC	24	1404.05.16
	24HRs / DUE TO REPEAT 7" L.LAP DRY TEST	OEOC	24	1404.05.17
	24HRs / DUE TO REPEAT 7" L.LAP DRY TEST	OEOC	2	1404.05.18
	10 HRs / WAIT ON REC PERFORATION TOOLS & EQP	OEOC	10	1404.05.19
	POOH/WAIT ON LOGGING EQUIP	OEOC	18	1404.05.20
	CIRC.	OEOC	9	1404.05.21
	R/UP TDS	OEOC	6	
	PERFORATION DUMMY RUN	OEOC	2	
	PERFORATION	OEOC	6	1404.05.22
	PERFORATION	OEOC	4	
	PERFORATION /COND. TRIP	OEOC	6	1404.05.23
	RUN COMPL. STRING	OEOC	10	1404.05.31

	POOH COMPL. STRING	OEOC	24	1404.06.01
	POOH COMPL. STRING	OEOC	24	1404.06.02
	POOH COMPL. STRING	OEOC	24	1404.06.03
	POOH COMPL. STRING	OEOC	24	1404.06.04
	POOH COMPL. STRING	OEOC	24	1404.06.05
	POOH COMPL. STRING	OEOC	15	1404.06.06
	FISHING	OEOC	11	1404.06.07
	DELAY IN OPERATION	OEOC	12	1404.06.08
	DELAY IN OPERATION	OEOC	6	1404.06.09

Table 3-2: AZNS-075-ST.1 NPT Time BreakDown (Based on Client's Order & Information)

4. Dry Test Report

4.1 7” L.Lap dry test

7” Liner Data
29 ppf Weight
L-80 Grade
6.059” Drift
TP-CQ premium connection

Table 4-1: AZNS-75 7" Liner Information

Exposed Formation Characteristics	
Datum Depth: 3850m TVD	
Datum Pressure: 6500 psi (0.29 psi/ft)	
Cushion Type	Drill Water
Cushion Density	63
Packer Depth	2316m
Datum Depth(3850m) Pressure	6500^{psi}
Packer Depth Pressure	3845^{psi}
7” Liner Lap Pressure	3922^{psi}
Drive Force	2000^{psi}
Cushion Depth	1285 m water

Table 4-2: AZNS-075-ST1 Dry Test Information

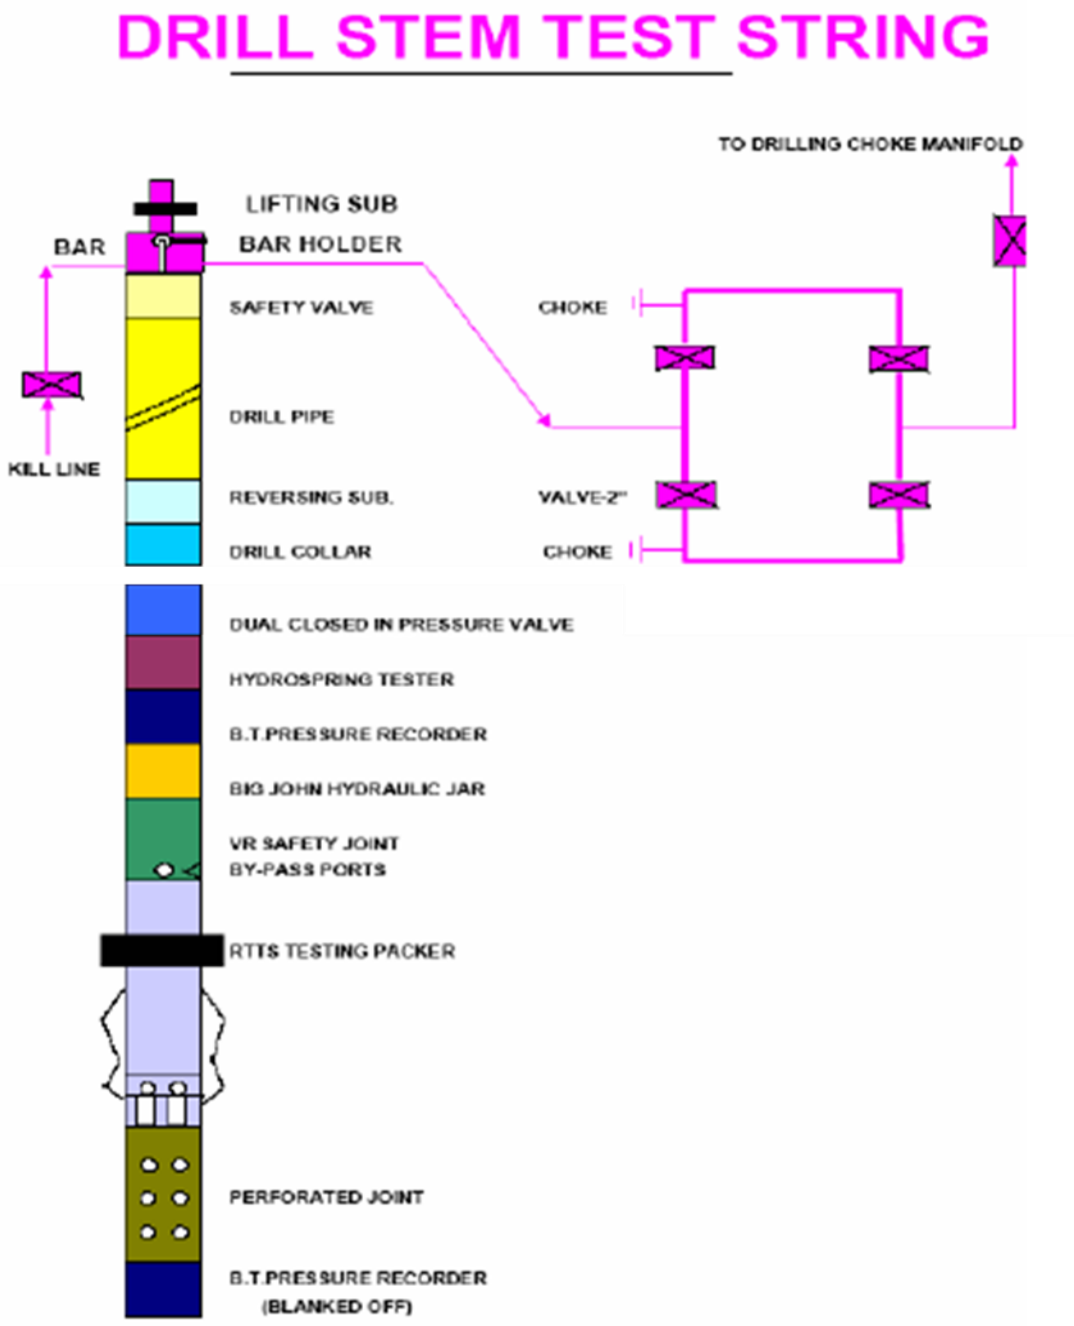


Figure 4-1: AZNS-075-ST1 Dry Test Event

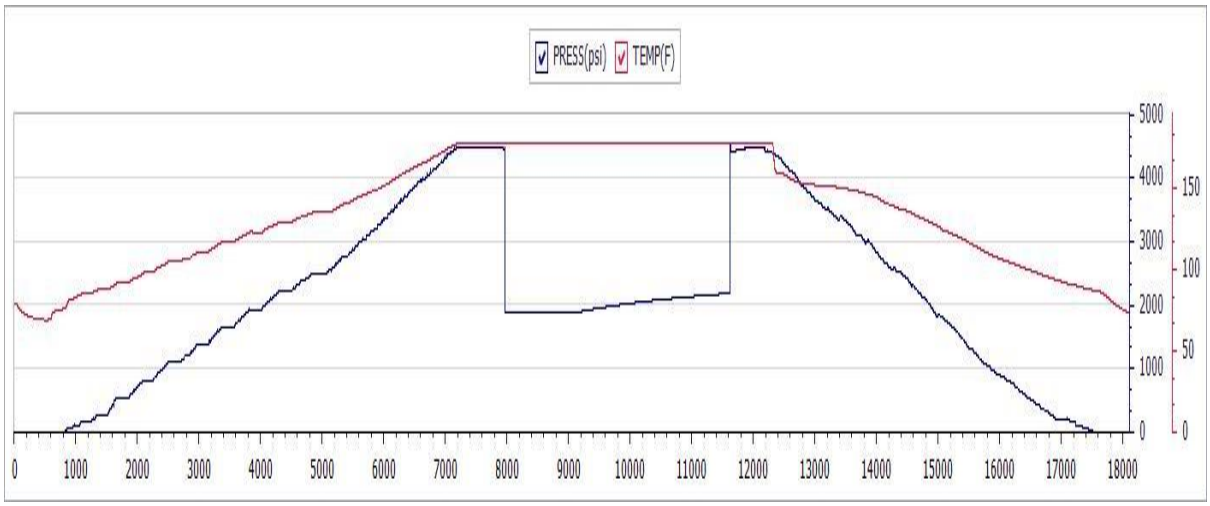


Figure 4-2: AZNS-075-ST1 7” L.Lap Dry test result – Middle BT

4.2 5” L.Lap Dry test

Row	Description	Time	Bottom Bt.	Middle Bt.
1	Initial Mud Static Pressure (psia)	17:18	6558	6542
2	Open Well Pressure (psia)	2025/07/26 17:26	3588	3572
		2025/07/26 20:29	3588	3572
3	Close Well Pressure (psia)	2025/07/26 20:29	3588	3572
		2025/07/27 2:30	3814	3798
4	Final Hydrostatic Pressure (psia)	5:43	6524	6508

Table 4-3: AZNS-075-ST1 Downhole Test Result Data


5” Liner Data
18 ppf Weight
L-80 Grade
4.276” Drift
HSG3-FJTHD

Table 4-4: AZNS-075-ST1 5" Liner Information

Exposed Formation Characteristics	
Datum Depth: 3500m ^{m} TVD	
Datum Pressure: 5600 ^{psi} (0.29 psi/ft)	
Cushion Type	Fresh Water
Cushion Density	62.4
Packer Depth	3570 m
Datum Depth(4000^{m}) Pressure	5600 psi (0.48 psi/ft)
Packer Depth Pressure	2449.59 psi
7” Liner Lap Pressure	5494.11 psi
Drive Force	2000 psi
Cushion Depth	2564.61 m water

Table 4-5: AZNS-075-ST1 5” Dry Test Information

DRILL STEM TEST STRING

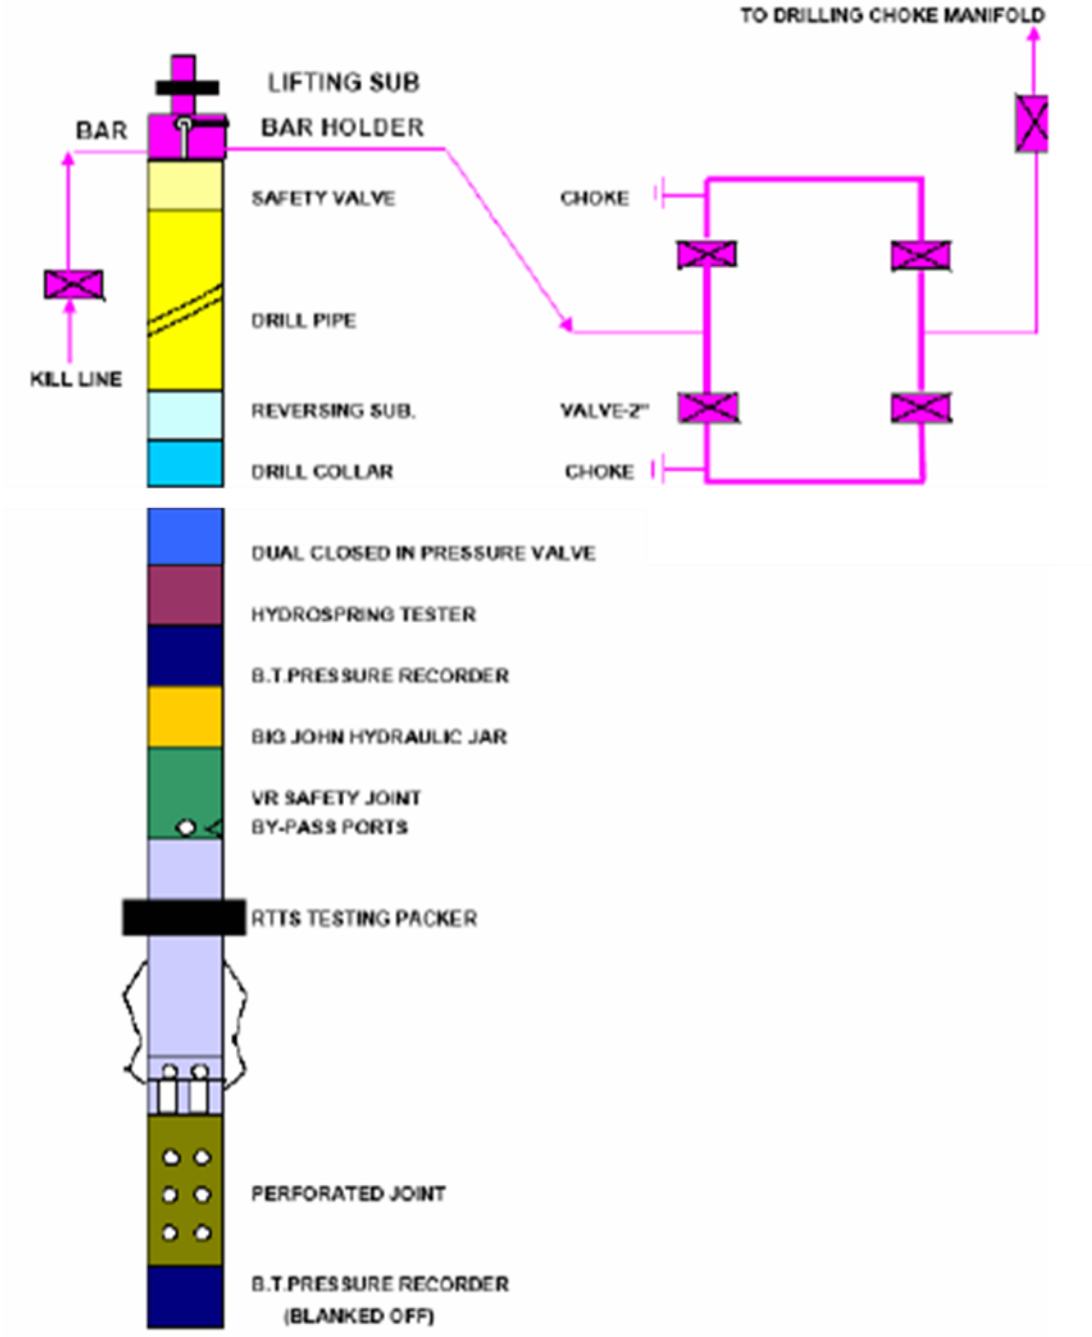

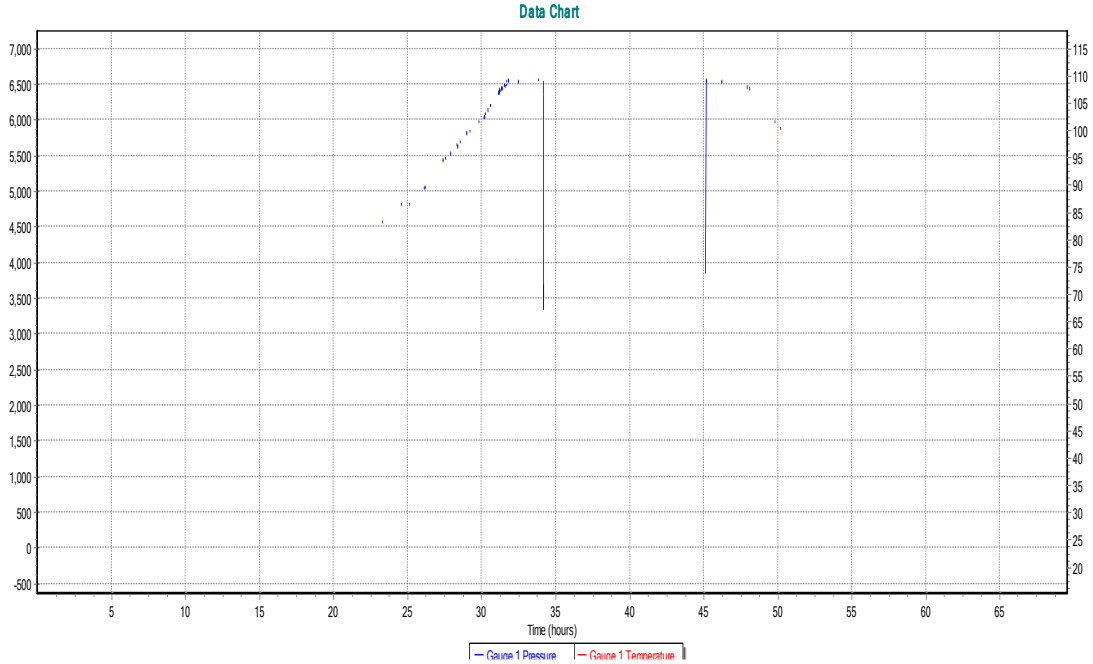


Figure 4-3: AZNS-075-ST1 5" L.Lap Dry test result – Middle BT

5. Geological & Logging Reports

5.1 Stratigraphy

The well was sidetracked as Sidetrack-1 (S.T.-1) from within the Tarbur Member and drilled down to the total depth (T.D.). The following section describes the stratigraphic characteristics of the drilled intervals.

- **Gurpi Formation**

This formation consists of three main units: a) Upper Gurpi Member b) Tarbour Member c) Lower Gurpi Member.

- **Tarbur Member**

In the western Abadan Plain about 50 meters thick chalky limestone was encountered in the middle part of the Gurpi Formation, which contains abundant fragments of bioclasts, suggesting very shallow depositional environment. This interval is equivalent to the Tarbur Formation with reservoir quality in other regions.

- **Lower Gurpi Member**

This Member begins with off white, cream, soft to medium hard argillaceous limestone and light gray to gray, soft, sticky marl. The Member consisting of dark gray to gray, light gray, soft to medium hard argillaceous limestone and light cream and soft. II, A. chalky limestone beds.

- **Ilam Formation**

This formation is mostly consisting of limestone interbedded with shale and claystone beds. The Limestone is cream, buff to buff gray, light brown, soft to medium hard, chalky, II, A, oil stained partly slightly argillaceous. The Shale is green gray to light green gray, mostly brown gray, medium hard, pyritic, slightly calcareous. The Claystone is green gray to light green gray and soft, slightly calcareous.

- **Laffan Member**

  The Laffan Member is mostly consists of greenish-grey pyritic shale layer with ostracods fauna interbedded with Claystone beds that capping the Sarvak Formation.

- **Sarvak Formation**

  The Sarvak Formation developed a carbonate unit, which was gradually overlying the Kazhdumi Formation, and it is abruptly terminated by an erosion phase, covered by a various late Cretaceous sediment. The lithology of Sarvak consists of the dark grey fine grained nodular argillaceous limestone interbedded with thin marls in the bottom. The Limestone graded upward into a white-to-buff massive chalky limestone with siliceous nodules; developed a very massive tan-to-brown limestone containing abundant rudist debris in the middle part. In the upper part is made up of rubbly limestone with red staining and leached zones of breccia and the top of Sarvak Formation is very ferruginous. For the layering scheme of the reservoir section, sequence stratigraphic concept was applied to the Azadegan wells. Judging from the characteristics of gamma ray and other wireline logs, relative sea- level change during the deposition of the reservoir sections were interpreted in terms of sequence stratigraphic context. Based upon the sea-level change inferred, the sections were interpreted as vertical accumulation of a number of zones, each of which is geologically termed as a depositional sequence, implicitly representing a genetically related body of sedimentary sequence. The formation was divided totally into thirteen zones by interpreting.

- **Kazhdumi Formation**

  This formation is start with dark brown to dark green gray, medium hard to hard, soft to medium, high bituminous, calcareous shale interbedded with argillaceous limestone, sandy claystone, claystone, marl, sandy limestone, limestone beds. the middle part developed light-grey, micritic to chalky limestone, the low part, is around 40-60m in thickness clean channel sands interbedded with argillaceous sands with streaks of shale.

- **Dariyan Formation**

In the Azadegan Field, the average thickness of the Dariyan Formation is 183.5 m; its greatest thickness is 197.5 m in well AZN-1. This formation overlies the Gadvan Formation conformably and is overlain disconformably by the Kazhdumi Formation. Dariyan Formation starts with white-to-white cream grey clean limestone type I/II, I. Base of Dariyan Formation appears grey, green pyritic shale interbedded with argillaceous limestone. This zone called transition zone and thickness is 16m. after last grey limestone indicates of Gadvan Formation.

- **Gadvan Formation**

In this formation a variety of lithological rock types such as carbonates, rich organic shales and sandstones were deposited in various environments. The lower part of the Gadvan Formation is composed of low- energy, but not very deep, micritic, often argillaceous limestone with echinoids and algal fragments. Two sandstone units were defined in the Gadvan Formation lateral changes and especially discontinuity of the sandstone layers which are consist of fine clastic (shales and siltstones) may be expected The Gadvan formation divided to three parts:

- **Upper Gadvan**

The upper part appears with occurrence of terrigenous rock. The lithology is composed of grey claystone and some shale.

- **Khalij Member**

The Khalij Member appear with pure limestone, cream, light brown and in some intervals oil stain.

- **Lower Gadvan**

The lower part consisting of alternating of marl, argillaceous limestone, limestone, claystone, sandy claystone and sandstone beds. The Marl is green gray, soft, sticky, slightly calcareous. The Argillaceous Limestone is gray white gray medium hard to soft, partly pyritic. The Limestone is white, white to light gray, hard. The Claystone is light gray, soft, sticky. The Sandy Claystone is light gray, soft, sticky,

fine sand grained. The Sandstone is brown to gray, partly white buff, gray, friable, sorted, sub rounded, medium quartz grained, partly calcareous. This sandstone which occurs in Zone-3 and Zone-5 are the reservoir of this formation and in this part is equivalent with Kushk Member.

Lithostratigraphic Unit	Formation Tops (m)				TVD Thickness	Difference	Casing & Liner Data	
	Forecast	MD (Sample)	MD (Log)	TVDss		($MD_{Forecast}$-MD_{Log})	Size	Depth
	(m)	(m)	(m)	(m)	(m)	(m)	(Inch)	(m)
Original								
Tarbur	-	-	2226.44	-2213.37	-	-		
Side Track								
K.O.P. at 2262.5m inside of Tarbur Member								
L. Gurpi	2327.90	2328	2327.34	-2314.10	145.17	-0.56		
Ilam	2469.10	2469	2475.13	-2459.27	58.27	6.03		
Ilam-Main	-	-	2536.74	-2517.54	17.05	-		
Laffan	2549.30	2549	2555.26	-2534.59	6.48	5.96		
Sarvak (Sar.-1)	2555.70	2556	2562.35	-2541.07	19.43	6.65		
Sar.-2	2577.80	-	2583.74	-2560.50	7.22	5.94		
Sar.-3	2584.50	-	2591.79	-2567.72	33.74	7.29		
Sar.-4	2623.10	-	2629.92	-2601.46	27.64	6.82		
Sar.-5	2655.30	-	2661.88	-2629.10	33.87	6.58		
Sar.-6	2694.30	-	2700.95	-2662.97	26.23	6.65		
Sar.-7	2724.10	-	2731.14	-2689.20	16.49	7.04		
Sar.-8	2742.90	-	2750.08	-2705.69	56.88	7.18		
Sar.-9	2814.30	-	2815.89	-2762.57	40.70	1.59		
Sar.-10	2856.70	-	2863.12	-2803.27	36.73	6.42		
Sar.-11	2899.90	-	2905.94	-2840.00	45.07	6.04		
Sar-12	2950.90	-	2958.58	-2885.07	52.58	7.68		
Sar.-Intra	-	-	3020.11	-2937.65	46.81	-		
Ahmadi Shale	3063.30	-	3073.37	-2984.46	18.80	10.07		
Basal Sarvak	3089.60	-	3094.99	-3003.26	182.53	5.39		
Kazhdumi	3302.60	3299	3305.26	-3185.79	128.82	2.66		
Kaz.-1	3447.80	-	3452.08	-3314.61	12.12	4.28		
Kaz.-2	3463.30	-	3466.04	-3326.73	10.02	2.74		
Kaz.-2-2	3484.20	-	3477.52	-3336.75	13.54	-6.68		
Kaz.-3	3500.80	-	3492.97	-3350.29	2.02	-7.83		
Kaz.-4	3507.30	-	3495.27	-3352.31	23.78	-12.03		
Kaz.-5	3526.20	-	3522.26	-3376.09	10.23	-3.94		
Dariyan	3539.60	3527	3533.80	-3386.32	157.73	-5.8		
Gadvan (Gad.-1)	3722.50	3709	3715.67	-3544.05	11.04	-6.83	7" L.	2034 - 3692
Gad.-2u	3734.95	-	3728.73	-3555.09	59.21	-6.22		
Khalij	3801.10	-	3798.63	-3614.30	7.98	-2.47		
Gad.-21	3810.10	-	3808.14	-3622.28	4.85	-1.96		
Gad.-3	3815.10	-	3813.91	-3627.13	6.59	-1.19		
Gad.-4	3824.10	-	3821.76	-3633.72	13.49	-2.34		
Gad.-5a	3837.70	-	3837.77	-3647.21	7.25	0.07		
Gad.-5b	3846.50	-	3846.35	-3654.46	2.74	-0.15		
Gad.-5c	3849.40	-	3849.60	-3657.20	2.04	0.2		
Gad.-5c-2	-	-	3852.01	-3659.24	11.33	-		
Gad.-6	3868.70	-	3865.38	-3670.57	19.24	-3.32		
T.D.	3888.50	3888	3888	-3689.81		-0.5	5" L.	3593.5-3888

Table 5-1: AZNS-075-ST1 Formation & Reservoir Sub Layers Top

Well General Data			
Area	Abadan Plain, Block-III		
Field	South Azadegan		
Pad No.	80		
Rig No.	OEOC-201		
Well No.	AZNS-075 S.T.-1		
Well Type	Deviated Well		
T.D. & Fm	3888m (-3689.81mc)/Gadvan		
Wellhead Coordinates	WGS-1984	E: 186,427m	
		N: 3,436,066m	
E. Point in Gadvan Fm.	WGS-1984	E: 187,053.2	
		N:3,436,062.95	
T.D. Coordinates	WGS-1984	E: 187,145.01	
		N: 3,436,065.94	
Elevation	R.T.E.	12.95m	
	G.L.E.	3.95m	
Spudded Rig Date:	20-Mar-25		
Released Rig Date:	01-Sep-25		
Start of Drilling Date:	19-Apr-25		
End of Drilling Date:	12-Jun-25		

Casing & Liner			
Size (inch)	Depth (m)		Remarks
	From	To	
7	2034	3692	Set inside of Dariyan Fm.
5	3593.5	3888	At the base of Gadvan Fm.

Mud Properties	
Hole Size (inch)	Mud Type & Weight
8 3/8	(KCL) S.S Polymer Mud (76-78 pcf)
6 1/8	KCL S.S Polymer Mud (78pcf)

Electrical Logs (Based on Header)					
Electrical Logs	Company	Hole Size	Run No.	Depth Interval (m)	Date
Sonic / Resestivity / GR	Sealand	6 1/8"	1	3700.5 - 3882	08-Jul-25
CNT/NGS	Sealand	5" L.	2	3645 - 3875	19-Jul-25
SBT / CCL / VDL / GR	Sealand	7" L.	1	2160 - 3669	04-Jun-25
SBT / CCL / VDL / GR	Sealand	5" L.	1	3541 - 3875	06-Aug-25
SBT / CCL / VDL / GR	Sealand	5" L.	1	3596 - 3870	19-Jul-25

Perforation Data (5" - WCP Method) / Based on Header				
Interval (m)		Thickness (m)	Total Thickness (m)	Company
3865	3853	12	19.3	Sealand
3852	3849	3		
3846.3	3842	4.3		

8 3/8" Hole Section Summary
This section drilling started with (KCL) S.S Polymer Mud (76-78pcf) from 2262.2m to 3715.67m. Ran 7" LNR from 2034m to 3692m and cemented.
6 1/8" Hole Section Summary
This section drilling started with KCL S.S Polymer Mud (78pcf) from 3715.67m to 3888m. Ran 5" LNR from 3593.5m to 3888m and cemented.

Formation and Reservoir Sub Layer Tops			
Lithostratigraphic Units	MD (Log)	TVDss (mc)	Thickness (TVD)
Original Hole			
Tarbur	2226.44	-2213.37	-
SideTrack Hole			
K.O.P. at 2262.5m (inside of Tarbur Member)			
L. Gurpi	2327.34	-2314.1	145.17
Ilam	2475.13	-2459.27	58.27
Ilam-Main	2536.74	-2517.54	17.05
Laffan	2555.26	-2534.59	6.48
Sarvak (Sar.-1)	2562.35	-2541.07	19.43
Sar.-2	2583.74	-2560.5	7.22
Sar.-3	2591.79	-2567.72	33.74
Sar.-4	2629.92	-2601.46	27.64
Sar.-5	2661.88	-2629.10	33.87
Sar.-6	2700.95	-2662.97	26.23
Sar.-7	2731.14	-2689.20	16.49
Sar.-8	2750.08	-2705.69	56.88
Sar.-9	2815.89	-2762.57	40.7
Sar.-10	2863.12	-2803.27	36.73
Sar.-11	2905.94	-2840.00	45.07
Sar-12	2958.58	-2885.07	52.58
Sar.-Intra	3020.11	-2937.65	46.81
Ahmadi Shale	3073.37	-2984.46	18.8
Basal Sarvak	3094.99	-3003.26	182.53
Kazhdumi	3305.26	-3185.79	128.82
Kaz.-1	3452.08	-3314.61	12.12
Kaz.-2	3466.04	-3326.73	10.02
Kaz.-2-2	3477.52	-3336.75	13.54
Kaz.-3	3492.97	-3350.29	2.02
Kaz.-4	3495.27	-3352.31	23.78
Kaz.-5	3522.26	-3376.09	10.23
Dariyan	3533.80	-3386.32	157.73
Gadvan (Gad.-1)	3715.67	-3544.05	11.04
Gad.-2u	3728.73	-3555.09	59.21
Khalij	3798.63	-3614.3	7.98
Gad.-21	3808.14	-3622.28	4.85
Gad.-3	3813.91	-3627.13	6.59
Gad.-4	3821.76	-3633.72	13.49
Gad.-5a	3837.77	-3647.21	7.25
Gad.-5b	3846.35	-3654.46	2.74
Gad.-5c	3849.60	-3657.20	2.04
Gad.-5c-2	3852.01	-3659.24	11.33
Gad.-6	3865.38	-3670.57	19.24
T.D.	3888	-3689.81	

Table 5-2: AZNS-075-ST1 Well Data Summary

Hole Type	Date	Formation/Member	From (m)	To (m)	Mud Type	Mud Weight (pcf)	Loss (BPD)	Gain (BPD)
8 3/8	20/04/2025	Tarbur	2266	2293.5	(KCl) S.S.Polymer Mud	76	-	-
	21/04/2025		2293.5	2310		76	-	-
	22/04/2025	Lower Gurpi	2310	2364		76	49	-
	23/04/2025		2364	2425.5		76	24	-
	24/04/2025	Lower Gurpi - Ilam	2425.5	2501.0		76	48	-
	25/04/2025	Ilam - Laffan - Sarvak	2501.0	2565.4		76	49	-
	26/04/2025	Sarvak	2565.4	2610.0		76	72	-
	27/04/2025		2610.0	2620.0		76	135	-
	29/04/2025		2620.0	2665.5		76	114	-
	30/04/2025		2665.5	2718.3		76	130	-
	01/05/2025		2718.3	2781.8		76	140	-
	02/05/2025		2781.8	2817.0		76	138	-
	03/05/2025		2817.0	2864.5		76	134	-
	04/05/2025		2864.5	2884.0		76	125	-
	06/05/2025		2884.0	2912.6		76	72	-
	07/05/2025		2912.6	2951.3		76	62	-
	08/05/2025		2951.3	2979.7		76	46	-
	10/05/2025		2979.7	3012.0		76	91	-
	11/05/2025		3012.0	3065.4		76	76	-
	12/05/2025		3065.4	3151.3		76	88	-
	13/05/2025		3151.3	3238.7		76	89	-
	14/05/2025		3238.7	3297.7		76	87	-
	15/05/2025		3297.7	3304.5		76	87	-
	16/05/2025	Sarvak - Kazhdumi	3304.4	3335.4		76	110	-
	17/05/2025	Kazhdumi	3335.4	3401.5		76	92	-
	18/05/2025		3401.5	3450.6		76	96	-
	19/05/2025	Kazhdumi - Dariyan	3450.6	3543.3		76	96	-
	20/05/2025	Dariyan	3543.3	3573.8		76	96	-
	21/05/2025		3573.8	3594.0		76	88	-
	23/05/2025		3594.0	3675.0		76	92	-
	24/05/2025		3675.0	3692.0		76	89	-
6 1/8	06/06/2025	Dariyan	3692.0	3697.0		78	0	-
	08/06/2025	Dariyan - Gadvan	3697.0	3751.0		78	0	-
	09/06/2025	Gadvan	3751.0	3760.0		78	0	-
	11/06/2025		3760.0	3818.4		78	0	-
	12/06/2025		3818.4	3888.0		78	0	-

Table 5-3: AZNS-075-ST1 Mud Loss & Gain

No.	Depth	Formation	Thickness	Shows
1	2469	Ilam	1	Weak
2	2470		1	Fair
3	2471		1	Weak to fair
4	2472 - 2473		2	Weak
5	2559 - 2560	Sarvak	2	Fair
6	2565 - 2566		2	Weak
7	2596		1	Weak to fair
8	2598 - 2600		3	Weak
9	2602 - 2604		7	Weak to fair
10	2606		1	Fair
11	2608		1	Weak to fair
12	2610		1	Fair
13	2614 - 2618		7	Fair to good
14	2626 - 2628		3	Fair
15	2634		1	Fair to good
16	2636		1	Fair
17	2638 - 2644		7	Weak
18	2648		1	Fair to good
19	2650 - 2654		5	Weak
20	2656 - 2660		5	Weak to fair
21	2662		1	Fair to good
22	2664		1	Fair
23	2666 - 2668		3	Good
24	2670 - 2678		9	Fair to good
25	2680		1	Fair
26	2694		1	Weak to fair
27	2696 - 2702		7	Fair
28	2704 - 2714		11	Weak
29	2734		1	Weak
30	3020 - 3048		49	Weak
31	3240 - 3250		11	Weak
32	3252		1	Weak To Fair
33	3254 - 3256		3	Weak
34	3258 - 3260		3	Weak To Fair
35	3262 - 3272		11	Weak
36	3300	Kazhdumi	1	Weak
37	3310		1	Weak To Fair
38	3340 - 3350		11	Weak
39	3360 - 3380		21	Weak To Fair
40	3390		1	Weak
41	3450 - 3490		41	Weak To Fair
42	3500 - 3556		57	Weak
43	3702 - 3850	Gadvan	149	Weak
44	3852 - 3864		13	Good
45	3866 - 3888		23	Weak

Table 5-4: AZNS-075-ST1 Hydrocarbon Shows

5.2 Logging and Testing Reports

Log	Company	Hole Size (inch)	Run No.	Depth Interval (m)	Date
Sonic / Resistivity / GR	Sealand	6 1/8"	1	3700.5 - 3882	08-Jul-25
CNT / NGS *	Sealand	5" L.	2	3645 - 3875	19-Jul-25
SBT / CCL / VDL / GR	Sealand	7" L.	1	2160 - 3669	04-Jun-25
SBT / CCL / VDL / GR	Sealand	5" L.	1	3541 - 3875	06-Aug-25
SBT / CCL / VDL / GR	Sealand	5" L.	1	3596 - 3870	19-Jul-25

Table 5-5: AZNS-075-ST1 Logging Information

5.3 Perforation Reports

Intervals (m)		Thickness (m)	Method	Size	Company
From	To				
3865	3853	12	WCP	5"	Sealand
3852	3849	3			
3846.3	3842	4.3			

Table 5-6: AZNS-075-ST1 Perforation Data

5.4 Directional Drilling Report

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
Original Hole											
2226.44	0.71	2.64	2226.32	-2213.37	0.43	-2.73	-2.73	4.941	3436066.43	186424.27	Tarbur
SideTrackHole											
K.O.P. at 2262.5m (inside of Tarbur Member)											
2265	0.72	266.01	2264.88	-2251.93	1.56	-2.81	-2.81	0	3436066.56	186424.19	
2278.5	4.3	68	2278.36	-2265.41	1.74	-2.43	-2.43	11.083	3436066.74	186424.57	
2288.3	4.6	90	2288.14	-2275.19	1.88	-1.69	-1.69	5.271	3436066.88	186425.31	
2295.5	4.5	86	2295.31	-2282.36	1.9	-1.12	-1.12	1.386	3436066.9	186425.88	
2306.8	4.7	95	2306.58	-2293.63	1.89	-0.22	-0.22	1.986	3436066.89	186426.78	
2316.3	4.6	97	2316.05	-2303.10	1.81	0.55	0.55	0.602	3436066.81	186427.55	
2325.7	4.7	91	2325.41	-2312.46	1.75	1.31	1.31	1.584	3436066.75	186428.31	
2327.34	4.71	89.96	2327.05	-2314.10	0.75	1.44	1.44	1.583	3436066.75	186428.44	L. Gurpi
2335.3	4.8	85	2334.98	-2322.03	1.78	2.1	2.1	1.583	3436066.78	186429.1	
2344.9	5	86.4	2344.55	-2331.60	1.84	2.92	2.92	0.728	3436066.84	186429.92	
2354.4	5.6	87	2354.01	-2341.06	1.89	3.79	3.79	1.903	3436066.89	186430.79	
2364	6.3	90.4	2363.55	-2350.60	1.91	4.79	4.79	2.448	3436066.91	186431.79	
2373.5	7.6	92	2372.98	-2360.03	1.89	5.94	5.94	4.15	3436066.89	186432.94	
2384.15	9	93	2383.52	-2370.57	1.82	7.47	7.47	3.964	3436066.82	186434.47	
2392.74	10	92	2391.99	-2379.04	1.76	8.89	8.89	3.54	3436066.76	186435.89	
2402.1	11.1	92.8	2401.2	-2388.25	1.69	10.6	10.6	3.557	3436066.69	186437.6	
2411.7	11.8	92.1	2410.6	-2397.65	1.61	12.5	12.5	2.23	3436066.61	186439.5	
2421.1	12.1	92.2	2419.8	-2406.85	1.53	14.45	14.45	0.96	3436066.53	186441.45	
2430.7	12.8	91.5	2429.18	-2416.23	1.47	16.52	16.52	2.238	3436066.47	186443.52	
2440.2	13.7	91.2	2438.42	-2425.47	1.42	18.69	18.69	2.85	3436066.42	186445.69	
2449.7	14	90.9	2447.65	-2434.70	1.37	20.97	20.97	0.974	3436066.37	186447.97	
2459.3	14.6	90.8	2456.95	-2444.00	1.34	23.34	23.34	1.877	3436066.34	186450.34	
2468.9	15.4	91	2466.22	-2453.27	1.3	25.82	25.82	2.505	3436066.3	186452.82	
2475.13	15.92	91.33	2472.22	-2459.27	0.27	27.51	27.51	2.536	3436066.27	186454.51	Ilam
2478.5	16.2	91.5	2475.46	-2462.51	1.24	28.44	28.44	2.536	3436066.24	186455.44	
2488.1	17	92.8	2484.66	-2471.71	1.14	31.18	31.18	2.756	3436066.14	186458.18	
2497.7	17.9	92.4	2493.82	-2480.87	1.01	34.05	34.05	2.837	3436066.01	186461.05	
2507.3	18.9	92.5	2502.93	-2489.98	0.88	37.08	37.08	3.127	3436065.88	186464.08	
2516.8	20	92	2511.88	-2498.93	0.76	40.24	40.24	3.513	3436065.76	186467.24	
2526.4	21	91	2520.88	-2507.93	0.67	43.6	43.6	3.311	3436065.67	186470.6	
2536	22	89.5	2529.81	-2516.86	0.65	47.12	47.12	3.566	3436065.65	186474.12	
2536.74	22.08	89.43	2530.49	-2517.54	-0.34	47.4	47.4	3.34	3436065.66	186474.4	Ilam-Main
2545.5	23	88.6	2538.58	-2525.63	0.71	50.76	50.76	3.34	3436065.71	186477.76	
2555.2	23.8	88.7	2547.49	-2534.54	0.81	54.61	54.61	2.477	3436065.81	186481.61	
2555.26	23.8	88.7	2547.54	-2534.59	-0.19	54.63	54.63	8.458	3436065.81	186481.63	Laffan
2556	23.9	89.2	2548.22	-2535.27	0.81	54.93	54.93	8.458	3436065.81	186481.93	
2562.35	24.25	89.31	2554.02	-2541.07	-0.16	57.52	57.52	1.661	3436065.84	186484.52	Sarvak (Sar.-1)
2574.2	24.9	89.5	2564.79	-2551.84	0.9	62.45	62.45	1.661	3436065.9	186489.45	
2583.5	25.9	89.7	2573.19	-2560.24	0.92	66.44	66.44	3.238	3436065.92	186493.44	
2583.74	25.92	89.68	2573.41	-2560.5	-0.08	66.54	66.54	2.736	3436065.92	186493.54	Sar.-2

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
2591.79	26.58	88.94	2580.63	-2567.72	-0.03	70.1	70.1	2.736	3436065.97	186497.1	Sar.-3
2593.3	26.7	88.8	2581.98	-2569.03	0.98	70.78	70.78	2.736	3436065.98	186497.78	
2602.8	27.4	88.3	2590.44	-2577.49	1.09	75.1	75.1	2.324	3436066.09	186502.1	
2612.7	27.9	88.6	2599.21	-2586.26	1.21	79.69	79.69	1.573	3436066.21	186506.69	
2622.2	28.1	88.4	2607.6	-2594.65	1.33	84.15	84.15	0.698	3436066.33	186511.15	
2629.92	28.99	88.89	2614.38	-2601.46	0.42	87.84	87.84	3.59	3436066.42	186514.84	Sar.-4
2631.7	29.2	89	2615.93	-2602.98	1.43	88.7	88.7	3.59	3436066.43	186515.7	
2641.3	30.2	89	2624.27	-2611.32	1.52	93.46	93.46	3.125	3436066.52	186520.46	
2650.8	30.5	89.2	2632.47	-2619.52	1.59	98.26	98.26	1	3436066.59	186525.26	
2660.3	30.6	89.5	2640.65	-2627.70	1.65	103.09	103.09	0.576	3436066.65	186530.09	
2661.88	30.53	89.48	2642.01	-2629.1	0.65	103.89	103.89	1.301	3436066.65	186530.89	Sar.-5
2669.6	30.2	89.4	2648.67	-2635.72	1.69	107.79	107.79	1.301	3436066.69	186534.79	
2679.5	29.9	89.6	2657.24	-2644.29	1.74	112.75	112.75	0.958	3436066.74	186539.75	
2689	29.4	89.8	2665.5	-2652.55	1.76	117.45	117.45	1.61	3436066.76	186544.45	
2698.63	29.8	90	2673.87	-2660.92	1.77	122.2	122.2	1.284	3436066.77	186549.2	
2708.2	29.9	90	2682.17	-2669.22	1.77	126.97	126.97	0.313	3436066.77	186553.97	
2717.9	29.7	89.7	2690.59	-2677.64	1.78	131.79	131.79	0.772	3436066.78	186558.79	
2727.4	29.3	90	2698.86	-2685.91	1.79	136.47	136.47	1.347	3436066.79	186563.47	
2700.95	29.82	90	2675.88	-2662.97	0.77	123.36	123.36	0.313	3436066.77	186550.36	Sar.-6
2731.14	29.26	90	2702.12	-2689.2	0.79	138.3	138.3	0.312	3436066.79	186565.3	Sar.-7
2737	29.2	90	2707.23	-2694.28	1.79	141.16	141.16	0.312	3436066.79	186568.16	
2746.5	29.7	90.2	2715.51	-2702.56	1.79	145.83	145.83	1.609	3436066.79	186572.83	
2750.08	29.78	90.24	2718.61	-2705.69	0.78	147.6	147.6	0.651	3436066.78	186574.6	Sar.-8
2756	29.9	90.3	2723.75	-2710.80	1.76	150.55	150.55	0.651	3436066.76	186577.55	
2765.5	29.8	90.1	2731.99	-2719.04	1.75	155.28	155.28	0.446	3436066.75	186582.28	
2775	30	90.3	2740.22	-2727.27	1.73	160.01	160.01	0.706	3436066.73	186587.01	
2784.5	30.3	90.4	2748.44	-2735.49	1.7	164.78	164.78	0.961	3436066.7	186591.78	
2794	30.3	90.4	2756.64	-2743.69	1.67	169.58	169.58	0	3436066.67	186596.58	
2803.5	30.5	90.1	2764.84	-2751.89	1.65	174.38	174.38	0.793	3436066.65	186601.38	
2813	30.6	90	2773.02	-2760.07	1.64	179.21	179.21	0.354	3436066.64	186606.21	
2815.89	30.51	90.06	2775.51	-2762.57	0.64	180.68	180.68	1	3436066.64	186607.68	Sar.-9
2822.5	30.3	90.2	2781.21	-2768.26	1.64	184.03	184.03	1	3436066.64	186611.03	
2832.2	30.4	90.1	2789.58	-2776.63	1.62	188.93	188.93	0.347	3436066.62	186615.93	
2841.7	30.5	90	2797.77	-2784.82	1.62	193.74	193.74	0.354	3436066.62	186620.74	
2851.2	30.5	90.1	2805.95	-2793.00	1.61	198.57	198.57	0.16	3436066.61	186625.57	
2860.8	30.7	90	2814.22	-2801.27	1.61	203.45	203.45	0.645	3436066.61	186630.45	
2863.12	30.8	90.03	2816.21	-2803.27	0.61	204.64	204.64	1.301	3436066.61	186631.64	Sar.-10
2879.4	31.5	90.2	2830.14	-2817.19	1.59	213.06	213.06	1.301	3436066.59	186640.06	
2889	30.9	90	2838.35	-2825.40	1.58	218.03	218.03	1.903	3436066.58	186645.03	
2898.6	30.5	89.7	2846.61	-2833.66	1.6	222.93	222.93	1.338	3436066.6	186649.93	
2905.94	30.73	89.78	2852.92	-2840.00	0.61	226.67	226.67	0.951	3436066.61	186653.67	Sar.-11
2908.2	30.8	89.8	2854.87	-2841.92	1.62	227.83	227.83	0.951	3436066.62	186654.83	
2917.7	30.9	89.2	2863.02	-2850.07	1.66	232.7	232.7	1.022	3436066.66	186659.7	
2927.2	31.1	89.2	2871.17	-2858.22	1.73	237.59	237.59	0.632	3436066.73	186664.59	

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
2936.7	31.2	89	2879.3	-2866.35	1.81	242.5	242.5	0.454	3436066.81	186669.5	
2946.2	31.2	89.5	2887.42	-2874.47	1.87	247.43	247.43	0.818	3436066.87	186674.43	
2955.7	31.3	89.6	2895.54	-2882.59	1.91	252.35	252.35	0.356	3436066.91	186679.35	
2958.58	31.39	89.66	2898	-2885.07	0.92	253.85	253.85	0.982	3436066.92	186680.85	Sar-12
2965.4	31.6	89.8	2903.82	-2890.87	1.94	257.41	257.41	0.982	3436066.94	186684.41	
2974.9	32	89.2	2911.89	-2898.94	1.98	262.42	262.42	1.61	3436066.98	186689.42	
2984.6	32	89	2920.12	-2907.17	2.06	267.56	267.56	0.328	3436067.06	186694.56	
2994.1	32	89.3	2928.18	-2915.23	2.14	272.59	272.59	0.502	3436067.14	186699.59	
3003.8	31	88.5	2936.45	-2923.50	2.23	277.66	277.66	3.352	3436067.23	186704.66	
3013.35	29.8	88.3	2944.68	-2931.73	2.37	282.49	282.49	3.783	3436067.37	186709.49	
3020.11	29.09	88.23	2950.57	-2937.65	1.47	285.81	285.81	3.145	3436067.47	186712.81	Sar.-Intra
3022.9	28.8	88.2	2953.01	-2940.06	2.51	287.16	287.16	3.145	3436067.51	186714.16	
3032.4	28.4	88.1	2961.35	-2948.40	2.66	291.71	291.71	1.272	3436067.66	186718.71	
3041.9	28	88	2969.72	-2956.77	2.81	296.19	296.19	1.272	3436067.81	186723.19	
3051.38	28.1	88.5	2978.09	-2965.14	2.95	300.65	300.65	0.809	3436067.95	186727.65	
3060.9	28.5	88.6	2986.47	-2973.52	3.06	305.16	305.16	1.269	3436068.06	186732.16	
3070.4	29.1	89.1	2994.8	-2981.85	3.15	309.74	309.74	2.042	3436068.15	186736.74	
3073.37	29.29	89.16	2997.39	-2984.46	2.17	311.19	311.19	1.92	3436068.17	186738.19	Ahmadi Shale
3079.9	29.7	89.3	3003.07	-2990.12	3.22	314.4	314.4	1.92	3436068.22	186741.4	
3089.4	29.6	89.3	3011.33	-2998.38	3.27	319.1	319.1	0.316	3436068.27	186746.1	
3094.99	29.57	89.27	3016.19	-3003.26	2.31	321.86	321.86	0.176	3436068.31	186748.86	Basal Sarvak
3108.4	29.5	89.2	3027.86	-3014.91	3.4	328.47	328.47	0.176	3436068.4	186755.47	
3118	29.5	89.3	3036.21	-3023.26	3.46	333.2	333.2	0.154	3436068.46	186760.2	
3127.6	29.5	89.3	3044.57	-3031.62	3.52	337.92	337.92	0	3436068.52	186764.92	
3137.1	29.5	89.3	3052.84	-3039.89	3.57	342.6	342.6	0	3436068.57	186769.6	
3146.74	29.8	89.5	3061.22	-3048.27	3.62	347.37	347.37	0.983	3436068.62	186774.37	
3156.27	29.7	89.5	3069.49	-3056.54	3.66	352.1	352.1	0.315	3436068.66	186779.1	
3165.8	30.1	89.7	3077.75	-3064.80	3.7	356.85	356.85	1.298	3436068.7	186783.85	
3175.3	30.2	89.9	3085.97	-3073.02	3.71	361.62	361.62	0.448	3436068.71	186788.62	
3184.9	30.4	90	3094.25	-3081.30	3.72	366.46	366.46	0.645	3436068.72	186793.46	
3194.5	30.4	90.2	3102.53	-3089.58	3.71	371.32	371.32	0.316	3436068.71	186798.32	
3204	30.6	90.2	3110.72	-3097.77	3.69	376.14	376.14	0.632	3436068.69	186803.14	
3213.6	30.7	90.2	3118.98	-3106.03	3.68	381.04	381.04	0.312	3436068.68	186808.04	
3223.17	30.5	90.4	3127.22	-3114.27	3.65	385.91	385.91	0.704	3436068.65	186812.91	
3232.68	30.7	90.4	3135.4	-3122.45	3.62	390.75	390.75	0.631	3436068.62	186817.75	
3242.3	30.2	90.5	3143.7	-3130.75	3.58	395.63	395.63	1.567	3436068.58	186822.63	
3251.9	29.8	90.5	3152.01	-3139.06	3.54	400.43	400.43	1.25	3436068.54	186827.43	
3261.5	29.2	90.5	3160.36	-3147.41	3.5	405.15	405.15	1.875	3436068.5	186832.15	
3271	28.8	90.7	3168.67	-3155.72	3.45	409.76	409.76	1.3	3436068.45	186836.76	
3280.5	28.7	90.7	3177	-3164.05	3.39	414.33	414.33	0.316	3436068.39	186841.33	
3289.5	28.5	91	3184.9	-3171.95	3.33	418.63	418.63	0.821	3436068.33	186845.63	
3299.1	29	91.3	3193.32	-3180.37	3.23	423.25	423.25	1.626	3436068.23	186850.25	
3305.26	29	91.43	3198.71	-3185.79	2.16	426.24	426.24	0.306	3436068.16	186853.24	Kazhdumi
3308.6	29	91.5	3201.63	-3188.68	3.12	427.86	427.86	0.306	3436068.12	186854.86	

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
3318.16	28.7	91.8	3210	-3197.05	2.99	432.47	432.47	1.045	3436067.99	186859.47	
3327.74	28.3	91.9	3218.42	-3205.47	2.84	437.04	437.03	1.261	3436067.84	186864.04	
3337.3	29	91.5	3226.81	-3213.86	2.71	441.62	441.62	2.278	3436067.71	186868.62	
3346.9	28.8	91.9	3235.22	-3222.27	2.57	446.25	446.25	0.869	3436067.57	186873.25	
3356.4	28.5	92.2	3243.55	-3230.60	2.41	450.81	450.81	1.051	3436067.41	186877.81	
3366	28	92.4	3252.01	-3239.06	2.22	455.35	455.35	1.59	3436067.22	186882.35	
3375.5	27.4	92.5	3260.42	-3247.47	2.03	459.76	459.76	1.9	3436067.03	186886.76	
3385.1	28	91	3268.92	-3255.97	1.9	464.22	464.22	2.874	3436066.9	186891.22	
3394.7	27.7	90.7	3277.41	-3264.46	1.83	468.7	468.7	1.035	3436066.83	186895.7	
3404.3	28.1	89.4	3285.89	-3272.94	1.83	473.19	473.19	2.275	3436066.83	186900.19	
3414	29	89.3	3294.41	-3281.46	1.88	477.83	477.83	2.787	3436066.88	186904.83	
3423.5	29.4	89.8	3302.71	-3289.76	1.92	482.46	482.46	1.479	3436066.92	186909.46	
3434.04	29.8	90.7	3311.87	-3298.92	1.89	487.67	487.67	1.702	3436066.89	186914.67	
3442.56	29.8	90.7	3319.26	-3306.31	1.84	491.9	491.9	0	3436066.84	186918.9	
3452.08	29.8	91	3327.52	-3314.61	0.77	496.63	496.63	0.467	3436066.77	186923.63	Kaz.-1
3452.13	29.8	91	3327.57	-3314.62	1.77	496.66	496.66	0.467	3436066.77	186923.66	
3461.6	29.6	91.2	3335.79	-3322.84	1.68	501.35	501.35	0.707	3436066.68	186928.35	
3466.04	29.51	91.29	3339.66	-3326.73	0.63	503.54	503.54	0.704	3436066.63	186930.54	Kaz.-2
3471.1	29.4	91.4	3344.06	-3331.11	1.58	506.03	506.03	0.704	3436066.58	186933.03	
3477.52	29	91.67	3349.67	-3336.75	0.49	509.16	509.16	1.971	3436066.49	186936.16	Kaz.-2-2
3480.7	28.8	91.8	3352.45	-3339.50	1.45	510.69	510.69	1.971	3436066.45	186937.69	
3490.3	28.6	91.9	3360.87	-3347.92	1.3	515.3	515.3	0.643	3436066.3	186942.3	
3492.97	28.57	91.93	3363.22	-3350.29	0.25	516.58	516.58	0.346	3436066.25	186943.58	Kaz.-3
3495.27	28.55	91.95	3365.24	-3352.31	0.22	517.68	517.68	0.346	3436066.22	186944.68	Kaz.-4
3499.9	28.5	92	3369.3	-3356.35	1.14	519.89	519.89	0.346	3436066.14	186946.89	
3509.5	28.4	92	3377.74	-3364.79	0.98	524.46	524.46	0.312	3436065.98	186951.46	
3518.92	27.8	92.2	3386.05	-3373.10	0.82	528.89	528.89	1.934	3436065.82	186955.89	
3522.26	27.7	92.44	3389.01	-3376.09	-0.24	530.45	530.45	1.382	3436065.76	186957.45	Kaz.-5
3528.52	27.5	92.9	3394.56	-3381.61	0.62	533.34	533.34	1.382	3436065.62	186960.34	
3533.8	27.39	92.9	3399.24	-3386.32	-0.5	535.77	535.77	0.626	3436065.5	186962.77	Dariyan
3538.1	27.3	92.9	3403.06	-3390.11	0.4	537.75	537.75	0.626	3436065.4	186964.75	
3547.7	27.7	92.4	3411.58	-3398.63	0.19	542.17	542.17	1.443	3436065.19	186969.17	
3557.03	28.2	91.9	3419.82	-3406.87	0.03	546.54	546.54	1.776	3436065.03	186973.54	
3566.49	28.3	91.4	3428.15	-3415.20	-0.1	551.02	551.02	0.815	3436064.9	186978.02	
3575.95	28.8	91.4	3436.46	-3423.51	-0.21	555.54	555.54	1.586	3436064.79	186982.54	
3585.39	29.1	91.2	3444.72	-3431.77	-0.31	560.11	560.11	1.002	3436064.69	186987.11	
3594.9	29.4	91.2	3453.02	-3440.07	-0.41	564.75	564.75	0.946	3436064.59	186991.75	
3604.5	29.4	91.4	3461.38	-3448.43	-0.52	569.46	569.46	0.307	3436064.48	186996.46	
3614	29.9	91.2	3469.64	-3456.69	-0.62	574.16	574.16	1.61	3436064.38	187001.16	
3623.7	30	91.6	3478.05	-3465.10	-0.74	579	579	0.691	3436064.26	187006	
3633.2	30.1	91.6	3486.27	-3473.32	-0.88	583.76	583.76	0.316	3436064.12	187010.76	
3642.9	30.4	91.9	3494.65	-3481.70	-1.03	588.64	588.64	1.039	3436063.97	187015.64	
3652.45	30.8	91.9	3502.87	-3489.92	-1.19	593.5	593.5	1.257	3436063.81	187020.5	
3662	31	91.8	3511.06	-3498.11	-1.34	598.4	598.4	0.649	3436063.66	187025.4	

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
3671.52	31.2	92	3519.21	-3506.26	-1.51	603.32	603.32	0.709	3436063.49	187030.32	
3678	31.2	92.2	3524.76	-3511.81	-1.63	606.67	606.67	0.48	3436063.37	187033.67	
3692.5	31	92.2	3537.17	-3524.22	-1.92	614.16	614.16	0.414	3436063.08	187041.16	
3702.5	31.1	91	3545.74	-3532.79	-2.06	619.31	619.31	1.881	3436062.94	187046.31	
3711.8	31.7	89.5	3553.68	-3540.73	-2.08	624.16	624.16	3.178	3436062.92	187051.16	
3715.67	31.99	88.84	3556.97	-3544.05	-3.05	626.2	626.2	3.496	3436062.95	187053.2	Gadvan (Gad.-1)
3722.5	32.5	87.7	3562.74	-3549.79	-1.94	629.84	629.84	3.496	3436063.06	187056.84	
3728.73	32.21	87.48	3568	-3555.09	-2.8	633.17	633.17	1.521	3436063.2	187060.17	Gad.-2u
3731	32.1	87.4	3569.93	-3556.98	-1.75	634.38	634.38	1.521	3436063.25	187061.38	
3742	31.7	87.6	3579.27	-3566.32	-1.5	640.19	640.19	1.128	3436063.5	187067.19	
3750	32	87.7	3586.06	-3573.11	-1.32	644.41	644.41	1.142	3436063.68	187071.41	
3759.6	32.2	87.7	3594.19	-3581.24	-1.12	649.5	649.5	0.625	3436063.88	187076.5	
3769.1	32	87.6	3602.24	-3589.29	-0.91	654.55	654.55	0.653	3436064.09	187081.55	
3778.8	31.8	87.5	3610.48	-3597.53	-0.69	659.67	659.67	0.64	3436064.31	187086.67	
3788.2	32.4	87.8	3618.44	-3605.49	-0.49	664.66	664.66	1.981	3436064.51	187091.66	
3797.7	33	88	3626.43	-3613.48	-0.3	669.79	669.79	1.925	3436064.7	187096.79	
3798.63	32.99	87.98	3627.21	-3614.3	-1.28	670.29	670.29	0.462	3436064.72	187097.29	Khalij
3807.3	32.9	87.8	3634.49	-3621.54	-0.11	675.01	675.01	0.462	3436064.89	187102.01	
3808.14	32.89	87.81	3635.19	-3622.28	-1.09	675.46	675.46	0.356	3436064.91	187102.46	Gad.-21
3813.91	32.83	87.87	3640.04	-3627.13	-0.97	678.59	678.59	0.356	3436065.03	187105.59	Gad.-3
3816.9	32.8	87.9	3642.55	-3629.60	0.09	680.21	680.21	0.356	3436065.09	187107.21	
3821.76	32.75	87.95	3646.64	-3633.72	-0.82	682.84	682.84	0.359	3436065.18	187109.84	Gad.-4
3826.4	32.7	88	3650.54	-3637.59	0.27	685.35	685.35	0.359	3436065.27	187112.35	
3835.9	32.5	88.6	3658.55	-3645.60	0.42	690.46	690.46	1.2	3436065.42	187117.46	
3837.77	32.46	88.64	3660.12	-3647.21	-0.55	691.47	691.47	0.712	3436065.45	187118.47	Gad.-5a
3845.46	32.3	88.8	3666.62	-3653.67	0.54	695.58	695.58	0.712	3436065.54	187122.58	
3846.35	32.29	88.78	3667.37	-3654.46	-0.45	696.06	696.06	0.46	3436065.55	187123.06	Gad.-5b
3849.6	32.26	88.71	3670.12	-3657.2	-0.41	697.79	697.79	0.46	3436065.59	187124.79	Gad.-5c
3852.01	32.23	88.66	3672.16	-3659.24	-0.38	699.08	699.08	0.46	3436065.62	187126.08	Gad.-5c-2
3855	32.2	88.6	3674.69	-3661.74	0.66	700.67	700.67	0.46	3436065.66	187127.67	
3864.4	32	88.8	3682.65	-3669.70	0.77	705.67	705.67	0.723	3436065.77	187132.67	
3865.38	31.97	88.84	3683.48	-3670.57	-0.22	706.18	706.18	1.146	3436065.78	187133.18	Gad.-6
3874	31.7	89.2	3690.8	-3677.85	0.86	710.73	710.73	1.146	3436065.86	187137.73	
3888	31	89.5	3702.76	-3689.81	0.94	718.01	718.01	1.537	3436065.94	187145.01	T.D.

Table 5-7: AZNS-075-ST1 Directional Drilling Survey

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
1	2268	Tarbur	Good	52	2368	Lower Gurpi	Good
2	2270	Tarbur	Good	53	2370	Lower Gurpi	Good
3	2272	Tarbur	Good	54	2372	Lower Gurpi	Good
4	2274	Tarbur	Good	55	2374	Lower Gurpi	Good
5	2275	Tarbur	Good	56	2376	Lower Gurpi	Good
6	2276	Tarbur	Good	57	2378	Lower Gurpi	Good
7	2278	Tarbur	Good	58	2380	Lower Gurpi	Good
8	2280	Tarbur	Good	59	2382	Lower Gurpi	Good
9	2282	Tarbur	Good	60	2384	Lower Gurpi	Good
10	2284	Tarbur	Good	61	2386	Lower Gurpi	Good
11	2286	Tarbur	Good	62	2388	Lower Gurpi	Good
12	2288	Tarbur	Good	63	2390	Lower Gurpi	Good
13	2290	Tarbur	Good	64	2392	Lower Gurpi	Good
14	2292	Tarbur	Good	65	2394	Lower Gurpi	Good
15	2294	Tarbur	Good	66	2396	Lower Gurpi	Good
16	2296	Tarbur	Good	67	2398	Lower Gurpi	Good
17	2298	Tarbur	Good	68	2400	Lower Gurpi	Good
18	2300	Tarbur	Good	69	2402	Lower Gurpi	Good
19	2302	Tarbur	Good	70	2404	Lower Gurpi	Good
20	2304	Tarbur	Good	71	2406	Lower Gurpi	Good
21	2306	Tarbur	Good	72	2408	Lower Gurpi	Good
22	2308	Tarbur	Good	73	2410	Lower Gurpi	Good
23	2310	Tarbur	Good	74	2412	Lower Gurpi	Good
24	2312	Tarbur	Good	75	2414	Lower Gurpi	Good
25	2314	Tarbur	Good	76	2416	Lower Gurpi	Good
26	2316	Tarbur	Good	77	2418	Lower Gurpi	Good
27	2318	Tarbur	Good	78	2420	Lower Gurpi	Good
28	2320	Tarbur	Good	79	2422	Lower Gurpi	Good
29	2322	Tarbur	Good	80	2424	Lower Gurpi	Good
30	2324	Tarbur	Good	81	2426	Lower Gurpi	Good
31	2326	Tarbur	Good	82	2428	Lower Gurpi	Good
32	2328	Lower Gurpi	Good	83	2430	Lower Gurpi	Good
33	2330	Lower Gurpi	Good	84	2432	Lower Gurpi	Good
34	2332	Lower Gurpi	Good	85	2434	Lower Gurpi	Good
35	2334	Lower Gurpi	Good	86	2436	Lower Gurpi	Good
36	2336	Lower Gurpi	Good	87	2438	Lower Gurpi	Good
37	2338	Lower Gurpi	Good	88	2440	Lower Gurpi	Good
38	2340	Lower Gurpi	Good	89	2442	Lower Gurpi	Good
39	2342	Lower Gurpi	Good	90	2444	Lower Gurpi	Good
40	2344	Lower Gurpi	Good	91	2446	Lower Gurpi	Good
41	2346	Lower Gurpi	Good	92	2448	Lower Gurpi	Good
42	2348	Lower Gurpi	Good	93	2450	Lower Gurpi	Good
43	2350	Lower Gurpi	Good	94	2452	Lower Gurpi	Good
44	2352	Lower Gurpi	Good	95	2454	Lower Gurpi	Good
45	2354	Lower Gurpi	Good	96	2456	Lower Gurpi	Good
46	2356	Lower Gurpi	Good	97	2458	Lower Gurpi	Good
47	2358	Lower Gurpi	Good	98	2460	Lower Gurpi	Good
48	2360	Lower Gurpi	Good	99	2462	Lower Gurpi	Good
49	2362	Lower Gurpi	Good	100	2464	Lower Gurpi	Good
50	2364	Lower Gurpi	Good	101	2466	Lower Gurpi	Good
51	2366	Lower Gurpi	Good	102	2467	Lower Gurpi	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
103	2468	Lower Gurpi	Good	154	2556	Sarvak	Good
104	2469	Ilam	Good	155	2557	Sarvak	Good
105	2470	Ilam	Good	156	2558	Sarvak	Good
106	2471	Ilam	Good	157	2560	Sarvak	Good
107	2472	Ilam	Good	158	2562	Sarvak	Good
108	2473	Ilam	Good	159	2564	Sarvak	Good
109	2474	Ilam	Good	160	2566	Sarvak	Good
110	2476	Ilam	Good	161	2568	Sarvak	Good
111	2478	Ilam	Good	162	2570	Sarvak	Good
112	2480	Ilam	Good	163	2572	Sarvak	Good
113	2482	Ilam	Good	164	2574	Sarvak	Good
114	2484	Ilam	Good	165	2576	Sarvak	Good
115	2486	Ilam	Good	166	2578	Sarvak	Good
116	2488	Ilam	Good	167	2580	Sarvak	Good
117	2490	Ilam	Good	168	2582	Sarvak	Good
118	2492	Ilam	Good	169	2584	Sarvak	Good
119	2494	Ilam	Good	170	2586	Sarvak	Good
120	2496	Ilam	Good	171	2588	Sarvak	Good
121	2498	Ilam	Good	172	2590	Sarvak	Good
122	2500	Ilam	Good	173	2592	Sarvak	Good
123	2502	Ilam	Good	174	2594	Sarvak	Good
124	2504	Ilam	Good	175	2596	Sarvak	Good
125	2506	Ilam	Good	176	2598	Sarvak	Good
126	2508	Ilam	Good	177	2600	Sarvak	Good
127	2510	Ilam	Good	178	2602	Sarvak	Good
128	2512	Ilam	Good	179	2604	Sarvak	Good
129	2514	Ilam	Good	180	2606	Sarvak	Good
130	2516	Ilam	Good	181	2608	Sarvak	Good
131	2518	Ilam	Good	182	2610	Sarvak	Good
132	2520	Ilam	Good	183	2612	Sarvak	Good
133	2522	Ilam	Good	184	2614	Sarvak	Good
134	2524	Ilam	Good	185	2616	Sarvak	Good
135	2526	Ilam	Good	186	2618	Sarvak	Good
136	2528	Ilam	Good	187	2620	Sarvak	Good
137	2530	Ilam	Good	188	2622	Sarvak	Good
138	2532	Ilam	Good	189	2624	Sarvak	Good
139	2534	Ilam	Good	190	2626	Sarvak	Good
140	2536	Ilam	Good	191	2628	Sarvak	Good
141	2538	Ilam	Good	192	2630	Sarvak	Good
142	2540	Ilam	Good	193	2632	Sarvak	Good
143	2542	Ilam	Good	194	2634	Sarvak	Good
144	2544	Ilam	Good	195	2636	Sarvak	Good
145	2546	Ilam	Good	196	2638	Sarvak	Good
146	2548	Ilam	Good	197	2640	Sarvak	Good
147	2549	Laffan	Good	198	2642	Sarvak	Good
148	2550	Laffan	Good	199	2644	Sarvak	Good
149	2551	Laffan	Good	200	2646	Sarvak	Good
150	2552	Laffan	Good	201	2648	Sarvak	Good
151	2553	Laffan	Good	202	2650	Sarvak	Good
152	2554	Laffan	Good	203	2652	Sarvak	Good
153	2555	Laffan	Good	204	2654	Sarvak	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
205	2656	Sarvak	Good	256	2758	Sarvak	Good
206	2658	Sarvak	Good	257	2760	Sarvak	Good
207	2660	Sarvak	Good	258	2762	Sarvak	Good
208	2662	Sarvak	Good	259	2764	Sarvak	Good
209	2664	Sarvak	Good	260	2766	Sarvak	Good
210	2666	Sarvak	Good	261	2768	Sarvak	Good
211	2668	Sarvak	Good	262	2770	Sarvak	Good
212	2670	Sarvak	Good	263	2772	Sarvak	Good
213	2672	Sarvak	Good	264	2774	Sarvak	Good
214	2674	Sarvak	Good	265	2776	Sarvak	Good
215	2676	Sarvak	Good	266	2778	Sarvak	Good
216	2678	Sarvak	Good	267	2780	Sarvak	Good
217	2680	Sarvak	Good	268	2782	Sarvak	Good
218	2682	Sarvak	Good	269	2784	Sarvak	Good
219	2684	Sarvak	Good	270	2786	Sarvak	Good
220	2686	Sarvak	Good	271	2788	Sarvak	Good
221	2688	Sarvak	Good	272	2790	Sarvak	Good
222	2690	Sarvak	Good	273	2792	Sarvak	Good
223	2692	Sarvak	Good	274	2794	Sarvak	Good
224	2694	Sarvak	Good	275	2796	Sarvak	Good
225	2696	Sarvak	Good	276	2798	Sarvak	Good
226	2698	Sarvak	Good	277	2800	Sarvak	Good
227	2700	Sarvak	Good	278	2802	Sarvak	Good
228	2702	Sarvak	Good	279	2804	Sarvak	Good
229	2704	Sarvak	Good	280	2806	Sarvak	Good
230	2706	Sarvak	Good	281	2808	Sarvak	Good
231	2708	Sarvak	Good	282	2810	Sarvak	Good
232	2710	Sarvak	Good	283	2812	Sarvak	Good
233	2712	Sarvak	Good	284	2814	Sarvak	Good
234	2714	Sarvak	Good	285	2816	Sarvak	Good
235	2716	Sarvak	Good	286	2818	Sarvak	Good
236	2718	Sarvak	Good	287	2820	Sarvak	Good
237	2720	Sarvak	Good	288	2822	Sarvak	Good
238	2722	Sarvak	Good	289	2824	Sarvak	Good
239	2724	Sarvak	Good	290	2826	Sarvak	Good
240	2726	Sarvak	Good	291	2828	Sarvak	Good
241	2728	Sarvak	Good	292	2830	Sarvak	Good
242	2730	Sarvak	Good	293	2832	Sarvak	Good
243	2732	Sarvak	Good	294	2834	Sarvak	Good
244	2734	Sarvak	Good	295	2836	Sarvak	Good
245	2736	Sarvak	Good	296	2838	Sarvak	Good
246	2738	Sarvak	Good	297	2840	Sarvak	Good
247	2740	Sarvak	Good	298	2842	Sarvak	Good
248	2742	Sarvak	Good	299	2844	Sarvak	Good
249	2744	Sarvak	Good	300	2846	Sarvak	Good
250	2746	Sarvak	Good	301	2848	Sarvak	Good
251	2748	Sarvak	Good	302	2850	Sarvak	Good
252	2750	Sarvak	Good	303	2852	Sarvak	Good
253	2752	Sarvak	Good	304	2854	Sarvak	Good
254	2754	Sarvak	Good	305	2856	Sarvak	Good
255	2756	Sarvak	Good	306	2858	Sarvak	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
307	2860	Sarvak	Good	358	2962	Sarvak	Good
308	2862	Sarvak	Good	359	2964	Sarvak	Good
309	2864	Sarvak	Good	360	2966	Sarvak	Good
310	2866	Sarvak	Good	361	2968	Sarvak	Good
311	2868	Sarvak	Good	362	2970	Sarvak	Good
312	2870	Sarvak	Good	363	2972	Sarvak	Good
313	2872	Sarvak	Good	364	2974	Sarvak	Good
314	2874	Sarvak	Good	365	2976	Sarvak	Good
315	2876	Sarvak	Good	366	2978	Sarvak	Good
316	2878	Sarvak	Good	367	2980	Sarvak	Good
317	2880	Sarvak	Good	368	2982	Sarvak	Good
318	2882	Sarvak	Good	369	2984	Sarvak	Good
319	2884	Sarvak	Good	370	2986	Sarvak	Good
320	2886	Sarvak	Good	371	2988	Sarvak	Good
321	2888	Sarvak	Good	372	2990	Sarvak	Good
322	2890	Sarvak	Good	373	2992	Sarvak	Good
323	2892	Sarvak	Good	374	2994	Sarvak	Good
324	2894	Sarvak	Good	375	2996	Sarvak	Good
325	2896	Sarvak	Good	376	2998	Sarvak	Good
326	2898	Sarvak	Good	377	3000	Sarvak	Good
327	2900	Sarvak	Good	378	3002	Sarvak	Good
328	2902	Sarvak	Good	379	3004	Sarvak	Good
329	2904	Sarvak	Good	380	3006	Sarvak	Good
330	2906	Sarvak	Good	381	3008	Sarvak	Good
331	2908	Sarvak	Good	382	3010	Sarvak	Good
332	2910	Sarvak	Good	383	3012	Sarvak	Good
333	2912	Sarvak	Good	384	3014	Sarvak	Good
334	2914	Sarvak	Good	385	3016	Sarvak	Good
335	2916	Sarvak	Good	386	3018	Sarvak	Good
336	2918	Sarvak	Good	387	3020	Sarvak	Good
337	2920	Sarvak	Good	388	3022	Sarvak	Good
338	2922	Sarvak	Good	389	3024	Sarvak	Good
339	2924	Sarvak	Good	390	3026	Sarvak	Good
340	2926	Sarvak	Good	391	3028	Sarvak	Good
341	2928	Sarvak	Good	392	3030	Sarvak	Good
342	2930	Sarvak	Good	393	3032	Sarvak	Good
343	2932	Sarvak	Good	394	3034	Sarvak	Good
344	2934	Sarvak	Good	395	3036	Sarvak	Good
345	2936	Sarvak	Good	396	3038	Sarvak	Good
346	2938	Sarvak	Good	397	3040	Sarvak	Good
347	2940	Sarvak	Good	398	3042	Sarvak	Good
348	2942	Sarvak	Good	399	3044	Sarvak	Good
349	2944	Sarvak	Good	400	3046	Sarvak	Good
350	2946	Sarvak	Good	401	3048	Sarvak	Good
351	2948	Sarvak	Good	402	3050	Sarvak	Good
352	2950	Sarvak	Good	403	3052	Sarvak	Good
353	2952	Sarvak	Good	404	3054	Sarvak	Good
354	2954	Sarvak	Good	405	3056	Sarvak	Good
355	2956	Sarvak	Good	406	3058	Sarvak	Good
356	2958	Sarvak	Good	407	3060	Sarvak	Good
357	2960	Sarvak	Good	408	3062	Sarvak	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
409	3064	Sarvak	Good	460	3166	Sarvak	Good
410	3066	Sarvak	Good	461	3168	Sarvak	Good
411	3068	Sarvak	Good	462	3170	Sarvak	Good
412	3070	Sarvak	Good	463	3172	Sarvak	Good
413	3072	Sarvak	Good	464	3174	Sarvak	Good
414	3074	Sarvak	Good	465	3176	Sarvak	Good
415	3076	Sarvak	Good	466	3178	Sarvak	Good
416	3078	Sarvak	Good	467	3180	Sarvak	Good
417	3080	Sarvak	Good	468	3182	Sarvak	Good
418	3082	Sarvak	Good	469	3184	Sarvak	Good
419	3084	Sarvak	Good	470	3186	Sarvak	Good
420	3086	Sarvak	Good	471	3188	Sarvak	Good
421	3088	Sarvak	Good	472	3190	Sarvak	Good
422	3090	Sarvak	Good	473	3192	Sarvak	Good
423	3092	Sarvak	Good	474	3194	Sarvak	Good
424	3094	Sarvak	Good	475	3196	Sarvak	Good
425	3096	Sarvak	Good	476	3198	Sarvak	Good
426	3098	Sarvak	Good	477	3200	Sarvak	Good
427	3100	Sarvak	Good	478	3202	Sarvak	Good
428	3102	Sarvak	Good	479	3204	Sarvak	Good
429	3104	Sarvak	Good	480	3206	Sarvak	Good
430	3106	Sarvak	Good	481	3208	Sarvak	Good
431	3108	Sarvak	Good	482	3210	Sarvak	Good
432	3110	Sarvak	Good	483	3212	Sarvak	Good
433	3112	Sarvak	Good	484	3214	Sarvak	Good
434	3114	Sarvak	Good	485	3216	Sarvak	Good
435	3116	Sarvak	Good	486	3218	Sarvak	Good
436	3118	Sarvak	Good	487	3220	Sarvak	Good
437	3120	Sarvak	Good	488	3221	Sarvak	Good
438	3122	Sarvak	Good	489	3222	Sarvak	Good
439	3124	Sarvak	Good	490	3224	Sarvak	Good
440	3126	Sarvak	Good	491	3226	Sarvak	Good
441	3128	Sarvak	Good	492	3228	Sarvak	Good
442	3130	Sarvak	Good	493	3230	Sarvak	Good
443	3132	Sarvak	Good	494	3232	Sarvak	Good
444	3134	Sarvak	Good	495	3234	Sarvak	Good
445	3136	Sarvak	Good	496	3236	Sarvak	Good
446	3138	Sarvak	Good	497	3238	Sarvak	Good
447	3140	Sarvak	Good	498	3240	Sarvak	Good
448	3142	Sarvak	Good	499	3242	Sarvak	Good
449	3144	Sarvak	Good	500	3244	Sarvak	Good
450	3146	Sarvak	Good	501	3245	Sarvak	Good
451	3148	Sarvak	Good	502	3246	Sarvak	Good
452	3150	Sarvak	Good	503	3248	Sarvak	Good
453	3152	Sarvak	Good	504	3250	Sarvak	Good
454	3154	Sarvak	Good	505	3252	Sarvak	Good
455	3156	Sarvak	Good	506	3254	Sarvak	Good
456	3158	Sarvak	Good	507	3256	Sarvak	Good
457	3160	Sarvak	Good	508	3258	Sarvak	Good
458	3162	Sarvak	Good	509	3260	Sarvak	Good
459	3164	Sarvak	Good	510	3262	Sarvak	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
511	3264	Sarvak	Good	562	3334	Kazhdumi	Good
512	3266	Sarvak	Good	563	3336	Kazhdumi	Good
513	3268	Sarvak	Good	564	3338	Kazhdumi	Good
514	3270	Sarvak	Good	565	3340	Kazhdumi	Good
515	3272	Sarvak	Good	566	3342	Kazhdumi	Good
516	3274	Sarvak	Good	567	3344	Kazhdumi	Good
517	3276	Sarvak	Good	568	3346	Kazhdumi	Good
518	3278	Sarvak	Good	569	3348	Kazhdumi	Good
519	3280	Sarvak	Good	570	3350	Kazhdumi	Good
520	3282	Sarvak	Good	571	3352	Kazhdumi	Good
521	3284	Sarvak	Good	572	3354	Kazhdumi	Good
522	3286	Sarvak	Good	573	3356	Kazhdumi	Good
523	3288	Sarvak	Good	574	3358	Kazhdumi	Good
524	3290	Sarvak	Good	575	3360	Kazhdumi	Good
525	3292	Sarvak	Good	576	3362	Kazhdumi	Good
526	3294	Sarvak	Good	577	3364	Kazhdumi	Good
527	3295	Sarvak	Good	578	3366	Kazhdumi	Good
528	3296	Sarvak	Good	579	3368	Kazhdumi	Good
529	3297	Sarvak	Good	580	3370	Kazhdumi	Good
530	3298	Sarvak	Good	581	3372	Kazhdumi	Good
531	3299	Kazhdumi	Good	582	3374	Kazhdumi	Good
532	3300	Kazhdumi	Good	583	3376	Kazhdumi	Good
533	3301	Kazhdumi	Good	584	3378	Kazhdumi	Good
534	3302	Kazhdumi	Good	585	3380	Kazhdumi	Good
535	3303	Kazhdumi	Good	586	3382	Kazhdumi	Good
536	3304	Kazhdumi	Good	587	3384	Kazhdumi	Good
537	3305	Kazhdumi	Good	588	3386	Kazhdumi	Good
538	3306	Kazhdumi	Good	589	3388	Kazhdumi	Good
539	3307	Kazhdumi	Good	590	3390	Kazhdumi	Good
540	3308	Kazhdumi	Good	591	3392	Kazhdumi	Good
541	3309	Kazhdumi	Good	592	3394	Kazhdumi	Good
542	3310	Kazhdumi	Good	593	3396	Kazhdumi	Good
543	3311	Kazhdumi	Good	594	3398	Kazhdumi	Good
544	3312	Kazhdumi	Good	595	3400	Kazhdumi	Good
545	3313	Kazhdumi	Good	596	3402	Kazhdumi	Good
546	3314	Kazhdumi	Good	597	3404	Kazhdumi	Good
547	3315	Kazhdumi	Good	598	3406	Kazhdumi	Good
548	3316	Kazhdumi	Good	599	3408	Kazhdumi	Good
549	3317	Kazhdumi	Good	600	3410	Kazhdumi	Good
550	3318	Kazhdumi	Good	601	3412	Kazhdumi	Good
551	3319	Kazhdumi	Good	602	3414	Kazhdumi	Good
552	3320	Kazhdumi	Good	603	3416	Kazhdumi	Good
553	3321	Kazhdumi	Good	604	3418	Kazhdumi	Good
554	3322	Kazhdumi	Good	605	3420	Kazhdumi	Good
555	3323	Kazhdumi	Good	606	3422	Kazhdumi	Good
556	3324	Kazhdumi	Good	607	3424	Kazhdumi	Good
557	3325	Kazhdumi	Good	608	3426	Kazhdumi	Good
558	3326	Kazhdumi	Good	609	3428	Kazhdumi	Good
559	3328	Kazhdumi	Good	610	3430	Kazhdumi	Good
560	3330	Kazhdumi	Good	611	3432	Kazhdumi	Good
561	3332	Kazhdumi	Good	612	3434	Kazhdumi	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
613	3436	Kazhdumi	Good	664	3531	Dariyan	Good
614	3438	Kazhdumi	Good	665	3532	Dariyan	Good
615	3440	Kazhdumi	Good	666	3533	Dariyan	Good
616	3442	Kazhdumi	Good	667	3534	Dariyan	Good
617	3444	Kazhdumi	Good	668	3535	Dariyan	Good
618	3445	Kazhdumi	Good	669	3536	Dariyan	Good
619	3446	Kazhdumi	Good	670	3538	Dariyan	Good
620	3447	Kazhdumi	Good	671	3540	Dariyan	Good
621	3448	Kazhdumi	Good	672	3542	Dariyan	Good
622	3449	Kazhdumi	Good	673	3544	Dariyan	Good
623	3450	Kazhdumi	Good	674	3546	Dariyan	Good
624	3452	Kazhdumi	Good	675	3548	Dariyan	Good
625	3454	Kazhdumi	Good	676	3550	Dariyan	Good
626	3456	Kazhdumi	Good	677	3552	Dariyan	Good
627	3458	Kazhdumi	Good	678	3554	Dariyan	Good
628	3460	Kazhdumi	Good	679	3556	Dariyan	Good
629	3462	Kazhdumi	Good	680	3558	Dariyan	Good
630	3464	Kazhdumi	Good	681	3560	Dariyan	Good
631	3466	Kazhdumi	Good	682	3562	Dariyan	Good
632	3468	Kazhdumi	Good	683	3564	Dariyan	Good
633	3470	Kazhdumi	Good	684	3566	Dariyan	Good
634	3472	Kazhdumi	Good	685	3568	Dariyan	Good
635	3474	Kazhdumi	Good	686	3570	Dariyan	Good
636	3476	Kazhdumi	Good	687	3572	Dariyan	Good
637	3478	Kazhdumi	Good	688	3574	Dariyan	Good
638	3480	Kazhdumi	Good	689	3576	Dariyan	Good
639	3482	Kazhdumi	Good	690	3578	Dariyan	Good
640	3484	Kazhdumi	Good	691	3580	Dariyan	Good
641	3486	Kazhdumi	Good	692	3582	Dariyan	Good
642	3488	Kazhdumi	Good	693	3584	Dariyan	Good
643	3490	Kazhdumi	Good	694	3586	Dariyan	Good
644	3492	Kazhdumi	Good	695	3588	Dariyan	Good
645	3494	Kazhdumi	Good	696	3590	Dariyan	Good
646	3496	Kazhdumi	Good	697	3592	Dariyan	Good
647	3498	Kazhdumi	Good	698	3594	Dariyan	Good
648	3500	Kazhdumi	Good	699	3596	Dariyan	Good
649	3502	Kazhdumi	Good	700	3598	Dariyan	Good
650	3504	Kazhdumi	Good	701	3600	Dariyan	Good
651	3506	Kazhdumi	Good	702	3602	Dariyan	Good
652	3508	Kazhdumi	Good	703	3604	Dariyan	Good
653	3510	Kazhdumi	Good	704	3606	Dariyan	Good
654	3512	Kazhdumi	Good	705	3608	Dariyan	Good
655	3514	Kazhdumi	Good	706	3610	Dariyan	Good
656	3516	Kazhdumi	Good	707	3612	Dariyan	Good
657	3518	Kazhdumi	Good	708	3614	Dariyan	Good
658	3520	Kazhdumi	Good	709	3616	Dariyan	Good
659	3522	Kazhdumi	Good	710	3618	Dariyan	Good
660	3524	Kazhdumi	Good	711	3620	Dariyan	Good
661	3526	Kazhdumi	Good	712	3622	Dariyan	Good
662	3528	Dariyan	Good	713	3624	Dariyan	Good
663	3530	Dariyan	Good	714	3626	Dariyan	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
715	3628	Dariyan	Good	766	3718	Gadvan	Good
716	3630	Dariyan	Good	767	3720	Gadvan	Good
717	3632	Dariyan	Good	768	3722	Gadvan	Good
718	3634	Dariyan	Good	769	3724	Gadvan	Good
719	3636	Dariyan	Good	770	3726	Gadvan	Good
720	3638	Dariyan	Good	771	3728	Gadvan	Good
721	3640	Dariyan	Good	772	3730	Gadvan	Good
722	3642	Dariyan	Good	773	3732	Gadvan	Good
723	3644	Dariyan	Good	774	3734	Gadvan	Good
724	3646	Dariyan	Good	775	3736	Gadvan	Good
725	3648	Dariyan	Good	776	3738	Gadvan	Good
726	3650	Dariyan	Good	777	3740	Gadvan	Good
727	3652	Dariyan	Good	778	3742	Gadvan	Good
728	3654	Dariyan	Good	779	3744	Gadvan	Good
729	3656	Dariyan	Good	780	3746	Gadvan	Good
730	3658	Dariyan	Good	781	3748	Gadvan	Good
731	3660	Dariyan	Good	782	3750	Gadvan	Good
732	3662	Dariyan	Good	783	3752	Gadvan	Good
733	3664	Dariyan	Good	784	3754	Gadvan	Good
734	3666	Dariyan	Good	785	3756	Gadvan	Good
735	3668	Dariyan	Good	786	3758	Gadvan	Good
736	3670	Dariyan	Good	787	3760	Gadvan	Good
737	3672	Dariyan	Good	788	3762	Gadvan	Good
738	3674	Dariyan	Good	789	3764	Gadvan	Good
739	3676	Dariyan	Good	790	3766	Gadvan	Good
740	3678	Dariyan	Good	791	3768	Gadvan	Good
741	3680	Dariyan	Good	792	3770	Gadvan	Good
742	3682	Dariyan	Good	793	3772	Gadvan	Good
743	3684	Dariyan	Good	794	3774	Gadvan	Good
744	3686	Dariyan	Good	795	3776	Gadvan	Good
745	3688	Dariyan	Good	796	3778	Gadvan	Good
746	3690	Dariyan	Good	797	3780	Gadvan	Good
747	3692	Dariyan	Good	798	3782	Gadvan	Good
748	3694	Dariyan	Good	799	3784	Gadvan	Good
749	3696	Dariyan	Good	800	3785	Gadvan	Good
750	3697	Dariyan	Good	801	3786	Gadvan	Good
751	3698	Dariyan	Good	802	3787	Gadvan	Good
752	3700	Dariyan	Good	803	3788	Gadvan	Good
753	3702	Dariyan	Good	804	3789	Gadvan	Good
754	3704	Dariyan	Good	805	3790	Gadvan	Good
755	3705	Dariyan	Good	806	3791	Gadvan	Good
756	3706	Dariyan	Good	807	3792	Gadvan	Good
757	3707	Dariyan	Good	808	3793	Gadvan	Good
758	3708	Dariyan	Good	809	3794	Gadvan	Good
759	3709	Gadvan	Good	810	3795	Gadvan	Good
760	3710	Gadvan	Good	811	3796	Gadvan	Good
761	3711	Gadvan	Good	812	3798	Gadvan	Good
762	3712	Gadvan	Good	813	3800	Gadvan	Good
763	3713	Gadvan	Good	814	3802	Gadvan	Good
764	3714	Gadvan	Good	815	3804	Gadvan	Good
765	3716	Gadvan	Good	816	3806	Gadvan	Good

No.	Sample Depth	Formation/ Member	Sample Quality	No.	Sample Depth	Formation/ Member	Sample Quality
817	3808	Gadvan	Good	842	3842	Gadvan	Good
818	3810	Gadvan	Good	843	3844	Gadvan	Good
819	3812	Gadvan	Good	844	3846	Gadvan	Good
820	3814	Gadvan	Good	845	3848	Gadvan	Good
821	3816	Gadvan	Good	846	3850	Gadvan	Good
822	3818	Gadvan	Good	847	3852	Gadvan	Good
823	3820	Gadvan	Good	848	3854	Gadvan	Good
824	3822	Gadvan	Good	849	3856	Gadvan	Good
825	3823	Gadvan	Good	850	3858	Gadvan	Good
826	3824	Gadvan	Good	851	3860	Gadvan	Good
827	3825	Gadvan	Good	852	3862	Gadvan	Good
828	3826	Gadvan	Good	853	3864	Gadvan	Good
829	3827	Gadvan	Good	854	3866	Gadvan	Good
830	3828	Gadvan	Good	855	3868	Gadvan	Good
831	3829	Gadvan	Good	856	3870	Gadvan	Good
832	3830	Gadvan	Good	857	3872	Gadvan	Good
833	3831	Gadvan	Good	858	3874	Gadvan	Good
834	3832	Gadvan	Good	859	3876	Gadvan	Good
835	3833	Gadvan	Good	860	3878	Gadvan	Good
836	3834	Gadvan	Good	861	3880	Gadvan	Good
837	3835	Gadvan	Good	862	3882	Gadvan	Good
838	3836	Gadvan	Good	863	3884	Gadvan	Good
839	3837	Gadvan	Good	864	3886	Gadvan	Good
840	3838	Gadvan	Good	865	3888	Gadvan	Good
841	3840	Gadvan	Good				

Table 5-8: AZNS-075-ST1 Sample Interval & Quality (Cutting Collection)

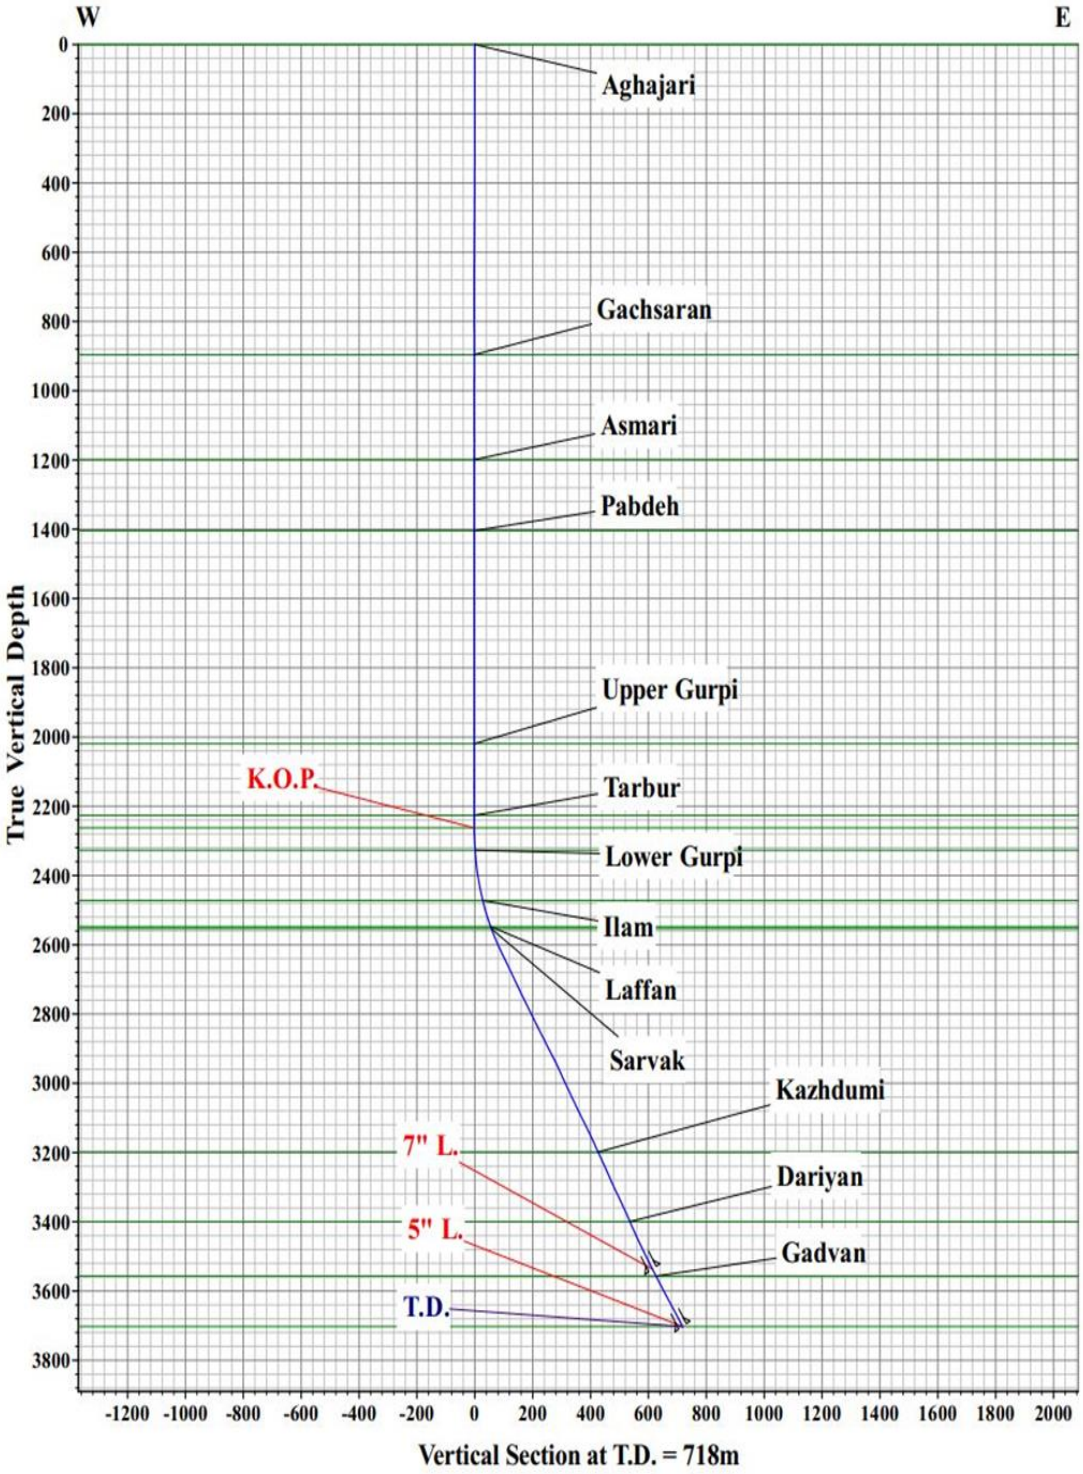


Figure 5-1: AZNS-075-ST1 Cross Section

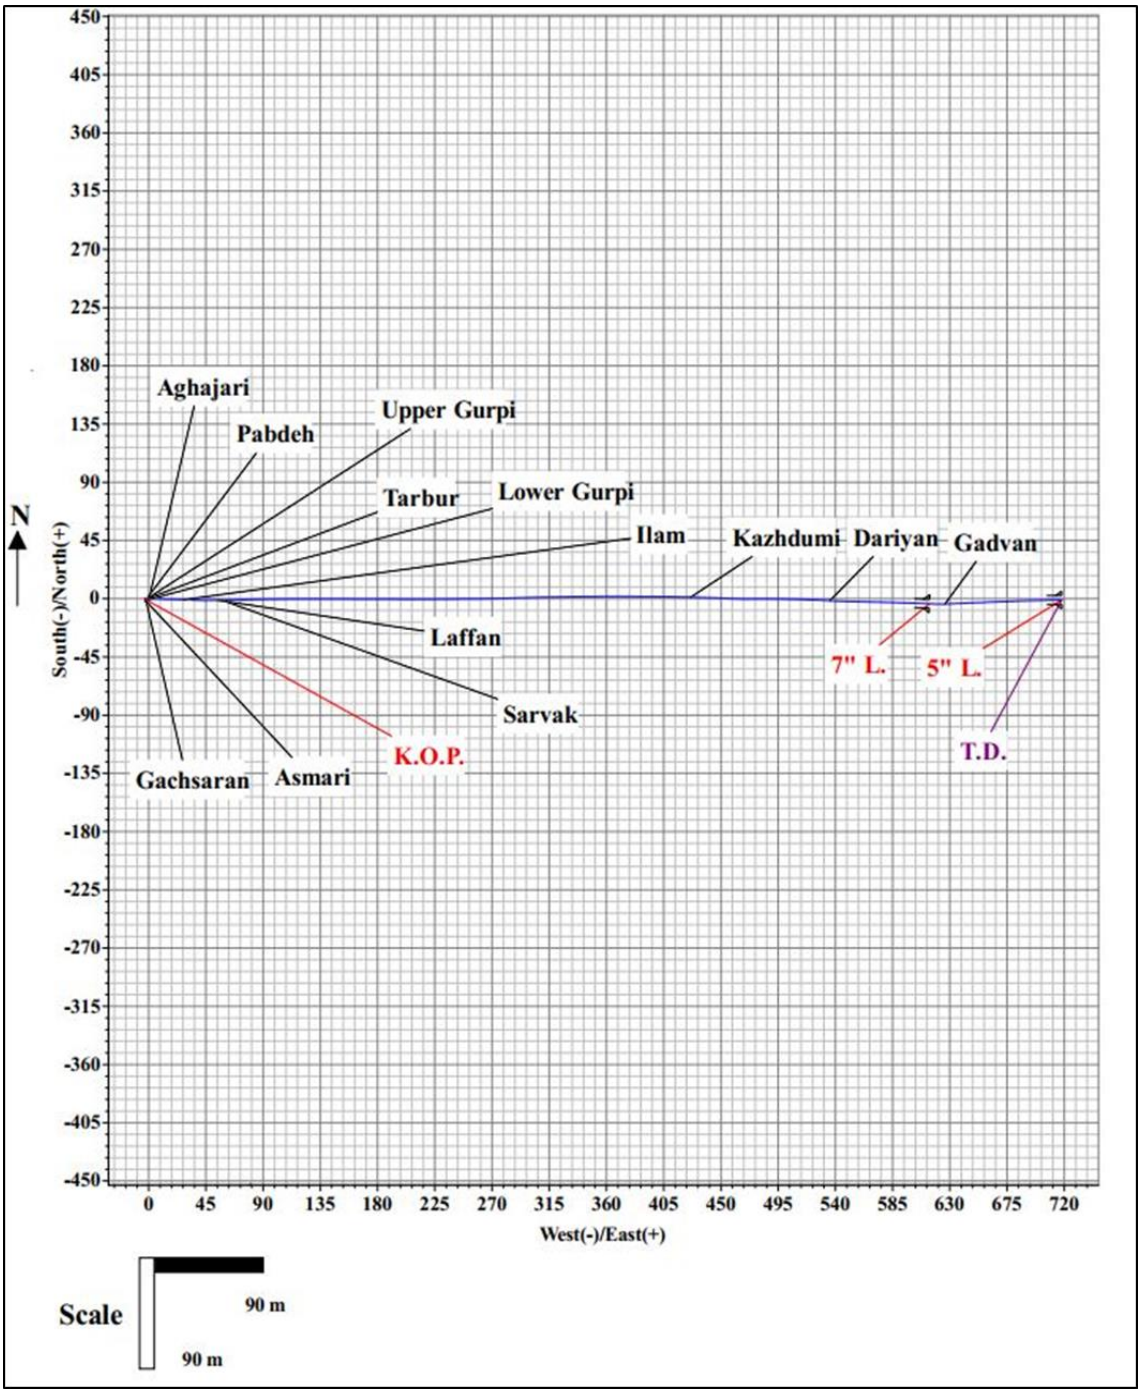


Figure 5-2: AZNS-075-ST1 Plan View

6. Bottom Hole Assembly Record

This is a record of the bottom hole assemblies (BHA) used to drill the various sections of this well.

Each assembly has been treated for every bit run in the hole and besides the listing of the components of the drilling assembly, it also includes additional information of interest pertaining to that run such as the drilling and mud parameters, casing details, highlights of the run, discharge to RPM ratios of down hole motors, hydraulic inferences such as bit efficiencies, annular and impact velocities, ECD, circulating hours that are all inclusive for the bit run, a record of met rage and Bit life for that run and the cumulative life and met rage produced where bits are re-run, tripping times and any other data that might be considered relevant or interesting.

Date : 29.03.2025

7" Liner Shoe @ 3799.5m ; ID: 6.184" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA # 1	Length	Cum Lgth
B.Bit	0.14	0.14
7" Scraper	1.06	1.20
Bit sub	0.86	2.05
12 × 3 ½" HWDP	110.41	112.46
116 × 3 ½" DP	1117.82	1230.28
XOS	1.030	1231.31
9 ⅝" Scraper	1.63	1232.94
TOTAL BHA		**1232.94**

Bit Data

Bit #	1
Size	6"
Type	B.Bit
Mfgr	--
Serial No.	--
Nozzles	Open
IADC Code	--
Depth In	3799.5
Depth Out	3799.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	41
PV / YP	12/7
Gel 0 / 10	2/4
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to run log.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 03.04.2025

7" Liner Shoe @ 3799.5m ; ID: 6.184" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA # 2	Length	Cum Lgth
6 ⅛" Tri-Cone Bit	0.14	0.14
Bit sub	0.86	1.00
27 × 3 ½" HWDP	248.63	249.63
90 × 3 ½" DP	866.57	1116.20
XOS	1.03	1117.23
TOTAL BHA		**1117.23**

Bit Data

Bit #	2
Size	6 ⅛"
Type	Tri-Cone Bit
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3799.5
Depth Out	3799.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-DTF

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	41
PV / YP	12/7
Gel 0 / 10	2/4
Alk. / HPHT	9.3
FLT °C	--

Reason for POOH :

POOH due to downhole tool failure.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 07.04.2025

7" Liner Shoe @ 3799.5m ; ID: 6.184" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA # 3	Length	Cum Lgth
8 ½" Tri Cone bit	0.24	0.24
6 ½" Bit sub	0.95	1.19
9 × 6 ½" DC	81.52	82.71
TOTAL BHA		**82.71**

Bit Data

Bit #	3
Size	8½"
Type	Tri-Cone
Mfgr	--
Serial No.	HGT517GL
Nozzles	Open
IADC Code	--
Depth In	3799.5
Depth Out	3799.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	41
PV / YP	12/7
Gel 0 / 10	2/4
Alk. / HPHT	9.3
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 12.04.2025

7" Liner Shoe @ 3799.5m ; ID: 6.184" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA # 4	Length	Cum Lgth
8 ½" Tri Cone bit	0.24	0.24
6 ½" Bit sub	0.95	1.19
9 ⅝" Scraper	1.63	2.82
3 × 6 ½" DC	27.10	29.92
TOTAL BHA		29.92

Bit Data

Bit #	3 Run#2
Size	8½"
Type	Tri-Cone
Mfgr	--
Serial No.	HGT517GL
Nozzles	Open
IADC Code	--
Depth In	3799.5
Depth Out	3799.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	80-84
FV (sec)	38-41
PV / YP	12/6
Gel 0 / 10	2/4
Alk. / HPHT	9.3-10.2
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 18.04.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 5	Length	Cum Lgth
8 ⅜" B.Bit	0.25	0.25
6 ¾" PDM	8.02	8.27
6 ¾" F.Sub	0.42	8.69
6 ½" UBHO	1.00	9.69
6 ⅜" NMDC	9.22	18.91
6 ½" Gyro sub	0.60	19.51
24 × 5" HWDP	222.79	242.30
6 ½" Jar + FLEX	8.79	251.09
6 × 5" HWDP	55.76	306.85
TOTAL BHA		306.85

Bit Data

Bit #	5
Size	8 ⅜"
Type	Tri cone mill
Mfgr	king Dream
Serial No.	2417584JH
Nozzles	Open
IADC Code	3 × 16
Depth In	3799.5
Depth Out	3799.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	38
PV / YP	11/9
Gel 0 / 10	2/4
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 18.04.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 6	Length	Cum Lgth
8 ⅜" B.Bit	0.25	0.25
6 ¾" PDM	8.02	8.27
6 ¾" F.Sub	0.42	8.69
6 ½" UBHO	1.00	9.69
6 ⅜" NMDC	9.22	18.91
6 ½" Gyro sub	0.60	19.51
24 × 5" HWDP	222.79	242.30
6 ½" Jar + FLEX	8.79	251.09
6 × 5" HWDP	55.76	306.85
TOTAL BHA		**306.85**

Bit Data

Bit #	5 Run#2
Size	8 ⅜"
Type	Tri cone mill
Mfgr	king Dream
Serial No.	2417584JH
Nozzles	3 × 16
IADC Code	HJT537G
Depth In	2266
Depth Out	2310
Metrage	44.00
Hours Run	18.9
Av. ROP	2.33
Condition	1.1.WT.A.E.I.NO.BHA

Performance Record :

Total Revolution On Bit : 113.40 krev

This Run (44m) : 18.9 hrs

Cumulative Bit Life (44m) : 18.9 hrs

Drilling & Mud Parameters :

WOB (klb)	12-18
RPM (rpm)	35-162
TOR (lbf.ft)	2-7
SPP (psi)	1580-1680
FLOW (gpm)	450
MW (pcf)	76
FV (sec)	38
PV / YP	10/11
Gel 0 / 10	2/4
Alk. / HPHT	9.1
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 21.04.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 7	Length	Cum Lgth
8 ⅜" PDC Bit	0.28	0.28
6 ¾" PDM	8.02	8.30
6 ¾" F.Sub	0.42	8.72
6 ½" UBHO	1.00	9.72
6 ⅜" NMDC	9.22	18.94
24 × 5" HWDP	222.79	241.73
6 ½" Jar + FLEX	8.79	250.52
6 × 5" HWDP	55.76	306.28
TOTAL BHA		**306.28**

Bit Data

Bit #	6
Size	8 ⅜"
Type	PDC Bit
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M1375
Depth In	2310
Depth Out	2620
Metrage	310
Hours Run	125.25
Av. ROP	2.15
Condition	0-1-BT-S-X-I-NO-DMF

Performance Record :

Total Revolution On Bit : 751.50 krev

This Run (310m) : 125.25 hrs

Cumulative Bit Life (310m) : 125.25 hrs

Drilling & Mud Parameters :

WOB (klb)	5-20
RPM (rpm)	35-160
TOR (lbf.ft)	1-4
SPP (psi)	1300-1600
FLOW (gpm)	380-490
MW (pcf)	76
FV (sec)	39-40
PV / YP	9/10
Gel 0 / 10	2/4
Alk. / HPHT	9.1/9.2
FLT °C	--

Reason for POOH :

POOH due to downhole motor failure.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 28.04.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 8	Length	Cum Lgth
8 ⅜" PDC Bit	0.28	0.28
6 ¾" PDM	7.99	8.27
6 ¾" F.Sub	0.47	8.74
6 ½" UBHO	1.00	9.74
6 ⅜" NMDC	9.22	18.96
24 × 5" HWDP	222.79	241.75
6 ½" Jar + FLEX	8.79	250.54
6 × 5" HWDP	55.76	306.30
TOTAL BHA		**306.30**

Bit Data

Bit #	6 Run#2
Size	8 ⅜"
Type	PDC Bit
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M1375
Depth In	2620
Depth Out	2884
Metrage	264
Hours Run	100.75
Av. ROP	2.45
Condition	2-3-WT-A-X-I-NO-BHA

Performance Record :

Total Revolution On Bit : 1356.00 krev

This Run (264m) : 100.75 hrs

Cumulative Bit Life (574m) : 226.0 hrs

Drilling & Mud Parameters :

WOB (klb)	2-18
RPM (rpm)	35-160
TOR (lbf.ft)	2-5
SPP (psi)	1350-1650
FLOW (gpm)	435-465
MW (pcf)	76
FV (sec)	47
PV / YP	9/14
Gel 0 / 10	3/4
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 05.05.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 9	Length	Cum Lgth
8 ⅜" PDC Bit	0.28	0.28
6 ¾" PDM	7.96	8.24
6 ¾" F.Sub	0.42	8.66
6 ½" UBHO	0.84	9.50
6 ⅜" NMDC	9.13	18.63
24 × 5" HWDP	222.79	241.42
6 ½" Jar + FLEX	8.79	250.21
6 × 5" HWDP	55.76	305.97
TOTAL BHA		**305.97**

Bit Data

Bit #	6 Run#3
Size	8 ⅜"
Type	PDC Bit
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M1375
Depth In	2884
Depth Out	2979.7
Metrage	95.7
Hours Run	47.25
Av. ROP	2.00
Condition	2-3-WT-A-X-I-NO-BHA

Performance Record :

Total Revolution On Bit : 1667.85 krev

This Run (95.7m) : 47.25 hrs

Cumulative Bit Life (669.7m) : 273.3 hrs

Drilling & Mud Parameters :

WOB (klb)	4-20
RPM (rpm)	40-180
TOR (lbf.ft)	3-6
SPP (psi)	1750-2150
FLOW (gpm)	450-500
MW (pcf)	76
FV (sec)	46
PV / YP	10/13
Gel 0 / 10	2/4
Alk. / HPHT	9.6
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 09.05.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 10	Length	Cum Lgth
8 ⅜" PDC Bit	0.28	0.28
6 ¾" PDM	7.96	8.24
6 ¾" F.Sub	0.42	8.66
S.Stabilizer	1.79	10.45
6 ½" UBHO	0.84	11.29
6 ⅜" NMDC	9.13	20.42
24 × 5" HWDP	222.79	243.21
6 ½" Jar + FLEX	8.79	252.00
6 × 5" HWDP	55.76	307.76
TOTAL BHA		307.76

Bit Data

Bit #	6 Run#4
Size	8 ⅜"
Type	PDC Bit
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M1375
Depth In	2979.7
Depth Out	3304.5
Metrage	324.8
Hours Run	120.19
Av. ROP	2.96
Condition	3-5-BT-A-X-I-BU(5%)-BHA

Performance Record :

Total Revolution On Bit : 1667.85 krev

This Run (324.8m) : 120.19 hrs

Cumulative Bit Life (994.5m) : 393.44 hrs

Drilling & Mud Parameters :

WOB (klb)	5-20
RPM (rpm)	30-40/170-180
TOR (lbf.ft)	3-10
SPP (psi)	2000-2400
FLOW (gpm)	470-510
MW (pcf)	76
FV (sec)	45
PV / YP	14/11
Gel 0 / 10	2/4
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 16.05.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 11	Length	Cum Lgth
8 ⅜" PDC Bit	0.28	0.28
6 ¾" PDM	7.96	8.24
6 ¾" F.Sub	0.42	8.66
S.Stabilizer	1.79	10.45
6 ½" UBHO	0.84	11.29
6 ⅜" NMDC	9.13	20.42
24 × 5" HWDP	222.79	243.21
6 ½" Jar + FLEX	8.90	252.11
6 × 5" HWDP	55.76	307.87
TOTAL BHA		307.87

Bit Data

Bit #	7
Size	8 ⅜"
Type	PDC Bit
Mfgr	Best
Serial No.	220793
Nozzles	7 × 14
IADC Code	M1375
Depth In	3304.5
Depth Out	3594
Metrage	289.5
Hours Run	117
Av. ROP	2.48
Condition	1.1.WT.A.X.I.NO.BHA

Performance Record :

Total Revolution On Bit : 1472.20 krev

This Run (289.5m) : 117.00 hrs

Cumulative Bit Life (289.5m) : 117.00 hrs

Drilling & Mud Parameters :

WOB (klb)	10-40
RPM (rpm)	30-40/170-180
TOR (lbf.ft)	3-8
SPP (psi)	2100-2400
FLOW (gpm)	490-510
MW (pcf)	76
FV (sec)	47
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 22.05.2025

9 ⅝" Casing Shoe @ 2477.5m ; ID: 8.681" ; Weight : 47lb/ft

Phase Diameter : 8 ⅜"

BHA # 12	Length	Cum Lgth
8 ⅜" PDC Bit	0.28	0.28
6 ¾" PDM	7.96	8.24
6 ¾" F.Sub	0.42	8.66
6 ½" UBHO	0.91	9.57
6 ⅜" NMDC	9.17	18.74
24 × 5" HWDP	222.79	241.53
6 ½" Jar + FLEX	8.90	250.43
6 × 5" HWDP	55.76	306.19
TOTAL BHA		306.19

Bit Data

Bit #	7 Run#2
Size	8 ⅜"
Type	PDC Bit
Mfgr	Best
Serial No.	220793
Nozzles	7 × 14
IADC Code	M1375
Depth In	3594
Depth Out	3692
Metrage	98
Hours Run	48
Av. ROP	2.04
Condition	1.1.WT.A.X.I.NO.TD

Performance Record :

Total Revolution On Bit : 1731.40 krev

This Run (98m) : 48.00 hrs

Cumulative Bit Life (387.5m) : 165.00 hrs

Drilling & Mud Parameters :

WOB (klb)	3-10
RPM (rpm)	30-40/140-150
TOR (lbf.ft)	5-10
SPP (psi)	2450-2650
FLOW (gpm)	480-500
MW (pcf)	76
FV (sec)	45
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.1
FLT °C	--

Reason for POOH :

POOH due to 7" Liner depth.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 27.05.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 8 ⅜"

BHA # 13	Length	Cum Lgth
8 ⅜" B.Bit	0.25	0.25
6 ½" Bit sub	0.95	1.20
21 ×3 ½" HWDP	194.96	196.16
TOTAL BHA		196.16

Bit Data

Bit #	5 Run#3
Size	8 ⅜"
Type	B.Bit
Mfgr	King Dream
Serial No.	2417584JH
Nozzles	3 × 16
IADC Code	HJT537G
Depth In	3692
Depth Out	3692
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	48
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 28.05.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 8 ⅜"

BHA # 14	Length	Cum Lgth
8 ⅜" B.Bit	0.25	0.25
6 ½" Bit sub	0.95	1.20
9 ⅝" Scraper	1.63	2.83
15 × 3 ½" HWDP	138.91	141.74
TOTAL BHA		141.74

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Reason for POOH :

POOH due to Dry Test.

Bit Data

Bit #	5 Run#4
Size	8 ⅜"
Type	B.Bit
Mfgr	King Dream
Serial No.	2417584JH
Nozzles	3 × 16
IADC Code	HJT537G
Depth In	3692
Depth Out	3692
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	48
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)
Pump 2: 6.299" Q = 4.616 gal/stk (95%)
Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 30.05.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 8 ⅜"

BHA # 15	Length	Cum Lgth
6 ⅛" B.Bit	0.19	0.19
4 ¾" Bit sub	0.99	1.18
27 × 3 ½" HWDP	248.30	249.48
156× 3 ½"DP	1502.40	1751.88
X.O.S	1.12	1753.00
TOTAL BHA		1753.00

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Reason for POOH :

POOH due to Dry test.

Bit Data

Bit #	2 Run#2
Size	6⅛"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3692
Depth Out	3692
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-BHA

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	47
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)
Pump 2: 6.299" Q = 4.616 gal/stk (95%)
Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 28.05.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 8 ⅜"

BHA # 14	Length	Cum Lgth
8 ⅜" B.Bit	0.25	0.25
6 ½" Bit sub	0.95	1.20
9 ⅝" Scraper	1.63	2.83
15 × 3 ½" HWDP	138.91	141.74
TOTAL BHA		141.74

Bit Data

Bit #	5 Run#4
Size	8 ⅜"
Type	B.Bit
Mfgr	King Dream
Serial No.	2417584JH
Nozzles	3 × 16
IADC Code	HJT537G
Depth In	3692
Depth Out	3692
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	48
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to Dry Test.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 30.05.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 8 ⅜"

BHA # 15	Length	Cum Lgth
6 ⅛" B.Bit	0.19	0.19
4 ¾" Bit sub	0.99	1.18
27 × 3 ½" HWDP	248.30	249.48
156× 3 ½"DP	1502.40	1751.88
X.O.S	1.12	1753.00
TOTAL BHA		1753.00

Bit Data

Bit #	2 Run#2
Size	6⅛"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3692
Depth Out	3692
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	47
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to Dry test.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 07.06.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA # 18	Length	Cum Lgth
6 ⅛" PDC	0.23	0.23
4 ¾"PDM	7.01	7.24
5 ⅞"S.Stab	1.37	8.61
4 ¾"Float Sub	0.40	9.01
4 ¾"MWD Sub	0.91	9.92
4 ¾"NMDC	9.05	18.97
24 × 3 ½" HWDP	220.66	239.63
D.Pin	0.55	240.18
4 ¾"D.Jar	6.35	246.53
3× 3 ½" HWDP	27.64	274.17
165× 3 ½"DP	1589.35	1863.52
X.O.S	1.12	1864.64
TOTAL BHA		1864.64

Bit Data

Bit #	8
Size	6⅛"
Type	PDC
Mfgr	Best
Serial No.	255421
Nozzles	3×22
IADC Code	M1665
Depth In	3697
Depth Out	3760
Metrage	63.00
Hours Run	20.8
Av. ROP	3.00
Condition	--

Performance Record :

Total Revolution On Bit : 49.92 krev

This Run (63m) : 20.80 hrs

Cumulative Bit Life (63m) : 20.80 hrs

Drilling & Mud Parameters :

WOB (klb)	8-10
RPM (rpm)	40
TOR (lbf.ft)	3000-5000
SPP (psi)	1950-2250
FLOW (gpm)	200
MW (pcf)	76
FV (sec)	47
PV / YP	15/13
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 10.06.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 19	Length	Cum Lgth
6 ⅛" PDC	0.23	0.23
4 ¾" PDM	7.01	7.24
4 ¾" Float Sub	0.40	7.64
4 ¾" MWD Sub	0.91	8.55
4 ¾" NMDC	9.05	17.60
24 × 3 ½" HWDP	220.66	238.26
D.Pin	0.55	238.81
4 ¾" D.Jar	6.35	245.16
3× 3 ½" HWDP	27.64	272.80
165 × 3 ½" DP	1589.35	1862.15
X.O.S	1.12	1863.27
TOTAL BHA		1863.27

Bit Data

Bit #	8 Run#2
Size	6 ⅛"
Type	PDC
Mfgr	Best
Serial No.	255421
Nozzles	3 × 22
IADC Code	M1665
Depth In	3760
Depth Out	3888
Metrage	128.00
Hours Run	52.60
Av. ROP	3.20
Condition	1-1-WT-A-X-I-NO-TD

Performance Record :

Total Revolution On Bit : 350.58 krev

This Run (128m) : 52.60 hrs

Cumulative Bit Life (191m) : 73.40 hrs

Drilling & Mud Parameters :

WOB (klb)	6-12
RPM (rpm)	40-50
TOR (lbf.ft)	3000-6000
SPP (psi)	1850-2400
FLOW (gpm)	190-250
MW (pcf)	78
FV (sec)	46-47
PV / YP	13-14/11-12
Gel 0 / 10	3/5-2.4
Alk. / HPHT	9.2-9.6
FLT °C	45

Reason for POOH :

POOH due to total depth.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 10.06.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 20	Length	Cum Lgth
6 ⅛" PDC	0.23	0.23
4 ¾" PDM	7.01	7.24
4 ¾" Float Sub	0.40	7.64
4 ¾" MWD Sub	0.91	8.55
4 ¾" NMDC	9.05	17.60
24 × 3 ½" HWDP	220.66	238.26
D.Pin	0.55	238.81
4 ¾" D.Jar	6.35	245.16
3× 3 ½" HWDP	27.64	272.80
165 × 3 ½" DP	1589.35	1862.15
X.O.S	1.12	1863.27
TOTAL BHA		1863.27

Bit Data

Bit #	8 Run#3
Size	6 ⅛"
Type	PDC
Mfgr	Best
Serial No.	255421
Nozzles	3 × 22
IADC Code	M1665
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : *350.58* krev

This Run (m) : -- hrs

Cumulative Bit Life (191m) : *73.40* hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	78
FV (sec)	46-47
PV / YP	13-14/11-12
Gel 0 / 10	3/5-2.4
Alk. / HPHT	9.2-9.6
FLT °C	45

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 15.06.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 21	Length	Cum Lgth
6 ⅛" B.Bit	0.190	0.190
4 ¾" Bit sub	0.990	1.180
3 × 4 ¾" DC	27.545	28.725
24 × 3 ½"HWDP	220.660	249.385
D.Pin	0.550	249.935
4 ¾" D.Jar	6.370	256.305
3 × 3 ½" HWDP	27.640	283.945
165 × 3 ½" DP	1588.440	1872.385
X.O.S	1.120	1873.505
TOTAL BHA		1873.51

Bit Data

Bit #	2 Run#5
Size	6 ⅛"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-LOG

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	83-84
FV (sec)	44-45
PV / YP	12/15
Gel 0 / 10	3/5
Alk. / HPHT	9.1
FLT °C	45

Reason for POOH :

POOH due to run log.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 24.06.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 22	Length	Cum Lgth
8 ⅜" B.Bit	0.250	0.250
6 ½" Bit sub	0.940	1.190
2 × 6 ½" DC	54.310	55.500
3 × 5" HWDP	83.750	139.250
TOTAL BHA		139.25

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Reason for POOH :

POOH due to change BHA.

Bit Data

Bit #	5 Run#5
Size	8 ⅜"
Type	B.Bit
Mfgr	King Dream
Serial No.	2417584JH
Nozzles	Open
IADC Code	HJT537G
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-1-WT-A-E-I-NO-BHA

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	41
PV / YP	16/11
Gel 0 / 10	3/5
Alk. / HPHT	10.2
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)
Pump 2: 6.299" Q = 4.616 gal/stk (95%)
Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 26.06.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 23	Length	Cum Lgth
6 ⅛" B.Bit	0.190	0.190
4 ¾" Bit sub	0.990	1.180
3 × 4 ¾" DC	27.545	28.725
24 × 3 ½"HWDP	220.660	249.385
4 ¾" D.Jar	5.310	254.695
3 × 3 ½" HWDP	27.640	282.335
165 × 3 ½" DP	1588.440	1870.775
X.O.S	1.120	1871.895
TOTAL BHA		1871.90

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Reason for POOH :

POOH due to run log.

Bit Data

Bit #	2 Run#6
Size	6 ⅛"
Type	Tci-Cone
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-LOG

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84-85
FV (sec)	41-45
PV / YP	16/13-14
Gel 0 / 10	3/5
Alk. / HPHT	9.4-10.8
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)
Pump 2: 6.299" Q = 4.616 gal/stk (95%)
Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 03.07.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 24	Length	Cum Lgth
6 ⅛" PDC BIT	0.230	0.230
4 ¾" Bit sub	0.990	1.220
2 × 4 ¾" DC	18.200	19.420
5 ⅞"Stabilizer	1.390	20.810
1 × 4 ¾" DC	9.345	30.155
24 × 3 ½"HWDP	220.660	250.815
4 ¾" D.Jar	5.310	256.125
3 × 3 ½" HWDP	27.640	283.765
165 × 3½" DP	1588.440	1872.205
X.O.S	1.120	1873.325
TOTAL BHA		1873.33

Bit Data

Bit #	8 Run#4
Size	6 ⅛"
Type	PDC
Mfgr	Best
Serial No.	255421
Nozzles	3 × 22
IADC Code	M1665
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-2-BT-T-X-I-WT-LOG

Performance Record :

Total Revolution On Bit : *350.58* krev

This Run (m) : -- hrs

Cumulative Bit Life (191m) : *73.40* hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	85
FV (sec)	46-49
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to run log.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 07.07.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 25	Length	Cum Lgth
6 ⅛" PDC BIT	0.230	0.230
4 ¾" Bit sub	0.990	1.220
2 × 4 ¾" DC	18.200	19.420
5 ⅞"Stabilizer	1.390	20.810
1 × 4 ¾" DC	9.345	30.155
24 × 3 ½"HWDP	220.660	250.815
4 ¾" D.Jar	5.310	256.125
3 × 3 ½" HWDP	27.640	283.765
165 × 3 ½" DP	1588.440	1872.205
X.O.S	1.120	1873.325
TOTAL BHA		1873.325

Bit Data

Bit #	8 Run#5
Size	6 ⅛"
Type	PDC
Mfgr	Best
Serial No.	255421
Nozzles	3 × 22
IADC Code	M1665
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-2-BT-T-X-I-WT-LOG

Performance Record :

Total Revolution On Bit : *350.58* krev

This Run (m) : -- hrs

Cumulative Bit Life (191m) : *73.40* hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	85
FV (sec)	74
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to logging.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 07.07.2025

7" liner Shoe @ 3692m ; ID: 6.18" ; Weight : 29lb/ft

Phase Diameter : 6 ⅛"

BHA# 26	Length	Cum Lgth
6 ⅛" PDC BIT	0.230	0.230
4 ¾" Bit sub	0.990	1.220
165 × 3 ½" DP	1588.440	1589.660
X.O.S	1.120	1590.780
TOTAL BHA		1590.780

Bit Data

Bit #	8 Run#6
Size	6 ⅛"
Type	PDC
Mfgr	Best
Serial No.	255421
Nozzles	3 × 22
IADC Code	M1665
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-2-BT-T-X-I-WT-TD

Performance Record :

Total Revolution On Bit : *350.58* krev

This Run (m) : -- hrs

Cumulative Bit Life (191m) : *73.40* hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	87
FV (sec)	48
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to run 5" liner.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 11.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 27	Length	Cum Lgth
6 ⅛" B.Bit	0.190	0.190
4 ¾" Bit sub	0.990	1.180
9 × 4 ¾" DC	81.283	82.463
18 × 3 ½"HWDP	165.415	247.878
165 × 3 ½" DP	1589.610	1837.488
X.O.S	1.000	1838.488
TOTAL BHA		1838.488

Bit Data

Bit #	2 Run#7
Size	6 ⅛"
Type	Tci-Cone
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-WT-A-E-I-BT-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	87
FV (sec)	45
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 13.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 28	Length	Cum Lgth
4 ⅛" J.Mill	0.870	0.870
3 ⅛" Bit sub	0.980	1.850
21 × 3 ⅛" DC	193.240	195.090
15 × 2 ⅞"DP	141.790	336.880
X.O.S	1.170	338.050
162 × 3 ½" DP	1560.355	1898.405
X.O.S	1.170	1899.575
TOTAL BHA		1899.575

Bit Data

Bit #	--
Size	4 ⅛"
Type	--
Mfgr	T.S.E.KH
Serial No.	944
Nozzles	5 × 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	10% used

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	87
FV (sec)	45
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 16.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 29	Length	Cum Lgth
3 ¾" J.Mill	0.870	0.870
3 ⅛" Bit sub	0.980	1.850
21 × 3 ⅛" DC	193.240	195.090
15 × 2 ⅞" DP	141.790	336.880
X.O.S	1.170	338.050
162 × 3 ½" DP	1560.355	1898.405
X.O.S	1.170	1899.575
TOTAL BHA		1899.575

Bit Data

Bit #	--
Size	3 ¾"
Type	--
Mfgr	T.S.E.KH
Serial No.	101
Nozzles	5 × 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	86
FV (sec)	43
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to run log.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 19.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 30	Length	Cum Lgth
5 ⅞" C.Cut Bit	0.250	0.250
4 ¾" Bit sub	0.855	1.105
3 × 3 ½" DP	28.780	29.885
X.O.S	1.170	31.055
9 ⅝" Scraper	1.630	32.685
TOTAL BHA		32.685

Bit Data

Bit #	--
Size	5 ⅞" C.Cut Bit
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	86
FV (sec)	43
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 20.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 31	Length	Cum Lgth
7 5/16" Polish Mill	0.490	0.490
15 × 5" HWDP	138.910	139.400
TOTAL BHA		139.400

Bit Data

Bit #	--
Size	7 5/16" Polish Mill
Type	--
Mfgr	--
Serial No.	--
Nozzles	4 × 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	86
FV (sec)	43
PV / YP	15/12
Gel 0 / 10	3/4
Alk. / HPHT	9
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 21.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 31	Length	Cum Lgth
7 " S.N.Packer	3.500	3.500
12 × 6 ½" DC	108.420	111.920
18 × 5" HWDP	166.990	278.910
TOTAL BHA		278.910

Bit Data

Bit #	--
Size	7 " S.N.Packer
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	86
FV (sec)	43
PV / YP	15/12
Gel 0 / 10	3/4
Alk. / HPHT	9
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 21.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 33	Length	Cum Lgth
5 ⅛" Polish Mill	0.400	0.400
4 ¾" Double Pin	0.330	0.730
4 ¾" Bit Sub	0.990	1.720
27 × 3 ½" HWDP	248.300	250.020
129 × 3 ½" DP	1242.610	1492.630
XOS	1.170	1493.800
TOTAL BHA		1493.800

Bit Data

Bit #	--
Size	5 ⅛" Polish Mill
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	86
FV (sec)	43
PV / YP	15/12
Gel 0 / 10	3/4
Alk. / HPHT	9
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 22.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 34	Length	Cum Lgth
5 ⅛" Polish Mill	0.400	0.400
4 ¾" Double Pin	0.330	0.730
7" Scraper	1.060	1.790
4 ¾" Bit Sub	0.990	2.780
27 × 3 ½" HWDP	248.300	251.080
129 × 3 ½" DP	1242.610	1493.690
XOS	1.170	1494.860
TOTAL BHA		1494.860

Bit Data

Bit #	--
Size	5 ⅛" Polish Mill
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	85
FV (sec)	43
PV / YP	15/12
Gel 0 / 10	3/4
Alk. / HPHT	9.1
FLT °C	--

Reason for POOH :

POOH due change BHA

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 23.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 35	Length	Cum Lgth
5" S.N.Packer	3.540	3.540
Neck Packer	1.680	5.220
18 × 4 ¾" DC	163.120	168.340
27 × 3 ½" HWDP	248.300	416.640
114 × 3 ½" DP	1098.530	1515.170
XOS	1.170	1516.340
TOTAL BHA		1516.340

Bit Data

Bit #	--
Size	5" S.N.Packer
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	43
PV / YP	11/13
Gel 0 / 10	3/4
Alk. / HPHT	9.1
FLT °C	--

Reason for POOH :

POOH due to dry test.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 30.07.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 36	Length	Cum Lgth
7 5/16" Polish Mill	0.480	0.480
15 × 5" HWDP	138.910	139.390
TOTAL BHA		139.390

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Reason for POOH :

POOH due change BHA

Bit Data

Bit #	--
Size	7 5/16" Polish Mill
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	43
PV / YP	13/11
Gel 0 / 10	3/4
Alk. / HPHT	9
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 01.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 37	Length	Cum Lgth
8 ⅜" B.Bit	0.230	0.230
6 ½" Bit sub	0.940	1.170
6 × 6 ½" DC	54.310	55.480
30 × 5" HWDP	278.550	334.030
TOTAL BHA		334.030

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Reason for POOH :

POOH due change BHA

Bit Data

Bit #	5 Run#6
Size	8 ⅜"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	2417584JH
Nozzles	3 × 18
IADC Code	537
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	43
PV / YP	13/11
Gel 0 / 10	3/4
Alk. / HPHT	9
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 02.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 38	Length	Cum Lgth
6 ⅛" B.Bit	0.190	0.190
4 ¾" Bit sub	0.990	1.180
27 × 3 ½" HWDP	248.300	249.480
150 × 3 ½" DP	1444.180	1693.660
XOS	1.170	1694.830
TOTAL BHA		1694.830

Bit Data

Bit #	2 Run#8
Size	6 ⅛"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	2304674JH
Nozzles	Open
IADC Code	537
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	40
PV / YP	11/9
Gel 0 / 10	3/4
Alk. / HPHT	9.8
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 04.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 39	Length	Cum Lgth
3 ¾" J.Mill	0.870	0.870
3 ⅛" Bit sub	0.980	1.850
21 × 3 ⅛" DC	193.240	195.090
15 × 2 ⅞" DP	141.790	336.880
X.O.S	1.170	338.050
162 × 3 ½" DP	1560.355	1898.405
X.O.S	1.170	1899.575
TOTAL BHA		1899.575

Bit Data

Bit #	--
Size	3 ¾"
Type	--
Mfgr	T.S.E.KH
Serial No.	101
Nozzles	5 × 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	45
PV / YP	13/16
Gel 0 / 10	3/4
Alk. / HPHT	9.8
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 06.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 40	Length	Cum Lgth
8 ⅜" B.Bit	0.230	0.230
6 ½" Bit sub	0.940	1.170
9 ⅝" Scraper	1.630	2.800
1× 6 ½" DC	27.100	29.900
2 × 5" HWDP	56.410	86.310
TOTAL BHA		86.310

Bit Data

Bit #	5 Run#7
Size	8 ⅜"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	2417584JH
Nozzles	Open
IADC Code	537
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1.1.WT.A.E.I.NO.BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	45
PV / YP	13/16
Gel 0 / 10	3/4
Alk. / HPHT	9.8
FLT °C	--

Reason for POOH :

POOH due to dry test.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 08.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 41	Length	Cum Lgth
3 ¾" J.Mill	0.870	0.870
3 ⅛" Bit sub	0.980	1.850
21 × 3 ⅛" DC	193.240	195.090
15 × 2 ⅞" DP	141.790	336.880
X.O.S	1.170	338.050
162 × 3 ½" DP	1560.355	1898.405
X.O.S	1.170	1899.575
TOTAL BHA		1899.575

Bit Data

Bit #	--
Size	3 ¾"
Type	--
Mfgr	T.S.E.KH
Serial No.	101
Nozzles	5 × 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	45
PV / YP	13/16
Gel 0 / 10	3/4
Alk. / HPHT	9.6
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 14.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 42	Length	Cum Lgth
3 ¾" J.Mill	0.870	0.870
3 ⅛" Bit sub	0.980	1.850
21 × 3 ⅛" DC	193.240	195.090
15 × 2 ⅞" DP	141.790	336.880
X.O.S	1.170	338.050
162 × 3 ½" DP	1560.355	1898.405
X.O.S	1.170	1899.575
TOTAL BHA		1899.575

Bit Data

Bit #	--
Size	3 ¾"
Type	--
Mfgr	T.S.E.KH
Serial No.	101
Nozzles	5 × 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	45
PV / YP	13/16
Gel 0 / 10	3/4
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due change BHA.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 17.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 43	Length	Cum Lgth
5 ⅞" B.Bit	0.180	0.180
7" Scraper	1.060	1.240
4 ¾" Bit Sub	0.990	2.230
6 × 3 ½" HWDP	55.330	57.560
162 × 3 ½" DP	1560.355	1617.915
X.O.S	1.170	1619.085
TOTAL BHA		1619.085

Bit Data

Bit #	9
Size	5 ⅞"
Type	Tri-Cone
Mfgr	K.Dream
Serial No.	--
Nozzles	Open
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	45
PV / YP	13/16
Gel 0 / 10	3/4
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to run TBG.

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

Date : 24.08.2025

5" liner Shoe @ 3888m ; ID: 4.276" ; Weight : 18lb/ft

Phase Diameter : 6 ⅛"

BHA# 44	Length	Cum Lgth
6 ⅛" Mill	0.640	0.640
6 ⅛" Bit Sub	0.990	1.630
27 × 3 ½" HWDP	250.720	252.350
48 × 3 ½" DP	461.700	714.050
X.O.S	1.170	715.220
TOTAL BHA		715.220

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Reason for POOH :

POOH due to run tubing.

Bit Data

Bit #	--
Size	6 ⅛""
Type	--
Mfgr	T.S.E.KH
Serial No.	763
Nozzles	4 x 10
IADC Code	--
Depth In	3888
Depth Out	3888
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	
FLOW (gpm)	--
MW (pcf)	84
FV (sec)	44
PV / YP	12/15
Gel 0 / 10	3/4
Alk. / HPHT	9.4
FLT °C	--

PUMP DATA

Pump 1: 6.299" Q = 4.616 gal/stk (95%)

Pump 2: 6.299" Q = 4.616 gal/stk (95%)

Pump 3: 6.299" Q = 4.616 gal/stk (95%)

7. Casing Information

Size (in)	Shoe Depth (mMD)	Specification
20	151.5	K – 55, 94^{ppf}, BTC
13 – 3/8	1155.5	N – 80, 68^{ppf}, BTC
9 – 5/8	2477.5	L – 80, 47^{ppf}, PJE
7 (side track)	2167.5 – 3692	L – 80, 29^{ppf}, TPCQ
7 SN PKR	2167.5	
7 (tie back)	2034 – 2165	L – 80, 29^{ppf}, TPCQ
5 (side track)	3593.5 – 3888	L – 80, 18^{ppf}, HSG3 – FJTHD
5 SN PKR	3593.5	

Table 7-1: AZNS-075-ST1 Final Casing Data

8. Cement Job Report

8.1 7” Liner Cementing Operation Information

Operation Type: 7” Liner cementing job
Hole Size: 8 – 3/8”
Liner Depth: 3692m
Liner Lap: 2165m
Total Volume:

- Lead Excess: 50%
- Tail Excess: 50%
- 86.0 bbl. Lead Slurry (98 PCF)- 100 m Overlap
- Using 10.8 MT Dry Cement
- 73.7 bbl. Tail Slurry (118 PCF)
- 3.0 bbl. Tail Slurry Behind the Dart as part of Displacement
- Using 16.4 MT Blend Cement

Total Displacement Volume: Displace with 309.4 ^{bbl} mud

8.2 Engineering Data

Casing Data				
MD (m)	OD (in)	Weight (lb/ft.)	ID (in)	Grade
3692	7	29	6.184	L-80
Slurry Data				
Name	Volume (bbl)	Density (pcf)	Remark	
Lead Slurry	86	98	-	
Tail Slurry	73.7	118	-	

Table 8-1: AZNS-075-ST1 Engineering Data


8.3 Operation Sequence

1. Determine the proper Tanks, clean up and prepare chemicals for spacer.
2. Check and test the salinity of mixing water and its properties prior to prepare CMT solution to avoid any un-wanted flash set.
3. Fill up Mud Pit and Batch Mixer with mixing water for preparing mixing fluid and test the salinity of mixing water. 4. 6 hours before reaching liner shoe, start mixing cement additives For Lead and tail with Company Man approval at the Batch Mixer .
Note: Efficiency time of solution is up to 36 hours 5. Load dart (pump down plug) inside 7" cement head in the presence of company representative and check the wiper plug & dart & cement head's O-Rings and plug holder by Hangerman (offline job).
6. After liner running, make up cement head, connect cement line by Hangerman.
7. Perform a Pre-Job safety Meeting with all personnel involved on the operation as well as the client representative.
8. Ensure communication between Cementer and Rig floor with phone/walkie-talkie.
9. Test surface cement line with 500/3000 psi using cement unit (5 min/10 min).
Note: Circulate bottoms up for at least two-hole volumes before cementing. Make sure that the shale shakers are clean of cutting and mud weight in and mud weight out are the same.
Note: Carefully monitor losses at all stages of the operation. 10. Pump 20.0 bbls of 62.4 pcf Chemical Wash by Cement Unit. 11. Pump 50.0 bbls of 85.0 pcf Spacer Wash by Rig Pump. 12. Transfer Lead Solution By Batch mixer to Cement unit and Mix and Pump 86.0 bbl. 98 PCF / 5 BPM lead slurry by cement unit and Stat to Fly mix and Pump lead Slurry By Cement unit. 13. Mix 73.7 bbl. 118 PCF / 5 BPM tail slurry by Batch Mixer and Pump by Cement unit.
14. Release displacement dart. 15. Pump 3.0 bbl. of 118 pcf Cement Slurry behind the dart (as a part of displacement). 16. Total displacement volume is 309.4 bbl. 17. Continue displacement by Cement unit with Mud (306.5 bbl)
18. Slow down pump rate for 10.0 bbl. before displacement dart reaches wiper plug (Calculate at rig site based on last tally and tool joint data).
19. Watch for indication of dart latching into wiper plug on pressure gauge. If a peak in pressure is noticed when both plugs latches, recalculate the remaining displacement volume to bump the plug.
20. When Cement Slurry comes to the annulus, Loss amount should be carefully monitored from this time by mud engineer and mud logging. 21. Decrease pump rate of last 10.0 bbl. displacement volume (Up to Company Man Decision) 22. Bump plug to Surface pump pressure ± 500 or 1000 & perform liner integrity test (LIT) to 2000 psi and keep the final pressure for 15 minutes.
Note: Be careful not to exceed 75% of burst pressure of liners/pipes. Note: If plug does not bump, do not over displace more than 25% of the shoe track volume.
23. Bleed off pressure and monitor return line for checking backflow. 24. POOH 5 stands of drill pipe from top of liner lap (± 2265 m), circulate 1.2 bottoms up, POOH to surface. Close the well, and hold 500 psi pressure on top of the cement to prevent fluid migration until cement sets.

8.4 Mixing Sequence

Mixing Sequence	
Chemical Wash	
1. Fresh Water	
2. Musol (Mutual Solvent)	
3. PA-DA 5 (Surfactant)	
Spacer	
1. Fresh Water	
2. E-DA 500 (Chemical Spacer)	(It needs to be pre-hydrated for 1 hour in water)
3. CaCO3	
4. Musol (Mutual Solvent)	
5. PA-DA 5 (Surfactant)	
6. DF-DA 3 (Defoamer)	
Lead Slurry	
1. Fresh Water	
2. Bentonite	(It needs to be pre-hydrated for 120 min in water)
3. FLC-DA 9 (Fluid Loss Controller)	(It needs to be pre-hydrated for 40 min in water)
4. Paragas (Anti Gas Migration)	
5. DF-DA 3 (Defoamer)	
Tail Slurry	
1- Fresh Water	
2- Silica Flour	
3- FLC-DA 9 (Fluid Loss Controller)	(It needs to be pre-hydrated for 40 min in water)
4- Paragas (Anti Gas Migration)	
1- CFR-DA 3 (Dispersant)	
2- CR-DA 4 (Retarder)	
3- DF-DA 3 (Defoamer)	

8.5 Job Graph

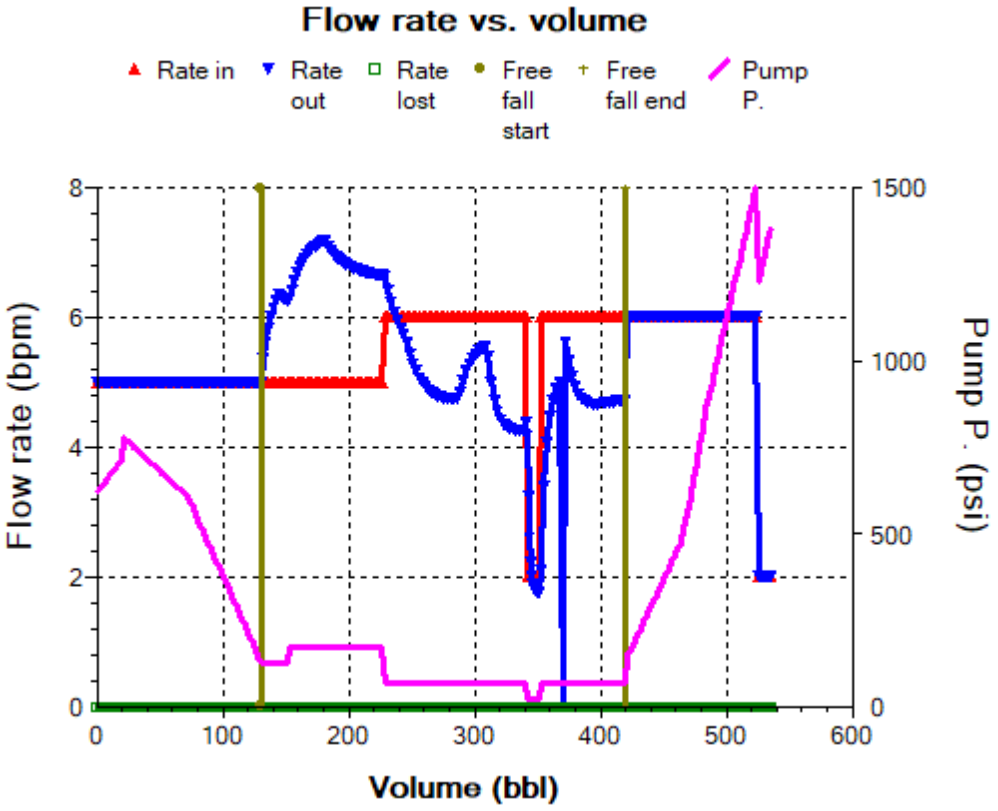
Flow rate vs. volume
Rate in
Rate out
Rate lost
Free fall start
Free fall end
Pump P.
Flow rate (bpm)
Pump P. (psi)
Volume (bbl)
0
2
4
6
8
0
500
1000
1500
0
100
200
300
400
500
600

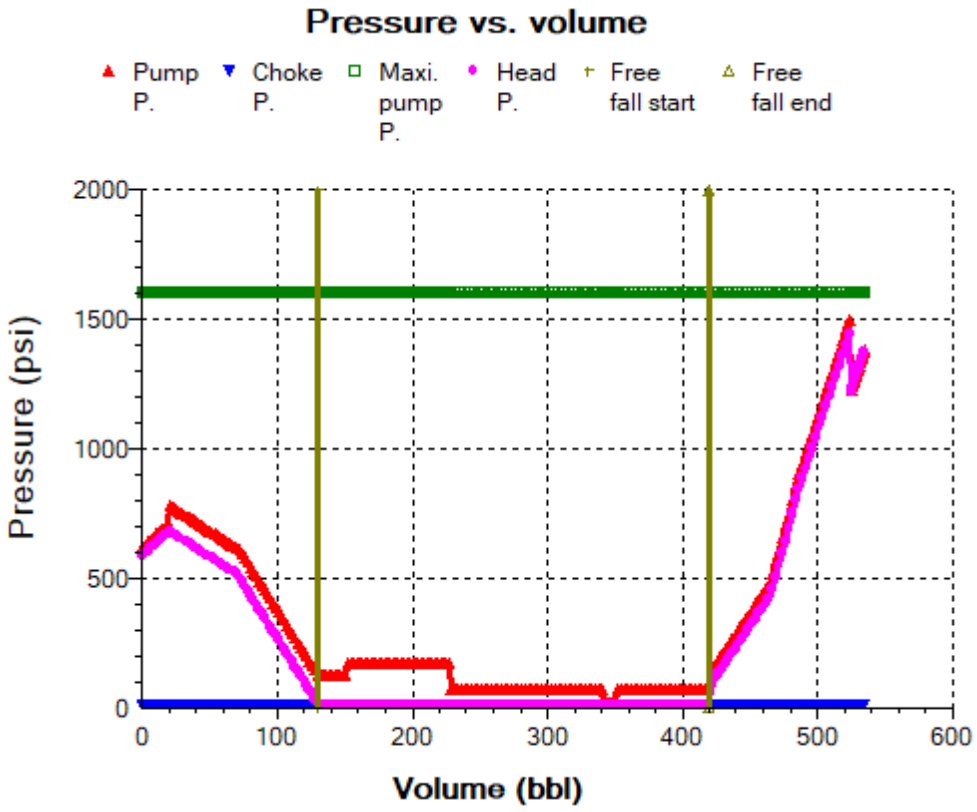


Figure 8-1: AZNS-075-ST1 7" Liner Job Graph

8.6 Timing Schedule

Timing Schedule				
Stage	**Rate** (bbl/min)	**Volume** (bbl)	**Time** (min)	**Total Time** (min)
Chemical Wash	5.0	20.0	4.0	4
Spacer	5.0	50.0	10.0	14
Lead Slurry	5.0	86.0	17.2	31
Tail Slurry	5.0	73.7	14.7	46
Release Dart	--		5.0	51
Tail Slurry behind dart	5.0	3.0	0.6	52
Mud	6.0	113.2	18.9	70
Mud (Slow down to shear)	2.0	10.0	5.0	75
Mud	6.0	173.3	28.9	104
Mud (Slow down to bump)	2.0	10.0	5.0	109
POOH Drill Pipe W/ Setting tool	--		45.0	**154**

Table 8-2: AZNS-075-ST1 Timing Schedule

8.7 Amount of Material & Used in Operation

Lead Slurry:									
QC Code	Additives	Conc.		Qty		Mixing Time	Slurry Volume:	400	ml
	Fresh Water	11.31	gal/sk	270.49	ml		Slurry Density:	98.0	PCF
MSA Supplied	Bentonite	5.00%	bwoc	15.77	gr	5 min			
D-FLC9-34	FLC-DA 9	0.80%	bwoc	2.52	gr	3 min	Mixing Water:	11.31	gal/sk
D-PG-57	Paragas	0.90	gal/sk	21.53	ml	40 s			
D-DF3-33	DF-DA 3	0.04	gal/sk	0.96	ml	10 s	Mixing Fluid:	12.58	gal/sk
D-CMT-140	"G" Class Cement			315.37	gr	35 s			
							Slurry Yield:	2.23	ft^3/sk
							Base of Cal.:	110	lb/sack of CMT

Tail Slurry:									
QC Code	Additives	Conc.		Qty		Mixing Time	Slurry Volume:	400	ml
	Fresh Water	6.879	gal/sk	204.61	ml		Slurry Density:	118.0	PCF
D-FLC9-34	FLC-DA 9	0.4%	bwoc	1.57	gr	3 min			
D-PG-57	Paragas	0.60	gal/sk	17.85	ml	40 s	Mixing Water:	6.88	gal/sk
D-CFR3-52	CFR-DA 3	0.2%	bwoc	0.78	gr	10 s			
D-CR4-37	CR-DA 4	0.07%	bwoc	0.27	gr	10 s	Mixing Fluid:	7.57	gal/sk
D-DF3-33	DF-DA 3	0.020	gal/sk	0.59	ml	10 s			
D-CMT-140	*Blended Cement			529.25	gr	35 s	Slurry Yield:	1.80	ft^3/sk
D-SF-18									
							Base of Cal.:	110	lb/sack of CMT

*: Blended Cement = ("G" Class Cement + 35% bwoc SF-DA 1)

Spacer:									
QC Code	Additives	Conc.		Qty		Mixing Time	Slurry Volume:	400	ml
	Fresh water	32.08	gal/bbl	305.53	ml				
D-E500-38	E-DA 500	9.50	lb/bbl	10.84	gr	5 min			
MSA Supplied	CaCO3	194.49	lb/bbl	221.96	gr	5 min	Slurry Density:	85.0	PCF
D-Musol-42	Musol	0.50	gal/bbl	4.76	ml	40 s			
D-PA5-42	PA-DA 5	0.20	gal/bbl	1.90	ml	40 s			
D-DF3-30	DF-DA 3	0.10	gal/bbl	0.95	ml	10 s			

Table 8-3: AZNS-075-ST1 Material Used Table

8.8 7” Liner Tie-Back Cementing Operation Information

Operation Type: 7” Liner Tie-Back cementing job

Hole Size: 8-3/8”

Liner Depth: 2165-2034.5 ^{m}

Total Volume:

- Pump 20^{bbl} Spacer 62.4^{pcf} as spacer
- Pump 30^{bbl} cement slurry 118^{pcf}

Total Displacement Volume: Displace with 125^{bbl} mud

8.9 Engineering Data

Casing Data				
MD (m)	OD (in)	Weight (lb/ft.)	ID (in)	Grade
2165-2034.5	7	29	6.184	L-80
Slurry Data				
Name	Volume (bbl)	Density (pcf)	Remark	
Cement Slurry	30	118	-	

Table 8-4: AZNS-075-ST1 Engineering Data

8.10 Operation Sequence

JOB PROCEDURE

1- Cheking equipments and ensuring of proper condition

2- Taking work permission

3- Holding Pre-job safety meeting & tool box under supervision of HSE officer

4- Line up cement unit to the rig floor and secure the lines

5- Clean up mud pits, preparing chemicals for mixing fluid.

6- Fill tanks with fresh water (**15.2** bbl) for mixing fluids.

7- Before finished running Liner & Drill Pipe with Co. man approval, start mixing cement additives and preparing mixing fluids according to below:

Main cement solution mixing procedure

Add Micro Silica (SE-MS) and allow mixing for 30 minutes

Add Dispersant (SE-D01) and allow mixing for 10 minutes

Add Dispersant (SE-D31) and allow mixing for 10 minutes

Add FLC (SE-F29) and allow mixing for 10 minutes

Add Anti-foam (SE-A20) to fresh water and allow mixing for 5 minutes

8- Prepare pre job safety meeting with involving personnel

9- Test the lines W/500psi 5 min. and 3000 psi for 10 min.

10- RIH Liner to 2165 m, then circulate to condition the hole.

11- When the liner reach 2165 m, start to pumping **20** bbl (62.4 pcf) spacer (Rate:2 bpm)

12- After that mix and Pump **16.55** bbl Cement slurry (118 PCF) with rate 4 bpm

13- Release pump down plug

14- Displace With mud at optimum rate. Slow Down Pumping rate to 2 bpm for last 10 bbl & Liner Volume before Pump down Plug reache to Wiper Plug

15- Land Plug with 1000 psi over final displacement pressure and displace liner volume

16- Bleed off pressure and monitor U-Tube return

17- Never over-displace more than half the shoe track volume if bumping is not observed (**2 bbl**)

18- **Pull out drill pipe above the top of the cement**, flush the Line and hold 50 psi pressure on top of the cement until Cement sets. (Optional)

19- Rig down cement lines

20- WOC 24 hr

8.11 Pumping Schedule

Name	Flow Rate (bb/min)	Volume (bbl)	Stage Time	Comments
Spacer	2	20	10	-
Slurry	4	26.55	6.6	-
Displacement	5	125	25	-

Table 8-5: AZNS-075-ST1 Pumping Schedule

8.12 Amount of Material & Used in Operation

Slurry Type				
Wt: 118^{pcf}	S.V: 26.55^{bbl}	Mixed W. V: 15.2^{bbl}	Mixed F. V: 15.6^{bbl}	S.Y: 1.3602 ft^2/sk
Row	**Material Name**	**Consumbles**	**Unit**	**Description**
1	Cement G class	109.58	sks	-
2	Silica Flour	109.6	lb	-
3	Dispersant SE-D-01	11	lb	-
4	Dispersant SE-D-31	3.8	gal	-
5	FLC SE-F-29	11	lb	-
6	Anti foam SE-A20	3.3	gal	-

Table 8-6: AZNS-075-ST1 Material Used Table

8.13 5” Liner Cementing Operation Information

Operation Type: 5” Liner cementing job

Hole Size: 6-1/8”

Liner Depth: 3593.5 – 3888^{m}

Total Volume:

- Pump 15^{bbl} Chemical Wash 62.4^{pcf}
- Pump 20^{bbl} Spacer 62.4^{pcf}
- Pump 30.72^{bbl} cement slurry 118^{pcf}
- L – 80, 18^{ppf}, HSG3 – FJTHD

Total Displacement Volume: Displace with 170.5^{bbl} mud

8.14 Engineering Data

Casing Data				
MD (m)	OD (in)	Weight (lb/ft.)	ID (in)	Grade
3593-3888	5	18	4.276	L-80
Slurry Data				
Name	Volume (bbl)	Density (pcf)	Remark	
Cement Slurry	30.72	118	-	

Table 8-7: AZNS-075-ST1 Engineering Data

8.15 Operation Sequence

	JOB PROCEDURE
1	Checking equipment and ensuring of proper condition
2	Cleaning mud pits and preparing cement additives
3	Taking work permission before the end of running the Liner
4	Holding pre job safety meeting & tool box under supervision of HSE officer
5	Filling mud pit with fresh water and start mixing of required additives for making Spacer
6	Filling Batch mixer with fresh water and start mixing of required additives for making Solution based on the program
6_1	Slurry solution mixing procedure: Mix Water: 15.6 bbl Add Micro silica (SE-MS01) and allow mixing for 30 min Add Anti-gas mig. (SE-G30) and allow mixing for 15 min Add Dispersant (SE-D31) and allow mixing for 15 min Add Retarder (SE-R02) and allow mixing for 15 min Add F.L.C (SE-F29) and allow mixing for 15 min Add Anti-foam (SE-A20) and allow mixing for 5 min
7	Setting cement pumps & Batch mixer in suitable position
8	Connecting silo containing dry cement to Batch mixer
9	Connecting Batch mixer to cement pump trucks
10	Starting the circulation of drilling fluid by 1.5 times of well capacity for well cleaning and consider well conditions
11	Starting the air compressor and reach to the working pressure of silos (25 psi)
12	Start mixing and preparing slurry in the batch mixer.
13	Pressure test cement line to 500 psi for 5 min. and slowly increase the pressure to 3000 psi and hold for 5 min. Then release the pressure
14	Line up pipes from cement pumps to drill string
15	Pumping 15 bbl **Chemical wash** by pump truck
16	Pumping 20 bbl **Spacer** by Rig pump
17	Start transferring slurry from batch mixer to pump truck
18	Mixing and Pumping slurry down to the well with cement pump truck 30.72 bbl Rate 3 BPM
19	Release Dart plug
21	Displacement slurry with Drilling fluids by pump truck 170.5 bbl Rate 3 BPM
22	Landing Plug, bleed off pressure and check for float shoe and collar
23	Never over-displace more than half the shoe track volume if bumping is not observed (1 bbl)
24	Pull out 3 stands drill pipe, flush string and hold 50 psi pressure on top of the cement to pervent gas migration until cement sets
25	Equipment, pipe lines and tools disassembled
26	End of operation
27	W.O.C

8.16 Pumping Schedule

Name	Flow Rate (bb/min)	Volume (bbl)	Stage Time	Comments
Chemical Wah	4	15	4	-
Spacer	4	20	5	-
Slurry	3	30.7	10	-
Displacement	3	170.5	57	-

Table 8-8: AZNS-075-ST1 Pumping Schedule

8.17 Amount of Material & Used in Operation

Slurry Type				
Wt: 118^{pcf}	S.V: 30.7^{bbl}	Mixed W. V: 15.6^{bbl}	Mixed F. V: 17.1^{bbl}	S.Y: 1.7676 ft^2/sk
Row	**Material Name**	**Consumbles**	**Unit**	**Description**
1	Cement G class	97.57	sks	-
2	Silica Flour	3576.76	lb	-
4	Micro Silica	39.03	lb	-
5	Anti Gas	19.51	Gal	-
6	Dispersant SE-D-31	5.85	gal	-
7	FLC SE-F-29	19.51	lb	-
8	Anti foam SE-A20	2.93	gal	-

Table 8-9: AZNS-075-ST1 Material Used Table

9. Completion Report

9.1 Completion Tubing Information

Tubing Size (in)	Weight (ppf)	Grade	Ultimate Strengths	Connection	Collapse Pressure (psi)	Burst Pressure (psi)	Interval (m)
4 – 1/2	18.9	L – 80	233^{klb}	HSM3	13830	13380	0 – 1939.43
3 – 1/2	10.2	L – 80	440^{klb}	HSM3	12120	11560	1939.43 – 2374.68

Table 9-1: AZNS-075-ST1 Tubing Data

9.2 Completion Tools Specification Checklist

Item	Equipment Description	
1	**CONTROL LINE "WEIQIXIN":**	
	THINKNESS:	0.065"
	WORK PRESSURE:	15,000 PSI
	O.D.:	0.25"
	TYPE:	SEAMLESS
	MATERIAL:	INC 825
	LENGTH:	120m/Roll
2	**UPPER FLOW COUPLING " WEIQIXIN" :**	
	OD:	**5.5"**
	ID:	3.640"
	THREADS:	4-1/2" 18.9 PPF, HSM3
	WORKING PRESSURE:	7,500 PSI
	LENGTH:	6 FT
	MATERIAL:	9Cr1MO
	LOWER FLOW COUPLING " WEIQIXIN" :	
	OD:	5.550"
	ID:	3.640"
	THREADS:	4-1/2" 18.9 PPF, HSM3
	WORKING PRESSURE:	7,500 PSI
	LENGTH:	4 FT
	MATERIAL:	9Cr1MO
3	**TUBING RETRIEVABL SAFETY VALVE " WEIQIXIN" :**	
	SETTING DEPTH:	62.456^{m}
	WORKING PRESSURE:	7,500 PSI
	TEMPERATURE:	325 DEG F

	MAX O.D.:	7.5"
	MIN. I.D.:	3.437"
	PROFILE:	AF
	SELF-EQUALIZING FEATURE	HYDRAULIC CONTROL
	MATERIAL:	9Cr1MO
	THREADS:	4-1/2" 18.9 PPF HSM3
	PROTECTION SLEEVE	
	PROFILE	AF
	MIN ID	2.9"
4	**TRAVELING JOINT " WEIQIXIN" :**	
	STROKE LENGTH	10 FT
	SHEAR PIN SET:	20,000LB
	ELASTOMER:	AFLAS
	WORKING PRESSURE:	7,500 psi
	TEMPERATURE:	300 DEG F
	TOOL OD:	5.315"
	TOOL ID:	2.922"
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	9Cr1MO
	TRANSFER TORQUE FEATURE	YES
5	**SLIDING SIDE DOOR " WEIQIXIN" :**	
	PROFILE:	X
	MAX.OD:	4.551"
	MIN ID:	2.750"
	PRESSURE RATING:	7,500 PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	9Cr1MO
	OPEN METHOD	DOWNWARD OPEN
6	**COMPLETION PACKER " WEIQIXIN" :**	
	TYPE:	RETRIEVABLE
	CASING :	7" 29 PPF
	OD:	5.689"
	ID:	2.922"
	WORKING PRESSURE:	7,500 PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	9Cr1MO
	ELEMENT MATERIAL:	AFLAS
7	**LANDING NIPPLE " WEIQIXIN" :**	
	PROFILE TYPE:	XN
	WORKING PRESSURE:	7,500 PSI
	MAX O.D.:	4.5"
	SEAL BORE:	2.750”
	MIN ID:	2.441”

	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	TEMPERATURE:	300 DEG F
	MATERIAL:	9Cr1MO
8	**RE-ENTRY GUIDE SHOE " WEIQIXIN" :**	
	OD:	4.5"
	MIN ID:	2.922"
	TOP CONNECTION	3-1/2" 10.20 PPF HSM3 BOX
	MATERIAL:	9Cr1MO
9	**3-1/2" CHEMICAL INJECTION" WEIQIXIN" :**	
	TYPE	TUBING RETRIVABLE
	MAX OD	5.00"
	MIN ID	2.922"
	MATERIAL:	13CR-110KSI
	TEMPERATURE	300 DEG F
	CONNECTION	3-1/2" 10.20 PPF HSM3 B*P
	CIV CONNECTION	NPT 3/8" BOX FOR CIV
	1.00"CIV VALVE	
	TYPE	DUAL CHECK VALVE WITH RUPTURE DISC
	WORKING PRESSURE	15,000PSI
	MARERIAL	13CR-110KSI
	TEMPERATURE:	300 DEG F
	TOP CONNECTION	3/8" AUTOCLAVE
	BOTTOM CONNECTION	3/8" NPT
	RUPTURE DISC PRESSURE	6,000PSI

Item	Name	Description
1	**Tubing Hanger**	11" BOWL x 4-1/2" 18.9 10K PPF BOX TPCQ-EX CONNECTION BOTTOM & 4-1/2" 4-2G ACME BOX TOP WITH 4-1/2" EXTENDED NECK, WITH ONE CONTINUOUS 1/4" NPT C. LINE EXIT FOR SSSV, ONE 1/4" LINE EXIT FOR DHPG, TWO CONTINIOUSE 3/8" NPT CHEMICAL INJECTION LINE FOR CIV INSTALLATION COMPLETE WITH RELATED FITTINGS AND PLUGS, BPV: 4" TYPE H THREAD PREPARATION, TWO S-SEAL & ONE METAL SEAL TO PACK OFF THE UPPER NECK AND TWO S-SEAL TO PACK OFF THE BODY OF HANGER, MATERIAL: 410SS. M.C: FF-0.5 T.C: U PSL:3G PR:2 COMPANY: MSP
2	**Fluted Adaptor**	4 1/2" 18.9 PPF, L – 80 HSM3 PIN * TPCQ EX PIN, OD: 5.5'' ID: 3.64'' SLOTS: 6 * 1 INCH WIDTH

Table 9-2: AZNS-075-ST1 Completion Equipment Checklist

9.3 Assembling Test Report


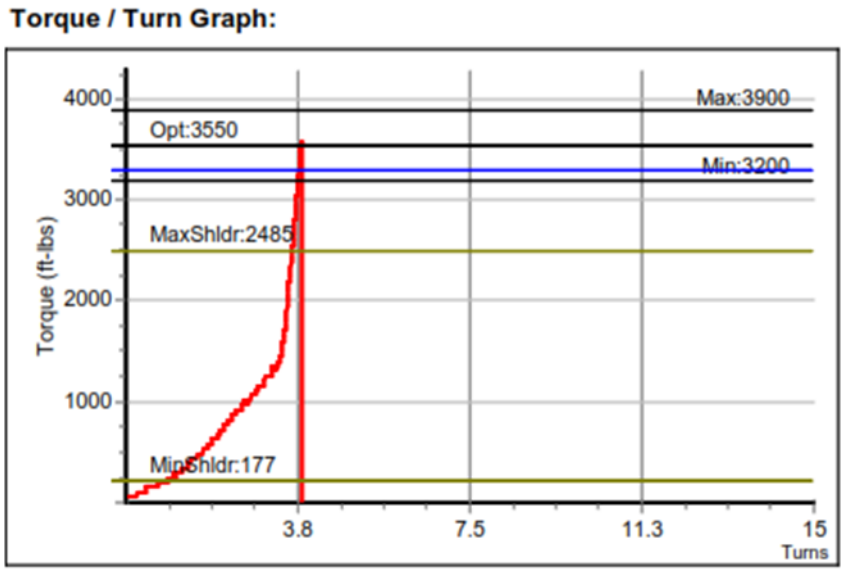


Figure 9-1: AZNS-075-ST1 Retrievable Packer Connection

Torque / Turn Graph:

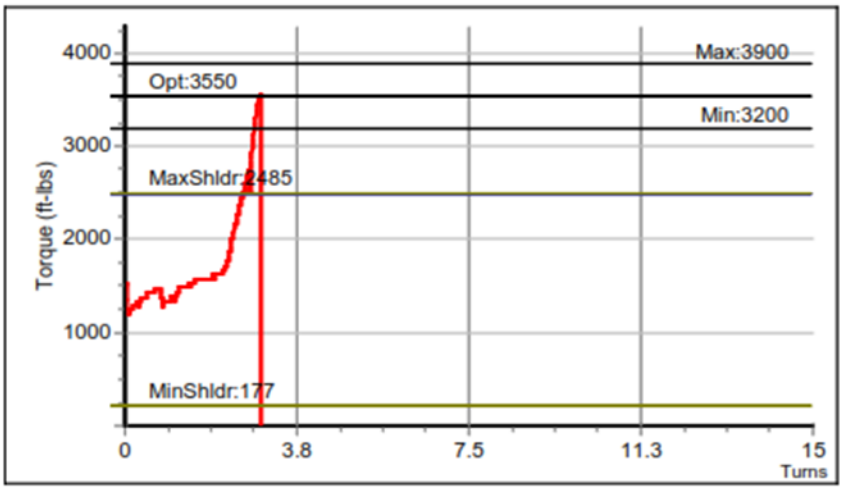

Torque / Turn Graph:


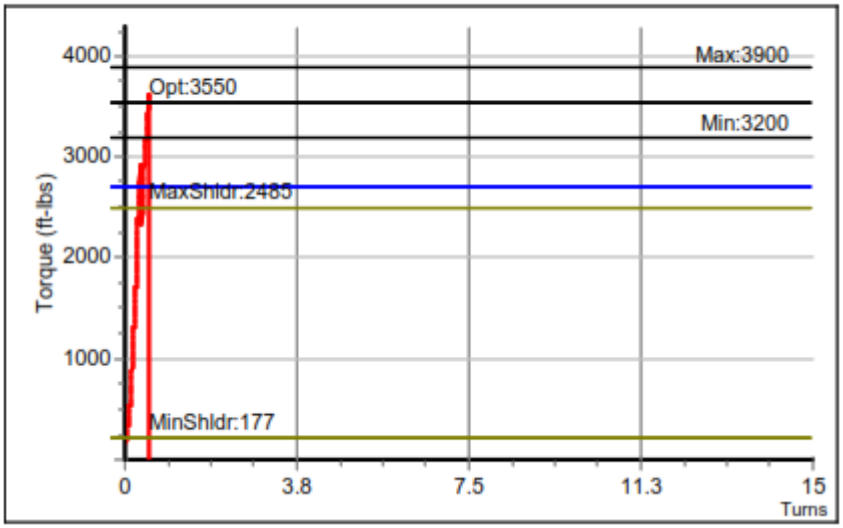


Figure 9-2: AZNS-075-ST1 SSD Connections

Torque / Turn Graph:

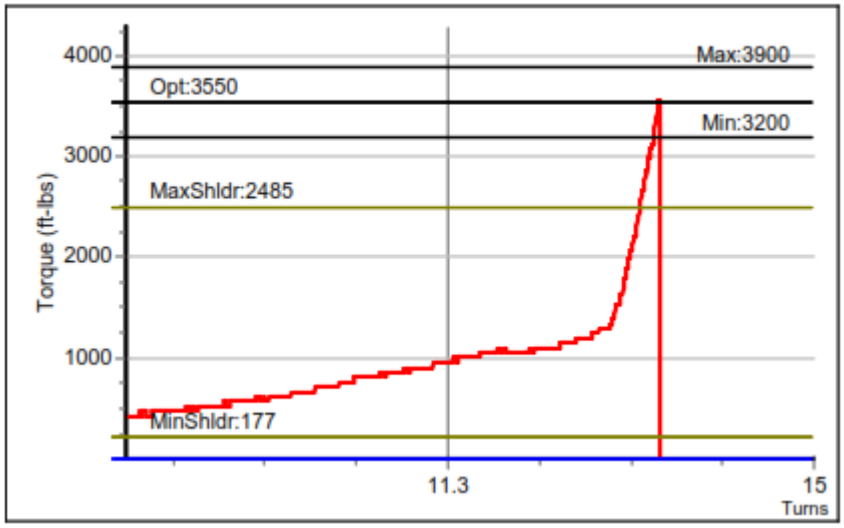

Torque / Turn Graph:


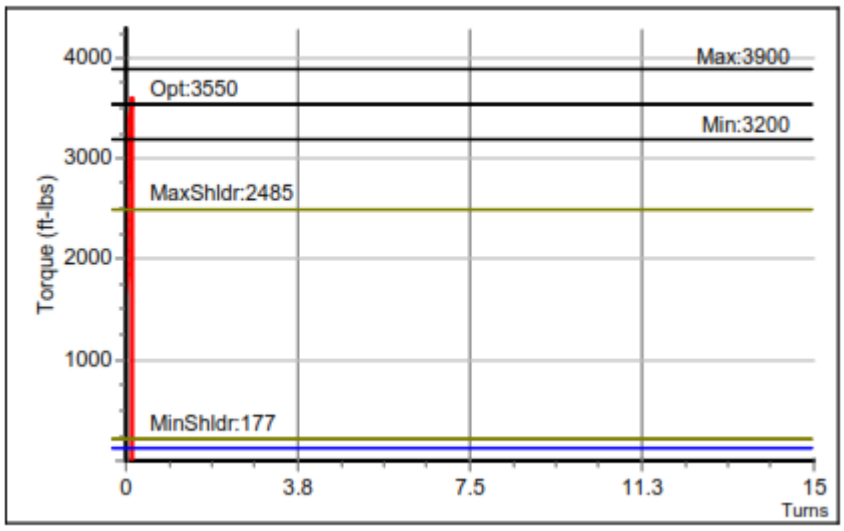


Figure 9-3: AZNS-075-ST1 EX Jt Connections

Torque / Turn Graph:

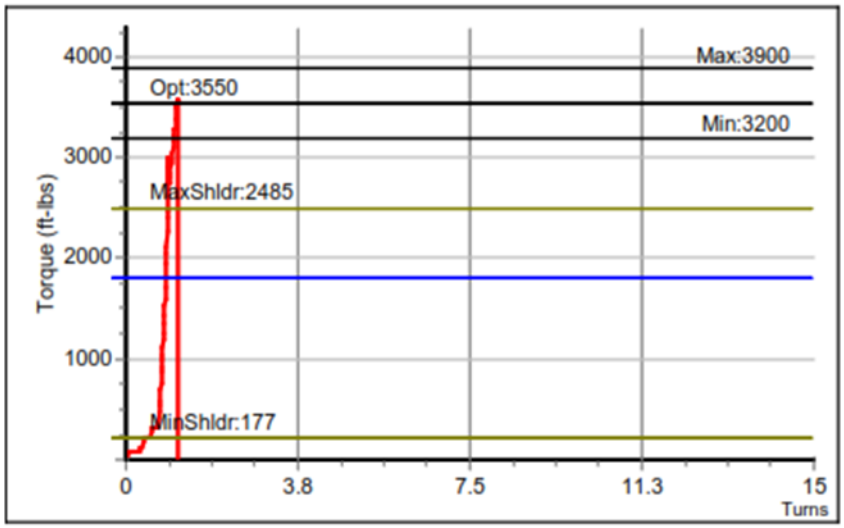

Torque / Turn Graph:


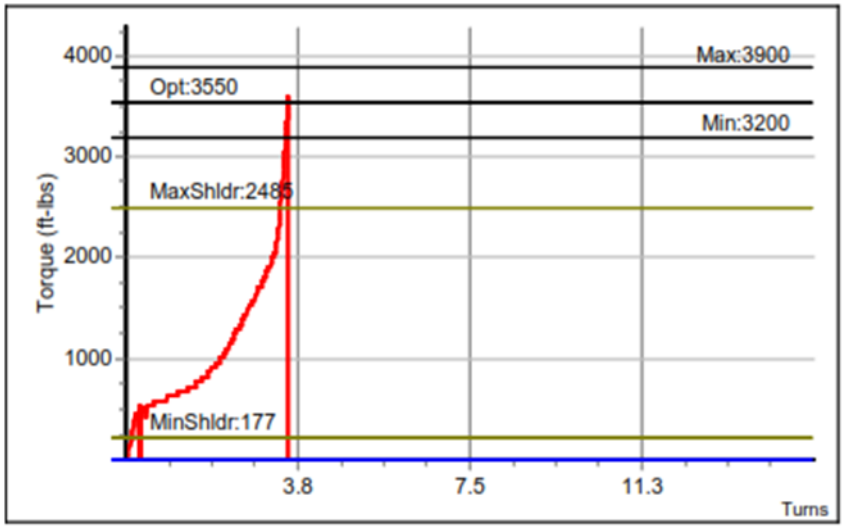


Figure 9-4: AZNS-075-ST1 Landing Nipple Connections

Torque / Turn Graph:

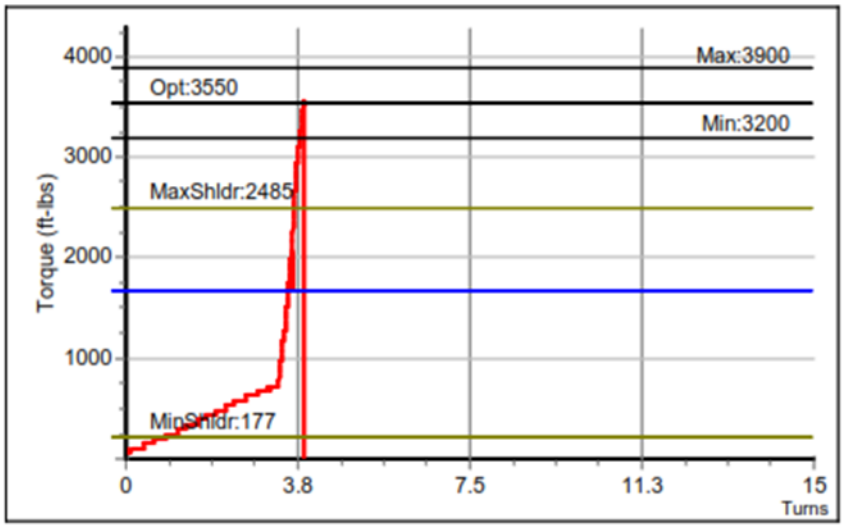

Torque / Turn Graph:


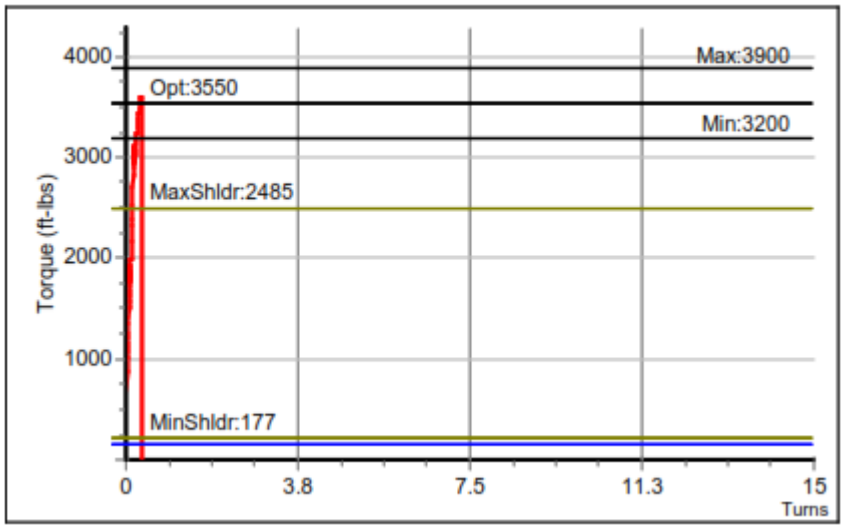


Figure 9-5: AZNS-075-ST1 First CIM Connections

Torque / Turn Graph:

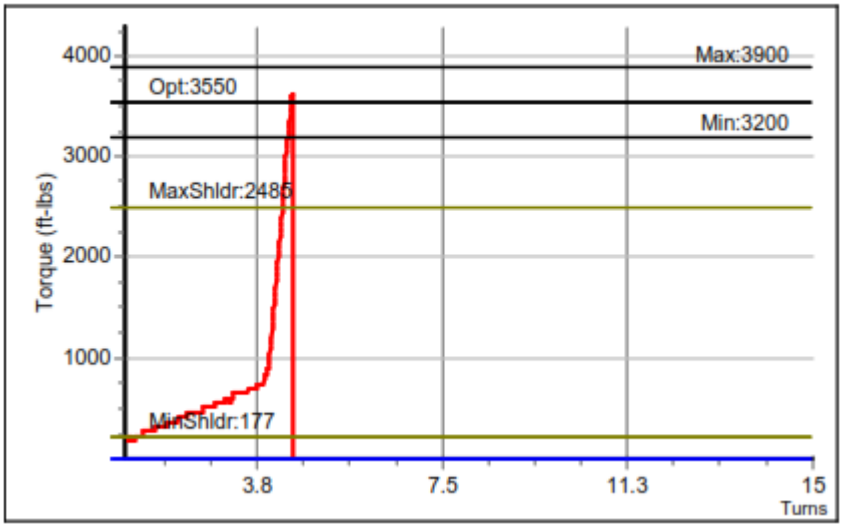

Torque / Turn Graph:

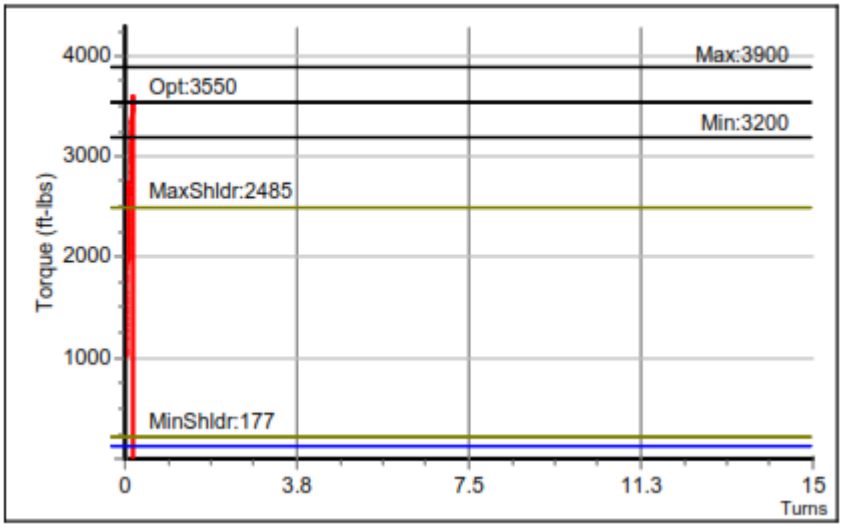


Figure 9-6: AZNS-075-ST1 Second CIM Connections

9.4 Completion Operation Checklist

Item	Operation Name	Remark	Check Mark✓
1	Scraper Trip	Packer depth should be scraped	√
2	Pre-job preparation	Pre-connection All Down Hole Equipment With Upper & Lower Pup Joints On Confirmed Thread-makeup at Workshop, And Pressure Test Prior To Being Transported To Well Site.	X
		Retrieve Wear Bushing, M/U Jet Sub And Flush BOP Stack & Well Head With Fresh Water.	√
		All Crossovers, Pup Joints For Space Out Measured Put In Right Place.	√
		Lift Control Line And Protectors On Rig Floor.	√
		Hold A Pre Job Safety Meeting For Running Upper Completion String.	√
3	Assembling and RIH	M/U 3-1/2" Re-entry Guide Shoe And 3-1/2" BTM No Go Landing Nipple	√
		Check The Conditions Landing Nipple To Make Sure There Is No Damage, Observe There Is No Any Trash Trapped Inside.	√
		Assemble Landing Nipple.	√
		RIH 1 Joint Tubing As Per Tally	√
		P/U And M/U Hydraulic-Set RETRIEVABLE Production Packer.	√
		Much More Care Should Be Taken When Packer Is Passing Well Head And Liner Hanger While RIH.	√
		Slack Off Packer Assembly, Double Check The Quantity Of Shear Pins, Remove The Tape On The Element, Check If Any Damages On It.	√

		RIH 1 Joint Tubing As Per Tally	√
		M/U Pup Joint And SSD (close Position) To Tubing String With check valve Inside.	√
		Pressure Test Tubing String 6000psi/15min Every 100 JTs.	√
		RIH Completion String and M/U traveling joint as per running tally.	√
		Cont. Running Tubing as per Tally.	-
		M/U TRSSSV	√
		Install control line to TRSSSV and pressure test control line 6000psi x 15mins. And then keep 3000psi pressure while running to ensure TRSSSV open. Install TRSSSV protector for the 1/4” control line. Continue to run 4-1/2” tubing as per running tally.	√
4	M/U and Space out Tubing Hanger	Pick up & M/U tubing hanger with double pin crossover. M/U landing joint. Check string weight upward and downward.	√
		Roughly cut control line about 2 meters above tubing hanger, wrap 2-3 turns and then feed through Tubing Hanger.	√
		Check string weight upward and downward and Space out Tubing Hanger 1.5 m (Half stroke) above tubing head spool	√
Item	**Operation Name**	**Remark**	**Check Mark✓**
5	Set production packer	R/Up Slick Line. Remove Check valve inside SSD	√
		RIH and Set check vlve in Landing Nipple. POOH to surface.	√
		Pressurize inside tubing to 500psi to ensure traveling joint is full open. Increase Pressure gradually to SET PACKER. Increase pressure to 6000 psi to Test String.	√


6	Land Tubing hanger	Move down completion string and apply required weight to shear traveling joint load pins and Land Tubing hanger in T.H.S. Slack off completely & Record the weight.	√
		Drain the BOP stack through the gate valves of tubing head before landing hanger in THS. Leave the valves open.	√
		Tie Down Screws on THS should be fully open before Operation	√
7	N/D BOP & N/U X-mas tree	Tighten tie down screws.	√
		Test inside string w/ 6000 psi, 15 min.	√
		R/Up Slick Line. RIH with slick line and Ret. Check valve from Landing Nipple. POOH to surface.	√
		Test Annulus w/ 2000 psi 15min.	√
		Close Hydrill and test above tubing hanger (annulus between BOP and landing joint) to 1000psi.	√
		B/O & L/D landing joint.	√
		Set 4” 2Way in TBG Hanger & Test it, Back off and L/D Running Tool.	√
		N/D BOP.	√
		Feed control line, through head bonnet.	√
		Check hanger for any damage and pressure test control line to 8000psi	√
		Pressure test chemical injection line & rapture the disc after installing Bonnet.	-
		N/U X-mass tree as program. (Bottom Master)	√
		Perform required tests for X-mass tree. (Bottom Master)	√

		Connect from X-mass tree kill valve to the pump unit and test X-Mas tree body to 1000/6000 psi for 15 min against TWCV.	√
		Remove 4" two way, install 4" one way	√
		Close TRSSSV	√
		Release the rig. Clean the well site.	√

Table 9-3: AZNS-075-ST1 Operation Checklist

9.5 Completion Sketch & Tally

Contractor		Completion Well Schematic						Client				
		Liner & Tubing Data										
Field	AZADEGAN	Description	7" Liner	7" Tie-Back	5" Liner	3 1/2" Tubing	4 1/2" Tubing	Perforation	7" Liner Lap			2167.5
Well Number:	AZNS-75	OD[in]	7	7	5	3.5	4.5	3842 - 3846.3	7" Tie-Back Liner Lap			2034.5
Rig :	OEOC-201	Nominal weight [lb/ft]	29	29	18	10.2	18.9		5" Liner Lap			3596
RTE-GLE	3.95	Grade	L-80	L-80	L-80	L-80	L-80	3849 - 3852	5" Liner Shoe			3888
RTE-THF	12.95	Thread	HSM1	TPCQ	HSG3-FJTHD	HSM3	HSM3		Total Depth:			3888
Rig Spudded Date :	TBA	Inside diameter [in]	6.184	6.184	4.276	2.92	3.64	3853 - 3856	X-mass Tree:			MSP-DRILEX
End of Operation	31.Aug.2025	API Drift Diameter	6.059	6.059	4.151	2.8	3.515		Size & Rating:			4 1/16", 10 k

Schematic		Description Elevation (floor - TBG Head Flange)	Max OD	Min ID	Length (m)	BTM(m)	TOP(m)
	1	TBG HANGER 11" * 4-1/2" ACME Box up * 4-1/2" TPCQ-EX Box Down , M/C: FF-0.5 T/C: U PSL: 3G PR: 2, 4" Type "H" Two Way, MSP Drilex	11	3.68	0.37	10.52	10.15
	3	4-1/2" FLUTED SWAGE ADAPTER D/P, 18.9# TPCQ-EX PIN ON TOP X HSM3 PIN ON DOWN* 9Cr1MO, Weiqixin Co	5.5	3.64	1.018	11.538	10.52
	4	5 JOINTs TUBING 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	47.571	59.109	11.538
	5	PUP JOINT 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	1.622	60.731	59.109
	6	4-1/2" FLOW COUPLING,18.9#,9Cr1MO,HSM3 , 6 FT, Weiqixin Co	5.5	3.64	1.725	62.456	60.731
	7	TRSSV Tubing Retrievable Saftey Valve, 4-1/2", 18.9# w/ 3.437" Seal bore,HSM3 ,9Cr1MO, 7.5K WP with AF Profile, Flapper Type, Weiqixin Co	7.5	3.437	1.783	64.239	62.456
	8	4-1/2" FLOW COUPLING, 18.9#,9Cr1MO,HSM3 , 4' FT , Weiqixin Co	5.5	3.64	1.115	65.354	64.239
	9	PUP JOINT 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	1.624	66.978	65.354
	10	197 JOINTs TUBING 4-1/2"HSM3 18.9#, L-80	5.118	3.64	1872.458	1939.436	66.978
	11	X-over 4-1/2"HSM3, 18.9# BOX * 3-1/2"HSM3 , 10.2# PIN, Weiqixin Co	5.25	2.922	1.124	1940.56	1939.436
	12	38 JOINTs TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	359.954	2300.514	1940.56
	17	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.865	2302.379	2300.514
	18	Second 3 1/2" CIV TUBING RETRIEVABLE CHEMICAL INJECTION MANDRELHSM3 , 10.2#,SUPER 13CR-110KSI W/CHECK VALVE, DUAL TYPE & RUPTURE DISC, Weiqixin Co	5	2.922	0.728	2303.107	2302.379
	19	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.87	2304.977	2303.107
	24	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.514	2314.491	2304.977
	17	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.863	2316.354	2314.491
	18	First 3 1/2" CIV TUBING RETRIEVABLE CHEMICAL INJECTION MANDRELHSM3 , 10.2#,SUPER 13CR-110KSI W/CHECK VALVE, DUAL TYPE & RUPTURE DISC, Weiqixin Co	5	2.922	0.728	2317.082	2316.354
	19	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.62	2318.702	2317.082
	24	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.517	2328.219	2318.702
	21	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.73	2329.949	2328.219
	22	3-1/2" EXP. JOINT,HSM3 , 9Cr1MO, 10' STK (Half Closed) Splind Rotational Lock System Any Position, Shear Pin Set 15,000 LBS, Weiqixin Co	5.315	2.922	5.8	2335.749	2329.949
	23	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.9	2337.649	2335.749
	24	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.52	2347.169	2337.649
	25	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.925	2349.094	2347.169
	26	3-1/2" NON-ELASTOMERIC SLIDING SIDE DOOR, 9Cr1MO, HSM3 with Type X Selective Profile (PROFILE: 2.750" X, DOWNWARD OPEN) , Weiqixin Co	4.551	2.75	1.195	2350.289	2349.094
	27	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.856	2352.145	2350.289
	28	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.52	2361.665	2352.145
	31	7" 29 PPF CASING HYDRAULIC SET RETRIEVABLE PRODUCTION PACKER TO BE RUN IN 7.00" 29 PPF CASING, 9Cr1MO, HSM3 pin * box, Weiqixin Co	5.91	2.922	2.87	2364.535	2361.665
	34	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.524	2374.059	2364.535
	36	3-1/2" BOTTOM NO-GO LANDING,HSM3 , 10.2#, 9Cr1MO w/ Seal Bore 2.75" TYPE XN (NO-GO ID: 2.635"), Weiqixin Co	4.5	2.75	0.374	2374.433	2374.059
	38	3-1/2" 10.2# RE-ENTERYY GUIDE SHOE, 9Cr1MO, HSM3 box, Weiqixin Co	4.25	2.922	0.247	2374.68	2374.433
		END OF COMPLETION STRING				2374.68	2374.68

Tubing Retrievable Saftey Valve	64.239	62.456
Traveling Joint	2335.749	2329.949
SSD	2350.289	2349.094
7'' HYDRAULIC SET RETRIEVABLE PRODUCTION PACKER	2364.535	2361.665
NO-GO Landing Nipple	2374.433	2374.059
Entry Guide	2374.68	2374.433

Figure 9-7: AZNS-075-ST1 Completion Sketch

MSA

Field :	S.Azadegan	Well NO:	AZNS075	Rig NO:	OEOC201	Drig CO:	OEOC
PEDEC, PPL		Completion String					

Grade	ID "	Drift "	Weight lb/ft	Burst psi	Collaspse psi	Yield klbs	Coupling "	TQ ft x lb	Nominal Dia. OD
L-80	2.922	2.797	10.2	11,560.0	12,120.0	233	3.962	3200-3550-3900	3-1/2"
L-80	3.640	3.515	18.9	13,380.0	13,820.0	440	5.137	7920-8800-9680	4-1/2"

BTM NO GO Depth:	2374.06	Formation Name :	Gadvan	Hook Weight :	68 k lb
BTM of String	2374.68	Formation Top :	3708	VOLUME (TOTAL)	#REF!
Packer Depth :	2361.67			Mud Weight (pcf) :	84

Number on jt	Grade	Run In No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	VOL(BBL)	Remarks	
								joint no	IN / OUT
					2374.68	68.00			
3-1/2" Wireline Re-Entry Guide, 10.2 #, HSM3, 9CR1MO, WEIQIXIN Co	3-1/2" Mule Shoe		0.247	0.25	2374.433	68.01	0.01		
3-1/2" BTM No-Go LND Nipple, HSM3, 10.2#, 9CR1MO, Seal Bore 2.750" TYPE XN, WEIQIXIN Co, 7.5K	3-1/2" BTM NO GO		0.374	0.62	2374.059	68.02	0.02		
1	TBG 3-1/2", 10.2#, L-80,HSM3	1	9.524	10.15	2364.535	68.28	0.28	1	
7" 29# CSG Hydraulic set retrievable production packer to be run in 7.00" 29 PPF CSG, WEIQIXIN Co	PKR		2.870	13.02	2361.665	68.36	0.35		
2	TBG 3-1/2", 10.2#, L-80,HSM3	2	9.520	22.54	2352.145	68.62	0.61	2	
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		2	24.39	2350.289	68.62	0.61		
3-1/2" Non-Elastomeric Sliding Side Door, 9CR1MO, HSM3 w/ Type X Selective profile (Profile: 2.750" X, Downward open), 7.5K	SSD		1.195	25.59	2349.094	68.66	0.65		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.925	27.51	2347.169	68.71	0.70		
3	TBG 3-1/2", 10.2#, L-80,HSM3	3	9.520	37.03	2337.649	68.97	0.96	3	
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.900	38.93	2335.749	69.03	1.01		
3-1/2" EXP. Jt,HSM3 , 9CR1MO, 10' STK (Fully Open) Splind Rotational Lock System Any Position, Shear Pin Set 20 Klbs, WEIQIXIN Co	Traveling Jt		5.800	44.73	2329.949	69.19	1.17		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.730	46.46	2328.219	69.24	1.21		
4	TBG 3-1/2", 10.2#, L-80,HSM3	4	9.517	55.98	2318.702	69.50	1.47	4	
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.620	57.60	2317.082	69.50	1.47		
3 1/2" 15K CIV TBG Retrievable Chemical Injection Mandrel, HSM3 , 10.2#,Super 13CR-110KSI w/ check valve, dual type & rupture disc, Weiqixin Co	CIV #1		0.728	58.33	2316.354	69.52	1.49		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.863	60.19	2314.491	69.57	1.54		
5	TBG 3-1/2", 10.2#, L-80,HSM3	5	9.514	69.70	2304.977	69.84	1.80	5	Protector
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.870	71.57	2303.107	69.84	1.80		
3 1/2" 15k CIV TBG Retrievable Chemical Injection Mandrel, HSM3 , 10.2#,Super 13CR-110KSI w/ check valve, dual type & rupture disc, Weiqixin Co	CIV #2		0.728	72.30	2302.379	69.86	1.82		
3-1/2" Pup Jt,HSM3 , 10.2#, L-80, Type-1	Pup Jt 3-1/2", 10.2#,HSM3		1.865	74.17	2300.514	69.91	1.87		Protector
6	TBG 3-1/2", 10.2#, L-80,HSM3	6	9.514	83.68	2291.000	70.17	2.13	6	Protector
7	TBG 3-1/2", 10.2#, L-80,HSM3	7	9.524	93.20	2281.476	70.44	2.39	7	Protector
8	TBG 3-1/2", 10.2#, L-80,HSM3	8	9.515	102.72	2271.961	70.70	2.65	8	Protector
9	TBG 3-1/2", 10.2#, L-80,HSM3	9	9.527	112.25	2262.434	70.96	2.91	9	Protector
10	TBG 3-1/2", 10.2#, L-80,HSM3	10	9.519	121.77	2252.915	71.23	3.17	10	Protector
11	TBG 3-1/2", 10.2#, L-80,HSM3	11	9.519	131.28	2243.396	71.49	3.43	11	Protector
12	TBG 3-1/2", 10.2#, L-80,HSM3	12	9.521	140.81	2233.875	71.75	3.69	12	Protector
13	TBG 3-1/2", 10.2#, L-80,HSM3	13	9.517	150.32	2224.358	72.02	3.95	13	Protector
14	TBG 3-1/2", 10.2#, L-80,HSM3	14	9.527	159.85	2214.831	72.28	4.20	14	Protector
15	TBG 3-1/2", 10.2#, L-80,HSM3	15	9.509	169.36	2205.322	72.55	4.46	15	Protector
16	TBG 3-1/2", 10.2#, L-80,HSM3	16	9.529	178.89	2195.793	72.81	4.72	16	Protector
17	TBG 3-1/2", 10.2#, L-80,HSM3	17	9.515	188.40	2186.278	73.07	4.98	17	Protector
18	TBG 3-1/2", 10.2#, L-80,HSM3	18	9.511	197.91	2176.767	73.34	5.24	18	Protector
19	TBG 3-1/2", 10.2#, L-80,HSM3	19	9.504	207.42	2167.263	73.60	5.50	19	Protector
20	TBG 3-1/2", 10.2#, L-80,HSM3	20	9.329	216.75	2157.934	73.86	5.75	20	Protector
21	TBG 3-1/2", 10.2#, L-80,HSM3	21	9.524	226.27	2148.410	74.12	6.01	21	Protector
23	TBG 3-1/2", 10.2#, L-80,HSM3	22	9.514	235.78	2138.896	74.39	6.27	22	Protector
24	TBG 3-1/2", 10.2#, L-80,HSM3	23	9.519	245.30	2129.377	74.65	6.53	23	Protector
25	TBG 3-1/2", 10.2#, L-80,HSM3	24	9.507	254.81	2119.870	74.91	6.79	24	Protector
26	TBG 3-1/2", 10.2#, L-80,HSM3	25	9.52	264.33	2110.350	75.18	7.05	25	Protector
27	TBG 3-1/2", 10.2#, L-80,HSM3	26	9.524	273.85	2100.826	75.44	7.31	26	Protector

28	TBG 3-1/2", 10.2#, L-80,HSM3	27	9.522	283.38	2091.304	75.71	7.57	27	Protector
29	TBG 3-1/2", 10.2#, L-80,HSM3	28	9.522	292.90	2081.782	75.97	7.83	28	Protector
30	TBG 3-1/2", 10.2#, L-80,HSM3	29	9.522	302.42	2072.260	76.23	8.08	29	Protector
31	TBG 3-1/2", 10.2#, L-80,HSM3	30	9.524	311.94	2062.736	76.50	8.34	30	Protector
32	TBG 3-1/2", 10.2#, L-80,HSM3	31	9.52	321.46	2053.216	76.76	8.60	31	Protector
33	TBG 3-1/2", 10.2#, L-80,HSM3	32	9.058	330.52	2044.158	77.01	8.85	32	Protector
34	TBG 3-1/2", 10.2#, L-80,HSM3	33	9.504	340.03	2034.654	77.28	9.11	33	Protector
35	TBG 3-1/2", 10.2#, L-80,HSM3	34	9.324	349.35	2025.330	77.53	9.36	34	Protector
36	TBG 3-1/2", 10.2#, L-80,HSM3	35	9.502	358.85	2015.828	77.80	9.62	35	Protector
37	TBG 3-1/2", 10.2#, L-80,HSM3	36	9.415	368.27	2006.413	78.06	9.88	36	Protector
38	TBG 3-1/2", 10.2#, L-80,HSM3	37	9.524	377.79	1996.889	78.32	10.14	37	Protector
39	TBG 3-1/2", 10.2#, L-80,HSM3	38	9.426	387.22	1987.463	78.58	10.39	38	Protector
40	TBG 3-1/2", 10.2#, L-80,HSM3	39	9.407	396.62	1978.056	78.85	10.65	39	Protector
41	TBG 3-1/2", 10.2#, L-80,HSM3	40	9.06	405.68	1968.996	79.10	10.89	40	Protector
42	TBG 3-1/2", 10.2#, L-80,HSM3	41	9.509	415.19	1959.487	79.36	11.15	41	Protector
43	TBG 3-1/2", 10.2#, L-80,HSM3	42	9.4	424.59	1950.087	79.62	11.41	42	Protector
44	TBG 3-1/2", 10.2#, L-80,HSM3	43	9.527	434.12	1940.560	79.88	11.67	43	Protector
X-over 4-1/2"HSM3, 18.9# BOX * 3-1/2"HSM3 , 10.2# PIN,	TBG 4-1/2", 18.9#, L-80,HSM3	0	1.124	435.24	1939.436	79.94	11.72	0	Protector
51	TBG 4-1/2", 18.9#, L-80,HSM3	44	9.549	444.79	1929.887	80.43	12.12	44	Protector
52	TBG 4-1/2", 18.9#, L-80,HSM3	45	9.526	454.32	1920.361	80.92	12.52	45	Protector
53	TBG 4-1/2", 18.9#, L-80,HSM3	46	9.519	463.84	1910.842	81.41	12.92	46	Protector
54	TBG 4-1/2", 18.9#, L-80,HSM3	47	9.526	473.36	1901.316	81.90	13.33	47	Protector
55	TBG 4-1/2", 18.9#, L-80,HSM3	48	9.527	482.89	1891.789	82.39	13.73	48	Protector
56	TBG 4-1/2", 18.9#, L-80,HSM3	49	9.522	492.41	1882.267	82.88	14.13	49	Protector
57	TBG 4-1/2", 18.9#, L-80,HSM3	50	9.527	501.94	1872.740	83.37	14.53	50	Protector
58	TBG 4-1/2", 18.9#, L-80,HSM3	51	9.53	511.47	1863.210	83.86	14.93	51	Protector
59	TBG 4-1/2", 18.9#, L-80,HSM3	52	9.565	521.04	1853.645	84.35	15.34	52	Protector
60	TBG 4-1/2", 18.9#, L-80,HSM3	53	9.533	530.57	1844.112	84.84	15.74	53	Protector
61	TBG 4-1/2", 18.9#, L-80,HSM3	54	9.548	540.12	1834.564	85.33	16.14	54	Protector
62	TBG 4-1/2", 18.9#, L-80,HSM3	55	9.539	549.66	1825.025	85.82	16.55	55	Protector
63	TBG 4-1/2", 18.9#, L-80,HSM3	56	9.422	559.08	1815.603	86.30	16.95	56	Protector
64	TBG 4-1/2", 18.9#, L-80,HSM3	57	9.55	568.63	1806.053	86.79	17.35	57	Protector
65	TBG 4-1/2", 18.9#, L-80,HSM3	58	9.566	578.19	1796.487	87.28	17.75	58	Protector
66	TBG 4-1/2", 18.9#, L-80,HSM3	59	9.394	587.59	1787.093	87.77	18.15	59	Protector
67	TBG 4-1/2", 18.9#, L-80,HSM3	60	9.533	597.12	1777.560	88.26	18.55	60	Protector
68	TBG 4-1/2", 18.9#, L-80,HSM3	61	9.532	606.65	1768.028	88.75	18.95	61	Protector
69	TBG 4-1/2", 18.9#, L-80,HSM3	62	9.53	616.18	1758.498	89.23	19.36	62	Protector
70	TBG 4-1/2", 18.9#, L-80,HSM3	63	9.526	625.71	1748.972	89.72	19.76	63	Protector
71	TBG 4-1/2", 18.9#, L-80,HSM3	64	9.527	635.24	1739.445	90.21	20.16	64	Protector
72	TBG 4-1/2", 18.9#, L-80,HSM3	65	9.528	644.76	1729.917	90.70	20.56	65	Protector
73	TBG 4-1/2", 18.9#, L-80,HSM3	66	9.429	654.19	1720.488	91.19	20.96	66	Protector
74	TBG 4-1/2", 18.9#, L-80,HSM3	67	9.528	663.72	1710.960	91.68	21.36	67	Protector
75	TBG 4-1/2", 18.9#, L-80,HSM3	68	9.408	673.13	1701.552	92.16	21.76	68	Protector

76	TBG 4-1/2", 18.9#, L-80,HSM3	69	9.528	682.66	1692.024	92.65	22.16	69	Protector
77	TBG 4-1/2", 18.9#, L-80,HSM3	70	9.552	692.21	1682.472	93.14	22.57	70	Protector
78	TBG 4-1/2", 18.9#, L-80,HSM3	71	9.528	701.74	1672.944	93.63	22.97	71	Protector
79	TBG 4-1/2", 18.9#, L-80,HSM3	72	9.551	711.29	1663.393	94.12	23.37	72	Protector
80	TBG 4-1/2", 18.9#, L-80,HSM3	73	9.531	720.82	1653.862	94.61	23.78	73	Protector
81	TBG 4-1/2", 18.9#, L-80,HSM3	74	9.555	730.37	1644.307	95.10	24.18	74	Protector
82	TBG 4-1/2", 18.9#, L-80,HSM3	75	9.245	739.62	1635.062	95.57	24.57	75	Protector
83	TBG 4-1/2", 18.9#, L-80,HSM3	76	9.557	749.18	1625.505	96.07	24.97	76	Protector
84	TBG 4-1/2", 18.9#, L-80,HSM3	77	9.552	758.73	1615.953	96.56	25.38	77	Protector
85	TBG 4-1/2", 18.9#, L-80,HSM3	78	9.543	768.27	1606.410	97.05	25.78	78	Protector
86	TBG 4-1/2", 18.9#, L-80,HSM3	79	9.556	777.83	1596.854	97.54	26.18	79	Protector
87	TBG 4-1/2", 18.9#, L-80,HSM3	80	9.543	787.37	1587.311	98.03	26.59	80	Protector
88	TBG 4-1/2", 18.9#, L-80,HSM3	81	9.24	796.61	1578.071	98.50	26.98	81	Protector
89	TBG 4-1/2", 18.9#, L-80,HSM3	82	9.526	806.14	1568.545	98.99	27.38	82	Protector
90	TBG 4-1/2", 18.9#, L-80,HSM3	83	9.527	815.66	1559.018	99.48	27.78	83	Protector
91	TBG 4-1/2", 18.9#, L-80,HSM3	84	9.526	825.19	1549.492	99.97	28.18	84	Protector
92	TBG 4-1/2", 18.9#, L-80,HSM3	85	9.416	834.60	1540.076	100.45	28.58	85	Protector
93	TBG 4-1/2", 18.9#, L-80,HSM3	86	9.403	844.01	1530.673	100.94	28.98	86	Protector
94	TBG 4-1/2", 18.9#, L-80,HSM3	87	9.375	853.38	1521.298	101.42	29.37	87	Protector
95	TBG 4-1/2", 18.9#, L-80,HSM3	88	9.533	862.92	1511.765	101.91	29.78	88	Protector
96	TBG 4-1/2", 18.9#, L-80,HSM3	89	9.531	872.45	1502.234	102.40	30.18	89	Protector
97	TBG 4-1/2", 18.9#, L-80,HSM3	90	9.521	881.97	1492.713	102.89	30.58	90	Protector
98	TBG 4-1/2", 18.9#, L-80,HSM3	91	9.422	891.39	1483.291	103.37	30.98	91	Protector
99	TBG 4-1/2", 18.9#, L-80,HSM3	92	9.446	900.84	1473.845	103.85	31.38	92	Protector
100	TBG 4-1/2", 18.9#, L-80,HSM3	93	9.553	910.39	1464.292	104.35	31.78	93	Protector
101	TBG 4-1/2", 18.9#, L-80,HSM3	94	9.327	919.72	1454.965	104.82	32.17	94	Protector
102	TBG 4-1/2", 18.9#, L-80,HSM3	95	9.552	929.27	1445.413	105.31	32.58	95	Protector
103	TBG 4-1/2", 18.9#, L-80,HSM3	96	9.282	938.55	1436.131	105.79	32.97	96	Protector
104	TBG 4-1/2", 18.9#, L-80,HSM3	97	9.435	947.98	1426.696	106.28	33.37	97	Protector
105	TBG 4-1/2", 18.9#, L-80,HSM3	98	9.543	957.53	1417.153	106.77	33.77	98	Protector
106	TBG 4-1/2", 18.9#, L-80,HSM3	99	9.424	966.95	1407.729	107.25	34.17	99	Protector
107	TBG 4-1/2", 18.9#, L-80,HSM3	100	9.433	976.38	1398.296	107.73	34.57	100	Protector
108	TBG 4-1/2", 18.9#, L-80,HSM3	101	9.539	985.92	1388.757	108.22	34.97	101	Protector
109	TBG 4-1/2", 18.9#, L-80,HSM3	102	9.532	995.46	1379.225	108.71	35.37	102	Protector
110	TBG 4-1/2", 18.9#, L-80,HSM3	103	9.522	1004.98	1369.703	109.20	35.78	103	Protector
111	TBG 4-1/2", 18.9#, L-80,HSM3	104	9.531	1014.51	1360.172	109.69	36.18	104	Protector
112	TBG 4-1/2", 18.9#, L-80,HSM3	105	9.532	1024.04	1350.640	110.18	36.58	105	Protector
113	TBG 4-1/2", 18.9#, L-80,HSM3	106	9.53	1033.57	1341.110	110.67	36.98	106	Protector
114	TBG 4-1/2", 18.9#, L-80,HSM3	107	9.537	1043.11	1331.573	111.16	37.39	107	Protector
115	TBG 4-1/2", 18.9#, L-80,HSM3	108	9.056	1052.16	1322.517	111.63	37.77	108	Protector
116	TBG 4-1/2", 18.9#, L-80,HSM3	109	9.532	1061.70	1312.985	112.12	38.17	109	Protector
117	TBG 4-1/2", 18.9#, L-80,HSM3	110	9.529	1071.22	1303.456	112.61	38.57	110	Protector
118	TBG 4-1/2", 18.9#, L-80,HSM3	111	9.528	1080.75	1293.928	113.09	38.98	111	Protector
119	TBG 4-1/2", 18.9#, L-80,HSM3	112	9.533	1090.29	1284.395	113.58	39.38	112	Protector
120	TBG 4-1/2", 18.9#, L-80,HSM3	113	9.526	1099.81	1274.869	114.07	39.78	113	Protector
121	TBG 4-1/2", 18.9#, L-80,HSM3	114	9.568	1109.38	1265.301	114.56	40.18	114	Protector
122	TBG 4-1/2", 18.9#, L-80,HSM3	115	9.53	1118.91	1255.771	115.05	40.59	115	Protector
123	TBG 4-1/2", 18.9#, L-80,HSM3	116	9.526	1128.44	1246.245	115.54	40.99	116	Protector
124	TBG 4-1/2", 18.9#, L-80,HSM3	117	9.526	1137.96	1236.719	116.03	41.39	117	Protector
125	TBG 4-1/2", 18.9#, L-80,HSM3	118	9.541	1147.50	1227.178	116.52	41.79	118	Protector
126	TBG 4-1/2", 18.9#, L-80,HSM3	119	9.528	1157.03	1217.650	117.01	42.20	119	Protector
127	TBG 4-1/2", 18.9#, L-80,HSM3	120	9.421	1166.45	1208.229	117.50	42.59	120	Protector
128	TBG 4-1/2", 18.9#, L-80,HSM3	121	9.424	1175.88	1198.805	117.98	42.99	121	Protector
130	TBG 4-1/2", 18.9#, L-80,HSM3	122	9.398	1185.27	1189.407	118.46	43.39	122	Protector
131	TBG 4-1/2", 18.9#, L-80,HSM3	123	9.399	1194.67	1180.008	118.95	43.79	123	Protector
132	TBG 4-1/2", 18.9#, L-80,HSM3	124	9.526	1204.20	1170.482	119.43	44.19	124	Protector
133	TBG 4-1/2", 18.9#, L-80,HSM3	125	9.393	1213.59	1161.089	119.92	44.59	125	Protector
134	TBG 4-1/2", 18.9#, L-80,HSM3	126	9.539	1223.13	1151.550	120.41	44.99	126	Protector
136	TBG 4-1/2", 18.9#, L-80,HSM3	127	9.531	1232.66	1142.019	120.90	45.39	127	Protector
137	TBG 4-1/2", 18.9#, L-80,HSM3	128	9.543	1242.20	1132.476	121.39	45.79	128	Protector
138	TBG 4-1/2", 18.9#, L-80,HSM3	129	9.528	1251.73	1122.948	121.88	46.20	129	Protector
139	TBG 4-1/2", 18.9#, L-80,HSM3	130	9.214	1260.95	1113.734	122.35	46.59	130	Protector

141	TBG 4-1/2", 18.9#, L-80,HSM3	131	9.526	1270.47	1104.208	122.84	46.99	131	Protector
142	TBG 4-1/2", 18.9#, L-80,HSM3	132	9.525	1280.00	1094.683	123.33	47.39	132	Protector
143	TBG 4-1/2", 18.9#, L-80,HSM3	133	9.552	1289.55	1085.131	123.82	47.79	133	Protector
144	TBG 4-1/2", 18.9#, L-80,HSM3	134	9.516	1299.07	1075.615	124.31	48.19	134	Protector
145	TBG 4-1/2", 18.9#, L-80,HSM3	135	9.526	1308.59	1066.089	124.80	48.60	135	Protector
146	TBG 4-1/2", 18.9#, L-80,HSM3	136	9.525	1318.12	1056.564	125.29	49.00	136	Protector
147	TBG 4-1/2", 18.9#, L-80,HSM3	137	9.526	1327.64	1047.038	125.77	49.40	137	Protector
148	TBG 4-1/2", 18.9#, L-80,HSM3	138	9.521	1337.16	1037.517	126.26	49.80	138	Protector
150	TBG 4-1/2", 18.9#, L-80,HSM3	139	9.528	1346.69	1027.989	126.75	50.21	139	Protector
151	TBG 4-1/2", 18.9#, L-80,HSM3	140	9.517	1356.21	1018.472	127.24	50.61	140	Protector
152	TBG 4-1/2", 18.9#, L-80,HSM3	141	9.528	1365.74	1008.944	127.73	51.01	141	Protector
153	TBG 4-1/2", 18.9#, L-80,HSM3	142	9.553	1375.29	999.391	128.22	51.41	142	Protector
154	TBG 4-1/2", 18.9#, L-80,HSM3	143	9.528	1384.82	989.863	128.71	51.82	143	Protector
155	TBG 4-1/2", 18.9#, L-80,HSM3	144	9.527	1394.34	980.336	129.20	52.22	144	Protector
156	TBG 4-1/2", 18.9#, L-80,HSM3	145	9.412	1403.76	970.924	129.68	52.62	145	Protector
157	TBG 4-1/2", 18.9#, L-80,HSM3	146	9.533	1413.29	961.391	130.17	53.02	146	Protector
158	TBG 4-1/2", 18.9#, L-80,HSM3	147	9.528	1422.82	951.863	130.66	53.42	147	Protector
159	TBG 4-1/2", 18.9#, L-80,HSM3	148	9.529	1432.35	942.334	131.15	53.82	148	Protector
160	TBG 4-1/2", 18.9#, L-80,HSM3	149	9.528	1441.87	932.806	131.64	54.23	149	Protector
161	TBG 4-1/2", 18.9#, L-80,HSM3	150	9.551	1451.43	923.255	132.13	54.63	150	Protector
162	TBG 4-1/2", 18.9#, L-80,HSM3	151	9.524	1460.95	913.731	132.62	55.03	151	Protector
163	TBG 4-1/2", 18.9#, L-80,HSM3	152	9.548	1470.50	904.183	133.11	55.43	152	Protector
164	TBG 4-1/2", 18.9#, L-80,HSM3	153	9.553	1480.05	894.630	133.60	55.84	153	Protector
165	TBG 4-1/2", 18.9#, L-80,HSM3	154	9.528	1489.58	885.102	134.09	56.24	154	Protector
166	TBG 4-1/2", 18.9#, L-80,HSM3	155	9.528	1499.11	875.574	134.58	56.64	155	Protector
167	TBG 4-1/2", 18.9#, L-80,HSM3	156	9.521	1508.63	866.053	135.07	57.04	156	Protector
169	TBG 4-1/2", 18.9#, L-80,HSM3	157	9.523	1518.15	856.530	135.56	57.45	157	Protector
170	TBG 4-1/2", 18.9#, L-80,HSM3	158	9.522	1527.67	847.008	136.05	57.85	158	Protector
171	TBG 4-1/2", 18.9#, L-80,HSM3	159	9.528	1537.20	837.480	136.54	58.25	159	Protector
172	TBG 4-1/2", 18.9#, L-80,HSM3	160	9.529	1546.73	827.951	137.03	58.65	160	Protector
173	TBG 4-1/2", 18.9#, L-80,HSM3	161	9.526	1556.26	818.425	137.52	59.06	161	Protector
174	TBG 4-1/2", 18.9#, L-80,HSM3	162	9.184	1565.44	809.241	137.99	59.44	162	Protector
175	TBG 4-1/2", 18.9#, L-80,HSM3	163	9.527	1574.97	799.714	138.48	59.85	163	Protector
176	TBG 4-1/2", 18.9#, L-80,HSM3	164	9.525	1584.49	790.189	138.97	60.25	164	Protector
177	TBG 4-1/2", 18.9#, L-80,HSM3	165	9.526	1594.02	780.663	139.46	60.65	165	Protector
178	TBG 4-1/2", 18.9#, L-80,HSM3	166	9.528	1603.55	771.135	139.94	61.05	166	Protector
179	TBG 4-1/2", 18.9#, L-80,HSM3	167	9.527	1613.07	761.608	140.43	61.46	167	Protector
180	TBG 4-1/2", 18.9#, L-80,HSM3	168	9.523	1622.60	752.085	140.92	61.86	168	Protector
181	TBG 4-1/2", 18.9#, L-80,HSM3	169	9.523	1632.12	742.562	141.41	62.26	169	Protector
182	TBG 4-1/2", 18.9#, L-80,HSM3	170	9.55	1641.67	733.012	141.90	62.66	170	Protector
183	TBG 4-1/2", 18.9#, L-80,HSM3	171	9.414	1651.08	723.598	142.39	63.06	171	Protector
184	TBG 4-1/2", 18.9#, L-80,HSM3	172	9.393	1660.48	714.205	142.87	63.46	172	Protector
185	TBG 4-1/2", 18.9#, L-80,HSM3	173	9.538	1670.01	704.667	143.36	63.86	173	Protector
186	TBG 4-1/2", 18.9#, L-80,HSM3	174	9.538	1679.55	695.129	143.85	64.26	174	Protector
187	TBG 4-1/2", 18.9#, L-80,HSM3	175	9.403	1688.95	685.726	144.33	64.66	175	Protector
188	TBG 4-1/2", 18.9#, L-80,HSM3	176	9.524	1698.48	676.202	144.82	65.06	176	Protector
189	TBG 4-1/2", 18.9#, L-80,HSM3	177	9.558	1708.04	666.644	145.31	65.47	177	Protector
190	TBG 4-1/2", 18.9#, L-80,HSM3	178	9.521	1717.56	657.123	145.80	65.87	178	Protector
191	TBG 4-1/2", 18.9#, L-80,HSM3	179	9.529	1727.09	647.594	146.29	66.27	179	Protector
192	TBG 4-1/2", 18.9#, L-80,HSM3	180	9.528	1736.61	638.066	146.78	66.67	180	Protector
193	TBG 4-1/2", 18.9#, L-80,HSM3	181	9.548	1746.16	628.518	147.27	67.08	181	Protector
194	TBG 4-1/2", 18.9#, L-80,HSM3	182	9.511	1755.67	619.007	147.76	67.48	182	Protector
195	TBG 4-1/2", 18.9#, L-80,HSM3	183	9.521	1765.19	609.486	148.25	67.88	183	Protector
196	TBG 4-1/2", 18.9#, L-80,HSM3	184	9.411	1774.61	600.075	148.73	68.28	184	Protector
197	TBG 4-1/2", 18.9#, L-80,HSM3	185	9.52	1784.13	590.555	149.22	68.68	185	Protector
198	TBG 4-1/2", 18.9#, L-80,HSM3	186	9.527	1793.65	581.028	149.71	69.08	186	Protector
199	TBG 4-1/2", 18.9#, L-80,HSM3	187	9.53	1803.18	571.498	150.20	69.48	187	Protector
200	TBG 4-1/2", 18.9#, L-80,HSM3	188	9.527	1812.71	561.971	150.69	69.89	188	Protector

202	TBG 4-1/2", 18.9#, L-80,HSM3	189	9.525	1822.23	552.446	151.18	70.29	189	Protector
203	TBG 4-1/2", 18.9#, L-80,HSM3	190	9.545	1831.78	542.901	151.67	70.69	190	Protector
204	TBG 4-1/2", 18.9#, L-80,HSM3	191	9.526	1841.31	533.375	152.16	71.09	191	Protector
205	TBG 4-1/2", 18.9#, L-80,HSM3	192	9.532	1850.84	523.843	152.65	71.50	192	Protector
206	TBG 4-1/2", 18.9#, L-80,HSM3	193	9.522	1860.36	514.321	153.13	71.90	193	Protector
207	TBG 4-1/2", 18.9#, L-80,HSM3	194	9.543	1869.90	504.778	153.62	72.30	194	Protector
208	TBG 4-1/2", 18.9#, L-80,HSM3	195	9.528	1879.43	495.250	154.11	72.70	195	Protector
209	TBG 4-1/2", 18.9#, L-80,HSM3	196	9.525	1888.96	485.725	154.60	73.11	196	Protector
210	TBG 4-1/2", 18.9#, L-80,HSM3	197	9.404	1898.36	476.321	155.09	73.50	197	Protector
211	TBG 4-1/2", 18.9#, L-80,HSM3	198	9.527	1907.89	466.794	155.58	73.91	198	Protector
212	TBG 4-1/2", 18.9#, L-80,HSM3	199	9.526	1917.41	457.268	156.06	74.31	199	Protector
213	TBG 4-1/2", 18.9#, L-80,HSM3	200	9.519	1926.93	447.749	156.55	74.71	200	Protector
214	TBG 4-1/2", 18.9#, L-80,HSM3	201	9.528	1936.46	438.221	157.04	75.11	201	Protector
215	TBG 4-1/2", 18.9#, L-80,HSM3	202	9.526	1945.99	428.695	157.53	75.51	202	Protector
216	TBG 4-1/2", 18.9#, L-80,HSM3	203	9.527	1955.51	419.168	158.02	75.92	203	Protector
217	TBG 4-1/2", 18.9#, L-80,HSM3	204	9.42	1964.93	409.748	158.51	76.31	204	Protector
218	TBG 4-1/2", 18.9#, L-80,HSM3	205	9.529	1974.46	400.219	158.99	76.72	205	Protector
219	TBG 4-1/2", 18.9#, L-80,HSM3	206	9.578	1984.04	390.641	159.49	77.12	206	Protector
220	TBG 4-1/2", 18.9#, L-80,HSM3	207	9.518	1993.56	381.123	159.98	77.52	207	Protector
221	TBG 4-1/2", 18.9#, L-80,HSM3	208	9.447	2003.00	371.676	160.46	77.92	208	Protector
222	TBG 4-1/2", 18.9#, L-80,HSM3	209	9.423	2012.43	362.253	160.94	78.32	209	Protector
223	TBG 4-1/2", 18.9#, L-80,HSM3	210	9.538	2021.97	352.715	161.43	78.72	210	Protector
224	TBG 4-1/2", 18.9#, L-80,HSM3	211	9.528	2031.49	343.187	161.92	79.13	211	Protector
225	TBG 4-1/2", 18.9#, L-80,HSM3	212	9.523	2041.02	333.664	162.41	79.53	212	Protector
226	TBG 4-1/2", 18.9#, L-80,HSM3	213	9.543	2050.56	324.121	162.90	79.93	213	Protector
227	TBG 4-1/2", 18.9#, L-80,HSM3	214	9.539	2060.10	314.582	163.39	80.33	214	Protector
228	TBG 4-1/2", 18.9#, L-80,HSM3	215	9.413	2069.51	305.169	163.88	80.73	215	Protector
229	TBG 4-1/2", 18.9#, L-80,HSM3	216	9.519	2079.03	295.650	164.36	81.13	216	Protector
230	TBG 4-1/2", 18.9#, L-80,HSM3	217	9.53	2088.56	286.120	164.85	81.54	217	Protector
231	TBG 4-1/2", 18.9#, L-80,HSM3	218	9.528	2098.09	276.592	165.34	81.94	218	Protector
232	TBG 4-1/2", 18.9#, L-80,HSM3	219	9.521	2107.61	267.071	165.83	82.34	219	Protector
233	TBG 4-1/2", 18.9#, L-80,HSM3	220	9.521	2117.13	257.550	166.32	82.74	220	Protector
235	TBG 4-1/2", 18.9#, L-80,HSM3	221	9.528	2126.66	248.022	166.81	83.14	221	Protector
236	TBG 4-1/2", 18.9#, L-80,HSM3	222	9.518	2136.18	238.504	167.30	83.55	222	Protector
237	TBG 4-1/2", 18.9#, L-80,HSM3	223	9.524	2145.70	228.980	167.79	83.95	223	Protector
238	TBG 4-1/2", 18.9#, L-80,HSM3	224	9.544	2155.24	219.436	168.28	84.35	224	Protector
239	TBG 4-1/2", 18.9#, L-80,HSM3	225	9.547	2164.79	209.889	168.77	84.75	225	Protector
240	TBG 4-1/2", 18.9#, L-80,HSM3	226	9.525	2174.32	200.364	169.26	85.16	226	Protector
241	TBG 4-1/2", 18.9#, L-80,HSM3	227	9.528	2183.84	190.836	169.75	85.56	227	Protector
242	TBG 4-1/2", 18.9#, L-80,HSM3	228	9.524	2193.37	181.312	170.24	85.96	228	Protector
243	TBG 4-1/2", 18.9#, L-80,HSM3	229	9.519	2202.89	171.793	170.73	86.36	229	Protector
244	TBG 4-1/2", 18.9#, L-80,HSM3	230	9.525	2212.41	162.268	171.22	86.77	230	Protector
245	TBG 4-1/2", 18.9#, L-80,HSM3	231	9.527	2221.94	152.741	171.70	87.17	231	Protector
246	TBG 4-1/2", 18.9#, L-80,HSM3	232	9.541	2231.48	143.200	172.19	87.57	232	Protector
247	TBG 4-1/2", 18.9#, L-80,HSM3	233	9.523	2241.00	133.677	172.68	87.97	233	Protector
248	TBG 4-1/2", 18.9#, L-80,HSM3	234	9.528	2250.53	124.149	173.17	88.38	234	Protector
249	TBG 4-1/2", 18.9#, L-80,HSM3	235	9.518	2260.05	114.631	173.66	88.78	235	Protector
250	TBG 4-1/2", 18.9#, L-80,HSM3	236	9.527	2269.58	105.104	174.15	89.18	236	Protector

251	TBG 4-1/2", 18.9#, L-80,HSM3	237	9.547	2279.12	95.557	174.64	89.58	237	Protector
252	TBG 4-1/2", 18.9#, L-80,HSM3	238	9.527	2288.65	86.030	175.13	89.98	238	Protector
253	TBG 4-1/2", 18.9#, L-80,HSM3	239	9.527	2298.18	76.503	175.62	90.39	239	Protector
254	TBG 4-1/2", 18.9#, L-80,HSM3	240	9.525	2307.70	66.978	176.11	90.79	240	Protector
Pup Jt 4 1/2",HSM3 ,18.9#, L-80, Type-1			1.624	2309.33	65.354	176.11	90.79		
4-1/2" Flow Coupling, 18.9#, 9CR1MO, HSM3, 4' ft, WEIQIXIN Co			1.115	2310.44	64.239	176.11	90.79		
4 1/2" TRSSV Tubing Retrievable Saftey Valve, 18.9# w/ 3.437" Seal bore, HSM3, 9CR1MO, 7.5K WP w/ AF Profile, Flapper Type, WEIQIXIN Co			1.783	2312.22	62.456	176.11	90.79		
4-1/2" Flow Coupling,18.9#, 9CR1MO, HSM3, 6' ft, WEIQIXIN Co			1.725	2313.95	60.731	176.11	90.79		
Pup Jt 4 1/2",HSM3 ,18.9#, L-80, Type-1			1.622	2315.57	59.109	176.11	90.79		
276	TBG 4-1/2", 18.9#, L-80,HSM3	241	9.531	2325.10	49.578	176.60	91.19	241	Protector
277	TBG 4-1/2", 18.9#, L-80,HSM3	242	9.474	2334.58	40.104	177.09	91.59	242	Protector
278	TBG 4-1/2", 18.9#, L-80,HSM3	243	9.528	2344.10	30.576	177.57	91.99	243	Protector
279	TBG 4-1/2", 18.9#, L-80,HSM3	244	9.523	2353.63	21.053	178.06	92.40	244	Protector
280	TBG 4-1/2", 18.9#, L-80,HSM3	245	9.515	2363.14	11.538	178.55	92.80	245	Protector
4-1/2" Fluted swage adapter D/P, 18.9# TPCQ-EX Pin on top X HSM3 Pin on down, 9CR1MO, WEIQIXIN Co	Fluted Swage	0	1.018	2364.16	10.520	178.60	92.84	0	
TBG HANGER MSP/Drilex, 7.5K, 11" X 4 1/2" ACME Box up X 4 1/2" TPCQ-EX Box Down L-80 18.9#, M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type "H" Two Way (Min Bore: 3.68")	TBG HGR	0	0.370	2364.53	10.150	178.62	92.86	0	

Table 9-4: AZNS-075-ST1 Completion Tally

9.6 Completion String Pressure Test

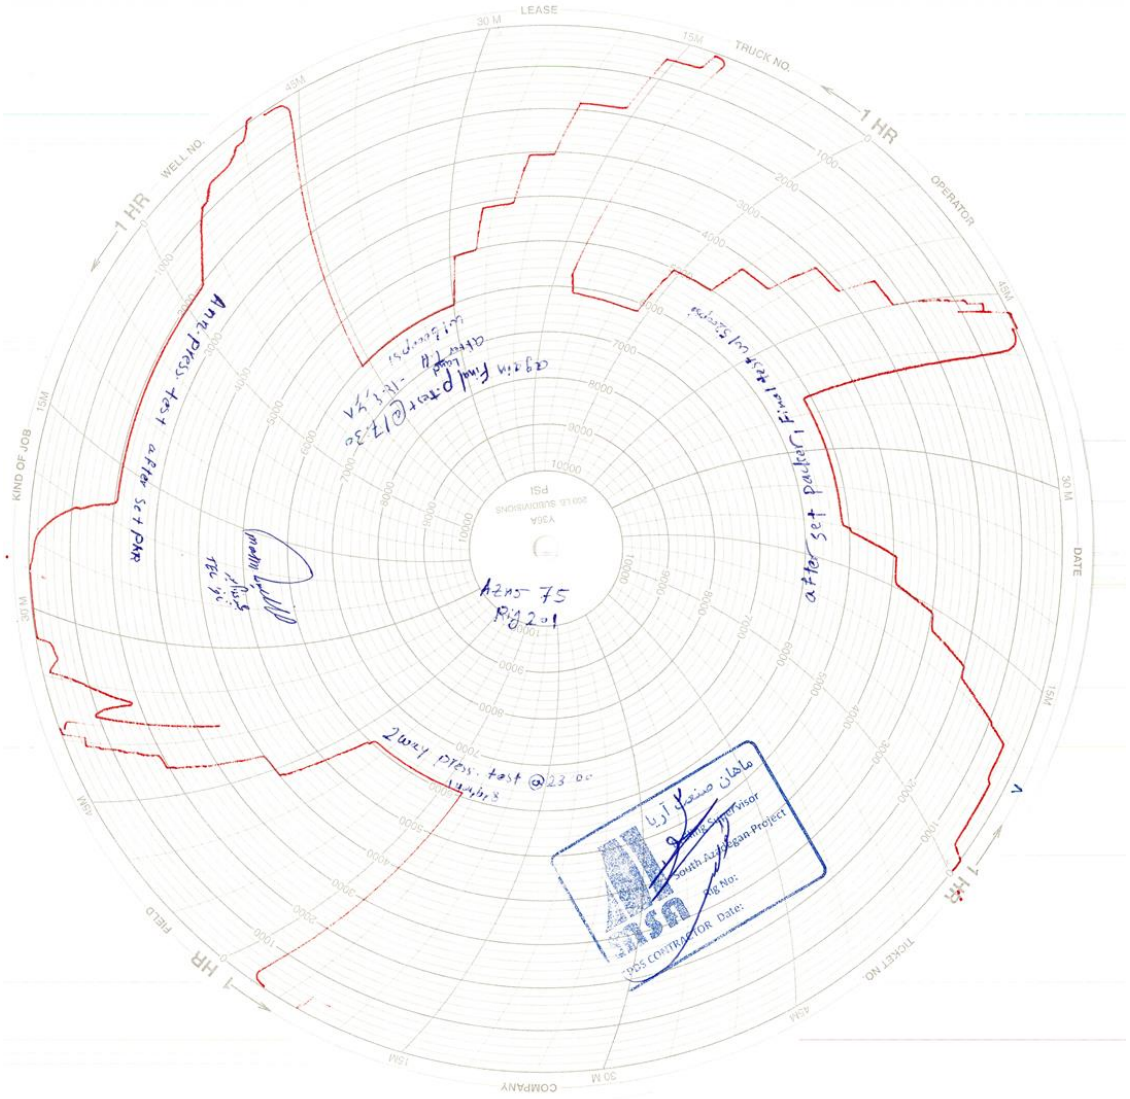


Figure 9-8: AZNS-075-ST1 Annulus Pressure Test, String Pressure Test after Packer Setting Graph

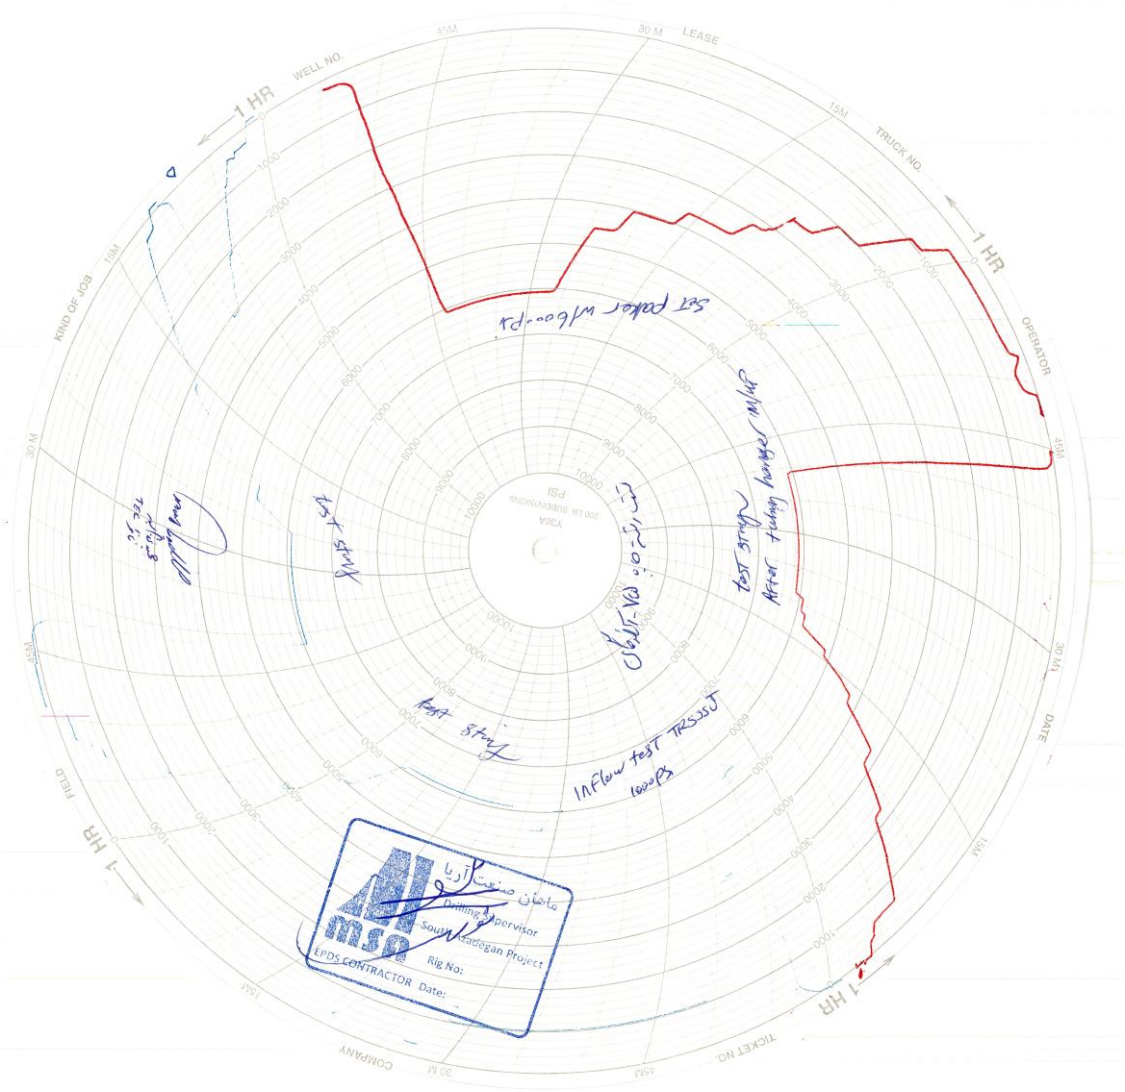


Figure 9-9: AZNS-075-ST1 Packer Setting, TRSSSV Inflow Test & String Pressure Test after M/H TBG HGR Graph

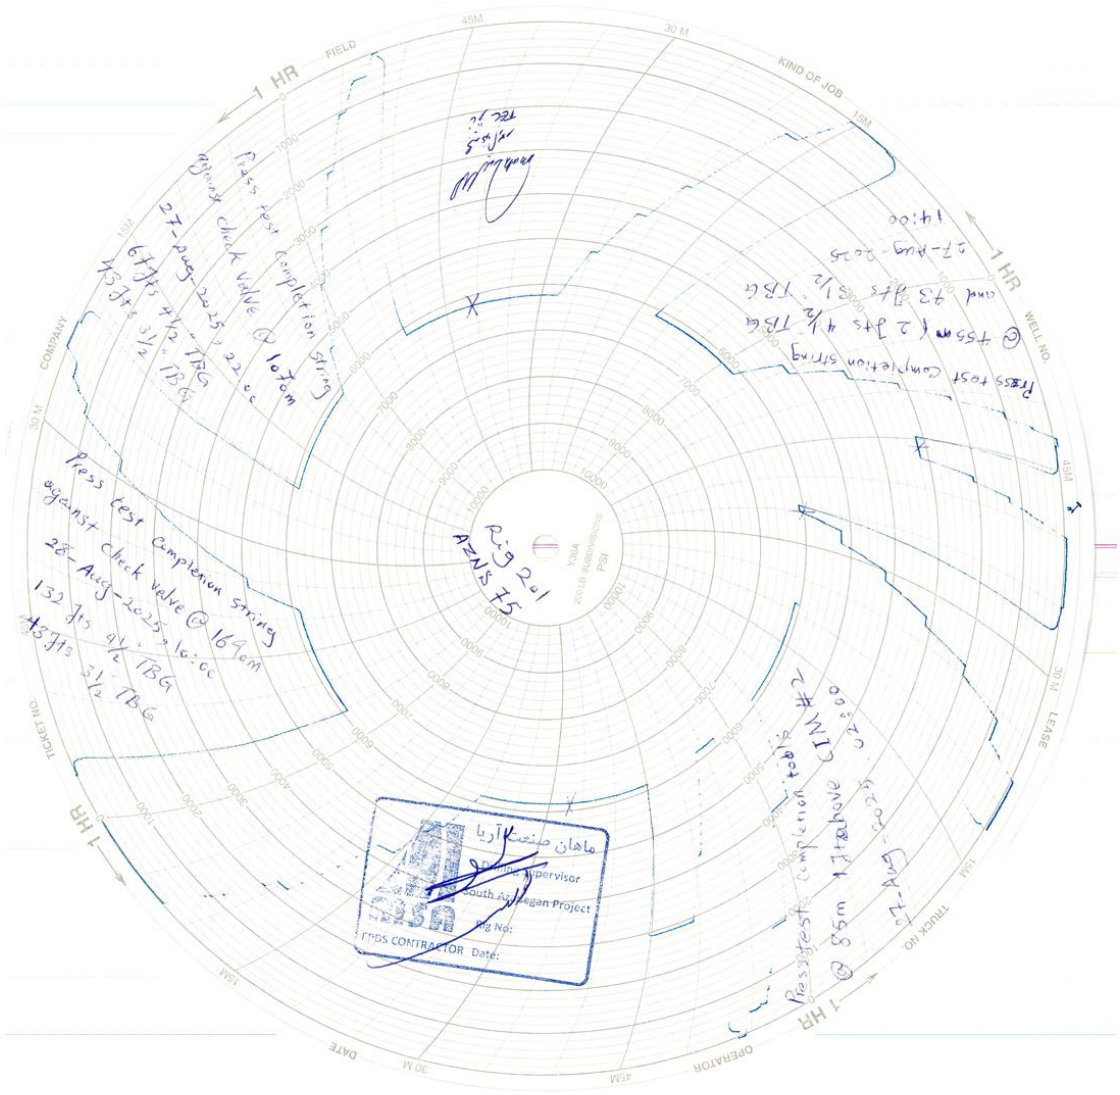


Figure 9-10: AZNS-075-ST1 Completion String Pressure Test

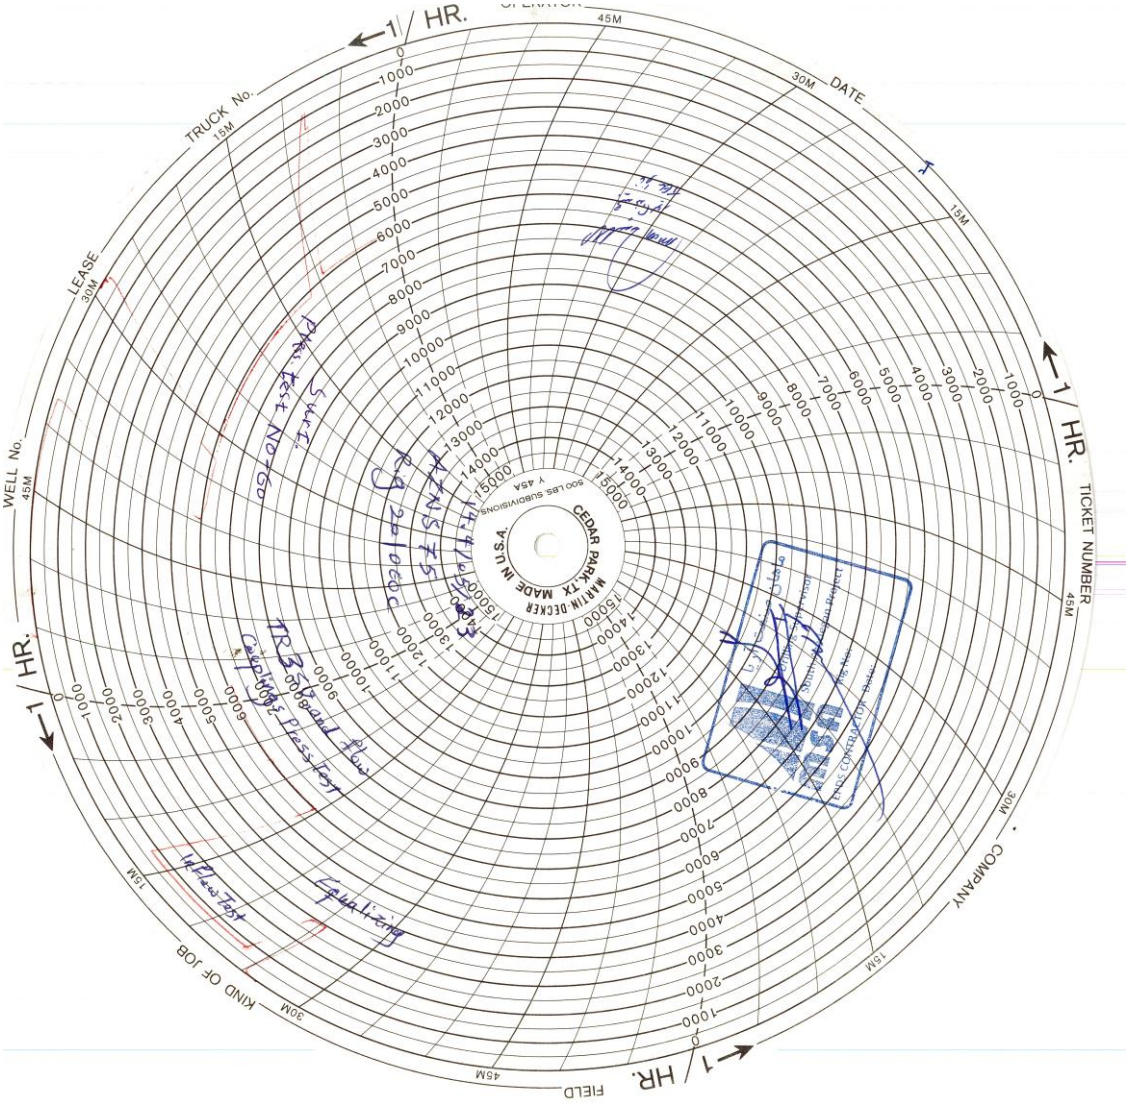


Figure 9-11: AZNS-075-ST1 Completion TRSSSV Pressure Test

10. Wellhead Report

10.1 Final Well Status

Well Head

Item	Specification (size, pressure rating, M/C)	Test Pressure	Test Duration
C.H.H (MSP Drillex)	20-3/4'' 3K, DD-0.5 PSL1, PR1	Already Installed	-
C.H.S (MSP Drillex)	20-3/4'' 3K * 13-5/8'' 5K , DD-0.5, PSL1, PR1	Already Installed	-
T.H.S (MSP Drillex)	13-5/8'' 5K * 11''-10K, FF-0.5, PSL3, PR2	Already Installed	15 MIN
MSP Drilex X-MASS TREE(BTM)	4-1/16''-10K, FF-0.5, PSL3G, PR2	6,000 psi	15 MIN

Wellbore Completion Fluids

Well bore	Fluid Type	Weight (pcf)
Cased Hole	$CaCl_2$	84

Well Head Pressure Recor

Annulus	Pressure (psi)	Date / Time
Wellhead	0	1404. 06. 08
Tubing- 9 5/8"	0	1404. 06. 08
9 5/8" – 13 3/8"	0	1404. 06. 08
13 3/8" – 20"	0	1404. 06. 08

Barriers

Barrier Type	Depth	Pressure Test	Date Tested
Close TRSSSV	62.456^{m}	1,000 psi (inflow test after finish flow the well)	1404. 06. 07

Temporary Installed Equipment:

Table 10-1: AZNS-075-ST1 Final Well Status

10.2 Wellhead & X-mass tree Specification

Well Type	Specification	Check and Remark
MSP Drilex Well Head 10,000 Psi for Fahliyan Wells	**TUBING HEAD ADAPTOR** BOTTOM STUDDED FLANGE 11", 10000 PSI, BX158 TOP STUDDED FLANGE 4-1/16" 10000 PSI BX155 FULL BORE PREPARED WITH TWO S-SEAL AND ONE METAL TO METAL SEAL TO PACK TOP NECK OF TUBING HANGER C/W RELATED TEST AND INJECTION PORTS PREPARTION. C/W TWO CONTINUOUS FEED THROUGH TYPE 1/4" NPT CONTROL LINE EXITS PREPARTION (ONE FOR 1/4" TRSSSV CL AND ONE FOR 1/4" DOWNHOLE PRESSURE GAUGE) AND TWO 3/8" NPT CONTINUOUS FEED THROUGH TYPE LINE PORTS FOR CHEMCIAL INJECTION LINE EXIT INCLUDING RELATED SWAGE LOCK FITTINGS C/WITH ONE 4-1/16", 10K WP FULL BORE MANUAL GATE VALVE FORGED BODY AND BONNET, ALLOY STAINLESS STEEL 410SS GATE & SEAT AISI 410 COATED WITH TUNGSTEN CARBIDE USING HVOF METHOD STEM: INCONEL 718 WITH BACK SEAT CAPABILITY, NON RISING STEM METAL TO METAL SEAL BETWEEN SEAT AND GATE C/W HAND WHEEL FORGED BODY ALLOY STEEL AISI 410 MAXIMUM HEIGHT: 800MM M/C:FF-0.5 T/C:U PSL:3G PR:2 CROSS T-TYPE SOLID BLOCK CROSS T-TYPE SOLID BLOCK, BOTTOM FLANGED 4-1/16" API 10000 PSI WP TOP FLANGED STUDDED 4-1/16" API 10000 PSI WP FOR TREE CAP WITH TWO STUDDED SIDE OUTLETS 4-1/16" 10000PSI WP ELEVATED AT 900 DEG AND TWO 4-1/16", 10000 PSI MANUAL GATE VALVE AT THE TOP AND BOTTOM AND ONE 4-1/16", 10000 PSI WP SAFETY VALVE EQUIPPED WITH HYDRAULIC WIRE CUT	

	ACTUATOR AS UPPER MASTER VALVE MATERIAL OF BODY,BONNET: AISI 410 SEAT, GATE: AISI 410SS HARD FACED WITH TUNGSTEN CARBIDE UASING HVOP METHOD MATERIAL OF STEM: INCONEL 718 M/C:FF-0.5 T/C:U PSL:3G PR:2G. MANUAL GATE VALVE API 4-1/16" 10000 PSI WP. FLANGED ENDS AND FULL BORE METAL TO METAL SEAL BETWEEN BODY/SEAT/GATE WITH BACK SEAT CAPABILITY, NON RISING STEM C/W HANDWHEELS MATERIAL OF BODY,BONNET,SEAT,GATE: AISI 410SS MATERIAL OF STEM: INCONEL 718 GATE&SEAT HARD FACED WITH TUNGSTEN CARBIDE BY HOVF METHOD M/C:FF-0.5 T/C:U PSL:3G PR:2 X-MAS TREE CAP 4-1/16" API 10000 PSI WP, FLANGED BOTTOM (4-1/16", BORE) 8-3/8"-4ACME-2G THREAD TOP, BLANKING PLUG TAPPED WITH 1/2" NPT THREAD, FORGED BODY, MATERIAL: STAINLESS STEEL 410 M/C:FF-0.5 T/C:U PSL:3G PR:2	

Table 10-2: AZNS-075-ST1 Wellhead Equipment Specification

10.3 Wellhead Schematic

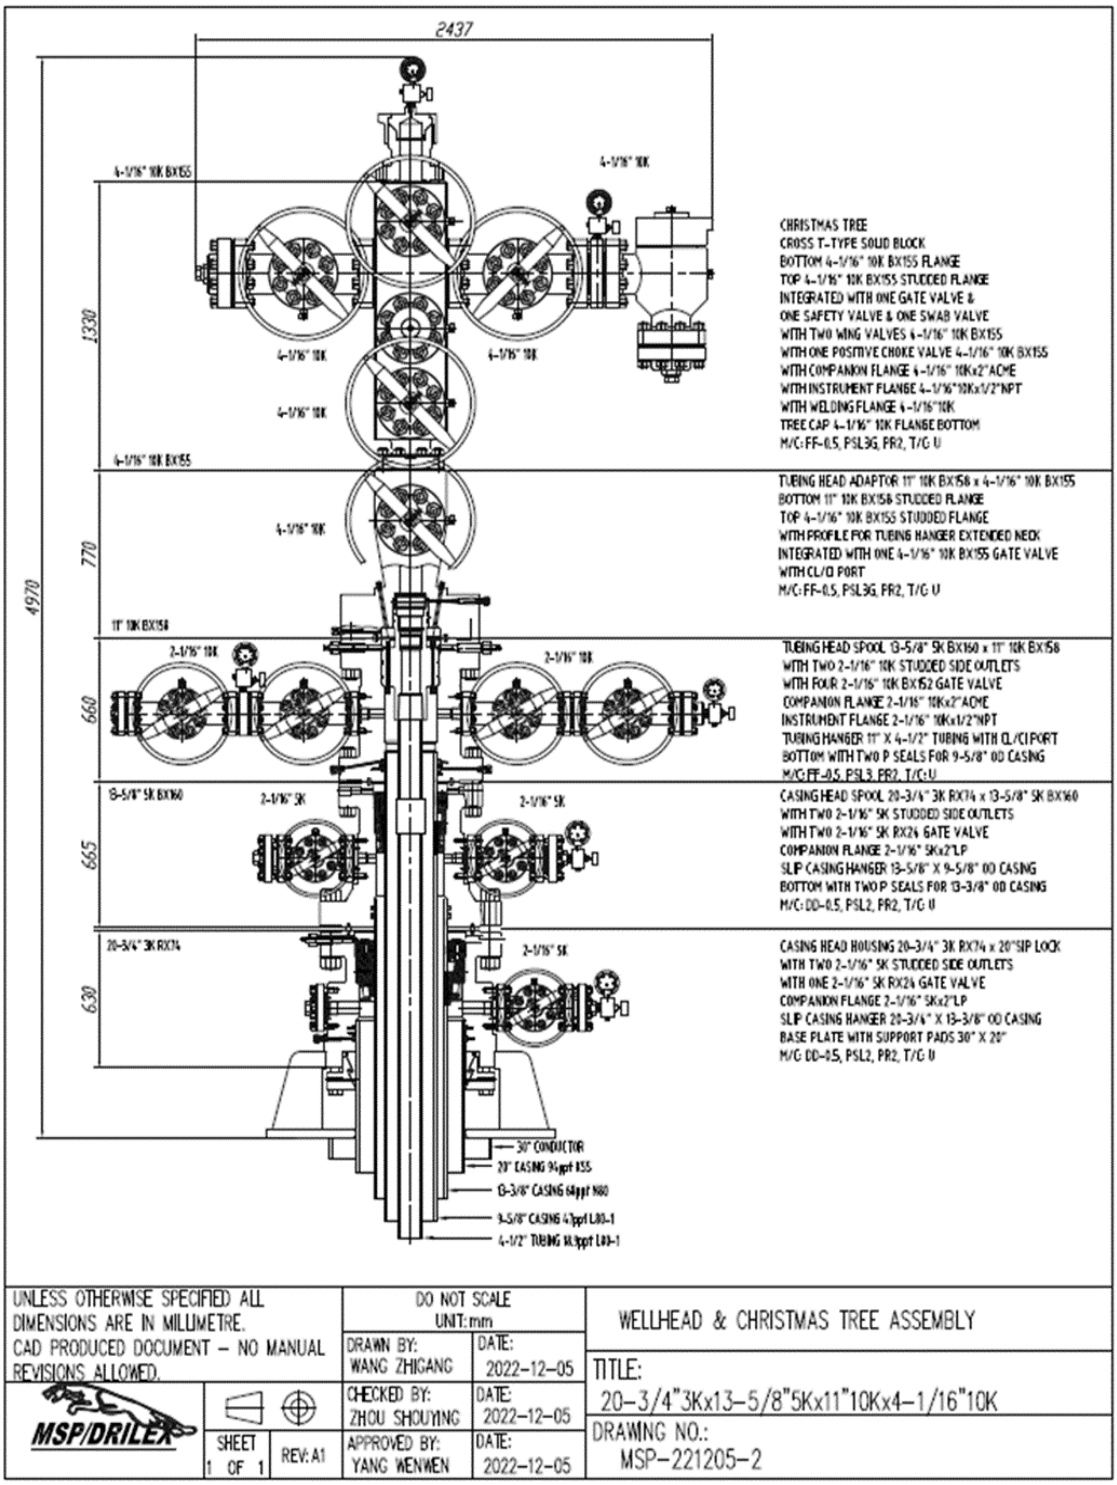


Figure 10-1: AZNS-075-ST1 Wellhead Sketch

10.4 X-mass Tree Specification (Section D)

Item	Equipment	M/C	T/C	PSL	Qty
1	BTM Master Valve 11” * 4 1/16” 10K	FF-0.5	U	3G	1
2	TOP Master Valve 4 1/16” 10K	FF-0.5	U	3G	1
3	Surface Safety Valve 4 1/16” 10K	FF-0.5	U	3G	1
4	Deeping Valve 4 1/16” 10K	FF-0.5	U	3G	1
5	Wing gate valve-1 (Kill Valve) 4 1/16" 10K	FF-0.5	U	3G	1
6	Wing gate valve-2 (production valve) 10K	FF-0.5	U	3G	1
7	41/16" Choke valve 4 1/16" 10K	FF-0.5	U	3G	1
8	Christ Mas Tree	FF-0.5	U	3G	1

Table 10-3: AZNS-075-ST1 Section "D" Specification

10.5 X-mass Tree Pressure Test Report (Section D – befor install)

Item	Test	Check Mark and Result
1	Pressure test for the kill Valve W/ 1,000 & 8,000 Psi / 15 min	OK
2	Pressure test for the SSV W/ 1,000 & 8,000 Psi / 15 min	OK
3	Pressure test for the top master valve W/ 1,000 & 8,000 Psi / 15 min	OK
4	Pressure test for Swab valve W/ 1,000 & 8,000 Psi / 15 min	OK
5	Pressure test for the Production valve W/ 1,000 & 8,000 Psi / 15 min	OK

Table 10-4: AZNS-075-ST1 Section "D" Test Report Befor Installation

10.6 X-mass Tree Pressure Test Report (Section D – after install)

Item	Test	Check mark and Result
1	Pressure test X-MAS TREE solid block and bottom section W/1,000 & 6,000 psi for 15min	OK
2	Pressure test for the SSV Exit block W/ 6,000 psi / 15 min	OK
3	Pressure test neck of tubing hanger metal seal W/1,000 & 6,000 psi for 15min	OK
4	Pressure test for Swab valve W/ 6,000 psi / 15 min	OK
5	Pressure test for Production valve W/6,000 psi / 15 min	OK
6	Pressure test cavity of FS.seal and Ring Gasket W 6,000 psi / 15 min	OK

Table 10-5: AZNS-075-ST1 Section "D" Test Report After Installation

10.7 Wellhead Related Test Reports

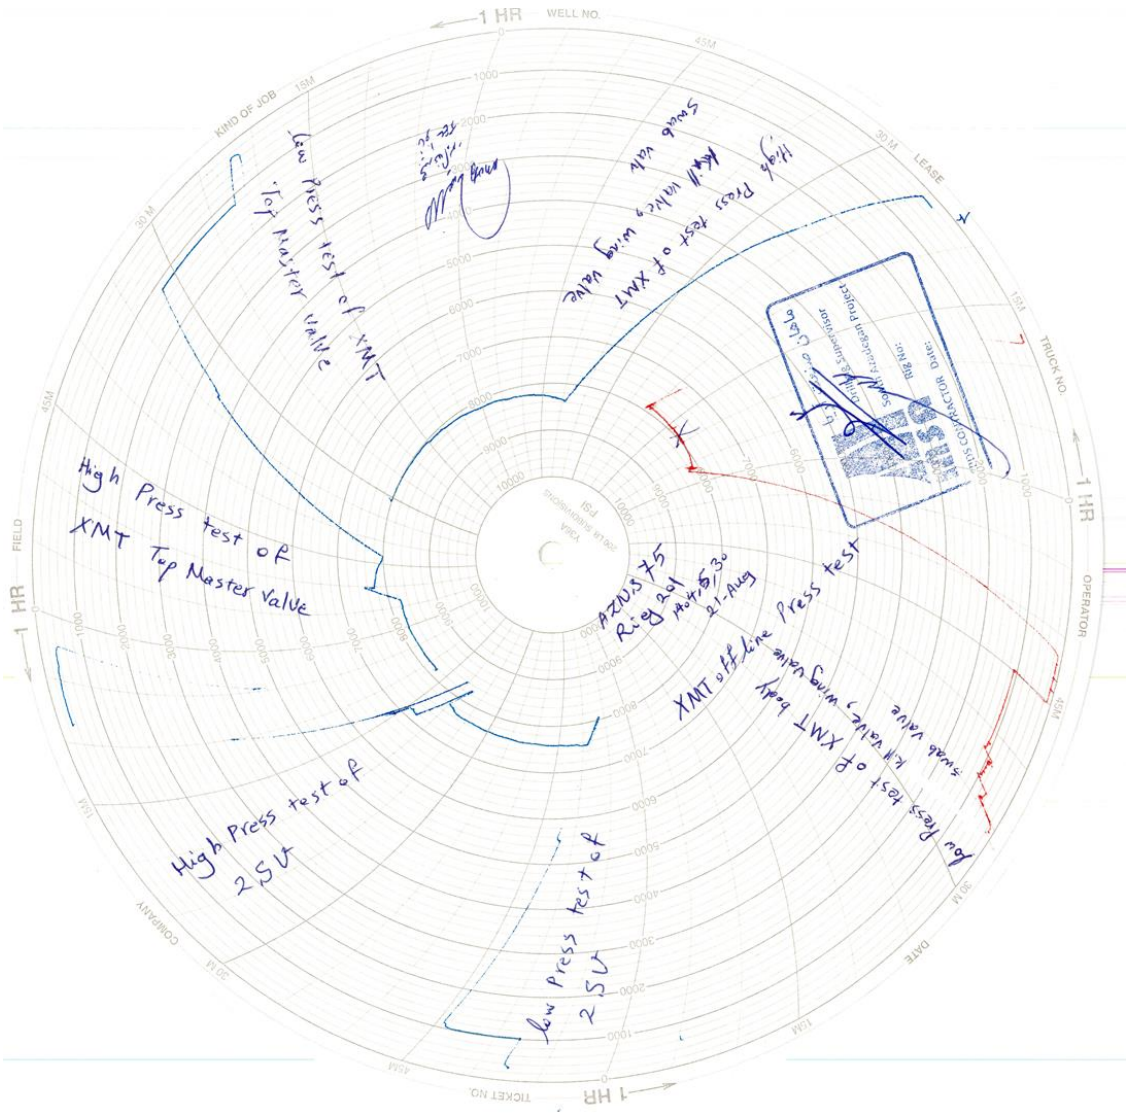


Figure 10-2: AZNS-075-ST1 X-Mass Tree Body Pressure Test Graph Before Installation

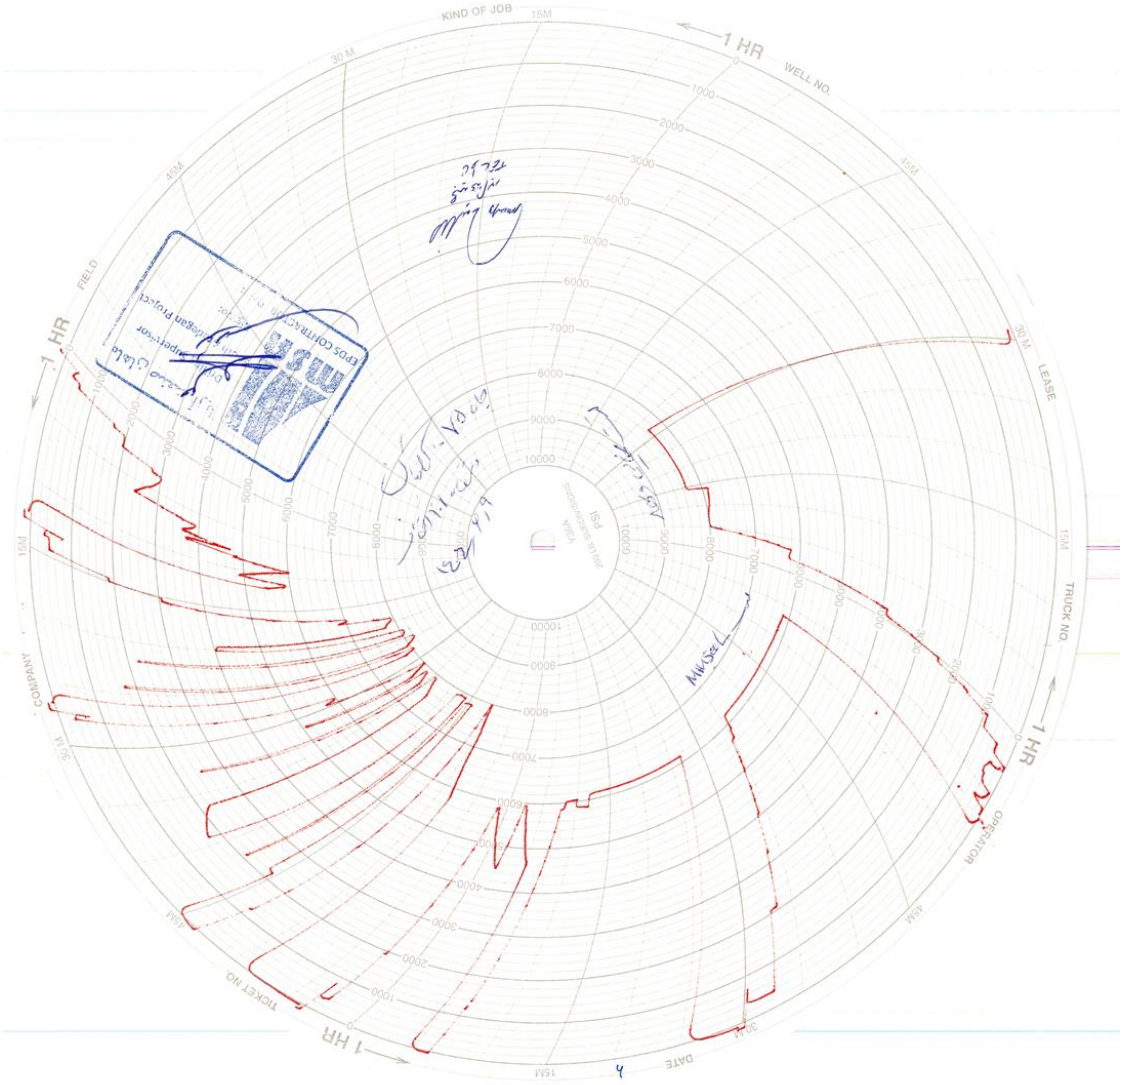


Figure 10-3: AZNS-075-ST1 X-Mass Tree Body Pressure Test Graph After Installation

تاریخ: ۱۴۰۴/۰۶/۰۳
پیوست: دارد

بسمه تعالی

موضوع: صورتجلسه تست سطحی تاج چاه ۷۵ آزادگان جنوبی، قبل از نصب در دکل ۲۰۱ عملیات اکتشاف نفت

بدینوسیله در مورخه 1404/06/03 تست‌های سطحی تاج چاه "X-Mass Tree Solid Block "T" Type 4 – 1/16 10k, MSP DRILEX مرتبط به چاه شماره 75 آزادگان جنوبی با حضور نماینده محترم کارفرما (پتروپارس) در محل دستگاه 201 عملیات اکتشاف نفت، قبل از نصب بر روی تاج چاه به شرح ذیل انجام پذیرفت:

- Body Pressure Test of X – Mass Tree Solid Block w/ 1000psi, 5min & 8000psi, 15min "OK" S/N: CT2302A A/0 XC230003
- Inflow Pressure Test of 4 – 1/16" Production (WING) Valve w/ 1000psi, 5min & 8000psi, 15min "OK". S/N: 002929B X30230008
- Inflow Pressure Test of 4 – 1/16" Dipping (SWAB) Valve w/ 1000psi, 5min & 8000psi, 15min "OK". S/N: 008929K XC230003
- Inflow Pressure Test of 4 – 1/16" Kill Valve w/ 1000psi, 5min & 8000psi, 15min "OK" S/N: 002929B XC230007
- Inflow Pressure Test of 4 – 1/16" Surface Safety Valve w/ 1000psi, 5min & 8000psi, 15min "OK". S/N: 096041-SY SF230001 6269167C XC230001
- Inflow & Out Flow Pressure Test of 4 – 1/16" Top Master Valve w/ 1000psi, 5min & 8000psi, 15min "OK". S/N: 0089291 XC230003
- Pressure Test of 2SV Actuator w/ 2500psi, 15min "OK".

– گراف مربوط به تست فشار پیوست صورتجلسه گردید.

نماینده محترم تکمیل چاه کارفرما
شرکت مشاوران انرژی تهران

ناظر عملیات حفاری
شرکت ماهان صنعت آریا

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No: 201 OEOC
EPDS CONTRACTOR Date:

Figure 10-4: AZNS-075-ST1 Wellhead MOM Befor Installation



تاریخ:۱۴۰۴/۰۶/۰۸
پیوست: دارد

بسمه تعالی

موضوع: صورتجلسه تست‌های پس از نصب تاج و ولهد چاه ۷۵ ازادگان جنوبی بعد از نصب در دکل ۲۰۱ عملیات اکتشاف نفت

بدینوسیله در مورخه 1404/06/08 تست‌های تاج چاه X-Mass Tree Solid Block "T" Type 4 – 1/16" 10k, MSP DRILEX و ولهد چاه شماره 75 ازادگان جنوبی با حضور نماینده محترم تکمیل چاه کارفرما و نماینده عملیات حفاری ماهان صنعت آریا در محل دستگاه حفاری ۲۰۱ عملیات اکتشاف نفت بعد از نصب بر روی چاه به شرح ذیل انجام پذیرفت:

- Body Pressure Test of X – Mass Tree Solid Block w/ 10k 11" * 4 – 1/16" 10k Tubing Head Adaptor (BTM MASTER VALVE) 10k MSP/DRILEX w/ 8000psi for 15min, "OK". S/N: 0089291 X30230002
- Pressure Test TBG HGR Metal Seal to 500psi for 5min, 6000psi for 15min, "OK".
- Pressure Test F–Seal & Ring Gasket between T.H.S & Tubing Head Adaptor (BTM MASTER VALVE) to 6000psi for 15min, "OK".
- Pressure Test Neck of TBG HGR F-Seal to 6000psi for 15min, "OK".
- Pressure Test 1/4" Control Line (CL) to 6000psi for 15min, "OK".
- Pressure Test 3/8" Control Injection Lines (CIL) to 2000psi "OK".

- فشار تمامی دالیزها بررسی گردید که فشار آنها صفر بود.
- خروجی کنترل لاین شیر ایمنی درون چاهی در جهت شیر اصلی پایینی می‌باشد و همچنین CIV شماره یک در جهت ویست پیت و CIV شماره دو در خلاف جهت ویست پیت می‌باشد و همچنین بر روی دو CIV و کنترل لاین بلاک کپ نصب گردید.
- گراف مربوط به تست فشار پیوست صورتجلسه گردید.

نماینده محترم تکمیل چاه کارفرما
شرکت مشاوران انرژی تهران

ناظر عملیات حفاری
شرکت ماهان صنعت آریا

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No: 201 OEOC
EPDS CONTRACTOR Date:

Figure 10-5: AZNS-075-ST1 Wellhead MOM After Installation

11. Drilling Fluid Information

11.1 Summary

Holw Size (in)	CSG Size (in)	CSG Depth (m)	Drilling Fluid Sys.	Mud Properties
26	20	151.1	Already installed	
17 – 1/2	13 – 3/8	1155.5	Already installed	
12 – 1/4	9 – 5/8	2477.5	Already installed	
8 – 1/2	7	2034 – 3692	KCl Poly Mud	76 pcf
6 – 1/8	5	3593.5 – 3888	KCl Poly Mud	78 – 87 pcf
	Completion Section		$CaCl_2$	84 pcf

Table 11-1: AZNS-075-ST1 Summary of Fluid

11.2 Interval Remark

11.2.1 WorkOver & 8 3/8” Hole Section

- RIH with 6 1/8" D/O BHA to 2171 m, start D/O P.O.B to 2730 m, RIH to 3607 with wash down & ream down, D/O CMT & LDC to 3672 m, POOH to surface.
- RIH with tandem scraper & performed scraper job.
- Performed logging job.
- RIH with 6 1/8" Tri-Cone bit to 3672 m, Resumed D/O CMT to 3692 m, Increased MW from 76 PCF to 78PCF then POOH to surface.
- RIH with D.D BHA to bottom and commenced drilling 6 1/8" hole section as slid & rotary mode to 3888 m, then performed condition trip & work on that while increased MW to 83PCF step by step, POOH to surface.
- Change BHA & RIH, Performed condition trip whit 84 PCF.
- Performed logging job.
- Performed CMT plug job @ 3299 m & 2167 m.
- RIH with 8 3/8" Tri-Cone bit to 2013, start D/O CMT to 2167.5 m (L. Liner) and POOH to surface.
- RIH with 6 1/8" B. BIT to 3170 m, D/O CMT to 3300 m, RIH to 3888 m while OBS, tight hole condition @3750-3888 m, POOH pump out to 3689 m, RIH back to 3791 m with wash down & ream down, try to pass the same point with "NO SUCC", work on tight hole condition several time while stuck & bottom, POOH to surface.
- Performed logging job.
- RIH with 6 1/8" condition BHA to bottom with wash down & ream Down, POOH to surface.
- Performed logging job.
- RIH with 6 1/8" condition BHA to bottom with wash down & ream Down, POOH to surface.
- Performed logging job.
- RIH with 6 1/8" condition BHA to bottom with wash down & ream Down, POOH to surface.
- Run 5” liner and performed CMT Job as per program successfully.
- RIH with 6 1/8" BHA to 3596 m (L. Liner) and POOH to surface.
- RIH with 4 1/8" M.M Junk Mill to 3601.4 m (P.O.B), D/O P.O.B and RIH to 3864.5, try to D/O P.D.P, L.W.P and L.D.C with "NO SUCC", POOH to surface.

- RIH with 3 3/4" M.M.J. Mill to 3864.5, D/O LDC & CMT to 3876.7 F. Coller debt and POOH to surface.
- Performed logging job.
- Performed scraper & polish mill job.
- RIH with SN Packer and set it before 7" L. Liner (2165 m).
- Performed scraper & polish mill job.
- Performed dry test.
- RIH with 5 " tie back packer assy and set @ 3596 m.
- Performed dry test several time.
- Performed 7 5/16 polish mill job.
- Run 7” tie back assy and performed CMT Job as per program successfully.
- RIH with 8 3/8" D/O BHA to 2007 m, D/O CMT to 2034.5 m, new 7" L. Liner, POOH to surface.
- RIH with 5 7/8" D/O BHA to 2035 m, D/O CMT to 2038.28 m then RIH with wash down to 3593 m and POOH to surface.
- RIH with 3 3/4" clean out BHA to 3876 m then POOH to surface.
- Performed logging job.
- Performed scraper trip.
- Performed dry test.
- RIH with 3 3/4" M.M.J. Mill to 3876 m, spot 26 bbls 84 PCF brine and POOH to surface.
- Performed perforation job.
- RIH with 3 3/4" M.M.J. Mill to 3876 m, spot 20 bbls 84 PCF brine and POOH to surface.

11.2.1.1 Drilling Fluid type

FLUID PROPERTIES RECAP					
		Drilling start	Range		Drilling End
MW (min)	pcf	76	76	76.0	76.0
Funnel Viscosity	sec/qt	38	38	52	45
PV	cps	11	9	15	15
YP	lb/100sq.ft	9	9	14	12
API Fluid loss	cc	4	2	4	2
pH		9.2	9	9.6	9.1
Solid	%	14	14	14	14
KCL	%	0	3	5.5	5.5
Cl (NaCl)	mg/L	148,000	145,000	165,000	165,000
Total Hardness	mg/L	2,340	2,040	2,340	2,120
Ca Hardness	mg/L	2,100	1,880	2,100	1,880

Table 11-2: AZNS-075-ST1 Fluid Properties Recap Table

11.2.1.2 Material Consumption Analysis

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Caustic Soda	47	55	2,585	lbs	0.32	ppb
Limestone	158	2,200	347,600	lbs	42.52	ppb
Caco3 LCM	17.8	2,200	39,160	lbs	4.79	ppb
Bentonite	1	2,200	2,200	lbs	0.00	ppb
Citric acid	31	55	1,705	lbs	0.21	ppb
KCL	54	2,200	118,800	lbs	14.53	ppb
Starch LV	1,549	55	85,195	lbs	10.42	ppb
Sodium Bicarb	29	55	1,595	lbs	0.20	ppb
Xantan gum	124	55	6,820	lbs	0.83	ppb
Salt (NACL)	226	2,200	497,200	lbs	60.82	ppb
Soda Ash	74	55	4,070	lbs	0.50	ppb
Lime	345	55	18,975	lbs	2.32	ppb

Initial Volume	0.0	bbl
Total Volume Built	8,175.6	bbl
Volume received	758.0	bbl
Left In Hole	198.0	bbl
Total Volume Consumed	7,225	bbl
Volume Transfer to Next Section	1,510.6	bbl
Meter Drilled	1,430.0	m

Table 11-3: AZNS-075-ST1 Material Consumption Analysis Table

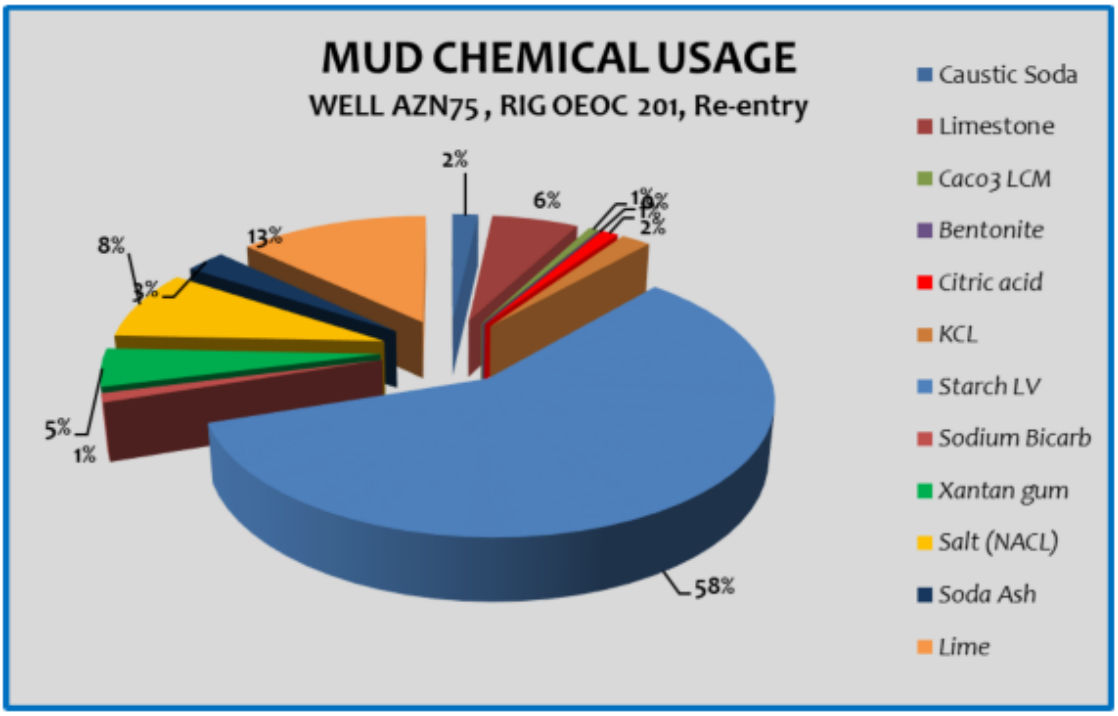


Figure 11-1: AZNS-075-ST1 Mud Chemical Usage

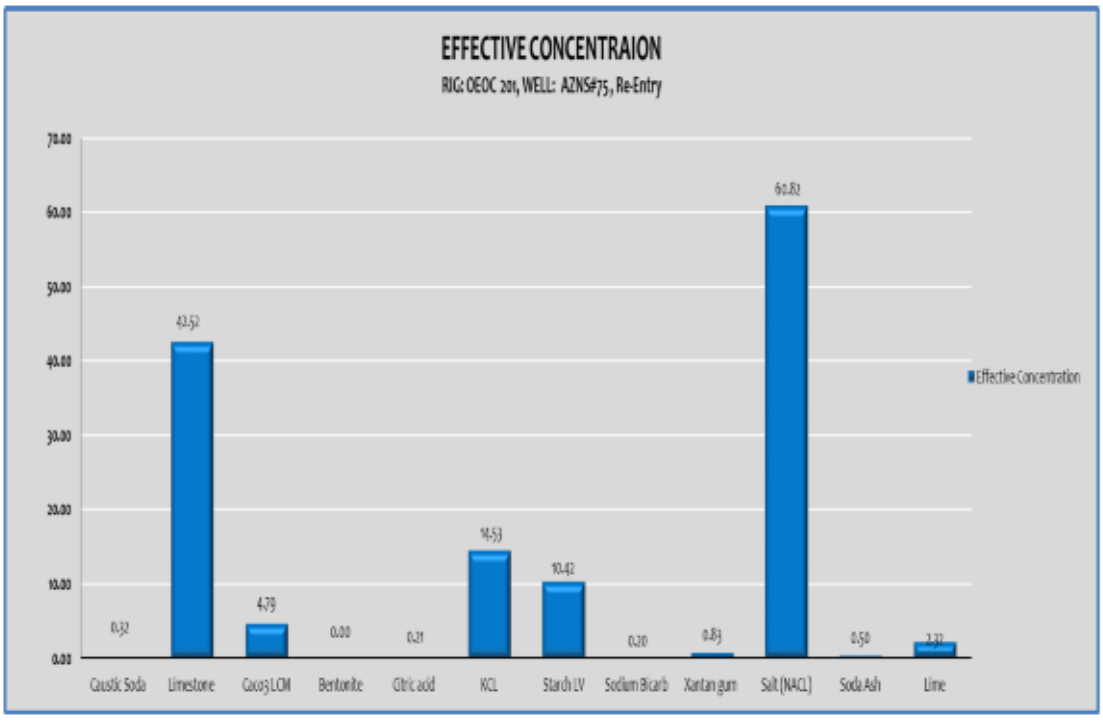


Figure 11-2: AZNS-075-ST1 Effective Concentration

11.2.1.3 Volume Analysis

RIG: OEOC 201, WELL: AZNS#75 , Re-Entry VOLUME ANALYSIS		
Initial Volume	bbls	0.0
Received Volume	bbls	758.0
Left In Hole	bbls	198.0
Volume Built	bbls	8,175.6
Surface Losses/Dumped	bbls	4,221.0
Formation Losses	bbls	3,004.0
Total Losses	bbls	7,225.0
Volume Transfer Out	bbls	1,511

Table 11-4: AZNS-075-ST1 Volume Analysis Table

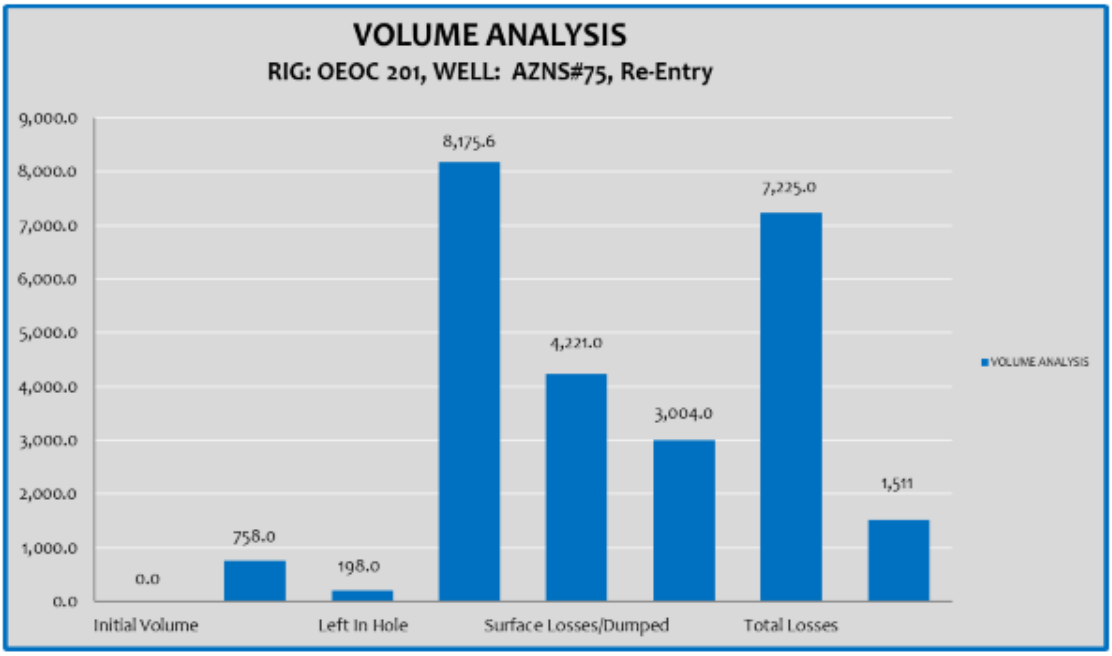


Figure 11-3: AZNS-075-ST1 Volume Analysis Chart

11.2.1.4 Daily volume Breakdown

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
20-Mar-25	1	845.2	0	0
21-Mar-25	2	0.0	0	0
22-Mar-25	3	190.6	720	0
23-Mar-25	4	255.4	0	0
24-Mar-25	5	0.0	0	0
25-Mar-25	6	0.0	0	0
26-Mar-25	7	0.0	0	0
27-Mar-25	8	133.8	7	0
28-Mar-25	9	0.1	0	0
29-Mar-25	10	0.0	18	0
30-Mar-25	11	0.0	33	0
31-Mar-25	12	0.0	0	0
1-Apr-25	13	0.1	15	0
2-Apr-25	14	143.6	35	0
3-Apr-25	15	0.2	40	0
4-Apr-25	16	120.7	78	0
5-Apr-25	17	0.0	0	0
6-Apr-25	18	65.0	10	0
7-Apr-25	19	0.0	0	0
8-Apr-25	20	70.0	8	0
9-Apr-25	21	0.0	10	0
10-Apr-25	22	22.3	32	0
11-Apr-25	23	2.1	47	0
12-Apr-25	24	2.2	66	0
13-Apr-25	25	0.0	15	0
14-Apr-25	26	0.4	0	0
15-Apr-25	27	9.4	60	0
16-Apr-25	28	313.2	10	0
17-Apr-25	29	197.4	113	0
18-Apr-25	30	0.0	0	0
19-Apr-25	31	41.0	60	0
20-Apr-25	32	118.9	15	0

21-Apr-25	33	0.3	24	0
22-Apr-25	34	56.1	107	0
23-Apr-25	35	13.7	94	0
24-Apr-25	36	110.5	46	48
25-Apr-25	37	122.5	30	49
26-Apr-25	38	0.7	36	72
27-Apr-25	39	153.1	177	135
28-Apr-25	40	338.9	104	138
29-Apr-25	41	179.1	15	114
30-Apr-25	42	177.0	79	130
1-May-25	43	176.8	79	140
2-May-25	44	175.1	62	138
3-May-25	45	178.6	96	134
4-May-25	46	337.5	163	125
5-May-25	47	176.5	3	94
6-May-25	48	1.8	16	70
7-May-25	49	172.1	62	62
8-May-25	50	171.5	161	46
9-May-25	51	0.1	65	45
10-May-25	52	320.6	90	91
11-May-25	53	173.6	38	76
12-May-25	54	290.7	64	88
13-May-25	55	320.1	95	89
14-May-25	56	151.4	97	87
15-May-25	57	1.4	129	87
16-May-25	58	467.0	25	110
17-May-25	59	0.3	110	92
18-May-25	60	335.9	84	96
19-May-25	61	170.5	82	96
20-May-25	62	151.5	124	96
21-May-25	63	300.5	97	88
22-May-25	64	0.0	0	96
23-May-25	65	153.0	79	92
24-May-25	66	169.6	157	89
25-May-25	67	0.0	50	91
26-May-25	68	96.0	0	0
27-May-25	69	0.0	79	0
28-May-25	70	0.0	10	0
29-May-25	71	0.0	0	0
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		8,176	4,221	3,004

Table 11-5: AZNS-075-ST1 Daily Volume Break Down Table

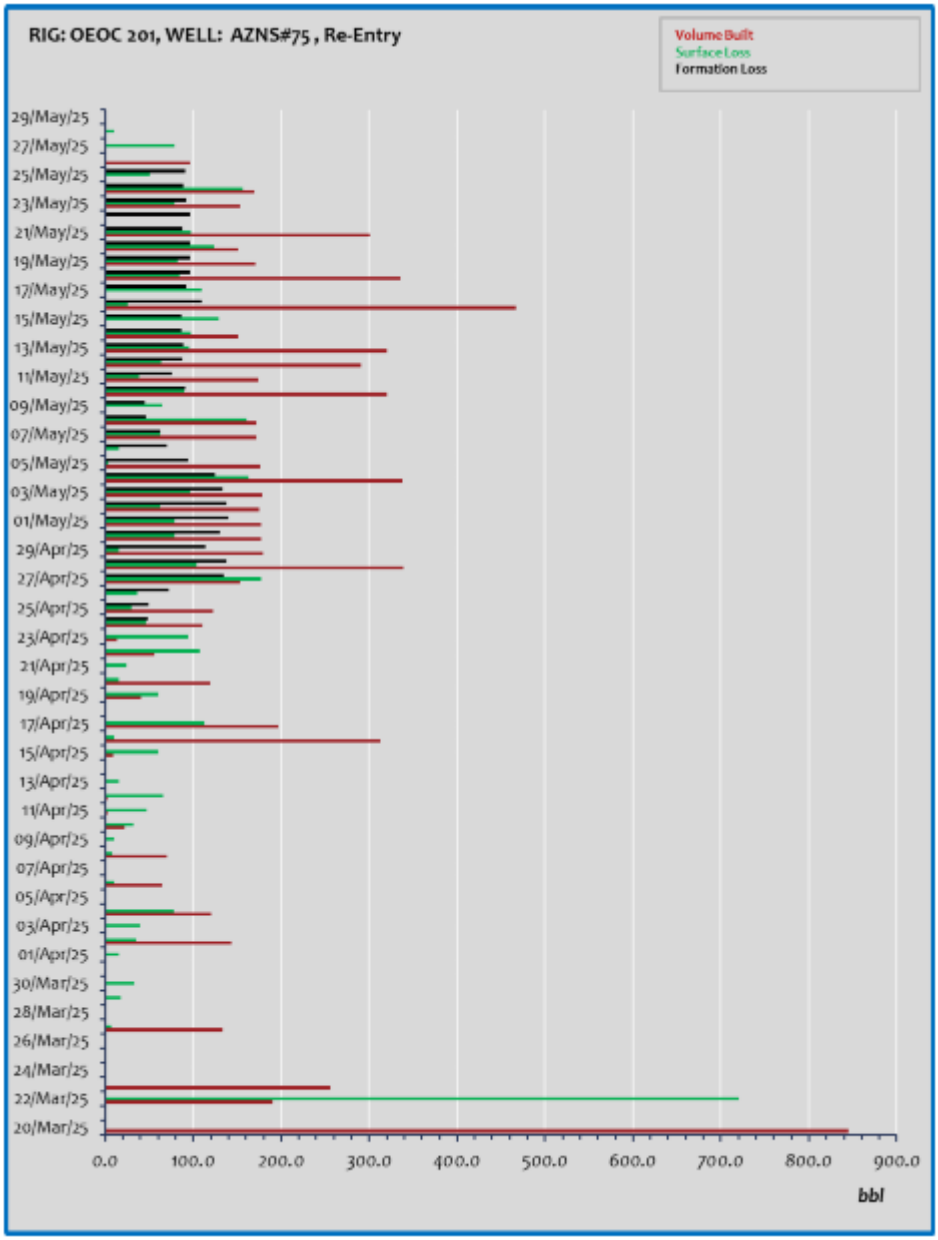


Figure 11-4: AZNS-075-ST1 Daily Volume Break Down Chart

11.2.1.5 Loss Distribution

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
20-Mar-25	1	845.2	0	0	0	0	0	0	0	0	0
21-Mar-25	2	0.0	0	0	0	0	0	0	0	0	0
22-Mar-25	3	190.6	685	0	0	0	0	0	0	0	35
23-Mar-25	4	255.4	0	0	0	0	0	0	0	0	0
24-Mar-25	5	0.0	0	0	0	0	0	0	0	0	0
25-Mar-25	6	0.0	0	0	0	0	0	0	0	0	0
26-Mar-25	7	0.0	0	0	0	0	0	0	0	0	0
27-Mar-25	8	133.8	0	0	0	0	7	0	0	0	0
28-Mar-25	9	0.1	0	0	0	0	0	0	0	0	0
29-Mar-25	10	0.0	0	0	0	0	8	0	0	0	10
30-Mar-25	11	0.0	0	0	0	0	23	0	10	0	0
31-Mar-25	12	0.0	0	0	0	0	0	0	0	0	0
1-Apr-25	13	0.1	0	0	0	0	0	0	0	0	15
2-Apr-25	14	143.6	0	0	0	0	0	0	0	0	35
3-Apr-25	15	0.2	0	15	0	0	0	0	0	0	25
4-Apr-25	16	120.7	0	25	0	0	13	0	0	0	40
5-Apr-25	17	0.0	0	0	0	0	0	0	0	0	0
6-Apr-25	18	65.0	0	0	0	0	10	0	0	0	0
7-Apr-25	19	0.0	0	0	0	0	0	0	0	0	0
8-Apr-25	20	70.0	0	0	0	0	8	0	0	0	0
9-Apr-25	21	0.0	0	0	0	0	10	0	0	0	0
10-Apr-25	22	22.3	18	0	0	0	14	0	0	0	0
11-Apr-25	23	2.1	0	42	0	0	0	0	0	0	5
12-Apr-25	24	2.2	0	40	0	0	11	0	0	0	15
13-Apr-25	25	0.0	0	0	0	0	15	0	0	0	0
14-Apr-25	26	0.4	0	0	0	0	0	0	0	0	0
15-Apr-25	27	9.4	0	25	0	0	0	0	0	0	35
16-Apr-25	28	313.2	0	0	0	0	10	0	0	0	0
17-Apr-25	29	197.4	0	0	0	0	13	0	0	0	100
18-Apr-25	30	0.0	0	0	0	0	0	0	0	0	0
19-Apr-25	31	41.0	0	0	0	0	60	0	0	0	0
20-Apr-25	32	118.9	0	0	0	0	0	0	0	0	15

21-Apr-25	33	0.3	0	0	0	0	24	0	0	0	0
22-Apr-25	34	50.1	0	43	0	0	0	0	0	0	64
23-Apr-25	35	13.7	0	15	0	0	0	0	40	0	39
24-Apr-25	36	110.5	0	31	0	5	0	0	0	48	10
25-Apr-25	37	122.5	0	0	0	22	0	0	0	49	8
26-Apr-25	38	0.7	0	13	3	20	0	0	0	72	0
27-Apr-25	39	153.1	0	18	4	13	77	0	0	135	65
28-Apr-25	40	338.9	0	5	4	0	0	0	0	138	95
29-Apr-25	41	179.1	0	12	3	0	0	0	0	114	0
30-Apr-25	42	177.0	0	24	4	6	0	0	0	130	45
1-May-25	43	176.8	0	24	3	12	0	0	0	140	40
2-May-25	44	175.1	0	24	3	15	0	0	0	138	20
3-May-25	45	178.6	0	28	3	20	0	0	0	134	45
4-May-25	46	337.5	0	16	4	8	80	0	0	125	55
5-May-25	47	176.5	0	0	3	0	0	0	0	94	0
6-May-25	48	1.8	0	12	4	0	0	0	0	70	0
7-May-25	49	172.1	0	10	3	4	0	0	0	62	45
8-May-25	50	171.5	0	20	3	8	85	0	0	40	45
9-May-25	51	0.1	0	0	4	0	38	0	0	45	23
10-May-25	52	320.6	0	28	3	14	0	0	0	91	45
11-May-25	53	173.6	0	20	0	8	0	0	0	70	10
12-May-25	54	290.7	0	24	0	8	0	0	0	88	32
13-May-25	55	320.1	0	27	0	20	0	0	0	89	48
14-May-25	56	151.4	30	28	0	18	0	0	6	87	15
15-May-25	57	1.4	0	16	0	12	79	0	22	87	0
16-May-25	58	407.0	0	25	0	0	0	0	0	110	0
17-May-25	59	0.3	0	20	0	32	0	0	0	92	52
18-May-25	60	335.9	0	32	0	22	0	0	0	96	30
19-May-25	61	170.5	0	34	0	18	0	0	0	90	30
20-May-25	62	151.5	0	28	0	48	0	0	0	96	48
21-May-25	63	300.5	0	23	0	18	28	0	0	88	28
22-May-25	64	0.0	0	0	0	0	0	0	0	96	0
23-May-25	65	153.0	0	32	0	32	0	0	0	92	15
24-May-25	66	169.6	0	17	0	0	85	0	0	89	55
25-May-25	67	0.0	0	0	0	0	32	0	0	91	18
26-May-25	68	96.0	0	0	0	0	0	0	0	0	0
27-May-25	69	0.0	79	0	0	0	0	0	0	0	0
28-May-25	70	0.0	0	0	0	0	10	0	0	0	0
29-May-25	71	0.0	0	0	0	0	0	0	0	0	0

Total (bbl)	Volume of Built	Dump/Contaminate	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
	8,175.0	812	802	51	383	740	0	78	3,004	1355.0

Table 11-6: AZNS-075-ST1 Loss Distribution

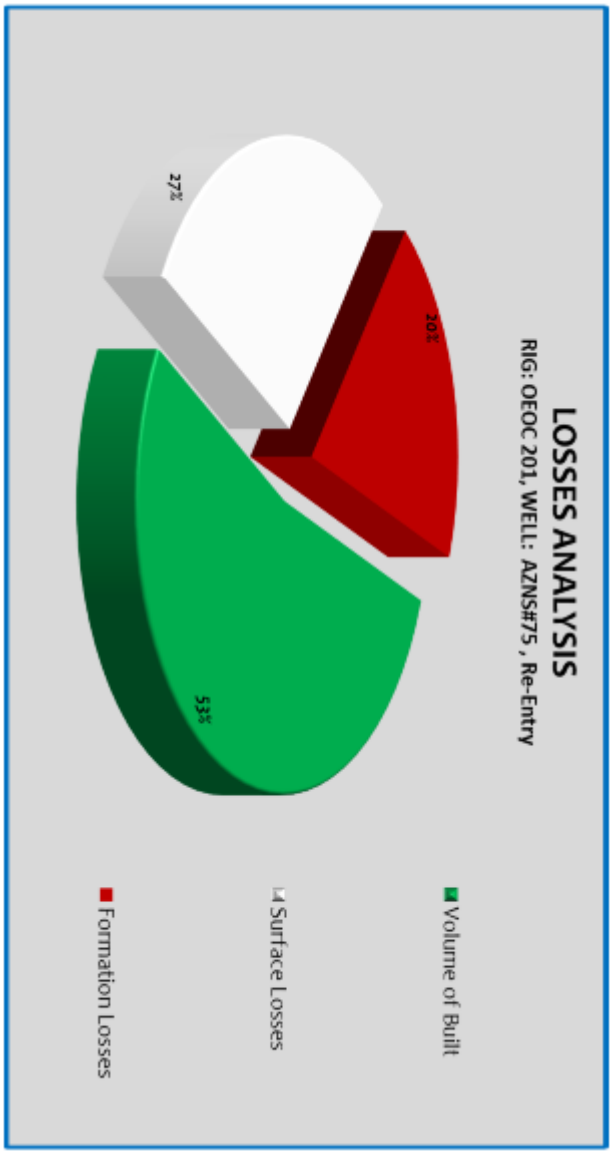


Figure 11-5: AZNS-075-ST1 Loss Analysis

11.2.1.6 Interval Fluid Properties Recap

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	Solid %	Chloride	KCL (%Wt)	Calcium	Total Hardness	Mud Type
20-Mar-25	3799.5	82	40	11	8	N.C	9.4	16	173000		680	820	SALT/POL MUD
21-Mar-25	3799.5	82	40	11	8	N.C	9.4	16	173000		680	820	SALT/POL MUD
22-Mar-25	3799.5	82	41	11	8	N.C	9.2	16	173000		680	820	SALT/POL MUD
23-Mar-25	3799.5	84	48	12	8	N.C	9.5	16	173000		680	820	SALT/POL MUD
24-Mar-25	3799.5	84	48	12	8	N.C	9.5	16	173000		680	820	SALT/POL MUD
25-Mar-25	3799.5	84	44	12	8	N.C	9.5	16	173000		680	820	SALT/POL MUD
26-Mar-25	3799.5	84	44	12	8	N.C	9.5	16	173000		680	820	SALT/POL MUD
27-Mar-25	3799.5	84	42	12	7	N.C	9.4	16	173000		680	820	SALT/POL MUD
28-Mar-25	3799.5	84	41	12	7	N.C	9.2	16	173000		680	820	SALT/POL MUD
29-Mar-25	3799.5	84	41	12	7	N.C	9.2	16	173000		680	820	SALT/POL MUD
30-Mar-25	3799.5	84	41	12	7	N.C	9.2	16	173000		680	820	SALT/POL MUD
31-Mar-25	3799.5	84	41	12	7	N.C	9.2	16	173000		680	820	SALT/POL MUD
1-Apr-25	3799.5	84	41	12	7	N.C	9.3	16	173000		680	820	SALT/POL MUD
2-Apr-25	3799.5	84	41	12	7	N.C	9.3	16	173000		680	820	SALT/POL MUD
3-Apr-25	3799.5	84	39	11	6	N.C	10	16	173000		1720	2000	SALT/POL MUD
4-Apr-25	3799.5	84	39	12	7	N.C	9.8	16	173000		1600	1720	SALT/POL MUD
5-Apr-25	3799.5	84	39	12	7	N.C	9.7	16	173000		1600	1720	SALT/POL MUD
6-Apr-25	3799.5	84	39	12	7	N.C	9.7	16	173000		1600	1720	SALT/POL MUD
7-Apr-25	3799.5	84	39	12	7	N.C	9.7	16	173000		1600	1720	SALT/POL MUD
8-Apr-25	3799.5	84	39	12	7	N.C	9.8	16	173000		1600	1720	SALT/POL MUD
9-Apr-25	3799.5	84	39	12	7	N.C	9.8	16	173000		1600	1720	SALT/POL MUD
10-Apr-25	3799.5	84	39	12	7	N.C	9.8	16	173000		1600	1720	SALT/POL MUD
11-Apr-25	3799.5	84	38	12	6	N.C	10.2	16	173000		1900	2040	SALT/POL MUD
12-Apr-25	3799.5	80	38	13	10	N.C	10.9	16	173000		2100	2340	SALT/POL MUD
13-Apr-25	3799.5	80	38	13	10	N.C	10.9	16	173000		2100	2340	SALT/POL MUD
14-Apr-25	3799.5	80	38	13	10	N.C	10.9	16	173000		2100	2340	SALT/POL MUD
15-Apr-25	2282	80	38	13	10	N.C	10.9	16	173000		2100	2340	SALT/POL MUD
16-Apr-25	2282.5	79	38	13	10	N.C	10.9	16	173000		2100	2340	SALT/POL MUD
17-Apr-25	2282.5	76	38	11	9	4	9.2	14	148000		2100	2340	SALT/POL MUD
18-Apr-25	2286.1	76	38	11	9	4	9.2	14	148000		2100	2340	SALT/POL MUD
19-Apr-25	2286.2	76	38	11	9	4	9.2	14	148000		2100	2340	SALT/POL MUD
20-Apr-25	2293	76	38	10	11	3.5	9.1	14	148000		2120	2340	SALT/POL MUD

21-Apr-25	2310	76	38	10	11	3.5	9.1	14	148000		2120	2340	SALT/POL MUD
22-Apr-25	2384.3	76	39	9	10	3	9.2	14	146000	3	2120	2340	Kd Poly Mud
23-Apr-25	2425.5	76	39	9	10	3	9.2	14	146000	4	2120	2340	Kd Poly Mud
24-Apr-25	2501	76	38	9	10	2.8	9.2	14	149000	4	2120	2340	Kd Poly Mud
25-Apr-25	2560	76	39	9	10	2.8	9.1	14	147000	5	1880	2120	Kd Poly Mud
26-Apr-25	2610	76	40	9	10	2.8	9.5	14	147000	5	1880	2120	Kd Poly Mud
27-Apr-25	2610	76	43	9	10	2.8	9.5	14	147000	5	1880	2120	Kd Poly Mud
28-Apr-25	2695.5	76	43	9	10	2.8	9.5	14	147000	5	1880	2120	Kd Poly Mud
29-Apr-25	2695.4	76	45	9	12	2.8	9.6	14	147000	5	1880	2120	Kd Poly Mud
30-Apr-25	2718.3	76	44	9	12	2.8	9.6	14	147000	5	1880	2120	Kd Poly Mud
1-May-25	2781.8	76	46	9	12	2.8	9.6	14	147000	5	1880	2120	Kd Poly Mud
2-May-25	2817	76	47	9	14	2.8	9.6	14	147000	5	1880	2040	Kd Poly Mud
3-May-25	2884.5	76	47	9	14	2.8	9.6	14	147000	5	1880	2040	Kd Poly Mud
4-May-25	2884	76	48	9	14	2.8	9.5	14	147000	5	1880	2040	Kd Poly Mud
5-May-25	2884	76	52	9	14	2.8	9.5	14	147000	5	1880	2040	Kd Poly Mud
6-May-25	2912.6	76	46	9	14	2.8	9.6	14	147000	5	1880	2040	Kd Poly Mud
7-May-25	2912.6	76	45	10	13	2.8	9.6	14	155000	5	1880	2040	Kd Poly Mud
8-May-25	2979	76	45	10	13	2.6	9.6	14	155000	5	1880	2040	Kd Poly Mud
9-May-25	2979.3	76	50	10	13	2.6	9.6	14	155000	5	1880	2120	Kd Poly Mud
10-May-25	3012	76	45	10	13	2.6	9.6	14	155000	5	1880	2120	Kd Poly Mud
11-May-25	3085.4	76	44	11	12	2.6	9.2	14	154000	5	1880	2120	Kd Poly Mud
12-May-25	3151.3	76	45	13	11	2.4	9.2	14	154000	5	1880	2120	Kd Poly Mud
13-May-25	3238	76	45	14	12	2.2	9.2	14	156000	5	1880	2120	Kd Poly Mud
14-May-25	3299	76	45	14	11	2.2	9.1	14	153000	5	1880	2120	Kd Poly Mud
15-May-25	3304	76	45	14	11	2.2	9.1	14	153000	5	1880	2120	Kd Poly Mud
16-May-25	3335	76	45	14	11	2	9.2	14	165000	5	1880	2120	Kd Poly Mud
17-May-25	3401.5	76	45	14	12	2	9.2	14	165000	5	1880	2120	Kd Poly Mud
18-May-25	3450	76	46	15	12	2	9.1	14	165000	5	1880	2120	Kd Poly Mud
19-May-25	3543	76	46	15	12	2	9.3	14	165000	5	1880	2120	Kd Poly Mud
20-May-25	3573.8	76	46	15	13	2	9.3	14	165000	5.5	1880	2120	Kd Poly Mud
21-May-25	3534	76	46	15	12	2	9.3	14	165000	5.5	1880	2120	Kd Poly Mud
22-May-25	3534	76	47	15	12	2	9	14	165000	5.5	1880	2120	Kd Poly Mud
23-May-25	3675	76	45	15	12	2	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
24-May-25	3692	76	45	15	12	2	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
25-May-25	3692	76	46	15	12	2	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
26-May-25	3692	76	46	15	12	2	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
27-May-25	3692	76	46	15	12	2	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
28-May-25	3692	76	46	15	12	2	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
29-May-25	3692	76	47	15	12	1.8	9.1	14	165000	5.5	1880	2120	Kd Poly Mud
Drilling Start													
Drilling End													

Table 11-7: AZNS-075-ST1 Fluid Properties Recap

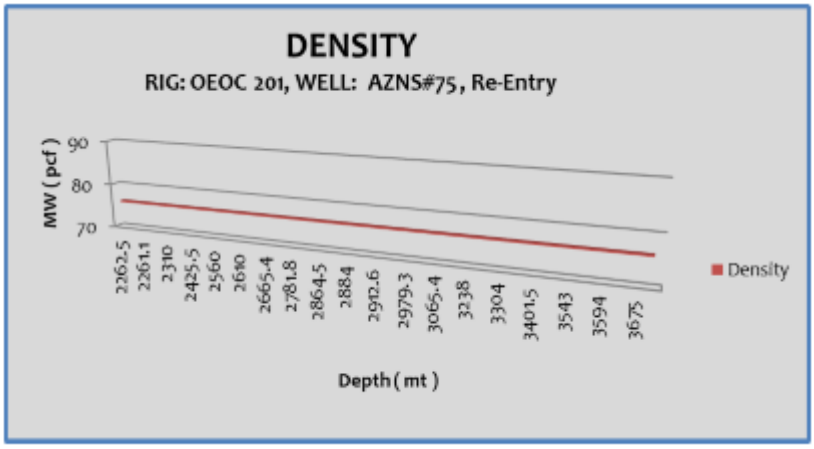


Figure 11-6: AZNS-075-ST1 8-1/2" Density Graph

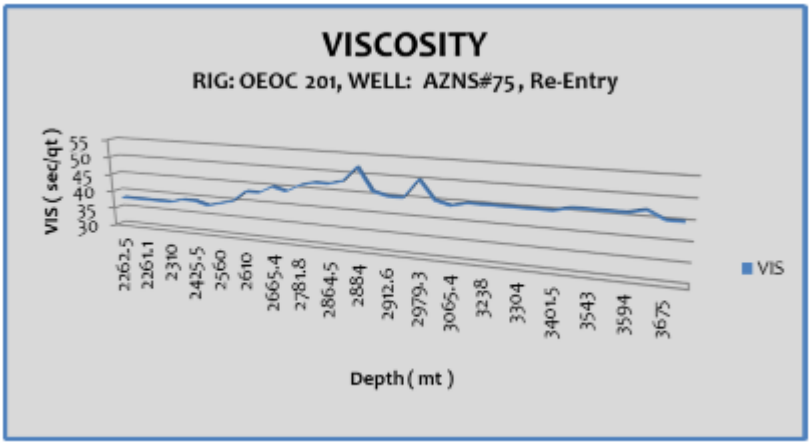


Figure 11-7: AZNS-075-ST1 8-1/2" Viscosity Graph

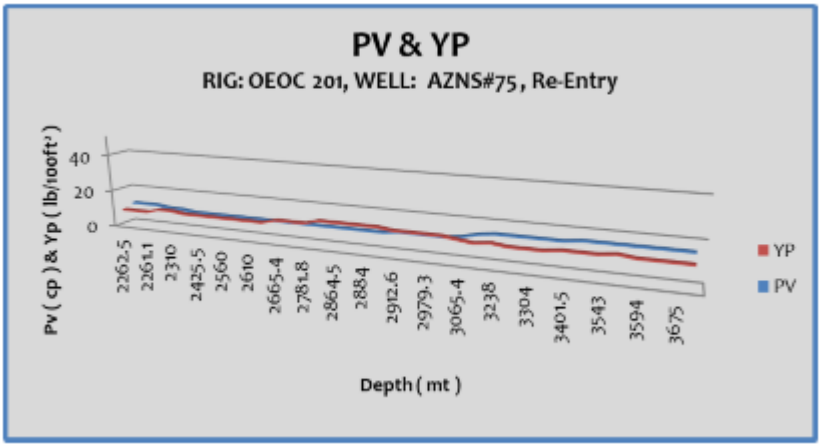


Figure 11-8: AZNS-075-ST1 8-1/2" PV & YP Graph

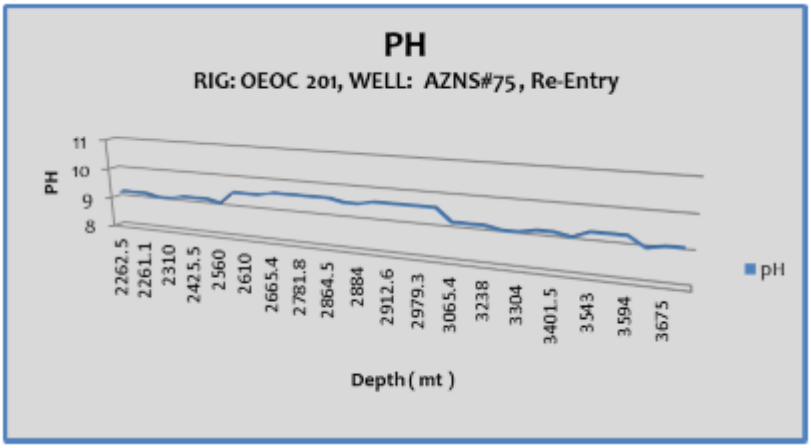


Figure 11-9: AZNS-075-ST1 8-1/2" PH Graph

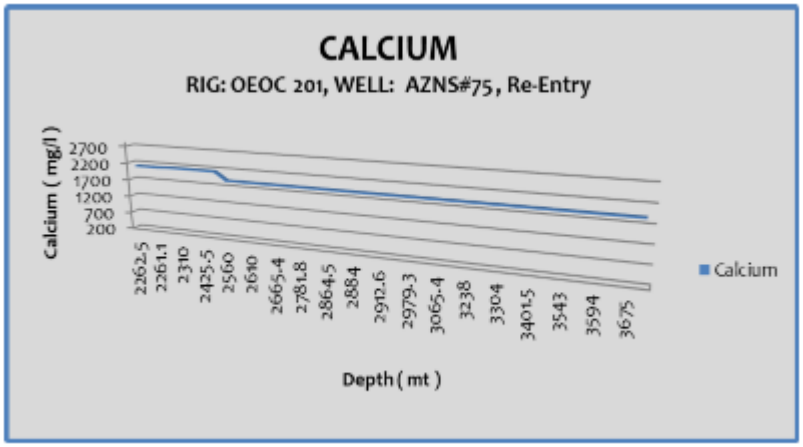


Figure 11-10: AZNS-075-ST1 8-1/2" Calcium Graph

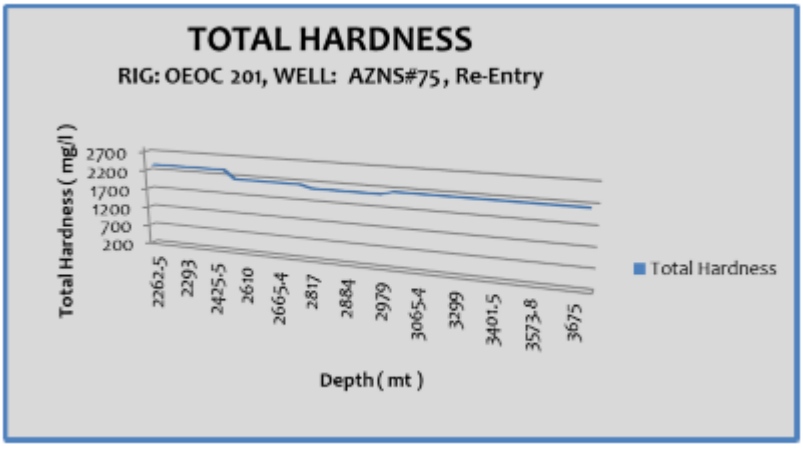


Figure 11-11: AZNS-075-ST1 8-1/2" Total Hardness Graph

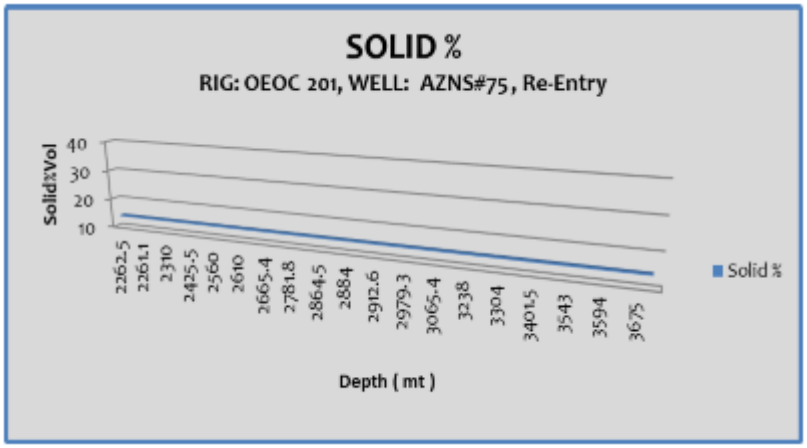


Figure 11-12: AZNS-075-ST1 8-1/2" Solid% Graph

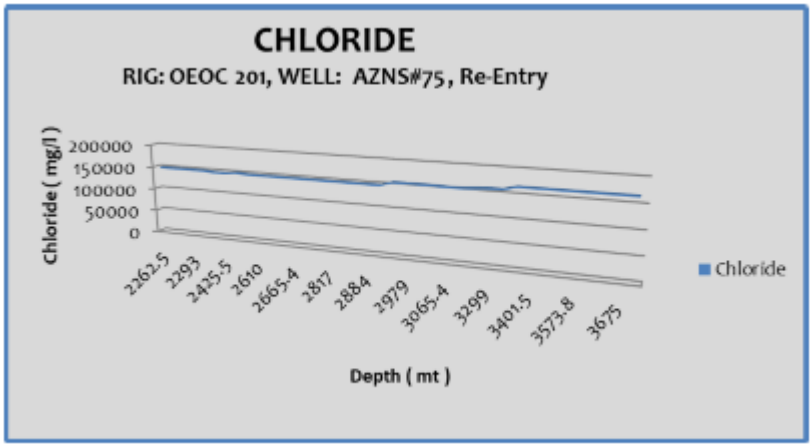


Figure 11-13: AZNS-075-ST1 8-1/2" Chloride Graph

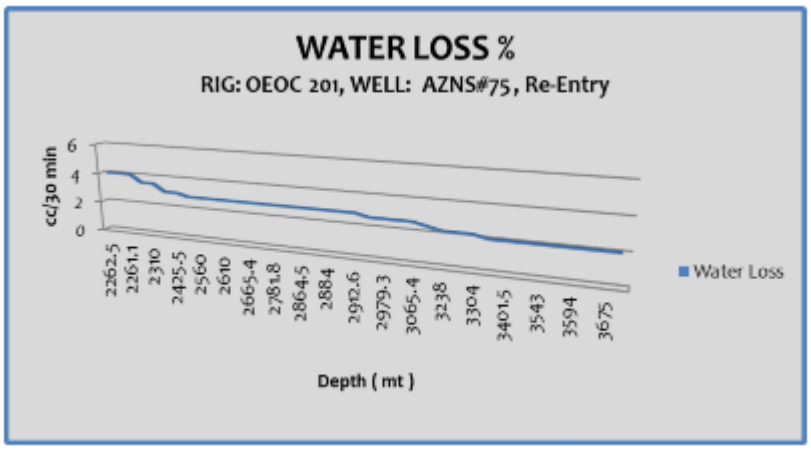


Figure 11-14: AZNS-075-ST1 8-1/2" Water Loss Graph

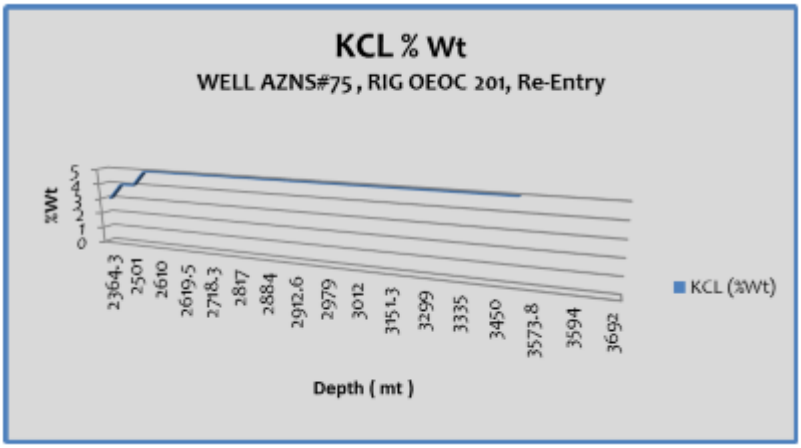


Figure 11-15: AZNS-075-ST1 8-1/2" KCl % Wt Graph

11.2.1.7 Solid Control Disscusion

Rig OEOC 208 has 3 shale shakers were dressed with:

Shaker#1: 170 Mesh Screen

Shaker#2: 200 Mesh Screen

Shaker#3: 170 Mesh Screen

RIG: OEOC 201, WELL: AZNS#75 , Re-Entry Solid Control Equipment Working Hr.s	
Derrick Shaker #1	584
Derrick Shaker #2	744
Derrick Shaker #3	660
Centrifuge # 01	285
Centrifuge # 02	266

Table 11-8: AZNS-075-ST1 8-1/2" Solid Control Desscusion

11.2.2 6 – 1/8" Hole Section Drilling Fluid Types

FLUID PROPERTIES RECAP					
		Drilling start	Range		Drilling End
MW (min)	pcf	78	78	87.0	87.0
Funnel Viscosity	sec/qt	46	44	46	44
PV	cps	14	13	14	13
YP	lb/100sq.ft	11	11	12	12
API Fluid loss	cc	2.4	2.4	2.4	2.4
pH		9.6	9.2	9.6	9.2
Solid	%	14	14	14	14
KCL	%	4.2	4.2	5.0	5
Cl (NaCl)	mg/L	165,000	165,000	170,000	170,000
Total Hardness	mg/L	1,100	1,100	1,360	1,360
Ca Hardness	mg/L	1,240	1,240	1,440	1,440

Table 11-9: AZNS-075-ST1 6-1/8" Fluid Properties Recap Table

11.2.2.1 6-1/8" Interval Material Consumption Analysis

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Caustic Soda	59	55	3,245	lbs	0.81	ppb
Limestone	115	2,200	253,000	lbs	100.76	ppb
Citric acid	23	55	1,265	lbs	0.31	ppb
KCL	7	2,200	15,400	lbs	6.13	ppb
Starch LV	546	55	30,030	lbs	7.47	ppb
Sodium Bicarb	22	55	1,210	lbs	0.48	ppb
Xantan gum	35	55	1,925	lbs	0.77	ppb
Salt (NACL)	80	2,200	176,000	lbs	70.09	ppb
Soda Ash	36	55	1,980	lbs	0.79	ppb
Lime	88	55	4,840	lbs	1.20	ppb

Initial Volume	1,511.0	bbl
Total Volume Built	2,511.0	bbl
Volume received	0.0	bbl
Left In Hole	0.0	bbl
Total Volume Consumed	3,302	bbl
Volume Transfer to Next Section	720.0	bbl
Meter Drilled	196.0	m

Table 11-10: AZNS-075-ST1 6-1/8" Interval Material Consumption Analysis

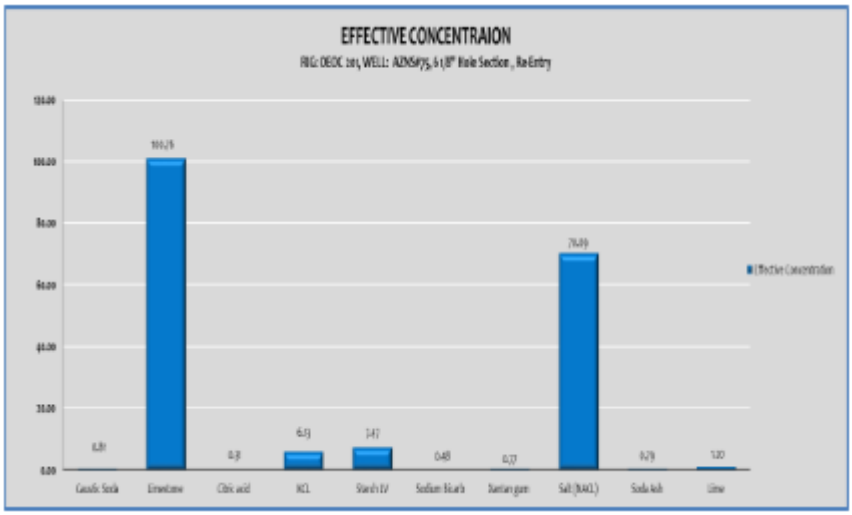


Figure 11-16: AZNS-075-ST1 6-1/8" Effective Concentration

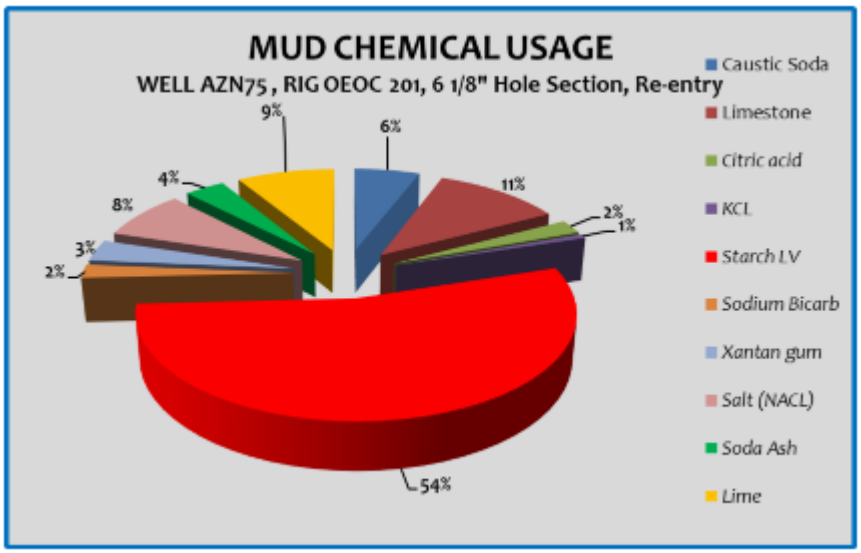


Figure 11-17: AZNS-075-ST1 6-1/8" Mud Chemical Usage

11.2.2.2 6-1/8” Interval Volume Analysis

RIG: OEOC 201, WELL: AZNS#75 , Re-Entry VOLUME ANALYSIS		
Initial Volume	bbls	1,511.0
Received Volume	bbls	0.0
Return	bbls	0.0
Volume Built	bbls	2,511.0
Surface Losses/Dumped	bbls	3,302.0
Formation Losses	bbls	0.0
Total Losses	bbls	3,302.0
Volume Transfer Out	bbls	720

Table 11-11: AZNS-075-ST1 6-1/8” Interval Volume Analysis

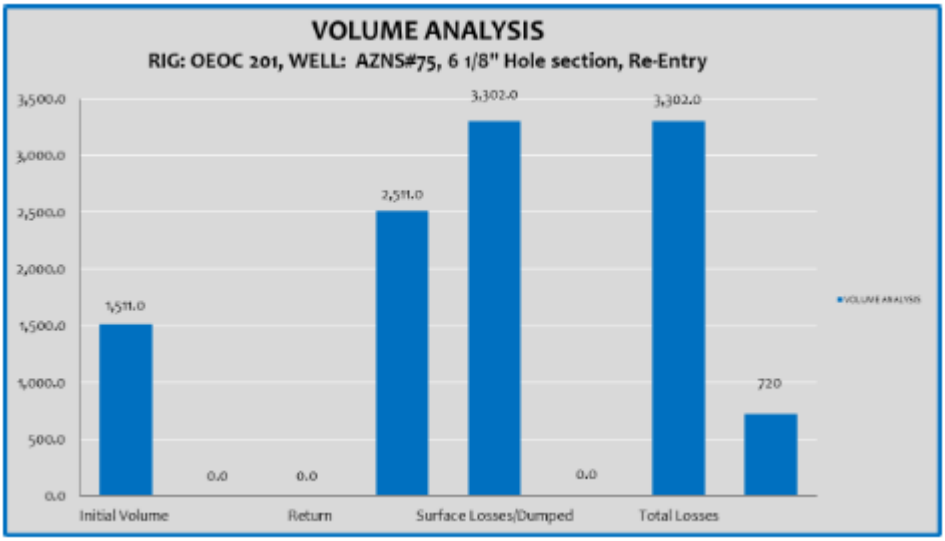


Figure 11-18: AZNS-075-ST1 6-1/8” Interval Volume Analysis

11.2.2.3 6-1/8" Interval Daily Volume Breakdown

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
30-May-25	1	0.0	109	0
31-May-25	2	0.0	39	0
1-Jun-25	3	0.4	22	0
2-Jun-25	4	20.5	51	0
3-Jun-25	5	0.1	6	0
4-Jun-25	6	226.5	85	0
5-Jun-25	7	0.0	4	0
6-Jun-25	8	9.4	52	0
7-Jun-25	9	0.5	63	0
8-Jun-25	10	169.9	94	0
9-Jun-25	11	284.0	117	0
10-Jun-25	12	0.4	2	0
11-Jun-25	13	1.2	38	0
12-Jun-25	14	4.1	22	0
13-Jun-25	15	103.1	85	0
14-Jun-25	16	32.9	39	0
15-Jun-25	17	19.1	107	0
16-Jun-25	18	0.2	25	0
17-Jun-25	19	31.6	120	0
18-Jun-25	20	0.0	37	0
19-Jun-25	21	0.7	10	0
20-Jun-25	22	0.0	27	0
21-Jun-25	23	89.8	0	0
22-Jun-25	24	0.0	85	0
23-Jun-25	25	0.0	0	0
24-Jun-25	26	0.0	4	0
25-Jun-25	27	0.4	53	0
26-Jun-25	28	143.3	7	0
27-Jun-25	29	152.9	81	0
28-Jun-25	30	0.1	5	0
29-Jun-25	31	217.1	208	0
30-Jun-25	32	2.4	51	0
1-Jul-25	33	0.0	31	0
2-Jul-25	34	0.1	85	0
3-Jul-25	35	0.0	5	0
4-Jul-25	36	0.1	85	0
5-Jul-25	37	0.0	27	0

6-Jul-25	38	138.5	128	0
7-Jul-25	39	0.0	35	0
8-Jul-25	40	113.1	23	0
9-Jul-25	41	0.2	41	0
10-Jul-25	42	58.0	10	0
11-Jul-25	43	0.0	73	0
12-Jul-25	44	0.0	25	0
13-Jul-25	45	64.5	23	0
14-Jul-25	46	0.0	4	0
15-Jul-25	47	0.3	8	0
16-Jul-25	48	99.0	45	0
17-Jul-25	49	0.2	13	0
18-Jul-25	50	125.0	37	0
19-Jul-25	51	0.0	3	0
20-Jul-25	52	0.1	23	0
21-Jul-25	53	120.3	23	0
22-Jul-25	54	55.4	106	0
23-Jul-25	55	0.3	31	0
24-Jul-25	56	0.0	23	0
25-Jul-25	57	0.0	11	0
26-Jul-25	58	0.4	0	0
27-Jul-25	59	0.4	24	0
28-Jul-25	60	26.0	0	0
29-Jul-25	61	0.3	0	0
30-Jul-25	62	0.0	15	0
31-Jul-25	63	0.0	15	0
1-Aug-25	64	0.8	25	0
2-Aug-25	65	0.5	20	0
3-Aug-25	66	0.8	30	0
4-Aug-25	67	131.5	115	0
5-Aug-25	68	1.5	35	0
6-Aug-25	69	2.0	15	0
7-Aug-25	70	0.0	5	0
8-Aug-25	71	0.5	29	0
9-Aug-25	72	0.0	21	0
10-Aug-25	73	0.0	132	0
11-Aug-25	74	0.0	60	0
12-Aug-25	75	0.0	27	0
13-Aug-25	76	0.0	5	0
14-Aug-25	77	0.0	4	0
15-Aug-25	78	0.0	0	0
16-Aug-25	79	0.0	144	0
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		2,511	3,302	0

Table 11-12: AZNS-075-ST1 6-1/8" Interval Daily Volume Breakdown

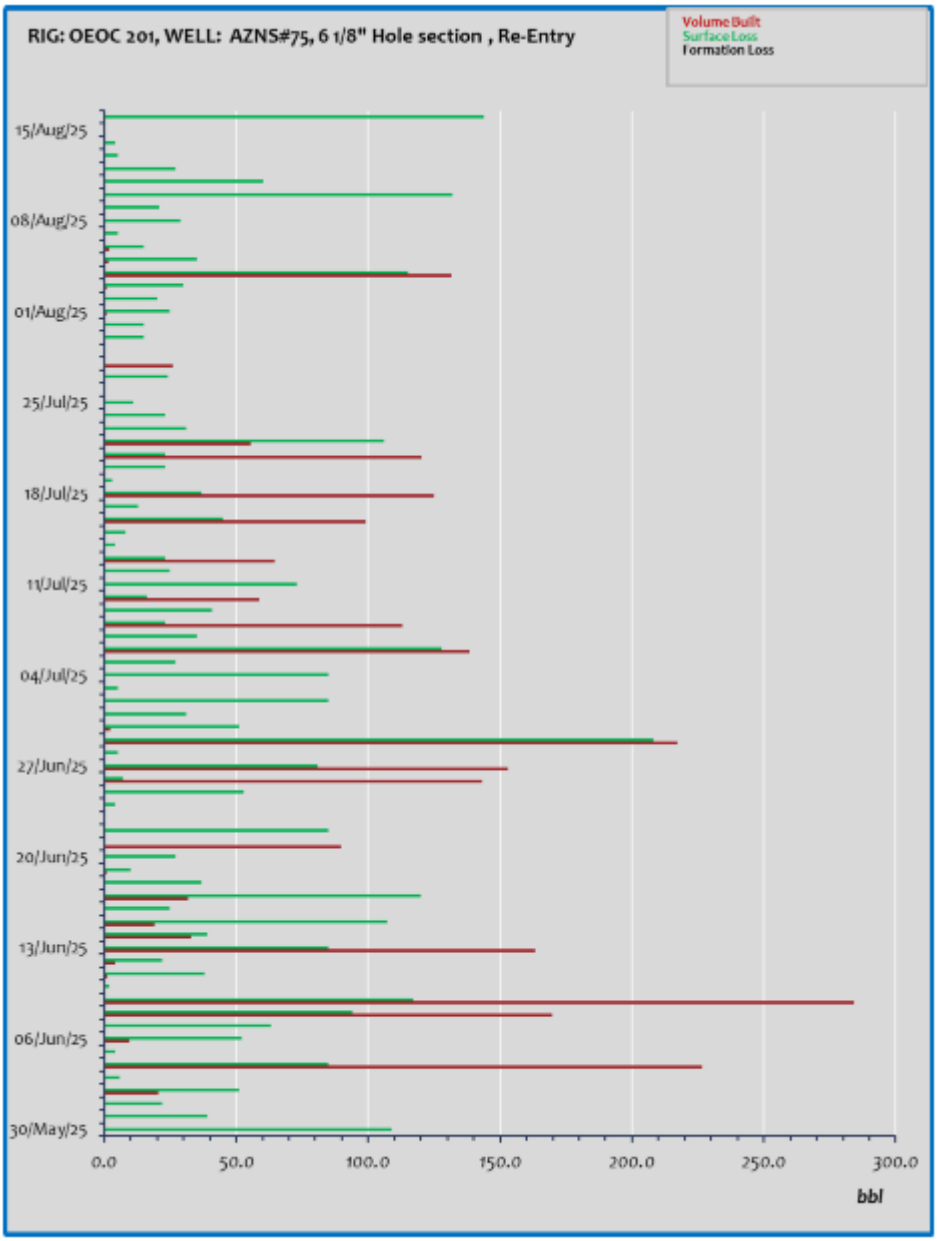


Figure 11-19: AZNS-075-ST1 6-1/8" Interval Daily Volume Breakdown

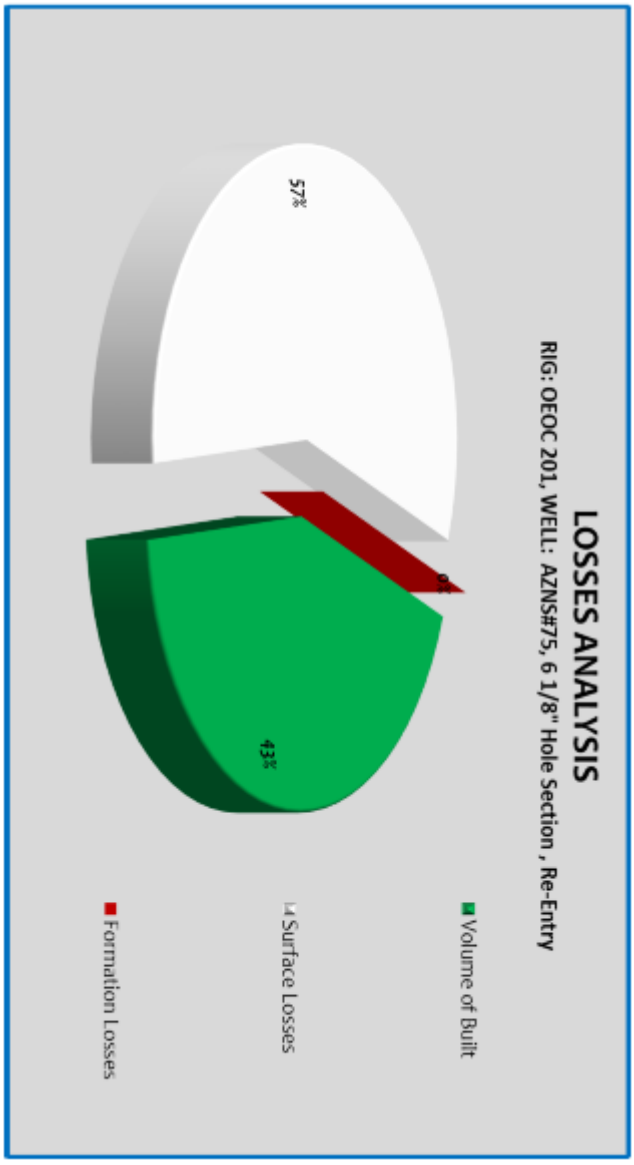


Figure 11-20: AZNS-075-ST1 6-1/8” Losses Analysis

11.2.2.4 6-1/8" Interval Loss Distribution

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
30-May-25	72	0.0	82	0	0	0	12	0	0	0	15
31-May-25	73	0.0	0	0	4	0	0	0	0	0	35
1-Jun-25	74	0.4	0	8	4	0	0	0	0	0	10
2-Jun-25	75	20.5	0	8	5	0	28	0	0	0	10
3-Jun-25	76	0.1	0	0	6	0	0	0	0	0	0
4-Jun-25	77	226.5	0	0	4	0	36	0	0	0	45
5-Jun-25	78	0.0	0	0	4	0	0	0	0	0	0
6-Jun-25	79	9.4	0	4	5	0	21	0	0	0	22
7-Jun-25	80	0.5	30	0	5	0	28	0	0	0	0
8-Jun-25	81	169.9	0	14	4	21	0	0	0	0	55
9-Jun-25	82	284.0	0	12	5	12	48	0	0	0	40
10-Jun-25	83	0.4	0	2	0	0	0	0	0	0	0
11-Jun-25	84	1.2	0	12	4	12	0	0	0	0	10
12-Jun-25	85	4.1	0	12	4	0	0	0	0	0	0
13-Jun-25	86	103.1	60	12	5	0	8	0	0	0	0
14-Jun-25	87	32.9	0	14	5	0	5	0	0	0	15
15-Jun-25	88	19.1	0	12	5	0	90	0	0	0	0
16-Jun-25	89	0.2	0	0	5	0	20	0	0	0	0
17-Jun-25	90	31.0	0	15	5	0	60	0	0	0	40
18-Jun-25	91	0.0	0	7	5	0	25	0	0	0	
19-Jun-25	92	0.7	0	5	5	0	0	0	0	0	0
20-Jun-25	93	0.0	0	7	5	0	15	0	0	0	0
21-Jun-25	94	89.8	0	0	0	0	0	0	0	0	0
22-Jun-25	95	0.0	0	0	5	0	15	0	0	0	65
23-Jun-25	96	0.0	0	0	0	0	0	0	0	0	0
24-Jun-25	97	0.0	0	0	4	0	0	0	0	0	0
25-Jun-25	98	0.4	0	0	5	0	23	0	0	0	25
26-Jun-25	99	143.3	0	0	7	0	0	0	0	0	0
27-Jun-25	100	152.9	0	0	5	0	0	0	0	0	76
28-Jun-25	101	0.1	0	0	5	0	0	0	0	0	0
29-Jun-25	102	217.1	158	0	5	0	0	0	0	0	45
30-Jun-25	103	2.4	0	0	4	0	0	0	0	0	47
1-Jul-25	104	0.0	0	0	4	0	0	0	0	0	27
2-Jul-25	105	0.1	0	0	5	0	38	0	0	0	42
3-Jul-25	106	0.0	0	0	5	0	0	0	0	0	0
4-Jul-25	107	0.1	0	0	4	0	34	0	0	0	47
5-Jul-25	108	0.0	0	0	0	0	27	0	0	0	0
6-Jul-25	109	138.5	0	0	5	0	10	0	0	0	113

7-Jul-25	110	0.0	0	0	4	0	31	0	0	0	0
8-Jul-25	111	113.1	0	0	4	0	19	0	0	0	0
9-Jul-25	112	0.2	0	0	5	0	28	0	0	0	8
10-Jul-25	113	58.0	0	0	4	0	0	0	0	0	12
11-Jul-25	114	0.0	0	0	0	0	33	0	30	0	10
12-Jul-25	115	0.0	0	0	4	0	21	0	0	0	0
13-Jul-25	116	64.5	0	0	4	0	19	0	0	0	0
14-Jul-25	117	0.0	0	0	4	0	0	0	0	0	0
15-Jul-25	118	0.3	0	0	5	0	0	0	0	0	3
16-Jul-25	119	99.0	0	0	4	0	29	0	0	0	12
17-Jul-25	120	0.2	0	0	5	0	0	0	0	0	8
18-Jul-25	121	125.0	0	0	4	0	27	0	0	0	6
19-Jul-25	122	0.0	0	0	3	0	0	0	0	0	0
20-Jul-25	123	0.1	0	0	4	0	15	0	0	0	4
21-Jul-25	124	120.3	0	0	4	0	19	0	0	0	0
22-Jul-25	125	55.4	48	3	4	0	25	0	20	0	6
23-Jul-25	126	0.3	0	0	4	0	27	0	0	0	0
24-Jul-25	127	0.0	6	0	4	0	8	0	5	0	0
25-Jul-25	128	0.0	0	0	2	0	9	0	0	0	0
26-Jul-25	129	0.4	0	0	0	0	0	0	0	0	0
27-Jul-25	130	0.4	0	0	2	0	16	0	0	0	6
28-Jul-25	131	26.0	0	0	0	0	0	0	0	0	0
29-Jul-25	132	0.3	0	0	0	0	0	0	0	0	0
30-Jul-25	133	0.0	0	0	5	0	10	0	0	0	0
31-Jul-25	134	0.0	0	0	5	0	10	0	0	0	0
1-Aug-25	135	0.8	0	0	0	5	20	0	0	0	0
2-Aug-25	136	0.5	0	0	5	0	15	0	0	0	0
3-Aug-25	137	0.8	0	0	0	5	0	0	0	0	25
4-Aug-25	138	131.5	0	0	0	5	20	0	0	0	90
5-Aug-25	139	1.5	0	0	5	0	30	0	0	0	0
6-Aug-25	140	2.0	0	0	5	0	10	0	0	0	0
7-Aug-25	141	0.0	0	0	5	0	0	0	0	0	0
8-Aug-25	142	0.5	0	0	5	0	24	0	0	0	0
9-Aug-25	143	0.0	0	0	4	0	0	0	17	0	0
10-Aug-25	144	0.0	0	0	0	0	55		42	0	35
11-Aug-25	145	0.0	0	0	0	0	0	0	60	0	0
12-Aug-25	146	0.0	0	0	0	0	0	0	27	0	0
13-Aug-25	147	0.0	0	0	5	0	0	0	0	0	0
14-Aug-25	148	0.0	0	0	4	0	0	0	0	0	0
15-Aug-25	149	0.0	0	0	0	0	0	0	0	0	0
16-Aug-25	150	0.0	31	0	4	0	47	0	62	0	0
Total (bbl)		Volume of Built	Dump/Contaminate	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
		2,511.0	415	147	288	60	1,110	0	263	0	1013.0

Note: Prepared 1188.2 Cacl2 brine (DMR#143,144,145,146,147,148,150) that is consider in Completion section.

Table 11-13: AZNS-075-ST1 6-1/8" Interval Loss Distribution

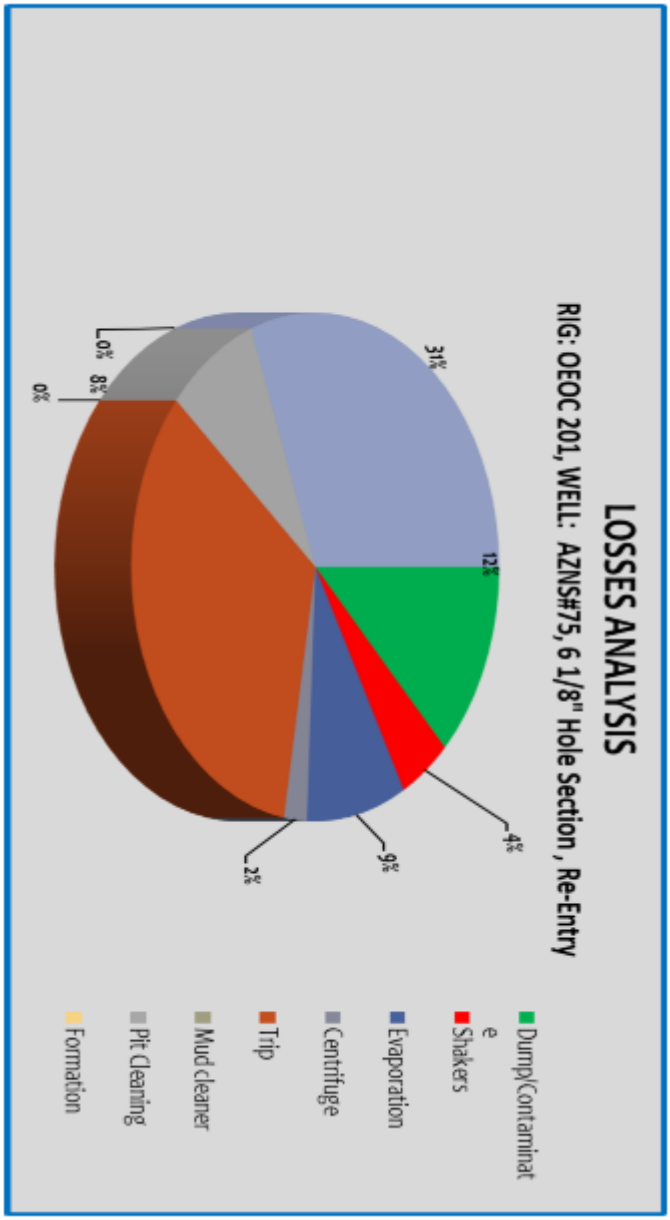


Figure 11-21: AZNS-075-ST1 6-1/8" Losses Analysis

11.2.2.5 6-1/8" Interval Fluid Properties Recap

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	Solid %	Chloride	KCL (WT)	Calcium	Total Hardness	Mud Type
30-May-25	3692	76	47	15	12	1.8	9.2	14	165000	5.5	1800	2120	Kd Poly Mud
31-May-25	3692	76	45	15	12	1.8	9.2	14	165000	5.5	1800	2120	Kd Poly Mud
1-Jun-25	3692	76	47	15	14	8	10	14	165000	5.5	2200	2400	Kd Poly Mud
2-Jun-25	3692	76	48	15	14	4.5	9	14	165000	5.5	1760	1920	Kd Poly Mud
3-Jun-25	3692	76	47	15	14	4.5	9.4	14	165000	5.5	2200	2400	Kd Poly Mud
4-Jun-25	3692	76	47	15	13	8	9.8	14	165000	5.5	2200	2400	Kd Poly Mud
5-Jun-25	3692	76	47	15	13	8	9.8	14	165000	5.5	2200	2400	Kd Poly Mud
6-Jun-25	3692	78	45	15	13	2.2	9.6	14	165000	4.2	1200	1360	Kd Poly Mud
7-Jun-25	3692	78	44	16	13	2.2	9.4	14	165000	4.2	1100	1240	Kd Poly Mud
8-Jun-25	3751	78	48	14	11	2.4	9.6	14	165000	4.2	1100	1240	Kd Poly Mud
9-Jun-25	3760	78	48	14	11	2.4	9.6	14	165000	5	1100	1240	Kd Poly Mud
10-Jun-25	3760	78	48	14	12	2.4	9.6	14	165000	5	1100	1240	Kd Poly Mud
11-Jun-25	3808	78	44	13	12	2.4	9.2	14	167000	5	1160	1280	Kd Poly Mud
12-Jun-25	3888	78	44	13	12	2.4	9.2	14	170000	5	1360	1440	Kd Poly Mud
13-Jun-25	3888	80	42	14	12	2.6	9.1	16	178000	5	2360	2520	Kd Poly Mud
14-Jun-25	3888	82	42	14	12	2.6	9.1	16	178000	5	2360	2520	Kd Poly Mud
15-Jun-25	3888	83	42	14	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
16-Jun-25	3888	83	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
17-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
18-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
19-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
20-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
21-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
22-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
23-Jun-25	3888	84	44	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
24-Jun-25	3888	84	45	15	12	2.6	9.1	18	180000	5	2360	2520	Kd Poly Mud
25-Jun-25	3888	84	41	16	11	4.4	10.2	18	180000	5	2820	2960	Kd Poly Mud
26-Jun-25	3888	84	41	16	11	5.2	10.4	18	180000	5	2360	2520	Kd Poly Mud
27-Jun-25	3888	84	45	16	13	1.8	10.6	18	180000	5	3520	3760	Kd Poly Mud
28-Jun-25	3888	84	45	16	13	1.8	10.8	18	180000	5	4800	5600	Kd Poly Mud
29-Jun-25	3888	85	47	16	14	1.8	9.6	18	180000	5	2800	3040	Kd Poly Mud
30-Jun-25	3888	85	45	16	14	1.8	9.6	18	180000	5	2800	3040	Kd Poly Mud
1-Jul-25	3888	85	44	16	14	1.6	9.5	18	180000	5	2800	3040	Kd Poly Mud
2-Jul-25	3888	85	44	16	14	1.6	9.4	18	180000	5	2800	3040	Kd Poly Mud
3-Jul-25	3888	85	49	16	14	1.6	9.4	18	180000	5	2800	3040	Kd Poly Mud
4-Jul-25	3888	85	46	16	13	1.6	9.4	18	180000	5	2800	3040	Kd Poly Mud
5-Jul-25	3888	85	49	16	13	1.6	9.4	18	180000	5	2800	3040	Kd Poly Mud
6-Jul-25	3888	85	46	16	13	1.6	9.2	18	180000	5	2800	3040	Kd Poly Mud
7-Jul-25	3888	85	47	16	13	1.6	9.2	18	180000	5	2800	3040	Kd Poly Mud
8-Jul-25	3888	87	48	16	13	1.6	9.1	21	180000	5	2800	3040	Kd Poly Mud
9-Jul-25	3888	87	48	16	13	1.6	9.2	21	180000	5	2800	3040	Kd Poly Mud
10-Jul-25	3888	87	48	16	13	1.6	9.2	21	180000	5	2800	3040	Kd Poly Mud

11-Jul-25	3888	87	48	16	13	1.6	9.2	21	180000	5	2800	3040	Kcl Poly Mud
12-Jul-25	3888	87	48	16	13	1.8	9	21	180000	5	2800	3040	Kcl Poly Mud
13-Jul-25	3888	87	45	16	13	1.8	9	21	180000	5	2800	3040	Kcl Poly Mud
14-Jul-25	3888	87	44	16	13	1.9	9	21	180000	5	2800	3040	Kcl Poly Mud
15-Jul-25	3888	87	43	16	13	2.2	9.2	21	180000	5	3240	3400	Kcl Poly Mud
16-Jul-25	3888	87	43	16	13	2.2	9.2	21	180000	5	3240	3400	Kcl Poly Mud
17-Jul-25	3888	87	43	16	13	2.5	9.1	21	180000	5	3240	3400	Kcl Poly Mud
18-Jul-25	3888	86	44	15	13	3.2	9.2	20	170000	5	3000	3160	Kcl Poly Mud
19-Jul-25	3888	86	43	15	12	3	9.2	20	170000	2.5	3200	3360	Kcl Poly Mud
20-Jul-25	3888	86	43	15	12	3	9	20	170000	2.5	3200	3360	Kcl Poly Mud
21-Jul-25	3888	86	43	15	12	3	9	20	170000	2.5	3200	3360	Kcl Poly Mud
22-Jul-25	3888	86	43	15	12	3	9	20	170000	2.5	3200	3360	Kcl Poly Mud
23-Jul-25	3888	85	43	15	12	3	9.1	19	170000	2.5	3200	3360	Kcl Poly Mud
24-Jul-25	3888	84	43	13	11	5.8	9.1	18	174000	2.5	2840	3000	Kcl Poly Mud
25-Jul-25	3888	84	43	13	11	5.8	9.1	18	174000	2.5	2840	3000	Kcl Poly Mud
26-Jul-25	3888	84	43	13	11	6	9.1	18	180000	2.5	2840	3000	Kcl Poly Mud
27-Jul-25	3888	84	43	13	11	10	9.1	18	180000	2.5	2840	3000	Kcl Poly Mud
28-Jul-25	3888	84	43	13	11	10	9.1	18	180000	2.5	2840	3000	Kcl Poly Mud
29-Jul-25	3888	84	43	13	11	10	9.1	18	180000	2.5	2840	3000	Kcl Poly Mud
30-Jul-25	3888	84	43	13	11	10	9.1	18	180000	2.5	2840	3000	Kcl Poly Mud
31-Jul-25	3888	84	43	13	11	12	9.1	18	180000	2.5	2840	3000	Kcl Poly Mud
1-Aug-25	3888	84	40	11	9	22	9.8	18	180000	2.5	3600	3800	Kcl Poly Mud
2-Aug-25	3888	84	40	11	10	22	10	18	180000	2.5	3800	4000	Kcl Poly Mud
3-Aug-25	3888	84	43	11	14	22	9.8	18	180000	2.5	3800	4000	Kcl Poly Mud
4-Aug-25	3888	84	45	13	16	14	9.8	18	180000	2.5	3520	3720	Kcl Poly Mud
5-Aug-25	3888	84	45	13	16	12	9.8	18	180000	2.5	3120	3320	Kcl Poly Mud
6-Aug-25	3888	84	45	13	16	6	9.8	18	180000	2.5	3000	3200	Kcl Poly Mud
7-Aug-25	3888	84	46	13	16	6	9.8	18	180000	2.5	3000	3200	Kcl Poly Mud
8-Aug-25	3888	84	46	13	16	6	9.8	18	180000	2.5	3000	3200	Kcl Poly Mud
9-Aug-25	3888	84	45	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
10-Aug-25	3888	84	45	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
11-Aug-25	3888	84	46	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
12-Aug-25	3888	84	46	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
13-Aug-25	3888	84	46	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
14-Aug-25	3888	84	46	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
15-Aug-25	3888	84	46	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
16-Aug-25	3888	84	45	13	16	6	9.6	18	180000	2.5	3000	3200	SALT/POL MUD
Drilling Start													
Drilling End													

Table 11-14: AZNS-075-ST1 6-1/8" Interval Fluid Properties

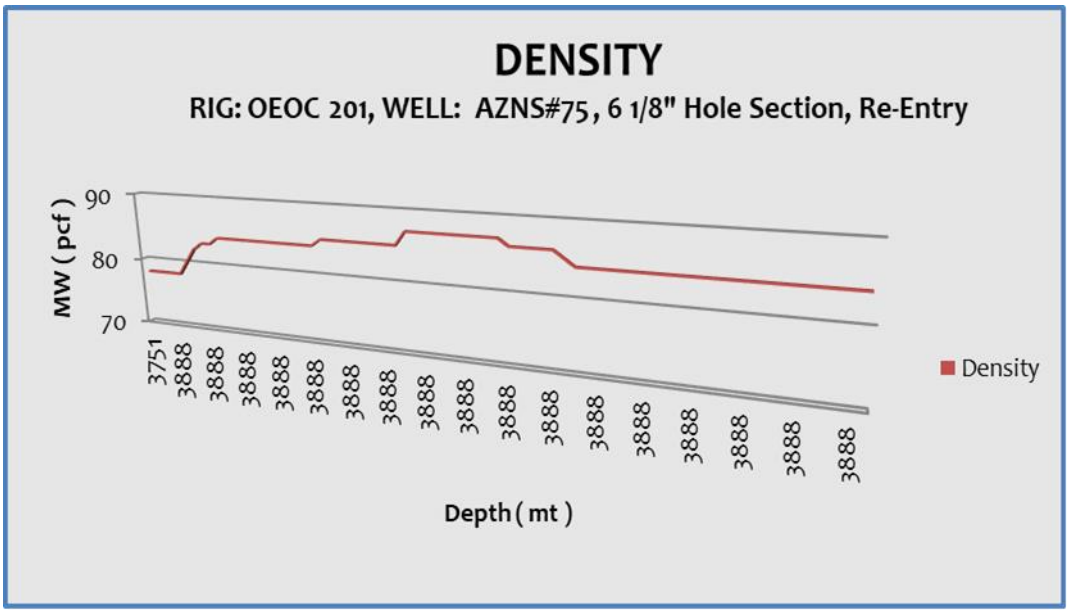


Figure 11-22: AZNS-075-ST1 6-1/8" Density Graph

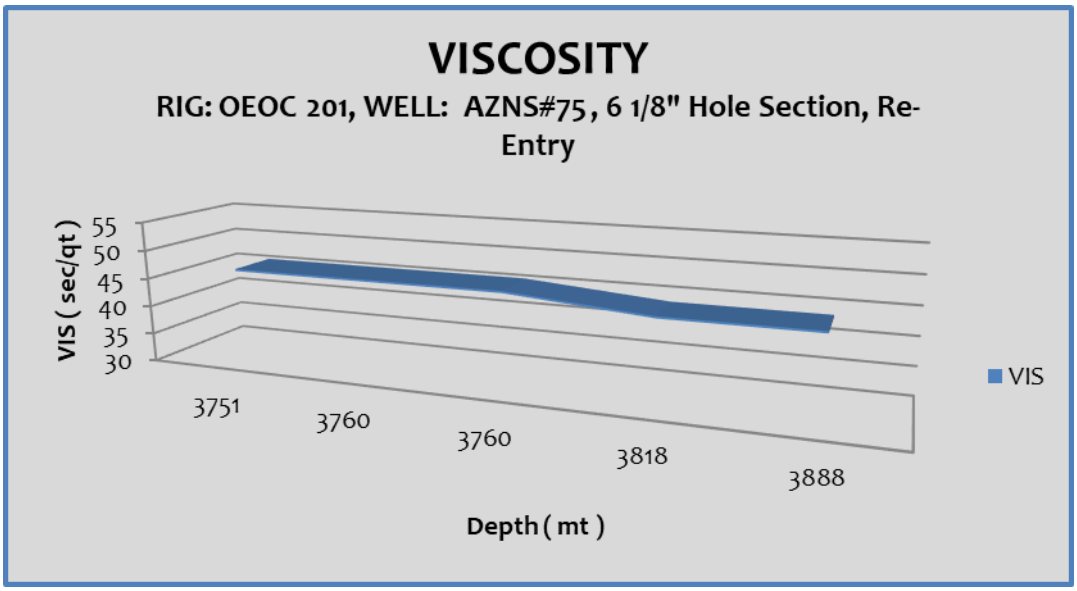


Figure 11-23: AZNS-075-ST1 6-1/8" Viscosity Graph

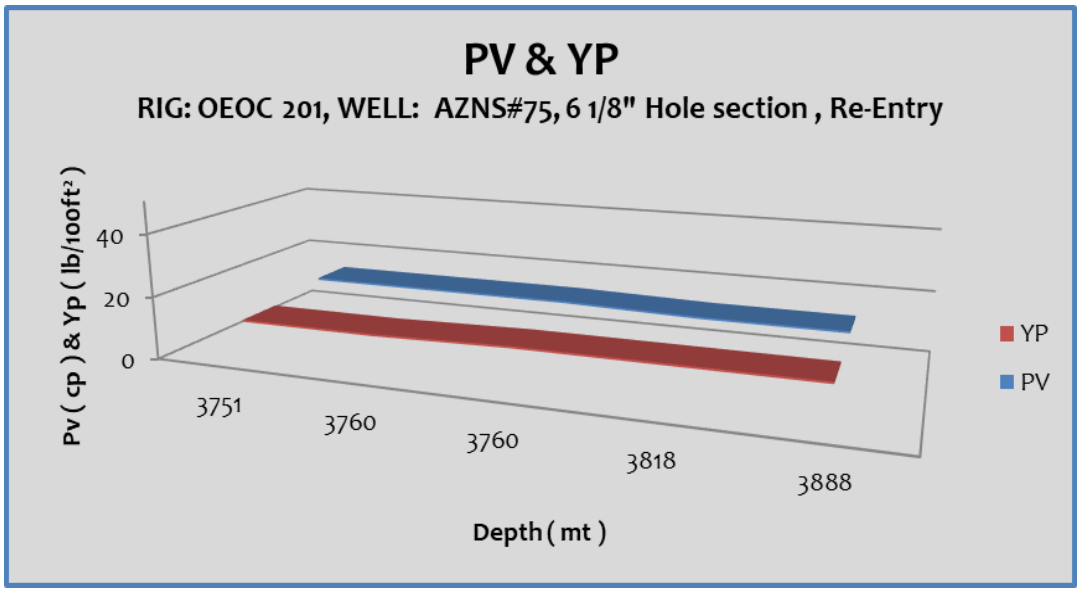


Figure 11-24: AZNS-075-ST1 6-1/8" PV & YP Graph

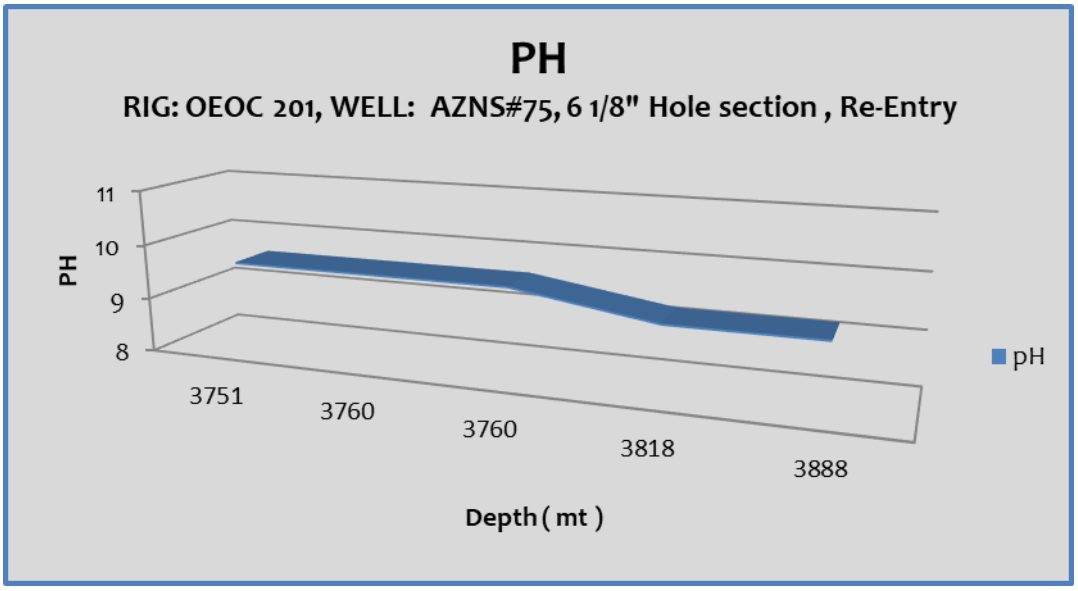


Figure 11-25: AZNS-075-ST1 6-1/8" PH Graph

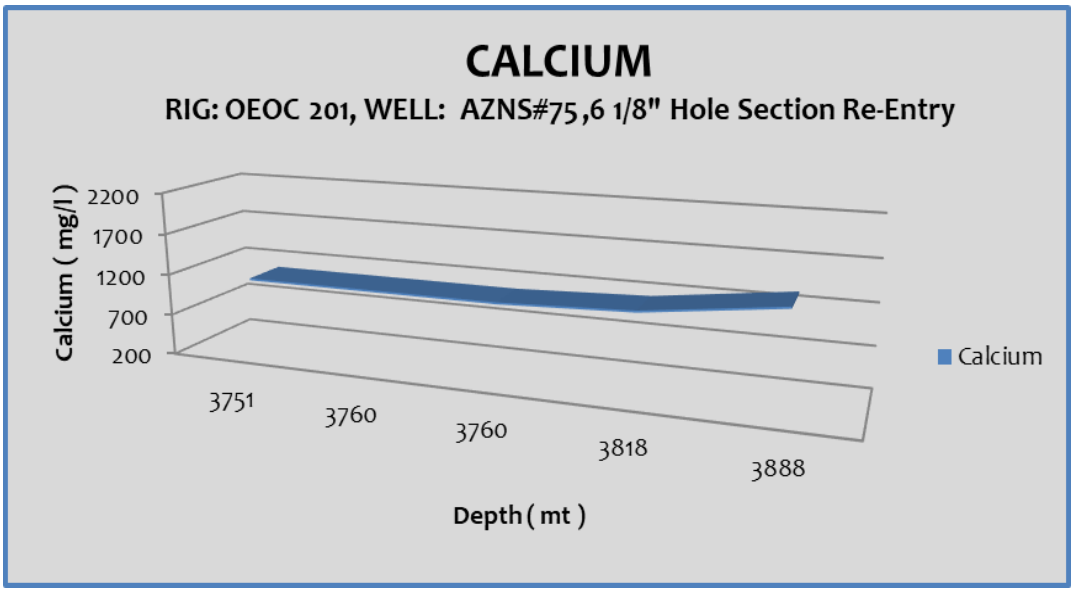


Figure 11-26: AZNS-075-ST1 6-1/8" Calcium Graph

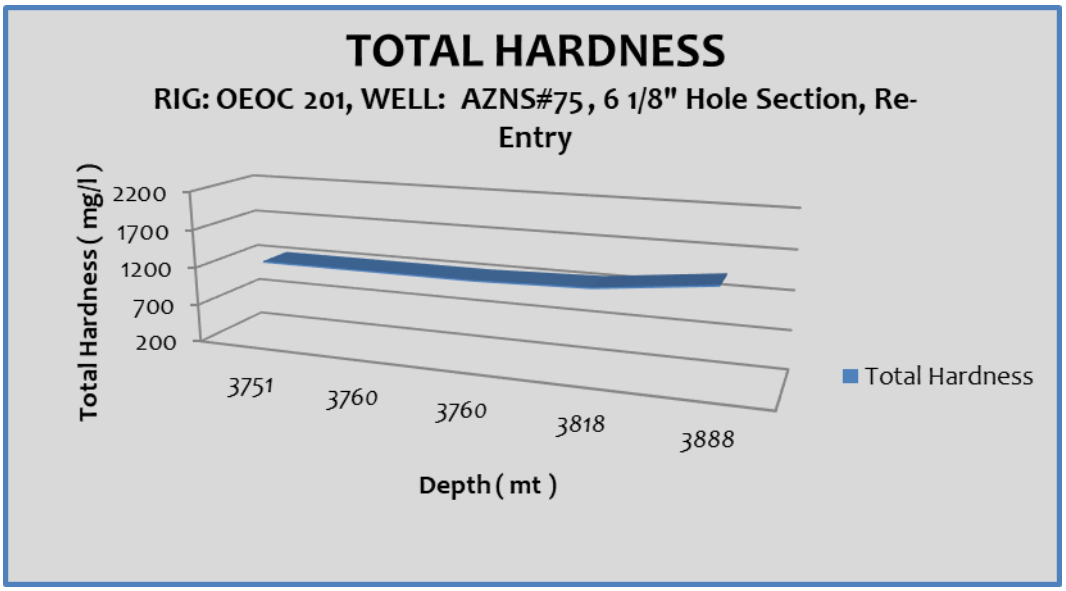


Figure 11-27: AZNS-075-ST1 6-1/8" Total Hardness Graph

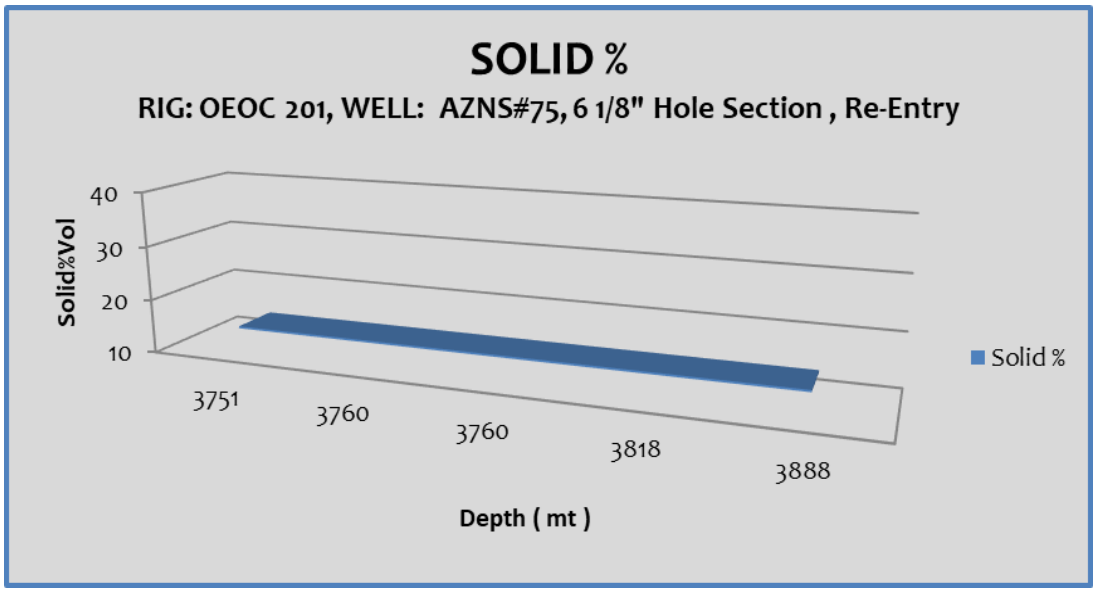


Figure 11-28: AZNS-075-ST1 6-1/8" Solid% Graph

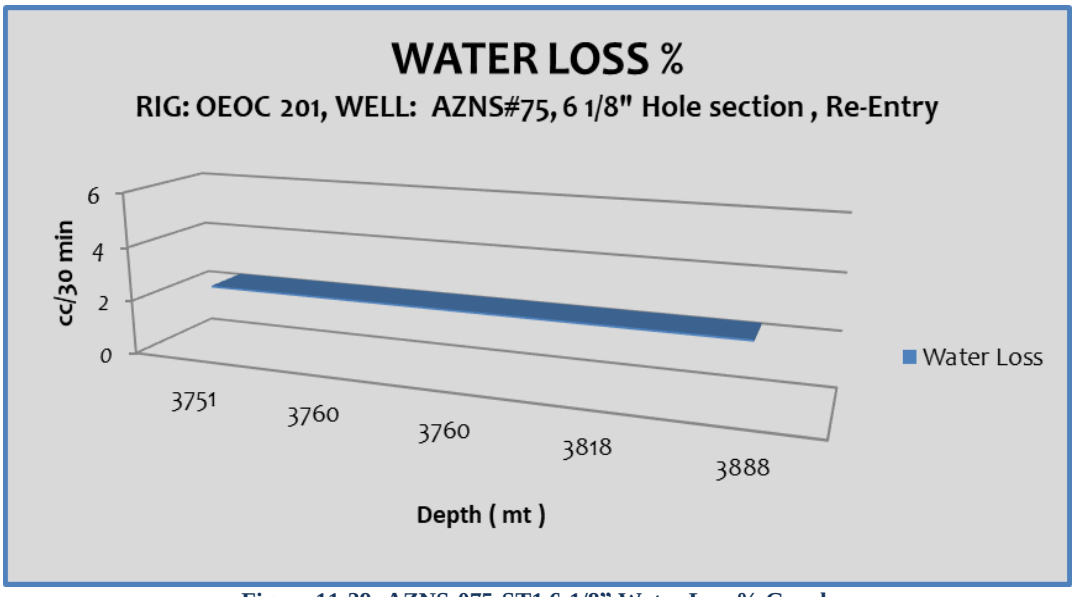


Figure 11-29: AZNS-075-ST1 6-1/8" Water Loss% Graph

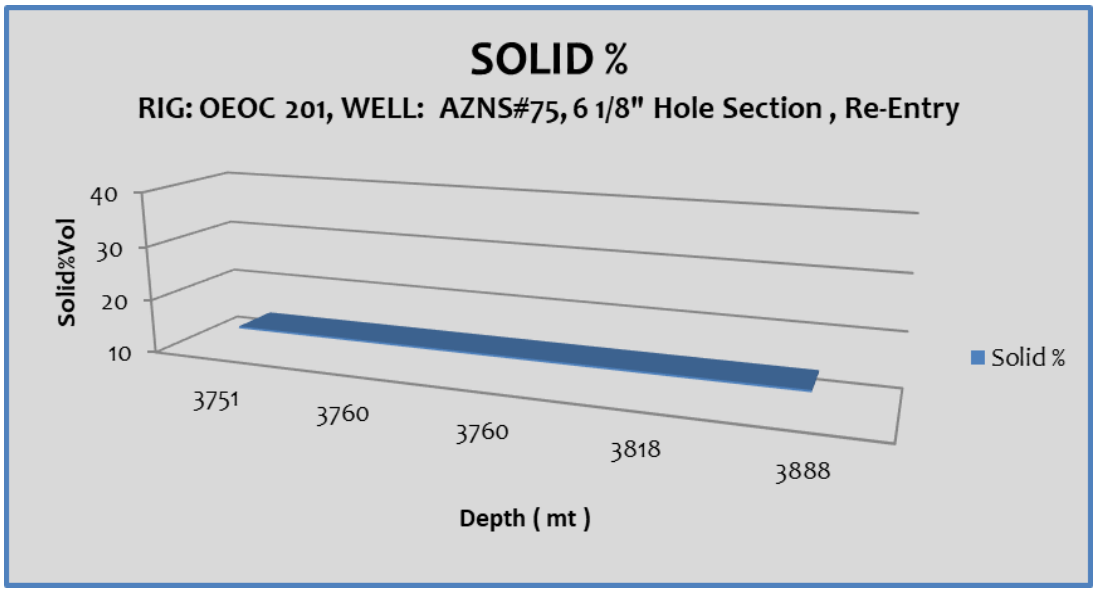


Figure 11-30: AZNS-075-ST1 6-1/8" Chloride Graph

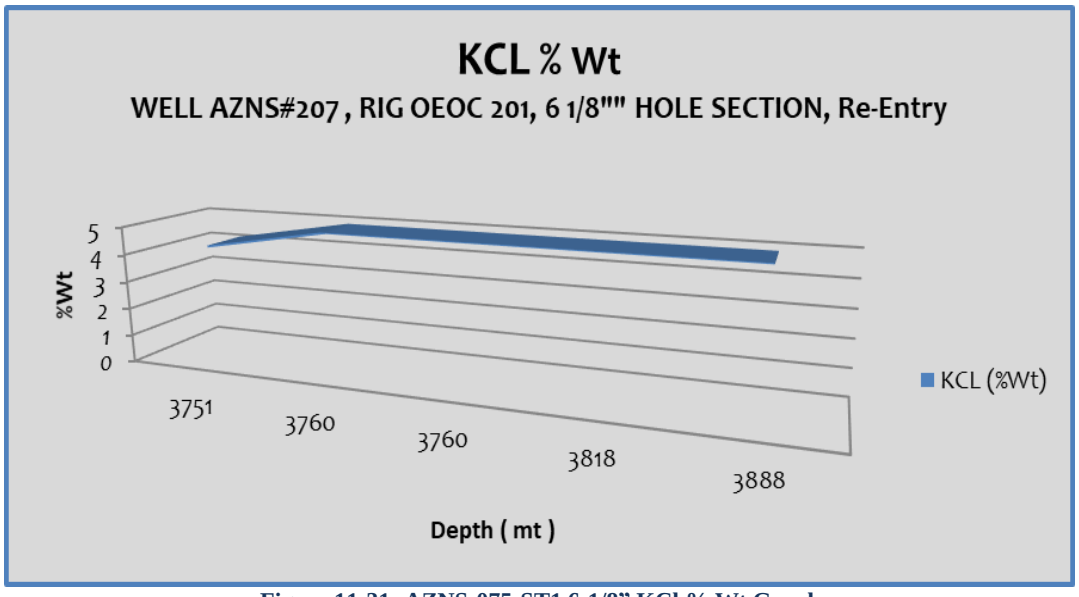


Figure 11-31: AZNS-075-ST1 6-1/8" KCl % Wt Graph

11.2.2.6 6-1/8" Interval Solid Control Disscusion

Rig OEOC 208 has 3 shale shakers were dressed with:

Shaker#1: 170 – 200 Mesh Screen

Shaker#2: 170 – 200 Mesh Screen

Shaker#3: 170 – 200 Mesh Screen

RIG: OEOC 201, WELL: AZNS#75 , Re-Entry Solid Control Equipment Working Hr.s	
Derrick Shaker #1	433
Derrick Shaker #2	826
Derrick Shaker #3	613
Centrifuge # 01	28
Centrifuge # 02	14

Table 11-15: AZNS-075-ST1 6-1/8" Solid Control Desscusion

11.2.3 Interval Completion Section

11.2.3.1 $CaCl_2$ Brine

This fluid is recommended to make from fresh water or is solutions made with water and the addition of one or more electrolytes. These fluids do not contain either suspended particles or viscosifiers, which mean neither filtration control or viscosity control, are provided.

11.2.3.2 Material Concentration

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Lime	61	55	3,355	lbs	2.8	ppb
Corrosion Inhibitor	7	55	385	gals	0.4	gpb
H_2S Scavenger	4	55	220	gals	0.2	gpb
O_2 Scavenger	4	55	220	gals	0.2	gpb
Xan.Gum	3	55	165	lbs	1.9	ppb
Salt	4	2,200	8,800	lbs	103.5	ppb
Cacl2	92	2,200	202,400	lbs	170.3	ppb

Prepared 90 bbl Hi-Vis Nacl brine & pumped 50 bbl as spacer.

Corrosion Inhibitor 0.4 gpb	= 1%vol
H_2S Scavenger 0.2 gpb	= 0.5%vol
O_2 Scavenger 0.2 gpb	= 0.5%vol

Hi-Vis Pill Vol.	90 bbl
Total Volume Built (Completion Fluid)	1,207.8 bbl

Table 11-16: AZNS-075-ST1 Completion Material Concentration

Note: after Prepared the 84 PCF $CaCl_2$ brine, filtrate the brine and adjust NTU (Nephelometric Turbidity Unit) and Suspended-solids Concentration in Range based on Standard policy.

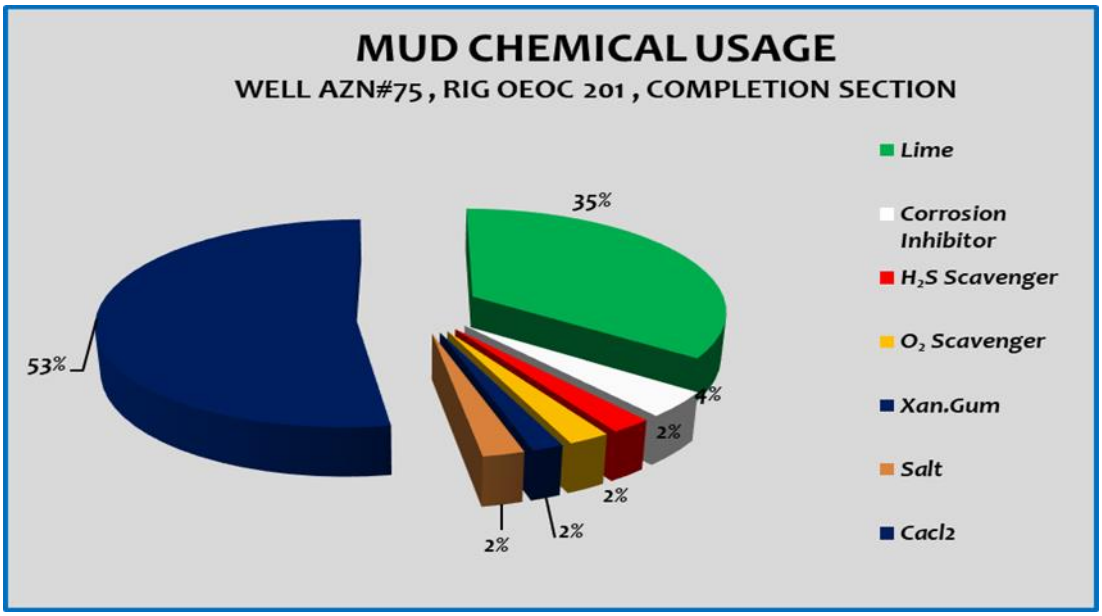


Figure 11-32: AZNS-075-ST1 Completion Section Mud Chemical Usage

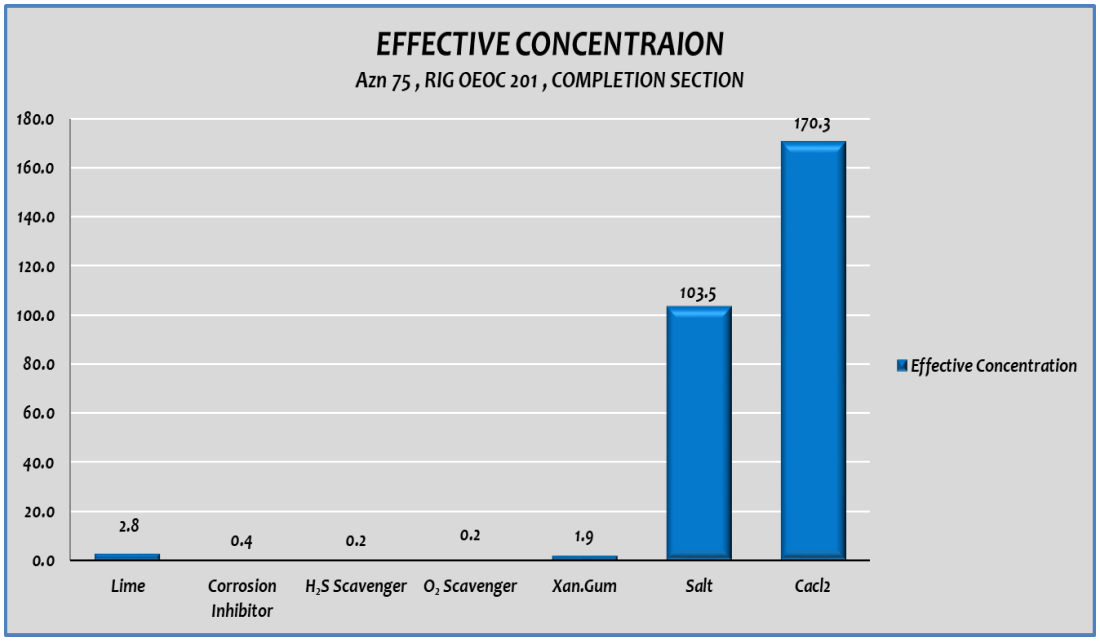


Figure 11-33: AZNS-075-ST1 Completion Section Effective Concentration

12. Waste Management Report

12.1 De – Completion Section

12.1.1 Operation's Recap

12.1.1.1 Fixation's Operation

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
4	20-Apr-2025	2295	32.5	0	0	0	0	0	0
5	21-Apr-2025	2295	0	0	0	0	0	0	0
6	22-Apr-2025	2364.3	69.3	0	0	0	0	0	0
7	23-Apr-2025	2425.5	61.2	0	0	0	0	0	0
8	24-Apr-2025	2501	75.5	0	0	0	0	0	0
9	25-Apr-2025	2560	59	0	0	0	0	0	0
10	26-Apr-2025	2601	41	0	0	0	0	0	0
11	27-Apr-2025	2610.2	9.2	0	0	0	0	0	0
12	28-Apr-2025	2619.5	9.3	0	0	0	0	0	0
13	29-Apr-2025	2665.4	45.9	0	0	0	0	0	0
14	30-Apr-2025	2718.3	52.9	0	0	0	0	0	0

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
15	1-May-2025	2781.8		0	0	0	0	0	0
16	2-May-2025	2817	35.2	0	0	0	0	0	0
17	3-May-2025	2864	47	0	0	0	0	0	0
18	4-May-2025	2884	20	0	0	0	0	0	0
19	5-May-2025	2884	0	0	0	0	0	0	0
20	6-May-2025	2912	28	0	0	0	0	0	0
21	7-May-2025	2951	39	0	0	0	0	0	0
22	8-May-2025	2979.3	28.3	0	0	0	0	0	0
23	9-May-2025	2979.3	0	0	0	0	0	0	0
24	10-May-2025	3012	32.7	0	0	0	0	0	0
25	11-May-2025	3065	53	0	0	0	0	0	0
26	12-May-2025	3151.3	86.3	0	0	0	0	0	0
27	13-May-2025	3299	147.7	100	100	100	100	100	100
28	14-May-2025	3304	5	50	150	50	150	50	150
29	15-May-2025	3335	31	100	250	100	250	100	250
30	16-May-2025	3401	66	100	350	100	350	50	300

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
31	17-May-2025	3450	49	100	450	100	450	50	350
32	18-May-2025	3450	0	100	550	100	550	50	400
33	19-May-2025	3573	123	100	650	0	550	0	400
34	20-May-2025	3594	21	100	750	0	550	0	400

Table 12-1: AZNS-075-ST1 De-Completion Section Solid Handling System

12.1.1.2 Analysis

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
4	20-Apr-2025	2295	32.5		0	0	0	0
5	21-Apr-2025	2295	0		0	0	0	0
6	22-Apr-2025	2364.3	69.3		0	0	0	0
7	23-Apr-2025	2425.5	61.2		0	0	0	0
8	24-Apr-2025	2501	75.5		0	0	0	0
9	25-Apr-2025	2560	59		0	0	0	0
10	26-Apr-2025	2601	41		0	0	0	0
11	27-Apr-2025	2610.2	9.2		0	0	0	0
12	28-Apr-2025	2619.5	9.3		0	0	0	0
13	29-Apr-2025	2665.4	45.9		0	0	0	0
14	30-Apr-2025	2718.3	52.9		0	0	0	0
15	1-May-2025	2781.8	63.5		0	0	0	0
16	2-May-2025	2817	35.2		0	0	0	0
17	3-May-2025	2864	47		0	0	0	0
18	4-May-2025	2884	20		0	0	0	0

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
19	5-May-2025	2884	0		0	0	0	0
20	6-May-2025	2912	28		0	0	0	0
21	7-May-2025	2951	39		0	0	0	0
22	8-May-2025	2979.3	28.3		0	0	0	0
23	9-May-2025	2979.3	0		0	0	0	0
24	10-May-2025	3012	32.7		0	0	0	0
25	11-May-2025	3065	53		0	0	0	0
26	12-May-2025	3151.3	86.3		0	0	0	0
27	13-May-2025	3299	147.7		0	0	0.1	0.004166667
28	14-May-2025	3304	5		0	0	0	0.004
29	15-May-2025	3335	31		0	0	0	0.003846154
30	16-May-2025	3401	66		0	0	0	0.003703704
31	17-May-2025	3450	49		0	0	0	0.003571429
32	18-May-2025	3450	0		0	0	0	0.003448276
33	19-May-2025	3573	123		0	0	0	0.003333333
34	20-May-2025	3594	21		0	0	0	0.003225806

Table 12-2: AZNS-075-ST1 De-Completion Section Fixation Analysis Table

12.1.2 Dewatering's Recap

12.1.2.1 Dewatering

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
4	20-Apr-2025	2295	32.5	2500	2500	400	400	0	0	0	0	0	0
5	21-Apr-2025	2295	0	0	2500	0	400	0	0	0	0	0	0
6	22-Apr-2025	2364.3	69.3	0	2500	0	400	350	350	0	0	50	50
7	23-Apr-2025	2425.5	61.2	0	2500	450	850	300	650	0	0	50	100
8	24-Apr-2025	2501	75.5	0	2500		850	0	650	45	45	0	100
9	25-Apr-2025	2560	59	0	2500		850	0	650	50	95	5	105
10	26-Apr-2025	2601	41	0	2500	350	1200	0	650	0	95	0	105
11	27-Apr-2025	2610.2	9.2	0	2500	0	1200	235	885	65	160	50	155
12	28-Apr-2025	2619.5	9.3	50	2550	400	1600	207	1092	143	303	50	205
13	29-Apr-2025	2665.4	45.9	50	2600	350	1950	0	1092	73	376	0	205
14	30-Apr-2025	2718.3	52.9	50	2650	0	1950	200	1292	73	449	0	205

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
15	1-May-2025	2781.8	63.5	50	2700	300	2250	327	1619	73	522	0	205
16	2-May-2025	2817	35.2	150	2850	300	2550	130	1749	73	595	0	205
17	3-May-2025	2864	47	300	3150	300	2850	220	1969	73	668	0	205
18	4-May-2025	2884	20	1000	4150	350	3200	200	2169	145	813	0	205
19	5-May-2025	2884	0	1000	5150	350	3550	288	2457	75	888	0	205
20	6-May-2025	2912	28	1000	6150	400	3950	350	2807	0	888	0	205
21	7-May-2025	2951	39	1000	7150	400	4350	377	3184	73	961	0	205
22	8-May-2025	2979.3	28.3	1000	8150	400	4750	327	3511	73	1034	0	205
23	9-May-2025	2979.3	0	1000	9150	400	5150	350	3861	0	1034	0	205
24	10-May-2025	3012	32.7	800	9950	400	5550	315	4176	135	1169	0	205
25	11-May-2025	3065	53	300	10250	400	5950	330	4506	70	1239	0	205
26	12-May-2025	3151.3	86.3	300	10550	400	6350	276	4782	124	1363	0	205
27	13-May-2025	3299	147.7	300	10850	400	6750	400	5182	0	1363	0	205

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
28	14-May-2025	3304	5	100	10950	400	7150	400	5582	0	1363	0	205
29	15-May-2025	3335	31	100	11050	400	7550	400	5982	0	1363	0	205
30	16-May-2025	3401	66	0	11050	400	7950	400	6382	0	1363	0	205
31	17-May-2025	3450	49	0	11050	400	8350	250	6632	95	1458	0	205
32	18-May-2025	3450	0	0	11050	400	8750	250	6882	95	1553	0	205
33	19-May-2025	3573	123	0	11050	400	9150	300	7182	70	1623	0	205
34	20-May-2025	3594	21	0	11050	400	9550	250	7432	135	1758	0	205

Table 12-3: AZNS-075-ST1 De-Completion Section Dewatering Data Table

12.1.2.2 Dewatering Analysis

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				45482	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
4	4/20/2025	2295	32.5	8.5	1200	50	80	30	1	40	1000
5	4/21/2025	2295	0	0	0	0	0	0	0	0	0
6	4/22/2025	2364.3	69.3	8.5	1200	50	80	30	1	40	1000
7	4/23/2025	2425.5	61.2	9	1200	46	73.6	20	1	14.3	1000
8	4/24/2025	2501	75.5				0				
9	4/25/2025	2560	59				0				
10	4/26/2025	2601	41	8.5	1200	40	64	20	1	15	1000
11	4/27/2025	2610.2	9.2	8	1200	40	64	20	1	15	1000
12	4/28/2025	2619.5	9.3	8.5	1400	33	52.8	6.8	1	16	1100
13	4/29/2025	2665.4	45.9	8.8	1200	22	35.2	8	1	16	1000
14	4/30/2025	2718.3	52.9	8.8	1200	22	35.2	8	1	16	1400
15	5/1/2025	2781.8	63.5	8.8	1800	32	51.2	8	1	16	1500
16	5/2/2025	2817	35.2	8.9	1800	32	51.2	8	1	16	1500
17	5/3/2025	2864	47	8.9	1700	32	51.2	8	1	16	1400
18	5/4/2025	2884	20	8.9	1500	33	52.8	8	1	16	1300

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				45482	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
19	5/5/2025	2884	0	8.9	1500	33	52.8	8	1	16	1300
20	5/6/2025	2912	28	8.8	1600	34	54.4	8	1	16	1400
21	5/7/2025	2951	39	8.9	1700	35	56	8	1	18	1500
22	5/8/2025	2979.3	28.3	8.7	1600	34	54.4	8	1	19	1400
23	5/9/2025	2979.3	0	8.2	1600	34	54.4	8	1	19	1400
24	5/10/2025	3012	32.7	8.8	1400	34	54.4	8	1	19	1200
25	5/11/2025	3065	53	8.8	1600	42	67.2	8	1	19	1400
26	5/12/2025	3151.3	86.3	7.5	1600	49	78.4	9	1	22	1400
27	5/13/2025	3299	147.7	8	1000	48	76.8	10	1	22	840
28	5/14/2025	3304	5	8	8000	45	72	7	2	30	650
29	5/15/2025	3335	31	8	900	40	64	9	2	40	650
30	5/16/2025	3401	66	8	1100	45	72	11	1	35	800
31	5/17/2025	3450	49	8	1100	45	72	11	1	35	800
32	5/18/2025	3450	0	8	1100	45	72	11	1	35	800
33	5/19/2025	3573	123	8	1100	45	72	11	1	35	800
34	5/20/2025	3594	21	8	1100	45	72	11	1	35	800

Table 12-4: AZNS-075-ST1 De-Completion Section Dewatering Analysis Table

12.1.3 Chemical

Chemical															
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg	
4	4/20/2025	0	0	0	0	0	0	0	0	100	100	25	25	0	0
5	4/21/2025	0	0	0	0	0	0	0	0	0	100	0	25	0	0
6	4/22/2025	0	0	0	0	0	0	0	0	0	100	0	25	0	0
7	4/23/2025	0	0	0	0	0	0	0	0	0	100	0	25	0	0
8	4/24/2025	0	0	0	0	0	0	0	0	0	100	0	25	0	0
9	4/25/2025	0	0	0	0	0	0	0	0	0	100	0	25	0	0
10	4/26/2025	0	0	0	0	0	0	0	0	75	175	0	25	25	25
11	4/27/2025	0	0	0	0	0	0	0	0	0	175	0	25	0	25
12	4/28/2025	0	0	0	0	0	0	0	0	75	250	25	50	25	50
13	4/29/2025	0	0	0	0	0	0	0	0	50	300	12.5	62.5	12.5	62.5
14	4/30/2025	0	0	0	0	0	0	0	0	50	350	12.5	75	12.5	75
15	5/1/2025	0	0	0	0	0	0	3	3	50	400	12.5	87.5	0	75
16	5/2/2025	0	0	0	0	0	0	3	6	50	450	12.5	100	0	75
17	5/3/2025	0	0	0	0	0	0	3	9	50	500	25	125	0	75
18	5/4/2025	0	0	0	0	0	0	3	12	50	550	25	150	0	75

Chemical															
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg	
19	5/5/2025	0	0	0	0	0	0	0	12	50	600	25	175	12.5	87.5
20	5/6/2025	0	0	0	0	0	0	0	12	50	650	25	200	12.5	100
21	5/7/2025	0	0	0	0	0	0	0	12	50	700	25	225	12.5	112.5
22	5/8/2025	0	0	0	0	0	0	0	12	50	750	25	250	12.5	125
23	5/9/2025	0	0	0	0	0	0	0	12	50	800	25	275	12.5	137.5
24	5/10/2025	0	0	0	0	0	0	0	12	75	875	50	325	12.5	150
25	5/11/2025	0	0	0	0	0	0	0	12	50	925	25	350	12.5	162.5
26	5/12/2025	0	0	0	0	0	0	0	12	75	1000	25	375	12.5	175
27	5/13/2025	0	0	10	10	0	0	2	14	50	1050	25	400	25	200
28	5/14/2025	0	0	0	10	0	0	2	16	50	1100	0	400	25	225
29	5/15/2025	0	0	0	10	0	0	2	18	50	1150	0	400	25	250
30	5/16/2025	0	0	0	10	0	0	2	20	50	1200	0	400	25	275
31	5/17/2025	0	0	0	10	0	0	2	22	50	1250	0	400	25	300
32	5/18/2025	0	0	0	10	0	0	2	24	50	1300	0	400	25	325
33	5/19/2025	0	0	0	10	0	0	2	26	50	1350	0	400	25	350
34	5/20/2025	0	0	0	10	0	0	0	26	25	1375	0	400	25	375

12.2 8 – 3/8" Hole Section

12.2.1 Operation's Recap

12.2.1.1 Fixation's Operation

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
35	21-May-2025	3594	0	100	100	0	550	0	400
36	22-May-2025	3675	81	60	160	0	550	0	400
37	23-May-2025	3692	17	60	220	0	550	0	400
38	24-May-2025	3692	0	60	280	0	550	0	400
39	25-May-2025	3692	0	60	340	0	550	0	400
40	26-May-2025	3692	0	60	400	0	550	0	400
41	27-May-2025	3692	0	60	460	0	550	0	400
42	28-May-2025	3692	0	60	520	0	550	0	400
43	29-May-2025	3692	0	60	580	0	550	0	400
44	30-May-2025	3692	0	60	640	600	1150	50	450
45	31-May-2025	3692	0	60	700	0	1150	100	550
46	1-Jun-2025	3692	0	60	760	0	1150	50	600
47	2-Jun-2025	3692	0	60	820	0	1150	50	650

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
48	3-Jun-2025	3692	0	60	880	0	1150	0	650
49	4-Jun-2025	3692	0	60	940	0	1150	0	650
50	5-Jun-2025	3692	0	0	940	0	1150	0	650
51	6-Jun-2025	3692	0	0	940	0	1150	0	650
52	7-Jun-2025	3692	0	0	940	0	1150	0	650
53	8-Jun-2025	3692	0	0	940	0	1150	0	650
54	9-Jun-2025	3692	0	0	940	0	1150	0	650
55	10-Jun-2025	3692	0	0	940	0	1150	0	650
56	11-Jun-2025	3692	0	0	940	0	1150	0	650
57	12-Jun-2025	3692	0	0	940	0	1150	0	650
58	13-Jun-2025	3692	0	0	940	0	1150	0	650
59	14-Jun-2025	3692	0	0	940	0	1150	0	650
60	15-Jun-2025	3692	0	0	940	0	1150	0	650
61	16-Jun-2025	3692	0	0	940	0	1150	0	650
62	17-Jun-2025	3692	0	0	940	0	1150	0	650
63	18-Jun-2025	3888	196	2540	3480	2540	3690	190	840

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
64	19-Jun-2025	3888	0		3480		3690	100	940
65	20-Jun-2025	3888	0		3480		3690	100	1040
66	21-Jun-2025	3888	0		3480		3690	100	1140
67	22-Jun-2025	3888	0		3480		3690	100	1240
68	23-Jun-2025	3888	0		3480		3690	100	1340

Table 12-5: AZNS-075-ST1 **8-3/8" Section Solid Handling System**

12.2.1.2 Analysis

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/ NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
35	21-May-2025	3594	0		0	0	0	0
36	22-May-2025	3675	81		0	0	0	0
37	23-May-2025	3692	17		0	0	0	0
38	24-May-2025	3692	0		0	0	0	0
39	25-May-2025	3692	0		0	0	0	0
40	26-May-2025	3692	0		0	0	0	0
41	27-May-2025	3692	0		0	0	0	0
42	28-May-2025	3692	0		0	0	0	0
43	29-May-2025	3692	0		0	0	0	0
44	30-May-2025	3692	0		0.833333333	0.083333328	0	0
45	31-May-2025	3692	0		0	0.075757571	0	0
46	1-Jun-2025	3692	0		0	0.06944444	0	0
47	2-Jun-2025	3692	0		0	0.06410256	0	0
48	3-Jun-2025	3692	0		0	0.05952381	0	0
49	4-Jun-2025	3692	0		0	0.055555556	0	0

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/ NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
50	5-Jun-2025	3692	0		0	0.052083332	0	0
51	6-Jun-2025	3692	0		0	0.049019605	0	0
52	7-Jun-2025	3692	0		0	0.046296295	0	0
53	8-Jun-2025	3692	0		0	0.043859649	0	0
54	9-Jun-2025	3692	0		0	0.041666664	0	0
55	10-Jun-2025	3692	0		0	0.039682537	0	0
56	11-Jun-2025	3692	0		0	0.037878785	0	0
57	12-Jun-2025	3692	0		0	0.036231883	0	0
58	13-Jun-2025	3692	0		0	0.03472222	0	0
59	14-Jun-2025	3692	0		0	0.033333331	0	0
60	15-Jun-2025	3692	0		0	0.03205128	0	0
61	16-Jun-2025	3692	0		0	0.030864196	0	0
62	17-Jun-2025	3692	0		0	0.029761905	0	0
63	18-Jun-2025	3888	196		1.968503937	0.096615076	0.066929134	0.002307901
64	19-Jun-2025	3888	0		0	0.09339457	0	0.002230971
65	20-Jun-2025	3888	0		0	0.090381846	0	0.002159004

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/ NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
66	21-Jun-2025	3888	0		0	0.087557413	0	0.002091535
67	22-Jun-2025	3888	0		0	0.084904157	0	0.002028156
68	23-Jun-2025	3888	0		0	0.082406975	0	0.001968504

Table 12-6: AZNS-075-ST1 8-3/8" Section Fixation Analysis Table

12.2.2 Dewatering's Recap

12.2.2.1 Dewatering

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
35	21-May-2025	3594	0	0	11050	400	9950	350	7782	0	1758	0	205
36	22-May-2025	3675	81	0	11050	400	10350	300	8082	65	1823	0	205
37	23-May-2025	3692	17	0	11050	400	10750	250	8332	75	1898	0	205
38	24-May-2025	3692	0	0	11050	400	11150	400	8732	0	1898	0	205
39	25-May-2025	3692	0	0	11050	400	11550	350	9082	38	1936	0	205
40	26-May-2025	3692	0	0	11050	400	11950	350	9432	0	1936	0	205
41	27-May-2025	3692	0	1867	12917	400	12350	350	9782	0	1936	0	205
42	28-May-2025	3692	0	1867	14784	400	12750	350	10132	0	1936	0	205
43	29-May-2025	3692	0	200	14984	400	13150	350	10482	0	1936	0	205
44	30-May-2025	3692	0	200	15184	0	13150	0	10482	0	1936	127	332
45	31-May-2025	3692	0	200	15384	400	13550	350	10832	0	1936	0	332

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
46	1-Jun-2025	3692	0	300	15684	400	13950	390	11222	10	1946	0	332
47	2-Jun-2025	3692	0	300	15984	400	14350	350	11572	50	1996	0	332
48	3-Jun-2025	3692	0	300	16284	400	14750	350	11922	0	1996	300	632
49	4-Jun-2025	3692	0	150	16434	400	15150	100	12022	100	2096	50	682
50	5-Jun-2025	3692	0	150	16584	400	15550	200	12222	0	2096	50	732
51	6-Jun-2025	3692	0	150	16734	400	15950	250	12472	0	2096	100	832
52	7-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
53	8-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
54	9-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
55	10-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
56	11-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
57	12-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
58	13-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
59	14-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
60	15-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
61	16-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
62	17-Jun-2025	3692	0	0	16734		15950		12472	0	2096		832
63	18-Jun-2025	3888	196	4370	21104	2800	18750	1550	14022	250	2346	1150	1982
64	19-Jun-2025	3888	0	200	21304		18750	150	14172		2346		1982
65	20-Jun-2025	3888	0	0	21304		18750	150	14322		2346		1982
66	21-Jun-2025	3888	0	0	21304	300	19050	300	14622		2346		1982
67	22-Jun-2025	3888	0	0	21304	300	19350	300	14922		2346		1982
68	23-Jun-2025	3888	0	0	21304	300	19650	300	15222		2346		1982

Table 12-7: AZNS-075-ST1 8-3/8" Section Dewatering Data Table

12.2.2.2 Dewatering Analysis

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
35	21-May-2025	3594	0	8	1000	50	80	2.714285714	1	30	800
36	22-May-2025	3675	81	8	1000	50	80	2.714285714	1	30	800
37	23-May-2025	3692	17	8	1200	45	72	2.714285714	1	30	800
38	24-May-2025	3692	0	8	1000	50	80	2.714285714	2	40	800
39	25-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
40	26-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
41	27-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
42	28-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
43	29-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
44	30-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
45	31-May-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
46	1-Jun-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
47	2-Jun-2025	3692	0	8	1200	45	72	2.714285714	2	35	800
48	3-Jun-2025	3692	0	8.2	1200	43	68.8	2.714285714	2	34	800
49	4-Jun-2025	3692	0	8	1250	46	73.6	2.714285714	1	34	850

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
50	5-Jun-2025	3692	0	8	1300	46	73.6	7	1	35	900
51	6-Jun-2025	3692	0	8	1500	49	78.4	<1	1	35	1300
52	7-Jun-2025	3692	0	8			0				1300
53	8-Jun-2025	3692	0	8			0				1300
54	9-Jun-2025	3692	0	8			0				1300
55	10-Jun-2025	3692	0	8			0				1300
56	11-Jun-2025	3692	0	8			0				1300
57	12-Jun-2025	3692	0	8			0				1300
58	13-Jun-2025	3692	0	8			0				1300
59	14-Jun-2025	3692	0	8			0				1300
60	15-Jun-2025	3692	0	8			0				1300
61	16-Jun-2025	3692	0	8			0				1300
62	17-Jun-2025	3692	0	8			0				1300
63	18-Jun-2025	3888	196	8	1200	56	89.6	<1	1	37	1300
64	19-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
65	20-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
66	21-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
67	22-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
68	23-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300

Table 12-8: AZNS-075-ST1 8-3/8" Section Dewatering Analysis Table

12.2.3 Chemical

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
35	21-May-2025	0	0	0	10	0	0	0	26	25	1400	0	400	0	0	25	400
36	22-May-2025	0	0	0	10	0	0	0	26	25	1425	0	400	0	0	25	425
37	23-May-2025	0	0	0	10	0	0	0	26	25	1450	0	400	0	0	25	450
38	24-May-2025	0	0	0	10	0	0	2	28	50	1500	0	400	0	0	25	475
39	25-May-2025	0	0	0	10	0	0		28	25	1525	0	400	0	0	25	500
40	26-May-2025	0	0	0	10	0	0		28	25	1550	0	400	0	0	25	525
41	27-May-2025	0	0	0	10	0	0	0	28	25	1575	0	400	0	0	25	550
42	28-May-2025	0	0	0	10	0	0	0	28	25	1600	0	400	0	0	25	575
43	29-May-2025	0	0	0	10	0	0	0	28	25	1625	0	400	0	0	25	600
44	30-May-2025	500	500	0	10	0	0	0	28	0	1625	0	400	0	0	0	600
45	31-May-2025	0	500	0	10	0	0	2	30	25	1650	0	400	0	0	25	625

46	1-Jun-2025	0	500	0	10	0	0	3	33	25	1675	0	400	0	0	25	650
47	2-Jun-2025	0	500	0	10	0	0	3	36	25	1700	0	400	0	0	25	675
48	3-Jun-2025	0	500	0	10	0	0	3	39	25	1725	0	400	0	0	25	700
49	4-Jun-2025	0	500	0	10	0	0	3	42	25	1750	0	400	0	0	25	725
50	5-Jun-2025	0	500	0	10	25	25	3	45	0	1750	0	400	0	0	25	750
51	6-Jun-2025	0	500	0	10	25	50	3	48	0	1750	0	400	0	0	25	775
52	7-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
53	8-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
54	9-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
55	10-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
56	11-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
57	12-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
58	13-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
59	14-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
60	15-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
61	16-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
62	17-Jun-2025	0	500	0	10	0	50	0	48	0	1750	0	400	0	0	0	775
63	18-Jun-2025	5000	5500	170	180	175	225	18	66	0	1750	0	400	0	0	75	850
64	19-Jun-2025		5500		180		225		66		1750		400		0		850

65	20-Jun-2025		5500		180		225		66		1750		400		0		850
66	21-Jun-2025		5500		180		225		66		1750		400		0		850
67	22-Jun-2025		5500		180		225		66		1750		400		0		850
68	23-Jun-2025		5500		180		225		66		1750		400		0		850

12.3 6 – 1/8" Hole Section

12.3.1 Operation's Recap

12.3.1.1 Fixation's Operation

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
69	24-Jun-2025	3888	0				3690	100	1440
70	25-Jun-2025	3888	0		0		3690	100	1540
71	26-Jun-2025	3888	0		0		3690	100	1640
72	27-Jun-2025	3888	0		0		3690	100	1740
73	28-Jun-2025	3888	0		0		3690	50	1790
74	29-Jun-2025	3888	0		0		3690	0	1790
75	30-Jun-2025	3888	0		0		3690	0	1790
76	1-Jul-2025	3888	0		0		3690	0	1790
77	2-Jul-2025	3888	0		0	540	4230	70	1860
78	3-Jul-2025	3888	0		0	0	4230	0	1860
79	4-Jul-2025	3888	0		0	0	4230	0	1860
80	5-Jul-2025	3888	0		0	0	4230	0	1860
81	6-Jul-2025	3888	0		0	0	4230	0	1860

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
82	7-Jul-2025	3888	0		0	0	4230	70	1930
83	8-Jul-2025	3888	0		0	0	4230	150	2080
84	9-Jul-2025	3888	0	900	900	900	5130	150	2230
85	10-Jul-2025	3888	0	344	1244	344	5474		2230
86	11-Jul-2025	3888	0		1244		5474		2230

Table 12-9: AZNS-075-ST1 **6-1/8" Section Solid Handling System**

12.3.1.2 Analysis

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
69	24-Jun-2025	3888	0		0	0	0	0
70	25-Jun-2025	3888	0		0	0	0	0
71	26-Jun-2025	3888	0		0	0	0	0
72	27-Jun-2025	3888	0		0	0	0	0
73	28-Jun-2025	3888	0		0	0	0	0
74	29-Jun-2025	3888	0		0	0	0	0
75	30-Jun-2025	3888	0		0	0	0	0
76	1-Jul-2025	3888	0		0	0	0	0
77	2-Jul-2025	3888	0		0.925925926	0.102880657	0.037037037	0.004115226
78	3-Jul-2025	3888	0		0	0.09259259	0	0.003703704
79	4-Jul-2025	3888	0		0	0.08417508	0	0.003367003
80	5-Jul-2025	3888	0		0	0.077160493	0	0.00308642
81	6-Jul-2025	3888	0		0	0.071225069	0	0.002849003
82	7-Jul-2025	3888	0		0	0.066137567	0	0.002645503
83	8-Jul-2025	3888	0		0	0.061728396	0	0.002469136

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
84	9-Jul-2025	3888	0		1.111111111	0.127314821	0.022222222	0.003703704
85	10-Jul-2025	3888	0		1.453488372	0.205325022	0	0.003485839
86	11-Jul-2025	3888	0		0	0.193918079	0	0.003292181

Table 12-10: AZNS-075-ST1 6-1/8” Section Fixation Analysis Table

12.3.2 Dewatering's Recap

12.3.2.1 Dewatering

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
69	24-Jun-2025	3888	0	100	21404	300	19950	300	15522		2346		1982
70	25-Jun-2025	3888	0	100	21504	300	20250	300	15822		2346		1982
71	26-Jun-2025	3888	0	100	21604	300	20550	300	16122		2346		1982
72	27-Jun-2025	3888	0	100	21704	300	20850	300	16422		2346		1982
73	28-Jun-2025	3888	0	100	21804	400	21250		16422		2346		1982
74	29-Jun-2025	3888	0	100	21904	0	21250	350	16772		2346		1982
75	30-Jun-2025	3888	0	100	22004	400	21650	0	16772	0	2346	0	1982
76	1-Jul-2025	3888	0	100	22104		21650	0	16772	0	2346	0	1982
77	2-Jul-2025	3888	0	100	22204		21650	200	16972	0	2346	0	1982
78	3-Jul-2025	3888	0	500	22704		21650	200	17172	0	2346	0	1982

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
79	4-Jul-2025	3888	0	500	23204	400	22050	0	17172	0	2346	0	1982
80	5-Jul-2025	3888	0	500	23704	0	22050	100	17272	0	2346	0	1982
81	6-Jul-2025	3888	0	300	24004	400	22450	345	17617	55	2401	0	1982
82	7-Jul-2025	3888	0	300	24304	0	22450	0	17617	0	2401	0	1982
83	8-Jul-2025	3888	0	300	24604	0	22450	200	17817	0	2401	0	1982
84	9-Jul-2025	3888	0	300	24904	0	22450	150	17967	0	2401	0	1982
85	10-Jul-2025	3888	0	300	25204	0	22450	100	18067	0	2401	0	1982
86	11-Jul-2025	3888	0	300	25504	450	22900	0	18067	0	2401	0	1982

Table 12-11: AZNS-075-ST1 6-1/8” Section Dewatering Data Table

12.3.2.2 Dewatering Analysis

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
69	24-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
70	25-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
71	26-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
72	27-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
73	28-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
74	29-Jun-2025	3888	0	8	1200	56	89.6	<1	1	37	1300
75	30-Jun-2025	3888	0	8	1600	73	116.8	<1	1	37	1400
76	1-Jul-2025	3888	0	8	1600	73	116.8	<1	1	37	1400
77	2-Jul-2025	3888	0	8	1600	73	116.8	<1	1	37	1400
78	3-Jul-2025	3888	0	8	1600	73	116.8	<1	1	37	1400
79	4-Jul-2025	3888	0	8	1600	73	116.8	<1	1	37	1400
80	5-Jul-2025	3888	0	8	1500	73	116.8	<1	1	37	1300
81	6-Jul-2025	3888	0	8	1300	73	116.8	<1	1	37	1140
82	7-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
83	8-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
84	9-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
85	10-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
86	11-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800

Table 12-12: AZNS-075-ST1 6-1/8" Section Dewatering Analysis Table

12.3.1 Chemical

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
69	24-Jun-2025		5500		180		225		66		1750		400		0		850
70	25-Jun-2025		5500		180		225		66		1750		400		0		850
71	26-Jun-2025		5500		180		225		66		1750		400		0		850
72	27-Jun-2025		5500		180		225		66		1750		400		0		850
73	28-Jun-2025		5500		180		225		66		1750		400		0		850
74	29-Jun-2025		5500		180		225		66		1750		400		0		850
75	30-Jun-2025		5500		180		225	3	69		1750		400		0		850
76	1-Jul-2025		5500		180		225		69		1750		400		0		850
77	2-Jul-2025	500	6000	20	200		225		69		1750		400		0		850
78	3-Jul-2025		6000		200		225		69		1750		400		0		850
79	4-Jul-2025		6000		200		225	3	72		1750		400		0		850
80	5-Jul-2025		6000		200		225		72		1750		400		0		850

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
81	6-Jul-2025		6000		200		225	5	77		1750		400		0		850
82	7-Jul-2025		6000		200		225		77		1750		400		0		850
83	8-Jul-2025		6000		200		225		77		1750		400		0		850
84	9-Jul-2025	1000	7000	20	220		225		77		1750		400		0		850
85	10-Jul-2025	500	7500		220		225		77		1750		400		0		850
86	11-Jul-2025		7500		220		225	3	80		1750		400		0		850

12.4 Completion Section

12.4.1 Operation's Recap

12.4.1.1 Fixation's Operation

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
87	12-Jul-2025	3888	0				5474	70	2300
88	13-Jul-2025	3888	0		0		5474	70	2370
89	14-Jul-2025	3888	0		0		5474	0	2370
90	15-Jul-2025	3888	0		0		5474	0	2370
91	16-Jul-2025	3888	0		0		5474	0	2370
92	17-Jul-2025	3888	0		0		5474	0	2370
93	18-Jul-2025	3888	0		0		5474	0	2370
94	19-Jul-2025	3888	0		0		5474	0	2370
95	20-Jul-2025	3888	0		0		5474	0	2370
96	21-Jul-2025	3888	0	190	190	190	5664	50	2420
97	22-Jul-2025	3888	0	90	280	0	5664	0	2420
98	23-Jul-2025	3888	0	0	280	0	5664	2750	5170
99	24-Jul-2025	3888	0	0	280	0	5664	0	5170
100	25-Jul-2025	3888	0	0	280	0	5664	0	5170

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
101	26-Jul-2025	3888	0	0	280	0	5664	0	5170
102	27-Jul-2025	3888	0	0	280	0	5664	0	5170
103	28-Jul-2025	3888	0	0	280	0	5664	0	5170
104	29-Jul-2025	3888	0	0	280	0	5664	70	5240
105	30-Jul-2025	3888	0	0	280	0	5664	70	5310
106	31-Jul-2025	3888	0	0	280	0	5664	70	5380
107	1-Aug-2025	3888	0	0	280	0	5664	0	5380
108	2-Aug-2025	3888	0	0	280	0	5664	70	5450
109	3-Aug-2025	3888	0	0	280	0	5664	70	5520
110	4-Aug-2025	3888	0	0	280	0	5664	70	5590
111	5-Aug-2025	3888	0	0	280	0	5664	0	5590
112	6-Aug-2025	3888	0	0	280	0	5664	0	5590
113	7-Aug-2025	3888	0	0	280	0	5664	0	5590
114	8-Aug-2025	3888	0	0	280	0	5664	0	5590
115	9-Aug-2025	3888	0	0	280	0	5664	0	5590
116	10-Aug-2025	3888	0	150	430	150	5814	50	5640
117	11-Aug-2025	3888	0	0	430	0	5814	50	5690

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
118	12-Aug-2025	3888	0	0	430	0	5814	50	5740
119	13-Aug-2025	3888	0	0	430	0	5814	50	5790
120	14-Aug-2025	3888	0	0	430	0	5814	0	5790
121	15-Aug-2025	3888	0	0	430	0	5814	0	5790
122	16-Aug-2025	3888	0	0	430	0	5814	0	5790
123	17-Aug-2025	3888	0	0	430	0	5814	0	5790
124	18-Aug-2025	3888	0	0	430	0	5814	0	5790
125	19-Aug-2025	3888	0	500	930	500	6314	0	5790
126	20-Aug-2025	3888	0	500	1430	0	6314	0	5790
127	21-Aug-2025	3888	0	500	1930	0	6314	50	5840
128	22-Aug-2025	3888	0	500	2430	0	6314	50	5890
129	23-Aug-2025	3888	0	500	2930	0	6314	0	5890
130	24-Aug-2025	3888	0	0	2930	0	6314	0	5890
131	25-Aug-2025	3888	0	400	3330	0	6314	100	5990
132	26-Aug-2025	3888	0	400	3730	240	6554	0	5990
133	27-Aug-2025	3888	0	350	4080	300	6854	50	6040
134	28-Aug-2025	3888	0	300	4380	200	7054	50	6090

Fixation									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Cutttings		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
135	29-Aug-2025	3888	0	200	4580	100	7154	50	6140
136	30-Aug-2025	3888	0	100	4680	0	7154	100	6240
137	31-Aug-2025	3888	0	100	4780	100	7254	0	6240
138	1-Sep-2025	3888	0	757	5537	758	8012	0	6240
139	2-Sep-2025	3888	0	0	5537	0	8012	0	6240
140	3-Sep-2025	3888	0	800	6337	1500	9512	0	6240
141	4-Sep-2025	3888	0	700	7037	699	10211	400	6640
142	5-Sep-2025	3888	0	600	7637	0	10211	100	6740
143	6-Sep-2025	3888	0	0	7637	0	10211	0	6740
144	7-Sep-2025	3888	0	0	7637	0	10211	100	6840
145	8-Sep-2025	3888	0	0	7637	0	10211	100	6940
146	9-Sep-2025	3888	0	0	7637	0	10211	100	7040
147	10-Sep-2025	3888	0	0	7637		10211		7040
148	11-Sep-2025	3888	0	0	7637	0	10211	400	7440
149	12-Sep-2025	3888	0	101.1	7738.1	3001.1	13212.1	400	7840
150	13-Sep-2025	3888	0		7738.1		13212.1	400	8240
151	14-Sep-2025	3888	0		7738.1		13212.1	400	8640

Table 12-13: AZNS-075-ST1 Completion Section Solid Handling System

12.4.1.2 Analysis

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
87	12-Jul-2025	3888	0		0.00	0.00	0	0
88	13-Jul-2025	3888	0		0.00	0.00	0	0
89	14-Jul-2025	3888	0		0.00	0.00	0	0
90	15-Jul-2025	3888	0		0.00	0.00	0	0
91	16-Jul-2025	3888	0		0.00	0.00	0	0
92	17-Jul-2025	3888	0		0.00	0.00	0	0
93	18-Jul-2025	3888	0		0.00	0.00	0	0
94	19-Jul-2025	3888	0		0.00	0.00	0	0
95	20-Jul-2025	3888	0		0.00	0.00	0	0
96	21-Jul-2025	3888	0	pass	1.05	0.11	0	0
97	22-Jul-2025	3888	0	pass	0.00	0.10	0	0
98	23-Jul-2025	3888	0	pass	0.00	0.09	0	0
99	24-Jul-2025	3888	0	pass	0.00	0.08	0	0
100	25-Jul-2025	3888	0	pass	0.00	0.08	0	0
101	26-Jul-2025	3888	0	pass	0.00	0.07	0	0
102	27-Jul-2025	3888	0	pass	0.00	0.07	0	0
103	28-Jul-2025	3888	0	pass	0.00	0.06	0	0

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
104	29-Jul-2025	3888	0	pass	0.00	0.06	0	0
105	30-Jul-2025	3888	0	pass	0.00	0.06	0	0
106	31-Jul-2025	3888	0	pass	0.00	0.05	0	0
107	1-Aug-2025	3888	0	pass	0.00	0.05	0	0
108	2-Aug-2025	3888	0	pass	0.00	0.05	0	0
109	3-Aug-2025	3888	0	pass	0.00	0.05	0	0
110	4-Aug-2025	3888	0	pass	0.00	0.04	0	0
111	5-Aug-2025	3888	0	pass	0.00	0.04	0	0
112	6-Aug-2025	3888	0	pass	0.00	0.04	0	0
113	7-Aug-2025	3888	0	pass	0.00	0.04	0	0
114	8-Aug-2025	3888	0	pass	0.00	0.04	0	0
115	9-Aug-2025	3888	0	pass	0.00	0.04	0	0
116	10-Aug-2025	3888	0	pass	0.00	0.04	0	0
117	11-Aug-2025	3888	0	pass	0.00	0.03	0	0
118	12-Aug-2025	3888	0	pass	0.00	0.03	0	0
119	13-Aug-2025	3888	0	pass	0.00	0.03	0	0
120	14-Aug-2025	3888	0	pass	0.00	0.03	0	0
121	15-Aug-2025	3888	0	pass	0.00	0.03	0	0

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
122	16-Aug-2025	3888	0	pass	0.00	0.03	0	0
123	17-Aug-2025	3888	0	pass	0.00	0.03	0	0
124	18-Aug-2025	3888	0	pass	0.00	0.03	0	0
125	19-Aug-2025	3888	0	pass	0.40	0.04	0	0
126	20-Aug-2025	3888	0	pass	0.00	0.04	0	0
127	21-Aug-2025	3888	0	pass	0.00	0.04	0	0
128	22-Aug-2025	3888	0	pass	0.00	0.03	0	0
129	23-Aug-2025	3888	0	pass	0.00	0.03	0	0
130	24-Aug-2025	3888	0	pass	0.00	0.03	0	0
131	25-Aug-2025	3888	0	pass	0.00	0.03	0	0
132	26-Aug-2025	3888	0	pass	0.00	0.03	0	0
133	27-Aug-2025	3888	0	pass	0.00	0.03	0	0
134	28-Aug-2025	3888	0	pass	0.00	0.03	0	0
135	29-Aug-2025	3888	0	pass	0.00	0.03	0	0
136	30-Aug-2025	3888	0	pass	0.00	0.03	0	0
137	31-Aug-2025	3888	0	pass	0.00	0.03	0	0
138	1-Sep-2025	3888	0	pass	0.40	0.04	0	0
139	2-Sep-2025	3888	0	pass	0.00	0.03	0	0

Fixation Analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		Sodsil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/bbl	kg/bbl	kg/bbl	kg/bbl
140	3-Sep-2025	3888	0	pass	2.67	0.08	0	0
141	4-Sep-2025	3888	0	pass	0.00	0.08	0	0
142	5-Sep-2025	3888	0	pass	0.00	0.08	0	0
143	6-Sep-2025	3888	0	pass	0.00	0.08	0	0
144	7-Sep-2025	3888	0	pass	0.00	0.08	0	0
145	8-Sep-2025	3888	0	pass	0.00	0.08	0	0
146	9-Sep-2025	3888	0	pass	0.00	0.08	0	0
147	10-Sep-2025	3888	0	pass	0.00	0.07	0	0
148	11-Sep-2025	3888	0	pass	0.00	0.07	0	0
149	12-Sep-2025	3888	0	pass	1.50	0.10	0	0
150	13-Sep-2025	3888	0	pass	0.00	0.09	0	0
151	14-Sep-2025	3888	0	pass	0.00	0.09	0	0

Table 12-14: AZNS-075-ST1 Completion Section Fixation Analysis Table

12.4.2 Dewatering's Recap

12.4.2.1 Dewatering

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
87	12-Jul-2025	3888	0	300	25804	0	22900	250	18317	0	2401	0	1982
88	13-Jul-2025	3888	0	300	26104	0	22900	200	18517	0	2401	0	1982
89	14-Jul-2025	3888	0	20	26124	0	22900	0	18517	0	2401	0	1982
90	15-Jul-2025	3888	0	20	26144	0	22900	0	18517	0	2401	0	1982
91	16-Jul-2025	3888	0	20	26164	400	23300	0	18517	0	2401	0	1982
92	17-Jul-2025	3888	0	20	26184	0	23300	100	18617	0	2401	0	1982

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
93	18-Jul-2025	3888	0	80	26264	0	23300	100	18717	0	2401	0	1982
94	19-Jul-2025	3888	0	5	26269	400	23700	0	18717	0	2401	200	2182
95	20-Jul-2025	3888	0	5	26274	400	24100	0	18717	0	2401	350	2532
96	21-Jul-2025	3888	0	5	26279	400	24500	0	18717	0	2401	400	2932
97	22-Jul-2025	3888	0	5	26284	0	24500	300	19017	25	2426	0	2932
98	23-Jul-2025	3888	0	5	26289	0	24500	0	19017	0	2426	0	2932
99	24-Jul-2025	3888	0	5	26294	0	24500	0	19017	0	2426	0	2932
100	25-Jul-2025	3888	0	5	26299	0	24500	0	19017	0	2426	0	2932

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
101	26-Jul-2025	3888	0	5	26304	0	24500	0	19017	0	2426	20	2952
102	27-Jul-2025	3888	0	5	26309	0	24500	0	19017	0	2426	20	2972
103	28-Jul-2025	3888	0	100	26409	350	24850	0	19017	0	2426	20	2992
104	29-Jul-2025	3888	0	100	26509	0	24850	200	19217	0	2426	20	3012
105	30-Jul-2025	3888	0	100	26609	400	25250	495	19712	0	2426	100	3112
106	31-Jul-2025	3888	0	100	26709	400	25650	0	19712	0	2426	100	3212
107	1-Aug-2025	3888	0	15	26724	0	25650	0	19712	0	2426	0	3212
108	2-Aug-2025	3888	0	20	26744	0	25650	0	19712	0	2426	0	3212

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
109	3-Aug-2025	3888	0	30	26774	0	25650	0	19712	0	2426	0	3212
110	4-Aug-2025	3888	0	300	27074	0	25650	300	20012	0	2426	0	3212
111	5-Aug-2025	3888	0	150	27224	400	26050	100	20112	0	2426	0	3212
112	6-Aug-2025	3888	0	50	27274		26050	50	20162	0	2426	0	3212
113	7-Aug-2025	3888	0	50	27324		26050	50	20212	0	2426	0	3212
114	8-Aug-2025	3888	0	150	27474		26050	0	20212	0	2426	0	3212
115	9-Aug-2025	3888	0	100	27574		26050	0	20212	0	2426	0	3212
116	10-Aug-2025	3888	0	100	27674		26050	0	20212	0	2426	0	3212

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
117	11-Aug-2025	3888	0	100	27774		26050	0	20212	0	2426	0	3212
118	12-Aug-2025	3888	0	100	27874		26050	0	20212	0	2426	0	3212
119	13-Aug-2025	3888	0	100	27974		26050	0	20212	0	2426	0	3212
120	14-Aug-2025	3888	0	100	28074		26050	0	20212	0	2426	0	3212
121	15-Aug-2025	3888	0	100	28174	0	26050	150	20362	0	2426	0	3212
122	16-Aug-2025	3888	0	50	28224	0	26050	50	20412	0	2426	0	3212
123	17-Aug-2025	3888	0	10	28234	0	26050	0	20412	0	2426	0	3212
124	18-Aug-2025	3888	0	10	28244	0	26050	0	20412	0	2426	0	3212

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
125	19-Aug-2025	3888	0	10	28254	400	26450	0	20412	0	2426	0	3212
126	20-Aug-2025	3888	0	10	28264	400	26850	350	20762	0	2426	0	3212
127	21-Aug-2025	3888	0	10	28274	0	26850	0	20762	0	2426	0	3212
128	22-Aug-2025	3888	0	10	28284	0	26850	0	20762	0	2426	0	3212
129	23-Aug-2025	3888	0	10	28294	0	26850	0	20762	0	2426	0	3212
130	24-Aug-2025	3888	0	10	28304	0	26850	0	20762	0	2426	250	3462
131	25-Aug-2025	3888	0	10	28314	400	27250	0	20762	0	2426	350	3812
132	26-Aug-2025	3888	0	10	28324	400	27650	0	20762	0	2426	300	4112

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
133	27-Aug-2025	3888	0	10	28334	250	27900	0	20762	0	2426	200	4312
134	28-Aug-2025	3888	0	600	28934	200	28100	0	20762	0	2426	200	4512
135	29-Aug-2025	3888	0	210	29144	250	28350	0	20762	0	2426	200	4712
136	30-Aug-2025	3888	0	510	29654	0	28350	0	20762	0	2426	0	4712
137	31-Aug-2025	3888	0	200	29854	0	28350	0	20762	0	2426	0	4712
138	1-Sep-2025	3888	0	50	29904	0	28350	0	20762	0	2426	0	4712
139	2-Sep-2025	3888	0	50	29954	0	28350	0	20762	0	2426	0	4712
140	3-Sep-2025	3888	0	50	30004	0	28350	0	20762	0	2426	0	4712

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
141	4-Sep-2025	3888	0	50	30054	0	28350	0	20762	0	2426	0	4712
142	5-Sep-2025	3888	0	50	30104	0	28350	0	20762	0	2426	0	4712
143	6-Sep-2025	3888	0	50	30154	0	28350	0	20762	0	2426	0	4712
144	7-Sep-2025	3888	0	50	30204	0	28350	0	20762	0	2426	0	4712
145	8-Sep-2025	3888	0	50	30254	0	28350	0	20762	0	2426	0	4712
146	9-Sep-2025	3888	0	0	30254	0	28350	0	20762	0	2426	0	4712
147	10-Sep-2025	3888	0	0	30254	0	28350	0	20762	0	2426	0	4712
148	11-Sep-2025	3888	0	0	30254	0	28350	0	20762	0	2426	0	4712

Dewatering													
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Used For Mud Made(BBL)		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
149	12-Sep-2025	3888	0	10	30264	0	28350	0	20762	0	2426	0	4712
150	13-Sep-2025	3888	0	10	30274	0	28350	0	20762	0	2426	0	4712
151	14-Sep-2025	3888	0	10	30284	0	28350	0	20762	0	2426	0	4712

Table 12-15: AZNS-075-ST1 Completion Section Dewatering Data Table

12.4.2.2 Dewatering Analysis

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
87	12-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
88	13-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
89	14-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
90	15-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
91	16-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
92	17-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
93	18-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
94	19-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
95	20-Jul-2025	3888	0	8.6	1000	71	113.6	<1	1	37	800
96	21-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
97	22-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
98	23-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
99	24-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
100	25-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
101	26-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
102	27-Jul-2025	3888	0	8.9	1200	60	96	<1	1	37	900
103	28-Jul-2025	3888	0	8.9	1000	60	96	<1	1	37	800
104	29-Jul-2025	3888	0	8.9	1000	60	96	<1	1	37	800

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
105	30-Jul-2025	3888	0	8.9	1000	60	96	<1	1	37	800
106	31-Jul-2025	3888	0	8.9	1300	70	112	<1	1	37	1480
107	1-Aug-2025	3888	0	8.9	1480	70	112	<1	1	37	1300
108	2-Aug-2025	3888	0				0				
109	3-Aug-2025	3888	0				0				
110	4-Aug-2025	3888	0				0				
111	5-Aug-2025	3888	0	9	1000	42	67.2	24	1	44	800
112	6-Aug-2025	3888	0	9	1000	42	67.2	24	1	44	800
113	7-Aug-2025	3888	0	9	1000	42	67.2	24	1	44	800
114	8-Aug-2025	3888	0				0				
115	9-Aug-2025	3888	0				0				
116	10-Aug-2025	3888	0				0				
117	11-Aug-2025	3888	0				0				
118	12-Aug-2025	3888	0				0				
119	13-Aug-2025	3888	0				0				
120	14-Aug-2025	3888	0				0				
121	15-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
122	16-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
123	17-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
124	18-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
125	19-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
126	20-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
127	21-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
128	22-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
129	23-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
130	24-Aug-2025	3888	0	8.5	1000	46	73.6	39	1	43	800
131	25-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
132	26-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
133	27-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
134	28-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
135	29-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
136	30-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
137	31-Aug-2025	3888	0	45846	900	46	73.6	40	1	47	700
138	1-Sep-2025	3888	0	45846	900	46	73.6	40	1	47	700
139	2-Sep-2025	3888	0	45846	900	46	73.6	40	1	47	700
140	3-Sep-2025	3888	0	45846	900	46	73.6	40	1	47	700
141	4-Sep-2025	3888	0	45846	900	46	73.6	40	1	47	700
142	5-Sep-2025	3888	0	45846	900	46	73.6	40	1	47	700
143	6-Sep-2025	3888	0				0				
144	7-Sep-2025	3888	0				0				

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	AL	Sulfate	Ca
				(7-9)	<800	<50	<80	<50	<3	<50	<600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
145	8-Sep-2025	3888	0				0				
146	9-Sep-2025	3888	0				0				
147	10-Sep-2025	3888	0				0				
148	11-Sep-2025	3888	0				0				
149	12-Sep-2025	3888	0				0				
150	13-Sep-2025	3888	0				0				
151	14-Sep-2025	3888	0				0				

Table 12-16: AZNS-075-ST1 Completion Section Dewatering Analysis Table

12.4.1 Chemical

Chemical																
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
87	12-Jul-2025		7500		220		225		80		1750		400		0		850
88	13-Jul-2025		7500		220		225		80		1750		400		0		850
89	14-Jul-2025		7500		220		225		80		1750		400		0		850
90	15-Jul-2025		7500		220		225		80		1750		400		0		850
91	16-Jul-2025		7500		220		225		80		1750		400		0		850
92	17-Jul-2025		7500		220		225		80		1750		400		0		850
93	18-Jul-2025		7500		220		225		80		1750		400		0		850
94	19-Jul-2025		7500		220		225		80		1750		400		0		850

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
95	20-Jul-2025		7500		220		225		80		1750		400		0		850
96	21-Jul-2025	200	7700		220		225		80		1750		400		0		850
97	22-Jul-2025		7700		220		225		80		1750		400		0		850
98	23-Jul-2025		7700		220		225		80		1750		400		0		850
99	24-Jul-2025		7700		220		225		80		1750		400		0		850
100	25-Jul-2025		7700		220		225		80		1750		400		0		850
101	26-Jul-2025		7700		220		225		80		1750		400		0		850
102	27-Jul-2025		7700		220		225		80		1750		400		0		850
103	28-Jul-2025		7700		220		225	3	83	25	1775	70	470	0	0	25	875

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
104	29-Jul-2025		7700		220		225		83		1775		470		0		875
105	30-Jul-2025		7700		220		225		83		1775		470		0		875
106	31-Jul-2025		7700		220		225	5	88	50	1825	50	520		0	25	900
107	1-Aug-2025		7700		220		225		88		1825		520		0		900
108	2-Aug-2025		7700		220		225		88		1825		520		0		900
109	3-Aug-2025		7700		220		225		88		1825		520		0		900
110	4-Aug-2025		7700		220		225		88		1825		520		0		900
111	5-Aug-2025		7700		220		225	8	96	75	1900	100	620	25	25		900
112	6-Aug-2025		7700		220		225		96		1900		620		25		900

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
113	7-Aug-2025		7700		220		225		96		1900		620		25		900
114	8-Aug-2025		7700		220		225		96		1900		620		25		900
115	9-Aug-2025		7700		220		225		96		1900		620		25		900
116	10-Aug-2025		7700		220		225		96		1900		620		25		900
117	11-Aug-2025		7700		220		225		96		1900		620		25		900
118	12-Aug-2025		7700		220		225		96		1900		620		25		900
119	13-Aug-2025		7700		220		225		96		1900		620		25		900
120	14-Aug-2025		7700		220		225		96		1900		620		25		900
121	15-Aug-2025		7700		220		225		96		1900		620		25		900

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
122	16-Aug-2025		7700		220		225		96		1900		620		25		900
123	17-Aug-2025		7700		220		225		96		1900		620		25		900
124	18-Aug-2025		7700		220		225		96		1900		620		25		900
125	19-Aug-2025	200	7900		220		225	2	98	50	1950		620		25	25	925
126	20-Aug-2025		7900		220		225		98		1950		620		25		925
127	21-Aug-2025		7900		220		225		98		1950		620		25		925
128	22-Aug-2025		7900		220		225		98		1950		620		25		925
129	23-Aug-2025		7900		220		225		98		1950		620		25		925
130	24-Aug-2025		7900		220		225		98		1950		620		25		925

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
131	25-Aug-2025		7900		220		225	2	100	25	1975	25	645		25	25	950
132	26-Aug-2025		7900		220		225		100		1975		645		25		950
133	27-Aug-2025		7900		220		225		100		1975		645		25		950
134	28-Aug-2025		7900		220		225		100		1975		645		25		950
135	29-Aug-2025		7900		220		225		100		1975		645		25		950
136	30-Aug-2025		7900		220		225		100		1975		645		25		950
137	31-Aug-2025		7900		220		225		100		1975		645		25		950
138	1-Sep-2025	300	8200		220		225		100		1975		645		25		950
139	2-Sep-2025		8200		220		225		100		1975		645		25		950

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
140	3-Sep-2025	4000	12200		220		225		100		1975		645		25		950
141	4-Sep-2025		12200		220		225		100		1975		645		25		950
142	5-Sep-2025		12200		220		225		100		1975		645		25		950
143	6-Sep-2025		12200		220		225		100		1975		645		25		950
144	7-Sep-2025		12200		220		225		100		1975		645		25		950
145	8-Sep-2025		12200		220		225		100		1975		645		25		950
146	9-Sep-2025		12200		220		225		100		1975		645		25		950
147	10-Sep-2025		12200		220		225		100		1975		645		25		950
148	11-Sep-2025		12200		220		225		100		1975		645		25		950

Chemical																	
Report No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda Ash		Citric Acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
149	12-Sep-2025	4500	16700		220		225		100		1975		645		25		950
150	13-Sep-2025		16700		220		225		100		1975		645		25		950
151	14-Sep-2025		16700		220		225		100		1975		645		25		950

13. List of Contractors

Item	Service Item	Contractor
1	Drilling Rig, Mobilization and Demobilization the Rig, Rig Move Between Well Pads	OEOC
2	Drilling Fluds and Completion Fluids	VIRA
3	Waste Management	Pars Haffaran Arvand
4	Electrical Logging and Perforation	Sealand
5	Mud Logging	Pars Geo Data
6	Directional Drilling (MWD)	HANA Energy
7	H_2S Monitoring and Control	BONYAN IMAN
8	Casing and Tubing Running	OEOC
9	Cementing	DANA / SPAD
10	Dry Test, DST and RTTS	OEOC
11	Slick Line	OEOC
12	Stimulation (Coiled Tubing and Acidizing and Nitrogen Lifting)	OEOC
13	Surface Well Testing	OEOC
14	Liner Hanger	PARS POOLAD
15	Well Head	OEOC

Table 13-1: AZNS-075-ST1 Contractors Involved

14. Appendix

14.1 DDR Summary

Item	Date	Remark
1	20-Mar-25	Spud the rig. M/U 26 STDs 5" DP. Connected Kill & choke lines to XMT. Install lubricator. Attempt to retrieve TWCV Obs. No TWCV existing. L/D Lubricator.
2	21-Mar-25	R/U Slick Line. Set protection sleeve in TRSSV. RIH gauge ring on SL to SSD depth. RIH with shifting tools and Attempt to Open SSD Several Times, No. Succ. Secure The Well. Waitting For Client Due to not Rec. Explosive Material.
3	22-Mar-25	Cont. Waiting For Client Due to not Rec. Explosive Material. Connected THS side outlet to Ch. Manifold. Apply pressure f/ top kill line in order to check tubing isolation. Circ. With 82 pcf fresh poly mud thru Ch. Manifold while apply 400psi back pressure, Inc. FR to 300 gpm step by step make which indicates that string is wash out. Cont. circ. Till balance MW (82pcf) in/out.
4	23-Mar-25	Cont. Circ and Inc. MW to 84pcf. R/U SL. Retrieve protection sleeve. Close TRSSV. Install TWCV. N/D XMT. N/U 13-5/8" 10k BOP Stack is in Progress.
5	24-Mar-25	N/U 13-5/8" 10k BOP Stack is in Progress.
6	25-Mar-25	N/U 13-5/8" 10k BOP Stack & Test it in Progress.
7	26-Mar-25	Wait on OEOC to Complete BOP Test While Cont. Fix BOP Leakages & Repair Choke manifold Valves at M.N.
8	27-Mar-25	Wait on OEOC to Complete BOP Test While Cont. Fix BOP Leakages & Repair Choke manifold Valves, Start Retrieving Completion String
9	28-Mar-25	Continue Retrieving Completion String .
10	29-Mar-25	Continue Retrieving Completion String. P/U & M/U 6" B.Bit#1 (Used, Open) + 7" Scraper for Scraper trip to 1093 .
11	30-Mar-25	Continue run 7" & 9-5/8" Scraper to PKR Depth, Circ BTM's up , POOH To 900m, NL.NG.
12	31-Mar-25	POOH to surf, Take Log CBIL-CDR-GR-CCL .

13	1-Apr-25	Take Log CBIL-CDR-GR-CCL. R/D Wireline logging Equipment (SEALAND Co.). RIH To 3260m, Circ Mud .
14	2-Apr-25	Perform CMT Plug Job According Program, POOH to 2550m Toll M.N.
15	3-Apr-25	Cont. POOH 3-1/2" & 5" OEDP F/ 2550m to surface, P/U & M/U 6-1/8" D/O BHA and RIH W/ Same BHA followed by 3-1/2" & 5" DPs to 3107m, Took Wt. @ 3107m, Attempt to Cont. RIH W/ Wash Dn, No Success, Start D/O Medium to Hard CMT Inside 7"LNR F/ 3107 to 3156m .
16	4-Apr-25	Cont. D/O CMT F/ 3156 To 3165m, Pump Hi-Vis Pill and Shaker it out to Sweep the Well, POOH 6-1/8" D/O BHA F/ 3165m to Surface, L/D BHA & 6-1/8" T.Cone Bit W/ Same Condition (Dull Grade: 2-2-WT-A-E-I-BT-DST), P/U & M/U 7"DST Tool Srting To 865m, While Pass Rabbit Thru. all Tubular, RIH W/ Speed Control at the request of OEOC DST Supervisor, and F/U Strg W/ Drill water as a Water Cushion at 5-Std intervals, W/ NL-NG .
17	5-Apr-25	Cont. 7"Dry Test Tool Srting To 3059m, R/U & Prepare Surface Line & DST Choke Manifold, Press. Test Same to 3000psi/15min, Ok, Record Up & Dnward Strg Weight, Rotate Strg 6 turn Forward, then Set 7" Dry Test PKR at 3057m, Monitor Open Period For 3Hrs. , No Bubble, While Obs. Annulus Level, Static, S/O Strg Wt. & Rotate 11 Turn Forward & Close Dry Test Assy DCIP Valve, Record Close Period for 6Hrs. is in progress @ M.N.
18	6-Apr-25	Cont. Record Close Period for 6Hrs. , Reverse Circ. Till balance the In/Out Mud, POOH 7" Dry Test Tool String F/ 3059 To 348m On Elvevator W/ Speed Control at the request of OEOC Dry Test supervisor, While Circ. C.W.H, W/ NL-NG
19	7-Apr-25	POOH 7" Dry Test Tool String to surface, B/O & L/D 7" Dry Test Tool String, Read 1st & 2nd Memory Gauge Data 6Hrs. Close-Period Monitoring Results: [Middle B.T: 3264 - 3358psi, BTM B.T: 3280-3374psi], and check Sample Properties between Hydro-spring & DCIP [MW: 80pcf, PH: 11.4 , Cl: 172000, Ca+: 1400 , PV: 8, YP:5], RIH w/ 9-5/8" Dry Test Tool String as 7" L.Lap Dry Test Assy To 2130m On Elvevator W/ Speed Control at the request of OEOC Dry Test supervisor, While Circ. C.W.H, W/ NL-NG
20	8-Apr-25	Cont. RIH W/ 9-5/8" Dry Test Tool String F/ 2130 To 2315m, Maintain open condition for 3 Hrs. , Start @ 03:15, no bubbles observed, Confirm Annulus fluid level is Static during observation, Maintain close condition for 6 Hrs. , Start @ 06:35, Confirm Annulus fluid level is Static during observation, Drop Bar to open Circ. valve, Establish Reverse Circulation, confirm balance mud is observed at the surface, Unset 9-5/8" Dry Test PKR, POOH 7" Dry Test Tool String F/ 2319 To 820m, while Circ. C.W.H, W/ NL-NG.
21	9-Apr-25	POOH 9-5/8" Dry Test Tool String to surface, B/O & L/D 7" Dry Test Tool String, Read 1st & 2nd Memory Gauge Data 6Hrs.

		Close-Period Monitoring Results: [Middle B.T: 1889 - 2189psi, BTM B.T: 1926-2226psi], and check Sample Properties between Hydro-spring & DCIP [PH: 11.2 , Chloride: 170000 mg/lit, Ca++: 1200 mg/lit , Total Hardness: 1360 mg/lit], Perform BOP Test, Ok, RIH W/ 3-1/2" OEDP To 278m, Slip & Cut Drlg Line @ 278m, Resume RIH W/ 3-1/2" & 5" OEDP 278 To 2300m, Conn. TDS & CBU @ 2300m, Meanwhile Prepare Rig Floor and R/U CMT Job Eqp. , W/ NL-NG.
22	10-Apr-25	Cont. CBU @ 2300m, Perform CMT Plug as follow: Pump 15bbl Spacer Ahead (MW: 62.4pcf) + Prepare CMT Solution and Mix W/ CMT Class G and Pump 35bbl CMT Slurry (Slurry Density: 118pcf) + Pump 1.8bbl Spacer Behind (MW: 62.4pcf), POOH 3-1/2" & 5" OEDP F/ 2100m to Surface, P/U & M/U 8-1/2" D/O BHA and RIH to 1989m, due to Windy Wheather, Stop Op. during RIH twice (at 338m & 1989m), W/ NL-NG.
23	11-Apr-25	Due to Windy Weather, Stop Operation @ 1989m, Cont. RIH W/ 8-1/2" D/O BHA F/ 1989 To 2134m, Conn. TDS and RIH W/ 8-1/2" D/O BHA W/ Wash Dn F/ 2134 To 2174m, Held up Strg Wt. & Tag TOC @ 2174m, CBU on TOC, D/O CMT W/ 8-1/2" D/O BHA F/2174 To 2270m, While Reciprocate Strg before each Conn. & Pump Hi-Vis Pill Periodically, W/ NL-NG.
24	12-Apr-25	Pump 40bbl Hi-Vis Pill, CBU & Shaker out Pumped Hi-Vis Pill, POOH 8-1/2" D/O BHA F/ 2270m To surface, P/U & M/U 9-5/8" Scraper BHA and RIH to TOC (2270m), Perform Mud Treatment to optimize Rheological properties and Reduce MW F/ 84 pcf To 80 pcf, Sev. Times Scrape PKR Interval of 9-5/8" Hyd. Whipstock Sys. , POOH 9-5/8" Scraper BHA F/ 2270 To 829m, While Circ. C.W.H, W/ NL-NG.
25	13-Apr-25	POOH 9-5/8" Scraper BHA F/ 829m To Surface On Elevator, B/O 8-1/2" Tri-Cone Bit W/ Same Conditon & rest of BHA, P/U & M/U 9-5/8" Cased-Hole Sidetrack BHA and RIH To 1634m, While Monitor the Well, W/ NL-NG.
26	14-Apr-25	Cont. RIH W/ Cased-Hole Sidetrack BHA and RIH To 2265m, R/U Surface Logging Eqp. ; P/U & Assemble Wire Line Tools as Gyro Tool String and RIH to 2257m (Gyro Sub Depth), Latch Gyro Tool String into Gyro Sub, Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success, POOH 2" Gyro Tool String to Surface; Wait on Receive Gyro Tool String; P/U & Assemble Received Wire Line Tools as Gyro Tool String RIH to 2257m, Latch Gyro Tool String into Gyro Sub, Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success,
27	15-Apr-25	Cont. Attempt to get Gyro data, Attempt Sev. Times W/O Success; POOH 2" Gyro Tool String to Surface; Change Mule Shoe, RIH W/ 2" Gyro Tool String, Latch Gyro Tool String into Gyro Sub, Attempt to get Gyro data, Ok, Set Whipface orientation to planned Azimuth (Az. :90deg), Set Whipstock PKR @ 2265m (Whipstock Top Depth: 2257.88m, Whipstock BTM Depth: 2265m), Shear

		Screw W/ 80klbs Overpull, Break knock off plugs, CBU @ 2265m to Shear In/Out Mud, Window Milling F/ 2265 To 2259.16m, W/ NL-NG.
28	16-Apr-25	Cont. Window Milling W/ 8-3/8" Cased-hole sidetrack BHA F/ 2259.2 To 2262.5m, Pump 40bbl Hi-Vis Pill, CBU @ 2262.5m, P/U & M/U 8-1/2" Window Dressing BHA including: [8-1/2" Tri-Mill (Lead Mill + Follow Mill + Watermelon) + 6-1/2" Running Tool + 1 Jt 5" DP + 4 Stds 6-1/2" DC] and RIH to 922m, While F/U Strg at 15-Std Intervals, W/ NL-NG.
29	17-Apr-25	RIH W/8-1/2" Milling to 2259.4m. Start Window Milling to 2266m. Pump Hi-Vis Pill to Clean the Hole while Dec. Mwt to 76pcf & Work on Mud Rheology. POOH to Surface and Lay down Tri Mill (10% Used). P/U 6-3/4" PDM (AKO: 1.5°) .
30	18-Apr-25	Run in hole to 2260m(BTM), P/U & Assemble Wire Line Tools as Gyro Tool String & Run in hole to 2247m (Gyro Sub Depth); Failed to get data due to tool malfunction, Attempt Sev. Times W/O Success; POOH Gyro Tool String to Surface and R/D Wire Line Tools
31	19-Apr-25	POOH Gyro Tool to Surface, POOH D.D BHA to Surface, Change in Wire line Tools (Change Key of Sleeve), RIH D.D BHA to 2262.5m, R/U & RIH Wire Line Tools to 680m
32	20-Apr-25	Cont RIH with Gyro Tool To 2247m, confirmed data OK. Strat D.DRLF 8-3/8" Hole section as Rot. & Slide Mode From 2266.10m to 2293.5m While Monitor the Well, W/ NL-NG
33	21-Apr-25	Cont. Directional Drilling 8-3/8" Hole Section to 2310m, Pump Hi Vis Pill to Clean the Hole, POOH to Surface, L/D Gyro Sub (Paniz Co.) & 8-3/8" Tri Cone No#1 , Check PDM & MWD Tools (Change Battery), M/U & RIH W/ 8-3/8" New PDC Bit No#2 + 6-3/4" PDM (AKO : 1.5) Conn To TDS and Perform Surface test, Ok. Cont RIH with D.D BHA to 1250m
34	22-Apr-25	Cont RIH TO 2310m, Cont Directional Drilling 8-3/8" Hole Section As Rotating & Slide Mode From 2310m to 2364m W/ 1.5-2 BPH Loss
35	23-Apr-25	Continue Directional Drilling 8-3/8" Hole Section As Rotating & Slide Mode F/ 2364m To 2425.5m while Pump Hi Vis Pill & B/R and R/D Each STD & Take Survey W/ 0.5-1 BPH Loss
36	24-Apr-25	Continue Directional Drilling 8-3/8" Hole Section As Rotating & Slide Mode F/ 2425.5m To 2501m while Pump Hi Vis Pill & B/R and R/D Each STD & Take Survey W/ 1-2 BPH Loss
37	25-Apr-25	Continue Directional Drilling 8-3/8" Hole Section As Rotating & Slide Mode F/ 2510m To 2565.4m while Pump Hi Vis Pill & B/R and R/D Each STD & Take Survey W/ 1-3 BPH Loss
38	26-Apr-25	Continue Directional Drilling 8-3/8" Hole Section As Rotating & Slide Mode F/ 2565.4m To 2610m, While Cont. Directional Drilling Observe Increase Loss to 8-10 BPH. Work on Loss Control

39	27-Apr-25	Cont. D.DRLG 8-3/8" Hole Section As Rotating Mode F/ 2610m To 2620m, Try to Cont. D.DRLG, No. Succ. Due to Low ROP. And Pressure Up PDM In Slide mode Drilling. Circ BTM's UP. POOH To Surf.
40	28-Apr-25	Make 25Std's and Rack Bake in Derrick, P/U & RIH with D.DRLG to 2620m W/ 5-6 BPH loss. (TD)
41	29-Apr-25	Cont D.DRLG 8-3/8" Hole Section As Sliding & Rotating Mode F/ 2620.13m To 2665.45m.
42	30-Apr-25	Cont D.DRLG 8-3/8" Hole Section As Sliding & Rotating Mode F/ 2620.13m To 2665.45m.
43	1-May-25	Cont D.DRLG 8-3/8" Hole Section As Sliding & Rotating Mode F/ 2718.3 To 2781.8m, While take survey and pump Hi-Vis Pill, W/ 5-6 BPH Loss
44	2-May-25	Cont D.DRLG 8-3/8" Hole Section As Sliding & Rotating Mode F/ 2781.8 To 2817m, While take survey and pump Hi-Vis Pill, W/ 5-6 BPH Loss.
45	3-May-25	Cont D.DRLG 8-3/8" Hole Section As Sliding & Rotating Mode F/ 2817 To 2864.5m, While take survey and pump Hi-Vis Pill, W/ 5-6 BPH Loss.
46	4-May-25	Cont D.DRLG 8-3/8" Hole Section As Sliding & Rotating Mode F/ 2864.5 To 2884m, While take survey and pump Hi-Vis Pill, CBU, POOH 8-3/8" D.DRLG BHA to 155m, Stop Op. due to bad weather, While Circ. C.W.H & Thru. Strg periodically, W/ 5-6 BPH Loss
47	5-May-25	Cont. Stop Op. at the request of OEOC Rig 201 HSE Officer due to windy weather, Cont. POOH 8-3/8" D.DRLG BHA to surface, L/D the same BHA, BOP Test, P/U & M/U 5" Stds and R/B in the Derrick, P/U & M/U 8-3/8" D.Drlg BHA and RIH to 2260m, Perform Functional Tests during RIH [Depth: 500m, F.R: 450gpm, SPP: 980psi ; Depth: 1500m, F.R: 450gpm, SPP: 1140-1180psi], W/ 3-4BPH Loss.
48	6-May-25	Cont. RIH W/ 8-3/8" Dir. Drlg BHA F/ 2260 To 2521m On Elevator, Hold Up Strg Wt. @ 2521m, Cont. RIH W/ 8-3/8" Dir. Drlg W/ Wash Dn F/ 2521 To 2575m, Hold Up Strg Wt. @ 2575m, Cont. RIH W/ 8-3/8" Dir. Drlg BHA F/ 2575 To 2884m W/ Soft to Medium Wash & Ream Dn, Resume Dir. Drlg 8-3/8" Hole Section As Slide & Rotating Mode F/ 2884 To 2912.6m, W/ 2-3BPH Loss.
49	7-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Slide & Rotating Mode F/ 2912.6 To 2951.3m, W/ 2-3BPH Loss.
50	8-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Slide & Rotating Mode F/ 2951.3 To 2979.7m, Pump 40 Hi-Vis Pill, CBU @ 2979.7m, POOH 8-3/8" Dir. Drlg BHA F/ 2979.7 To 2870m On Elevator, Cont. POOH 8-3/8" Dir. Drlg BHA F/ 2870 To 2528m W/ Pump out, Cont. POOH 8-3/8" Dir. Drlg BHA F/ 2528 To 155m On Elevator, W/ 1-2BPH Loss.

51	9-May-25	Cont. POOH 8-3/8" Dir. Drlg BHA To surface, L/D 8-3/8" Bit W/ Same Condition (D.G: 2-3-WT-A-X-I-NO-BHA) & rest of BHA, Attempt to B/O DHM Stabilizer, No Success, Decided to revise Dir. Drlg BHA, P/U & M/U 8-3/8" Dir. Drlg BHA and RIH to 2874, While monitor the well & Circ. Thru. Trip Tank, W/ 1-2BPH Loss.
52	10-May-25	Cont. POOH 8-3/8" Dir. Drlg BHA To surface, L/D 8-3/8" Bit W/ Same Condition (D.G: 2-3-WT-A-X-I-NO-BHA) & rest of BHA, Attempt to B/O DHM Stabilizer, No Success, Decided to revise Dir. Drlg BHA, P/U & M/U 8-3/8" Dir. Drlg BHA and RIH to 2874, While monitor the well & Circ. Thru. Trip Tank, W/ 1-2BPH Loss.
53	11-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3012 to 3065.4m, W/ 3-4BPH Loss.
54	12-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3065.4 to 3151.3m, W/ 3-4BPH Loss.
55	13-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3151.3 to 3238.7m, W/ 3-4BPH Loss.
56	14-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3238.7 to 3297.9m, W/ 3-4BPH Loss
57	15-May-25	Cont. Dir. Drlg 8-3/8" Hole Section As Sliding & Rotating Mode to 3304m, POOH To Surface , Change 8-3/8" PDC Bit & 6-3/4" PDM
58	16-May-25	Cont RIH TO 3304m (BTM) , Resume Directional Drilling 8-3/8" Hole Section As Sliding & Rotating Mode from 3304m to 3335.4m W/ 2-3 BPH Loss.
59	17-May-25	Directional Drilling 8-3/8" Hole Section As Sliding & Rotating Mode from 3335.4m to 3401.5m W/ 2-4 BPH Loss.
60	18-May-25	Directional Drilling 8-3/8" Hole Section As Sliding & Rotating Mode from 3401.5m to 3450.6m W/ 2-4 BPH Loss.
61	19-May-25	Directional Drilling 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3450.6m To 3543.3m W/ 2-4 BPH Loss.
62	20-May-25	Directional Drilling 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3543.3m To 3573.8m W/ 2-4 BPH Loss
63	21-May-25	Directional Drilling 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3573.8m To 3583.88m W/ 2-4 BPH Loss. Pump Hi Vis Pill to Clean the Hole, POOH TO 249
64	22-May-25	Cont POOH To surface. Perform BOP Test as NIOC Policy, P/U & RIH With 8-3/8" D.DRLG BHA To 3443m
65	23-May-25	Cont RIH With 8-3/8" D.DRLG BHA To 3594m (Tag BTM), Cont. Directional Drilling 8-3/8" Hole Section Rotating Mode To 3675 m while take survey W/ 2-4 BPH Loss.
66	24-May-25	Cont. Directional Drilling 8-3/8" Hole Section Rotating Mode To 3692 m while take survey W/ 2-4 BPH Loss. Perform Condition Trip, POOH to 1954m

67	25-May-25	POOH to Surf, Slip & Cut 100Ft DRLG Line, Run in hole with 7" LNR to 1056m (Totally : 94 Jts) W/2-3BPH Loss
68	26-May-25	Run 7" LNR Totally 135 Jts & Cont. Follow by 5" D.P to 3692m, Perform CMT Job, Ok.
69	27-May-25	POOH to Surf, L/D LNR Running tools. RIH With 8-3/8" Used TCI Bit + + Bit sub 6 1/2" + 7 STD'S 5" H.W.D.P & Follow by 5" D.P To 2134m, Start D/O Med To Hard CMT F/ 2134 To 2167.5 MT (New 7" L.Lap). Circ. BTM's UP.
70	28-May-25	POOH To Surface, Perform 9-5/8" Scraper Trip (Scrap From 2100 to 2165m), POOH To surface & L/D 9-5/8" Scraper
71	29-May-25	P/U & M/U 9-5/8"Dry Test Tool Srting and RIH To 2142m, While Pass Rabbit Thru. all Tubular, W/ Speed Control at the request of OEOC DST Supervisor, and F/U 886m of Strg W/ Drill water as a Water Cushion at 5-Std intervals, Prepare Rig Floor, Change TDS Links & Perform Dry Test Op. in Open Period Monitoring is in progress
72	30-May-25	Cont. Dry Test operation, POOH 9-5/8"Dry Test Tool Srting to surface, Read Middle & BTM B.T, 1.5Hrs. Open-Period Monitoring Results: [Middle B.T: 1455 - 2336psi, BTM B.T: 1480-2350psi], 6Hrs. Close-Period Monitoring Results: [Middle B.T: 2336 - 3352psi, BTM B.T: 2350-3370psi]; Check Sample Properties of flowing sample between DCIP & Hydrospring [MW: 71pcf, PH: 6.8 , Cl: 130000, Ca+: 4800]; Prepare Rig Floor to P/U & M/U 6-1/8" D/O BHA to D/O CMT inside 7" LNR is in progress
73	31-May-25	P/U & M/U 6-1/8" D/O BHA & RIH To 2167m On Elevator, Obs. Leakage on TDS Drlg Fluid Hose @ 2167m, POOH 6-1/8" D/O BHA To 2152m, Stop RIH Op. & Change TDS Drlg Fluid Hose; Resume RIH W/ 6-1/8" D/O BHA F/ 2152 To 2171m W/ Soft Wash & Ream Dn, Held up Strg Wt. & Tag Pack of Bushing @ 2171m; D/O P.O.B & Dress its interval Sev. Times; Cont. RIH W/ 6-1/8" D/O BHA F/ 2171 To 2730m On Elevator; Obs. Negligible Drag @ 2730m, Cont, RIH W/ 6-1/8" D/O BHA F/ 2730 To 2852m W/ Soft Wash & Ream Dn; Cont. RIH W/ 6-1/8" D/O BHA F/ 2852 To 3020m On Elevator, N-NG.
74	1-Jun-25	Cont. RIH W/ 6-1/8" D/O BHA F/ 3020 To 3563m On Elevator, Cont. RIH W/ 6-1/8" D/O BHA F/ 3563 To 3607m W/ Wash & Ream Dn, D/O CMT W/ 6-1/8" D/O BHA F/ 3607 To 3656m, Cont. D/O Soft to Medium CMT W/ 6-1/8" D/O BHA F/ 3656 To 3658.7m, While D/O LDC, Pump Down Plug, and Wiper Plug @ 3657m, Dress & Smooth LDC, Pump Down Plug, and Wiper Plug Sev. Times, pump Hi-Vis Pill & Reciprocate Strg, NL-NG.
75	2-Jun-25	Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3658.7 To 3672m, , While D/O F.Collar @ 3668m, Dress & Smooth F.Collar position Sev. Times, pump Hi-Vis Pill, Pump 30bbl Hi-Vis Pill, CBU @ 3672m till Shakering out Hi-Vis Pill, POOH 6-1/8" D/O BHA F/ 3672 To 1230m On Elevator, 7"L.Lap @ 2150m, Ok, Due to

		Windy weather Stop POOH Op. @ 1230m, While Slow Circ. Thru. Strg, Cont. POOH 6-1/8" D/O BHA F/ 1230m To Surface, L/D BHA & 6-1/8" Tri-cone Bit W/ Same Condition, Retrieve Wear Bushing, Change Top Rams F/ 4-1/2" × 7" VBR To 2-7/8" × 5" VBR is in progress
76	3-Jun-25	Cont. Change Top Rams Form 4-1/2" × 7" VBR To 2-7/8" × 5" VBR, Set Plug Tester, Press. Test the Same; P/U & M/U 9-5/8" × 7" Tandem Scraper BHA and RIH To 2276m; Due to Windy weather, Stop RIH Op. 2276m; Cont. RIH W/ 9-5/8" ×7" Tandem Scraper BHA F/ 2276 To 3612m On Elevator; Conn. TDS & Cont. RIH W/ 9-5/8" ×7" Tandem Scraper BHA F/ 3612 To 3671m W/ Wash Dn, Tag 7" L.Lap W/ 9-5/8" Scraper, NL-NG.
77	4-Jun-25	Conduct Multiple Scraping Passes On 7" S.N PKR Setting Interval; Pump 40bbl Hi-Vis Pill, CBU; POOH 9-5/8" ×7" Tandem Scraper BHA F/ 3671 To 1532m; Due to Windy weather, Stop POOH Op. @ 1532m; Cont. POOH 9-5/8" ×7" Tandem Scraper BHA F/ 1532 To 893m; Due to Windy weather, Stop POOH Op. @ 893m; Cont. POOH 9-5/8" ×7" Tandem Scraper BHA F/ 893m To Surface; Prepare Rig Floor to perform Wire Line Logging Op. & R/U Surface Wireline Tools; RIH W/ Same Wireline Logging Tool String To 2050m is in progress
78	5-Jun-25	Cont. Wireline Logging as plan; POOH Wireline Logging Tool String To Surface; R/U Surface Wireline Tools; Change 13-5/8" 10K Top Rams F/ 4-1/2" × 7" VBR To 2-7/8" × 5" VBR; P/U & M/U 6-1/8" BHA and RIH W/ Same BHA To 3660m, While F/U Strg & Break Circ. at 10-Std intervals
79	6-Jun-25	Cont. RIH W/ 6-1/8" D/O BHA F/ 3660 To 3672m W/ Wash Dn; D/O Medium to Hard CMT W/ 6-1/8" D/O BHA F/ 3672 To 3692m; Pump 40bbl Hi-Vis Pill & CBU @ 3693m, While optimize Drilling Fluid Parameters & Increase MW F/ 76 To 78pcf; Commence Drilling 6-1/8" Hole Section W/ 6-1/8" D/O BHA F/ 3692 To 3697m; Pump 40bbl Hi-Vis Pill & CBU @ 3697m; Static Flow Check @ 3697m, Well Static; POOH 6-1/8" D/O BHA F/ 3697 To 2095m On Elevator; Slip & Cut 100ft of Drlg Line; Cont. POOH 6-1/8" D/O BHA F/ 2095 To 1663m On Elevator, NL-NG.
80	7-Jun-25	POOH 6-1/8" D/O BHA To Surface; P/U & M/U 6-1/8" D.D BHA and RIH w/ 6-1/8" Dir. Drlg BHA To 3665m, While F/U String and Break Circ. at 15-Std intervals, and Perform DHM Functional Tests during RIH [Depth: 500m, F.R: 200gpm, SPP: 1030-1140psi; Depth: 1500m, F.R: 200gpm, SPP: 1400-1480psi; Depth: 3000m, F.R: 200gpm, SPP: 1850-1940psi], NL-NG.
81	8-Jun-25	Cont. Dir. Drlg 8-3/8" Hole Section As Sliding & Rotating Mode F/ 3697 to 3751m, NL-NG.
82	9-Jun-25	Cont. Dir. Drlg 6-1/8" Hole Section As Sliding & Rotating Mode F/ 3751 to 3760m; Obs. 350 psi Sudden Increase in SPP While Drilling; POOH Strg to 3723m, Check Pipe Screen and Surface

		Lines, Ok; POOH 6-1/8" Dri. Drlg BHA F/ 3760m To Surface On Elevator, L/D 6-1/8" PDC Bit & Rest of BHA is in progress, NL-NG.
83	10-Jun-25	Cont. L/D 6-1/8" PDC Bit & Rest of BHA; BOP Test; P/U & M/U 6-1/8" Dir. Drlg BHA, Cont. RIH W/ 6-1/8" Dri. Drlg BHA To 3658m, While conduct DHM Functional Tests during RIH and F/U Strg & Break Circ. At 15-Std intervals, NL-NG.
84	11-Jun-25	Conn. TDS & Cont. RIH W/ 6-1/8" Dir. Drlg BHA F/ 3695 To 3760m W/ Soft Wash & Ream Dn, Tag BTM @ 3760m; Resume Dir. Drlg 6-1/8" Hole Section As Rotating & Sliding Mode F/ 3760 3818.4m, While take Survey & Pump Hi-Vis Pill, NL-NG.
85	12-Jun-25	Resume Dir. Drlg 6-1/8" Hole Section As Rotating & Sliding Mode F/ 3818.4m to 3888m (TD), While take Survey & Pump Hi-Vis Pill, NL-NG.
86	13-Jun-25	Hole Condition from 3888m to 3692m Several time's, Inc. MW to 80pcf & Work on Mud Rheology. Work on Stuck with Downward and Apply max. 100klb weight Finally String got free. Cont. Back Ream to 3692m (7" shoe), Flow Check the well, "Static".
87	14-Jun-25	Perform Hole Condition from 3888 to 3692m (7" Shoe) Several Time While Inc. Mw to 82 PCF
88	15-Jun-25	Perform Hole Condition from 3692m (7" Shoe) to 3888m Several Time, POOH from 3888m (BTM) to 1398m
89	16-Jun-25	POOH To surface , Change BHA, Run in hole for Condition To 3752m
90	17-Jun-25	Perform Condition Trip With Inc Mw to 84 PCF , Spot 50 BBL Hi.Vis Pill, POOH to 1466m
91	18-Jun-25	Cont POOH to surface. R/U & RIH with Full Suite Logging Tools (SEALAND Co.) to 1045m
92	19-Jun-25	Cont RIH with Full Suite Logging Tools (SEALAND Co.) to 3450m, Take Log Down to 3788m, Took Weight, Log up to 3692m, Cont. POOH to 3450m, Disconnected C.S.E.S & R/D Shaves
93	20-Jun-25	Wait on client Due to Stop Operation By Clinet order To secure and suspend the well. Cont POOH with Full Suite Logging Tools To surface & L/D Full Suite Logging Tools. RIH with 3-1/2" & 5" D.Pipe OEDP to 1730m For CMT Plug
94	21-Jun-25	RIH TO 3299m, Perform CMT Plug Job. POOH TO 3040m, Flush string
95	22-Jun-25	POOH TO 2167m, Perform CMT Plug Job. POOH TO 2018.76m , Flush the string. Cont POOH to 1932.63m, Circ. BTM's Up. POOH To Surface. Close The Well
96	23-Jun-25	Close The Well.
97	24-Jun-25	Close The Well. Stop Operation Due to windy weather (dust strom), P/U & RIH with 8-3/8" Tri.cone Bit NO#4, RR3 + + Bit sub 6 1/2" + 2 STD 6-1/2" D.C + 3 STD 5" H.W.D.P & Follow By 5" D.Pipe to 995m W/NL.NG

98	25-Jun-25	D/O CMT Plug from 2103 to 2167.5m (7" L.Lap) Circ Btm's Up. POOH to 423m
99	26-Jun-25	Cont. POOH 8-3/8" D/O BHA To Surface, L/D 8-3/8" D/O BHA; P/U & M/U 6-1/8" D/O BHA and RIH To 3139.6m, While F/U Strg & Break Circ. At 15-Std intervals, Obs. Drag @ 3139.6m; Conn. TDS and Cont. RIH W/ 6-1/8" D/O BHA F/ 3139.6 To 3170m W/ Soft Wash & Ream Dn, Held up Stg Wt. & Tag TOC @ 3170m; D/O CMT W/ 6-1/8" D/O BHA F/ 3170 To 3211.6m, While Reciprocate Every Drilled out Std before each Conn. & Pump Hi-Vis Pill Periodically, W/ NL-NG.
100	27-Jun-25	Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3211.6 To 3280m; Pump 40Hi-Vis Pill, CBU @ 3280m To Sweep the Well and Shaker out the pumped Hi-Vis Pill, While optimize mud Props; Cont. D/O CMT W/ 6-1/8" D/O BHA F/ 3280 To 3300m; Cont. RIH W/ 6-1/8" D/O BHA F/ 3322 To 3664m On Elevator; Pump 40Hi-Vis Pill, CBU @ 3664m To Sweep the Well and Shaker out the pumped Hi-Vis Pill; Cont. RIH W/ 6-1/8" D/O BHA F/ 3664 To 3693.5m On Elevator; Cont. RIH W/ 6-1/8" D/O BHA F/ 3693.5 To 3780m W/ Med. To Hard W/R Dn, While Reciprocate and B/Ream Each Std Sev. Times,
101	28-Jun-25	Encounter Tight Hole Condition @ Interval 3750-3888m (TD), Conduct Hard Wash & Ream Dn W/ 6-1/8" D/O BHA on Same interval & Tag TD (3388m); Pump 40bbl Hi-Vis Pill @ 3888m (TD), CBU & Shaker out the pumped Hi-Vis Pill; POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3689m (3m above 7" Shoe Depth); RIH W/ 6-1/8" D/O BHA F/ 3689 To 3791 W/ Wash & Ream Dn, NL-NG.
102	29-Jun-25	Encounter Tight Hole Condition @ 3791m; Conduct Hard Wash & Ream Dn W/ 6-1/8" D/O BHA, Attempt to Pass the same point, No Success; POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3791 To 3670m (above 7" Shoe Depth); RIH W/ 6-1/8" D/O BHA F/ 3670 To 3791 W/ Wash & Ream Dn; Encounter Tight Hole Condition @ Interval 3791-3798m; Conduct Hard Wash & Ream Dn W/ 6-1/8" D/O BHA; Cont. RIH W/ 6-1/8" D/O BHA F/ 3798 To 3802.5 W/ Wash & Ream Dn, NL-NG.
103	30-Jun-25	Encounter Tight Hole Condition @ 3802.5-3808m; Conduct Hard Wash & Ream Dn W/ 6-1/8" D/O BHA; Cont. RIH W/ 6-1/8" D/O BHA F/ 3808 To 3888 W/ Wash & Ream Dn; POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3682m (above 7" Shoe Depth); RIH W/ 6-1/8" D/O BHA F/ 3682 To 3808 W/ Wash Dn, NL-NG.
104	1-Jul-25	Cont. RIH W/ 6-1/8" D/O BHA F/ 3808 To 3870m W/ Wash Dn; Cont. RIH W/ 6-1/8" D/O BHA F/ 3870 To 3888m W/ Wash & Ream Dn; POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3664m; Stop Op. @ 3664m at request of OEOC Rig 201 HSE Officer Due To Windy Weather; Cont. RIH W/ 6-1/8"

		D/O BHA F/ 3664 To 3880m W/ Wash Dn; Pump 40bbl Hi-Vis Pill @ 3888m, CBU & Shaker out Hi-Vis Pill is in progress
105	2-Jul-25	Cont. CBU & Shaker out Hi-Vis Pill @ 3888m; Then Spot 40bbl Hi-Vis Pill @ 3888m; Attempt To Start POOH 6-1/8" D/O BHA To Surface, Strg got Stuck @ 3880m, Work on Stuck Strg & Make it free; POOH 6-1/8" D/O BHA W/ Back Ream & Pump Out F/ 3888 To 3690m; RIH W/ 6-1/8" D/O BHA F/ 3690 To 3888m W/ Wash & Ream Dn; Pump 40bbl Hi-Vis Pill @ 3888m, CBU & Shaker out Hi-Vis Pill; Then Spot 40bbl Hi-Vis Pill @ 3888m; POOH 6-1/8" D/O BHA F/ 3888 To 3664m W/ Normal Hole Condition; Cont. POOH 6-1/8" D/O BHA F/ 3664 To 338m On Elevator
106	3-Jul-25	Cont. POOH 6-1/8" D/O BHA F/ 338m To Surf. ; Prepare For Logging, P/U & Assemble W/L Tool String As Full Suite Logging (Resistivity-Sonic-CDR-GR) and RIH To 3800m, Obs. W/L Cable Tension Drop @ 3800m, Decided To POOH W/L Tool String, Data Acquisition Logging Up F/ 3800 to Fully Cover Logging Interval; POOH W/L Tool String To Surface, L/D W/L Tool String; Prepare For P/U & M/U 6-1/8" Condition BHA, RIH W/ 6-1/8" Condition BHA To 3692m On Elevator Followed by 3-1/2" & 5" DPs, Cont. RIH W/ 6-1/8" Condition BHA F/ 3692 To 3752m W/ Soft Wash & Ream Dn, NL-NG.
107	4-Jul-25	Cont. RIH W/ 6-1/8" Condition BHA F/ 3752 To 3888m W/ Wash & Ream Dn; POOH 6-1/8" Condition BHA F/ 3888 To 3800m W/ Back Ream POOH to 3692m; RIH W/ 6-1/8" Condition BHA F/ 3692 To 3888m W/ Wash & Ream Dn, While Conduct Wash Ream & Back Ream Interval 3800-3888m Sev. Times, Normal Hole Condition confirmed; Pump 50bbl Hi-Vis Pill @ 3888m, CBU & Shaker out Hi-Vis Pill; POOH 6-1/8" Condition BHA F/ 3888 To 3692m On Elevator
108	5-Jul-25	Cont. POOH 6-1/8" Condition BHA F/ 1292m To Surface, L/D 6-1/8" Bit (1-2-BT-T-X-I-WT-LOG) & Rest of BHA; M/U Additional 3-1/2" Tubular needed for TLC Job Jt by Jt, Flush Tubular; Cont. RIH W/ Wireline Logging Tool String For TLC Logging F/ 27 To 314m ; Stop POOH Operation @ 314m Due to Windy Weather at the request of OEOC Rig 201 HSE Officer; Cont. RIH W/ Wireline Logging Tool String For TLC Logging F/ 314 To 1556m, NL-NG.
109	6-Jul-25	Cont. POOH 6-1/8" Condition BHA F/ 1292m To Surface, L/D 6-1/8" Bit (1-2-BT-T-X-I-WT-LOG) & Rest of BHA; M/U Additional 3-1/2" Tubular needed for TLC Job Jt by Jt, Flush Tubular; Cont. RIH W/ Wireline Logging Tool String For TLC Logging F/ 27 To 314m ; Stop POOH Operation @ 314m Due to Windy Weather at the request of OEOC Rig 201 HSE Officer; Cont. RIH W/ Wireline Logging Tool String For TLC Logging F/ 314 To 1556m, NL-NG.

110	7-Jul-25	24 HRs NPT for sealand co. Due to failure Equip. to TLC Full Suite Log. Cont. POOH Wireline Logging Tool String (Full-Suite) For 6 1/8" Open Hole F/ 2788m To Surface On Elevator, L/D Wireline Logging Tool String; Observed N Bridle (DLL Deep, SeaLand Co.) damaged and failed; R/D Wireline Logging Surface Tools; P/U & M/U 6-1/8" Condition BHA & RIH To 3692m On Elevator; Conn. TDS & F/U Strg, Cont. RIH W/ 6-1/8" Condition BHA F/ 3692 To 3877m W/ Wash Dn; Cont. RIH W/ 6-1/8" Condition BHA F/ 3877 To 3888m W/ Wash & Ream Dn, NL-NG.
111	8-Jul-25	Cont. CBU @ 3888m; POOH 6-1/8" Condition BHA To Surface; R/U SLD Wireline Surface Tools, RIH W/ Wireline Logging Tool String To 3888m; R/U SeaLand Wire Line Eqp. , P/U & Assemble Wireline Tool String As Full Suite Logging (Resistivity-Sonic-CDR-GR); Commence Data Acquisition Logging Up F/ 3885 To 3692m to Fully Cover Logging Interval, L/D Wireline Tool String, R/D Surface SeaLand Wireline Tools Eqp. & 7" Shooting Nipple; Slip & Cut 100ft Drlg Line; P/U & M/U 6-1/8" Condition BHA and RIH To 283.7m, F/U BHA & Break Circ. , NL-NG.
112	9-Jul-25	Cont. RIH 6-1/8" Condition BHA To 3888m, While Condtion 6-1/8" Open Hole; Pump 50bbl Hi-Vis Pill @ 3888m, CBU till Shaker out the pumped Hi-Vis Pill; POOH 6-1/8" Condition BHA F/ 3888m To 110m, Normal Hole Condition confirmed, NL-NG.
113	10-Jul-25	POOH to surf. Run 5" LNR as Program to 3450m
114	11-Jul-25	Cont. Run 5" LNR To TD and Set LNR HGR with 2000Psi @ 3887m, Ok. Release Setting tools, Perform CMT Job, Sting Out and Set Packer, Ok. POOH 10 STD, Flush The String, Cont. POOH 8STD. Circ. BTM's UP. Cont. POOH to Surface & L/D Setting Tools LNR HGR. RIH With 6-1/8" BHA For Tag 5" L.Lap To 390m
115	12-Jul-25	Cont RIH to 3596m & Confirm 5" L.LAP @ 3596m, Circ BTM's Up, POOH While L/D Extra 5" D.Pipe
116	13-Jul-25	Cont POOH While L/D Extra 5" & 3-1/2" D.Pipe, P/U & Run in hole with 4-1/8" M.M Junk Mill + 16 Jts 3-1/8" D.C to 142m
117	14-Jul-25	Cont. RIH with 4-1/8" D/O BHA to 3601.4m (P.O.B), D/O from 3601.4m to 3601.8m, Cont Wash & Ream to 3604m, Took weight. Continue D/Out to 3604.8m, drop weight. Continue run in Hole with wash Down to 3612.46m W/NL.NG
118	15-Jul-25	Cont RIH to 3861.13m, Cont D/Out P.D.P & L.W.P & LDC to 3864.5m, try to continue, No Progress. Circ BTm's Up. POOH with 4-1/8" D/O BHA From 3864.5m to 3467m W/NL.NG
119	16-Jul-25	POOH To surf. Perform BOP Test as NIOC Policy, P/U & RIH With 3-3/4" M.M.J.Mill and same BHA to 740m
120	17-Jul-25	Cont. RIH to to 3864.5m. While Break Circ Mud. W/NL.NG. Commence D/Out LDC to 3864.8m, Cont D/Oue Soft to Med CMT Below LDC from 3864.8 to 3868m and Med to Hard from

		3868 to 3876.7m (F.Coller Depth), Work on D/OUT interval for Smooth it Several times
121	18-Jul-25	D/Out Med to Hard 3876.7m (F.Coller Depth), Circ BTM's UP With Pump 20BBL Hi.Vis Pill While Work on reduce mud weight 1 PCF (from 87 to 86). Balance Mw In/Out (86 Pcf), POOH to Surf, R/U Wireline logging (SeaLand Co.)
122	19-Jul-25	Perform Log (2 Run), P/U & M\U 9-5/8" CSG Scraper to 2167m (7" L.Lap) while Scrap PKR depth Interval several time, Pump 30BBL Hi.Vis Pill
123	20-Jul-25	Cont POOH to surf & L/D 9-5/8" Scraper, Slip & Cut 97Ft DRLG Line. P/U & RIH with 7-5/16" Polish Mill to 2167 & Polish inside 7" L.Lap Several times. Pump 30BBl Hi.vis Pill, Circ Btm's up and Shaker out Hi.Vis Pill. POOH to 1421m
124	21-Jul-25	Cont POOH to Surf & L/D 7-5/16" Polish Mill. Run 7" S.N PKR (29#, L-80, ACME, PPA) and set in Before 7" LNR (2165m New 7" L.Lap), POOH to surf and L/D Setting Tools, P/U & Run 5-1/8" Polish Mill BHA to 450m W/NL.NG
125	22-Jul-25	Cont RIH with 5-1/8" Polish Mill BHA to 3596m, Polish inside 5" PBR, Dec. mud weight 1 PCF (from 86 to 85). Balance Mw In/Out (85 Pcf), POOH to Surf. P/U & RIH with 5-1/8" Polish Mill + 4-3/4" Double Pin + 7" Scraper + 4-3/4" Bit Sub + 1 Stds 3-1/2 H.W.D.P to 30m.
126	23-Jul-25	RIH to 3596m (5" L.Lap), Scrap 5" S.N PKR depth Interval, Pump 25BBL Hi.Vis Pill, Circ Btm's Up & Shaker Out Hi.Vis Pill and Work on Dec. mud weight 1 PCF. Balance Mw In/Out (84 Pcf). POOH to 3570m (Dry test PKR Depth) and scrap Dry test PKR Depth, Cont POOH to Surf
127	24-Jul-25	RIH W/ 5" Tie-Back Packer Assy. To 3596m (5" L.Lap); Set PKR (New 5"L.Lap @ 3593.5m), Perform 10 Klbs Pull Test – Test result OK, Release Setting Tool; POOH 5" Tie-Back Packer Assy. Running & Setting Tool F/ 3593.5 To 2231m, While Circ. C.W.H, NL-NG.
128	25-Jul-25	P/U & M/U 7"Dry Test Tool Srting and RIH To 1797m, While Pass Rabbit Thru. all Tubular, W/ Speed Control at the request of OEOC DST Supervisor, and F/U Strg W/ Drill water as a Water Cushion at 5-Std intervals is in progress
129	26-Jul-25	Cont. RIH W/ 7"Dry Test Tool String F/ 1797 To 3572m, While Pass Rabbit Thru. all Tubular, W/ Speed Control at the request of OEOC DST Supervisor, and F/U 2541m of Strg W/ Drill water as a Water Cushion at 5-Std intervals; Prepare Rig Floor, Change TDS Links & Perform Dry Test Op. in Open Period Monitoring, Maintain open condition and monitor for totally 3Hrs. for any bubbles at the surface for ongoing monitoring, No Bubbles observed, Confirm Annulus fluid level is Static during observation; Close Period Monitoring is in progress

130	27-Jul-25	Cont. Perform Dry Test operation as per plan; CBU Till Uniform In/Out MW @ 3563m and Flow Check, Well Static; POOH 7"Dry Test Tool String to 560m, While Circ. C.W.H, NL-NG.
131	28-Jul-25	Cont. POOH 7"Dry Test Tool String to surface, Read Memory Data & Recorded Test Data: 3Hrs. Open-Period Monitoring Results: [Middle B.T: 3572 - 3572psi, BTM B.T: 3588-3588psi], 6Hrs. Close-Period Monitoring Results: [Middle B.T: 3572 - 3798psi, BTM B.T: 3588-3814psi], Check Properties of flowing sample between DCIP & Hydrospring [MW: 74pcf, PH: 7.5 , Cl: 180000, Ca+: 2400]; Slip & Cut of 100ft Drlg Line; RIH W/ 9-5/8"Dry Test Tool String to 1950m, While F/U 678m of Strg W/ Drill water (62.4 pcf) as a Water Cushion at
132	29-Jul-25	Cont. RIH W/ 9-5/8"Dry Test Tool String F/ 1950 To 2148m; Perform 7" L.Lap Dry Test: No Bubbles observed during the first hour of Open Period Monitoring, Bubbles observed afterward; Bubbles continuously observed Thru. Strg & Annulus during Close Period Monitoring, 'Annulus fluid level exhibited fluctuations & Not remain Static throughout Observation; Reverse Circ. , Recovered approximately 20 bbl of Mud-contaminated fluid, 30 bbl of Drill water, and 10 bbl of Mud-contaminated fluid; CBU Thru. Strg @ 2140m; POOH 9-5/8" Dry Test Tool String F/ 2140 To 945m, NL-NG.
133	30-Jul-25	Cont. POOH 9-5/8" Dry Test Tool String To Surface; B/O & L/D BHA & Dry Test Tool String; Read Middle & BTM B.T; BOP Test; Stop RIH Operation Due to Windy Weather; P/U & M/U 7-5/16" Polish BHA and RIH To 850m; Stop RIH Operation @ 850m Due to Windy Weather; Cont. RIH W/ 7-5/16" Polish BHA F/ 850 To 2165m On Elevator; Cont. RIH W/ 7-5/16" Polish Mill W/ Wash Dn To 2167.5m & Tag L.G, Work on making mark on Polish Mill Nose; Polish Inside Tie-Back Sleeve W/ Pump out Sev. Times; Circ. BTMs Up; POOH 7-5/16" Polish BHA F/ 2170 To 1707m, While Circ. C.W.H.
134	31-Jul-25	POOH 7-5/16" Polish BHA F/ 1707m To Surface; RIH W/ 7" Tie-Back LNR To 2160m, Prepare to Set 7" Tie Back Assy, NL-NG is in progress
135	1-Aug-25	Set 7" Tie Back Assy and CMT as per plan; POOH Setting Tool To Surface; RIH W/ 8-3/8" D/O BHA To 1990m; Cont. RIH W/ 8-3/8" D/O BHA W/ Wash Dn F/ 1845 To1988m; CBU @ 1988m To Condition Mud; Cont. RIH W/ 8-3/8" D/O BHA F/ 1990 To 2007m W/ Wash Dn, NL-NG is in progress
136	2-Aug-25	D/O CMT Inside 9-5/8" CSG To 2034.5m (Top of 7" Tie-Back Sleeve); Pump 40bbl Hi-Vis Pill and CBU till Shakering out the pumped Hi-Vis Pill; POOH 8-3/8" D/O BHA to surface; P/U & M/U 5-7/8" D/O BHA and RIH To 1970m, Conn. TDS & Cont. RIH W/ 5-7/8" D/O BHA and Strart D/O CMT F/ 2035 To 2038m, While D/O CMT Inside PBR; D/O Pack of Bushing, NL-NG, is in progress

137	3-Aug-25	Cont. D/O Pack of Bushing W/ 6-1/8" D/O BHA To 2038.28m; Cont. RIH W/ 6-1/8" D/O BHA F/ 2038.28 To 2123m W/ Wash Dn; D/O Medium to Hard CMT W/ 6-1/8" D/O BHA F/ 2123 To 2178m; Pump 30bbl Hi-Vis Pill & CBU @ 2178m; Cont. RIH W/ 6-1/8" D/O BHA F/ 2178 To 2637m On Elevator
138	4-Aug-25	Cont. RIH W/ 6-1/8" D/O BHA F/ 2673 To 3593m; Pump 40bbl Hi-Vis Pill & CBU @ 3593m Till Shakering out the pumped Hi-Vis Pill; POOH 6-1/8" D/O BHA F/ 3593m To Surface On Elevator; P/U & M/U 3-3/4" Clean out BHA and RIH To 336m, F/U BHA & Break Circ. ; Cont. RIH W/ 3-3/4" Clean out BHA F/ 336 To 1028m, NL-NG
139	5-Aug-25	Cont. RIH W/ 3-3/4" Clean out BHA F/ 1028 To 3593.5m (5" L.Lap); Conn. TDS & Cont. RIH W/ 3-3/4" Clean out BHA W/ Wash Dn F/ 3593.5 To 3876m; Pump 40bbl Hi-Vis Pill & CBU @ 3876m (5" F.Collar Depth) Till Shakering out the pumped Hi-Vis Pill; POOH 3-3/4" Clean out BHA F/ 3876 To 1320m On Elevator,
140	6-Aug-25	Cont. POOH 3-3/4" Clean out BHA F/ 1320m To Surface, Run SBT Log For 5" LNR, Commence Data Acquisition Logging Up F/ 3875 To 3545m, Log Up in Interval 3850 To 3745m based on Client's Request for Verification, POOH Wireline Logging Tool String To Surface; P/U & M/U 9-5/8" Scraper BHA and RIH To 2034m, Scraping Passes On 9-5/8" Dry Test PKR Setting Interval; Pump 40bbl Hi-Vis Pill @ 2021m, CBU
141	7-Aug-25	POOH with 9-5/8" Scraper to surf. RIH with 9-5/8"Dry Test Tool String as Program to 2015m with F/U 732.7m of Strg W/ Drill water (62.4 pcf) as a water Cushion at 5-Std intervals, Set PKR DST
142	8-Aug-25	Perfoem 9-5/8" Dry Test as Program, POOH to Surface
143	9-Aug-25	Perfoem 9-5/8" Dry Test as Program, POOH to Surface & RIH With 3-3/4" M.M.J.Mill to 3876m, Spot 26BBL Brine
144	10-Aug-25	Spot 26BBL Brine (CaCl2, 84pcf), POOH to 595m
145	11-Aug-25	Wait on Client to Receive Material while Slow Circ C.W.H
146	12-Aug-25	Cont. Wait on OEOC to Receive TDS while Slow Circ C.W.H. R/U Wireline as program. Wait on Daylight.
147	13-Aug-25	Wait on Daylight. Perform Perforation Operation as Program Totally 3 Run
148	14-Aug-25	Wait on Daylight. Perform Perforation Run#4, POOH to surface & R/D Wireline Tools. Change Top Rams to 2-78" * 5" variable & Test it , OK. Install Wear bushing. P/U & RIH with 3-3/4" Clean out BHA including : (3-3/4" M.M.J.Mill + 7 STD 3-1/8" D.C + 5 STD 2-7/8" D.P) to 338m
149	15-Aug-25	Cont RIH to To 3876m (5" F.Coller) With Break Circ Each 15 STD W/Nl.NG. 'Circ. BTM's UP

150	16-Aug-25	Circ BTM's UP & Spot 20 BBL Non Solid (Cacl2, 84 PCF). POOH On Elavator to Surface while L/D 5 STD's 2-7/8" D.P & 6 STD's 3-1/8" D.C (Jts by Jts) and fill up the well, NL.NG.
151	17-Aug-25	Cont POOH to Surf and L/D All Useless Tubular in Derrick. Run in hole with 7" Scraper BHA to 1240m
152	18-Aug-25	Cont RIH to 3592m, Pump 50BBL Hi.Vis Pill as Spacer. Disp whole well With 650BBl (84Pcf , Non solid Comp. Fluid) and Got 50BBL contaminated with mud Return and Dump 200BBl (84Pcf) Mud & 50 BBL Hi.Vis Pill. Flow Check the well for 1hrs, Static. Start POOH with 7" Scraper from 3592m to 2932m meanwhile L/D all 5" D.P (Jts by Jts)
153	19-Aug-25	Cont POOH with 7" Scraper from 2932m to 227m meanwhile L/D 5" & 3-1/2" D.P (Jts by Jts)
154	20-Aug-25	Cont L/D All Tublur in Derrick in Progress (Jts by Jts) . Run Comp. String as per program to 130m
155	21-Aug-25	Cont. RIH W/ 7" Comp. Strg F/ 130 To 474m; P/U & Ass. 2.80" Guage Ring, RIH W/ Same Tool String to Top of SSD (Max ID: 2.750"), Ok, POOH to surface and R/D Slick Line Eqp. ; R/U CMT Unit and Connect Chiksan pipes to Circ. Swage, Perform Comp. Strg Press. Test at 474m W/ 6000psi, 15min, Ok; Cont. RIH W/ 7" Comp. Strg F/ 474 To 1300m, While Clean & Wash Connections; use Thread Seal Compound, and Torque/Turn Monitoring System; secure CILs using Cross Coupling Cable Protectors & Hold Pressure in both CILs & Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.
156	22-Aug-25	Cont. RIH W/ 7"Comp. Strg W/ 11Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 146Jts) F/ 1300 To 1413m; R/U CMT Unit and Connect Chiksan pipes to Circ. Swage, Perform Comp. Strg Press. Test at 1413m W/ 6000psi, 15min, Ok; Cont. RIH W/ 7"Comp. Strg W/ 167 Jts 4-1/2" TBG [18.9#, L-80,HSM3] (Totally: 213 Jts) F/ 1413 To 2050m; Obs. Hold up Comp. Strg Weight @ 2050m, Attempt to Pass This Point, No Success, Decide to POOH 7" Comp. Strg to surface and Check the same; RIH W/ 2.750" SB To 2025m; Retrieve Check Valve; POOH 7"Comp. Strg F/ 2050 To 2004m, NL-NG.
157	23-Aug-25	Cont. POOH 7"Comp. Strg F/ 2004 To 340m, While L/D TBGs Jt by Jt & Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.
158	24-Aug-25	Cont. POOH 7"Comp. Strg F/ 340m To Surface, While L/D TBGs Jt by Jt & Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG; R/U Surface Slickline Tools, Install 7" Shooting Nipple; P/U & Assemble 6.100" Gauge Ring Tool String and RIH To 7" L.Lap Depth, Attempt to Pass 7" L.Lap, No Success; POOH Slickline Tool String To Surface; R/D Slickline Tools & Shooting Nipple; P/U & M/U 6-1/8" Clean out BHA and RIH To 941m, NL-NG.
159	25-Aug-25	Cont. RIH W/ 6-1/8" Clean out BHA F/ 941 To 2600m Followed by 3-1/2" & 5" DPs Jt by Jt To 941m, While Smooth Interval 2037-2038m (7" Tie-Back L.Lap); Check 7" LDC Interval &

		Previous 7" L.Lap W/ & W/O Parameters; Break Circ. At 700m-intervals; POOH 6-1/8" Clean out BHA F/ 2600 To 2177m On Elevator, While L/D All Extra Tubular Jt by Jt and Circ. C.W.H Thru. T.Tank,
160	26-Aug-25	Cont. POOH 6-1/8" Clean out BHA F/ 2177m To Surface On Elevator While L/D6-1/8" Concave Junk Mill & All Extra Tubular Jt by Jt; Ret. Wear Bushing and Prepare Rig Floor To Run 7" 7.5k Comp. Strg; R/U NDCO LNR Running Equip. ; Held PJSM, RIH W/ 7" 7.5k Comp. Strg as per plan, While C.W.H Thru. T.Tank,
161	27-Aug-25	R/U Slickline Equipment. Run 2.8" Gauge Ring to Top of SSD: Ok. R/D Slickline Tools; Press. Test Comp. Strg against SSD Check Valve W/ 6000 Psi, Ok, L/D Chicksan Pipe; Cont. RIH W/ 7" 7.5k Comp. Strg To 455m; Press. Test Comp. Strg against SSD Check Valve @ 455m W/ 6000 Psi, Ok; Cont. RIH W/ 7" 7.5k Comp. Strg To 1070m; Press. Test Comp. Strg against SSD Check Valve @ 1070m W/ 6000 Psi, Ok; Cont. RIH W/ 7" 7.5k Comp. Strg To 1138m, While Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.
162	28-Aug-25	Cont. RIH W/ 7" 7.5k Comp. Strg F/ 1138 To 2325m, While Press. Test Comp. Strg @ 1689m, @ 2308m W/ 6000psi, Ok; P/U & Assemble TRSSV Assy. ; Then Flush & Conn. 1/4" CL To TRSSV CL Port, Press. Test Conn. @ 7000psi, Ok, While Circ. C.W.H by Trip Tank & Monitor the Well, NL-NG.
163	29-Aug-25	Press. Test Comp. Strg against SSD Check Valve @ 2325m W/ 6000 Psi / 15min, Ok; TRSSV closed; Comp. Strg bled down to 1000 psi for Inflow Test; Pressure stabilized @ 1000 psi / 15 min; Ok; Cont. RIH W/ 7" 7.5k Comp. Strg F/ 2325 To 2363m; P/U & M/U 4-1/2" Fluted Swage Adapter + TBG HGR + TBG HGR Running Tool + Landing Joint; Press. Test Comp. Strg against SSD Check Valve @ 2374m W/ 6000 Psi / 15min; Ruture CIVs, Ok; R/U Slickline Tool; Set Protection Sleeve; Att.to Set Plug, Slickline Cable tenstion Drop, PooH to surface, work on recover fish in progress.
164	30 – Aug – 25	Set 3.437" Protection Sleeve; Set 2.750" Blanking Plug in No-Go; Set Equa. Prong match W/ 2.750" Plug of No-Go; RIH W/ 2.75" Shifting Tool To SSD Depth, Confirm SSD closed; Set PKR @ 2362m, Press. Test PKR W/ 6000psi, Ok; PKR Pull Test W/ 15klbf, Shear Expansion Joint W/ 20kblf; Land TBG HGR In THS; Pressure Test TBG HGR @ 1,000 Psi / 10 Min – Ok; Press. Test Comp. Strg @ 6,000 Psi / 15 Min – Ok; Set 3.437" Protection Sleeve; Ret. Prong; Ret. Plug; Press. Test PKR & HGR Seal 2,000 Psi/10 Min – Ok; Ret. TRSSV Protection Sleeve; Press. Test TWCV @ 6,000 Psi/15 Min – Ok
165	31 – Aug – 25	N/D BOP; Install TBG HGR M.M.Seal, N/U T.H.A Integrated W/ One 4-1/16" Gate Valve, meanwhile Pass 1/4" CL & 3/8" CILs Thru. CL & CIL Ports; Install 4-1/16" 10k Comp. FLG On T.H.A, L/U Chiksan pipes and Test Line on Comp. FLG, Press. Test

		M.M.Seal @ 6,000 Psi / 15 Min – Ok; Conn. 1/4" CL to Exit Block, Press. Test TRSSV @ 6,000 Psi / 15 Min – Ok; Press. Test Both CILs @ 2000 Psi / 15 Min – Ok; Press. Test Between Lower S – Seal & Cavity Thru. Test port @ 6,000 Psi / 15 Min – Ok; Press. Test Between Neck of HGR S – Seal & Cavity Thru. Test port @ 6,000 Psi / 15 Min – Ok;
166	1 – Sep – 25	N/D BOP; Install TBG HGR M.M.Seal, N/U T.H.A Integrated W/ One 4-1/16" Gate Valve, meanwhile Pass 1/4" CL & 3/8" CILs Thru. CL & CIL Ports; Install 4-1/16" 10k Comp. FLG On T.H.A, L/U Chiksan pipes and Test Line on Comp. FLG, Press. Test M.M.Seal @ 6,000 Psi / 15 Min – Ok; Conn. 1/4" CL to Exit Block, Press. Test TRSSV @ 6,000 Psi / 15 Min – Ok; Press. Test Both CILs @ 2000 Psi / 15 Min – Ok; Press. Test Between Lower S – Seal & Cavity Thru. Test port @ 6,000 Psi / 15 Min – Ok; Press. Test Between Neck of HGR S – Seal & Cavity Thru. Test port @ 6,000 Psi / 15 Min – Ok;

Table 14-1: AZNS-075-ST1 Daily Drilling Report Summary
