END OF WELL REPORT

AZADEGAN OIL FIELD

END OF WELL REPORT

AZNS – 207 (PAD #93), TYPE: IIIF

Drilling Department

DECEMBER 2025

MSA/OEOC			
	Position	**Name**	**Date & Signature**
Prepared by	Drilling Engineering Department	M.H. Haji Taleb Asgar Eyvazi	
Approved by	Project Head of Drilling Engineering	Behnam Parvaresh	
	Project Head of Drilling Operation	Piran Farzaneh	
	Project Manager	Rashid Ansari	
PPL			
	Position	**Name**	**Date & Signature**
Check & Approved by	Drilling Operation Manager	Majid Nariman	
	Subsurface Engineering Manager	Mehdi Salim Mehr	
	Project Manager	Soheil Shadizadeh	
	Subsurface Project Manager	Keivan Davoodi Nejad	

TABLE OF CONTENTS

1. General Information 11
1.1 Field Introduction 11
1.2 AZNS – 207 (F – 20) Well Location Map 13
2. Well History 14
2.1 Well Information 14
2.2 AZNS – 207 Well History 15
26" Hole Section Summary 15
17-1/2" Hole Section Summary 16
12-1/4" Hole Section Summary 24
8-3/8" Hole Section Summary 36
Completion Summary 41
Liner Lap Dry Test Report 44
2.3 AZNS-207 Well Sketch 48
2.4 Mud Weight vs. Depth 49
2.5 Bit Record Table 50
2.6 Bit Parameters Plot 51
2.7 Survey Data Table 53
2.8 Formation losses Report 56
2.9 Hole Problem 59
2.10 Well Montage 60
3. Time Analysis Report 61
3.1 Time vs. Depth Chart 61
3.2 Total Time Break-Down of Operation 62
Activity Breakdown Chart 68
Activity Break down Plot 69
3.3 NPT Break-Down 70
4. Geological & Logging Reports 76
4.1 Geological Report 76
stratigraphy 76
4.2 Logging and Testing Reports 99
Wireline Logging Reports 99
4.3 9-5/8" Casing Cement Evaluation Log Result 100
4.4 7" Liner Cement Evaluation Log Result 109
5. Bottom Hole Assembly Record 112
6. Casing Information 136
6.1 20" Casing 136
20" Casing Report 136
20" Casing Tally 137
6.2 13 – 3/8" Casing 138
13-3/8" Casing Report 138
13-3/8" Casing Tally 139
6.3 9-5/8" Casing 142

9-5/8" Casing Report 142
9-5/8" Casing Tally 143
6.4 7" Liner 148
7" Liner Report 148
7" Liner Tally 149
7. Cement Reports 150
7.1 20" Casing Cement Report 150
7.2 13-3/8" Casing Cement Report 151
7.3 9-5/8" Casing Cement Report 152
7" Liner Cement Report 153
8. Completion Report 154
8.1 Tubing Information 154
8.2 Completion Tools Specification Checklist 154
8.3 Assembling Test Report 158
8.4 Completion Operation Checklist 175
8.5 Well Head and X-mass tree Specification (installed) 179
8.6 Completion Sketch 180
8.7 Completion Tally 181
8.8 Completion String Pressure Test 188
9. Wellhead Report 193
9.1 Final Well Status 193
9.2 Wellhead & X-mass tree Specification 194
9.3 Wellhead sketch 196
X-mass Tree Specification (Section D) 197
9.4 X-mass Tree Pressure Test Report (Section D – before install) 198
9.5 X-mass Tree Pressure Test Report (Section D – after install) 198
9.6 Wellhead Related Test Report 200
10. Drilling Fluid Information 207
10.1 26" Hole Section 207
Sections Remark: 207
Interval Information: 207
Drilling Fluid Type: 207
Interval Material Consumption Analysis: 208
Interval Volume Analysis: 209
Interval Daily Volume Break Down: 210
Interval Loss Distribution: 213
Interval Fluid Properties Recap: 214
Interval Solids Control Discussion: 218
10.2 17-1/2" Hole Section 219
Sections Remark: 219
Interval Information: 221
Drilling Fluid Types (main hole): 221
Drilling Fluid Types (side track): 222
Material Consumption Analysis (main hole): 223
Material Consumption Analysis (side track): 225

Volume Analysis (main hole): 227
Volume Analysis (side track): 228
Daily Volume Break Down (main hole): 229
Daily Volume Break Down (side track): 232
Loss Distribution (main hole): 235
Fluid Properties Recap (main hole): 237
Fluid Properties Recap (side track): 243
Solid Control Disscussion: 249

10.3 12-1/4" Hole Section 250

Sections Remark: 250
Interval Information: 252
Drilling Fluid Types: 252
Material Consumption Analysis: 253
Material Consumption Analysis: 255
Daily Volume Break Down: 256
Interval Loss Distribution: 259
Interval Fluid Properties Recap: 261
Solid Control Disscusion: 267

10.4 8-3/8" Hole Section 268

Sections Remark: 268
Interval Discussion: 269
Drilling Fluid Type: 270
Interval Material Consumption Analysis: 271
Interval Volume Analysis: 273
Interval Daily Volume Break Down: 274
Interval Loss Distribution: 276
Interval Fluid Properties Recap: 278
Interval Solid Control Discussion: 284

10.5 Completion Section 285

INHIBITED $CaBr_2$ BRINE 285
VOLUME AND MATERIAL CONSUMPTION 285

11. Waste Management Report 286

11.1 Waste Management Package 286
11.2 Waste Management End of Well Report 287
26" Hole Section Information 287
26" Hole Section Operation's Recap: 288
17 – 1/2" Hole Section Information 291
17 – 1/2" Hole Section Operation's Recap: 291
12 – 1/4" Hole Section Information 302
12 – 1/4" Hole Section Operation's Recap 303
8 - 3/8" Hole Section Information 313
8 - 3/8" Hole Section Operation's Recap 313

12. List of Contractors 317
13. Appendix 318

13.1 DDR Summary 318
Hole Section 12-1/4" 318

LIST OF TABLES

TABLE 2-1: AZNS-207 WELL INFORMATION 14
TABLE 2-2: AZNS-207 26" HOLE SECTION SUMMARY 15
TABLE 2-3: AZNS-207 17 – 1/2" HOLE SECTION SUMMARY 16
TABLE 2-4: AZNS-207 12 – 1/4" HOLE SECTION SUMMARY 24
TABLE 2-5: AZNS-207 8-3/8" HOLE SECTION SUMMARY 36
TABLE 2-6: AZNS-207 7" LINER INFORMATION 44
TABLE 2-7: AZNS-207 DOWNHOLE TEST RESULT DATA 47
TABLE 2-8: AZNS-207 BIT RECORD 50
TABLE 2-9: AZNS-207 BIT PARAMETERS PLOT 51
TABLE 3-1: AZNS-207 NPT TIME BREAK – DOWN (BASED ON CLIENT'S ORDER AND INFORMATION) 75
TABLE 4-1: AZNS-207 FORMATION & RESERVOIR SUB LAYER TOPS 81
TABLE 4-2: AZNS-207 WELL DATA SUMMARY 82
TABLE 4-3: AZNS-207 OPEN HOLE, CASING & MUD PROPERTIES 83
TABLE 4-4: AZNS-207 MUD LOSS & GAIN 84
TABLE 4-5: AZNS-207 HYDROCARBON SHOWS 85
TABLE 4-6: AZNS-207 PERFORATION DATA 86
TABLE 4-7: AZNS-207 SAMPLE INTERVAL & QUALITY (CUTTING COLLECTION) 96
TABLE 4-8: AZNS-207 LIST OF ELECTRICAL LOGS 99
TABLE 8-1: AZNS-207 COMPLETION TUBING INFORMATION 154
TABLE 8-2: AZNS-207 TOOLS SPECIFICATION 157
TABLE 8-3: AZNS-207 OPERATION CHECKLIST 178
TABLE 9-1: AZNS-207 STATUS 193
TABLE 9-2: AZNS-207 WELLHEAD SPECIFICATION 195
TABLE 9-3: AZNS-207 SECTION "D" SPECIFICATION 197
TABLE 9-4: AZNS-207 SECTION "D" PRESSURE TEST BEFORE INSTALLATION 198
TABLE 9-5: AZNS-207 SECTION "D" PRESSURE TEST AFTER INSTALLATION 199
TABLE 11-1: AZNS-207 WELL WASTE MANAGEMENT INFORMATION 286
TABLE 11-2: AZNS-207 26"" HOLE SECTION WASTE MANAGEMENT INFORMATION 287
TABLE 11-3: AZNS-207 8-3/8" HOLE WASTE MANAGEMENT INFORMATION 313
TABLE 13-1: AZNS-207 DAILY DRILLING REPORT SUMMARY 332

LIST OF FIGURES

FIGURE 1-1: SOUTH AZADEGAN OILFIELD LOCATION MAP 12
FIGURE 1-2: AZNS–207 (F-20) WELL LOCATION MAP 13
FIGURE 2-1: AZNS-207 DRY TEST EVENT 45
FIGURE 2-2: AZNS-207 BOTTOM BT CHART 46
FIGURE 2-3: AZNS-207 MIDDLE BT CHART 46
FIGURE 2-4: AZNS-207 WELL SKETCH 48
FIGURE 2-5: AZNS-207 MW VS. DEPTH CHART 49
FIGURE 2-6: BIT PARAMETERS CHART 52
FIGURE 3-1: AZNS-207 WELL TIME VS. DEPTH CHART 61
FIGURE 3-2: AZNS-207 NPT BREAK-DOWN CHART 70
FIGURE 4-1: AZNS-207 SIDE – TRACK CROSS SECTION 97
FIGURE 4-2: AZNS-207 SIDE – TRACK PLAN VIEW 98
FIGURE 4-3: AZNS-207 9-5/8" CMT EVALUATION LOG 108
FIGURE 4-4: AZNS-207 7" CMT EVALUATION LOG 111
FIGURE 8-1: AZNS-207 TRSSSV TEST REPORT 158
FIGURE 8-2: AZNS-207 TRSSSV CONNECTIONS GRAPH 159
FIGURE 8-3: AZNS-207 PERMANENT PACKER TEST REPORT 160
FIGURE 8-4: AZNS-207 ANCHOR SEAL TEST REPORT 161
FIGURE 8-5: AZNS-207 PERMANENT PACKER CONNECTIONS GRAPH 162
FIGURE 8-6: AZNS-207 SSD TEST REPORT 163
FIGURE 8-7: AZNS-207 SSD CONNECTION & PRESSURE TEST GRAPH 164
FIGURE 8-8: AZNS-207 EXPANSION JOINT TEST REPORT 165
FIGURE 8-9: AZNS-207 EXPANSION JOINT CONNECTION & PRESSURE TEST GRAPH 166
FIGURE 8-10: AZNS-207 LANDING NIPPLE TEST REPORT 167
FIGURE 8-11: AZNS-207 LANDING NIPPLE CONNECTION & PRESSURE TEST GRAPH 168
FIGURE 8-12: AZNS-207 FIRST CIV TEST REPORT 169
FIGURE 8-13: AZNS-207 FIRST CIM TEST REPORT 170
FIGURE 8-14: AZNS-207 FIRST CIM CONNECTION & PRESSURE TEST GRAPH 171
FIGURE 8-15: AZNS-207 SECOND CIV TEST REPORT 172
FIGURE 8-16: AZNS-207 SECOND CIM TEST REPORT 173
FIGURE 8-17: AZNS-207 SECOND CIM CONNECTION & PRESSURE TEST GRAPH 174
FIGURE 8-18: AZNS-207 COMPLETION SKETCH 180
FIGURE 8-19: AZNS-207 COMPLETION TALLY 187
FIGURE 8-20: AZNS-207 TUBING PRESSURE TEST GRAP 192
FIGURE 9-1: AZNS-207 WELLHEAD SKETCH 196
FIGURE 9-2: AZNS-207 WELLHEAD & XMASS TREE CHECKLIST 201
FIGURE 9-3: AZNS-207 WELLHEAD MOM BEFORE INSTALLATION 202
FIGURE 9-4: AZNS-207 X-MASS TREE PRESSURE TEST GRAPH BEFORE INSTALLATION 204
FIGURE 9-5: AZNS-207 WELLHEAD MOM AFTER INSTALLATION 205
FIGURE 9-6: AZNS-207 BODY & METAL SEAL OF X-MASS TREE PRESSURE TEST GRAPH 206
FIGURE 10-1: AZNS-207 FLUID PROPERTIES RECAP 207
FIGURE 10-2: AZNS-207 MATERIAL CONSUMPTION ANALYSIS 208
FIGURE 10-3: AZNS-207 MUD CHEMICAL USAGE GRAPH 208
FIGURE 10-4: AZNS-207 EFFECTIVE CONCENTRATION CHART 209
FIGURE 10-5: AZNS-207 VOLUME ANALYSIS TABLE 209
FIGURE 10-6: AZNS-207 VOLUME ANALYSIS CHART 210
FIGURE 10-7: AZNS-207 DAILY VOLUME BREAK DOWN TABLE 210
FIGURE 10-8: AZNS-207 DAILY VOLUME BREAK DOWN ANALYSIS GRAPH 211
FIGURE 10-9: AZNS-207 DAILY VOLUME BREAK DOWN CHART 212
FIGURE 10-10: AZNS-207 LOSS DISTRIBUTION TABLE 213
FIGURE 10-11: AZNS-207 LOSS ANALYSIS GRAPH 213
FIGURE 10-12: AZNS-207 INTERVAL FLUID PROPERTIES RECAP 214
FIGURE 10-13: AZNS-207 DENSITY CHART 214

FIGURE 10-14: AZNS-207 VISCOSITY CHART 215
FIGURE 10-15: AZNS-207 PV & YP CHART 215
FIGURE 10-16: AZNS-207 PH CHART 216
FIGURE 10-17: AZNS-207 CALCIUM CHART 216
FIGURE 10-18: AZNS-207 TOTAL HARDNESS CHART 217
FIGURE 10-19: AZNS-207 SOLID PERCENTAGE CHART 217
FIGURE 10-20: AZNS-207 CHLORIDE CHART 218
FIGURE 10-21: AZNS-207 SOLID CONTROL TABLE 218
FIGURE 10-22: AZNS-207 17-1/2" (MAIN HOLE) FLUID PROPERTIES RECAP TABLE 221
FIGURE 10-23: AZNS-207 17-1/2" (SIDE TRACK) FLUID PROPERTIES RECAP TABLE 222
FIGURE 10-24: AZNS-207 17-1/2" (MAIN HOLE) MATERIAL CONSUMPTION ANALYSIS TABLE 223
FIGURE 10-25: AZNS-207 17-1/2" (MAIN HOLE) MUD CHEMICAL USAGE GRAPH 224
FIGURE 10-26: AZNS-207 17-1/2" (SIDE TRACK) MATERIAL CONSUMPTION ANALYSIS TABLE 225
FIGURE 10-27: AZNS-207 17-1/2" (SIDE TRACK) MUD CHEMICAL USAGE GRAPH 226
FIGURE 10-28: AZNS-207 17-1/2" (MAIN HOLE) VOLUME ANALYSIS TABLE 227
FIGURE 10-29: AZNS-207 17-1/2" (MAIN HOLE) VOLUME ANALYSIS CHART 227
FIGURE 10-30: AZNS-207 17-1/2" (SIDE TRACK) VOLUME ANALYSIS TABLE 228
FIGURE 10-31: AZNS-207 17-1/2" (SIDE TRACK) VOLUME ANALYSIS CHART 228
FIGURE 10-32: AZNS-207 17-1/2" (MAIN HOLE) DAILY VOLUME BREAK DOWN TABLE 229
FIGURE 10-33: AZNS-207 17-1/2" (MAIN HOLE) DAILY VOLUME BREAK DOWN CHART 230
FIGURE 10-34: AZNS-207 17-1/2" (MAIN HOLE) LOSSES ANALYSIS GRAPH 231
FIGURE 10-35: AZNS-207 17-1/2" (SIDE TRACK) DAILY VOLUME BREAK DOWN TABLE 232
FIGURE 10-36: AZNS-207 17-1/2" (SIDE TRACK) DAILY VOLUME BREAK DOWN CHART 233
FIGURE 10-37: AZNS-207 17-1/2" (SIDE TRACK) DAILY VOLUME BREAK DOWN ANALYSIS GRAPH 234
FIGURE 10-38: AZNS-207 17-1/2" (MAIN HOLE) LOSS DISTRIBUTION TABLE 235
FIGURE 10-39: AZNS-207 17-1/2" (MAIN HOLE) LOSS ANALYSIS GRAPH 236
FIGURE 10-40: AZNS-207 17-1/2" (MAIN HOLE) FLUID PROPERTIES RECAP TABLE 237
FIGURE 10-41: AZNS-207 17-1/2" (MAIN HOLE) DENSITY CHART 238
FIGURE 10-42: AZNS-207 17-1/2" (MAIN HOLE) VISCOSITY CHART 238
FIGURE 10-43: AZNS-207 17-1/2" (MAIN HOLE) PV & YP CHART 239
FIGURE 10-44: AZNS-207 17-1/2" (MAIN HOLE) PH CHART 239
FIGURE 10-45: AZNS-207 17-1/2" (MAIN HOLE) CALCIUM CHART 240
FIGURE 10-46: AZNS-207 17-1/2" (MAIN HOLE) TOTAL HARDNESS CHART 240
FIGURE 10-47: AZNS-207 17-1/2" (MAIN HOLE) SOLID PERCENTAGE CHART 241
FIGURE 10-48: AZNS-207 17-1/2" (MAIN HOLE) CHLORIDE CHART 241
FIGURE 10-49: AZNS-207 17-1/2" (MAIN HOLE) WATERLOSS PERCENTAGE CHART 242
FIGURE 10-50: AZNS-207 17-1/2" (SIDE TRACK) FLUID PROPERTIES RECAP TABLE 243
FIGURE 10-51: AZNS-207 17-1/2" (SIDE TRACK) DENSITY CHART 243
FIGURE 10-52: AZNS-207 17-1/2" (SIDE TRACK) VISCOSITY CHART 244
FIGURE 10-53: AZNS-207 17-1/2" (SIDE TRACK) PV & YP CHART 244
FIGURE 10-54: AZNS-207 17-1/2" (SIDE TRACK) PH CHART 245
FIGURE 10-55: AZNS-207 17-1/2" (SIDE TRACK) CALCIUM CHART 245
FIGURE 10-56: AZNS-207 17-1/2" (SIDE TRACK) TOTAL HARDNESS CHART 246
FIGURE 10-57: AZNS-207 17-1/2" (SIDE TRACK) SOLID PERCENTAGE CHART 246
FIGURE 10-58: AZNS-207 17-1/2" (SIDE TRACK) CHLORIDE CHART 247
FIGURE 10-59: AZNS-207 17-1/2" (SIDE TRACK) WATERLOSS PERCENTAGE CHART 247
FIGURE 10-60: AZNS-207 17-1/2" (SIDE TRACK) KCL % WT CHART 248
FIGURE 10-61: AZNS-207 17-1/2" (SIDE TRACK) MBT CHART 248
FIGURE 10-62: AZNS-207 17-1/2" SOLID CONTROL EQUIPMENT TABLE 249
FIGURE 10-63: AZNS-207 12-1/4" DRILLING FLUID TYPE TABLE 252
FIGURE 10-64: AZNS-207 12-1/4" MATERIAL CONSUMPTION ANALYSIS TABLE 253
FIGURE 10-65: AZNS-207 12-1/4" MUD CHEMICAL USAGE GRAPH 254
FIGURE 10-66: AZNS-207 12-1/4" EFFECTIVE CONCENTRATION CHART 254
FIGURE 10-67: AZNS-207 12-1/4" MATERIAL CONSUMPTION ANALYSIS TABLE 255

FIGURE 10-68: AZNS-207 12-1/4" VOLUME ANALYSIS CHART 255
FIGURE 10-69: AZNS-207 12-1/4" DAILY VOLUME BREAK DOWN TABLE 257
FIGURE 10-70: AZNS-207 12-1/4" DAILY VOLUME BREAK DOWN CHART 258
FIGURE 10-71: AZNS-207 12-1/4" INTERVAL LOSS DISTRIBUTION TABLE 259
FIGURE 10-72: AZNS-207 12-1/4" INTERVAL LOSS ANALYSIS GRAPH 260
FIGURE 10-73: AZNS-207 12-1/4" INTERVAL FLUID PROPERTIES RECAP TABLE 262
FIGURE 10-74: AZNS-207 12-1/4" DENSITY CHART 262
FIGURE 10-75: AZNS-207 12-1/4" VISCOSITY CHART 263
FIGURE 10-76: AZNS-207 12-1/4" PV & YP CHART 263
FIGURE 10-77: AZNS-207 12-1/4" PH CHART 264
FIGURE 10-78: AZNS-207 12-1/4" CALCIUM CHART 264
FIGURE 10-79: AZNS-207 12-1/4" TOTAL HARDNESS CHART 265
FIGURE 10-80: AZNS-207 12-1/4" SOLID % CHART 265
FIGURE 10-81: AZNS-207 12-1/4" CHLORIDE CHART 266
FIGURE 10-82: AZNS-207 12-1/4" WATER LOSS % CHART 266
FIGURE 10-83: AZNS-207 12-1/4" SOLID CONTROL EQUIPMENT TABLE 267
FIGURE 10-84: AZNS-207 8-3/8" DRILLING FLUID TYPE TABLE 270
FIGURE 10-85: AZNS-207 8-3/8" MATERIAL CONSUMPTION TABLE 271
FIGURE 10-86: AZNS-207 8-3/8" MUD CHEMICAL USAGE GRAPH 272
FIGURE 10-87: AZNS-207 8-3/8" EFFECTIVE CONCENTRATION CHART 272
FIGURE 10-88: AZNS-207 8-3/8" VOLUME ANALYSIS TABLE 273
FIGURE 10-89: AZNS-207 8-3/8" VOLUME ANALYSIS CHART 273
FIGURE 10-90: AZNS-207 8-3/8" DAILY VOLUME BREAK DOWN TABLE 274
FIGURE 10-91: AZNS-207 8-3/8" DAILY VOLUME BREAK DOWN CHART 275
FIGURE 10-92: AZNS-207 8-3/8" DAILY VOLUME BREAK DOWN GRAPH 276
FIGURE 10-93: AZNS-207 8-3/8" LOSS DISTRIBUTION TABLE 277
FIGURE 10-94: AZNS-207 8-3/8" LOSS DISTRIBUTION GRAPH 278
FIGURE 10-95: AZNS-207 8-3/8" FLUID PROPERTIES RECAP TABLE 279
FIGURE 10-96: AZNS-207 8-3/8" DENSITY CHART 279
FIGURE 10-97: AZNS-207 8-3/8" VISCOSITY CHART 280
FIGURE 10-98: AZNS-207 8-3/8" PV & YP CHART 280
FIGURE 10-99: AZNS-207 8-3/8" PH CHART 281
FIGURE 10-100: AZNS-207 8-3/8" CALCIUM CHART 281
FIGURE 10-101: AZNS-207 8-3/8" TOTAL HARDNESS CHART 282
FIGURE 10-102: AZNS-207 8-3/8" SOLID % CHART 282
FIGURE 10-103: AZNS-207 8-3/8" CHLORIDE CHART 283
FIGURE 10-104: AZNS-207 8-3/8" WATER LOSS % CHART 283
FIGURE 10-105: AZNS-207 8-3/8" KCL % WT CHART 284
FIGURE 10-106: AZNS-207 8-3/8" SOLID CONTROL EQUIPMENT 285
FIGURE 10-107: AZNS-207 COMPLETION SECTION VOLUME & MATERIAL CONSUPMTION 285
FIGURE 11-1: 26" HOLE SECTION SOLID HANDLING SYSTEM TABLE 288
FIGURE 11-2: 26" HOLE SECTION SOLID HANDLING SYSTEM GRAPH 288
FIGURE 11-3: 26" HOLE SECTION SOLID HANDLING SYSTEM ANALYSIS TABLE 288
FIGURE 11-4: 26" HOLE SECTION DEWATERING TABLE 289
FIGURE 11-5: 26" HOLE SECTION DEWATERING ANALYSIS TABLE 289
FIGURE 11-6: 26" HOLE SECTION DEWATERING GRAPH 289
FIGURE 11-7: 26" HOLE SECTION CHEMICAL TABLE 290
FIGURE 11-8: 17 – 1/2" HOLE SECTION SOLID HANDLING SYSTEM TABLE 293
FIGURE 11-9: 17 – 1/2" HOLE SECTION SOLID HANDLING SYSTEM GRAPH 293
FIGURE 11-10: 17 – 1/2" HOLE SECTION SOLID HANDLING SYSTEM ANALYSIS TABLE 295
FIGURE 11-11: 17 – 1/2" HOLE SECTION DEWATERING TABLE 297
FIGURE 11-12: 17 – 1/2" HOLE SECTION DEWATERING ANALYSIS TABLE 299
FIGURE 11-13: 17 – 1/2" HOLE SECTION DEWATERING RECAP GRAPH 299
FIGURE 11-14: 17 – 1/2" HOLE SECTION CHEMICAL TABLE 301

FIGURE 11-15: 12 – 1/4" HOLE SECTION SOLID HANDLING SYSTEM TABLE 304
FIGURE 11-16: 12 – 1/4" HOLE SECTION SOLID HANDLING SYSTEM GRAPH 304
FIGURE 11-17: 12 – 1/4" HOLE SECTION SOLID HANDLING SYSTEM ANALYSIS TABLE 306
FIGURE 11-18: 12 – 1/4" HOLE SECTION DEWATERING TABLE 308
FIGURE 11-19: 12 – 1/4" HOLE SECTION DEWATERING ANALYSIS TABLE 310
FIGURE 11-20: 12 – 1/4" HOLE SECTION DEWATERING RECAP GRAPH 310
FIGURE 11-21: 12 – 1/4" HOLE SECTION CHEMICAL TABLE 312
FIGURE 11-22: 8 – 3/8" HOLE SECTION SOLID HANDLING SYSTEM TABLE 313
FIGURE 11-23: 8 – 3/8" HOLE SECTION SOLID HANDLING SYSTEM ANALYSIS TABLE 314
FIGURE 11-24: 8 – 3/8" HOLE SECTION SOLID HANDLING SYSTEM GRAPH 314
FIGURE 11-25: 8 – 3/8" HOLE SECTION DEWATERING TABLE 315
FIGURE 11-26: 8 – 3/8" HOLE SECTION DEWATERING ANALYSIS TABLE 315
FIGURE 11-27: 8 – 3/8" HOLE SECTION DEWATERING RECAP GRAPH 316
FIGURE 11-28: 8 – 3/8" HOLE SECTION CHEMICAL TABLE 316

1. General Information

1.1 Field Introduction

Azadegan South Oil Field is situated in West Karoun province on a large long-axis anticline with N-S trending with approximate dimensions about 20^{km} width and 60^{km} length near to Iran-Iraq border, to the east of Yaran Oil Field.

The trap area of the south Azadegan is limited to 43.2x17.2^{km}. The Azadegan Oil field was discovered in 1999, when Well AZN-1 was drilled vertically down to the Cretaceous Fahliyan Formation with total depth of 4,643^{m}. The results of this well, revealed the reservoir characteristics of the field. Following to the result of the well no. AZN-1, another 5 exploration wells was drilled in different parts of this huge field down to Fahliyan Formation. In the later stage the well No.10 assumed as exploration well for evaluation of deeper formations. This well was drilled in 2008, down to the depth of 5340^{m} (Neyriz Fm.), mainly to evaluate the Jurassic formations.

Based on the exploration wells results, carbonate reservoir of Sarvak Formation is broadly developed in Azadegan Field. This formation was penetrated in all of seven exploration wells (AZN-1, AZN-2, AZN-3, AZN-4, AZN-5, AZN-6 and AZN-10). Clastic oil-bearing zones of Kazhdumi Formation developed in main anticline of Azadegan Field, extending from north to center of South Azadegan. The Clastic oil-bearing zones of Gadvan Formation developed only in crest area and south parts of South Azadegan Filed, which was discovered by AZN-1 in crest and AZN-4 in south parts. The carbonates of Fahliyan Formation also developed in Azadegan field, but the oil reservoir of this formation developed in South part of South Azadegan.

The Azadegan Field is an elongated anticline, trending in N-S direction, belonging to "Arabian Trend".

The stratigraphy sequence of the field includes AghaJari, Gachsaran, Asmari, Pabdeh/Jahrum, Pabdeh, Gurpi, Ilam, Laffan, Sarvak, Kazhdumi, Dariyan, Gadvan and Fahliyan Formations, from top to bottom. This sequence in well no AZN-10, the deepest up to now drilled well of the field, continues with Garau, Gotnia, Najmah, Sargalu, Alan, Mus and Neyriz formations.

The Dominant lithofacies of Sarvak Formation are Rudist-bearing packstone and partially grainstone, which contains abundant bioclasts. Some other facies like matrix-dominated wackestone and mudstone are also found.

The AZADEGAN Oilfield is located in Khuzestan province and is approximately located 80 Kilometers West of Ahwaz City, near to Iran-Iraq Border. It is in the Northwest of the YADAVARAN Field and in the West of JUFEYR Field. the average monthly Temperature is 45$^{\circ C}$ in summer, and highest temperature is 52$^{\circ C}$. The lowest temperature is -4.4$^{\circ C}$ in winter. Maximum rainfall is 78^{mm} in February, winter Season.

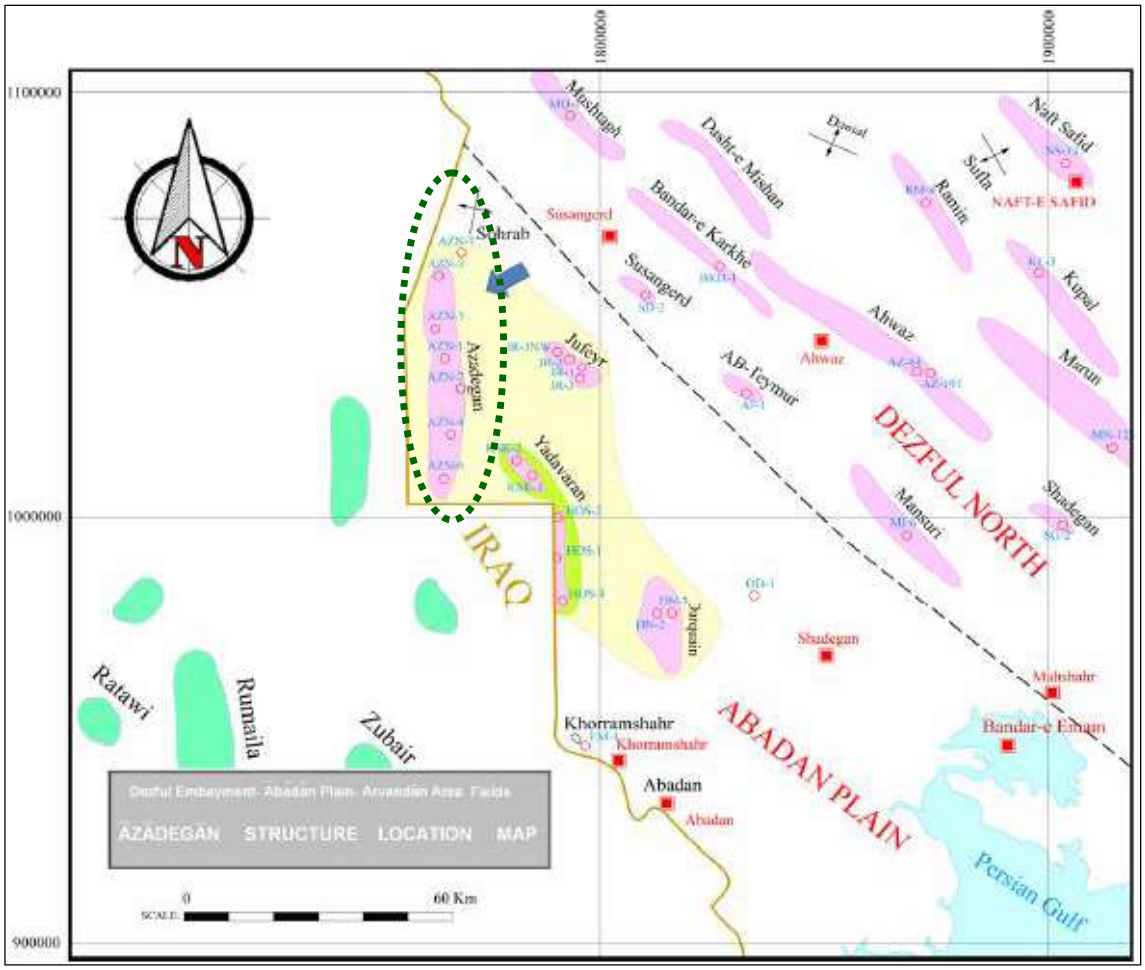


Figure 1-1: South Azadegan Oilfield Location Map

1.2 AZNS – 207 (F – 20) Well Location Map

AZNS – 207 (F – 20), which is Fahliyan producer as a vertical well, is planned to be drilled in pad-93, located amongst AZNS-070-ST2 & AZNS-049 wells as Fahliyan wells & AZNS-173 as Gadvan well in the area-III. This well was supposed to be drilled in pad-72, then a decision was made by client to change the pad to a new location (pad-93), so the geoname was changed from G20 to F20.

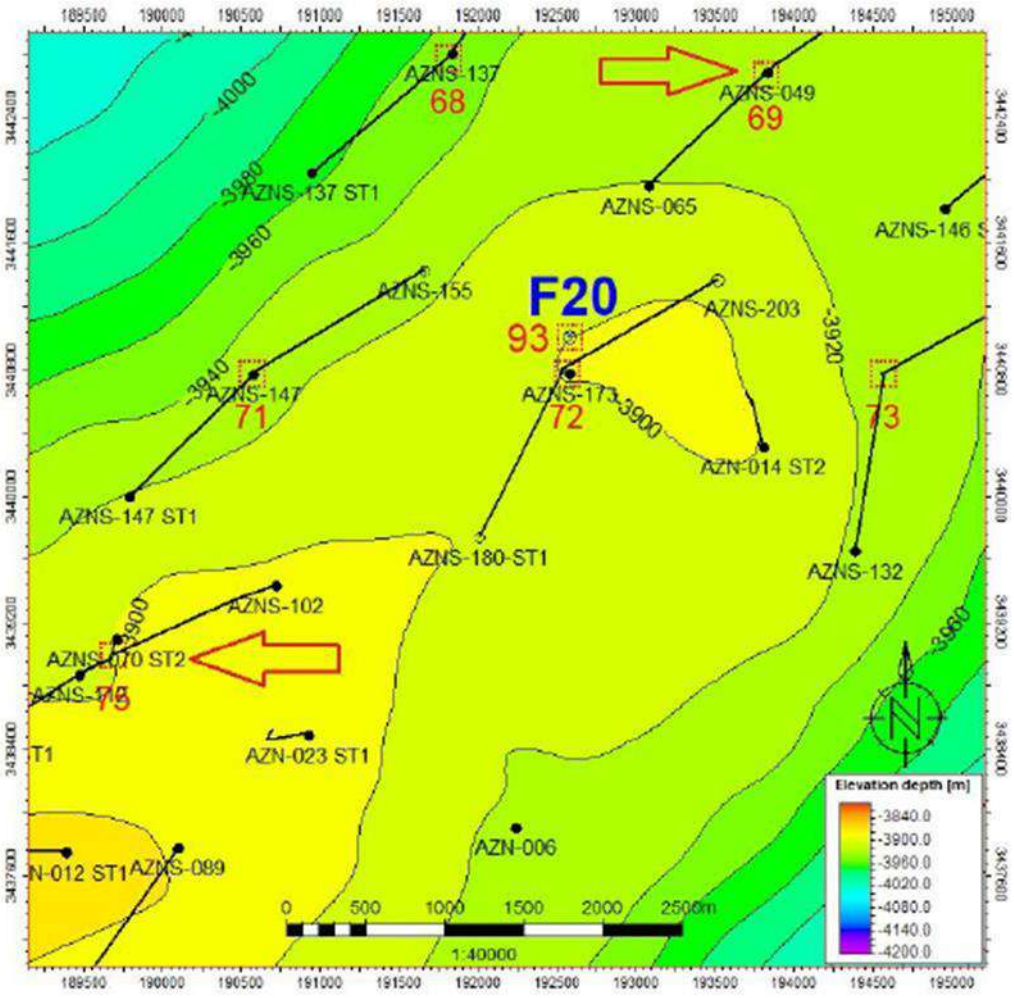


Figure 1-2: AZNS–207 (F-20) Well Location Map

2. Well History

2.1 Well Information

Rig name	208	**Owner**	PEDEC/PPL
Rig type	Land Rig 2000HP	**Contractor**	MSA/OEOC
Well Name	AZNS – 207	**Management Contractor**	MSA
Well Type	Vertical IIIF	**Field**	South Azadegan
Completion Type	4.5"*3.5" ,10K	**RTE**	14.45
Planned TD / Actual TD	4200^{m} / 4180^{m}	**GLE**	3.95
Surface Coordinate		E: 192,581^{m} - N: 3,441,012^{m}	
Target Coordinate		E: 192,676.53^{m} - N: 3,441,007.63^{m}	
Drilling & Suspension		**Completion**	
Spud Date	17 - Oct - 2024	**Spud Date**	13–Mar–2025
Released Date	17–Mar–2025	**Released Date**	17-Mar-2025
End of Drilling	17 – Feb – 2025	**End of Drilling**	-
Rig Days Actual/Plan	152 / 125	**Rig Days Actual/Plan**	-

Size (in)	Shoe Depth (mMD)	Specification
20	149	K-55, 94^{ppf}, BTC
13 – 3/8	1648	N-80, 68^{ppf}, BTC
9 – 5/8	3895	110SS, 53.5^{ppf}, HSM-3
7	3786-4179.5	TP110SS, 35^{ppf}, TPCQ

Table 2-1: AZNS-207 Well Information

2.2 AZNS – 207 Well History

The AZNS – 207 well was drilled by rig OEOC – 208. The rig was spud on 15 – Oct – 2024 at 18:00 & started to M/U & R/B stands in derrick to 16 – Oct – 2024 totally 85 STDs while prepare 390^{bbl} Bentonite mud. The operation described as following:

26" Hole Section Summary

Date	17 – October – 2024
Drilling Depth	151^{m}
Casing Size / Shoe	20", K – 55, 94$^{\#}$, BTC – 149^{m}
Formation	Aghajari
FIT Depth / Pressure Test	-
Mud Weight	66 – 70^{pcf}

Table 2-2: AZNS-207 26" Hole Section Summary

This section was drilled on 17 – Oct – 2024. Performed magnet trip w/ 15" fishing magnet. P/U & M/U new 26" MT bit & RIH to 14^{m} & tag the ground, commenced drlg to 32^{m} while POOH to surface due to low ROP at 21^{m} & 29^{m} and observed bit balled up, clean same. P/U & M/U 26" S. Stabilizer @ 20^{m}, RIH back to bottom & resume drlg to 60^{m}. run totco every 50^{m}. Continued drlg to 151^{m} (CSG point), performed condition trip, pumped & Circ. 60^{bbl} & spotted Hi-Vis pill. POOH 26" bit & drlg BHA to surface & L/D same. R/U 20" casing running equipment, run & cement 20" CSG (K-55, 94$^{\#}$, BTC) to 149^{m}, POOH to surface & L/D same, meanwhile drain & flush conductor pipe. H/U casing string weight by elevator & WOC to get hard. L/D mouse hole, L/D landing joint, L/D 30" conductor pipe & install 20 – ¾" 3k C.H.H, energize P-seal & pressure test to 400^{psi}, Ok. N/U 20 – ¾" BOP stack (20 – ¾" 3k * 3k DSA + spacer spool + drlg spool + double rams (blind rams, 5" fix rams) + Ann. Preventer. Tightened all nuts & side outlet valve & kill valve were connecting. Perform BOP pressure test. Retrieve plug tester & set wear bushing in place.

17-1/2" Hole Section Summary

Date	21 – October – 2024
Drilling Depth	1648.5^{m}
Casing Size / Shoe	13 – 3/8", N – 80, 68$^{\#}$, BTC / 1648^{m}
Formation	Pabdeh / Jahrum
Mud Weight	71 – 85^{pcf}

Table 2-3: AZNS-207 17 – 1/2" Hole Section Summary

This section was drilled on 21-Oct-2024 with new 17-1/2" MT bit & RIH to tag CMT, D/O hard CMT to 149^{m}. D/O shoe & smooth. D/O rat hole to 151^{m}. Commence drlg 17-1/2" hole section from 151^{m} to 165^{m}. due to obs. SPP dropped gradually 100^{psi}, decided to POOH to surface, observed 2 No. of nozzle seat areas washed out. Decision was made to RIH w/ 2 open nozzles. Commence drlg from 165^{m} to 451^{m}, B/R to 360^{m}, cont. POOH to 150^{m} & RIH back to BTM & commence drlg to 495^{m}, meanwhile pumped bentonite hi-vis pill & B/R & R/D last drilled stand. Continued drlg to 730^{m}, meanwhile prepared mud volume & ran mud & cleaners & centrifuge. Due to overflow shale shakers, Dec. FR to 800-850 GPM. Continued drlg to 793^{m}, while drlg Obs. stall string & bit bouncing several times. POOH bit to 750^{m}, run totco. Hard B/R to 650^{m}. Cont. POOH to surface, F/U the well, NL. Obs. balled up 17-1/2" S. Stab & bit, retrieved totco survey: 0.75 Deg. @ 750^{m} & L/D bit.

P/U & M/U 17-1/2" new PDC bit & previous BHA & RIH & commenced drlg from 793 to 800^{m} w/ low parameters, NL. Cont. drlg to 1107^{m}, B/R & R/D last drilled stand. POOH bit to 1020^{m} w/ good condition. Soft B/R to 900^{m}, Cont. POOH to 792^{m} w/ good hole condition as wiper trip. Ran back to 1050^{m}. Ran totco survey (Inc. 0.8 Deg). Washed & R/D to bottom @1107^{m} & resumed drlg to 1373^{m}. Due to low ROP decided POOH to surface. B/R to 1280^{m} while dropped totco survey at 1350^{m}. Cont. POOH drlg BHA to surface with good hole condition. F/U well w/ NL. Retrieved totco (Ind.: 0.5 Deg).

P/U & M/U new 17 – ½" new PDC bit & RIH. Medium wash & R/D to the bottom. Pumped 60^{bbl} & Circ. out hi-vis pill. Continued drlg to 1479^{m}, B/R & R/D last drilled stand w/NL. Due to observed severe FM losses 40 – 50BPG, stopped drlg & POOH 1 stand & pumped 50^{bbl} LCM pill (15^{ppb} Mica M & Kwik Seal M) & displaced same 10^{bbl} over. Continued POOH 2 more stands to 1395^{m}, monitored the well, 40 – 50BPH loss, wash & R/D to bottom w/3 – 5BPH loss. Pimped 20^{bbl} LCM pill & resume drlg to 1480.3^{m} w/2BPH loss.

While drlg 17-1/2" hole section at 1480.3[m], suddenly observed pressure drop 300[psi], checked surface pressure equipment & string weight, observed 8 – 10[klbs] string weight lost, decided to POOH string w/0-2BPH. POOH string to surface & observed string twisted off from top of first 9-1/2" DC (left in hole: 17-1/2" PDC bit + Bit Sub + 1jt 9-1/2" DC. Fish Length: 10.52[m]. TOF: 1469.78[m]).

P/U & M/U 12-3/4" * 15-1/2" overshot & fishing assembly & RIH to TOF. Established Circ. mud, engaged with the fish & POOH to 1450[m], suddenly sting weight dropped 8[klbs] & the fish was lost. Continued work on engaging & catching the fish by applying different parameters for several times, No success. POOH to surface & L/D overshot. P/U & M/U 11-3/4" * 15-1/2" fishing assembly & RIH to TOF w/0-2BPH loss. Engaged w/fish, commenced POOH fishing assay with the fish to 1220[m] while got overpull at several depths, Cont. POOH to surface & recovered the fish.

P/U & M/U recovered 17-1/2" PDC bit & RIH w/ drlg BHA to 1479[m] (1[m] off bottom) while W&R last stand w/ 1-4BPH loss. Pumped 30[bbl] hi-vis pill, Circ. & uniform mud weight in/out w/ 1-6BPH loss. Resumed drlg from 1480.3 to 1548[m] while stopped drlg several times & pumped LCM pill w/ 6-60BPH loss. Cont. drlg to 1562[m] while stopped drlg several times & pumped LCM pill w/ 10-40BPH loss. Due to low ROP Cont. drlg w/ different lithology, No success. 15-20BPH loss. Decided to POOH to surface in order to check bit condition while pumped & spotted 100[bbl] LCM pill. L/D PDC bit & P/U & M/U new 17-1/2" rock bit & commenced RIH w/ 5-10BPH loss to 714[m], took weight, Cont. RIH w. hard W/R to 1562[m] (BTM) w/5-20BPH loss. Worked on junk sub several times, resumed drlg f/ 1562 to 1564.5[m] w/10-25BPH loss. Pumped & spotted 100[bbl] LCM pill & POOH to 1460[m], in order to improve mud properties, Circ. bottom's up while activating system w/ fresh salt polymer mud 76[pcf]. Cont. POOH to surface & L/D junk sub & rock bit.

P/U & M/U new 17-1/2" PDC bit & drlg BHA & RIH to 1290[m] w/ soft to medium W&R. Cont. RIH w/ hard W&R to 1515.5[m], suddenly Obs. 300[psi] dropped in SPP & lost 1—20[klbs] string weight. Decided was make to POOH to check string. Obs. part of string left in hole. (17-1/2" PDC bit + Bit Sub + 2jts 9-1/2" DC, fish length: 19.84[m], TOF: 1495.66[m]).

P/U & M/U 11-3/4" overshot & RIH w/ fishing BHA to TOF w/ 2-4BPH loss. While washed down Obs. fish dropped to 1531[m], worked on fish w/ different parameters without any succeed. POOH to surface & L/D fishing BHA.

P/U & M/U 17-1/2" taper mill & RIH as hard wash & ream down to 700[m] w/ 1-3 BPH loss. Meanwhile add 1% Vol diesel to active mud system. POOH taper mill to surface & L/D totally 9 Jts 8-1/2" DC. P/U & M/U 7-7/8" center cut bit & RIH as soft wash & ream down to 1[m] above TOF at 1541.5[m]. Tried to continue W & R/D with no success. POOH string to 1536[m] & space out. L/U CMT line to string, pressure test CMT line to 500/3000[psi] for 15min. Ok. Pumped 27[bbl] 75[pcf] brine as spacer ahead. Mixed & pumped

848^{sxs} (SV: 204^{bbl} SW: 118^{pcf}) CMT "G" Delijan. Pumped 1.7^{bbl} 75^{pcf} brine as spacer behind. Displaced w/ 71^{bbl} 85^{pcf} mud w/ 7-8 BPH loss. B/O CMT line & POOH 10 stds to 1250^{m}, flush the string & POOH 10 more stds to 960^{m}. M/U FOSV on string, closed top rams & WOC to get hard. Open the well. Established Circ. Mud, while reciprocate string; 1-3 BPH Losses.

RIH w/ 7-7/8" Center Cut Bit f/ 960 to 1330m (Expected TOC). While W/D (100 GPM) last 3 Stds w/o any drag. CBU, meanwhile reciprocate string; 1-2 BPH Losses. Resume W/D (100 GPM) to 1486m w/o any drag; 1-2 BPH Losses. Try to W/D w/ max 560 GPM; No-Succ. CBU, Meanwhile L/U CMT Line & Prepare CMT Slurry solution.; 1-2 BPH Losses. L/U CMT line to string, Press test CMT line to 500/3000 psi for 15 min; Ok. Pump 27 bbl. 75 pcf brine as spacer ahead. Mix & Pump 848 sxs (SV:204 bbl. SW: 118 pcf) CMT "G" Delijan. Pump 1.7 bbl. 75 pcf brine as spacer behind. Displace w/ 68 bbl. 85 pcf mud (2 bbl. short); 25 bbl. total losses during CMT Job. B/O CMT Line, POOH 10 Stds to 1192m, Flush the string. Resume POOH w/ 7-7/8" C. Cut Bit to 130m. Circ. Across wellhead; 1-3 BPH Losses. Stop operation. Work on TDS Blowers & Fix same; while Circ. Thru string; 1-3 BPH Losses. Resume POOH w/ 7-7/8" C. Cut Bit to surface. Circ. Across wellhead; 1-3 BPH Losses.

L/D 3 Jts 9-1/2" DC. P/U & M/U 17-1/2" TCI Bit (Used, Kingdream, 415, Type: GAT415GC, 3 x 18/32" + C. Jet 16/32") + 9-1/2" Bit Sub (F. Valve In.) + 2 Jts 9-1/2" DC + 17-1/2" S. Stab (1/8" U.G) + 1 Jt 9-1/2" DC (Jt by Jt) + XOS + 1 Std 8-1/2" DC + XOS + 3 Stds 5" HWDP & Followed by 5" DPs to 790m on elevator w/ good hole condition, F/ U string & Break Circ. Every 15 Stds. Cont. RIH as soft to Med wash and ream down to 960m, Med to hard wash and ream down to 1330m; 2-3 BPH Losses. Hard W/R Parameters: Drag: 10-15 Klbs, Rot: 90 RPM, TQ: 2-8 Klbs. Ft, F.R: 750 GPM, SPP: 1550-1650 Psi.

Cont. Med to hard wash and ream down f/ 1330 to 1407m; 2-3 BPH Losses. Hard W/R Parameters: Drag: 10-15 Klbs, Rot: 90 RPM, TQ: 2-8 Klbs. Ft, F.R: 750 GPM, SPP: 1550-1650 Psi. D/O Med. CMT f/ 1407 to 1420m, Cont. D/O Hard CMT f/1420 to 1429m, 2-3BPH Losses. Check CMT Plug Hardness w/ 760 GPM, 2000 psi, 20-25klb Weight; "OK". Meanwhile D/O CMT Run Centrifuge as Super Clone Method & Work on Mud Rheology (Decrease Ca2+ & FL). Also Add. Fresh Mud & Solution to active mud system. 3-5 BPH Losses. Hard CMT D/Out Parameters: WOB:12klb, RPM:90, GPM:760, SPP:2000psi, TRQ: 6-8klb.ft, ROP: Avg. 5-2mph). CBU While reciprocate string; Obs. 100% CMT Sample & Confirm Hard CMT Interval by D.D Man. 3-5 BPH Losses. Cont. Circ. Mud & Cont. Work on mud properties while add Fresh Mud & 3% Vol KCl to mud active system. 3-5 BPH Losses. Commence POOH w/ 17-1/2" TCI Bit f/ 1429 to 1377m w/ pump out, Cont. B/R to 1350m till MN. 3-5 BPH Losses.

Cont. POOH w/ 17-1/2" TCI Bit f/ 1350m to surface on elevator w/ good hole condition, Meanwhile smooth tight hole intervals. Circ. Across Wellhead; 3-5 BPH Losses. Bit Dull Grading: (1-3-BT-G-E-I-BU-BHA). Tight Hole: 1377-1376m, 1334-1333m, 1325-

1321m, 962-959m. P/U 9-5/8" DHM (PDM, Lang Fang, AKO: 2.6 Deg, Lube: 7:8, Stage: 5), M/U 9-5/8" Float Sub, Perform DHM shallow test (300GPM 100psi & 600GPM 470psi). M/U 8 1/2" UBHO & 9 1/2" NMDC. Set MWD tools inside UBHO. Try to M/U 17 1/4" Stab Under DHM; No-Succ. M/U 17 1/4" Stab Under DHM & M/U 17 1/2" MT Bit (Used, Kingdream, 135, GAT135G, 3 X Open NZLs) Under Stab. Try to perform MWD Shallow Test; Obs. Failure to receive effective signal. change out MWD tools. Repeat again shallow test & Check MWD Pulse; "OK". Set AKO to 2.6 deg. P/U & M/U 8-1/2" DC. P/U & M/U 8" Drlg Jar & Check same; Obs. Leakage f/ alley key after seat in Slips. L/D 8" D. Jar. Wait on Rec. Another 8" Drlg Jar, While slow Circ. Mud thru string @ 60m; 2-3BPH Losses. Rec. 8" Drlg Jar. P/U & M/U 8" Drlg Jar c/w Flex Jt. Resume RIH w/ 1 Jt 8-1/2" DC + XOS + 1 Jt 5" HWDP & Followed by 5" DPs to 142m, F/U string & Break Circ.; "Ok".

Cont. RIH w/ 17-1/2" MT Bit & Directional BHA f/ 142 to 166m on elevator. Wash Down to 1419m w/ max 5-10 Klbs drag & Press Up several times. String stuck 438, 687, 1130m. Work on stuck upward; Got free w/ Max 100 Klbs Overpull. Meanwhile perform shallow test DHM (670 GPM, 930 psi); "OK". 3-4 BPH Losses.

Cont. Wash Down w/ 17-1/2" MT Bit & Directional BHA f/ 1419 to 1429.4m (TOC) w/ max 5-10 Klbs drag & Press Up several times. While String stuck @ 1424, 1425m. Work on stuck upward; Got free w/ Max 150 Klbs Overpull. Dress & Smooth 3m interval above TOC, meanwhile orient tool face on desirable azimuth (90 Deg); 3-4 BPH Losses. While Take SCR & Survey @ 1415m (Inc.: 0.9 Deg, Azimuth: 46 Deg). Commence Directional Drlg 17-1/2" HS (DHM AKO: 2.6 Deg) as time Drlg in slide mode to sidetrack the well f/1429.4 to 1439.5m, 3-4 BPHL. Directional Drlg Parameters: WOB: 2-12 Klbs, DHM SR: 0.132 Rev/Gal, DHM Rot: 92-96 RPM, F.R: 700-730 GPM, SPP: 1480-1780 Psi, ROP: 0.5-1 MPH

KOP Confirmed @ 1435m by MSA WSG.

Cont. Directional Drlg 17-1/2" HS (DHM AKO: 2.6 Deg) as time Drlg in slide mode to sidetrack the well f/1439.5 to 1447m, 2-3 BPH Losses. Directional Drlg Parameters: WOB: 10-12 Klbs, DHM SR: 0.132 Rev/Gal, DHM Rot: 96 RPM, F.R: 730 GPM, SPP: 1650-1780 Psi, ROP: 1-2 MPH

Circ. BTMs Up to take last sample while reciprocate string to smooth hole; 2-3 BPHL. Take Survey @ 1433m (Inc.: 3.4 Deg, Azi.: 85 Deg). Commence POOH w/ 17-1/2" MT Bit & Directional BHA f/ 1447 to 1420 as pump out w/ 25 Klbs overpull. Cont. POOH on elevator to 1350m w/ max 25 Klbs overpull. Cont. POOH on elevator f/ 1350 to surface w/ good hole condition; Circ. Across wellhead; 1-2 BPHL. L/D 17-1/2" MT Bit. Bit Dull: (1-1-WT-A-E-1/8"-BU/WO-BHA) & Stab & Bit 60% Bulled up. Meanwhile static flow check @ 130m; 1 BPHL. Check & Service MWD Tools. P/U & M/U 17-1/2" TCI Bit (Kingdream, Type: HJT517GL, 3 x 22/32" NZL) under 9-5/8" DHM (PDM, Lang Fang, AKO: 1.5 Deg, Lube: 7:8, Stage: 5, 17-1/4" Stab) + 9 5/8" Float Sub + 9

1/2" UBHO + 9 1/2" NMDC. Set MWD tools inside UBHO. Perform shallow test Motor & MWD Tools; "OK" (FR: 700, SPP: 1080 Psi). Change TDS saver sub. Resume RIH w/ 1 Std 9 1/2" DC + XOS + 1 Std 8 1/2" DC + 8" Drlg Jar c/w Flex Jt + 1 Std 8 1/2" DC + XOS + 3 Stds 5" HWDP & Followed by 5" DPs to 500m till MN, F/U string & Break Circ.; "Ok" 2-3 BPH Losses.

Cont. RIH w/ 17-1/2" TCI Bit & Directional BHA (DHM AKO: 1.5 Deg) f/ 500 to 1429m on elevator w/ good hole condition; F/U String & Break Circ. Every 10 Stds; 2-3 BPHL. Align Tool face to 90 Deg, Wash & Ream Down to 1447m. Meanwhile test DHM & MWD @ 500m "OK". Commence Directional Drlg 17-1/2" HS (DHM AKO: 1.5 Deg) in Rotation mode to sidetrack the well w/ Control parameters to get last survey f/1447 to 1462 m; 8-10BPHL. Meanwhile add 5 sxs/hr. (5 ppb) Limestone Chips F to active mud system. Cont. Directional Drlg as slide mode 1462 to 1467m Meanwhile add 5 sxs/hr. (5 ppb) Limestone Chips F to active mud system; 4-5 BPHL. Cont. Directional Drlg as rotation mode to 1472m Meanwhile add 5 sxs/hr. (5 ppb) Limestone Chips F to active mud system; 4-8 BPH Losses. Rotation Mode Drlg Parameters: WOB: 5-12 Klbs, Surface Rot: 30 RPM, TQ: 2-5 Klb. ft., DHM Rot: 94-99 RPM, F.R: 700-750 GPM, SPP: 1950-2300 Psi, ROP: 2 MPH Slide Mode Drlg Parameters: WOB: 10-15 Klbs, DHM Rot: 93 RPM, F.R: 700 GPM, SPP: 2000-2080 Psi, ROP: 1.2 MPH

B/R & R/D f/ 1472 to 1456m. Cont. Directional Drlg as slide mode to f/ 1472 to 1477m, 4-5 BPHL. Cont. Directional Drlg as rotation mode f/1477 to 1487m, 4-8 BPHL. Cont. Directional Drlg as slide mode f/1487 to 1492m, 4-6 BPHL. Cont. Directional Drlg as rotation mode f/1492 to 1497m, 3-5 BPHL. Cont. Directional Drlg as slide mode f/1497 to 1507m, 2-5 BPHL.

Rotation Mode Drlg Parameters: WOB: 5-20 Klbs, Surface Rot: 30 RPM, TQ: 2-5 Klb. ft., DHM Rot: 80-99 RPM, F.R: 600-750 GPM, SPP: 1500-2300 Psi, ROP: 1.8 MPH

Slide Mode Drlg Parameters: WOB: 10-15 Klbs, DHM Rot: 80-93 RPM, F.R: 600-700 GPM, SPP: 1500-2080 Psi, ROP: 1.5 MPH

Added 5 sxs/hr. Limestone Chips F to active mud system to reduce loss ratio.

Cont. Directional Drlg as rotation mode f/1507 to 1510m, 3-5 BPHL. Cont. Directional Drlg as slide mode f/1510 to 1513m, 2-5 BPHL. Cont. Directional Drlg as rotation mode f/1513 to 1515m, 2-4 BPHL. Cont. Directional Drlg as slide mode f/1515 to 1523m, 2-4 BPHL. Cont. Directional Drlg as rotation mode f/1523 to 1542m, 2-3 BPHL. Cont. Directional Drlg as slide mode f/1542 to 1547.5m, 2-4 BPHL. Cont. Directional Drlg as rotation mode f/1547.5 to 1552m, 2-3 BPHL. Due to low ROP decide to stop drlg and POOH to surf. Rotation Mode Drlg Parameters: WOB: 5-25 Klbs, Surface Rot: 30 RPM, TQ: 2-7 Klb. Ft. DHM Rot: 80-99 RPM, F.R: 600-750 GPM, SPP: 1500-2300 Psi, ROP: 2.2 MPH Slide Mode Drlg Parameters: WOB: 5-27 Klbs, DHM Rot: 80-93 RPM, F.R:

600-750 GPM, SPP: 1500-2300 Psi, ROP: 2.4 MPH. Added 5 sxs/hr. Limestone Chips F to active mud system to reduce loss ratio.

POOH directional BHA w/ pump out f/1552 to 1435m (K.O.P) M Try to Passed this point Several time w/diff. parameters, (passed w/ 95 Klbs O. pull) cont. POOH on elevator w/good Cond. f/1420m to 20m. 1-3 BPHL. Cont. POOH while Function test DHM, B/O & L/D 17-1/2" TCI Bit, B/O DHM Sleeve & L/D DHM. L/D MWD tools. P/U & M/U New DHM (PDM, Lang Fang, Lobe7:8, Stage: 5,), B/O 16-19/32" Sleeve. M/U 17-1/4"sleeve. Function tested DHM; OK. M/U 9 1/2" UBHO + 9 1/2" NMDC. Set MWD tools inside UBHO. Shallow tested DHM (630GPM 550-600psi). Set AKO: 1.5 Degree. P/U & M/U 17-1/2" PDC Bit (GEO DIAMOND, 6 Blade, 16MM, 5*20/32 & 3*18/32 NZL). 1-3 BPHL. "Cont. RIH w/ 1 Std 9 1/2"" DC + XOS + 1 Std 8 1/2"" DC + 8"" Drlg Jar c/w Flex Jt + 1 Std 8 1/2"" DC + XOS + 3 Stds 5"" HWDP & Followed by 5" DPs to 900m till MN, F/U string & Break Circ. 1-3 BPHL.

Cont. RIH w/ 17-1/2" PDC Bit and directional BHA f/ 900m to 1429m. Try to pass w/o circ. No success. Set tool face, stablish circ. Cont. wash down & Work on smooth KOP area to 1440m (still not able to pass w/o circ.) Cont. RIH w/ wash down to 1552m (BTM). 1-3 BPHL. Soft Wash down: 997-1027m, 1060-1090m, 1300-1370m, 1429-1552m. Resume drlg formation w/ 17-1/2" PDC Bit and directional BHA, 2-4 BPHL. as: Slide mode 1552-1558m Rot. mode: 1558-1564m Cont. drlg formation w/ 17-1/2" PDC Bit and directional BHA, 2-4 BPHL. as: Slide mode 1564-1567m Rot. mode: 1567-1571m

Cont. drlg formation w/ 17-1/2" PDC Bit and directional BHA, 1-3 BPHL. as: Rot. mode: 1571-1576m Slide mode 1576-1580m Rot. mode: 1580-1586m Slide mode 1586-1591m Rot. mode: 1591-1592.90m

Due to low ROP (Dec. to 0.5mph) stopped drlg, decided to POOH to surface. POOH w/ directional BHA f/ 1592.9 to 1060m. 1-2PBHL. Wash up: 1592.9-1541m On elevator: 1541-1060m

POOH w/ directional BHA on elevator f/ 1060m to surface. B/O and L/D Directional BHA & MWD Tools. L/D 17-1/2" PDC Bit. 1-2PBHL. BIT Dull Cond.: (6-8-RO-N/S/G-X-1/8"-BF-PR) P/U & M/U 17-1/2" Used Insert Bit (King Dream, 517, 3*22/32" Nozzle), Bit sub, 2Jts 9-1/2" DC, 17" Full Gauge S. Stab, 1 Jts 9-1/2" DC, XOS, 5Jt 8-1/2" DC, 8" D. Jar, 1 Jts 8-1/2" DC, XOS, 3Std 5" HWDP Followed by 5" DP to 1592.9m (BTM), 1-2BPH Loss. Took Weight @770 &1170m. Passed 17-1/2" Insert bit & 17" S. Stab @ K.O.P W/Max 5-10klb Drag., Smooth K.O.P W/S. Stab "OK". Pump 100bbl Hi-vis pill while Fan the bottom Several time to profile the Bit, resume drlg 17-1/2" HS f/ 1592.9 to 1594m till MN, 1-2 BPHL. Drilling Parameters: WOB: 5-15 Klbs, Rot: 50-150 RPM, TQ: 2-5 Klb.ft, F.R: 850 GPM, SPP: 2100-2300 Psi, ROP: 1 MPH

Cont. drlg 17-1/2" HS f/ 1594 to 1616m, 1-2 BPHL. Due to observe gradually decrease in SPP (80 psi) stop drlg, check MW in/out; OK, Check mud pumps and surface lines; OK. Take SCR observe 10-35 psi decrease in same GPM. Decided to POOH to surface.

Start POOH while check string for any wash out f/1616m to surface on elevator with good hole condition. 1-2BPH Loss. Obs. 2" wash on body of first 5" DP above BHA. Bit Dull Grade: 1-1-WT-A-E-I-No-PP M/U same 17-1/2" Used Insert Bit (King Dream, 517, 3*22/32" Nozzle), Bit sub, 2Jts 9-1/2" DC, 17" Full Gauge S. Stab, 1 Jts 9-1/2" DC, XOS, 5Jt 8-1/2" DC, 8" D. Jar, 1 Jts 8-1/2" DC, XOS, 3Std 5" HWDP Followed by 5" DP to 1616m (BTM), 1-2BPH Loss. Fan the bottom Several time to profile the Bit, resume drlg 17-1/2" HS f/ 1616 to 1617.5m till MN, 1-2 BPHL. Due to string bouncing applied different parameters.

Cont. drlg 17-1/2" HS f/ 1617.5 to 1636m, 1-2 BPHL. Drilling Parameters: WOB: 5-30 Klbs, Rot: 50-125 RPM, TQ: 2-5 Klb.ft, F.R: 600-750 GPM, SPP: 1250-1900 Psi, ROP: 0.5-1.5 MPH

Cont. drlg 17-1/2" HS f/ 1636 to 1648.5m (section TD), 1-2 BPHL. Drilling Parameters: WOB: 5-30 Klbs, Rot: 50-125 RPM, TQ: 2-5 Klb.ft, F.R: 600-750 GPM, SPP: 1250-1900 Psi, ROP: 0.5-1.5 MPH>> Due to string bouncing applied different parameters. Pump Hi-Vis pill periodically while drilling. Strat POOH w/ soft back reaming as wiper trip to 1420m till MN, 1-2 BPHL. Smooth the KOP interval several times, checked same without RPM & FR; OK

RIH wash down as wiper trip f/ 1420 to 1648.5m (BTM). 1-2 BPHL. Pumped & circ. out 50 bbl. Hi-Vis pill 1-2 BPHL. FR: 760gpm, SPP:1950psi Pump and spot 300 bbl. Hi-Vis pill at bottom. 1-2 BPHL. POOH on elevator f/ 1648.5 to surf. with good hole condition. B/O & L/D 17-1/2" B. Bit and 8-1/2" D. Jar. 1-2 BPHL. Bit Dull Grading: 2-3-WT-A-I-F-BT-TD Arrange rig floor, Retrieve wear bushing. R/U 13-3/8" Casing running equipment. Held P.J.S.M, P/U & M/U shoe track as: 13 3/8” F. Shoe + 2 Jts 13-3/8” CSG (68#, N-80, BTC) + 13 3/8” F. Collar, M/U swage, Check F. Shoe & F. Collar function; OK. Cont. RIH 13-3/8” CSG (68#, N-80, BTC) to 343m (Totally 30 Jts). Fill up every 10 Jts. Used centralizer as per program.

Cont. RIH 13-3/8” CSG (68#, N-80, BTC) f/ 343 to 400m (Totally 35 Jts). 1-2BPH Loss. Used centralizer as per Tally. M/U circ. Swage, Change TDS Links to 500-T, M/U fill up tools and spider elevator (slips type). 1-2BPH Loss. Cont. RIH 13-3/8” CSG (68#, N-80, BTC) f/ 400m to 1648.5m, Tag BTM, pull out STRG to 1648m (0.5mT Off BTM) Meanwhile use side door slips @ 827mt with 1-2BPH Loss L/D Fill up tools & excess CSG handling equipment. M/U circ. Swage, Stablish circulation. 1-2BPH Loss. Cont. circulate 1.2 Cap of CSG STRG while prepare cement solution Meanwhile Set CMT Equip. & L/U Related Lines Rig floor. 1-2BPH Loss. Cont. prepare tail cement solution & spacer in mud tank meanwhile circ. Through CSG STRG. 1-2 BPH Loss. L/up cement line on casing string & established circ. While P/up string weight by spider elevator &

L/D side door slips. Perform press test cement line with 500/1500psi for 10 min; OK. Mix and pump 20 bbl. Ch. Wash w/ pump truck. Pump 100 bbl. Spacer w/ rig pump, 1-2 BPH Loss.

PUMP 1202 BBL CMT SLURRY (94PCF, "G" DELIJAN, 2780 SXS) AS LEAD CMT, PUMP 135.5 BBL CMT SLURRY (118 PCF, "G" DELIJAN, 555 SXS) AS TAIL CMT, DROP TOP PLUG, DISPLACE CMT W/ 795 BBL MUD (85PCF), OBS BUMPING & PERFORM CIT W/ 1500PSI FOR 15MIN "OK". Did not get cement in return. Hold pressure inside casing until the cement get hard while H/U BOP & drop CSG HGR, slack off 50% off casing string weight. H/Off BOP & Cont. Weight on CMT to get 100% hard. Released casing string press to zero. Slack off 100%strg weight on casing HGR & press. Test to 1000psi, ok. R/D CMT head, H/U BOP Stack. Rough cut L.J & L/D same. N/D Hydrill, Double rams. Disconnect Kill line valves & Choke line valves. N/D Drilling spool. H/U BOP Stack. Rough cut L.J & L/D same. N/D Hydrill, Double rams. Disconnect Kill line valves & Choke line valves. Cont. Disconnect Kill line valves & Choke line valves. N/D Drilling spool. Final Cut CSG neck, Dress & Bevel same. Install 20-3/4" 3K x 13-5/8" 5K C.H.S. (MSP/Drillex, S/N: CS1806 XC230001) c/w 1 No. 2-1/16" 5K G. Valve in each side. Tighten all nuts. Inject Plastic packing & Energize P-Seals. Press Test between ring gasket / 1st P-Seal & between 1st / 2nd P-Seal to 1700 psi for 15 Min; Ok. N/U 13-5/8" 3K x 13-5/8" 10K DSA (Tie down flange), 10K Spacer spool, 10K Single pipe ram (5" Fix), 10K Double pipe ram (Shear-Blind/ 5" Fix), 5K Ann Preventer & Bell nipple. Tighten nuts & Connect Choke lines/Kill lines & Hydraulic hoses. Set 13-5/8" plug tester in place. Perform BOP Press test as NIOC policy, Press test Ann preventer to 500/2500 psi for 5/10 min; Ok. Press test 5" Fix BTM Ram, 5" Fix Top Ram to 500/4500 psi for 5/10 min; Ok

Cont. Perform BOP Press test as NIOC policy, Press test Shear/Blind Ram, All manual/HCR side outlet valve & C/M valves to 500/4500 psi for 5/10 min; Ok. Meanwhile rectify leakage. Press test burning line & related valve to 500/1000 psi for 10 min; Ok. Function test accumulator system, driller & auxiliary remote panels; Ok. Retrieve plug tester. Install 13-5/8" wear bushing in CHS. L/U CMT Line to 20" X 13-3/8" Ann. Press test line. Perform injectivity test; Pump & Inject 20 bbl. F. Water w/ 3 BPM rate 200 psi Press. L/D 1 Std 9-1/2" DC. P/U & M/U 3 Jts 8-1/2" DC and R/B Same. L/D 3 Stds 5" HWDP. P/U & M/U 3 Jts 5" HWPD and R/B Same. Mix & pump 170 bbl. 94pcf CMT Slurry as CMT Top job while monitor pumping Press. (150-300psi / 2-3BPM rate), Suddenly decrease Press to Zero. Stop pumping check Ann level; "Empty" & Close Ann. Valve. Wait on CMT to get hard. Meanwhile slip & cut 114 ft. 1-1/2" Drlg line. RIH w/ pendulum BHA as: P/U & M/U 12-1/4" PDC Bit (Burintekh, Used, NZL: 6X15/32) + Bit Sub (F. Valve, Baffle Plate in) + 3 Stds 8-1/2" DC (12-1/4" S. Stab (1/16" U.G @ 20m) + 8" Drlg Jar c/w Flex Jt + 1 Jt 8-1/2" DC + XOS (6-5/8" REG X 4-1/2" IF) + 3 Stds 5" HWDP & Followed by 5" DPs to 1590m till M.N. Meanwhile open Ann; Obs. Ann level is empty. F/U Ann w/ 10 bbl. 94 pcf CMT Slurry and got return. Stop pumping and flash the side valve.

Cont. RIH w/ 12-1/4" PDC Bit & Pendulum BHA to 1623.5 m, while D/O Hard CMT & Plugs. Run Totco survey @ 1623m (Inc.: 6 Deg). D/O 13-3/8" F. Collar, Cont. D/O Hard CMT to 1648m. D/O 13-3/8" Shoe. Meanwhile smooth F. Collar & Shoe interval several times. Commence Drlg 12-1/4" H.S f/ 1648 to 1653m. POOH to 1647m and Displace the well w/ 73 pcf mud; NL-NG. Wash and clean divider, under shakers. Run back to BTM, Resume Drlg 12-1/4" HS to 1654m. Drlg Parameters: WOB: 5-20 Klbs, Rot: 80-130 RPM, TQ: 2-8 Klb.ft, F.R: 300-700 GPM, SPP: 590-1800 Psi, Av. ROP: 0.6 MPH.

Cont. Drlg 12-1/4" HS f/ 1654 to 1678m. Drlg Parameters: WOB: 20-25 Klbs, Rot: 130 RPM, TQ: 2-10 Klb.ft, F.R: 700-750 GPM, SPP: 1300-1500 Psi, Av. ROP: 5 MPH. POOH to 13-3/8" CSG Shoe. Close Top Rams. Perform FIT to EMW 90 pcf; Apply 630 psi press stepwise, Hold press for 15 min, OK. Totally pump 3 bbl. 73 pcf mud & got same volume in return after bleed off.

12-1/4” Hole Section Summary

Date	15 – December – 2024
Drilling Depth	3895^{m}
Casing Size / Shoe	9 – 5/8”, 110SS, $53.5^{\#}$, HSM-3 / 3895^{m}
Formation	Pabdeh / Jahrum / U.Gurpi / Tarbur / L.Gurpi / Ilam / Laffan / Sarvak / Kazhdumi / Dariyan / Gadvan
Mud Weight	$77 – 82^{pcf}$

Table 2-4: AZNS-207 12 – 1/4" Hole Section Summary

Run back to BTM, Resume Drlg 12-1/4" HS to 1689m, meanwhile pump Hi-Vis Pill periodically; 0-2 BPH Losses. Due to Obs. Leakage f/ Lower IBOP; Stop drilling. POOH to 13-3/8" Shoe. While slow Circ. Thru string, Change lower IBOP and test same; "Ok". Run back to BTM w/ good hole condition. 0-2 BPH Losses. Resume Drlg 12-1/4" HS to 1713m, Meanwhile Pump 20 ppb (10 ppb Limestone Chips F + 5 ppb Fiber lock + 5 ppb Oyster Shell) Hi-Vis LCM Pill periodically & Add 5 Sxs/Hr. LCM to active system; 0-20 BPH Losses. Drlg Parameters: WOB: 10-25 Klbs, Rot: 100-160 RPM, TQ: 2-10 Klb.ft, F.R: 800-420 GPM, SPP: 1650-570 Psi, Av. ROP: 5 MPH.

Cont. Drlg 12-1/4" HS f/ 1713 to 1828m. Drlg Parameters: WOB: 10-30 Klbs, Rot: 110-160 RPM, TQ: 2-12 Klb.ft, F.R: 420-380 GPM, SPP: 570-470 Psi, Av. ROP: 5.5 MPH.

Cont. Drlg 12-1/4" HS f/ 1828 to 1831m. Stop Drlg due to low ROP Meanwhile Pump 20 ppb (10 ppb Limestone Chips F, M + 5 ppb Oyster Shell F + 5 ppb Mica F) Hi-Vis

LCM Pill periodically & Add 5 Sxs/Hr. LCM to active system; 10-15 BPH Losses. Drlg Parameters: WOB: 10-30 Klbs, Rot: 160 RPM, TQ: 2-12 Klb.ft, F.R: 380-420 GPM, SPP: 470-570 Psi, Av. ROP: 1 MPH. Pump 70 bbl. 20 ppb Hi-Vis LCM Pill (10 ppb Limestone Chips F, M + 5 ppb Oyster Shell F + 5 ppb Mica F) & Displace same till Pill in Ann. Drop totco. Commence POOH w/ 12-1/4" PDC Bit & Drlg BHA to 1684m (13-3/8" CSG Shoe) on elevator w/ good hole condition. Cont. POOH to surface; Circ. Across wellhead; 6-8 BPH Losses. B/O & L/D 12-1/4"PDC Bit (8-8-RO-A-X-I-WT-PR). Meanwhile retrieve totco (Inc.: almost 2.8 Deg @ 1830m). P/U & M/U 12-1/4"B. Bit (537, New, Open, Kingdream) + Bit Sub (F. Valve, Baffle Plate In) + 3 Stds 8-1/2" DC (12-1/4" S. Stab (1/16" U.G @ 20m) + 8" Drlg Jar c/w Flex Jt + 1 Jt 8-1/2" DC + XOS (6-5/8" REG X 4-1/2" IF) + 3 Stds 5" HWDP & Followed by 5"DPs to 1831m (BTM hole) on elevator w/ good hole condition & Wash down last two Std. Meanwhile F/U string & Break Circ. every 15 Stds. Resume Drlg 12-1/4" HS to 1851m w/1-6 BPH losses. B/R & R/D last drilled Std. Cont. Drlg 12-1/4" HS to 1861m w/1-6 BPH losses. Meanwhile Pump Hi-Vis Pill periodically. Drlg Parameters: WOB: 10-20 Klbs, Rot: 70-110 RPM, TQ: 2-7 Klb.ft, F.R: 400-600 GPM, SPP: 350-760 Psi, Av. ROP: 6.6 MPH.

Cont. Drlg 12-1/4" HS to 1994m, 1-4 BPH Losses. Drlg Parameters: WOB: 10-20 Klbs, Rot: 70-110 RPM, TQ: 2-7 Klb.ft, F.R: 400-600 GPM, SPP: 350-760 Psi, Av. ROP: 6.5 MPH. Confirm Top of Pabdeh @ 1991m.

Cont. Drlg 12-1/4" HS to 2000m. 1-4 BPH Loss. Drlg Parameters: WOB: 10-20 Klbs, Rot: 110 RPM, TQ: 2-7 Klb.ft, F.R: 600 GPM, SPP: 960 Psi, Av. ROP: 6 MPH. In order to take last sample; Circ. BTM's Up. Commence POOH w/ 12-1/4" TCI Bit f/ 2000 to 1648m (13-3/8" CSG Shoe) on elevator w/ good hole condition. Cont. POOH to surface, F/U the well; 1-3 BPH Losses. L/D 12-1/4" TCI Bit. Bit Dull Cond.: 1-1-WT-A-E-I-NO-BHA P/U & M/U 8-1/2" C. Cut Bit, Bit Sub (F. Valve in) & Followed by 5" DP to 1648m (13-3/8" CSG Shoe). Circ. w/ 800 GPM; 2BPH Loss. Cont. RIH w/ C. Cut to 1890m. While Prepare 200 bbl. LCM Pill 90 ppb; 2BPH Losses. Pump 160 bbl. 90 ppb Hi-Vis LCM Pill (20 ppb Limestone Chips C, M + 20 ppb Mica C, M + 20 ppb Fiber Lock + 10 ppb Oyster Shell C) & Displace same till Pill in Ann. POOH to 1530m (Top of LCM Pill). Close Top Rams. Pump & Inject LCM Pill w/ 80 bbl. 75 pcf mud (F.R: 1 BPM, Pumping Press: 150-250 Psi)

Cont. Pump & Inject LCM Pill w/ totally 160 bbl. 75 pcf mud (F.R: 1 BPM, Pumping Press: 150-250 Psi) Open the well. Pump 8 bbl. and got return. RIH to 1950m; 20-25 BPH Losses. Circ. BTM's Up. 20 BPH Losses. POOH to 1860m. L/U CMT Line to string. Press test surface line to 3000 psi; "Ok". Pump 12bbl brine 75pcf as spacer ahead, Mix & Pump 342 sxs CMT Slurry (SV: 144bbl, SW:95pcf). Pump 1.5 bbl. behind spacer. Displace CMT w/ 83bbl 75pcf Mud as balance (3 bbl. Short). POOH to 1450m. Flush String. Cont. POOH to 1370m. Obs. the Well for 0.5 Hr.; 1 BPH Loss. Close the well & Inject 25 bbl. CMT in Formation w/ 70-340 psi. Open the well & Perform Static Flow Check; "Static". Circ. & Check Formation Loss w/ F.R: 600 GPM, SPP: 600 Psi, 1BPH Loss. Wash Down f/ 1370 to 1648m (13-3/8" CSG Shoe). Circ. w/ 800 GPM,

SPP:950Psi & Monitor pit level Static. Cont. Wash Down w/400 gpm to 1656m. Took 5klb Weight, Cont. Wash Down w/700 gpm, 3-5klb Drag to 1690m, C.B.U till Clean Shaker & Got 40bbl Contaminate Soft CMT; NL-NG. POOH w/ C. Cut f/ 1690m to surface, F/U the well; NL-NG.

P/U & M/U 12-1/4" TCI Bit (537, Used, Open, Kingdream) + Bit Sub (F. Valve, Baffle Plate In) + 3 Stds 8-1/2" DC (12-1/4" S. Stab (1/16" U.G @ 20m) + 8" Drlg Jar c/w Flex Jt + 1 Jt 8-1/2" DC + XOS (6-5/8" REG X 4-1/2" IF) + 3 Stds 5" HWDP & Followed by 5"DPs to 1690m, F/U string & Break Circ. every 15 Stds. D/O Soft to Med CMT f/ 1690 to 1850m, Wash Down f/ 1850 to 2000m (bottom) While Pump Hi-vis pill each Std; NL-NG. Meanwhile over flow Shakers due to Plug Screen several times. D/O Parameters: WOB:3-10klb, Rot: 90 RPM, FR:400-450 GPM, SPP:500-600 psi, TRQ:2-3 Klb.ft, ROP:30 MPH Pump 50 bbl. Hi-Vis Pill @2000m, Circ. BTM's Up w/ Flow Rate 850 Gpm, SPP:2000 psi till clean Shaker; NL-NG. POOH to 1648m (13-3/8" CSG Shoe) w/ Good hole condition. While Prepare 1300 bbl. 75pcf mud, Wash & Clean Mud tank & Mud Lines, Run back to 2000m till MN; NL-NG. While Displace the well w/ 900 bbl. 77 pcf mud, Resume Drlg 12-1/4" HS f/ 2000 to 2022m. Perform Drill off test to obtain optimum Drlg parameters.

Cont. Drlg 12-1/4" HS to 2150m. Meanwhile pump Hi-Vis Pill periodically & Work on mud rheology; 1-3 BPH Losses. Drlg Parameters: WOB: 5-20 Klbs, Rot: 70-140 RPM, TQ: 3-5 Klb.ft, F.R: 350-600 GPM, SPP: 350-1300 Psi, Av. ROP: 5.2 MPH. Circ. Out 40 bbl. Hi-Vis Pill; 1-2 BPH Losses. Commence POOH w/ 12-1/4" TCI Bit f/ 2150 to 2100m on elevator w/ good hole condition; 1 BPH Losses. Run totco Survey (Inc:2.8 Deg). Resume POOH w/ 12-1/4" TCI Bit to 1648m (13-3/8" CSG Shoe) on elevator w/ good hole condition. Cont. POOH to 200m, F/U the well; 1 BPH Losses. Meanwhile perform flow check the well @ Shoe; 1 BPH Losses. P/U & M/U 24 Jts 5" DP "S" & RIH to 420m. Circ. Hi-Rate. POOH to 200m and R/B same. Cont. POOH to 80m, F/U the well; 1 BPH Losses.

Cont. POOH f/ 80m to surface, F/U the well; 1 BPH Losses. L/D Bit. Bit Dull condition: 1-2-BT-G-E-I-WT-PR. P/U & M/U 12-1/4" PDC Bit (Best, New, M423, 2X12/32" + 5X13/32" + 2X14/32" NZLs) + Bit Sub (F. Valve, Baffle Plate in) + 3 Stds 8-1/2" DC (12-1/4" S. Stab (1/16" U.G @ 20m) + XOS (6-5/8" REG X 4-1/2" IF) + 3 Stds 5" HWDP to 170m, Meanwhile Obs. Failure of Drlg Jar during RIH, L/D Same. Cont. RIH w/ 5"DPs Jt by Jt (totally 162jts) to 1716m, Circ. w/hi-flow rate every 10 Jts, spot hi-vis pill to bottom, 1 BPH Losses. Cleaning w/blow air, Wash & Passed drift for all DPs. POOH & rack back new 5" DPs (54 STD G-Grade) f/ 1716m to 84m. 1 BPH Losses. P/U & M/U 8" D. Jar & F. Joint (NEW) and RIH back w/12-1/4" PDC Bit (Best, New, M423, 2X12/32" + 5X13/32" + 2X14/32" NZLs) + Bit Sub (F. Valve, Baffle Plate in) + 3 Stds 8-1/2" DC on 5" DPs to 250m till MN. 1 BPH Losses.

Cont. RIH back w/12-1/4" PDC Bit (Best, New, M423, 2X12/32" + 5X13/32" + 2X14/32" NZLs) + Bit Sub (F. Valve, Baffle Plate in) + 3 Stds 8-1/2" DC + D. Jar + 1

Jts 8-1/2" DC followed by 5" DPs to 2150m w/ good hole condition. F/U string & break circ. Every 15 STDs. 1 BPH Losses. Pump Hi-Vis, break circ. Fan the bottom & profile the bit. Resume drlg f/ 2150 to 2151m.

Due to Abnormal fluctuation in SPP stop drlg. Check surf. Equipment. Obs. Leakage from 4-1/16" stand pipe manifold (Genuine TDS hose valve). POOH to 2070m. Work on leakage, no success. POOH to 1620m (Inside 13-5/8" CSG) w/ good hole condition. Change stand pipe manifold valve while circ. thru string. Press. test same w/ 2000psi; "OK". RIH back on elevator to 2151m (bottom). 0-1 BPHL. Resume drlg 12-1/4" HS f/ 2151 to 2509m till MN, 0-3 BPHL. Drlg parameters: WOB: 15-17 Klb, Rot: 160-180 rpm, Tq.: 4-7 Klb.ft, FR: 700-750 gpm, SPP: 2050-2250psi. ROP: 5-6 m

Pump 40 bbl. Hi-Vis pill and circ. while B/R and R/D last drilled stand prior to perform wiper trip. POOH w/ soft B/R as wiper trip f/ 2509 to 2395m. Due to high wind speed stopped POOH. RIH on elevator to 2509m (bottom), 1 BPHL.

Cont. drlg 12-1/4" HS f/ 2395 to 2696.5m while Obs. drop ROP, Pumped Hi-Vis pill and performed drill-off test several times, due to low progress decided to POOH. 2 BPHL. Drlg parameters: WOB: 8-30 Klb, Rot: 60-180 rpm, Tq: 5-12 Klb.ft, FR: 600-750 gpm, SPP: 1650-2250psi. POOH f/ 2696.5m to 1620m (inside 13-5/8" CSG shoe) on elevator w/ good hole condition. 0-1 BPHL. Static flow checked: 0.5 BPH formation loss. Resume POOH f/ 1620m to surf. B/O & L/D 12-1/4" PDC Bit, 0-1 BPHL. Bit Dull condition: 4-4-LT-N/C-X-I-WT-PR. Obs. oil leakage on connection of 8" D. Jar, L/D same. Perform BOP Press test as NIOC policy, Press test Ann preventer to 500/2500 psi for 5/10 min; Ok. Press test 5" Fix BTM Ram, 5" Fix Top Ram to 500/3500 psi for 5/10 min; Ok. Press test Shear/Blind Ram, All manual/HCR side outlet valve & C/M valves to 500/3500 psi for 5/10 min; Ok. Ok. Function test accumulator system, driller & auxiliary remote panels; Ok. Retrieve plug tester. Install 13-5/8" wear bushing in CHS. P/U & M/U 12-1/4" PDC Bit (Best, New, M423, 5X13/32" + 4X14/32" NZL) Bit Sub (F. Valve, Baffle Plate in) + 3 Stds 8-1/2" DC + D. Jar & F. Jt (NEW) + 1 Jts 8-1/2" DC followed by 5" DPs to 250m. 0-1 BPH Losses.

Cont. RIH w/ 12-1/4" PDC Bit (Best, New, M423, 5X13/32" + 4X14/32" NZL) Bit Sub (F. Valve, Baffle Plate in) + 3 Stds 8-1/2" DC + D. Jar (NEW) + 1 Jts 8-1/2" DC followed by 5" DPs to 2680m on elevator w/ good hole condition. 0-1 BPH Losses. Wash down to 2696.5m (bottom) break circ. till uniform MW, Pump 50 bbl. Hi-Vis Pill & Touch the bottom while circ. out pills Several times, Pump again 20bbl hi-vis pill & Fan the bottom. 0-1 BPHL. Resume drlg 12-1/4" HS f/ 2696.5 to 2710m w/control parameters. 2-4 BPHL. Resume drlg 12-1/4" HS f/ 2710 to 2810m. 2-4 BPHL. Drlg parameters: WOB: 5-15 Klb, Rot: 60-180 rpm, Tq: 4-7 Klb.ft, FR: 750-800 gpm, SPP: 2100-2450psi. ROP: 2-6 mph

Obs. Suddenly 300psi drop in SPP while drlg. Stopped operation, checked SCR and all surface equip; OK. Decided to POOH in order to check string. POOH on elevator / 2810 to 1550m. 1BPHL

Cont. POOH f/1550m to surface, Obs string twist off from box of string stabilizer while circulate across wellhead with 1 BPH losses. Left in hole: 12-1/4" PDC Bit + 8-1/2" B.Sub + 2Jts 8-1/2" DC + 12-1/4" S.Stab Fish Length: 21.525m TOF: 2788.47m

P/U 10-1/8" O.Shot and dress by 8" Spiral + 1 Jt 8-1/2" DC + Oil Jar + 1 Jt 8-1/2" DC + XOS + 3 Stds HWDP followed by 5" DP to 2788.47m (TOF) . 1 BPH losses. Engaged with fish and catch it.Try to POOH Obs string stuck, work on it. String got free. 1 BPH losses. Start POOH to 2100m w/ max 10 Kips O.Pull, 1 BPH losses.

Cont. POOH f/ 2100m to surface w/ max 10 Kips O.Pull. 1 BPH losses Released the fish & L/D Overshot. 1 BPH Losses. M/U same 12-1/4" PDC Bit (Best, M423, 5X13/32" + 4X14/32" NZL) Bit Sub (New,F.Valve & Baffle Plate In) + 2Jts 8-1/2" DC + S.Stab (@20m) 3 Stds 8-1/2" DC + D.Jar + 1 Jts 8-1/2" DC + XOS (New) + 3 Stds 5" HWDP followed by 5" DPs to 800m , 1 BPH Losses. Hang up T.Block. Slip & Cut 100 ft of drilling line while slow circ. Through strg. 1 BPH Losses. Resume RIH to 2200m on elevator w/ good hole condition, 1 BPH Losses.

Cont. RIH w/ 12-1/4" PDC Bit (Best, M423, 5X13/32" + 4X14/32" NZL) Bit Sub (New,F.Valve & Baffle Plate In) + 2Jts 8-1/2" DC + S.Stab (@20m) 7 Jts 8-1/2" DC + D.Jar + 1 Jts 8-1/2" DC + XOS (New) + 3 Stds 5" HWDP followed by 5" DPs f/ 2200 to 2770m on elevator w/ good hole condition. 0-1 BPH Losses.

Wash down to 2810m (btm) break circ. till uniform MW. Pump 40 bbl Hi-Vis Pill & tag the btm while circ. out pill & fan the btm. 1-3 BPH Losses. Profile the bit and resume drlg 12-1/4" H.S f/ 2810 2868m while perform drill off test to Inc. penetration ratio; no success. Decided to POOH. 2-4 BPH Losses. Drlg parameters: WOB: 10-20 Klb, Rot: 120-180 rpm, Tq: 4-9 Klb.Ft, FR: 720-800 gpm, SPP: 2050-2550psi. ROP: 3-1 mph

POOH on elevetor f/2868m to surface with good hole condition. B/O & L/D PDC bit. 1-2 BPH losses. P/U & M/U 12-1/4" PDC Bit (Best, New, M423, 5X13/32" + 4X14/32" NZL) + Bit Sub (F.Valve & Baffle Plate In) + 2Jts 8-1/2" DC + S.Stab (@20m) + 7 Jts 8-1/2" DC + D.Jar + 1 Jts 8-1/2" DC + XOS + 3 Stds 5" HWDP followed by 5" DPs to 2830m , 1-2 BPH losses. Wash down to 2868m (btm) break circ. Pump 40 bbl Hi-Vis Pill & tag the btm while circ. out pill & fan the btm. 1-2 BPH losses. Profile the bit and resume drlg 12-1/4" H.S with controlled parameters f/ 2868 3006.7m. 2-4 BPH Losses. Drlg parameters: WOB: 5-10 Klb, Rot: 65-140 rpm, Tq: 4-7 Klb.Ft, FR: 800 gpm, SPP: 2450-2550psi. ROP: 2 mph

Obs. Twist off string indications (Dropped 10-12 Klbs strg weight, Dec. 450 psi in SPP, Inc. FR to 20 gpm, dropped Tq to 2-3 Klb.ft). Decided to POOH in order to check string.

2-4 BPH Losses. POOH f/3006.72m to surface, Obs string twist off from box of string stabilizer while circulate across wellhead with 1-2 BPH losses. Assembled 10-1/8" short catch O.Shot, dressed by 8-1/8" Spiral grapple, Control & top packer.

P/U 10-1/8" Short catch O.Shot (Dressed w/ 8-1/8" Spiral Grapple & Spiral Grapple Control) + 1 Jt 8-1/2" DC + 8" Fishing Jar + XOS + 3 Stds HWDP followed by 5" DP to 2984.5m (TOF); 1-2 BPH losses. Clean TOF. Try to engage fish by applying rotation & weight while Circ., Obs. Press up; Catch fish confirmed. Stop pumping & Apply 30 klbs Wt. P/U string; Obs. 10 Klbs excess Wt on M/D. POOH w/ 10-1/8" Short catch Over shot & Fishing BHA f/ 2984.5m (O.Shot Depth) to surface on elevator w/ good hole condition; F/U the well, 1-2 BPHL. All the time Pull out chain out.

10-1/8" Over shot on surface. L/D 8" Fishing Jar. Release over shot. L/D 1 Jt 8 1/2" DC, 10-1/8" over shot & Recovered Fish. Bit Dull Condition: 1-2-LT-N-X-I-PN-LIH. Unplug Bit & Bit Sub. While wait on OEOC; P/U & M/U 12-1/4" PDC Bit (Best, Used, M423, 5x13/32" + 4x14/32" NZL) + Bit Sub (F.Valve, Baffle Plate In) + 2 Jts 8-1/2" DC + 12-1/4" S.Stab @ 20m + 7 Jts 8-1/2" DC +8" Drlg Jar c/w Flex Jt + 1 Jt 8-1/2" DC + XOS (6-5/8" REG X 4-1/2" IF) + 3 Stds 5" HWDP & Followed by 5" DPs to 1850m, F/U string & Break Circ. Every 15 Stds; 0-2 BPHL. Med to hard wash and ream down f/ 1850 to 2480m; 0-2 BPHL.

Cont. Hard wash and ream down f/ 2480 to 3006m; 0-2 BPHL. Pump 40 bbl Hi-Vis Pill & Circ. Out same. Resume 12-1/4" H.S f/ 3006 to 3017.5m, Meanwhile increased MW to 80 pcf. 2-4 BPH Losses.

Drlg Parameters: WOB: 4-25 Klbs, Rot: 80-180 RPM, TQ: 3-7 Klb.ft, F.R: 750-780 GPM, SPP: 2400-2600 Psi, Av. ROP: 1 MPH.

Cont. Drlg 12-1/4" H.S f/ 3017.5 to 3019.5m; 2-4 BPH Losses. Due to a burst on upper iBOP, Drilling stopped. POOH w/ 12-1/4" PDC Bit f/ 3019.5 to 1648m (13-3/8" CSG Shoe) on elevator w/ good hole condition, F/U the well; 2 BPH losses. Change out TDS Upper, lower iBOP and saver sub. Press test same; Ok. Run back w/ 12-1/4" PDC Bit f/ 1648m (13-3/8" CSG Shoe) to 3019.5m (BTM) on elevator w/ good hole condition, F/U string & Break Circ. Every 10 Stds; 2 BPH Losses. Meanwhile Wash & Ream Dn last 2 Std. Resume Drlg 12-1/4" HS f/ 3019.5 to 3023.5m; 2 BPH Losses.

Cont. Drlg 12-1/4" H.S f/ 3023.5 to 3027m; 2-3 BPH Losses. Meanwhile perform drill off test to obtain optimum Drlg parameters. Last Chert depth: 3024m. Due to low ROP; Commence POOH w/ 12-1/4" PDC Bit f/ 3027 to 1648m (13-3/8" CSG Shoe) on elevator w/ good hole condition; F/U the well; 1-2 BPH losses. Perform flow check; 1 BPH Losses. Resume POOH w/ 12-1/4" PDC Bit f/ 1648m to surface; F/U the well; 1-2 BPH losses. L/D Jar & Bit. Bit Dull: 3-8-RO-N-X-I-(BT, CT)-PR. P/U & M/U 12-1/4" PDC Bit (Best, New, M423, 5x13/32" + 4x14/32" NZL) + Bit Sub (F.Valve, Baffle Plate In) + 2 Jts 8-1/2" DC + 12-1/4" S.Stab @ 20m + 7 Jts 8-1/2" DC + 8" Drlg Jar c/w Flex

Jt + 1 Jt 8-1/2" DC + XOS (6-5/8" REG X 4-1/2" IF) + 3 Stds 5" HWDP and followed by 5" DPs to 900m till M.N, F/U string and break Circ. Every 15 Stds; 0-1 BPHL.

Cont. RIH w/ 12-1/4" PDC Bit and Pendulum BHA f/ 900 to 1648m (CSG Shoe). Cont. RIH to 2996m on elevator w/ good hole condition, F/U string and break Circ. Every 15 Stds; 0-1 BPHL. Run totco @ 2996m (31 mt off BTM). Result: 0.5 Deg. Wash down to 3027m (BTM). Establish Circ. Hi-Rate, meanwhile pump and Circ. Out 70 bbl Hi-Vis pill @ 2 step as clean BTM of hole. Fan the BTM. Resume drill ahead 12-1/4" HS f/ 3027 to 3240m; 2-5 BPH Losses. Meanwhile pump Hi-Vis pill. Drilling Parameters: WOB: 10-20 klbs, Rt: 160 RPM, TQ: 4-9 Klbs.ft, F.R: 750-780 GPM, SPP: 2600-2750 psi, Av. ROP: 2 MPH. Obs. Decrease SPP. Stop Drlg, check SCR & surface equipment. During take SCR; Suddenly lost 170 Klbs string Wt. & SPP: zero. POOH to surface. Obs. String twist off. M/U 10-1/8" O.Shot w/ Extension & Deressed by (6-3/8" B.Grapple & 6-1/2" M.Control) + 1Jt 8-1/2" D.C + 1 Std 5"HWDP & followed by 5" DPs to 1425m. Catch the fish. POOH to f/ 3240m (BTM hole) with normal drag. Cont. Pull out string to 3155m. Stuck string. Work on stuck to Max. 120 klbs down ward; String got free. Cont. Pull out string w/ hard Back ream to 3150m. Cont. POOH to 2700m on elevator w/ good hole condition, F/U the well; 4-8 BPH losses. Cont. POOH f/ 2700 to 1813m on elevator w/ good hole condition. Release overshot. L/D 8-1/2" DC. L/D 2 Jts 5" DP. Cont. POOH string to surface, F/U the well; 4-8 BPH losses. Check Jar was Failed. L/D Jar & 12-1/4" PDC Bit, 3 BPHLoss. Bit Dull: 5-3-LT-N/S-X-1/16"-BT-LIH. Obs. 4 Jts 5" DP & 3 JTs 5" HWDP Buckled.

Retrieve W.Bushing, Install Plug tester. Perform BOP Press test as NIOC policy, Press test Ann preventer to 500/3500 psi for 5/10 min; Ok. Press test 5" Fix BTM Ram, 5" Fix Top Ram, Shear/Blind Ram, All manual/HCR side outlet valve & C/M valves to 500/4000 psi for 5/10 min; Ok. Function test accumulator system, driller & auxiliary remote panels; Ok. Retrieve plug tester. Install 13-5/8" wear bushing in CHS. Slip & Cut 100 ft 1-1/2" Drlg line. P/U & M/U 12-1/4" PDC Bit (Smith Bit, Geo Diamond, New, Made in Italy, M88VPXX, M424, 8 blade, 8x16/32" Nozzle) + 8-1/2" Bit sub + 2 Jts 8-1/2" DC + 12-1/4" F. G S.Stab @ 20m + 7 Jts 8-1/2" DC + XOS + 3 Stds 5" HWDP + followed by 5" DPs to 560m, F/U string & Break Circ. Every 15 Stds; 1-3 BPH Losses. Meanwhile L/D 3 Jts 5" HWDP buckled.

Cont. RIH w/ 12-1/4" PDC Bit & Pendulum BHA f/ 560 to 3240m on elevator w/ good hole condition, F/U string & Break Circ. Every 15 Stds; 1-3 BPH Losses. Pump 30 bbl Hi-Vis Pill. Circ. out the bit & clean BTM Several time without Rotation. Pump 30 bbl Hi-vis pill. Commence drill ahead 12-1/4" HS f/3240 to 3274m; 2-6BPHL

Cont. drill ahead 12-1/4" HS f/ 3274 to 3275m; 3-6 BPHL. Meanwhile pump 30bbl Hi-Vis Pill & Pump Tandem Pill: 30 bbl LV Pill & 30 bbl HV Pill. Perform drilloff test to beter ROP. B/R Last Drilled Std. Drilling Parameters: WOB:10-25 klb Max, Rot:120-170 RPM, FR:780 GPM, SPP:2700psi, TQ:3-5 Klb.ft, Avg ROP:0.25 MPH. Due to low ROP. POOH w/ 12-1/4" PDC Bit f/ 3275 to 1648m (13-3/8" CSG Shoe) on elevator w/

good hole condition, F/U the well; 3-5 BPHL. Cont. POOH f/ 13-3/8" CSG Shoe to surface. L/D Bit. (Bit Dull Condition: 6-7-B Blade-N-X-1/8"-BT/LT-PR). Meanwhile Static flow check @ Shoe & BHA; 3 BPH Losses. P/U & M/U 12-1/4" TCI Bit (King Dream, 537, 3*20/32" Nozzle) + 9-1/2" Junk Sub +8-1/2" Bit sub (Float & Baffle Plate in) +2 Jts 8-1/2" DC + 12-1/4" F. G S.Stab 20m + 7 Jts 8-1/2" DC + XOS + 3 Stds 5" HWDP + followed by 5" DPs to 1648m (13-3/8" CSG Shoe), F/U string & Break Circ. Every 15 Stds; 1-3 BPH Losses. Cont. RIH w/ 12-1/4" TCI Bit & Junk sub to 2100m on elevator w/ good hole condition, F/U string & Break Circ. Every 15 Stds; 0-3 BPH Losses.

Cont. RIH w/ 12-1/4" TCI Bit & 9-1/2" Junk Sub f/ 2100 to 3275m on elevator w/ good hole condition, F/U string & Break Circ. Every 15 Stds; 1-3 BPH Losses. Pump & Circ. Out 30 bbl Hi-Vis Pill to clean the hole, meanwhile reciprocate string. Pump 50 bbl Hi-Vis pill. Displace same every 10 bbl to Ann & Work on J.Sub. Cont. Work on Junk Sub several times. while pump Hi-vis pill periodically. Resume drill ahead 12-1/4 HS f/3275 to 3282m; 3-4BPHL. Pump Hi-vis pill, C.B.U & WORK ON Junk Sub Several times. Resume drill ahead 12-1/4 HS f/3282 to 3284.4m; 3-4BPHL. Due to low ROP; Decided to POOH. Drlg. Parameters: WOB:10-20 Klbs, Rot: 40-80 RPM, FR:400-750 GPM, SPP:900-2850 psi, TQ:5-6 klb.ft, Av. ROP:0.25 MPH Work on Junk Sub several times. POOH w/ 12-1/4" TCI Bit & Junk Sub f/ 3284.4 to 1648m (CSG Shoe) on elevator w/ good hole condition, F/U the well; 3-4 BPHL.While Static flow check @ Shoe; 4 BPHL. Cont. POOH w/ 12-1/4" TCI BIT & 9-1/2" Junk Sub to surface, F/U the well; 3-4 BPHL. L/D Bit & J.Sub. Recover 17gr PDC Pieces Junk. Bit Dull: 2-4-BT-G-E-I-WT-PR. While Static flow check @ BHA; 4 BPHL. P/U & M/U 10-1/8" Rev. Circ. Junk Basket + 2 Stds 8-1/2" DC + 3 Stds HWDP & Followed by 5" DPs to 3284m while Passed 2.5" Drift thru all tubular; 3-4 BPHL. Circ. Mud.

Drop ball and chase same to seat. Work on RCJB f/ 3284.5 to 3284.9m; 3-4 BPH losses. Wt:3-5klbs, Rotation:10-25 RPM, TQ:3-6 Klbf.ft, FR:400-450 GPM, SPP:800-1000psi

POOH RCJB f/ 3284.9m to 1100m. While f/up the well from T.Tank; 3-4 BPH losses. Work on TDS Hydraulic line. Resume POOH RCJB f/ 1100m to surf. While f/up the well from T.Tank; 3-4 BPH losses. B/O & L/D RCJB. Recovered 50cm formation core W/O any metal parts or junk.

P/U & M/U 12-1/4" PDC Bit (Beste, New, M1664, 9*13/32" Nozzle) + 8-1/2" Bit sub (Float & Baffle in) +2 Jts 8-1/2" DC + 12-1/4" F. G S.Stab 20m + 7 Jts 8-1/2" DC + 8" D.Jar + 1 Jt 8-1/2" DC + XOS + 3 Stds 5" HWDP + followed by 5" DPs to 3284.5m with good hole condition, F/U string & Break Circ. Every 15 Stds; 2-3 BPH Losses. Pump 30 bbl Hi-Vis pill and circ. Same out. 3-4 BPH Losses. Enlarge the 10-1/8" pilot hole f/ 3284.5 to 3284.9m. Cont. Drlg 12-1/4" HS with low parameters while fan the bottom and profile the bit f/ 3284.9 to 3287m. Cont. Drlg 12-1/4" HS f/3287 to 3620m. 4-6 BPH Losses. Drilling Parameters: WOB: 7-12 klbs, Rt: 170 RPM, TQ: 7-10 Klbs.ft, F.R: 730 GPM, SPP: 2800 psi, Av. ROP: 4-5 MPH.

B/R & R/D drilled stand, rack back same and start POOH w/ soft B/R as wiper trip to 3570m while clear tight spot @ 3590m till MN, 3-5 BPH losses. Cont. POOH w/ soft B/R as wiper trip f/ 3570 to 3250m, while clear tight spots @ 3500 & 3260m, 2-3 BPH losses. RIH back f/ 3250 to 3600m on elevator with good hole condition. 2-3 BPH losses. Perform Totco survey; inclination: 0.8 degree.

Connected last stand. R/D to 3620m (BTM). Pumped 30 bbl Hi-Vis pill and circ. Out f/bit. Resume Drlg 12-1/4" HS f/3620 to 3738m. 3-5 BPH Losses.

Obs. Gradually 70 psi decrease in SPP and get min MW: 82 pcf in return mud. Stop drlg. Cont. circulation to check mud parameters & surface equipment while monitor SPP (constantly 70 psi less than SPP with same GPM during drlg) till balance MW in/out on 83 pcf. Take SCR, resume drlg with low parameters to 3741m and monitor the SPP; Constant.

Cont. Drlg 12-1/4" HS f/3741 to 3814m, 3-4 BPH Losses.

Due to Obs. Leakage from wash pipe stop drlg. POOH w/ back reaming to 3770m. M/U swage, stablish circulation thru string and change wash pipe. RIH back w/ R/D to 3814m (BTM). Resume Drlg 12-1/4" HS f/3814 to 3842m, 6-12 BPH Losses.

Due to Obs. Leakage from wash pipe stop drlg. POOH w/ back reaming to 3770m. M/U swage, stablish circulation thru string and change wash pipe. RIH back w/ R/D to 3842m (BTM). 7-9 BPH Losses. Resume Drlg 12-1/4" HS f/3842 to 3857m. 9-13 BPH Losses.

Drilling Parameters: WOB: 7-25 klbs, Rt: 130-170 RPM, TQ: 7-10 Klbs.ft, F.R: 670-0 GPM, SPP: 2670-2820 psi, Av. ROP: 0.8-1.5 MPH.

B/R & R/D drilled stand and made connection. Pump and spot 30 bbl LCM pill (20ppb, Fine size) before connection.

Cont. Drlg 12-1/4" HS f/3857 to 3872m. Due to low progress stop drlg. 8-12 BPH Losses. Pump and spot 60 bbl LCM pill (20ppb, Fine size) prior to POOH to surf. POOH on elevator f/3872 to 1700m with good hole condition, 8-12 BPH Losses.

Pump and spot 140 bbl LCM pill (40ppb, Fine & Medium size) in Jahrum formation. Resume POOH to surf. Change D. Jar. B/O & L/D 12-1/4" PDC bit. 10-15 BPH Losses. P/U & M/U 12-1/4" PDC Bit (Burintekh, Used, M323, 6*15/32" Nozzle) + 8-1/2" Bit sub (Float & Baffle in) +2 Jts 8-1/2" DC + 12-1/4" S.Stab @ 20m + 7 Jts 8-1/2" DC + 8" D.Jar (New) + 1 Jt 8-1/2" DC + XOS + 3 Stds 5" HWDP + followed by 5" DPs to 3872m (btm) with good hole condition; 10-15 BPH Losses.

Resume drilling 12-1/4" HS f/3872 to 3891m, 15-20 BPH losses. Due to leakage from Uper IBOP stop drlg, POOH w/ pump out f/ 3891 to 3799m with good hole condition.

Work on change TDS upper IBOP and changed same. Function and pressure tested; OK. 20-30 BPH losses.

Start RIH to 3856m. Connected TDS, try to stablish circ, obs abnormal high pressure. Checked flow line; no return. String was pluged.

Work on unplug string by apply pressure and jerking string, got return but still obs. abnormal high pressure. (At least 3 no nozzeles plugged) . 25-30 BPH losses. POOH w/ pump out while check SPP f/ 3856 to 3713m, did not get normal pressure. 25-30 BPH losses. Cont. POOH on elevator f/ 3713 to 1623m (inside 13-3/8" CSG) with good hole condition. 25-30 BPH losses. Connect TDS & Circ. Through strg to check SPP, obs abnormal high pressure with same conditions. 25-35 BPH losses. Slip & cut 100ft of drilling line, 25-35 BPH losses. Connect TDS & Circ. Through strg to check SPP, obs abnormal high pressure with same conditions. 25-35 BPH losses. RIH back f/ 1623 to 1880m. Try to fill up string, Obs. String plugged. 25-35 BPH losses. POOH f/1880 to surf. B/O the 12-1/4" PDC bit, obs. flapper of float valve is broken and drop down on bit also 4 nozzles were plugged. Changed float valve, unplugged the bit and removed 3 no zozzles. (3*15/32"+3*Open). 25-35 BPH losses.

M/U same 12-1/4" PDC Bit (Burintekh, Used, M323, 3*15/32" + 3* Open Nozzles) + 8-1/2" Bit sub (Float Valve In) +2 Jts 8-1/2" DC + 12-1/4" S.Stab @ 20m + 7 Jts 8-1/2" DC + 8" D.Jar + 1 Jt 8-1/2" DC + XOS + 3 Stds 5" HWDP & followed by 5" DPs to 1648m (CSG Shoe), F/U string & Break Circ. Every 12 Stds; 25-35 BPH Losses. Cont. RIH w/ 12-1/4" PDC bit to 3891m (BTM hole) w/ good hole condition, while soft W/R last 20m. Resume Drlg 12-1/4" HS f/3891 to 3893m; 20-30 BPH Losses. Cont. Drlg to 3895m, meanwhile decrease MW to 80 pcf, Pump 40 bbl 40 ppb Hi-Vis LCM Pill & Add Lst Chips (8 sxs/Hr) to active mud system; Increase Losses to 80-90 BPH. Drlg Parameters: WOB: 15-25 Klbs, Rot: 140-160 RPM, TQ: 6-9 Klbs.ft, FR: 550-450 GPM, SPP: 1750-1350 psi, Av ROP: 2 MPH

Decided to POOH to 3600m. POOH w/ 12-1/4" PDC Bit f/ 3895 to 3750m; 70-75 BPHL. Cont. POOH w/ 12-1/4" PDC Bit f/ 3750 to 3380m, meanwhile pump & Spot 100 bbl 40 ppb (20 ppb Lst Chips M, C / 10 ppb Oyster Shell M / 10 ppb Mica M) LCM Pill @ 3595, 3500 & 3385m; 70-90 BPHL.

Cont. POOH w/ 12-1/4" PDC Bit on elevator w/ good hole condition to 1648m (CSG Shoe). Meanwhile Circ. Across wellhead; 70-90 BPH Losses. Pump & Spot 160 bbl 70 ppb LCM Pill. Cont. POOH w/ 12-1/4" PDC Bit to 1210m. Meanwhile Circ. Across wellhead; 70-90 BPH Losses. Stop POOH Operation due to high wind speed. Meanwhile Circ. Across Wellhead and occasionally pump thru string; 70-90 BPHL.

Cont. Stop POOH Operation due to high wind speed. Meanwhile Circ. Across Wellhead and occasionally pump thru string; 70-90 BPHL. Resume POOH w/ 12-1/4" PDC Bit f/ 1210 to 90m. Meanwhile Circ. Across wellhead; 70-90 BPH Losses. Stop POOH

Operation due to high wind speed. Meanwhile Circ. Across Wellhead and occasionally pump thru string; 70-90 BPHL. Resume POOH f/ 90 m to surface, While soft break 8-1/2" DCs. Bit Dull Condition: 1-1-WT-A-X-I-NO-HP. 65-75 BPHL. RIH w/ 8-1/2"C. Cut Bit and followed by 5"DPs to 3100 m. Meanwhile Circ. Across wellhead; 65-75 BPHL. Pump 160 bbl 140 ppb Hi-Vis LCM Pill (Mica C, M: 35 ppb / Lst Chips C, M: 35 ppb / Shell Fish C, M: 40 ppb / Fiber Lock: 30 ppb) till M.N. 65-75 BPHL.

Spot LCM Pill. POOH w/ 8-1/2" C.Cut Bit f/ 3100 to 1648m (CSG Shoe). Meanwhile Circ. Across wellhead; 65-75 BPHL. Pump & Spot 220 bbl 140 ppb Hi-Vis LCM Pill (Mica C, M: 35 ppb / Lst Chips C, M: 35 ppb / Shell Fish C, M: 40 ppb / Fiber Lock: 30 ppb); 65-75 BPHL. Resume POOH w/ 8-1/2" C.Cut Bit to 500m while Obs. Gradually reduce formation loss F/70 to 6BPH. Flow check The well @ 500m. Resume POOH to surfacfe. L/D 8-1/2"C. Cut Bit while Obs. Gradually increase formation loss to 30 BPH.

Retrieved 13-5/8"wear bushing. Close Shear/Blind Rams. Change Top rams to 9-5/8" fix, Meanwhile Circ.thru C/M; 30 BPH losses. Perform Pres test Top Rams; "Ok". R/U OEOC CSG Running equipment. Set Jam System. Held PJSM. P/U 1 Jt 9-5/8" CSG (53.5#, 110SS, Pin: N.Vam Box: HSM-3), M/U 9-5/8" F.Shoe (53.5#, T-95, N.Vam, Double Valve) on shoe Jt. M/U 1 Jt 9-5/8" CSG (53.5#, 110SS, HSM-3), F/U String & check flow pass thru; Ok. M/U 9-5/8" Float Collar (53.5#, 110SS, HSM-3) below 1 Jt 9-5/8" CSG (53.5#, 110SS, HSM-3) & RIH to 400m (Totally: 34 Jts). Meanwhile F/U string every 10 Jts, Break Circ. Every 20 Jts and Circ. Across wellhead all the time; 35-20 BPHL & Install 9-5/8" x 12-1/4" Bow Centralizer as per tally. Cont. Run 9-5/8" CSG (53.5#, 110SS, HSM-3) f/ 400 to 1275m (Totally: 107 Jts). Meanwhile F/U string every 10 Jts, Break Circ. Every 20 Jts and Circ. Across wellhead all the time; 35-15BPHL & Install 9-5/8" x 12-1/4" Bow Centralizer as per tally.

Stop RIH operation, Change TDS links to 500 Ton. Install spider elevator, Slips & Fill up tools. Cont. Run 9-5/8" CSG (53.5#, 110SS, HSM-3) to 3700 m meanwhile F/U string & Break Circ. Every 10 Jts. Wash Dn w/ 9-5/8" CSG string f/ 3700 to 3895 m. (Totally: 327 Jts) Tag BTM w/ 10 Klb Wt; 5-2 BPHL; Install Centralizer as per tally. Meanwhile prepare 1000 bbl CMT Solution & Transfer to CMT solution tanks. Slow circulate mud Thru CSG string meanwhile R/D CSG handling equpment. while prepare CMT spacer.

R/U 9-5/8" CMT head, plug already loaded. L/U CMT head. Held PJSM. L/U CMT line to CMT head, Press test CMT line to 500/3000 psi; OK. Pump 40 bbl 62.4 pcf Chemical wash, 60 bbl 90 pcf Spacer ahead. Mix & Pump 2600 sxs CMT G Delijan (SV: 1108 bbl, SW: 95pcf) as lead slurry, Mix & Pump 371 sxs CMT G Delijan blended w/ 36.66 lb/sxs Silica Flour (SV: 116 bbl, SW: 118 pcf) as tail slurry; 2-3 BPHL, Drop top plug. Displace w/ 400 bbl 80 pcf mud is in progress till M.N. 2-3BPHL.

Displace w/ totally 903 bbl 80 pcf mud; Observe bumping w/ 2000psi (80% Burst Press). Check back flow; OK. Got 230 bbl Contaminated CMT (80-90 pcf) & 170 bbl Green CMT slurry (95 pcf) on return & Totally 30 bbl losses during displace. Drain & Flush

BOP Stack & CHS, H/U BOP stack, Set 13-5/8" x 9-5/8" CSG slips (MSP/Drillex) in CHS. Land BOP Stack & Tighten Bolts. Slack off 200 Klbs CSG Wt on CSG Slips. Close Top Rams & Perform 13-5/8" x 9-5/8" CSG slips Press test to 1000 psi for 10 min; OK. While WOC monitor inside 9-5/8" CSG Press; Build up to 700 psi; Gradually bleed off to 200 psi, Build up to 300psi. Fully slack off CSG Wt on CSG slips; No movement. Bleed off Press to zero. R/D CMT Head.L/D CSG Slips.

H/U BOP Stack. Rough cut CSG. L/D landing Jt. N/D DSA & Spacer Spool. Final cut CSG neck, Dress & Bevel same. Install 13-5/8” 5k x 9-5/8" 10k THS (MSP/Drillex, S/N: TH806FXC230004) c/w 4 No. 2-1/16" 10 K side outlet valves. Tighten all nut. Inject Plastic packing & Energize P-Seals. Press Test between ring gasket / 1st P-Seal & between 1st / 2nd P-Seal with Max 80% of CSG Collapse Press; Ok. N/U 11" 10 k x 13-5/8"-10k DSA, 13-5/8"-10k x 13-5/8" 10k Spacer spool & Install 13-5/8"-10K BOP Stack on same. Tighten all nuts. Connect 2" & 4" choke line f/ BOP Stack to C/M & 2" Kill Lines to BOP Stack.

Cont. N/U 13-5/8" 10 K BOP Stack & Weld 2" choke line. Change Top Ram f/ 9-5/8” Fix Ram to 4-1/2” x 7” VBR. Set 11" Plug tester in place. Perform BOP Press test as NIOC Policy: Press test Ann Preventer to 500/3500 psi, Press test 5" Fix BTM Ram, 4-1/2" x 7" VBR top ram, Shear/Blind Ram, All manual/HCR side outlet valve & C/M valves to 500/7500 psi for 5/10 min; Ok. Meanwhile rectify several leakages. Press test burning line & related valve to 500/1000 psi for 10 min; Ok. Function test accumulator system, driller & auxiliary remote panels; Ok. Retrieve plug tester. Set 11" Wear bushing in THS. L/D 9 Jts 8-1/2" D.C.

P/U & M/U 8-3/8" PDC Bit (Best, New, M433,7 x 14/32" NZL) + Bit Sub (F.Valve) + 12 Jts 6-1/2" DC (8-3/8" S.Stab (1/4" UG) @ 20m) + 6-1/2" Drlg Jar+ 3 Jts 6-1/2" DC + 3 Stds 5" HWDP to 260m, F/U String & Break Circ.; Ok. Cont. RIH w/ 8-3/8" PDC Bit to 1400m; F/U string & Break Circ. Every 15 Stds.

Cont. RIH w/ 8-3/8" PDC Bit f/ 1400 to 3800 m; F/U string & Break Circ. Every 10 Stds. Wash Down to 3867m. D/O Med CMT to 3870m, D/O Plugs & Float Collar, Smooth This Interval several times. D/O Med to hard Shoe track CMT to 3894.5m (Top of 9-5/8" CSG Float Shoe)

8-3/8” Hole Section Summary

Date	13 – February – 2024
Drilling Depth	4180^{m}
Casing Size / Shoe	7”, P-110SS, 35$^{\#}$, TPCQ / 3786-4179.5^{m}
Formation	Gadvan / Fahliyan
Mud Weight	100 – 103^{pcf}

Table 2-5: AZNS-207 8-3/8" Hole Section Summary

Stop D/O due to Obs. Leakage from TDS Saver sub. POOH 1Std & R/B same. While Slow Circ. Thru string Change out TDS Saver sub & Work on TDS. Test same; OK. Run back to BTM. Resume D/O 9-5/8" CSG Shoe to 3895m. NL-NG. Smooth this interval several times. Commence Drlg ahead 8-3/8" HS f/ 3895 to 3928m; NL-NG. Drlg Parameters: WOB:5-18klb, Rot:50-80 RPM, TQ:9-12klb.ft, F.R:500-600 GPM, SPP:1750psi, ROP:2.5MPH.

Pump 40 bbl Hi-Vis Pill & CBU till Clean Hole. POOH w/ 8-3/8" PDC Bit to 3856m (Cased Hole). Close Top Rams, Perform FIT 8-3/8 HS to EMW:105pcf; Apply 2260psi Press stepwise, Hold Press; "OK". (Pump totally 7bbl 80 pcf Mud & Got same volume in return after bleed off) RIH to 3928m Work on TDS TRQ While Circ Mud w/ 300 GPM, NL-NG. Due to unable to increase TDS Rot above 80 RPM. POOH to 3890m. While Wait on Repair TDS TQ; Establish Circ Mud thru strng & Prepare 1000 bbl 100 pcf mud; NL-NG. Run back to BTM, Displace the well w/ 100 pcf mud; NL-NG. Meanwhile reciprocate string.

Resume Drlg ahead 8-3/8" HS f/ 3928 to 3963m, meanwhile increase MW to 102pcf; 3-8 BPH Losses. Stop Drlg., Pump & Spot 20 bbl LCM Pill 20 ppb, POOH to 3963m, POOH to 3780m. Circ. w/ Hi-FR top of Pill; Decrease FM loss f/8 to 4 BPH loss. RIH to 3895m Circ. Mud W/ Hi-FR; Decrease FM loss to 2 BPH losses. Meanwhile increase Mw to 102.5Pcf. Run Back to BTM. Circ. Meanwhile Cont. Increase Mw to 102.5Pcf; 2 BPH Losses. Resume Drlg ahead 8-3/8" HS f/3963 4180m (Well TD); 1-2 BPH Losses., Meanwhile work on Mud rheology.

Drlg Parameters: WOB:15-18klb, Rot:120-150 RPM, FR:350-470GPM, SPP:1450-2200psi, TRQ:2-11klb.ft, ROP:3MPH

Circ. BTM's up in order to take last Sample by Well Site Geologist & Confirm 7" Liner Point. Meanwhile reciprocate string; 1-2 BPH Losses. B/R f/ 4180 to 4120m, Cont.

POOH w/ 8-3/8" PDC Bit to 3820m on elevator w/ good hole condition, Circ. Across Wellhead; 2 BPH Losses.

Establish Slow Circ. Thru string & Monitor Pit Level; 0-1 BPH Losses. Run back to 4080m on elevator w/ good hole condition, Wash & Ream to 4180m (BTM). 0-2 BPH Losses. Pump 40 bbl Hi-Vis pill and circulated till shakers clean. Spot 50 bbl Hi-Vis pill @ BTM. 2 BPH Losses. POOH w/ 8-3/8" PDC Bit f/ 4180m to surface on elevator w/ good hole condition, Circ. Across Wellhead; 2 BPH Losses. B/O & L/D D.jar & 8-3/8" PDC Bit. Bit Dull condition: 1-1-WT-A-X-I-BT-TD. Observed the well @ 1000m; 2 BPH Losses. Retrieve wear bushing and prepare to R/U wireline logging equip. 2 BPH Losses.

L/D mouse hole, install shooting nipple. R/U WL logging equip. Pressure tested WL BOP using shooting nipple with 1000 psi/ 10min; OK. 0-1 BPH Losses. M/U logging assembly as run #1 (Resistivity/Sonic/CDR-GR), Surface checked; OK. RIH to 3895m (9-5/8" CSG shoe). Log down to 4180m (btm). Log up f/ 4180 to 3895m. Repeat Interval: 3895-3960m. POOH to surf. L/D Run #1 logging tools. 0-1 BPH Losses. M/U logging assembly as run #2 (Nuclear Run) LDT/CNT/NGS, Surface checked; OK. RIH to 3895m (9-5/8" CSG shoe). Log down to 4180m (btm). Log up f/ 4180 to 3895m. POOH to surf. L/D Run #2 logging tools. 0-1 BPH Losses. M/U logging assembly as run #3 SBT/CCL/VDL-GR, Surface checked; OK. RIH to 700m till MN. 0-1 BPH Losses.

Cont. RIH as Run #3 SBT/CCL/VDL-GR to 1648m (13-3/8" CSG shoe). Log down to 3895m (9-5/8" CSG shoe). Log up f/ 3895 to 3300m. Obs. Failure of logging tools. POOH to surf. Work on troubleshooting of logging tools. RIH as R.Run #3 to 3300m 0-1 BPH Losses. Resume log up with SBT/CCL/VDL-GR logging tools f/ 3300 to 1648m (13-3/8" CSG shoe). POOH to surf. L/D logging tools. R/D WL unit and equip. 0-1 BPH Losses. Slip & Cut 97ft of drilling line. 0-1 BPH Losses. Install mouse hole & wear bushing in place. 0-1 BPH Losses. P/U & M/U 8-3/8" PDC Bit (Best, Used, M433,7 x 14/32" NZL) + Bit Sub (F.Valve in) + 5 STDs 6-1/2" DC (8-3/8" S.Stab (1/4" UG) @ 20m) + 3 Stds 5" HWDP followed by 5"DP to 1250m.

Cont. RIH with 8-3/8" PDC bit f/ 1250 to 3920m, wash down to 3960m, RIH W/ good condition to 4080m, took weight, soft ream & back ream to 4085m, check this interval "OK", RIH to 4170m, took weight, Soft Ream to 4180m (BTM). 0-1 BPH Losses. Circ. Till uniform the mud. Spot 60 bbl Hi-Vis pill at btm. 0-1 BPH Losses. POOH on elevator with good hole condtion f/ 4180m (btm) to surf. B/O & L/D 8-3/8" PDC bit, 0-1 BPH Losses.

R/U 7" liner running equipment. M/U 7" Reamer F.shoe, RIH 2 Jts 7" liner (35#, TP110SS, TPCQ), M/U 7" F.Collar, RIH 1 Jt 7" liner (35#, TP110SS, TPCQ), M/U 7" LDC and cont. RIH 27 Jts 7" liner (35#, TP110SS, TPCQ), P/U & M/U 7" Rot. Hyd.

Liner hanger assembly to 397m. 0-1 BPH Losses. RIH with 5" DPs to 3500m while pass drift thru all drill pipes till MN, 0-1 BPH Losses.

Cont. RIH 7" Liner on 5" DPs f/ 3500 to 4180m, tag btm while pass drift thru all drill pipes, 0-1 BPH Losses. Establish circ. Record WT up & downward. Set liner hanger position (0.5m off btm). Dropped ball and circ. Till ball seat in LDC. Set hanger. Shear LDC by applly 2700psi with rig pump. turn string 27 rounds clockwise and released setting tools. check string WT, confirmed set liner hanger. 0-1 BPH Losses.

M/U cement manifold (loaded dart), prepare & make cmt solution & spacer (chemical wash) meanwhile circ. mud thru string as 1.5 cap of string, L/U cmt line & press. test same w/ 3000psi, OK, pump 15bbl chemical wash as spacer, pump cmt slurry (S.V: 52bbl, S.W: 118pcf), release dart & disp. cmt slurry w/ totally 253bbl drlg fluid 103pcf, obs shearing (213bbl & 3000psi) & bumping (253bbl & 2700psi), during cementing & disp. same obs 3bbl loss), disconnected cmt line, pull out dog sub from PBR & slack off 40kips weight on the lap of tie-back to set top PKR (obs shock string on weight indicator). POOH with liner hanger setting tools to 3552m (8std & the first 3std. wet), flush the string cont. POOH to 3322m, CBU, cont. POOH to surf. L/D liner hanger setting tools. while F/U well continuously, NL-NG.

P/U & M/U 8-3/8" PDC Bit (Best, Used, M433,7 x 14/32" NZL) + Bit Sub (F.Valve in) + 3 STDs 6-1/2" DC + 3 Stds 5" HWDP followed by 5"DP to 3550m, Pump Down to 3650m, Try To wash down This Point w/Hi-Flow Rate, No Progress. Start D/Out Soft CMT f/3650 to 3690m, D/Out Med CMT to 3725m, D/Out Hard Cmt F/3725 to 3786m string stalled and obs. jumping. Confirmed 7" L.Lab @ 3786m.

Pump Hi-Vis pill and circulated till shakers clean. POOH with 8-3/8" PDC bit f/ 3786 to 3300m.

POOH with 8-3/8" PDC bit f/ 3300m to surf. B/O & L/D 8-3/8" PDC bit. Change Top Ram f/4-1/2” x 7” VBR to 2-7/8” x 5” VBR. Perform BOP Press test as NIOC Policy: Press test Ann Preventer to 500/3500 psi, Press test 5" Fix BTM Ram, 2-7/8” x 5” VBR top ram, Shear/Blind Ram, All manual/HCR side outlet valve & C/M valves to 500/7500 psi for 5/10 min; Ok. Meanwhile rectify leakages. Function test accumulator system, driller & auxiliary remote panels; Ok. Retrieve plug tester. Set 11" Wear bushing in THS.

M/U 5 7/8" R.Bit (K.Dream, Used, 3*Open Nozz) + 4-3/4" B.Sub +15 Jts 4 3/4" DC + 9 Jts 3-1/2" HWDP + 16 Jts 3-1/2" DP Jt by Jt to 370m.

Cont RIH with 5-7/8" R.Bit (K.Dream, Used, 2204638JH, 3*Open Nozz) and clean out BHA Jt by Jt f/ 370 to 507m. Change elevator and Cont. RIH on 5" DPs to 3786m (7" L.Lap), Ream Down To 3787m. D/Out CMT to 3789m (P.O.B), Start D/Out P.O.B @

3789m to 3790m, Wash & Ream Down While Work on Mud to 4141m (0.5m Top Of LDC), D/Out Debries Junk of P.O.B & CMT to 4141.5m (LDC).

Pump 30 bbl Hi-Vis Pill, Ciculated till shakers clean. POOH f/ 4141 to 3780m. Closed top rams and performed Liner Intigrity Test with 1500 psi for 15 min, OK. Resume POOH f/ 3780 to surface, B/O 5-7/8" R.Bit. Retrieved bushing. M/up & RIH By 5-7/8" Tri-Cone Bit (used,open) with 7" & 9-5/8" scraper as Tandem BHA to 3800m.

Cont. RIH By 5-7/8" Tri-Cone Bit (used, open) with 7" & 9-5/8" scraper as Tandem BHA to 4141.5m (LDC depth) while scrap inside 7" liner & Dry test packer set depth inside 9-5/8" CSG interval (3700-3740m) several times. Pump 40 bbl Hi-Vis pill and circulated btm's up. Pump and spot 30 bbl Non-Solid brine (CaBr2) inside 7" liner. POOH 5-7/8" Tri-Cone Bit with 7" & 9-5/8" scraper f/ 4141 to 1000m. Slip & Cut drilling line.

Resume POOH to Surf. B/O & L/D 5-7/8" Tri-Cone Bit. Held PJSM, P/U & M/U dry test assembly and RIH with 4 STDs 6-1/2" DC followed by 5" DPs to 1650m while fill up string with cushion fluid under supervision of dry test supervisor. Slip & Cut 1040 ft of damaged drilling line. Resume RIH with dry test assembly f/ 1650 to 3004m while fill up string with cushion fluid under supervision of dry test supervisor. Cont. RIH with dry test assembly f/ 3004 to 3734m.

Change TDS Link. M/U FOSV on string. R/U Dry test surface Equip & L/U to C.M. Press test surface line to 2500 psi/10min; OK. Record P/U & S/O string. Set 9-5/8" Dry test PKR @ 3730m. Closed top rams, apply 500 psi in to annulus for set packer test; OK. Start monitoring flow thru DST Ch. Manifold for 3 Hrs; No-Bubble. While Obs. Ann Level; Static. Close DCIP and monitor the well for 6 Hrs. Drop Bar & Rev. circ. until balanced MW on 103Pcf while dump to 20bbl water. Unset PKR. R/D 9-5/8 Dry test surface tools. Changed TDS links. POOH with dry test assembly f/ 3734 to to suf. L/D Dry test tools while take flowing sample.

Change top rams to 4-1/2" X 7" VBR, L/D mouse hole, install shooting nipple and R/U WL logging tools & perform body test against logging BOP, ok. Run SBT/VDL/CCL/GR log to 3772m, took weight, try to pass, sev. times, no succ. POOH WL to surf. RIH WL with 2jt 4.5" guns as dummy run to 3772m. Held up. Try to pass several times; "No-Succ". POOH WL to surface. R/D WL Equipment. L/D shooting nipple.

P/U & M/U 5-7/8" MT Bit (Kingdream, Used, 3X Open NZLs) + 4-3/4" B.Sub, RIH w/ 5 Stds 4-3/4" DC + 3 Stds 3-1/2" HWDP + 10 Stds 3-1/2" DP & Followed by 5" DPs to 4141.5m (LDC Depth). F/U string & Break Circ. every 15 Stds. Meanwhile Wash Dn f/ 3700m. CBU & Uniform MW (in/Out), Meanwhile work on mud rheology. Pump & Spot 30 bbl 95 pcf CaBr2 (Non-Solid Brine). Commence POOH w/ 5-7/8" MT Bit f/ 4141.5 to surface, F/U the well; NL-NG. L/D Bit. Bit Dull: 2-2-BT-A-F-I-LT-LOG.

Set 7" shooting nipple. Install logging BOP. Test same to 1000 psi; OK. R/U & Assemble SeaLand Co. CCL/GR/SBT/VDL Logging tools & Equip. RIH w/ W/L logging tools (CCL/GR/SBT/VDL: Max OD: 3.5", Total Len: 16.49 m, Total Wt: 364 Kg) f/ surface to 4138.5m (3m above Top of LDC). Power on SBT tools, Log up f/ 4138.5m

to 3750m. RIH again as repeat log f/4125m to 4000m. Power off tools. POOH W/L logging tools to surface. R/D SeaLand Co. CCL/GR/SBT/VDL Logging tools & Equip.

Perforation Summary

Set 7" shooting nipple. Install logging BOP. Test same to 1000 psi; OK. Meanwhile load 4.5" gun by 101 No. Bullet for run #1 & prepare wire line cable head. Wait on daylight due to explosive material safety regulation. All the times Circ. Across well head; NL-NG.

Cont. Wait on daylight due to explosive material safety regulation. Meanwhile load bullets on gun carrier. Due to the cloudy sky, Sealand refuses to armed WCP HSD Gun Assy. Held PJSM. Armed the WSP gun. RIH w/ 4.5" WCP HSD Gun Assy as Run #1 (Gun length: 6.45m, Net Length: 6.09m, Shot Density: 5 SPF, No. of Charge: 101, Phasing: 72 Deg, Explosive Type: HMX) to 4082m. Meanwhile perform depth correlation. Stop at shoot interval (Perforation Interval: 4075.91-4082m). Fire the gun. Obs. Shooting indication. POOH to surface; Obs. All bullets fired. L/D gun Assy run #1. RIH w/ 4-1/2" WCP HSD Gun Assy as Run #2 (Gun length: 6.45m, Net Length: 1.41m, Shot Density: 5 SPF, Phasing: 72 Deg, No. of Charge: 24, Explosive Type: HMX) to 4075.91m. Meanwhile perform depth correlation. Stop at shoot interval (4074.5-4075.91m). Fire the gun. Obs. Shooting indication. Check Ann. Level; "Static". POOH to surface; Obs. all bullet fired. L/D gun Assy run #2. While wait on daylight due to explosive material safety regulation, load bullets in gun carrier. Open Top rams & P/U 7" Shooting Nipple. Close the SBR, Established Circ. Across well head thru C/M; NL-NG.

Due to the cloudy sky, Sealand refuses to armed WCP HSD Gun Assy. Held PJSM. Armed the WSP gun. RIH w/ 4.5" WCP HSD Gun Assy as Run #3 (Gun length: 6.45m, Net Length: 3m, Shot Density: 5 SPF, No. of Charge: 50, Phasing: 72 Deg, Explosive Type: HMX) to 4070.5m. Meanwhile perform depth correlation. Stop at shoot interval (Perforation Interval: 4067.5-4070.5m). Fire the gun. Obs. Shooting indication. POOH to surface; Obs. All bullets fired. L/D gun Assy run #3.

Due to the cloudy sky & Bad weather, Sealand refuses to armed WCP HSD Gun Assy. While wait on daylight due to explosive material safety regulation, load bullets in gun carrier. Open Top rams & P/U 7" Shooting Nipple. Close the SBR, Established Circ. Across well head thru C/M; NL-NG.

Due to the cloudy sky, Sealand refuses to armed WCP HSD Gun Assy.

Held PJSM. Armed the WSP gun. RIH w/ 4.5" WCP HSD Gun Assy as Run #4 (Gun length: 6.45m, Net Length: 3m, Shot Density: 5 SPF, No. of Charge: 50, Phasing: 72 Deg, Explosive Type: HMX) to 4066m. Meanwhile perform depth correlation. Stop at shoot interval (Perforation Interval: 4063-4066m). Fire the gun. Obs. Shooting indication. POOH to surface; Obs. All bullets fired. L/D gun Assy run #4. Meanwhile load bullets on gun carrier.

Armed the WSP gun. RIH w/ 4.5" WCP HSD Gun Assy as Run #5 (Gun length: 6.45m, Net Length: 4.4m, Shot Density: 5 SPF, No. of Charge: 73, Phasing: 72 Deg, Explosive Type: HMX) to 4061.4m. Meanwhile perform depth correlation. Stop at shoot interval (Perforation Interval: 4057-4061.4m). Fire the gun. Obs. Shooting indication.

POOH to surface; Obs. All bullets fired. L/D gun Assy run #5. Meanwhile load bullets on gun carrier. Armed the WSP gun. RIH w/ 4.5" WCP HSD Gun Assy as Run #6 (Gun length: 6.45m, Net Length: 6.09m, Shot Density: 5 SPF, No. of Charge: 101, Phasing: 72 Deg, Explosive Type: HMX) to 4045m. Meanwhile perform depth correlation. Stop at shoot interval (Perforation Interval: 4038.91-4045m). Fire the gun. Obs. Shooting indication. POOH to surface; Obs. All bullets fired. L/D gun Assy run #6. Meanwhile load bullets on gun carrier.

While wait on daylight due to explosive material safety regulation, load bullets in gun carrier.

Completion Summary

Open Top rams & P/U 7" Shooting Nipple. Close the SBR, Established Circ. Across well head thru C/M; NL-NG.

L/D 5 Stds 6-1/2" DC Jt by Jt. P/U & M/U 5-7/8" M.M J.Mill (CylanderSazi, Used, 5* 12/32" Port) & RIH w/ 4-3/4" Bit sub (Float valve in) + 5 Stds 4-3/4" DC+ 3 Stds 3-1/2" HWDP + 10 Std 3-1/2" DP & Followd by 5" DPs to 4132m (9m Above 7" LDC) while F/U string & break Circ. Every 15 Stds; NL-NG. Manwhile Wash down f/ 3786 (7" L.Lap) to 4132m w/o any drag. Circ. BTM's Up, while reciprocate string; NL-NG. M/U FOSV on string. L/U CMT Line to string. Cont. Circ. BTM's Up, while reciprocate string; NL-NG. Press test CMT Line w/ 3500 psi; "OK".

Displace whole well @ 4132m w/ 870 bbl 104 pcf Non-Solid Completion Fluid (Got 40 bbl contaminated w/ mud on return); NL-NG. Close FOSV. Perform flow check the well; Static. Meanwhile wash & Clean divider & flow line. POOH w/ 5-7/8" M.M J.Mill f/4132 to 2250m, RIH w/ 10 Stds 5" DP to 2550m, POOH to 2400m (L/D Totally 190 Jts 5"DP Jt by Jt), while F/U the well w/ Non-Solid Completion Fluid.

POOH w/ 5-7/8" M.M J.Mill f/ 2400m to surface (L/D Totally 474 Jts 5"DP, 30 Jts 3-1/2" DP, 9 Jts 3-1/2" HWPD & 15 Jts 4-3/4" DC Jt by Jt), while F/U the well w/ Non-Solid Compleition Fluid; NL-NG. L/D 5-7/8" M.M J.Mill.

Retrieve 11" wear bushing. Clear rig floor. R/U Sarvak Kish Co. Completion string running equipment. R/U Slick line equipment. Run 2.75" Gauge Ring to NO-GO depth & check all connections; OK. Cont. RIH w/ 3 1/2" Pup Jt + 3 1/2" SSD (Seal Bore: 2.75", X profile, Close position, Downward open) + 3 1/2" Pup Jt + 1 Jt 3 1/2" TBG + 3 1/2" Pup Jt + 3 1/2" Traveling Jt (full open position, Dressed w/ 3 No. Shear Pin, Splined Type) + 3 1/2" Pup Jt + 1 Jt 3 1/2" TBG + 3 1/2" Pup Jt + 3 1/2" CIV#1 & Tubing retrievable CIM(10 2#, Dual Check Valve, WP: 15K psi) + 3 1/2" Pup Jt + 1 Jt 3 1/2" TBG + 3 1/2" Pup Jt + 3 1/2" CIV#2 & Tubing retrievable CIM(10 2#, Dual Check Valve, WP: 15K psi) + 3 1/2" Pup Jt to 75m. P/U & Install CIL #1,2 in spooler machine & Install Pulley in monkey board. Pass CILs f/ pulley. Connect CILs to CIVs. Test them separately, both CILs to 2000 psi for 20 min; "OK". Cont. RIH w/ totally 12 Jts 3-1/2" TBG to 146m. P/U & M/U XOS 3-1/2" x 4-1/2" HSM-3. Cont. RIH w/ 2 Jts 4-1/2" TBG to 166m. R/U Slick Line equipment. Run 2.875" Gauge Ring to top of SSD. R/D Slick line tools. Press test surface test line w/ 8000 psi; "Ok". Line up surface test Line to string. Perform Press test completion string against SSD Check valve @ 166m w/ 7000 psi for 15min; "Ok".

Cont. Run 3-1/2" x 4-1/2" Completion string 1030m. Line up surface test Line to string. Perform Press test completion string against SSD Check valve w/ 7000 psi for 15min; "Ok".

Cont. Run 3-1/2" x 4-1/2" Completion string to 2012m. Line up surface test Line to string. Perform Press test completion string against SSD Check valve w/ 7000 psi for 15min; "Ok". Cont. Run 3-1/2" x 4-1/2" Completion string 3100m.

Line up surface test Line to string. Perform Press test completion string against SSD Check valve w/ 7000 psi for 15min; "Ok". Cont. Run 3-1/2" x 4-1/2" Completion string f/ 3100 to 3780m.

Line up surface test Line to string. Perform Press test completion string against SSD Check valve w/ 7000 psi for 15min; "Ok". Cont. Run 3-1/2" x 4-1/2" Completion string to 3812m. P/U & M/U TR3SV Assy on string. Connect control line and Press test to 7500 psi for 15min; "OK". Bleed of Press to 5000 psi. M/U 1 Jt 4-1/2" TBG and RIH to 3829m.

Line up surface test Line to string. Perform Press test completion string & TR3SV Assy against SSD Check valve w/ 7000 psi for 15min; "Ok". Bleed of control line Press to Zero. Bleed of Press above flapper to 1000 psi. Monitor for any Press build up as inflow test of flapper; Negative. Check & Test Equalizing Function of TR3SV; "OK". M/U & RIH 4 Jts 4-1/2" TBG to 3867m. Apply 5200 psi Press in CIL #1 and rupture CIV #1 rupture disk, check string; Obs return (indication of successful rupture). Apply 5500 psi Press in CIL #2 and rupture CIV #2 rupture disk, check string; Obs return (indication of successful rupture). M/U 4-1/2" Fluted Swage (18.9# TPCQ-EX Pin Up X HSM3 Pin Down) & TBG HGR (MSP, 10K X 11" Bowl X 4 1/2" ACME Box Up X 4 1/2" TPCQ-

EX Box Down, 2 Set O-Ring on Body & 2 Set O-Ring on Extended neck). M/U 4-1/2" Running & Pulling tools for TBG HGR (ACME X TPCQ-EX) & L/J (18.9#, L-80, TPCQ-EX) on HGR. Pass CILs & CL thru TBG HGR. Cut CILs & CL 1.5m above TBG HGR. Cont RIH on L/J to 3877m. Secure CILs on each connection by cross coupling protectors. Apply & Hold 1000 psi Press in both CILs during RIH. All the time Monitor pit level; "NL-NG".

Line up surface test Line to string. Perform Press test completion string, TBG HGR & L/J against SSD Check valve w/ 7000 psi for 15min; "Ok". Install Golpa. Flange & 4-1/16" Gate Valve on Completion string. R/U slick line equipment. RIH & Set 3.437" Protection sleeve in TR3SV. Retrieve 2.75" WFB Check valve from SSD. RIH w/ 2.562" plug to No-Go depth. Set Plug in No-Go L/N. POOH to surface. RIH w/ 2" prong to No-Go depth & Set in No-Go L/N. POOH to surface. RIH w/ 2.8" B Shifting tools to SSD Depth. Check SSD is full close & drift string. POOH to surface. R/D Slick line equipment. L/D Golpa Flange. POOH to 3879.3m, Space out 1.5 m above THS. Line up surface test Line. Press test same w/ 8000 psi; "Ok". Line up surface test Line to string. Set PKR as per procedure and increase Press Gradually to 3500 psi (Obs. Set PKR indication). Increase Press to 7000 psi as completion string Press test; "Ok". Release Press. Perform pull test w/ 15 klbs overpull; "OK". S/O 20 Klbs Wt. and Obs. Back flow from string after expansion joint pins sheared. Land TBG hanger in THS. Tighten all Tie- Down Screws. Close Hy-drill and Press test Tie-Downs to 2000 psi; "OK". Line up surface test line to string. Perform Press test completion string to 5000 psi for 15 min as final completion string test; "OK". L/U to 9-5/8" Ann. Press test to 2000 psi; "OK". R/U Slick line & Retrieve 3.437" Protection Sleeve of TR3SV. Bleed off CL Press to zero & Close TR3SV. N/D Bell Nipple. Back off L/J & TBG HGR Running tools f/ TBG HGR. B/O & L/D same. Install 4" 10k TWCV. Pass 1/4" Plugged CL f/ BOP Stack while L/D Mouse hole. Press test 4" 10K TWCV against SBR to 6400 psi; "OK".

N/D 13-5/8" BOP Stack; 5K Ann Preventer, 10K 2-7/8" X 5" VBR Top Rams + 10K SBR Middle Rams, Drlg Spool,10K 5" Fix BTM Rams & Spacer Spool. Disconnect all hydraulic hoses, Choke lines & Kill lines.

Install FS Seal inside top of TBG HGR neck. N/U & Install 11" X 4 1/16"-10K BTM master valve. Meanwhile P/U BMV; Connect & Pass 1/4" CL & 3/8" CILs thru BMV Flange. Tighten BMV Bolts. In order to energize & Press test FS Seal of TBG HGR. L/U pump truck to BMV. Press test FS Seal of THG HGR w/ 8000/1000 psi for 15/5 min; "Ok". Tighten All nuts.

Connect CL to C/L Exit block cap. Press test CL connection to bottom section & U-Ring to 8000 psi for 15min; "OK". Press test 3/8"CILs to 2000 psi for 15min; "OK". Press test between 2 O-Ring of TBG HGR neck to 8000 psi for 15 min; "OK". Cavity Press test between S-Seal, THS & TBG Head Adapter Ring gasket, 2nd TBG HGR O-Ring, Tie-Dn Screws, CIV Port, Exit port to 8000 psi for 15 min; "OK". N/U 4-1/16"-10K X-mass

tree Solid block (MSP - Drilex) & Install same on BMV. Tighten all bolts. Perform body test to 8000psi; "OK".

Ret. 4" TWCV. Open TR3SV. R/U slick line Equip. Install SL BOP & Lubricator. Press test; "OK". Set 3.437" Protection Sleeve in TR3SV. Run w/ 2" SB Pulling & Ret. prong f/ No-Go. POOH to surface. Run w/ GS Pulling & Ret. Plug f/ No-Go. L/U to 9-5/8" Ann. Press test to 2000 psi; "OK". Ret. 3.437" Protection Sleeve. Bleed off CL Press & Close TR3SV. Install 4" TWCV in TBG HGR. Close All XMT Valve except BMV & Secure the well. Released the rig. Release the Rig @ 17-Mar-2025 (1403-12-27), 24:00

Liner Lap Dry Test Report

7” Liner Data
35 ppf Weight
110ss Grade
5.879” Drift
TP-CQ premium connection

Table 2-6: AZNS-207 7" Liner Information

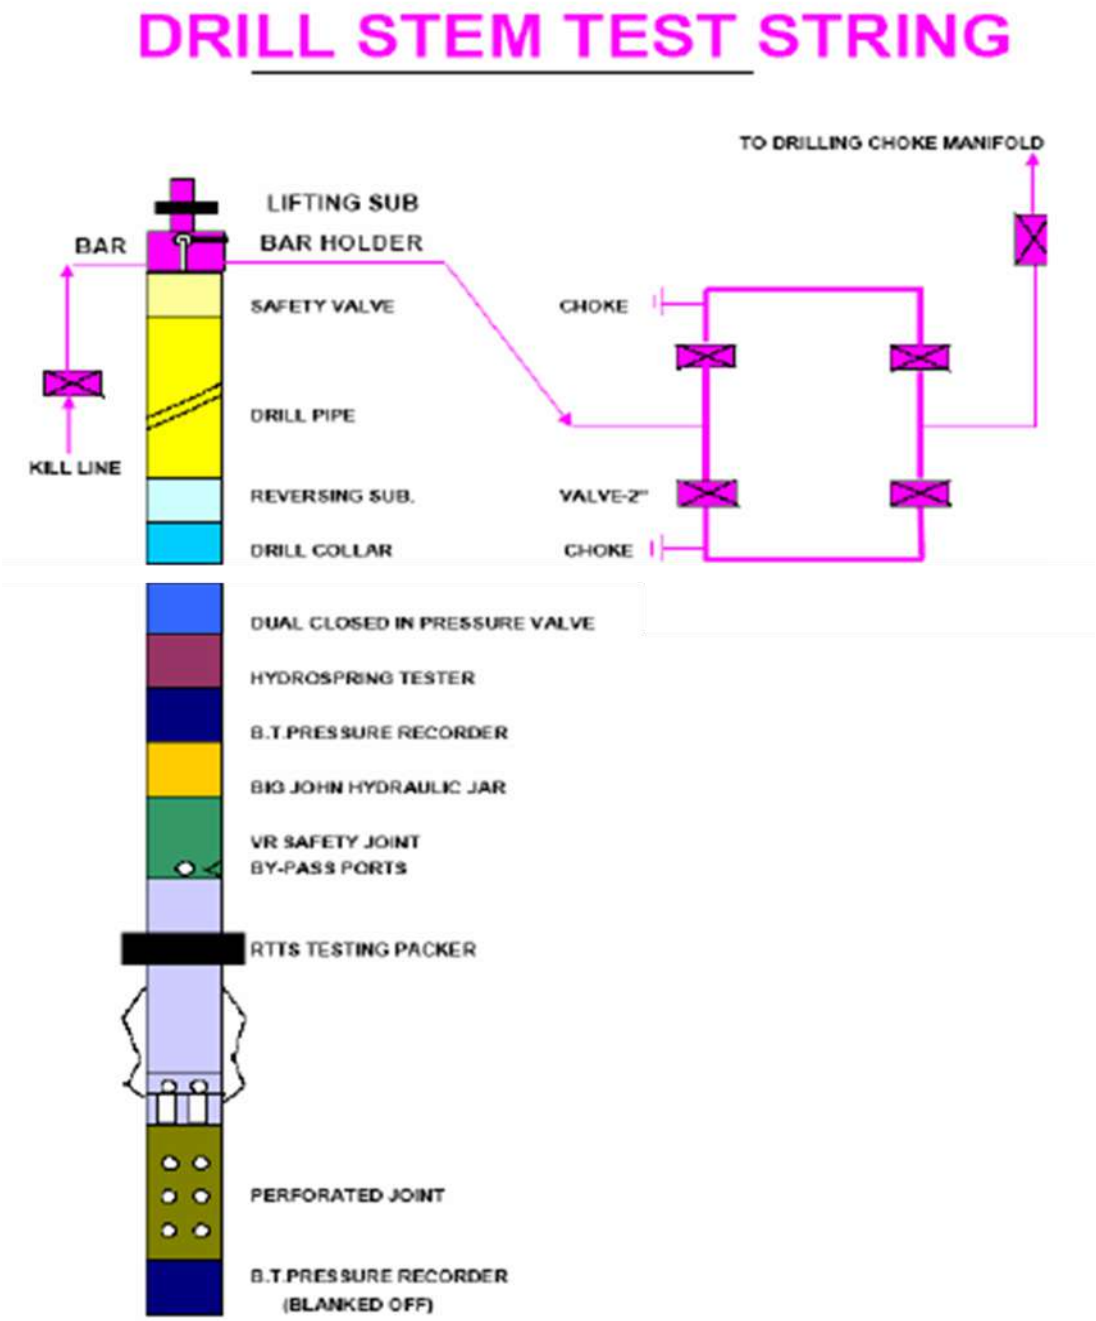


Figure 2-1: AZNS-207 Dry Test Event

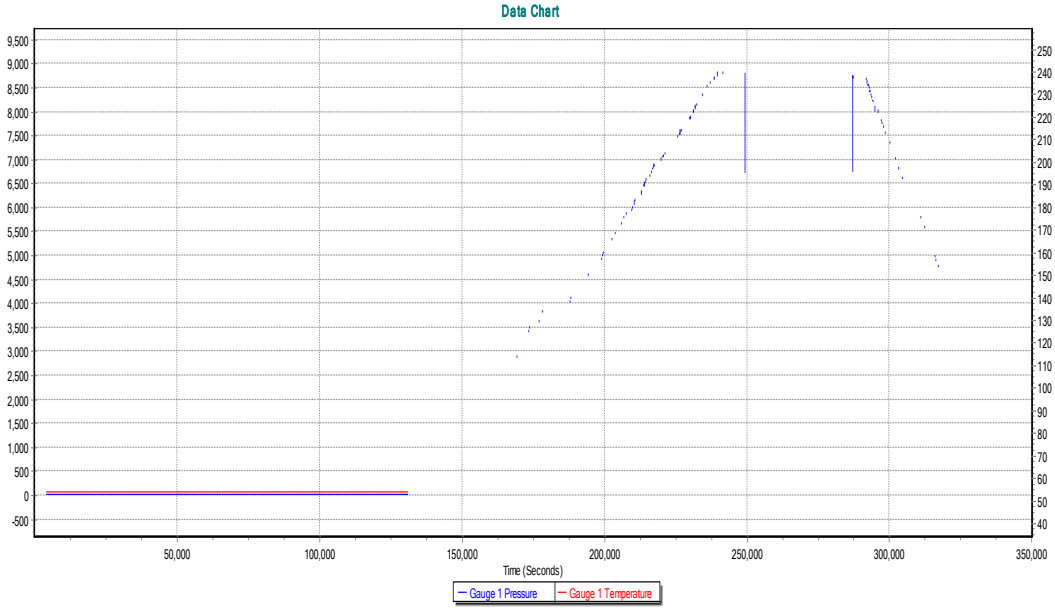


Figure 2-2: AZNS-207 Bottom BT Chart

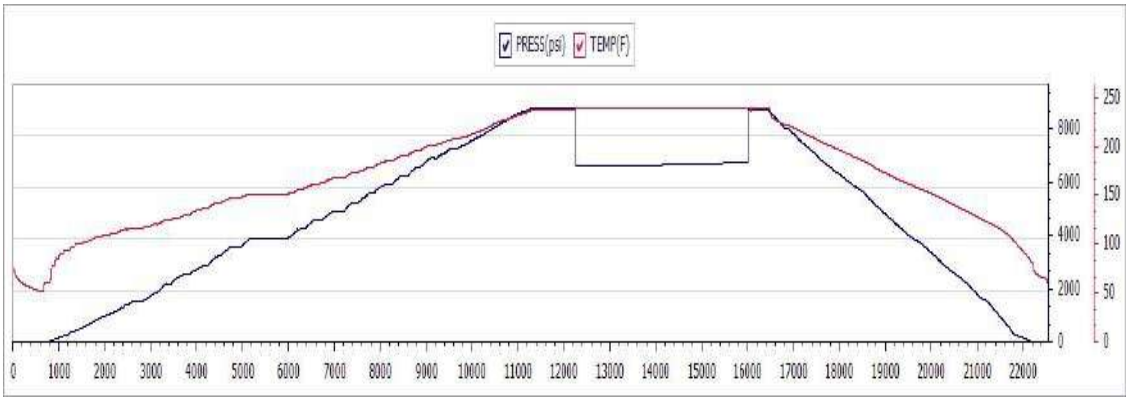


Figure 2-3: AZNS-207 Middle BT Chart

Row	Description	Time	Bottom Bt.	Middle Bt.
1	Initial Mud Static Pr. (psi)	06:00	8798	8763
2	Open Well Pr. (psi)	06:20	6629	6595
		09:20	6630	6595
3	Close Well Pr. (psi)	09:22	6630	6596
		15:05	6761	6722
4	Final Hydrostatic Pr. (psi)	-	8747	8710

Table 2-7: AZNS-207 Downhole Test Result Data

2.3 AZNS-207 Well Sketch

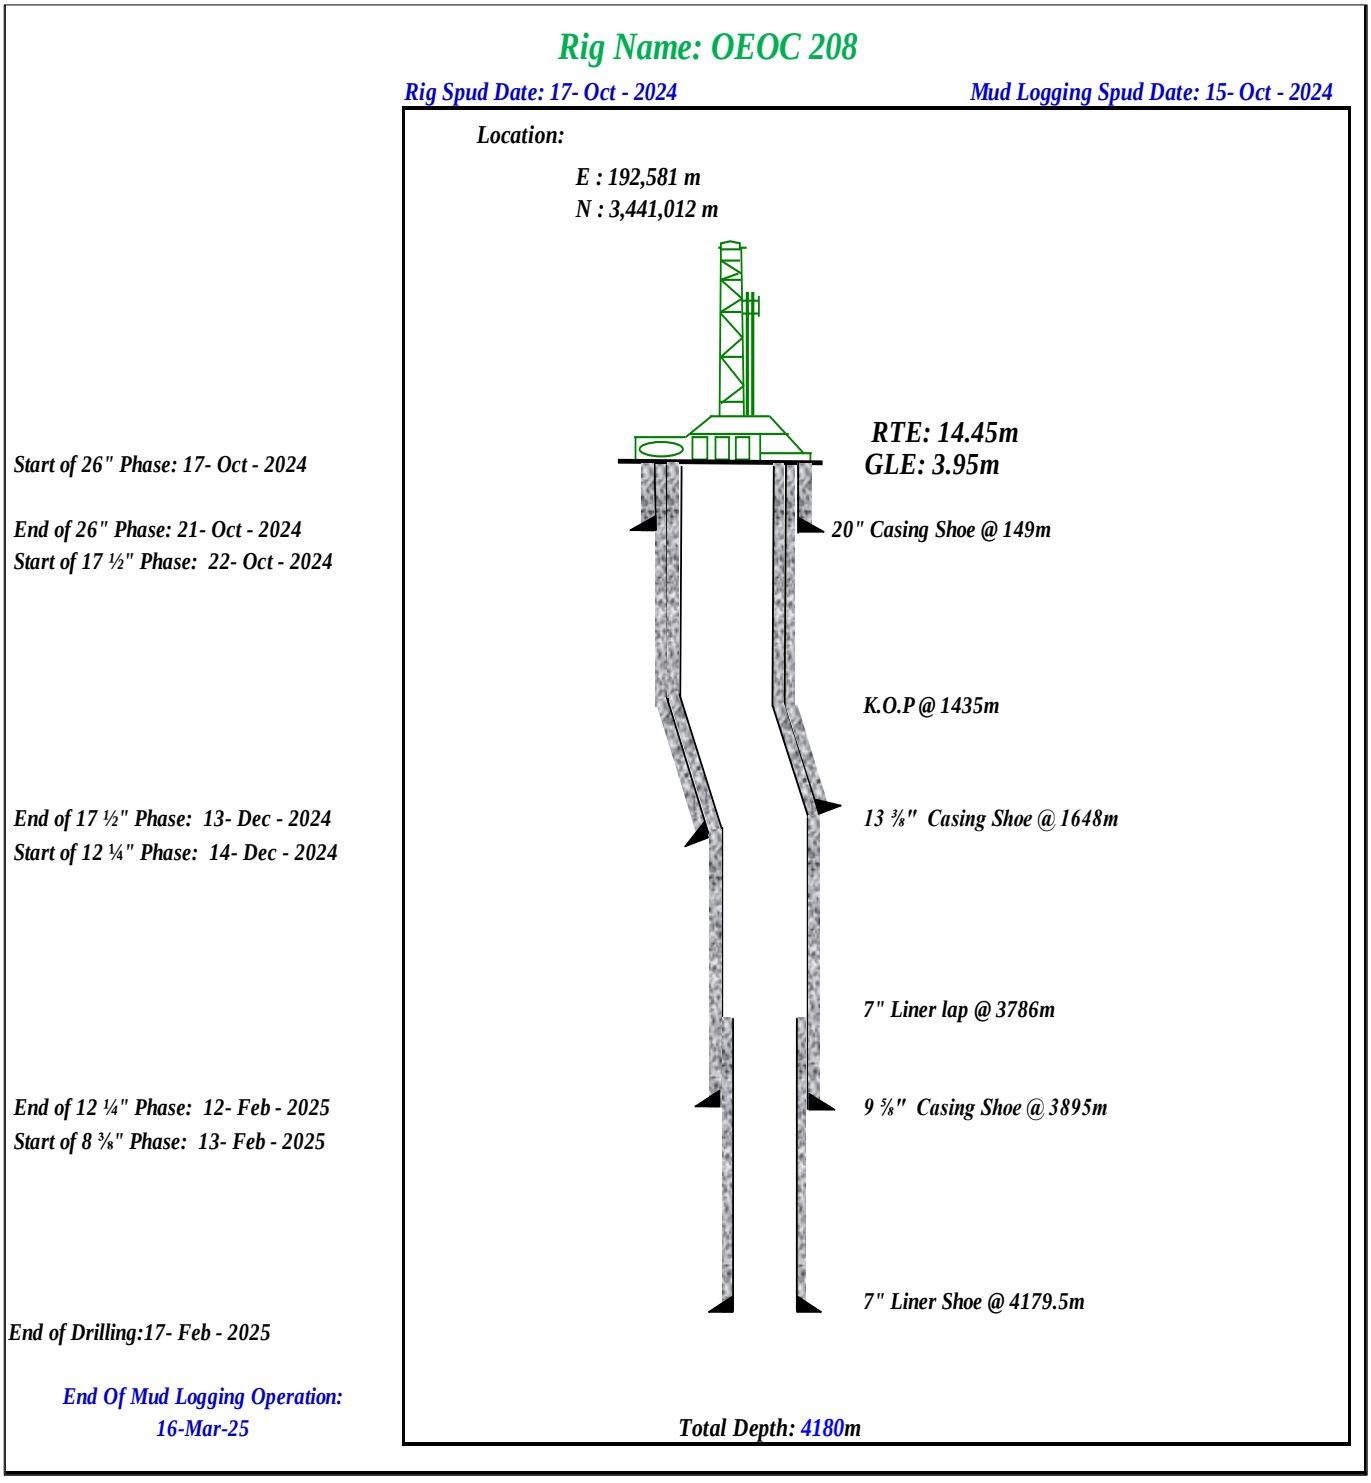


Figure 2-4: AZNS-207 Well Sketch

2.4 Mud Weight vs. Depth

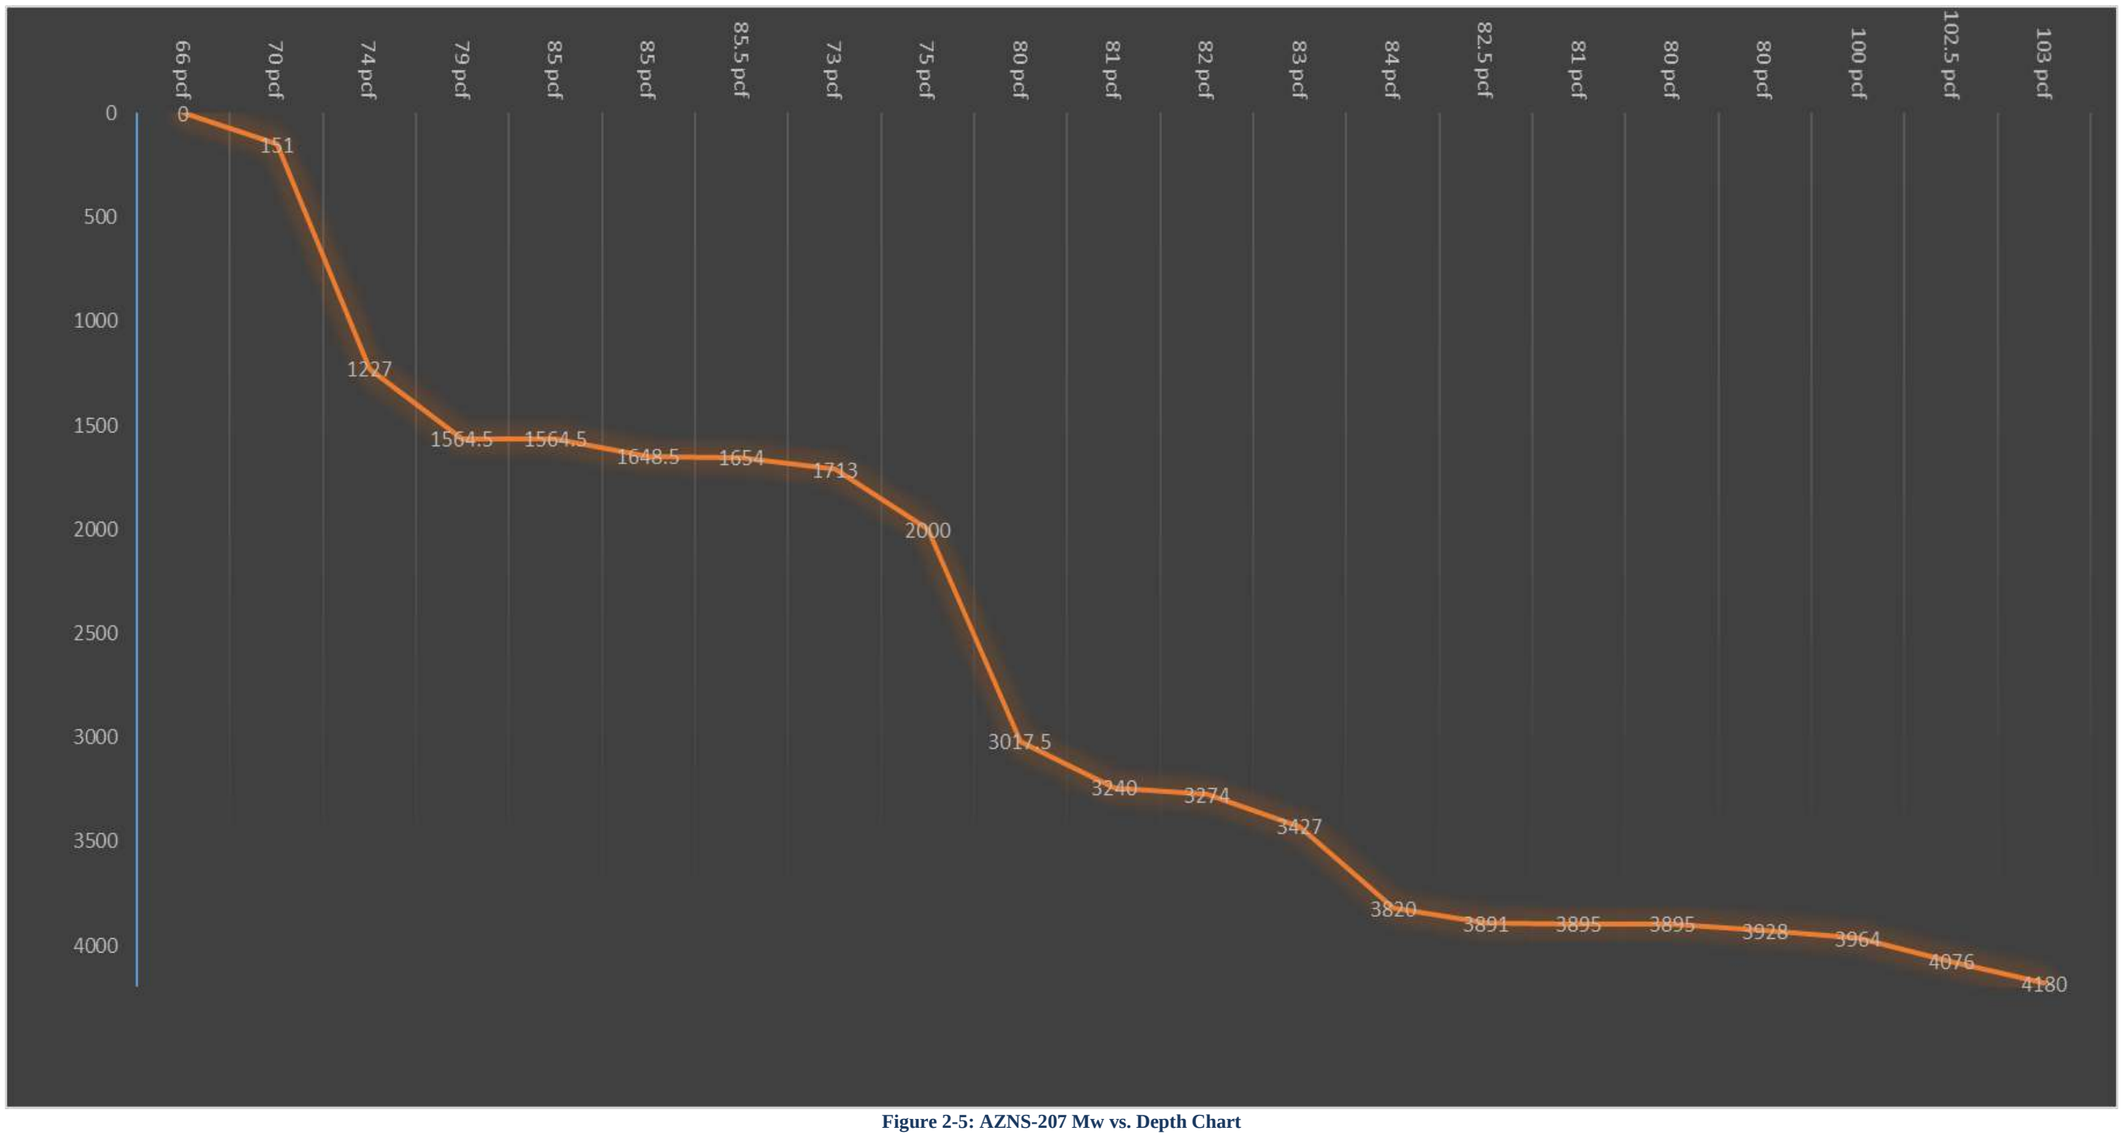


Figure 2-5: AZNS-207 Mw vs. Depth Chart

2.5 Bit Record Table

BHA Record AZNS-207, S.T-1

Seq. No.	Bit No.	Bit Diam. (inch)	Mfgr.	Bit Type	Mfgr. Serial No	IADC CODE	Jets (1/32")	Depth In (metres)	Depth Out (metres)	Drill. Time (hours)	R.O.P (avg) (m/hr)	MW (avg) (pcf)	*Bit Condition*
1	1	26	King Dream	M.T.	2207721JH	115	20 Center Jet + 3 × 18	14.0	151.0	25.0	5.48	68.0	1 1 WT A E I NO TD ***POOH Due to reach 20" Casing point***
2	2	17 ½	King Dream	M.T.	2306181JH	135	3 × 18	151.0	165.0	7.0	2.00	70.0	-- ***POOH Due to Change BHA***
3	2 run#2	17 ½	King Dream	M.T.	2306181JH	135	2 × open + 1 × 18	165.0	793.0	45.4	13.80	71.5	1 1 WT A E 1/16" BU,WO BHA ***POOH Due to Change BHA***
4	3	17 ½	Haliburton	PDC	16FX65S	S323	9 × 14/32"	793	1373.8	62	9.4	74.0	3 8 RO NT X 1/16" CT,BU PR ***POOH due to low ROP***
5	4	17 ½	Haliburton	PDC	FSX643Z	S234	2 × 14+ 7 × 16	1373.8	1480.3	10.5	10.2	76.0	2 1 CT N X I BU/BT TW ***POOH due to twist off string***
6	Overshot	12 ¾	--	Overshot	--	--	--	1480.3	1480.3	--	--	76.0	-- ***POOH Due to Change BHA***
7	Overshot	11 ¾	--	Overshot	--	--	--	1480.3	1480.3	--	--	76.0	-- ***POOH Due to Change BHA***
8	4 run#2	17 ½	Haliburton	PDC	FSX643Z	S234	2 × 14+ 7 × 16	1480.3	1562	18.5	1.67	76.0	5 8 LD A X 1/8 BU PR ***POOH due to low ROP***
9	2 run#3	17 ½	King Dream	M.T.	2306181JH	135	2 × open + 1 × 18	1562	1564.5	3.5	1.67	76.0	1 1 WT A E 1/16" BU,WO BHA ***POOH Due to Change BHA***
10	5	17 ½	Reed Hycalog	PDC	222691	TFR 716	7 × 16	1564.5	1564.5	--	--	76.0	Bit left in hole ***POOH due to twist off string***
11	Overshot	11 ¾	--	Overshot	--	--	--	1564.5	1564.5	--	--	76.0	-- ***POOH Due to Change BHA***
12	6	17 ½	King Dream	B.Bit	2205166JH	415	3 × 18 + Center Jet	1564.5	1564.5	--	--	83.0	1 3 BT G E I BU BHA ***POOH Due to Change BHA***
13	Overshot	11 ¾	--	Overshot	--	--	--	1564.5	1564.5	--	--	83.0	-- ***POOH Due to Change BHA***
14	Taper Mill	17 ½	--	Taper Mill	--	--	--	1564.5	1564.5	--	--	85.0	-- ***POOH Due to Change BHA***
15	6 run#2	17 ½	King Dream	B.Bit	2205166JH	415	3 × 18 + 1 × 16 center jet	1564.5	1564.5	--	--	85.0	-- ***POOH Due to Change BHA***
16	2 run#4	17 ½	King Dream	M.T.	2306181JH	135	3 × open	1435.00	1447.00	20.0	0.60	85.0	1 1 WT A E 1/8" BU/WO BHA ***POOH Due to Change BHA***
17	7	17 ½	King Dream	B.Bit	2301490JH	517	3 × 18 + Center Jet	1447.0	1552.00	55.0	1.90	85.0	1 1 WT A E I NO PR ***POOH due to penetration rate***
18	8	17 ½	Geo Diamond	PDC	20106	16MM	5 × 20 + 3 × 18	1552.00	1592.90	24.5	1.70	85.0	6 8 RO N/S/G X 1/8" BF PR ***POOH due to penetration rate***
19	7 run#2	17 ½	King Dream	B.Bit	2301490JH	517	3 × 22	1592.9	1616.00	20.0	1.15	85.0	1 1 WT A E I NO PP ***POOH due to decrease pump pressure***
20	7 run#3	17 ½	King Dream	B.Bit	2301490JH	517	3 × 22	1616.0	1648.50	55.0	0.59	85.0	2 3 WT A I F BT TD ***POOH due to reach casing point***
21	9	12 ¼	ReedHycalog	PDC	--	--	6 × 15	1648.50	1831.00	46.5	3.90	73.0	8 8 RO A X I WT PR ***POOH due to penetration rate***
22	10	12 ¼	King Dream	B.Bit	2304290JH	537	3 × open	1831.00	2000.00	24.0	7.00	75.0	1 1 WT A E I NO BHA ***POOH Due to Change BHA***
23	10 run#2	12 ¼	King Dream	B.Bit	2304290JH	537	3 × open	2000.00	2150.00	33.5	4.47	75.0	1 2 BT G E I NO PR ***POOH due to penetration rate***
24	11	12 ¼	Best	PDC	220799	M423	2 × 14 + 5 × 13 + 2 × 12	2150.00	2696.50	66.0	8.30	75-77	4 4 LT N/C X I WT PR ***POOH due to penetration rate***
25	12	12 ¼	Best	PDC	220798	M423	4 × 14 + 5 × 13	2696.50	2810.00	29.0	3.90	77+-78	1 1 WT A X I NO LIH ***POOH due to left in hole***
26	Over shot	10 ⅛"	--	--	--	--	--	2810.00	2810.00	--	--	77+-78	 ***POOH Due to Change BHA***
27	12 Run#2	12 ¼	Best	PDC	220798	M423	4 × 14 + 5 × 13	2810.00	2868.00	14.7	3.90	79.0	6 2 NT L X I BT PR ***POOH Due to Change bit***
28	13	12 ¼	Best	PDC	220796	M423	4 × 14 + 5 × 13	2868.00	3006.70	32.0	4.30	79.0	1 2 LT N X I PN LIH ***Due to fishing***
29	Over shot	10 ⅛"	--	--	--	--	--	3006.70	3006.70	--	--	79.0	
30	13 Run#2	12 ¼	Best	PDC	220796	M423	4 × 14 + 5 × 13	3006.70	3027.20	22.0	0.90	79-80	3 8 RO N X I BT PR ***POOH due to change bit***
31	14	12 ¼	Best	PDC	--	M423	4 × 14 + 5 × 13	3027.20	3240.00	49.5	4.30	80-81	5 3 LT NS X 1/16" BT WO ***POOH due to left in hole***
32	Over shot	10 ⅛"	--	--	--	--	--	3240.00	3240.00	--	--	81.0	
33	15	12¼"	SMITH	PDC	M88VPXX	M424	8 × 16	3240.00	3275.00	14	2.5	81-82	6 7 Blade N X 1/8" BT/LT PR ***POOH due to penetration rate***
34	10 Run#3	12 ¼	King Dream	B.Bit	2304290JH	537	3 × 20	3275.00	3284.40	11.0	0.90	82.0	2 4 BT G E I WT PR ***POOH due to penetration rate***
35	RCJB	10 ⅛"	--	--	--	--	--	3284.40	3284.90	--	--	82.0	
36	16	12 ¼"	Best	PDC	M1664	M424	9 × 13	3285.0	3872.0	166.5	3.5	82-84	2 2 WT A X I LT PR ***POOH due to penetration rate***
37	17	12 ¼"	Burintekh	PDC	4263	M323	6 × 15	3872.0	3891.0	19.0	2.7	82.5-84	-- ***POOH due to change and check BHA***
38	17 Run#2	12 ¼"	Burintekh	PDC	4263	M323	6 × 15	3891.0	3895.0	2.0	2.0	80-81	1 1 WT A X I NO HP ***POOH due to change BHA***
39	--	6 ½"	--	Center cut Bit	--	--	--	3895.0	3895.0	--	--	80.0	-- ***POOH due to run casing 9 ⅝"***
40	18	8 ⅜"	Best	PDC	220852	M433	7 × 14	3895.0	4180.0	57.0	5.0	100-103	1 1 WT A X I BT TD ***POOH due to reach to TD.***
41	18 Run#2	8 ⅜"	Best	PDC	220852	M433	7 × 14	4180.00	4180.00	--	--	103.0	1 1 WT A X I BT TD ***POOH due to run liner 7"***
42	18 Run#3	8 ⅜"	Best	PDC	220852	M433	7 × 14	4180.00	4180.00	--	--	103.0	1 3 BT G X I WT BHA ***POOH due to change BHA***
43	19	5 ⅞"	Kingdream	R. Bit	2204638JH		3 × Open	4180.00	4180.00	--	--	103.0	2 2 BT A E I LT BHA ***POOH due to change BHA***
44	19 Run#2	5 ⅞"	Kingdream	R. Bit	2204638JH		3 × Open	4180.00	4180.00	--	--	103.0	2 2 BT A F I LT BHA ***POOH due to change BHA***
45	RTTS	--	--	--	--	--	--	4180.0	4180.0	--	--	103.0	-- ***POOH due to Run log***
46	19 Run#3	5 ⅞"	Kingdream	R. Bit	2204638JH	--	3 × Open	4180.00	4180.00	--	--	103.0	2 2 BT A F I LT LOG ***POOH due to crun log***
47	Junk Mill	5 ⅞"	CylanderSazi	--	--	--	5 × 12	4180.00	4180.00	--	--	103.5	-- ***POOH due to completion String.***

Table 2-8: AZNS-207 Bit Record

2.6 Bit Parameters Plot

Bit Plot Data AZNS-207, S.T-1							
Bit Number	Bit Size	Bit Type	Serial Number	HOB (hr)	Average ROP (m/hr)	Average WOB (klb)	Average RPM Bit
1	26"	M.T.	2207721JH	25	5.48	5	45
2	17 ½"	M.T.	2306181JH	75.4	11.6	20	75
3	17 ½"	PDC	16FX65S	62	9.4	25	150
4	17 ½"	PDC	FSX643Z	29	6.5	10	90
7	17 ½"	B. BIT	2301490JH	130	1.23	16	100
8	17 ½"	PDC	20106	24.5	1.7	16	137
9	12 ¼"	PDC	--	46.5	3.9	20	160
10	12 ¼"	B.Bit	2304290JH	68.5	4.47	20	120
11	12 ¼"	PDC	220799	66	8.3	15	145
12	12 ¼"	PDC	220798	43.65	3.9	15	120
13	12 ¼"	PDC	220796	54	0.9	17	130
14	12 ¼"	PDC	220797	49.5	4.3	15	160
15	12 ¼"	PDC	M88VPXX	35	2.5	18	150
16	12 ¼"	PDC	M1664	166.5	3.53	16	160
17	12 ¼"	PDC	4263	9	2.35	17.5	158
18	8 ⅜"	PDC	220852	57	5	15	115

Table 2-9: AZNS-207 Bit Parameters Plot

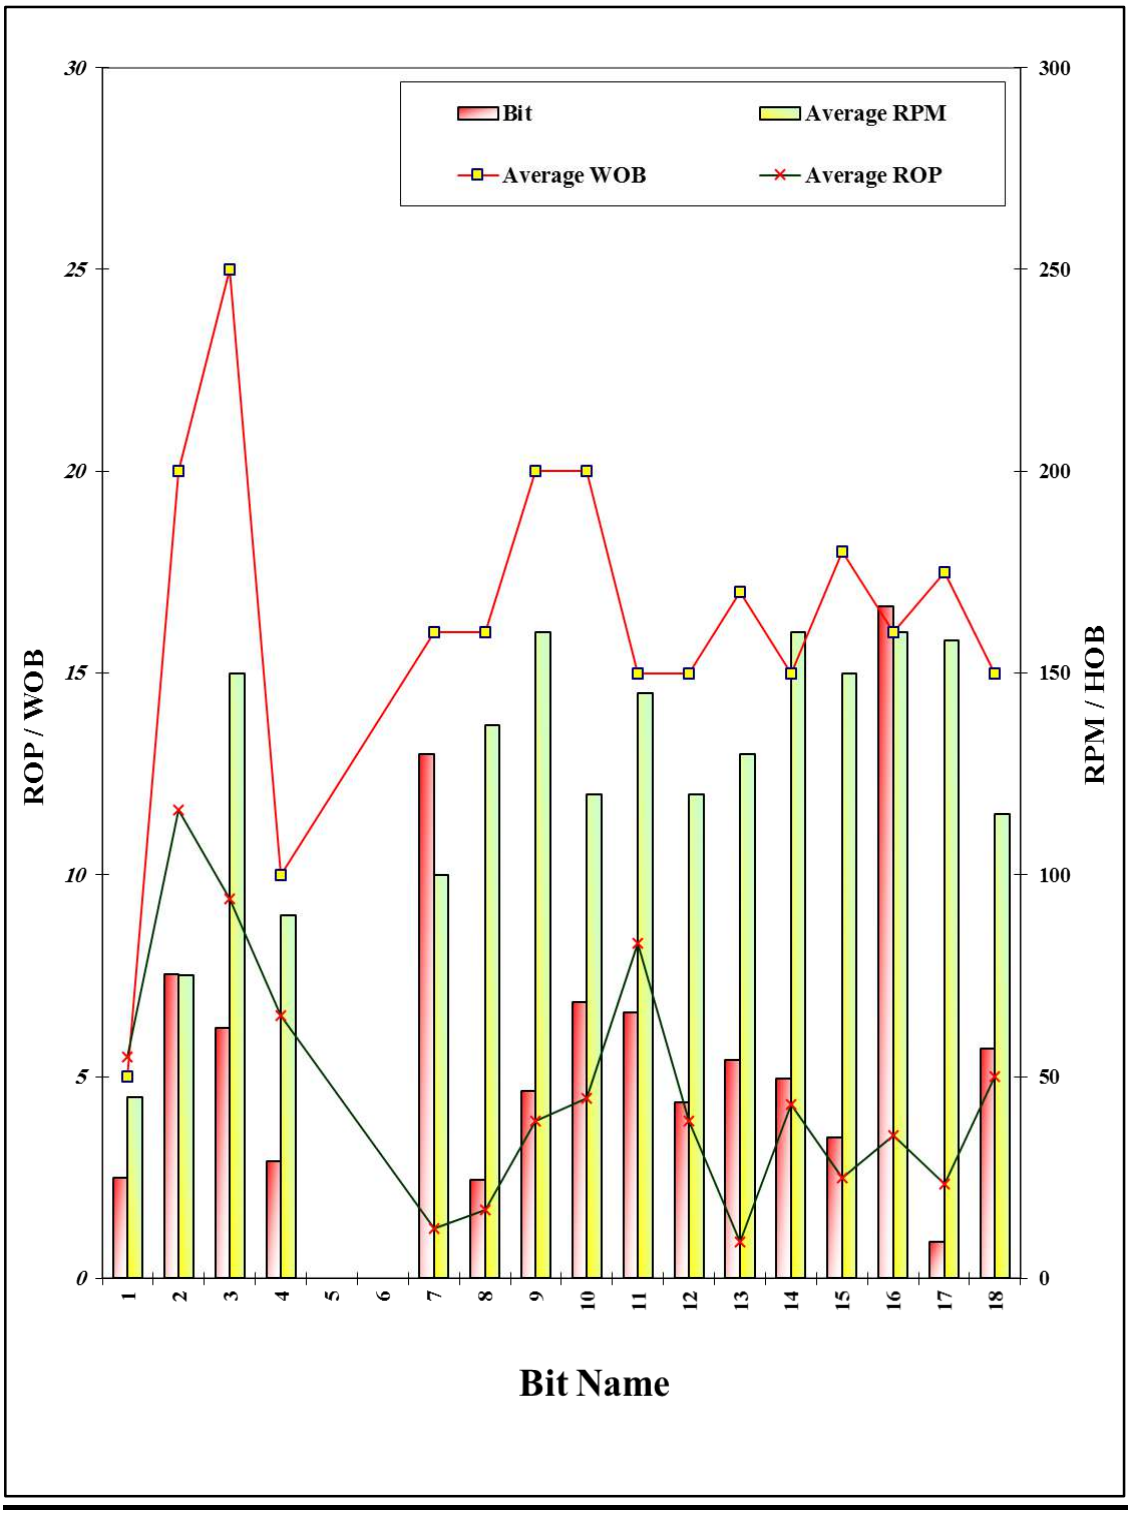


Figure 2-6: Bit Parameters Chart

2.7 Survey Data Table

Survey Data Table of AZNS-207, S.T-1 (TOTCO)		
Date	***Depth (m)***	***INC. (Degree)***
10/18/2024	*50*	*0*
10/18/2024	*108*	*0.25*
10/19/2024	*151*	*0.25*
10/23/2024	*422*	*0.75*
10/25/2024	*750*	*0.75*
10/27/2024	*1050*	*0.8*
10/30/2024	*1350*	*0.5*
12/14/2024	*1623*	*6*
12/17/2024	*1830*	*2.8*
12/23/2024	*2100*	*2.8*

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
Original Hole											
0	0	0	0	14.45	0	0	0	0	3441012	192581	Aghajari
108	0.25	46.5	108	-93.55	0.16	0.17	0.16	0.069	3441012.16	192581.17	
151	0.25	46.5	151	-136.55	0.29	0.31	0.29	0	3441012.29	192581.31	
495	0.75	46.5	494.99	-480.54	2.36	2.48	2.37	0.044	3441014.36	192583.48	
750	0.75	46.5	749.96	-735.51	4.66	4.91	4.69	0	3441016.66	192585.91	
1020	0.8	46.5	1019.94	-1005.49	7.16	7.55	7.21	0.005	3441019.16	192588.55	Gachsaran
1050	0.8	46.5	1049.94	-1035.49	7.45	7.85	7.5	0.005	3441019.45	192588.85	
1350	0.5	46.5	1349.92	-1335.47	9.79	10.32	9.86	0.03	3441021.79	192591.32	
1368	0.61	46.5	1367.92	-1353.47	9.91	10.44	9.98	0.185	3441021.91	192591.44	Asmari
1415	0.9	46.5	1414.91	-1400.46	10.34	10.89	10.41	0.185	3441022.34	192591.89	
1430	2.9	83.5	1429.9	-1415.45	10.46	11.36	10.87	4.495	3441022.46	192592.36	
1433	3.4	84.6	1432.9	-1418.45	10.48	11.52	11.03	5.036	3441022.48	192592.52	
SideTrack Hole											
K.O.P. at 1435m (inside of Asmari Formation)											
1447	3.8	93.2	1446.87	-1432.42	10.49	12.4	11.9	1.438	3441022.49	192593.4	
1452.2	4	91.8	1452.06	-1437.61	10.48	12.75	12.26	1.278	3441022.48	192593.75	
1461.74	4.4	93.8	1461.57	-1447.12	10.44	13.45	12.96	1.339	3441022.44	192594.45	
1471.28	5.1	93	1471.08	-1456.63	10.4	14.24	13.75	2.211	3441022.4	192595.24	
1480.83	5.6	93.6	1480.59	-1466.14	10.34	15.13	14.64	1.58	3441022.34	192596.13	
1490.3	6.3	96.1	1490.01	-1475.56	10.26	16.1	15.62	2.364	3441022.26	192597.1	
1499.8	7.1	97	1499.44	-1484.99	10.13	17.2	16.72	2.548	3441022.13	192598.2	
1509.35	8	97.8	1508.91	-1494.46	9.97	18.45	17.97	2.846	3441021.97	192599.45	
1518.93	8.7	98.6	1518.39	-1503.94	9.77	19.83	19.36	2.222	3441021.77	192600.83	
1528.46	9.1	98.6	1527.8	-1513.35	9.55	21.28	20.82	1.259	3441021.55	192602.28	
1538	9.1	97.3	1537.22	-1522.77	9.34	22.78	22.33	0.647	3441021.34	192603.78	
1547.5	8.5	97.3	1546.61	-1532.16	9.16	24.22	23.77	1.895	3441021.16	192605.22	
1557.08	7.7	96.6	1556.1	-1541.65	8.99	25.56	25.12	2.524	3441020.99	192606.56	
1566.88	7.4	96	1565.81	-1551.36	8.85	26.84	26.41	0.95	3441020.85	192607.84	
1576.3	7.6	98.5	1575.15	-1560.7	8.7	28.06	27.63	1.219	3441020.7	192609.06	End of Directional Drilling (Motor & MWD pulled out)
1586.86	7.24	98.5	1585.62	-1571.17	8.5	29.41	28.99	1.028	3441020.5	192610.41	Pabdeh or Pd./Ja.
1623	6	98.5	1621.52	-1607.07	7.88	33.53	33.13	1.028	3441019.88	192614.53	
1684.84	5.04	98.5	1683.07	-1668.62	7	39.41	39.05	0.464	3441019	192620.41	Jahrum
1830	2.8	98.5	1827.88	-1813.43	5.53	49.23	48.93	0.464	3441017.53	192630.23	
1997.78	2.8	98.5	1995.46	-1981.01	4.32	57.34	57.08	0	3441016.32	192638.34	Pabdeh
2100	2.8	98.5	2097.56	-2083.11	3.58	62.28	62.05	0	3441015.58	192643.28	
2182.11	2.59	98.59	2179.58	-2165.13	3.01	66.09	65.89	0.077	3441015.01	192647.09	U. Gurpi
2344.72	2.17	98.82	2342.05	-2327.6	1.99	72.77	72.6	0.077	3441013.99	192653.77	Tarbur
2421.23	1.97	98.96	2418.51	-2404.06	1.56	75.5	75.35	0.077	3441013.56	192656.5	L. Gurpi
2563.64	1.61	99.31	2560.85	-2546.4	0.86	79.9	79.78	0.077	3441012.86	192660.9	Ilam
2631.64	1.43	99.55	2628.83	-2614.38	0.56	81.68	81.57	0.077	3441012.56	192662.68	Laffan
2637.73	1.42	99.57	2634.91	-2620.46	0.54	81.83	81.72	0.077	3441012.54	192662.83	Sarvak (Sar.-1)
2659.42	1.36	99.66	2656.6	-2642.15	0.45	82.35	82.24	0.077	3441012.45	192663.35	Sar.-2
2667.75	1.34	99.69	2664.92	-2650.47	0.41	82.54	82.44	0.077	3441012.41	192663.54	Sar.-3
2693.33	1.28	99.81	2690.5	-2676.05	0.32	83.12	83.02	0.077	3441012.32	192664.12	Sar.-4-6
2777.76	1.06	100.3	2774.91	-2760.46	0.02	84.81	84.72	0.077	3441012.02	192665.81	Sar.-7
2793.34	1.02	100.42	2790.49	-2776.04	-0.03	85.09	85	0.077	3441011.97	192666.09	Sar.-8
2853.21	0.87	100.95	2850.35	-2835.9	-0.22	86.06	85.98	0.077	3441011.78	192667.06	Sar.-9

MD (m)	Inc (°)	Azi (°)	TVD (m)	TVDss (m)	ΔN (m)	ΔE (m)	Vertical Section (m)	DLS (°/30m)	N (m)	E (m)	Remarks
2901.36	0.74	101.55	2898.49	-2884.04	-0.35	86.72	86.65	0.077	3441011.65	192667.72	Sar.-10
2925.99	0.68	101.93	2923.12	-2908.67	-0.41	87.02	86.95	0.077	3441011.59	192668.02	Sar.-11
2945.04	0.63	102.28	2942.17	-2927.72	-0.46	87.23	87.16	0.077	3441011.54	192668.23	Sar.-12
2996	0.5	103.56	2993.13	-2978.68	-0.57	87.72	87.66	0.077	3441011.43	192668.72	
3033.95	0.52	103.56	3031.08	-3016.63	-0.65	88.05	87.99	0.015	3441011.35	192669.05	Sar.-Intra
3276.37	0.64	103.56	3273.49	-3259.04	-1.22	90.43	90.39	0.015	3441010.78	192671.43	Kazhdumi
3412.5	0.71	103.56	3409.61	-3395.16	-1.6	91.99	91.96	0.015	3441010.4	192672.99	Kaz.-1-Shale
3423.3	0.71	103.56	3420.41	-3405.96	-1.63	92.12	92.1	0.015	3441010.37	192673.12	Kaz.-2-Sand
3449.76	0.73	103.56	3446.86	-3432.41	-1.71	92.44	92.42	0.015	3441010.29	192673.44	Kaz.-3-Shale
3455.46	0.73	103.56	3452.56	-3438.11	-1.72	92.51	92.49	0.015	3441010.28	192673.51	Kaz.-4-Sand
3461.02	0.73	103.56	3458.12	-3443.67	-1.74	92.58	92.56	0.015	3441010.26	192673.58	Kaz.-5-Shale
3471.45	0.74	103.56	3468.55	-3454.1	-1.77	92.71	92.69	0.015	3441010.23	192673.71	Dariyan
3600	0.8	103.56	3597.09	-3582.64	-2.17	94.38	94.39	0.015	3441009.83	192675.38	
3628.56	0.7	103.56	3625.65	-3611.2	-2.26	94.75	94.75	0.105	3441009.74	192675.75	Gadvan (Gad.-1)
3638.99	0.66	103.56	3636.08	-3621.63	-2.29	94.87	94.87	0.105	3441009.71	192675.87	Gad.-2u
3693.39	0.47	103.56	3690.47	-3676.02	-2.42	95.39	95.4	0.105	3441009.58	192676.39	Khalij
3702.78	0.44	103.56	3699.86	-3685.41	-2.44	95.47	95.48	0.105	3441009.56	192676.47	Gad.-2l
3706.49	0.43	103.56	3703.57	-3689.12	-2.44	95.49	95.5	0.105	3441009.56	192676.49	Gad.-3
3715.35	0.4	103.56	3712.43	-3697.98	-2.46	95.55	95.57	0.105	3441009.54	192676.55	Gad.-4
3730.3	0.34	103.56	3727.38	-3712.93	-2.48	95.65	95.66	0.105	3441009.52	192676.65	Gad.-5a
3740.75	0.31	103.56	3737.83	-3723.38	-2.49	95.71	95.72	0.105	3441009.51	192676.71	Gad.-5b
3743.13	0.3	103.56	3740.21	-3725.76	-2.5	95.72	95.73	0.105	3441009.5	192676.72	Gad.-5c
3753.96	0.26	103.56	3751.04	-3736.59	-2.51	95.77	95.78	0.105	3441009.49	192676.77	Gad.-6
3776.72	0.18	103.56	3773.8	-3759.35	-2.53	95.86	95.87	0.105	3441009.47	192676.86	Gad.-7
3798.15	0.11	103.56	3795.23	-3780.78	-2.54	95.91	95.92	0.105	3441009.46	192676.91	Gad.-8
3802.62	0.09	103.56	3799.7	-3785.25	-2.54	95.91	95.93	0.105	3441009.46	192676.91	
3830.05	0.34	331.44	3827.13	-3812.68	-2.48	95.9	95.91	0.444	3441009.52	192676.9	
3860.07	0.09	162.07	3857.15	-3842.7	-2.42	95.86	95.87	0.428	3441009.58	192676.86	
3890.09	0.19	174.82	3887.17	-3872.72	-2.49	95.87	95.89	0.104	3441009.51	192676.87	
3920.12	0.33	142.94	3917.2	-3902.75	-2.61	95.93	95.95	0.196	3441009.39	192676.93	
3928.34	0.32	145.06	3925.42	-3910.97	-2.65	95.96	95.98	0.068	3441009.35	192676.96	Fahliyan
3950.14	0.28	151.7	3947.22	-3932.77	-2.75	96.02	96.04	0.068	3441009.25	192677.02	
3969.4	0.31	147.76	3966.48	-3952.03	-2.83	96.07	96.1	0.051	3441009.17	192677.07	Fah.-1a
3980.01	0.32	145.86	3977.09	-3962.64	-2.88	96.1	96.13	0.051	3441009.12	192677.1	
3982.98	0.31	149.33	3980.06	-3965.61	-2.89	96.11	96.14	0.234	3441009.11	192677.11	Fah.-1b
3995.21	0.27	166.71	3992.29	-3977.84	-2.95	96.13	96.16	0.234	3441009.05	192677.13	Fah.-1c
4010.03	0.26	192	4007.11	-3992.66	-3.02	96.13	96.17	0.234	3441008.98	192677.13	
4028.81	0.17	201.39	4025.89	-4011.44	-3.08	96.11	96.15	0.155	3441008.92	192677.11	Fah.2a
4040.06	0.12	213.61	4037.14	-4022.69	-3.11	96.1	96.14	0.155	3441008.89	192677.1	
4045.36	0.16	199.55	4042.44	-4027.99	-3.12	96.09	96.14	0.281	3441008.88	192677.09	Fah.-2b
4057.05	0.25	184.85	4054.13	-4039.68	-3.16	96.09	96.13	0.281	3441008.84	192677.09	Fah.-3a
4061.82	0.3	181.71	4058.9	-4044.45	-3.18	96.08	96.13	0.281	3441008.82	192677.08	Fah.-3b
4070.08	0.37	177.98	4067.16	-4052.71	-3.23	96.09	96.13	0.281	3441008.77	192677.09	
4074.78	0.4	180.45	4071.86	-4057.41	-3.26	96.09	96.13	0.228	3441008.74	192677.09	Fah.-4a
4086.42	0.48	185.14	4083.5	-4069.05	-3.35	96.08	96.13	0.228	3441008.65	192677.08	Fah.-4b
4100.1	0.58	188.96	4097.18	-4082.73	-3.48	96.06	96.12	0.228	3441008.52	192677.06	
4111.56	0.52	189.14	4108.64	-4094.19	-3.59	96.05	96.11	0.16	3441008.41	192677.05	Fah.-5a
4130.12	0.42	189.54	4127.2	-4112.75	-3.74	96.02	96.09	0.16	3441008.26	192677.02	
4136.96	0.56	204.47	4134.04	-4119.59	-3.79	96.01	96.08	0.815	3441008.21	192677.01	Fah.-5b
4160.15	1.13	223.41	4157.22	-4142.77	-4.06	95.8	95.89	0.815	3441007.94	192676.8	
4180	1.26	218.02	4177.07	-4162.62	-4.37	95.53	95.63	0.26	3441007.63	192676.53	T.D.

2.8 Formation losses Report

AZNS-207, S.T-1 Formation Loss (Table-1)

Date	Depth From	Depth To	Loss (bbl)	Ave. Loss (bbl/hr)	Formation	Remark
2024.10.30	1450	1480.3	350	40-50		Pump LCM
2024.10.31	1480.3		61	0-2		Pump LCM
2024.11.01			24	0-1		Pump LCM
2024.11.02			24	1		Pump LCM
2024.11.03	1480.3	1548	694	1-60		Pump LCM
2024.11.04	1548	1562	361	5-40		Pump LCM
2024.11.05	1562		343	5-15		Pump LCM
2024.11.06			343	5-15		Pump LCM
2024.11.07	1562	1564.5	150	5-25		Pump LCM
2024.11.08	1564.5		150	2-6		
2024.11.09			82	2-10		
2024.11.10			85	2-6		
2024.11.11			144	2-4		
2024.11.12			135	2-4		
2024.11.13			138	4-8		
2024.11.14			220	4-8		
2024.11.15			120	3-6	Asmari	
2024.11.16			170	6-8		
2024.11.17			156	6-8		
2024.11.18			48	2		
2024.11.19			52	1-3		
2024.11.20			24	1		
2024.11.21			72	2-3		
2024.11.22			64	1-3		
2024.11.23			64	1-3		
2024.11.24			72	3		
2024.11.25	1435	1439.5	60	1-3		
2024.11.26	1439.5	1447	72	3		
2024.11.27	1447	1472	60	2-3		
2024.11.28	1472	1507	96	3-5		
2024.11.29	1507	1552	100	3-5		
2024.11.30	1552		43	1-2		
2024.12.01	1552	1571	43	1-2		
2024.12.02	1571	1592.9	48	2		
2024.12.03	1592.9	1594	27	1-2		
2024.12.04	1594	1616	38	2-3		
2024.12.05	1616	1617.5	36	2-3		
2024.12.06	1617.5	1636	30	1-2	Pd./Jr.	
2024.12.07	1636	1648.5	36	1-2		
2024.12.08	1648.5		36	1-2		
2024.12.09			32	1-2		
2024.12.10			36	1-2		
2024.12.16	1713	1828	360	10-20		
2024.12.17	1828	1861	108	1-6	Jahrum	
2024.12.18	1861	1994	75	1-4		
2024.12.19	1994	2000	160	1-20		
2024.12.20	2000		100	25-0		Pump LCM
2024.12.22	2000	2114	48	2-3	Pabdeh	
2024.12.23	2114	2150	38	1-2		
2024.12.24	2150		24	1		

AZNS-207, S.T-1 Formation Loss (Table-2)

Date	Depth		Loss	Ave. Loss	Formation	Remark
	From	To	(bbl)	(bbl/hr)		
2024.12.25	2150	2189	24	1	Pabdeh/Gurpi	
2024.12.26	2189	2339	40	1-2	Gurpi	
2024.12.27	2339	2509	72	3-4	Gurpi	
2024.12.28	2509	2686	96	4-6	Gurpi/Ilam/lafan/sarvak	
2024.12.29	2686	2696.5	55	2-4	Sarvak	
2024.12.30	2696.5	2737	55	2-4	Sarvak	
2024.12.31	2737	2810	45	2-4	Sarvak	
2025.01.01	2810		48	2-4	Sarvak	
2025.01.02			36	1-2	Sarvak	
2025.01.03	2810	2868	24	1	Sarvak	
2025.01.05	2870	2941	65	2-4	Sarvak	
2025.01.06	2941	3006.7	55	2-4	Sarvak	
2025.01.07	3006.7		55	2-4	Sarvak	
2025.01.08			24	1-2	Sarvak	
2025.01.09	3006.7	3017.5	45	0-2	Sarvak	
2025.01.10	3017.5	3023.5	45	0-2	Sarvak	
2025.01.11	3023.5	3027	28	0-2	Sarvak	
2025.01.12	3027	3054	40	2-3	Sarvak	
2025.01.13	3054	3140	54	2-4	Sarvak	
2025.01.14	3140	3236	90	2-5	Sarvak	
2025.01.15	3236	3240	96	4-6	Sarvak	
2025.01.16	3240		192	8	Sarvak	
2025.01.17	3240	3274	80	3-6	Sarvak/Kazhdumi	
2025.01.18	3274	3275	48	2-3	Kazhdumi	
2025.01.19	3275	3284	60	3	Kazhdumi	
2025.01.20	3284	3284.5	78	3-5	Kazhdumi	
2025.01.21	3284.5	3284.9	78	3-5	Kazhdumi	
2025.01.22	3284.9	3315	96	4-6	Kazhdumi	
2025.01.23	3315	3427	96	3-5	Kazhdumi	
2025.01.24	3427	3535	96	3-5	Kazhdumi/Dariyan	
2025.01.25	3535	3620	72	3-5	Dariyan	
2025.01.26	3620	3671	96	3-5	Dariyan/Gadvan	
2025.01.27	3671	3741	72	3-5	Gadvan	
2025.01.28	3741	3790	72	3-5	Gadvan	
2025.01.29	3790	3821	72	3-5	Gadvan	
2025.01.30	3821	3846	168	3-5	Gadvan	
2025.01.31	3846	3872	168	5-7	Gadvan	
2025.02.01	3872	3872	190	5-8	Gadvan	
2025.02.02	3872	3891	472	15-20	Gadvan	
2025.02.03	3891	3891	472	15-20	Gadvan	
2025.02.04	3891	3895	720	25-30	Gadvan	
2025.02.05	3895		960	35-40	Gadvan	
2025.02.06			1760	70-75	Gadvan	
2025.02.07			1896	75-80	Gadvan	
2025.02.08			798	30-35	Gadvan	
2025.02.09			334	10-15	Gadvan	
2025.02.10			72	2-3	Gadvan	
2025.02.11			72	2-3	Gadvan	
2025.02.15	3895	3964	24	1-2	Gadvan	
2025.02.16	3964	4076	24	1-2	Fahliyan	


AZNS-207, S.T-1 Formation Loss (Table-3)

Date	Depth		Loss	Ave. Loss	Formation	Remark
	From	To	(bbl)	(bbl/hr)		
2025.02.17	4180		36	1-2	Fahliyan	
2025.02.18			36	1-2	Fahliyan	
2025.02.19			36	1-2	Fahliyan	
2025.02.20			36	1-2	Fahliyan	
2025.02.21			12	0-1	Fahliyan	
2025.02.22			12	0-1	Fahliyan	
2025.02.23			12	0-1	Fahliyan	
	Total Loss		16462	bbl		

2.9 Hole Problem

Hole Size (in)	Depth (m)	Problem Description
17 – 1/2	1479	Formation loss, Cure
	1480	Left fish in hole due to twist off string, Retrieved.
	1515	Left fish in hole due to twist off, cause of side track.
	1616	String wash out, POOH
12 – 1/4	2000	Formation loss, CMT injection
	2810	Left fish in hole due to twist off string, Recovered
	3006	
	3027	Low ROP, Change bit
	3240	Left fish in hole due to twist off string, Recovered
	3275	Low ROP, Change bit
	3284	
	3500	Tight hole, Wash & Ream down
	3260	Tight hole during wiper trip
	3100	Formation loss, Spot pill

2.10 Well Montage

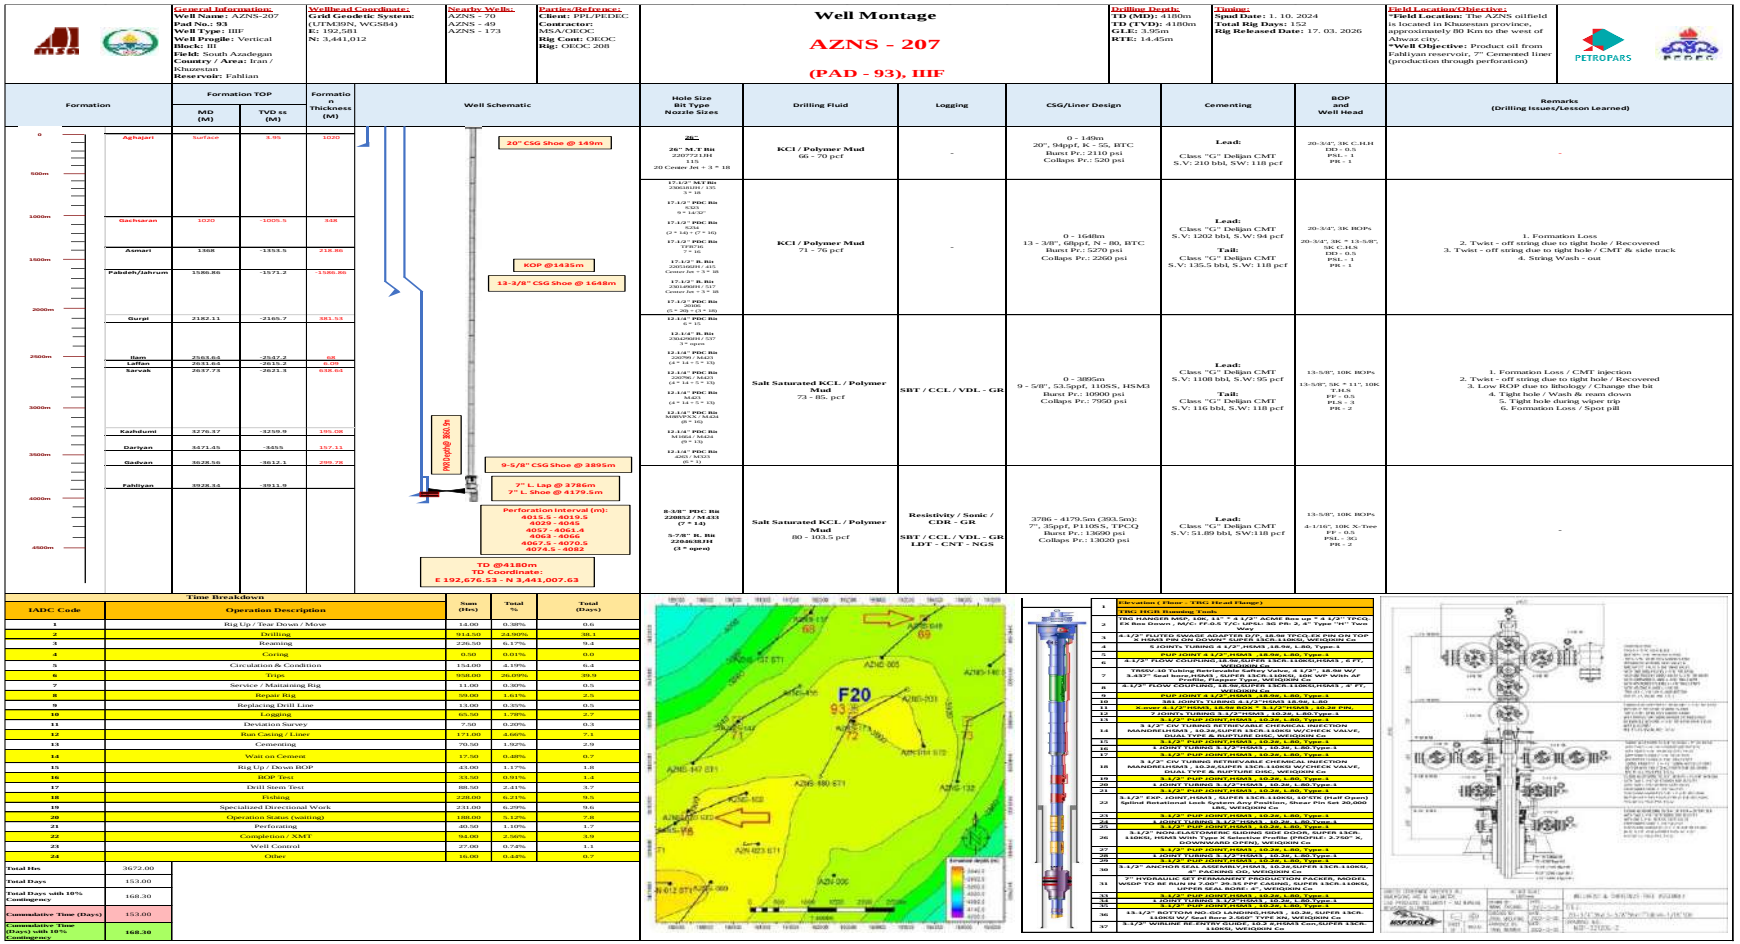

3. Time Analysis Report

3.1 Time vs. Depth Chart

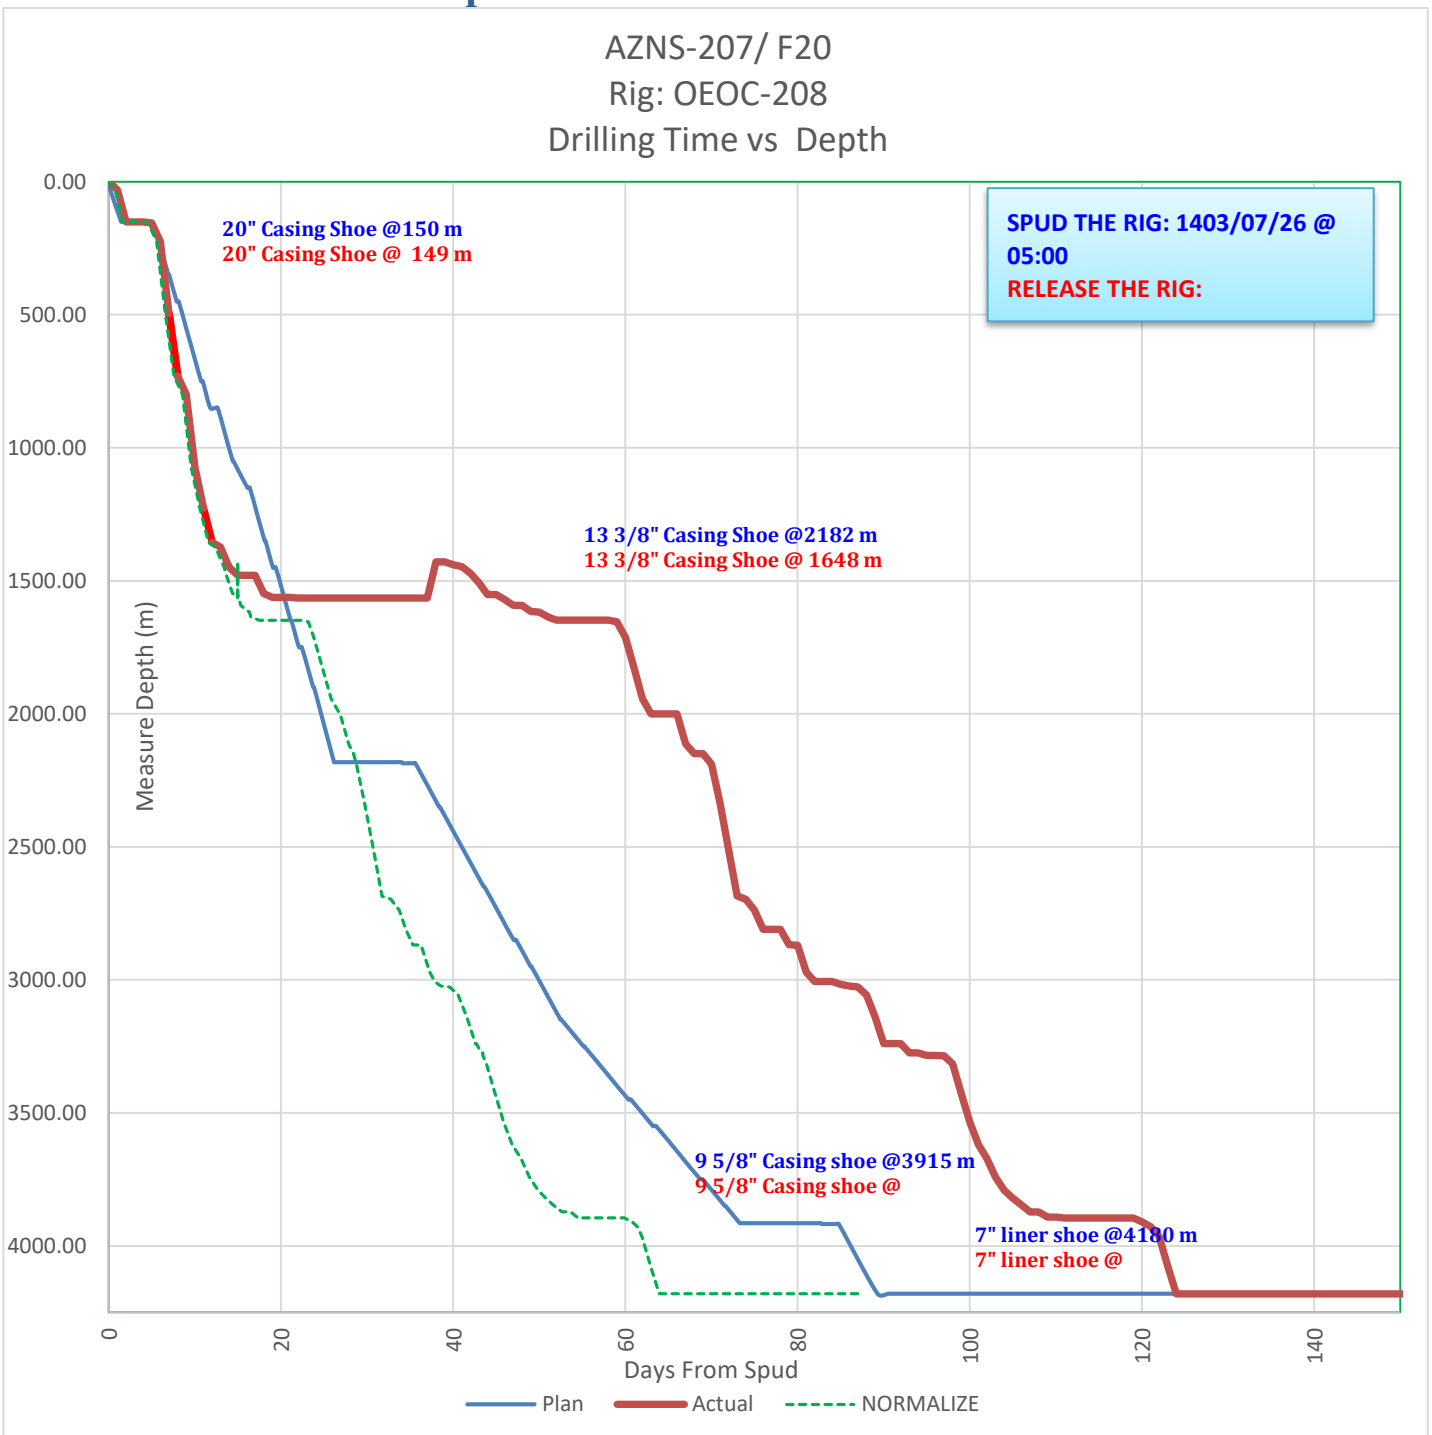


Figure 3-1: AZNS-207 Well Time vs. Depth Chart

3.2 Total Time Break-Down of Operation

Item No.	Drilling and Completion Operation TBD of Well: F-20	IADC Code	Interval (meters)	Formation	Depth (meters)	ROP Average (MPH)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (%) 10	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Actual Operation	Hour	Cum. Time Day	Depth (m)
	26" Hole Section / 20" Casing																
1	P/U & M/U 26" bit #1 (R.Bit) and 9-3/4" drill collars, RIH to tag formation @ ±14m.	Drilling	5	Agh.	14	0.0	0.0	0.00	0.0	0.0	0.0	0.00	0.0			0.00	0
2	Drilling 26" hole from 14 to 150m (20" casing point in Aghajari formation) using Hi-vis bentonite pill (Run Totco each 50m).	Drilling	136	Agh.	150	5.0	31.0	1.29	1.3	1.4	34.1	1.42	1.4	RACK BACK 68STD 5" DP, PERFORM MAGNET TRIP, SPUD THE RIG @1403.07.26 @05:00 O'CLOCK, M/U 26"R.BIT(K.D, 115, 3*18/32" NOZZLE + 20/32" C.JET) & RIH TO 14M, TAG FM, START DRLG 26"H.S TO 31M, NL-NG TILL M.N	19	1.00	31
3	Circulate and clean the hole. Spot high viscosity pill at bottom, drop Inclinometer (Totco).	Trip		Agh.	150		3.0	0.13	1.4	0.1	3.3	0.14	1.6	CONT DRLG 26" H.S TO 151M(20"CSG POINT), C.B.U, AS COND TRIP POOH TO SURF & RUN BACK TO 151M(BTM), C.B.U, POOH TO SURF, WHILE RUN TOTCO @50M "ZERO" & @100M W/ DEV: 0.25 DEG & DROP TOTCO @151M W/ DEV: 0.25 DEG. R/U CSG RUNNING EQUIP IN PROGRESS, NL-NG @R.T.	24	2.00	151
4	Perform hole condition prior to run casing. If observe any indication of drag, run back to bottom, POOH to surface.	Trip		Agh.	150		5.0	0.21	1.6	0.2	5.5	0.23	1.8	POOH F/ 151M TO SURF, R/U CSG RUNNING EQUIP (OEOC CO) & RUN 13 JT 20"CSG (94#, K-55, BTC) TO 149M(20"CSG SHOE), RIH 5" STINGER & 5"DPs INSIDE 20"CSG TO 149M, STING IN 20" F.SHOE, PERFORM CMT JOB AS PUMP 50 BBL F.WTR AS SPACER, PUMP 210 BBL CMT SLURRY (S.W:118 PCF) & GOT 20 BBL CONTAMINATED & 10 BBL SLURRY NET ON SURF, DISPLACE CMT SLURRY W/ 6 BBL F.WTR (2 BBL SHORT), CHECK BACKFLOW "OK". W.O.C TO GET HARD, ROUGH CUT CONDUCTOR PIPE & 20"CSG LJOINT WHILE SLACK OFF CSG "NO-MOVEMENT", INSTALL BASE PLATE IN PROGRESS @R.T	24	3.00	151
5	R/U casing running equipment & run 150 m approximately 13 Jts. 20" casing to 150 m.Fill casing by non-LON fresh mud.	Csg. Running		Agh.	150		13.0	0.54	2.2	0.6	14.3	0.60	2.4	SLACK OFF CSG "NO-MOVEMENT", DRESS & BEVEL 20" CSG NECK, INSTALL 20 3/4"-3K C.H.H & PRESS TEST P-SEALs W/ 400 PSI "OK", N/U 20 3/4"-3K BOP STACK (DOUBLE RAMS (BLIND/TOP [5"FIX]) & ANN PREVENTER) IN PROGRESS @R.T	24	4.00	151
6	Circ mud, RIH W/ Stringer on 5" DP, Circulate mud,Cement Casing as per program.POOH to Surf., L/D stinger, Wait on cement to get hard meanwhile perform top job(s) to fill annulus	CMT		Agh.	150		13.0	0.54	2.7	0.6	14.3	0.60	3.0	CONT N/U 20 3/4"-3K BOP STACK & PERFORM PRESS BOP TEST AS NIOC POLICY "OK", RIH 17 1/2" M.TOOTH BIT(K.D, 135, 3*18/32"NOZZLE) & DRLG BHA TO 148M, TAG CMT, D/O CMT & 20" CSG SHOE & RAT HOLE TO 151M, START DRLG 17 1/2" H.S F/ 151 TO 165M, NL-NG @R.T	24	5.00	155
7	Cut 30" conductor pipe, Cut & bevel 20" casing. Weld and Installed 20-3/4" x 3K C.H.H & pressure test same with 80% Casing Collapse.	wellHead		Agh.	150		9.0	0.38	3.1	0.4	9.9	0.41	3.4	CONT DRLG 17 1/2" H.S TO 165M, DUE TO OBS GRADUALLY DECREASE 100PSI PRESS, DECIDED TO POOH TO SURF, OBS WASH 2NO OF NOZZLE PORT, RIH 17 1/2" M.T BIT(HZ8R1 (K.D, 135, 1*18/32" NOZZLE + 2"OPEN) & DRLG BHA TO 165M, RES DRLG 17 1/2" H.S TO 225M, NL-NG TILL M.N	24	6.00	225
8	W/U BOP and releated lines and valves, test BOP & choke manifold as per NIOC policy.	N/U BOP & BOP Test		Agh.	150		26.0	1.08	4.2	1.2	28.6	1.19	4.6	CONT DRLG 17 1/2" H.S F/ 225 TO 450 M, C.B.U, PERFORM WIPER TRIP POOH TO 150M & RUN BACK TO BTM WHILE B/R F/ 450 TO 360M, RUN TOTCO @450M W/ INC: 0.75 DEG, CONT DRLG 17 1/2" H.S TO 495M, NL-NG TILL M.N	24	7.00	495
9	Drill out cement and shoe with 17-1/2" bit (R.Bit), work on junk sub.	D/Out		Agh.	150		4.0	0.17	4.3	0.2	4.4	0.18	4.8	CONT DRLG 17 1/2" H.S 495 TO 730M, WHILE DIS MUD IN HOLE W/ NaCl MUD (72 PCF) @ 565M, NL-NG TILL M.N	24	8.00	730
	Total Duration of 26" Hole Section:							*4.3*	*4.3*		*4.8*	*4.8*					

South Azadegan Oilfield Project

PETROPARS P.E.D.E.C.

Contract No: CCA/C/1403/31

End of Well Report AZNS – 207

Project	P/T	Zone	Dep.	Disc.	Type	Sequence	Rev.
SAC	P	IIF207	DR	De	PRG	0043	03

Item No.	Drilling and Completion Operation TBD of Well: F-20	IADC Code	Interval (meters)	Formation	Depth (meters)	ROP Average (MPH)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (%) 10	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Actual Operation	Hour	Cum. Time Day	Depth (m)
	17-1/2" Hole Section / 13-3/8" Casing																
10	Commence drilling 17-1/2" hole to 174m (bit#2).	Drilling	24	Agh.	174	5.0	5.0	0.21	4.5	0.2	5.5	0.23	5.0	CONT DRLG 17 1/2" H.S F/ 730 TO 793M, CBU, POOH TO 750 M, DROP TOTCO, CONT POOH TO SURF, OBS BALLED UP 17-1/2" S.STAB & BIT, RET. TOTCO SURVEY: 0.75 DEG @ 750M. RIH W/ 17 1/2" NEW PDC BIT (9 * 14/32" NOZ.) TO 793 M (BTM), RESUME DRLG 17 1/2" H.S F/ 793 TO 860 M MEAN WHILE INCREASE MUD WEIGHT F / 73 TO 74 PCF, NL-NG @ RT	24	9.00	800
11	Circulate and clean hole, POOH to surf.	Trip		Agh.	174		4.0	0.17	4.7	0.2	4.4	0.18	5.2	CONT DRLG 17 1/2" H.S F/ 800 TO 1107M, CBU, POOH ON ELEVATOR AS WIPER TRIP TO 970M W/ GOOD HOLE COND., NL-NG @ RT	24	10.00	1073
12	RIH w/ same bit (B, bit #2881) and S.Stab @ 20m to bottom.Survey shall be taken by running single shot (Each 100 m) & multishot (Each 300 m) in this hole section.	Trip		Agh.	174		4.0	0.17	4.9	0.2	4.4	0.18	5.4	CONT DRLG 17 1/2" H.S F/ 1073 TO 1107M, CBU, POOH AS WIPER TRIP TO 800M W/ GOOD HOLE COND. (F/ 1020 TO 900 M W/ SOFT B/R), RUN BACK TO 1107M MEANWHILE RUN TOTCO SURVEY @ 1050M. (INC.: 0.8 DEG), RESUME DRLG 17 1/2" H.S F/ 1107 TO 1252M, NL-NG @ RT	24	11.00	1227
13	Continue drilling 17-1/2" hole to +250m while pumping hi-vis pill periodically	Drilling	76	Agh.	250	6.0	15.0	0.63	5.5	0.7	16.5	0.69	6.1	CONT DRLG 17 1/2" H.S F/ 1227 TO 1370M, NL-NG @ RT	24	12.00	1356
14	Continue drilling 17-1/2" hole to +350m while pumping hi-vis pill periodically	Drilling	100	Agh.	350	6.0	19.0	0.79	6.3	0.9	20.9	0.87	6.9	CONT DRLG 17 1/2" H.S F/ 1356 TO 1373.8M, DUE TO LOW ROP, DECIDED POOH TO SURF, POOH STRING F/ 1373.8M TO SURF WHILE DROP TOTCO @ 1350 M, RET TOTCO 0.5 DEG, RIH W/ 17-1/2" PDC BIT (NEW, HALIBURTON, 6 BLADE, 13MM, (2 X 14/32" + 7 X 16/32" NOZZLE)) & PREVIOUS BHA TO 730 M, NL-NG @ RT	24	13.00	1373.8
15	Take survey	Survey		Agh.	350		2.0	0.08	6.4	0.1	2.2	0.09	7.0	CONT RIH W/ 17-1/2" NEW PDC BIT & PREVIOUS BHA F/ 50 TO 1373.8 M (BTM), PUMP 60 BBL HI-VIS PILL & CIRC. OUT SAME, RESUME DRLG 17-1/2" H.S F/ 1373.8 TO 1479M, DUE TO OBS SEVERE FM LOSSES; 40-50 BPH, POOH 1 STD (1450M), PUMP & SPOT 50 BBL LCM PILL (15 PPB MICA M & KWIK SEAL M), POOH TO 1395M. ESTABLISH CIRC. HI-FR & MONITOR THE WELL; 10-15 BPH LOSSES, WASH & R/D TO 1479M (BTM); 3-5 BPH LOSSES, PUMP 20 BBL LCM PILL (15 PPB MICA M & KWIK SEAL M) & RESUME DRLG 17-1/2" H.S F/ 1479 TO 1480 M, 2-5 BPH LOSSES @ RT	24	14.00	1450
16	Continue drilling 17-1/2" hole to +450m while pumping hi-vis pill periodically	Drilling	100	Agh.	450	6.0	19.0	0.79	7.2	0.9	20.9	0.87	7.9	CONT DRLG 17-1/2" H.S F/ 1450 TO 1479M, DUE TO OBS SEVERE FM LOSSES; 40-50 BPH, POOH 1 STD (1450M), PUMP & SPOT 50 BBL LCM PILL (15 PPB MICA M & KWIK SEAL M). POOH TO 1395M. ESTABLISH CIRC, 10-15BPH LOSSES, WASH & R/D TO 1479M (BTM), PUMP 20 BBL LCM PILL (15 PPB MICA M & KWIK SEAL M) & RESUME DRLG 17-1/2" H.S F/ 1479 TO 1480 M, SUDDENLY OBS DROP IN PRESS (300PSI @ SPP & 215PSI @ M/L), CHECK SURF PRESS EQUIP, NO PROBLEM, CHECK STRING WEIGHT, OBS APPROX 8-10KIP'S STRING WEIGHT LOST, POOH STRING F/ 1480M TO SURF, OBS	24	15.00	1480
17	Condition trip to 150m Run back, Take survey as multi-shot	Trip		Agh.	450		5.0	0.21	7.4	0.2	5.5	0.23	8.1	CONT WORK ON CATCH THE FISH SEVERAL TIMES, NO SUCC, POOH W/ 12-3/4" * 15-1/2" FISHING ASSEMBLY F/ 1460M TO SURF, M/U NEW 11 3/4" O.SHOT FISHING TOOLS ASSY W/ 11 3/4" * 15 1/2" WALL HOOK O.SIZE GUIDE, RIH W/ FISHING BHA TO 1469.78 (TOF), TRY TO ENGAGE THE FISH, CHECK STRING WT TO CONFIRM ENGAGED FISH (APPROX 168 KIPS), OK., POOH WITH FISH TO 365M WHILE GOT OVER PULL @ SEVERAL POINTS, 1BPH LOSS @ RT	24	16.00	1480
18	Continue drilling 17-1/2" hole to +550m while pumping hi-vis pill periodically	Drilling	100	Agh.	550	6.0	19.0	0.79	8.2	0.9	20.9	0.87	9.0	CONT POOH WITH FISH F/ 1220M TO SURF, RECOVER THE FISH: 9-1/2" DC, 9 1/2" BIT SUB & 17-1/2" PDC BIT, DUE TO DECIDED L/D ALL DCs: RIH W/ 17-1/2 USED PDC BIT + 9 1/2" B.SUB + 15TD 9-1/2DC + 25TD 8-1/2" DC TO 100M, POOH TO SURF. L/D ALL DCs, BIT SUB & XOS. M/U 17-1/2" PDC BIT (RECOVERED, HALIBURTON), RIH W/ BHA NO.#8 (INSPECTED DCs IT BY JT) TO 1479M, PUMP 30BBL HI-VIS PILL, CBU IS IN PROGRESS, 1 BPH LOSS @ RT	24	17.00	1480
19	Continue drilling 17-1/2" hole to +650m while pumping hi-vis pill periodically	Survey	100	Agh.	650	6.0	19.0	0.79	9.0	0.9	20.9	0.87	9.9	CONT RIH 17-1/2" PDC BIT (RECOVERED, HALIBURTON) F/ 110 TO 1479M, PUMP 30BBL HI-VIS PILL, CBU, RESUME DRLG 17-1/2" H.S F/ 1480 TO 1554M MEANWHILE PUMP LCM PILL 20PPB (10LB MICA M+10 LB KWIK SEAL M) PERODICALLY & SPOT LCM PILL 25 PPB (MICA M + KWIK SEAL M) @ 2 STAGES, 20-40BPH LOSSES @ RT	24	18.00	1548
20	Continue drilling 17-1/2" hole to +750m while pumping hi-vis pill periodically	Drilling	100	Agh.	750	6.0	19.0	0.79	9.8	0.9	20.9	0.87	10.7	CONT DRLG 17-1/2" H.S F/ 1548 TO 1562M MEANWHILE PUMP LCM PILL 20PPB (10LB MICA M+10 LB KWIK SEAL M) PERODICALLY, DUE TO LOW ROP, DECIDED TO POOH, SPOT 100BBL LCM HI-VIS PILL 25PPB, POOH W/ 17 1/2" PDC BIT F/ 1562 (BTM) TO 30M, 5-10BPH LOSSES @ RT	24	19.00	1562
21	Condition trip to 450m and Run back , displace mud in hole by 74pcf KCL/Polymer mud @ +750m,	Survey		Agh.	750		4.0	0.17	9.9	0.2	4.4	0.18	10.9	CONT POOH W/ 17 1/2" PDC BIT F/ 570M TO SURF, OBS HEEL ROW, GAUGE ROW & A PART OF NOSE ROW OF 17 1/2" PDC BIT SEVERE EROSION, RIH 17-1/2" M.TOOTH BIT + 12-7/8" ,SUB TO 916M (SOME INTERVALS W/ HARD W/R & VERY LOW PROGRESS), 5-15BPH LOSSES @ RT	24	20.00	1562
22	Continue drilling 17-1/2" hole to 850m (bit hrs), while pump hi-vis Pill periodically.	Drilling	100	Agh.	850	6.0	19.0	0.79	10.7	0.9	20.9	0.87	11.8	CONT RIH 17-1/2" M.TOOTH BIT + 12-7/8" ,I SUB F/ 734 TO 1562M (BTM) (SOME INTERVALS W/ HARD W/R, R/D & WASH DOWN, LOW PROGRESS), WORK ON JUNK SUB SEVERAL TIMES (1HOUR), RESUME DRLG 17-1/2" H.S F/ 1562 TO 1564.5M, SPUD 100BBL LCM PILL 40PPB, POOH ON ELEVATOR F/ 1564.5 TO 1460M, AV. 10BPH LOSSES @ RT	24	21.00	1562
23	Circulate clean hole, Take survey as multi-shot	Trip		Agh.	850		13.0	0.54	11.3	0.6	14.3	0.60	12.4	RESUME DRLG 17-1/2" H.S F/ 1562 TO 1564.5M, SPOT 100BBL LCM PILL 40PPB, POOH ON ELEVATOR TO 1450M, PUMP & MIX FRESH & TREAT MUD (50%-50%) TO THE WELL, CIRC 2 CYCLE (DRLG MUD IN RANGE, FL-6, OK), SPOT 50 BBL LCM PILL 40PPB, CONT POOH F/ 1450M TO SURF (SOME INTERVALS W/ PUMP OUT & B/R), 5-8BPH LOSS	24	22.00	1564.5
24	POOH to surface, change bit to PDC (bit #3), RIH to bottom while pick up drill pipe.	BOP Test		Agh.	850		6.0	0.25	11.5	0.3	6.6	0.28	12.7	CONT POOH F/ 300M TO SURF, RIH 17-1/2" PDC BIT & DRLG BHA TO 1300M, WHILE W&R SEVERAL POINTS, 2-6 BPH LOSS @R.T	24	23.00	1564.5
25	Continue drilling 17-1/2" hole to 950m while pump hi-vis Pill periodically.	Drilling	100	Agh.	950	6	19.0	0.79	12.3	0.9	20.9	0.87	13.5	CONT RIH 17 1/2" PDC BIT & DRLG BHA W/ HARD W&R F/ 1200 TO 1515.5M, SUDDENLY OBS DROP IN PRESS (300PSI) & APPROX 10-12 KLBS STRING WIGHT LOST, POOH TO CHECK STRG TO 600M, 4-8 BPH LOSS TILL M.N	24	24.00	1564.5
26	Continue drilling 17-1/2" hole to 1050m while pump hi-vis pill periodically.	Drilling	100	Agh.-Gas.	1050	6.0	19.0	0.79	13.1	0.9	20.9	0.87	14.4	CONT POOH 600M TO SURF, TWIST OFF STRING (LEFT IN HOLE: 17 1/2" PDC BIT + BIT SUB + APPROX 2 JT 9 1/2" DC: 19.84 M)(TOP OF FISH: 1495.66 M ESTIMATED TOF), M/U 11 3/4" O.SHOT FISHING TOOLS ASSY. W/ 11 3/4" * 15 1/2" WALL HOOK O.SIZE GUIDE & FISHING BHA TO 1531M (TOF), WORK ON FISHING WITH DIFFERENT PARAMETERS IN PROGRESS, 1-2 BPH LOSS TILL M.N	24	25.00	1564.5
27	Take survey	Survey		Agh.-Gas.	1050		2.0	0.08	13.2	0.1	2.2	0.09	14.5	CONT WORK ON FISHING W/ 11 3/4" O.SHOT FISHING TOOLS ASSY. & 11 3/4" * 15 1/2" WALL HOOK O.SIZE GUIDE F/ 1531 TO 1539M W/ DIFFERENT PARAMETERS "NO SUCC" MEANWHILE INC MW TO 79 PCF, POOH TO 1400M, 2-4 BPH LOSS TILL M.N	24	26.00	1564.5
28	Continue drilling 17-1/2" hole to 1150m while pump hi-vis pill periodically.	Drilling	100	Gas.	1150	3.3	35.0	1.46	14.6	1.6	38.5	1.60	16.1	CONT POOH 11 3/4" O.SHOT F/ 1400M TO SURF, RIH 17-1/2" INSERT BIT (K.D, 415, 3*18/32" NOZZLE+18/32"C.JET) TO 650 M, HARD W&R F/ 650 TO 930 M, MEAN WHILE INC MW TO 81 PCF, 4-8 BPH LOSS TILL M.N	24	27.00	1564.5
29	Perform Wiper Trip as POOH to 850 m & Run back to BTM. Take survey as multi-shot	Trip		Gas.	1150		6.0	0.25	14.9	0.3	6.6	0.28	16.4	CONT RIH 17 1/2" INSERT BIT F/ 930 TO 1380 M W/ HARD W&R, MEANWHILE INC MW TO 83 PCF, 3-8 BPH LOSS TILL M.N.	24	28.00	1564.5
30	Continue drilling 17-1/2" hole to 1250m while pump hi-vis pill periodically.	Drilling	100	Gas.	1250	6.0	19.0	0.79	15.7	0.9	20.9	0.87	17.2	CONT RIH 17 1/2" INSERT BIT W/ HARD W&R F/ 1380 TO 1542.4 M, TOOK WEIGHT & TAG FISH, CIRC MUD TO CLEAN THE HOLE MEANWHILE WORK ON MUD RHEOLOGY, 4-8 BPH LOSS TILL M.N	24	29.00	1564.5
31	Continue drilling 17-1/2" hole to 1350m while pump hi-vis pill periodically.	Drilling	100	Gas.	1350	6.0	19.0	0.79	16.5	0.9	20.9	0.87	18.1	POOH 17 1/2" INSERT BIT F/ 1542.40M TO SURF WHILE POOH W/ HARD & REAM @SEVERAL POINTS, L/D 17 1/2" INSERT BIT, 3-6 BPH LOSS TILL M.N	24	30.00	1564.4
32	Take survey	Survey		Gas.	1350		2.0	0.08	16.5	0.1	2.2	0.09	18.2	RIH 11 3/4" OVERSHOT (DRESS W/ 9 1/2" S.GRAPPLE, 9 1/2" CONTROL & W/ 15 1/2" O.SIZE GUIDE) W/ FISHING BHA TO 1539M, PUMP & CIRC OUT 50 BBL HI-VIS PILL MEAN WHILE HARD WASH & REAM F/ 1539 TO 1540.5M, 6-8 BPH LOSS TILL M.N	24	31.00	1564.5
33	Continue drilling 17-1/2" hole to 1450m while pump hi-vis pill periodically.	Drilling	100	Gas.-Ar.	1450	6.0	19.0	0.79	17.3	0.9	20.9	0.87	19.1	CONT HARD WASH & REAM W/ 11 3/4" OVERSHOT F/ 1540.5 TO 1541.4M(1M ABOVE TOF) DURING 16HRS, DUE TO NO ANY PROGRESS, POOH TO SURF, L/D 11 3/4" OVERSHOT, NO INDICATION OF ENGAGE W/ FISH. P/U & M/U 17 1/2" TAPER MILL(8*1 1/4" SIDE PORT+1*3 1/8" C.PORT) & RIH 1 IT 5" HWDP TO 10M, 4-6 BPH LOSS TILL M.N	24	32.00	1564.5
34	Perform Wiper Trip as POOH to 1150 m & Run back to BTM. Take survey as multi-shot	Trip		Ar.	1450		7.0	0.29	17.6	0.3	7.7	0.32	19.4	RIH 17 1/2" TAPER MILL(8*1 1/4" SIDE PORT + 1*3 1/8" C.PORT) TO 700 M WHILE RIH W/ W&R F/ 270 TO 700M, DUE TO CHANGE PROGRAM POOH F/ 700M TO 70M, 1-3 BPH LOSS TILL M.N	24	33.00	1564.5
35	Continue drilling 17-1/2" hole to 1550m while pump hi-vis pill periodically.	Drilling	100	Ar.	1550	6	19.0	0.79	18.4	0.9	20.9	0.87	20.3	CONT POOH W/ 17 1/2" TAPER MILL F/ 70M TO SURF, RIH 7 7/8" C.CUT BIT TO 1535M(7.4M ABOVE TOF), PERFORM CMT BALANCE PLUG JOB: PUMP 27 BBL BRINE (75 PCF) AS SPECER AHEAD THEN MIX & PUMP 204 BBL CMT G DELIJAN (118 PCF) & 1.7 BBL BRINE (75 PCF) AS SPACER BEHND, DISPLACE SLURRY W/ 71 BBL MUD (8.5 PCF (2 BBL SHORT), POOH TO 1250M, FLUSH STRG, CONT POOH TO 960M, C.B.U, W.O.C,	24	34.00	1564.5
36	Continue drilling 17-1/2" hole to 1650m while pump hi-vis pill periodically.	Drilling	100	AS/Ps.-Ja.	1650	6.0	19.0	0.79	19.2	0.9	20.9	0.87	21.1	RIH W/ W/D TO 1486M, TAG CMT, APPLY10KLB WEIGHT & 560GPM "NO WASH", C.B.U, PERFORM CMT BALANCE PLUG JOB: PUMP 27 BBL BRINE (75 PCF) AS SPECER AHEAD THEN MIX & PUMP 204 BBL CMT G DELIJAN (118 PCF) & 1.7 BBL BRINE (75 PCF) AS SPACER BEHIND, DISPLACE SLURRY W/ 68 BBL MUD (85 PCF (2 BBL SHORT), POOH TO 1190M, FLUSH STRG, CONT POOH TO SURF, 1-3 BPH LOSS TILL M.N	24	35.00	1564.5
37	Take survey	Survey		Ps.-Ja.	1650		2.0	0.08	19.3	0.1	2.2	0.09	21.2	RIH 17 1/2" INSERT BIT & D/O BHA TO 1330M WHILE W&R F/ 780 TO 1330 M, 1-3 BPH LOSS @ R.T	24	36.00	1564.5
38	Continue drilling 17-1/2" hole to 1750m while pump hi-vis pill periodically.if observe Chert particle while formation sampling Follow Contingency Plan#01	Drilling	100	Ja.	1750	6.0	19.0	0.79	20.1	0.9	20.9	0.87	22.1	CONT DRLG 17-1/2" INSERT BIT & D/O BHA WHILE W&R F/ 1330 TO 1407M, TAG CMT, D/O CMT F/ 1407 TO 1429M (MED TO HARD: F/ 1407 TO 1420M, HARD: 1420 TO 1429M), CIRC MUD & CONT WORK ON MUD PROPERTIES WHILE ADD FRESH MUD & KCL SOLUTION TO MUD ACTIVE SYSTEM (INCREASE KCL TO 3%), POOH W/ 17-1/2" INSERT BIT F/ 1429 TO 300M (SOME INTERVAL W/ PUMP OUT & B/R & MORE ON ELEVATOR), 3-5BPH LOSSES @ RT	24	37.00	1564.5
39	Perform Wiper Trip as POOH to 1450 m & Run back to BTM. Take survey as multi-shot	Trip		Ja.	1750		7.0	0.29	20.4	0.3	7.7	0.32	22.4	CONT POOH W/ 17-1/2" INSERT BIT F/ 1350M TO SURF (SOME INTERVAL W/ PUMP OUT & B/R & MORE ON ELEVATOR), RIH 17 1/2" M.TOOTH BIT & 9-5/8" DHM (PDM, LANG FANG, AKO: 2.6 DEG, LUBE: 7.8, STAGE: 5) & MWD TOOLS & DIR. DRLG BHA TO 1668M MEANWHILE PERFORM DHM SHALLOW TEST & MWD SHALLOW TEST , OK., WASH DN TO 1738M & PRESS UP SEVERAL TIMES, TOOK WT @ 438M, P/U STRING, OBS. STRING STUCK, WORK ON STUCK AS UPWARD; GOT FREE W/ MAX 40 KLBS OVERPULL. CONT WASH & R/D TO 520M, 2-3BPH LOSSES @ RT	24	38.00	1429.0
40	Continue drilling 17-1/2" hole to 1900m while pump hi-vis pill periodically.	Drilling	150	Ja.	1900	6.0	29.0	1.21	21.6	1.3	31.9	1.33	23.7	CONT RIH 17-1/2" M.TOOTH BIT & DIR. DRLG BHA (AKO: 2.6 DEG) F/ 142 TO 1668M ON ELEVATOR. WASH DOWN TO 1429M W/ MAX 5-10 KLB DRAG MEANWHILE PERFORM SHALLOW TEST DHM @ 470M (670 GPM, 930 PSI); "OK"., (STRING STUCK @ 438, 687, 1130, 1424 & 1425M. WORK ON STUCK UPWARD; GOT FREE W/ MAX 100-150 KLBS OVERPULL), DRESS & SMOOTH 3M INTERVAL ABOVE TOC MEANWHILE ORIENT TOOLFACE ON DESIRABLE AZIMUTH (90 DEG) IS IN PROGRESS, 3-4BPH LOSSES @ RT	24	39.00	1429.0
41	Take survey,	Survey		Ja.	1900		2.0	0.08	21.7	0.3	2.3	0.09	23.8	CONT RIH 17-1/2" M.TOOTH BIT & DIR. DRLG BHA (AKO: 2.6 DEG) AS WASH DOWN F/ 1419 TO 1429M (TOC) W/ MAX 5-10 KLB DRAG WHILE STRING STUCK @ 1424, 1425M. WORK ON STUCK UPWARD; GOT FREE W/ MAX 150 KLBS OVERPULL. DRESS & SMOOTH 3M INTERVAL ABOVE TOC MEANWHILE ORIENT TOOLFACE ON DESIRABLE AZIMUTH (90 DEG), COMMENCE DIR. DRILLING 17 1/2" H.S AS TIME DRILLING IN SLIDE MODE TO SIDE TRACK THE WELL F / 1429 TO 1447M, CBU TO TAKE LAST SAMPLE (1442-1447M, 100% FORMATION) WHILE RECIPROCATE STRING, TAKE SURVEY @	24	40.00	1439.5
42	Continue drilling 17-1/2" hole to 2000m while pump hi-vis pill periodically.	Drilling	100	Ja.-Pb.	2000	6.0	18.0	0.75	22.4	0.8	19.8	0.83	24.7	CONT DIR. DRLG 17 1/2" H.S AS TIME DRILLING IN SLIDE MODE TO SIDE TRACK THE WELL F/ 1439.5 TO 1447M, CBU TO TAKE LAST SAMPLE (1442-1447M, 100% FORMATION), TAKE SURVEY @ 1433M (INC : 3.4DEG, AZI : 85DEG), POOH 17-1/2" M.TOOTH BIT & DIR. DRLG BHA F/ 1447 TO 1420 AS PUMP OUT. CONT POOH ON ELEVATOR TO 1350M W/ MAX 25 KLBS OVERPULL, CONT POOH ON ELEVATOR F/ 1350M TO SURF W/ GOOD HOLE COND., STAB & BIT 60% BULLED UP, RIH 17-1/2" INSERT BIT & DIR. DRLG BHA (DHM AKO: 1.5 DEG) TO 1403M ON ELEVATOR W/ GOOD HOLE CONDITION	24	41.00	1447.0
43	Continue drilling 17-1/2" hole to 2100m while pump hi-vis pill periodically.	Drilling	100	Pb.	2100	6.0	18.0	0.75	23.2	0.9	19.8	0.83	25.5	CONT RIH 17-1/2" INSERT BIT & DIR. DRLG BHA (DHM AKO: 1.5 DEG) F/ 500 TO 1429M ON ELEVATOR W/ GOOD HOLE CONDITION MEAN WHILE PERFORM TEST MOTOR & MWD TOOLS @ 500M; "OK". RESUME DIR. DRLG 17-1/2" H.S (DHM AKO: 1.5 DEG) IN SLIDE & ROTATION MODE TO SIDETRACK THE WELL F / 1447 TO 1480M MEANWHILE TAKE SURVEY EVERY 1JT 5" DRILLED, DUE TO OBS INCREASE LOSS FORMATION ADDED 5 SXS/HR (5 PPB) LIMESTONE CHIPS FINE TO ACTIVE MUD SYSTEM, 4-8 BPH LOSSES @ RT	24	42.00	1472.0
44	Continue drilling 17-1/2" hole to 2182m (13-3/8" Casing point) while pump hi-vis pill periodically.	Drilling	82	U-Gu.	2182	6.0	15.0	0.63	23.8	0.7	16.5	0.69	26.2	CONT DIR. DRLG 17-1/2" H.S (DHM AKO: 1.5 DEG) IN SLIDE & ROTATION MODE TO SIDETRACK THE WELL F / 1472 TO 1533M MEANWHILE TAKE SURVEY EVERY 1JT 5" DRILLED & ADDED 5 SXS/HR (5 PPB) LIMESTONE CHIPS FINE TO ACTIVE MUD SYSTEM PERODICALLY, 4-5BPH LOSSES @ RT	24	43.00	1507.0
45	Take survey	Survey		U-Gu.	2182		2.0	0.08	23.9	0.1	2.2	0.09	26.3	CONT DIR. DRLG 17-1/2" H.S (DHM AKO: 1.5 DEG) IN SLIDE & ROTATION MODE TO SIDETRACK THE WELL F / 1507 TO 1552M MEANWHILE TAKE SURVEY EVERY 1JT 5" DRILLED & ADDED 6 SXS/HR (6PPB) LIMESTONE CHIPS FINE TO ACTIVE MUD SYSTEM PERODICALLY, 5-8BPH LOSSES @ RT	24	44.00	1552.0
46	Circulate and clean hole, Condition hole prior to run Log, POOH to surface	Hole Cond/Circ.		U-Gu.	2182		16.0	0.67	24.5	0.7	17.6	0.73	27.0	DUE TO LOW ROP DECIDED POOH TO SURF: POOH 17 1/2" INSERT BIT & DIR. DRLG BHA W/ PUMP OUT F/ 1552 TO 1420M (PASSED KOP @ 1435M W/ MAX 95KIPS OVER PULL), CONT POOH ON ELEVATOR TO SURF W/ GOOD HOLE COND., REDRESS MWD TOOLS, M/U NEW DHM (PDM, NEW, LANG FANG, LOBE 7.8, STAGE: 5), M/U 9 1/2" UBHO + 9 1/2" NMDC. SET DHM AKO: 1.5 DEG, SET MWD TOOLS INSIDE UBHO, SHALLOW TESTED DHM & MWD TOOLS (630GPM 550-600PSI), M/U 17-1/2" PDC BIT, RIH ON ELEVATOR W/ DIR. DRLG BHA (BHA#19) FOLLOWED BY 5" DPS TO 1435M (SOFT	24	45.00	1552.0
47	Run CDR/GR/Caliper log, POOH and L/D log	Log		U-Gu.	2182		13.0	0.54	25.1	0.6	14.3	0.60	27.6	CONT RIH 17 1/2" PDC BIT & DIR. DRLG BHA (AKO: 1.5DEG) F/ 910 TO 1435M (KOP), ADJUST & ALIGN DHM TOOL FACE, WASH DOWN TO 1552M (BTM) WHILE DRESS & SMOOTH KOP AREA SEVERAL TIMES, RESUME DIR. DRLG 17 1/2" H.S AS SLIDE & ROTATION MODE TO SIDE TRACK THE WELL F / 1552 TO 1586M MEANWHILE TAKE SURVEY EVERY 1JT 5" DP DRILLED & ADDED 5SXS/HR (5PPB) LIMESTONE CHIPS FINE TO ACT. MUD SYS. PERODICALLY TO REDUCE LOSS FORMATION, 3-4BPH& RT	24	46.00	1571.0
48	R/U casing running equipment, Run 13-3/8" casing as per program to bottom, Rig pump efficiency should be check in trip-tank before cement job.	Csg. Running		U-Gu.	2182		47.0	1.96	27.0	2.2	51.7	2.15	29.7	CONT DIR. DRLG 17 1/2" H.S AS SLIDE & ROTATION MODE TO SIDE TRACK THE WELL F/ 1571 TO 1593M MEANWHILE TAKE SURVEY EVERY 1JT 5" DP DRILLED & ADDED 5SXS/HR (5PPB) LIMESTONE CHIPS FINE TO ACT. MUD SYS. PERODICALLY TO REDUCE LOSS FORMATION, DUE TO LOW ROP, DECIDED TO POOH. POOH 17 1/2" PDC BIT & DIR. DRLG BHA F/ 1593 TO 100M, 1-2BPH& @ RT	24	47.00	1593.0
49	Circulate Mud one casing vol., Perform Cementing, Bump plug w/1500psi for 15min for CIT. (in case, not observing bumping during CMT job, perform CIT with 1500psi /15min after D/O 7m CMT above F.shoe)	CMT		U-Gu.	2182		11.0	0.46	27.5	0.5	12.1	0.50	30.1	CONT POOH 17 1/2" PDC BIT & DIR. DRLG BHA F/ 1060 TO SURF, RIH 17 1/2" INSERT BIT (K.D, 517, 3*22/32" NOZZLE) & DRLG BHA TO 1593M (BTM), WHILE W&R @ SEVERAL POINTS (770-784M & 1160-1183M & 1411-1470M), RESUME DRLG 17-1/2" HS F/ 1592.9 TO 1594M DUE TO LOW ROP "TNPT", 1-2 BPH LOSS. TILL M.N	24	48.00	1593.0
50	Set 13-3/8" casing slip and test to 800-1000psi, N/D BOP, Cut and L/D landing Joint, N/U 20-3/4" 3000 x 13-5/8" 5000psi C.H.S., inject and pressure test p-seals and cavity with maximum 80% of collapse pressure rating.(1800 psi)	well Head		U-Gu.	2182		24.0	1.00	28.5	1.1	26.4	1.10	31.4	CONT DRLG 17-1/2" H.S TO F/ 1594 TO 1616M WHILE PUMP HI-VIS PILL (PHPA) PERIODICALLY, DUE TO OBS GRADUALLY DECREASE IN SPP (80 PSI) STOP DRLG	24	49.00	1616.0
51	N/U 13-5/8" 10000psi BOP's stack meanwhile fill 13-3/8" casing annulus (Top Job) if required, perform BOPs test as MOC policy , (Set 4-1/2" ,7" Rams in top Rams)	N/U BOP & BOP TEST		U-Gu.	2182		36.0	1.50	30.0	1.7	39.6	1.65	33.0	POOH TO CHECK STRG F/ 1616M TO SURF, WHILE OBS WASHOUT ON 5" DP BODY @ 180M & L/D SAME, RIH 17 1/2" INSERT BITWRR02 (K.D, 517, 3*22/32" NOZZLE) & SAME BHA TO 1616M (BTM) WHILE W&R @ SEVERAL POINTS, RESUME DRLG 17 1/2" H.S TO 1617.5 M, 1-2 BPH LOSS TILL M.N	24	50.00	1617.5
52	P/UP 12-1/4" bit#5 & RIH joint by joint , Drill out f.collar and cement to 7m above shoe (in case not bumping plugs during cementing, perform casing integrity test with 1500psi/15min) drill out cement and shoe track, work on junk sub.	Dr.Out		U-Gu.	2182		22.0	0.92	30.9	1.0	24.2	1.01	34.0	CONT DRLG 17 1/2" H.S F/ 1617.5 TO 1636 M, 1-2 BPH LOSS	24	51.00	1636.0

Item No.	Drilling and Completion Operation TBD of Well: F-20	IADC Code	Interval (meters)	Formation	Depth (meters)	RDF Average (ft/hr)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (if any) (Hours)	Contingency (if any) (Days)	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Actual Operation	Hour	Cum. Time/Day	Depth (m)
	12-1/4" Hole Section / 9-5/8" Casing																	
53	Drilling new formation about 2-3m below shoe.	Drilling	3	U-Gs.	2186	2.0	2.0	0.08	31.0	0.1	2.1	0.09	34.1		CONT DRLG 17 1/2" H.S F/ 1636 TO 1648.5M (13 3/8" CSG POINT), C.B.U, AS WIPER TRIP POOH TO 1420M & TILL M.N	24	52.00	1648.5
54	Work on junk sub, Circulate and clean hole, POOH to Surf.	Cir.		U-Gs.	2186		15.0	0.63	31.6	0.7	16.5	0.69	34.8		RIH W/ WASH DOWN F/ 1420 TO 1648.5M (BTM). C.B.U, SPOT 300 BBL HI-VIS PILL, POOH ON ELEVATOR F/ 1648.5M TO SURF, RIH 30 JT 13 3/8"CSG (68#, N-80, BTC) TO 340M, WHILE F/UP CSG EACH 10 JT, 1-2 BPH LOSS TILL M.N	24	53.00	1648.5
55	P/U & M/U New 12 1/4" PDC bit (bit#6) and S.Stab @ 20m, RIH to bottom.	Trip		U-Gs.	2186		13.0	0.54	32.2	0.6	14.3	0.60	35.4		OBS. FAILURE OF F.SHOE & F.COLLAR FLOATING FUNCTION @343M, CONT RIH 115 JT 13 3/8"CSG (68#, N-80, BTC)(TOTALLY: 145 JTs) F/ 343 TO 1648.5M, TAG BTM, POOH TO 1648M, CIRC MUD MEANWHILE PREPARE CMT SOLUTION IN PROGRESS, 1-2 BPH LOSS @R.T	24	54.00	1648.5
56	Circulate and displace hole with new KCL polymer mud (76 pcf)	Cir.		U-Gs.	2186		5.0	0.21	31.8	0.2	5.5	0.23	35.6		CIRC MUD MEANWHILE PREPARE CMT SOLUTION, 1-2 BPH LOSS TILL M.N	24	55.00	1648.5
56	Perform FIT (2-5m below shoe: EMW should be equal to max. planned mud weight for next hole section plus 2 pcf, 550 PSI).	Testing		U-Gs.	2186		5.0	0.21	32.4	0.3	5.5	0.23	35.8		PERFORM 13 3/8" CSG CMT JOB: PUMP 100 BBL F.WATER (95PCF) AS SPACER, PUMP 1202 BBL CMT SLURRY (94 PCF, "G" DELIJAN, 2780 SXS) AS LEAD CMT, PUMP 135.5 BBL CMT SLURRY (118 PCF, "G" DELIJAN, 555 SXS) AS TAIL CMT, DISPLACE CMT W/ 797 BBL MUD (85PCF), OBS BUMPING & PERFORM CIT W/ 1500PSI FOR 15MIN "OK", WHILE 20 BPH LOSS DURING CMT JOB & NO RETURN CMT SLURRY, W.O.C WHILE INSTALL 13 3/8" CSG SLIPS & PRESS TEST IT W/ 1000 PSI "OK", ROUGH CUT 13 3/8" L.T & L/D SAME, N/D 20 3/4" BOP STACK IN PROGRESS TILL M.N	24	56.00	1648.5
57	Drilling 12-1/4" hole to 2350m while adjust MW based on hole condition ,Use single-shot every 100m multi-shot survey every 300m to control well deviation in this hole section.	Drilling	Vert	Tor.	2350	3.0	60.0	2.50	34.9	2.5	62.5	2.75	38.6		CONT N/D 20 3/4" BOP STACK, INSTALL 20 3/4" 3K * 13 5/8"-5K C.H.S & PRESS TEST P-SEALS W/ 1700 PSI "OK", N/U 13 5/8"-10K BOP STACK, PERFORM PRESS BOP TEST AS NIOC POLICY IN PROGRESS TILL M.N	24	57.00	1648.5
58	Take survey	Survey		Tor.	2350		2.0	0.08	35.0	0.1	2.2	0.09	38.7		CONT PERFORM PRESS BOP TEST AS NIOC POLICY "OK", PERFORM INJECTIVITY TEST, PUMP 8 /INJECT 20 BBL F.WATER W/ 3 BPM RATE 200 PSI PRESS, PERFORM CMT TOP JOB; PUMP 170 BBL CMT SLURRY (85 PCF, G-DELIJAN) W/ 2-3 BPM RATE & 150-300 PSI PRESS, STOP PUMPING & CLOSE ANN VALVE, WHILE W.O.C TO GET HARD SURF SAMPLE RIH 12 1/4" PDC BIT (USED, RERD HYCALOG, 6*15/32" NOZZLE) & 12 1/4" S.STAB @20M TO 1590M, TILL M.N	24	58.00	1648.5
59	Cont. drlg 12 1/4" hole section to 2450m,while pump hi-vis Pill periodically.	Drilling	100	L-Gurpi	2450	3.0	37.0	1.54	36.5	1.7	40.7	1.70	40.4		D/O CMT & SHOE TRACK & RAT HOLE TO 1648.5M, WHILE RUN TOTCO SURVEY @1623M W/ INC: 6 DEG, COMMENCE DRLG 12 1/4" H.S TO 1654 M, WHILE DISPLACE MUD IN HOLE W/ NEW KCL POLYMER MUD (73 PCF, 1% KCL)@1653M, OBS THE WELL "STATIC", @R.T	24	59.00	1654.0
60	Cont drlg 12 1/4" hole section to 2550m,while pump hi-vis Pill periodically.	Drilling	100	L-Gurpi	2550	3.0	37.0	1.54	38.0	1.7	40.7	1.70	42.1		CONT DRLG 12 1/4" H.S F/ 1654 TO 1678M, PERFORM FIT (W/ MAX 630 PSI PRESS, EMW: 90 PCF), RESUME DRLG 12 1/4" H.S F/ 1678 TO 1713M, WHILE PUMP 20 PPB HI-VIS LCM PILL PERIODICALLY & ADD 5 SXS/HR LCM TO ACTIVE SYSTEM, 0-20 BPH LOSS TILL M.N	24	60.00	1713.0
61	Cont drlg 12 1/4" hole section to 2650m while pump hi-vis Pill periodically.	Drilling	100	Hi-La-Sr	2650	3.0	37.0	1.54	39.6	1.7	40.7	1.70	43.8		CONT DRLG 12 1/4" H.S F/ 1713 TO 1828M, WHILE PUMP 20 PPB HI-VIS LCM PILL PERIODICALLY & ADD 5 SXS/HR LCM TO ACTIVE SYSTEM, 10-20 BPH LOSS TILL M.N	24	61.00	1828.0
62	Take survey	Survey		Hi-La-Sr	2650		2.0	0.08	39.7	0.1	2.2	0.09	43.9		CONT DRLG 12 1/4" H.S F/ 1828 TO 1831M, STOP DRLG DUE LOW ROP, DROP TOTCO, POOH TO SURF W/ GOOD OPEN HOLE CONDITION, RET TOTCO (DEV: 2.80DEG), RIH W/ 12-1/4" INSERT BIT TO 1831M W/ GOOD CONDITION & RESUME DRLG TO 1861M, LOSS: 4-6, ROP: 5.5MPH.	24	62.00	1943.0
63	cont drlg 12 1/4" hole section to 2750m while pump hi-vis Pill periodically.	Drilling	100	SV	2750	3.0	37.0	1.54	41.2	1.7	40.7	1.70	45.6		DRLG 12-1/4" H.SECTION F/ 1861M TO 1994M WHILE PUMP HI-VIS PILL PERIODICALLY, B/R & R/D AFTER DRILLED EACH STD, LOSS: 1-4BPH, ROP: 5.5MPH. (TOP OF PABDEH @ 1991M).	24	63.00	2000.0
64	cont drlg 12 1/4" hole section to 2850m while pump hi-vis Pill periodically.	Drilling	100	SV	2850	3.0	37.0	1.54	42.7	1.7	40.7	1.70	47.3		DRLG 12-1/4" H.SECTION F/ 1994M TO 2000M, LOSS: 1-4BPH, ROP: 6MPH, CBU, POOH W/ 12-1/4" INSERT BIT F/ 2000 TO SURF, RIH W/ 8-1/2" CNTR CUT BIT TO 1890M, SPOT 160BBLS 90PPB LCM PILL (20PPB LIMESTONE CHIPS C.M + 20PPB MICA C.M + 20PPB FIBER LOCE + 10PPB OYSTER SHELL C), POOH F/ 1890 TO 1530M (TOP OF LCM PILL), CLOSE TOP RAMS, INJECT LCM PILL W/ 800BLS 75 PCF MUD (F.R: 1 BPM, PUMPING PRESS: 150-250 PSI).	24	64.00	2000.0
65	BOP Test.	BOP Test		SV	2850		6.0	0.25	43.0	0.3	6.6	0.28	47.5		CONT WAIT CLOSE PILL W/ 800BLS MUD (75 PCF + 1% KCL) PUMPING PRESS: 150-250 PSI, OPEN THE WELL, RUN BACK F/ 1530M TO 1950M, CBU, LOSS: 20BPH, POOH TO 1860M, CBU ONCE LINE, PUMP 30BBLS BRINE (75PCF) AS SPACER AHEAD, MIX & PUMP 268 SXS CMT SLURRY (SG: 1.93KG/L, 15W-95PCF), PUMP 2BBLS DW AS BUMP SPACER, DISP CMT W/ 838BLS MUD (75PCF) AS BALANCE PLUG (CMT LOSSES: 358BLS), POOH TO 1370M & FLUSH STRG, MONITOR WELL; 2BPH LOSS, CLOSE TOP RAMS & SQUEEZE 258BLS CMT SLURRY BY APPLY PRESS (70-340 PSI) THROU ANN, OPEN TOP RAMS & MONITOR WELL "STATIC", CIRC & CHECK LOSS W/ F.R: 600 GPM, SPP: 600 PSI, 18BPH LOSS, WAIT DOWN CMT 13:30 TO 15:00HR, GET 3.5KLB DRAG, CBU, GOT 40BBLS CONTAMINATE CMT ON SHAKER, RI, RC	24	65.00	2000.0
66	cont drlg 12 1/4" hole section to 2950m while pump hi-vis Pill periodically.	Drilling	100	SV	2950	3.0	37.0	1.54	44.5	1.7	40.7	1.70	49.2		RIH W/ 12-1/4" INSERT BIT (537, USED, OPEN) & LAST BHA TO 1690M, D/O SOFT TO MED CMT F/ 1690 TO 1860M , WASH DOWN F/ 1860 TO 2000M (BTM), ROP:40 MPH, NI-NG, PUMP 50BBLS HI-VIS PILL @2000M, CIRC TILL CLEAN SHAKER POOH F/2000M TO 1648M (13-3/8" CSG SHOE) W/ GOOD HOLE CONDITION, SLOW CIRC THROU STRG WHILE WORK ON MUD PARAMETERS, RUN BACK F/1648M TO 2000M W/ GOOD CONDITION WHILE CONT WORK ON MUD PARAMETERS, NI-NG.	24	66.00	2000.0
67	Take survey	Survey		SV	2950		2.0	0.08	44.6	0.1	2.2	0.09	49.3		WHILE DISP WELL W/ 900BBLS MUD (77PCF); RESUME DRLG 12-1/4" H.SECTION F/ 2000 TO 2114M, LOSS: 1-3BPH, AV. ROP: 5MPH.	24	67.00	2114.0
68	cont drlg 12 1/4" hole section to 3050m while pump hi-vis Pill periodically.	Drilling	100	SV	3050	3.0	37.0	1.54	46.2	1.7	40.7	1.70	51.0		CONT DRLG 12-1/4" H.SECTION F/ 2114M TO 2150M W/ 1-3BPH LOSSES, ROP: 3MPH, STOP DRLG DUE TO LOW ROP, PUMP & CIRC OUT 40BBLS HI-VIS PILL, RUN TOTCO (DEV: 2.80DEG) & POOH TO 80M W/ GOOD OPEN HOLE CONDITION, WHILE P/U & M/U 24 JTS 5" DP "S" & RIH TO 420M. CIRC HI-RATE. POOH TO 200M & R/B SAME, LOSS: 1BPH.	24	68.00	2150.0
69	cont drlg 12 1/4" hole section to 3150m while pump hi-vis Pill periodically.	Drilling	100	SV	3150	3.0	37.0	1.54	47.7	1.7	40.7	1.70	52.7		POOH W/ 12-1/4" INSERT BIT & DRLG BHA F/ 80M TO SURF, M/U & RIH W/ 12-1/4" PDC BIT (BEST, NEW, M423, 2 x 12/32" + 5 x 13/32" + 2 x 14/32" ND13) & RELATED BHA WHILE OBS; FAILURE OF DRLG JAR DURING RIH, L/D SAME (RIH WITHOUT JAR), RIH W/ 5"DPS * 162/TS (IT BY /T) TO 1716M, REC 2/TS * 8" DRLG JAR ON LOC, POOH & R/BACK 5" DPS F/ 1716M TO 84M, F/U & M/U 8" D.MC & R/I W/ 12-1/4" PDC BIT (BEST, NEW, M423, 2X12/32" + 5X13/32" + 2X14/32" ND13) & DRLG BHA TO 250M, LOSS: 0-1BPH.	24	69.00	2150.0
70	CBU, POOH to surf (due to rotating HRS), change BHA & Bit, RIH W/BIT#7 to btm.	Trip		SV	3150		2.0	0.08	47.8	0.1	2.2	0.09	52.8		CONT. RIH TO 2150M (BTM) BREAK CIRC, RESUME DRLG 12-1/4" H.S TO 2151M, OBS ABNORMAL FLUCTUATION IN SPP STOP DRLG, POOH TO 1620M, CHANGE STAND PIPE MANIFOLD VALVE, RUN BACK TO BTM, RESUME DRLG 12-1/4" H.S TO 2222M W/ 0-3 BPHL.	24	70.00	2189.0
71	cont drlg 12 1/4" hole section to 3250m while pump hi-vis Pill periodically.	Drilling	100	SV	3250	2.0	56.0	2.33	50.1	2.6	61.6	2.57	55.4		CONT DRLG 12-1/4" HOLE SECTION F/ 2189 TO 2339M WHILE PUMP HI-VIS PERIODICALLY, B/R & R/D EVERY DRILLED STAND, WORK ON IMPROVE MUD RHEOLOGY W/ 0-4 BPHL	24	71.00	2339.0
72	Take survey	Survey		SV	3250		2.0	0.08	50.2	0.1	2.2	0.09	55.5		CONT DRLG 12-1/4" H.S F/ 2339 TO 2509M, PUMP HI-VIS PILL AND CIRCULATED WHILE B/R AND R/D LAST DRILLED STAND, POOH W/ SOFT B/R AS WIPER TRIP F/ 2509 TO 2395M, DUE TO HIGH WIND SPEED STOPPED POOH, RIH ON ELEVATOR TO 2509M (BTM), CONT DRLG 12-1/4" H.S F/ 2509 TO 2545M W/ 2-4 BPHL.	24	72.00	2509.0
73	cont drlg 12 1/4" hole section to 3350m while pump hi-vis Pill periodically.	Drilling	100	Kz.	3350	2.0	56.0	2.33	52.5	2.6	61.6	2.57	58.0		CONT. POOH W/ SOFT B/R AS WIPER TRIP F/ 2509 TO 2395M DUE TO HIGH WIND SPEED STOPPED POOH, RIH ON ELEVATOR TO 2509M (BTM), RESUME DRLG 12-1/4" H.S F/ 2509 TO 2695M W/ 1-3 BPHL.	24	73.00	2685.0
74	cont drlg 12 1/4" hole section to 3450m while pump hi-vis Pill periodically.	Drilling	HRDT1	Kz.	3450	2.0	56.0	2.33	54.9	2.6	61.6	2.57	60.6		CONT. DRLG 12-1/4" H.SEC F/ 2686 TO 2696.5M, DUE TO LOW PROGRESS STOP DRLG, POOH TO 1620M W/ GOOD HOLE CONDITION, STATIC FLOW CHECKED; 0.5 BPH FORMATION LOSS, RESUME POOH TO SURF, PERFORM BOP TEST, M/U & RIH 12-1/4" PDC BIT (BEST, NEW, M423, 5X13/32" + 4X14/32" ND1) + BIT SUB (F.VALVE, BAFFEL PLATE IN) + 3 STDS 8-1/2" DC + DJAR (NEW) + 1 JTS 8-1/2" DC FOLLOWED BY 5" DPS TO 2000M W/ 0-1 BPHL.	24	74.00	2696.5
75	Perform Wiper Trip as POOH till 3150m & Run back to BTM. Take survey as multi-shot	Trip		Kz.	3450		6.0	0.25	55.1	0.3	6.6	0.28	60.9		CONT RIH 12-1/4" PDC BIT & DRLG BHA TO 2696.5M, FAN THE BTM & PROFILE THE BIT, RESUME DRLG 12-1/4" H.S F/ 2696.5 TO 2762M WHILE PUMP HI-VIS PERIODICALLY & ADD LIMESTONE CHIPS FINE 3 SX/HR TO ACTIVE SYSTEM FOR CONTROL DOWN HOLE LOSS W/ 2-3 BPHL.	24	75.00	2738
76	cont drlg 12 1/4" hole section to 3550m while pump hi-vis Pill periodically.	Drilling	100	Da.	3550	2.0	56.0	2.33	57.5	2.6	61.6	2.57	63.4		CONT DRLG. 12-1/4" HOLE SECTION F/ 2738 TO 2810M, OBS SUDDENLY DROP PRESS. 300 PSI, CHECK SURF. EQUIPMENTS, "OK", POOH F/ 2810 TO 60 M W/ 0-3 BPHL.	24	76.00	2810
77	Take survey	Survey		Da.	3550		2.0	0.08	57.5	0.1	2.2	0.09	63.5		CONT. POOH AS CHECK STRING F/1550 TO SURF .OBS STRING TWIST OFF FROM TOP OF 12-1/4" S.STAB,F/U & ASSEMBLED 10-1/8" O.SHOT AND RIH TO 2788.47M (TOF). ENGAGED WITH FISH & CATCH SAME. POOH TO 600 M W/1-2 BPH LOSS @R.T.	24	77.00	2810
78	BOP Test.	BOP Test		Da.	3550		6.0	0.25	57.8	0.3	6.6	0.28	63.8		CONT. POOH F/ 2100M TO SURF. RELEASED THE FISH & L/D OVERSHOT, M/UP PREVIOUS 12-1/4" PDC BIT & BHA TO 2770 M W/ GOOD HOLE CONDITION & WASH DOWN TO 2810M (BTM) CIRC. TILL UNIFORM MW PUMP 40 BBL HI-VIS PILL, CIRC. OUT PILL ,RESUME DRLG 12-1/4" H.S F/ 2810 TO 2811 M W/1-2 BPH LOSS @R.T.	24	78.00	2810
79	cont drlg 12 1/4" hole section to 3650m while pump hi-vis Pill periodically.	Drilling	100	Gutta.	3650	2.0	56.0	2.33	60.1	2.6	61.6	2.57	66.4		CONT.RIH W/ 12-1/4"PDC BIT F/ 2200 TO 2810M (BTM). CIRC BTM'S UP. RESUMED DRLG 12-1/4" H.S F/2810 TO 2868M W/2-4 BPH LOSS. DUE TO LOW ROP DECIDED TO POOH F/2868 TO 3000 M W/ GOOD HOLE COND WHILE CIRC CROSS WELL HEAD W/1-2 BPH LOSS@R.T.	24	79.00	2868
80	cont drlg 12 1/4" hole section to 3750m while pump hi-vis Pill periodically.	Drilling	HRDT1	Ga.	3750	2.0	56.0	2.33	62.5	2.6	61.6	2.57	68.9		DUE TO LOW ROP, DECIDED TO POOH F/2868 TO SURF W/ GOOD HOLE CON, L/D 12-1/4" PDC BIT, BIT DULL GRADING: (5-2-LT-N-X-I-BT-PR),M/U & RIH 12-1/4" NEW PDC BIT + GRLG BHA FOLLOWDE BY 5" DP TO 2830M,WASH DOWN F/2830 TO 2868M,PUMP 40 BBL HI-VIS PILL & CIRC. OUT PILL,RESUME DRLG 12-1/4" H.S F/2868 TO 2890 M W/2-4 BPH LOSS @R.T.	24	80.00	2870
81	Perform Wiper Trip as POOH till 3450m & Run back to BTM. Take survey as multi-shot	Trip		Ga.	3750		6.0	0.25	62.7	0.3	6.6	0.28	69.2		CONT DRLG 12-1/4" H.S F/2870 TO 2978 M W/2-4 BPH LOSS WHILE PUMP HI-VIS PILL PERIDICALLY & B/R & R/D DRILLED STAND, MADE CONNECTION@R.T.	24	81.00	2971
82	cont drlg 12 1/4" hole section to 3850m while pump hi-vis Pill periodically.	Drilling	100	Ga.	3850	2.0	56.0	2.33	65.0	2.6	61.6	2.57	71.8		CONT. DRLG 12-1/4" H.S F/ 2941 TO 3006.7M. OBS. TWIST OFF STRING INDICATIONS. POOH TO SURF, OBS STRING TWIST OFF FROM TOP OF 12-1/4" S.STAB. ASSEMBLE 10-1/8" SHORT CATCH O.SHOT & RIH TO 2000 M W/1-2 BPH LOSS @R.T.	24	82.00	3007
83	Take survey	Survey		Ga.	3850		2.0	0.08	65.1	0.1	2.2	0.09	71.9		RIH W/ 10-1/8" O.SHOT TO TOF 2984.5, CATCH FISH, POOH TO SURFAC,OBS. OVERSHOT ENGAGE TO FISH, 1/D 8" FISHING JAR. RELEASE OVER SHOT&RECOVERED FISH, P/U & M/U 12-1/4" PDC Bit (Best, Used, M423, 5x13/32" + 4x14/32" ND1) + DRLG BHA TO 160 M W/1-2 BPH LOSS@R.T.	24	83.00	3007
84	cont drlg 12 1/4" hole section to 3915 inspection TD) while pump hi-vis Pill periodically.	Drilling	65	Ga-Fh.	3915	2.0	36.0	1.50	66.6	1.7	39.6	1.65	73.5		L/D 8" FISHING JAR. RELEASE OVER SHOT&RECOVERED FISH, M/U & RIH 12-1/4" PDC Bit (Best, Used, M423, 5x13/32" + 4x14/32" ND1) + DRLG BHA TO 1840 M, TOOK WEIGHT STRG, SOFT TO MED WASH & REAM DOWN F/1840 TO 2480 M & HARD WASH & REAM F/2480 TO 2850 M W/1-2 BPH LOSS @R.T.	24	84.00	3007
85	Take survey	Survey		FH.	3915		2.0	0.08	66.7	0.1	2.2	0.09	73.6		CONT. HARD WAR DOWN F/ 2480 TO 3000M W/1-2 BPH LOSS. PUMP HI-VIS PILL & CIRC. OUT,RESUME 12-1/4" H.S F/ 3006 TO 3019.5 M MEANWHILE INC MW F/79 TO 80 PCF W/2-4 BPH LOSSS,DUE TO OBS. LEAKAGE FROM UPPER IBOP,STOP DRLG. POOH W/ 12-1/4" PDC BIT F/ 3019.5 TO 2400M ON ELEVATOR W/ GOOD HOLE CONDITION F/U TIE WELL W/2 BPH LOSS @R.T.	24	85.00	3018
86	Circulate and clean hole, Condition hole prior to logging. POOH to surface.	Trip		FH.	3915		40.0	1.67	68.4	1.8	44.0	1.83	75.4		CONT. DRLG 12-1/4" H.S F/3017.5 TO 3019.5M, STOP DRLG DUE TO LEAKAGE F/ UPPER IBOP, POOH TO1648 M (13-3/8" CSG SHOE), CHANGE OUT IBOP ASSY, RUN BACK TO BTM, RESUME DRLG 12-1/4" H.S F/3019.5 TO 3026.5M W/2-3 BPH LOSS@R.T.	24.0	86.00	3024
87	R/U logging equipment, run Full Suite logs & Deviation tools as per program. POOH, L/D logging equipment.	Log		FH.	3915		45.0	1.88	70.2	2.1	49.5	2.06	77.5		CONT. DRLG 12-1/4" H.S F/ 3023.5 TO 3027M, DUE TO LOW ROP, POOH W/ 12-1/4" PDC BIT TO SURF ,PDC BIT. BIT DULL: 3-8-RO-N-X-I-(BT,CT)-PR., MEANWHILE FLOW CHECK THE WELL W/1 BPH LOSS @ SHOE AND BHA DEPTH, RIH W/ NEW 12-1/4" PDC BIT AND DRLG BHA TO 2550 M WHILE F/U STRING AND BREAK CIRC. EVERY 15 STD W/ 0-1 BPHL@R.T.	24.0	87.00	3027
88	R/U casing running equipment.Run 9-5/8" casing to bottom, rig pump efficiency should be check in trip-tank before cement job.	Csg. Running		FH.	3915		45.0	1.88	72.1	2.1	49.5	2.06	79.6		CONT.RIH W/ NEW 12-1/4" PDC BIT AND DRLG BHA TO 2996 M 'RUN TOTCO @ 2996M (31 MT OFF BTM). RESULT: 0.5 DEG. WASH DOWN TO 3027M (BTM) CIRC. HI-RATE, MEANWHILE PUMP AND CIRC. OUT 70 BBL HI-VIS PILL @ 2 STEP AS CLEAN BTM,RESUME DRLG 12-1/4" H.S F/ 3027 TO 3071 M W/2-3 BPH LOSS@R.T.	24.0	88.00	3057
89	Circulate one casing vol. mud, L/U CMT line & pressure test, Perform Cementing casing and displacing, In case of observed bumping; perform CIT With 3000psi/15 Min. (Max 80% Casing Burst) Record and Report the final pressure.(In case of not observing bumping during CMT job, perform CIT with 3000psi after D/O 7m CMT above F.shoe)	CMT		FH.	3915		17.0	0.71	72.8	0.8	18.7	0.78	80.3		CONT DRLG 12 1/4" HOLE SECTION TO 3121M, MEANWHILE INCREASE MW F/80PCF TO 80.5PCF W/2-3 BPHL, CONT DRLG 12 1/4" HOLE SECTION TO 3169M, ADD 3 SXS/HR LST CHIPS(F) TO MUD SYS W/3-5BPHL & ROP: 4.8MPH.	24.0	89.00	3140
90	Hang up BOPs. Set the 9-5/8" casing slip & Pressure test same w/ 800-1000psi. (open side outlet valves while testing), Cut and L/D landing Joint, N/U 13 5/8"-5000 x 11"-10000 T.H.S Pack & test p-seals & cavity w/ max 80% of CSG collapse pressure.(3800 psi)	well Head		FH.	3915		24.0	1.00	73.8	1.1	26.4	1.10	81.4		CONT DRLG 12 1/4" HOLE SECTION F/ 3140 TO 3240M MEANWHILE ADD 3 SKS/HR LST CHIPS F, M TO ACTIVE SYSTEM, PUMP HI-VIS PILL EACH STD & INCREASE MW F/ 80.5 TO 81 PCF, B/R & R/D EACH DRILLED STD, AV. ROP: 5MPH, OBS DECREASE SPP, STOP DRLG, TAKE SCR & CHECK SURFACE EQUIP., DURING TAKE SCR; SUDDENLY LOST 170KLBS SYRING WT & SPP: ZERO. POOH 35 STDS 5" DP TO CHECK STRING, 2-5BPHL @ RT	24.0	90.00	3240
91	N/U 13-5/8" x 10000 BOPs stack meanwhile fill the 9-5/8" casing annulus if required, Perform BOP's test as per NIOC Policy	H/U BOP & BOP Test		FH.	3915		24.0	1.00	74.8	1.1	26.4	1.10	82.5		CONT DRLG 12 1/4" H.S F/ 3236 TO 3240M, OBS DECREASE SPP, STOP DRLG, TAKE SCR & CHECK SURFACE EQUIP., DURING TAKE SCR; SUDDENLY LOST 170KLBS SYRING WT & SPP: ZERO. POOH 5" DPS TO CHECK STRING TO SURF, OBS STRING TWIST OFF FROM 5" DP (STD NO. 57), (LEFT IN HOLE: BHA + 5" DPS (5STDS + D +0.41M) ESTIMATE LENGTH 1813M, ESTIMATE TOF: 1426.6M), M/U 10-1/8" O.SHOT W/ EXTENSION & DERESSED BY (6-3/8" B GRAPPLE & 6-1/2" M.CONTROL) TO 1430M (TOF), TOOK WEIGHT, CATCH THE FISH, POOH FISH TO 1338M (BTM OF STRING F/ 3240 TO 3148M) W/ MED. DRAG, STUCK STRING, WORK ON STUCK AS DOWNWARD (MAX 120KLBS) SEVERAL TIMES, GOT FREE, POOH WITH HARD WASH & R/R 314SM, CONT POOH TO 1813M, RELEASE OVERSHOT, 6-8BPHL @ RT	24.0	91.00	3240
92	Drill out shoe track with 8-1/2" bit to 7m above shoe, in case not bumping plugs during cementing; perform casing integrity test with 3000psi, cont drill out shoe track and rat hole,	D/Out		FH.	3915		9.0	0.38	75.2	0.4	9.9	0.41	83.0					
	Total Duration of 12-1/4" Hole Section:							***44.5***	***75.2***			***48.9***	***83.0***					


Item No.	Drilling and Completion Operation TBD of Well: F-20	IADC Code	Interval (meters)	Formation	Depth (meters)	KOP Average (MW)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (if it)		Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Actual Operations	Hour	Cum. Time/Day	Depth (m)
	8-1/2" Hole Section / 7" Liner																	
93	Drilling new formation about 3-5m below shoe	Drilling	3	FH	3918	2	2.0	0.08	75.3	0.1	2.1	0.09	83.0	CONT POOH FISH F/ 2740 TO 1813M, RELEASE OVERSHOT, CONT POOH FISH TO SURF, RECOVER ALL OF FISH, PERFORM BOP PRESS TEST AS NIOC POLICY, OK. RIH NEW 12-1/4" PDC BIT (M424, 8 BLADE, BX16/32" NZL) & DRLG BHA (NO.#33) TO 2400M, 1-38PHL @ RT	24.0	92.00	3240
94	Work on junk sub, Circulate and clean hole, POOH to Surf.	Trip		FH	3918		20.0	0.83	76.1	0.9	22.0	0.92	84.0	CONT RIH NEW 12-1/4" PDC BIT (M424, 8 BLADE, BX16/32" NZL) & DRLG BHA (NO.#33) TO 3240M, RESUME DRLG 12 1/4" H.S F/ 3240 TO 3275M, DUE TO LOW ROP, POOH 12-1/4" PDC BIT F/ 3275 (BTM) TO 3100M MEANWHILE F/U THE WELL, 3-5 BPHL @ RT	24.0	93.00	3274.0
95	P/U & M/U New 8 1/2" PDC bit (bit#9) and S. Stab @ 20m, RIH to bottom.	Trip		FH	3918		18.0	0.75	76.9	0.8	19.8	0.83	84.8	CONT DRLG 12 1/4" H.S F/ 3274 TO 3275M, DUE TO LOW ROP, POOH 12-1/4" PDC BIT F/ 3275 (BTM) TO 3918M, RIH USED 12-1/4" INSERT BIT (537, 3*20/32" NZL)+ 9-1/2" JUNK SUB ON ELEVATOR TO 3275M (BTM), PUMP HI-VIS PILL, CBU IS IN PROGRESS, 1-38PHL @ RT	24.0	94.00	3275
96	Displace hole with KCL Polymer mud (100 pcf),	Hole Cond/Circ		FH	3918		5.0	0.21	77.1	0.2	5.5	0.23	85.0	CONT RIH USED 12-1/4" INSERT BIT (537, 3*20/32" NZL) + 9-1/2" JUNK SUB ON ELEVATOR F/ 2100 TO 3275M (BTM), PUMP HI-VIS PILL, CBU, WORK ON JUNK SUB SEVERAL TIMES, RESUME DRLG 12 1/4" H.S F/ 3275 TO 3284.5M, AGAIN WORK ON J.SUB SEVERAL TIMES, DUE TO LOW ROP POOH ON ELEVATOR F/ 3284.5 TO 1900, 3-4BPHL @ RT	24.0	95.00	3284
97	Perform FIT. (EMW (720 psi) should be equal to max. planned mud weight for 8-1/2" hole section plus 2 PCF),	Testing		FH	3918		5.0	0.21	77.3	0.2	5.5	0.23	85.2	CONT RESUME DRLG 12 1/4" H.S F/ 3284 TO 3284.5M, DUE TO LOW ROP DECIDED TO POOH, WORK ON J.SUB SEVERAL TIMES, POOH ON ELEVATOR F/ 3284.5M TO SURF, RECOVER J.SUB (0.037LB=17GR POC PIECES JUNK), RIH 10-1/8" REV. CIRC. JUNK BASKET TO 3284M, DROP BALL INSIDE STRING AND CHASE SAME TO SEAT IN 10-1/8" REV. CIRC. JUNK BASKET, WORK ON RCJB F/ 3284.5 TO 3285M, POOH 10-1/8" RCJB TO SURF, B/O & L/D SAME. RECOVERED 50CM FORMATION CORE WITH OUT ANY METAL PARTS OR JUNK, RIH NEW 12-1/4" PDC BIT (BESTE, 9*13/32" NZL) & DRLG BHA#36 TO 3600M, 1-38PHL @ RT	24.0	96.00	3284.5
98	Drilling 8-1/2" hole to 4180m (TD) While use single-shot every 100m, multi-shot survey every 300m to control well deviation in this hole section.	Drilling	262	FH-Sb	4180	3	98.0	4.08	81.2	4.5	107.8	4.49	89.5	RT 3284M, DROP BALL INSIDE STRING AND CHASE SAME TO SEAT IN 10-1/8" REV. CIRC. JUNK BASKET, WORK ON RCJB F/ 3284.5 TO 3285M, POOH 10-1/8" RCJB TO SURF, B/O & L/D SAME. RECOVERED 50CM FORMATION CORE WITH OUT ANY METAL PARTS OR JUNK, RIH NEW 12-1/4" PDC BIT (BESTE, 9*13/32" NZL) & DRLG BHA#36 TO 3600M, 1-38PHL @ RT	24.0	97.00	3285
99	Circuate clean hole, perform condition trip f/4180 to 3915m & run back to BTM, C.B.U and POOH to Surface.	Trip		FH-Sb	4180		27.0	1.13	82.3	1.2	29.7	1.24	90.7	RIH NEW 12-1/4" PDC BIT (BESTE, 9*13/32" NZL) & DRLG BHA#36 TO 3284.5M, PUMP HI-VIS PILL & CIRC. OUT SAME, ENLARGE THE HOLE (10-1/8" TO 12-1/4") F/ 3284.5 TO 3285M & RESUME DRLG 12-1/4" H.S F/ 3285 TO 3344M WHILE B/R & R/D EACH DRILLED STAND, 3-5BPHL @ RT	24.0	98.00	3315
100	BOP Test.	BOP Test		FH-Sb	4180		6.0	0.25	82.5	0.3	6.6	0.28	91.0	CONT DRLG 12-1/4" H.S F/ 3315 TO 3463M WHILE B/R & R/D DRILLED STANDS, & PUMP HI-VIS PILL PERIODICALLY TO SWEEP THE WELL, 3-5BPHL @ RT	24.0	99.00	3427
101	Change Ram, Install shooting nipple, R/U WL Logging Eq. Perform Logging (Full Suite/CDR/GR Logs.), R/D Logging Eq., change Ram.	Log		FH-Sb	4180		54.0	2.25	84.8	2.5	59.4	2.48	93.5	CONT DRLG 12-1/4" H.S F/ 3427 TO 3558M WHILE B/R & R/D DRILLED STANDS, & PUMP HI-VIS PILL PERIODICALLY TO SWEEP THE WELL & INCREASE MW TWICE (F/ 82 TO 82.5PCF & 82.5 TO 83PCF), 3-5BPHL @ RT	24.0	100.00	3535
102	RIH w/ 8-1/2" PDC Bit BHA (Without RWD), condition hole prior to 7" Liner running (RIH to 8m, CBU, Spot pill, POOH to surface)	Hole Cond/Circ		FH-Sb	4180		47.0	1.96	86.7	2.2	51.7	2.15	95.6	CONT DRLG 12-1/4" H.S F/ 3535 TO 3620M WHILE B/R & R/D DRILLED STANDS, & PUMP HI-VIS PILL PERIODICALLY TO SWEEP THE WELL, POOH W/ SOFT WASH & B/R AS CONDITION TRIP F/ 3620 TO 3250M WHILE SMOOTH TIGHT SPOTS @ 3590, 3500 & 3260M, RUN BACK ON ELEVATOR TO 3600M WITH GOOD HOLE CONDITION, 2-3BPHL @ RT	24.0	101.00	3620
103	R/U 7" Liner running Eq., Run 7" liner (+/- 365m LNR) to 8m @ 4180m, R/U CMT lines, Set L.Hanger +/- 3815m (100m overlap), release L.Hanger setting tool.	CSG		FH-Sb	4180		40.0	1.67	88.4	1.8	44.0	1.83	97.5	CONT POOH W/ SOFT WASH & B/R AS CONDITION TRIP F/ 3570 TO 3250M WHILE SMOOTH TIGHT SPOTS @ 3500 & 3260M, RUN BACK ON ELEVATOR TO 3600M WITH GOOD HOSE CONDITION, RUN TOTCO SURVEY, RETRIEVE SAME (0.8 DEG), CONT RIH 12 1/4" PDC BIT ON ELEVATOR TO 3620M, PUMP 30BBL HI-VIS PILL, RESUME DRLG 12-1/4" H.S F/ 3620 TO 3692M WHILE B/R & R/D DRILLED STANDS & PUMP HI-VIS PILL PERIODICALLY TO SWEEP THE WELL, 3-5BPHL @ RT	24.0	102.00	3671
104	Cement 7" Liner as per program.. perform liner integrity test w/ 3000 psi for 15 min while cementing.	CMT		FH-Sb	4180		10.0	0.42	88.8	0.5	11.0	0.46	97.9	CONT DRLG 12-1/4" H.S F/ 3671 TO 3738M, OBS GRADUALLY DECREASE SPP (70PSI) AND GET RETURN MINIMUM MW: 82 PCF, STOP DRLG, CIRCULATION WHILE MONITOR SPP (CONSTANTLY 70 PSI LESS THAN SPP WITH SAME GPM DURING DRLG) TILL BALANCE MW IN/OUT ON 83 PCF, CONT DRLG 12-1/4" H.S F/ 3738 TO 3756M MEANWHILE INCREASE MW F/ 83 TO 83.5PCF, 3-5BPHL @ RT	24.0	103.00	3741
105	POOH w/ L.Hanger setting tool to 3500m, Flush string & CBU, POOH to 3300m.	Trip		FH-Sb	4180		7.0	0.29	89.1	0.3	7.7	0.32	98.3	CONT DRLG 12-1/4" H.S F/ 3741 TO 3790M WHILE B/R & R/D EACH STAND & PUMP HI-VIS PILL PERIODICALLY MEANWHILE INCREASE MW F/ 83 TO 84PCF @2STAGE,3-5 BPHLTILL M.N.	24.0	104.00	3790
106	Open the Well. Cont' POOH to surface & L/D L.Hanger setting tool.	Trip		FH-Sb	4180		13.0	0.54	89.7	0.6	14.3	0.60	98.9	CONT DRLG 12-1/4" H.S F/ 3790 TO 3820M WHILE B/R & R/D EACH STAND & PUMP HI-VIS PILL PERIODICALLY MEANWHILE INCREASE MW F/ 84 TO 85PCF, @2STAGE,3-5 BPHLTILL M.N.	24.0	105.00	3820
107	P/U & M/U 8-1/2" MT Bit (BRR1) BHA, RIH to L.Lap @ +/- 3815m while D/Out cement (if any cement: Considered 75TD wet for CMT Job), Circ B clean the well, POOH.	Dr/Out		FH-Sb	4180		45.0	1.88	91.5	2.1	49.5	2.06	100.9	CONT DRLG 12-1/4" H.S F/ 3820 TO 3846M WHILE B/R & R/D EACH STAND & PUMP HI-VIS PILL PERIODICALLY MEANWHILE DEC. MW F/ 85 TO 84PCF STEP BY STEP,6-12 BPHL TILL M.N.	24.0	106.00	3846
108	P/U & M/U 5-7/8" MT Bit(bit#10) BHA, RIH to tag POB, D/Out POB, RIH to LDC depth while D/Out any cement, work on junk sub and CBU. Perform 7" Liner CIT. (80% of Burst press) with 3000 psi,for 10 min, (if not obs bumping). POOH to top of Liner Lap @ +/- 3815m, CBU, perform Liner lap positive test w/ 2000 psi, POOH to Surface. based on client approval for dry test 7" Liner lap follow contingency plan#2	Dr/Out		FH-Sb	4180		45.0	1.88	93.4	2.1	49.5	2.06	103.0	CONT DRLG 12-1/4" H.S F/ 3846 TO3872M , WHILE PUMP LCM PILL & HI-VIS PILL PERIODICALLY , POOH F/ 3872 TO 1707M, 6-13 BPHL TILL M.N.	24.0	107.00	3872
109	BOP Test.	BOP Test		FH-Sb	4180		7.0	0.29	93.7	0.3	7.7	0.32	103.3	CONT POOH F/ 3300 TO SURF. SPOT 140 BBL LCM PILL (40PPB)@ 1700M , CONT POOH TO SURF. L/D 8" D.JAR & 12 1/4" PDC BIT , RIH W/ 12 1/4" PDC BIT(USED) & 8"D.JAR NEW & SAME BHA TO 2900 M W/ 10-15 BPHL TILL M.N.	24.0	108.00	3872
110	Change Ram, Install shooting nipple, R/U WL Logging Eq. Perform CMT quality Logging of 7" Liner & 9-5/8" Casing from 7" liner LDC depth to Surface. (SBT/VDL/CCL/GR), R/D Logging Eq. change Ram.	Log		FH-Sb	4180		21.0	0.88	94.6	1.0	23.1	0.96	104.3	RIH F/ 2900TO 3784M TOOK WEIGHT STRG RIH AS W&R TO 3872 M(BTM), RESUME DRLG 12 1/4"H.S TO 3893 M, MEANWHILE DEC. MW F/ 83 TO 82.5 PCF, PUMP LCM PILL 40PPB AS PERIODICALLY OBS WASH OUT F/ BOP BODY POOH TO 3800 M CHANGE SAME RIH TO 3861 M, W/ 15-30 BPHL.TILL M.N.	24.0	109.00	3891
111	Hold pre-job safety meeting,Rig Up WL & Pressure Test,RIH CCL & Dummy Gun,POOH & Rig Down.	Completion		FH-Sb	4180		13.5	0.56	95.1	0.6	14.9	0.62	104.9	CONN TDS TO STRG @3861M, OBS PRESS UP STRG TRY TO UNPLUG STRG NO SUCC POOH TO 1623 M , TRY TO UNPLUGGED "NO SUCC." SUP & CUT 100FT D.LINE RIH TO 1880M TRY TO CIRC MUD OBS PLUGGED STRG POOH TO SURF. OBS FLAPPER OF FLOAT VALVE IS BROKEN + 4 NOZZL. PLUGGED , UNPLUGGED BITTILL M.N.	24.0	110.00	3891
112	Rig Up for Perforation,RIH String (Firing head & shooting CCL+Guns),Correlate Depth,Shooting the gun,POOH String & RIH again to Perforate all the Depths then Rig Down	Completion		FH-Sb	4180		96.0	4.00	99.1	4.4	105.6	4.40	109.3	M/U & RIH W/ 12-1/4" PDC BIT & SAME BHA TO 3891M W/25-35BPHL RESUME DRLG 12-1/4"H.S TO 3893M W/20-30 BPHL CONT DRLG TO 3895M MEANWHILE DECREASE MW TO 80 PCF, PUMP LCM PILL & ADD LST CHIPS (8 SXS/HR) TO ACTIVE MUD SYSTEM, INCREASE LOSSES TO 80-90 BPH. DECIDED TO POOH TO 3380M MEANWHILE PUMP & SPOT 100 BBL 40 PPB LCM PILL @ 3595, 3500 & 3385M W/70-90 BPHL	24.0	111.00	3895
113	Rig Up WL & Pressure Test,RIH CCL & Dummy Gun to cross checking perforated intervals,POOH & Rig Down.	Completion		FH-Sb	4180		13.0	0.54	99.7	0.6	14.3	0.60	109.9	CONT POOH W/ 12 1/4" PDC BIT TO 1210M MEANWHILE SPOT LCM PILL @ 3595, 3500, 3385 & 1648M. OBS THE WELL @1648(13 3/8" CSG SHOE), 50BPHL. STOP POOH OPERATION DUE TO HIGH WIND SPEED MEANWHILE CIRC CWH & OCCASIONALLY PUMP THRU STRING W/ 70-90 BPHL.	24.0	112.00	3895
114	Change Ram, Install shooting nipple, R/U WL Eq. RIH WL with CCL/GR Log to confirm Perforated intervals, POOH and R/D Logging Eq, change R/U and M/U 5-7/8" Mill and 7" Scraper. RIH to Perforation depth while Scrap 7" PKR setting depth interval, CBU. Displace well volume with CaBr2 Completion fluid.	Completion		FH-Sb	4180		10.0	0.42	100.1	0.5	11.0	0.46	110.3	CONT POOH TO SURF WHILE CIRC CWH W/70-90 BPHL. B/O 12 1/4" PDC BIT. RIH W/ 8 3/8" C.CUT BIT TO 3100M. PUMP 160 BBL 140 PPB HI-VIS LCM PILL (MICA C & M: 35 PPB / 1ST CHIPS C & M: 35 PPB / SHELL FISH C & M: 40 PPB / FIBER LOCK: 30 PPB).	24.0	113.00	3895
115	Perforate the well as per program, RIH to Perforation depth while Scrap 7" PKR setting depth interval, CBU. Displace well volume with CaBr2 Completion fluid.	Completion		FH-Sb	4180		36.0	1.50	101.6	1.7	39.6	1.65	112.0	POOH W/ 8 3/8" C.CUT BIT TO SURF. WHILE PUMP 220 BBL 140 PPB HI-VIS LCM PILL @ 1648M, 6-7S BPHL. CHANGE TOP RAMS TO 9 5/8" & TEST IT. OK. R/U CSG RUNNING EQUIP. RIH 34 JTS CSG 9 5/8" (53.5#, 110SS, HSM-3) TO 405M. F/U THE STRG, OBS PLUGGED., TRY TO UNPLUG STRG W/ 3 STAGES W/ APPLY PRESS: 550, 700PSI & 1000PSI, SUCC. CIRC MUD W/ 20-30 BPHL.	24.0	114.00	3895
116	POOH to surface while L/D all Tubulars.	Completion		FH-Sb	4180		63.0	2.63	104.2	2.9	69.3	2.89	114.9	CONT RUN 9 5/8"CSG (53.5#, 110SS, HSM-3) F/ 400 TO 2150M (TOTALLY 180JTS) & INSTALL CENTRALIZERS AS PER TALLY SHEET WHILE F/U THE STRG & BREAK CIRC EVERY 5JTS, 10-15BPHL @ RT	24.0	115.00	3895
117	BOP Test.	BOP TEST		FH-Sb	4180		6.0	0.25	104.5	0.3	6.6	0.28	115.2	CONT RUN 9 5/8"CSG (53.5#, 110SS, HSM-3) F/ 1650 TO 3700M MEANWHILE F/U STRING & BREAK CIRC EVERY 10STS, CONT RUN 9 5/8"CSG (53.5#, 110SS, HSM-3) AS WASH DOWN F/ 3700 TO 3800M (TOTALLY 319JTS) & INSTALL CENTRALIZERS AS PER TALLY SHEET, 4-6BPHL @ RT	24.0	116.00	3895
118	R/U Completion running Eq, Run 4-1/2" + 3-1/2", 10K Completion string as per program, R/D completion running Eq.	Completion		FH-Sb	4180		140.0	5.83	110.3	6.4	154.0	6.42	121.6	CONT RUN 9 5/8"CSG (53.5#, 110SS, HSM-3) F/ 3849 TO 3760M, CONT RUN 9 5/8"CSG (53.5#, 110SS, HSM-3) AS WASH DOWN W/ 3860, F/U 3895M (BTM) (TOTALLY 227JTS), TAG BTM, POOH TO 3849.5M, CIRC. OBS FLUID INSIDE PIPES, CSG MEANWHILE PREPARE & MIXED CMT SOLUTIONS, INSTALL CMT HEAD, PLUG, ALIGNED TUNDISH, PERFORM 5 5/8" CSG CMT JOB AS:	24.0	117.00	3895
119	Install BPV in TBG Hanger, N/D BOPs,N/U X-mas Tree, perform required test as per program,	Completion		FH-Sb	4180		40.0	1.67	112.0	1.8	44.0	1.83	123.4	CONT PERFORM 9 5/8" CSG CMT JOB AS: CONT DISP. CMT W/ 905BBL DRLG FLUID 80PCF, OBS BUMPING W/ 1930 TO 2050PSI FOR 5MIN (NOT PERFORM CIT), CHECK BACK FLOW, OK. GOT 230BBL CONTAMINATED CMT (80-90 PCF) & 175BBL GREEN CMT SLURRY (95 PCF) ON RETURN & TOTALLY 308BLL LOSSES DURING DISPLACE, DRAIN & FLUSH BOP STACK & CHS, F/U BOP STACK,	24.0	118.00	3895
120	Secure the well by set BPV in TBG Hanger, close all X-mas Tree valves except BMV, Release the Rig.	Completion		FH-Sb	4180		10.0	0.42	112.4	0.5	11.0	0.46	123.9	INSTALL BOP STACK, PERFORM BOP PRESS TEST AS NIOC POLICY MEANWHILE RECTIFY SEVERAL LEAKAGES, OK., RIH 8-3/8" PDC BIT (NEW, BEST, M433, 7 BLADE, 13MM, 7 X 14/32" NZL) TO 3200M @ RT	24.0	119.00	3895
121	R/U Slick Line, Set protection sleeve in TRSSSV, R/D Slick Line.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT RIH 8-3/8" PDC BIT (NEW, BEST, M433, 7 BLADE, 13MM, 7 X 14/32" NZL) TO 3867.5M, TOOK WEIGHT, START D/O SOFT TO MED CMT F/ 3867.5 TO 3895M MEANWHILE D/O TOP PLUG & 9 5/8" CSG FLOAT COLLAR & 9-5/8" CSG FLOAT SHOE, COMMENCE DRLG 8 3/8" H.S F/ 3895 TO 3924M, NL-NG @ RT	24.0	120.00	3910
122	R/U CTU, Stimulation and Well Testing Eq. RIH w/ CT to 8m, displace the well with Diesel, POOH CT to surface.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT DRLG 8 3/8" H.S F/ 3910 TO 3928M, PUMP 40 BBL HI-VIS PILL, POOH TO 3856M, PERFORM FIT 8-3/8 HS W/ APPLY 2260PSI PRESS STEPWISE (EMW:105PCF), PREPARE 1000BBL 100PCF CACO3/POLYMER MUD, DISPLACE THE WELL W/ 100PCF LIMESTON MUD, RESUME DRLG 8-3/8" HS F/ 3928 TO 3945M MEANWHILE INCREASE MW F/ 100 TO 101PCF, 0-2 BPH LOSSES @ RT	24.0	121.00	3928
123	R/U Slick Line, Retrieve protection sleeve from TRSSSV, R/D Slick Line.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	RESUME DRLG 8-3/8" HS F/ 3928 TO 3963M MEANWHILE INCREASE MW F/ 100 TO 102PCF @ 2 STAGE, 6-8BPL, DUE TO OBS INCREASE LOSS FORMATION & LACK OF MUD MATERIAL, SPOT 20BBL LCM PILL 20PPB (1ST CHIPS F & M) @ 3963M, POOH TO 3772M, CIRC MUD W/ MW-FLOW RATE (APPROX 1-5BHS), 128BL LOSSES, REC. MUD MATERIAL, RIH TO 3837M, CIRC MUD W/ MW-FLOW RATE (2-3BPHL) MEANWHILE INC MW TO 102.5PCF, 2BPHL, RUN BACK TO BTM, RESUME DRLG 8-3/8" HS F/ 3963 TO 3983M, 1-2BPHL MEANWHILE WORK ON MUD RHEOLOGY @ RT (WHILE DRLG OBSERVE TDS HIGH TORQUE FLUCTUATION)	24.0	122.00	3964
124	Flow the well as Pre-Acid clean up till acceptable BSW and reading stable flow rate on 2 different choke size for 72 hrs.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT DRLG 8-3/8" HS F/ 3964 TO 4108M, 1-2BPHL MEANWHILE WORK ON MUD RHEOLOGY @ RT (WHILE DRLG OBSERVE TDS HIGH TORQUE FLUCTUATION)	24.0	123.00	4076
125	R/U Slick Line, Set protection sleeve in TRSSSV, R/D Slick Line.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT DRLG 8-3/8" HS F/ 4076 TO 4180M (TD) (WHILE DRLG OBSERVE TDS HIGH TORQUE FLUCTUATION), CBU DUE TO W.S.GEOLOGIST REQUEST TO CONFIRM TD & 7" LNR POINT, POOH W/ SOFT TO MED B/R F/ 4180 (TD) TO 4120M, CONT POOH 8-3/8" PDC BIT TO 3820M ON ELEVATOR, SLOW CIRC & MONITOR PIT LEVEL; 0-1BPHL, RUN BACK TO 4080M ON ELEVATOR, SOFT WASH & REAM TO 4180M (TD), 2BPHL @ RT	24.0	124.00	4180
126	RIH w/ CT and perform Acid Wash as per program, POOH CT to surface.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT POOH 8-3/8" PDC BIT F/ 3980 TO 3820M ON ELEVATOR, SLOW CIRC & MONITOR PIT LEVEL; 0-1BPHL, RUN BACK TO 4080M ON ELEVATOR, SOFT WASH & REAM TO 4180M (TD), PUMP 40BBL HI-VIS PILL & CBU TO CLEAN THE WELL, SPOT 50BBL HI-VIS PILL, POOH 8-3/8" PDC BIT F/ 4180M (TD) TO SURF. RET. WEAR BUSHING, L/D MOUSE HOLE, INSTALL 7" SHOOTING NIPPLE, R/U WIRE LINE LOGGING EQUIP., PRESS TESTED W.L BOP USING SHOOTING NIPPLE WITH 1000 PSI/ 10MIN OK., PERFORM LOGGING (FULL SUITE/CDR/GR LOGS); RUN SONIC/DLL/MSFL/CDR-GR AS RUN#1 TO 4000M, 28PHL @ RT	24.0	125.00	4180
127	R/U Slick Line, Retrieve protection sleeve from TRSSSV, R/D Slick Line.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	INSTALL 7" SHOOTING NIPPLE, R/U WIRE LINE LOGGING EQUIP., PRESS TESTED W.L BOP USING SHOOTING NIPPLE OK., PERFORM LOGGING (FULL SUITE/CDR/GR LOGS); RUN SONIC/DLL/MSFL/CDR-GR AS RUN#1 TO 4000M (BTM), LOG UP F/ 4180 TO 3895M, REPEAT THE LOG, POOH TO SURF., RUN LOG LDT/CNT/NGS AS RUN#2 TO 3895M (9-5/8" CSG SHOE), LOG DOWN TO 4180M (BTM), LOG UP F/ 4180 TO 3895M (OBS ABNORMAL TENSION F/ 3974 TO 3900M), POOH TO SURF. RUN LOG SBT/CCL/VDL-GR TO 1648M (13-3/8" CSG SHOE). LOG DOWN TO 3895M (9-5/8" CSG SHOE). LOG UP F/ 3895 TO 3000M. OBS FAILURE OF LOGGING TOOLS. POOH TO SURF. WORK ON TROUBLESHOOTING & RECTIFY LOGGING TOOLS & RECHECKED, N.GOOD, R.T	24.0	126.00	4180
128	Flow the well as Post-Acid clean up till acceptable BSW and reading stable flow rate on 2 different choke size for 96 hrs.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT RUN LOG SBT/VDL/CCL-GR F/ 700 TO 1648M (13-3/8" CSG SHOE). LOG DOWN TO 3895M (9-5/8" CSG SHOE). LOG UP F/ 3895 TO 3300M. OBS FAILURE OF LOGGING TOOLS. POOH TO SURF. TRY TO TROUBLESHOOTING & RECTIFY LOGGING TOOLS, NO SUCC, USE BACK UP TOOLS, RUN LOG SBT/VDL/CCL-GR TO 3360M. LOG UP F/ 3360 TO 1648M (13-3/8" CSG SHOE). POOH TO SURF. L/D LOGGING TOOLS & EQUIPMENT, M/U R 8-3/8" PDC BIT (BEST, USED, 7BLADE, M433, 13MM, 7*14/32" NZL) + 6 1/2" 8.SUB, RIH 4S COND. TRIP TO 3200M, 0-1BPHL @ RT	24.0	127.00	4180
129	R/U Slick Line, Set protection sleeve in TRSSSV, R/D Slick Line.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT RIH USED 8 3/8" PDC BIT AS COND. TRIP F/ 1250 TO 4180M (TD), (WASH DOWN F/ 3867 TO 3954M, WASH & REAM DOWN F/ 4058 TO 4180M), PUMP 50BBL HI-VIS PILL & CBU, SPOT 60BBL HI-VIS PILL, POOH 8-3/8" PDC BIT F/ 4180M (TD) TO SURF. R/U 7" TUBULAR RUNNING EQUIPMENT, M/U 7" REAMER F.SHOE, RIH 7 JTS 7" LINER (35#, TP110SS, TPCQ), M/U 7" F.COLLAR, RIH 1 JT 7" LINER (35#, TP110SS, TPCQ), M/U 7" LDC AND CONT RUNNING 7" LINER (35#, TP110SS, TPCQ) AS PER PROGRAM & TALLY SHEET TO 50M (TOTALLY 41JTS 7" LNR), 0-1BPHL @ RT	24.0	128.00	4180
130	RIH w/ CT to 8m, displace well with Diesel, POOH CT to surface, R/D CTU and well Testing Eq.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT RUN 7" LINER (35#, TP110SS, TPCQ), M/U 7" F.COLLAR, RIH 1 JT 7" LINER (35#, TP110SS, TPCQ) AS PER PROGRAM & TALLY SHEET TO 50M (TOTALLY 41JTS 7" LNR), M/U 7" BOT HYDRO MECHANICAL SET LINER HANGER ASSEMBLY TO 397M (TIE-BACK ID: 7 3/8", TIE-BACK PBR LENGTH: 2.12M), CONT RIH 7" LNR & ASSY. FOLLOWED BY 5" DPS TO 4180M (TD) WHILE PASS RABBIT THRU ALL DRILL PIPES, TAG BTM, RECORD WT UP & DOWNWARD (0.5M OFF BTM), DROP BALL, ESTABLISH CIRC. TILL BALL SEATED ON LDC, SET LINER HANGER W/ INCREASE SLOWLY PRESS. TO 2000PSI & IN THE FUTURE INCREASED LDC BY APPLY 2700PSI, RELEASED SETTING TOOLS, M/U CMT MANIFOLD (LOADED DART), CIRC. MUD THRU STRING AS 1.5 CAP OF STRING, L/UP CMT LINE & PRESS TEST SAME W/ 3000PSI, OK., PUMP 15BBL CHEMICAL WASH AS SPACER, PUMP CMT SLURRY (S.V: 52BBL, S.W: 118PCF), RELEASE DART & DISP. CMT SLURRY W/ TOTALLY 253BBL DRLG FLUID 103PCF MEANWHILE OBS SHEARING (213BBL & 300BBL), PLUG LANDED & SHEARED AT 2200PSI, RELEASED PRESS, FLOAT EQUIP. HOLDING OK, R/U CMT HEAD, UNSCREW CMT LINE, PULL OUT SOME STRING, CIRCULATE OUT EXCESS CMT, L/D CMT HEAD, UNSCREW STRING ON WEIGHT INDICATOR, SCHLUMBERGER LINER HANGER SETTING TOOLS	24.0	129.00	4180
131	R/U Slick Line, RIH w/ SL and Install Plug and Prong into NO-GO L.NPL., POOH.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT RIH 7" LNR & ASSY. FOLLOWED BY 5" DPS TO 4180M (TD), TAG BTM, RECORD WT UP & DOWNWARD (0.5M OFF BTM), DROP BALL, ESTABLISH CIRC. TILL BALL SEATED ON LDC, SET LINER HANGER W/ INCREASE SLOWLY PRESS. TO 2000PSI & IN THE FUTURE INCREASED LDC BY APPLY 2700PSI, RELEASED SETTING TOOLS, M/U CMT MANIFOLD (LOADED DART), CIRC. MUD THRU STRING AS 1.5 CAP OF STRING, L/UP CMT LINE & PRESS TEST SAME W/ 3000PSI, OK., PUMP 15BBL CHEMICAL WASH AS SPACER, PUMP CMT SLURRY (S.V: 52BBL, S.W: 118PCF), RELEASE DART & DISP. CMT SLURRY W/ TOTALLY 253BBL DRLG FLUID 103PCF MEANWHILE OBS SHEARING (213BBL & 300BBL), PLUG LANDED & SHEARED AT 2200PSI, RELEASED PRESS, FLOAT EQUIP. HOLDING OK, R/U CMT HEAD, UNSCREW CMT LINE, PULL OUT SOME STRING, CIRCULATE OUT EXCESS CMT, L/D CMT HEAD, UNSCREW STRING ON WEIGHT INDICATOR, SCHLUMBERGER LINER HANGER SETTING TOOLS	24.0	130.00	4180
132	RIH w/ SL and Retrieve protection sleeve from TRSSSV, R/D Slick Line.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	RIH 8-3/8" PDC BIT (BEST, USED, 7BLADE, M433, 13MM, 7*14/32" NZL) & D/OUT BHA TO 3650M, TOOK WEIGHT, START D/O SOFT TO HARD CMT F/ 3650 TO 3786M, CONFIRMED 7" LNR @ 3786M, PUMP HI-VIS PILL AND CIRCULATED TILL SHAKERS CLEAN, POOH 8-3/8" PDC BIT F/ 3786 TO 1225M, NL-NG @ RT	24.0	131.00	4180
133	Secure the well by set BPV in TBG Hanger, close all X-mas Tree valves except BMV, Release the Rig.	Completion		FH-Sb	4180		Rig Loss	0.00	112.4	0.0	0.0	0.00	123.9	CONT POOH W/ 8-3/8" PDC BIT F/ 3300M TO SURF., L/D IT , PERFORM BOP PRESS TEST "OK" , M/U 5 7/8" R.BIT & CLEAN OUT BHA TO 370 M W/ NL-NG.	24.0	132.00	4180
	Total Duration of 8-1/2" Hole Section:							**37.4**	**112.4**		**41.1**	**123.9**

Item No.	Drilling and Completion Operation TBD of Well: F-20	IADC Code	Interval (meters)	Formation	Depth (meters)	ROP Average (M/Hr)	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (%)	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	Actual Operation	Hour	Cum. Time/Day	Depth (m)
	NOTE:													CONT. POOH WITH CLEAN OUT BHA F/ 3600M TO SURF. M/UP & RIH BY S-7/8" TRI-CONE BIT WITH 7" & 9-5/8" SCRAPER AS TANDEM BHA TO 3800M TILL MN.	24.0	134.00	4180
134	Total Duration for Cut & Slip DL in all hole section.	Cut & Slip		FH	4180		12.0	0.50	112.9	0.6	13.2	0.55	124.4	CONT. POOH TO SURF., L/D 5 7/8"BIT & SCRAPERS MEANWHILE SLIP & CUT D.LINE RIH W/ 7" DRY TEST BHA TO 185M F/UP STRG W/ CUSHION FLUID W/ 62.4 PCF F.WATER AS PROGRAM W/ NL-NG.	24.0	135.00	4180
135	Total Duration for Rig Service (Consider 0.5hr per day) in all hole section.	Rig Service		FH	4180		26.0	1.08	114.0	1.2	28.6	1.19	125.6	CONT. DRY TEST TOOLS AND RIH F/ 185 20 1650M. SLIP & CUT DRILLING LINE. RESUME RIH TO 3224M. @R.T.	24.0	136.00	4180
	Total Duration of F-20 Well:			FH	4180				114.0				125.6	CONT. RIH W/ DRY TEST TOLS F/ 3224 TO 3734M. SET PKR.@3730M, PERFORM 7" L.LAP DRY TEST (3HRS OPEN & 6 HRS CLOSE POSITION).DROP BAR REV. CIRC. TO BALANCE MUD POOH F/ 3734 TO 2300M TILL MN.	24.0	137.00	4180
	Contingency Plans TBD of Well: F-20	IADC Code	Internal (meters)	Formation	Depth (meters)	ROP	Time Duration (Hours)	Time Duration (Days)	Total Duration (Days)	Contingency (%)	Time Duration w/ contingency (Hours)	Time Duration w/ contingency (Days)	Total Duration w/ contingency (Days)	CONT. POOH F/ 2300M TO SURF. L/D 7" DRY TEST TOOLS , CHANGE TOP RAMS , INSTALL SHOOTING NIPPLE , PRESS TEST !! "OK", RIH W/ RUN SBT/VDL/CCL/GR LOGGING TOOLS TO 3772M., TRY TO PASS "NO SUCC", RIH AS DUMMY RUN TO 2700M, NL-NG.	24.0	138.00	4180
										10				CONT. RUN 2 JTS 4 1/2" BLANK GUN AS DUMMY RUN F/2700 TO 3770M, TRY TO PASS "NO SUCC", POOH TO SURF. L/D W.LINE TOOLS, RIH W/ 5 7/8" MT.BIT & CLEAN OUT BHA TO 4141M (TOP OF 7" LDC) WHILE WASH DOWN F/3650M IN GOOD CONDITION, CBU & UNIFORM MW WHILE WORK ON MUD RHEOLOGY W/NL-NG. SPOT 30 BBL NON SOLID PERF. FLUID (CABR2 95 PCF). POOH TO 3450M WHILE F/U HOLE W/NL-NG.	24.0	139.00	4180
	Based on operation situation in each step, the following contingency plans might be followed													CONT. POOH F/3450M TO SURF., L/D 5 7/8" MT.BIT. RUN LOGGING TOOLS (CCL/GR/SBT/VDL) TO 4138.5M (3M ABOVE LDC), LOG UP F/4138.5 TO 3750M, RUN BACK AGAIN & REPEAT LOG F/4125M TO 4000M. POWER OFF TOOLS. POOH & R/D LOGGING TOOLS & EQUIP., WAIT ON DAYLIGHT DUE TO EXPLOSIVE MATERIAL SAFETY REGULATION; NL-NG.	24.0	140.00	4180
136	Contingency plan #1 POOH to Surafce to change PDC Bit, P/U & M/U TCI Bit & RIH to	Drilling		FH-5b	4180		115.0	4.79	4.8	5.3	126.5	5.27	5.3	CONT. WAIT ON DAYLIGHT & WEATHER DUE TO EXPLOSIVE MATERIAL SAFETY REGULATION; PERFORM PERFORATIG AS PROGRAM W/ 4.5" WCP HSD GUN ASSY. (PHASING:72 DEG.) IN TWO RUN SUCCFULLY (PERF. INTERVALS:4075.91-4082M & 4074.5-4075.91M), WAIT ON DAYLIGHT WHILE CIRC. ACROSS WELL HEAD; NL-NG.	24.0	141.00	4180
137	Contingency plan #2 Perform scraper trip, RIH with 9-5/8" Dry test BHA, RIH to L.Lap @ +/- 3815m, Perform 7" Liner lap Dry Test (based on fahliyan Reservoir Datum Pressure), POOH.	Testing		FH-5b	4180		429.0	17.88	17.9	19.7	471.9	19.66	24.9	CONT. WAIT ON DAYLIGHT & WEATHER DUE TO EXPLOSIVE MATERIAL SAFETY REGULATION; PERFORM PERFORATIG AS PROGRAM W/ 4.5" WCP HSD GUN ASSY. (PHASING:72 DEG.) AS THIRD RUN SUCCFULLY (PERF. INTERVALS:4067.5-4070.5M), STOP OPERATION DUE TO CLOUD & RAINY WEATHER, WAIT ON DAYLIGHT WHILE CIRC. ACROSS WELL HEAD; NL-NG.	24.0	142.00	4180
	Total Duration of Contingency Plan F-20 Well:								22.7				24.9	CONT. WAIT ON DAYLIGHT DUE TO EXPLOSIVE MATERIAL SAFETY REGULATION; PERFORM PERFORATIG AS PROGRAM (RUN 4th & 5th & 6th) W/ 4.5" WCP HSD GUN ASSY. (PHASING:72 DEG.) SUCCFULLY (PERF. INTERVALS:4063-4066M & 4057-4061.4M & 4038.9-4045M), WAIT ON DAYLIGHT WHILE CIRC. ACROSS WELL HEAD; NL-NG.	24.0	143.00	4180
														CONT. WAIT ON DAYLIGHT; PERFORM PERFORATIG AS PROGRAM (RUN 7th & 8th & 9th) W/ 4.5" WCP HSD GUN ASSY. (PHASING:72 DEG.) SUCCFULLY (PERF. INTERVALS:4032.82-4038.9M & 4029-4032.8M & 4015.5-4019.5M), R/D LOGGING EQUIP. W/NL-NG. BOP TEST TO 4200 PSI,OK.	24.0	144.00	4180
														RIH 5-7/8" M.M I.MILL (CYLANDERSAZI, USED, 5* 12/32" PORT) & 4-3/4" BIT SUB (FLOAT IN) TO 4132M (9M ABOVE 7" LDC), CBU, M/U FOSV ON STRING. L/U CMT LINE TO STRING, PRESS TEST CMT LINE W/ 3500 PSI; "OK". DISPLACE WHOLE WELL @ 4132M W/ 870 BBL 104 PCF NON-SOLID COMPLETION FLUID CABR2 (GOT 40 BBL CONTAMINATED W/ MUD ON RETURN), NL-NG @ RT	24.0	145.00	4180
														CONT CBU @ 4132M (9M ABOVE 7" LDC), PRESS TEST CMT LINE W/ 3500 PSI; "OK". DISPLACE WHOLE WELL @ 4132M W/ 870 BBL 104 PCF NON-SOLID COMPLETION FLUID CABR2 (GOT 40 BBL CONTAMINATED W/ MUD ON RETURN), CLOSE FOSV, FLOW CHECK THE WELL; "STATIC", POOH 5 7/8" M.M I.MILL F/ 4132 TO 1500M MEANWHILE TOTALLY L/D 280 JTS 5"DP IT BY IT, NL-NG @ RT	24.0	146.00	4180
														CONT POOH 5 7/8" M.M (.MILL F/ 2400M TO SURF MEANWHILE TOTALLY L/D ALL PIPES, RET. W.BUSHING, R/U TUBULAR RUNNING EQUIPMENT, R/D & L/D COMPLETION TOOLS OF DE-COMPLETED FROM AZNS-122, RUN COMPLETION STRING AZNS207 AS PER PROGRAM & TALLY SHEET: M/U 3 1/2" WIRELINE RE-ENTRY GUIDE SHOE (10.2ft, HSM-3, ID: 2.922", WEIQIXIN) + 3 1/2" BTM NO-GO L.NIPPLE (10.2ft, HSM-3, SEAL BORE: 2.562", XN PROFILE, WEIQIXIN) + 3 1/2" PUP JT (10.2ft, L80, HSM3), RIH W/ 1 JT 3 1/2" TBG (10.2ft, L80, HSM-3) + 7" HYDRAULIC SET PERMANENT PACKER (MIN ID: 2.922", SUITABLE FOR 35 PPF CSG, WEIQIXIN) + 3 1/2" ANCHOR SEAL (MIN ID: 2.922",	24.0	147.00	4180
														CONT B/O & L/D COMPLETION TOOLS OF DE-COMPLETED FROM AZNS-122, RUN COMPLETION STRING AZNS207 AS PER PROGRAM & TALLY SHEET: M/U 3 1/2" WIRELINE RE-ENTRY GUIDE SHOE (10.2ft, HSM-3, WEIQIXIN) + 3 1/2" BTM NO-GO L.NIPPLE (10.2ft, HSM-3, WEIQIXIN), RIH W/ 1 JT 3 1/2" TBG (10.2ft, L80, HSM-3) + 7" HYDRAULIC SET PERMANENT PACKER (MIN ID: 2.922", 35PPF, WEIQIXIN) + 3 1/2" ANCHOR SEAL (MIN ID: 2.922", RATCH LATCH TYPE, WEIQIXIN) + 1 JT 3 1/2" TBG (10.2ft, L80, HSM-3) TO 29M. R/U SLICK LINE. RUN 2.75" GAUGE RING TO NO-GO DEPTH & CHECK ALL CONNECTIONS. OK. CONT. RIH W/ 3 1/2" SSD (CLOSE POSITION, DOWNWARD OPEN) + 1	24.0	148.00	4180
														CONT RUN COMPLETION STRING AS PER PROGRAM & TALLY SHEET: CONT RUN 3-1/2" X 4-1/2" COMPLETION STRING TO 3470M MEANWHILE PRESS TEST COMPLETION STRING W/ 7000 PSI @1030, 2012 & 3100M : OK.@ RT TOTALLY RUN 12 JTS 3-1/2" TBG (10.2ft, L-80, HSM-3, L-80) & 350 JTS 4-1/2" TBG (18.9ft, L-80, HSM-3, L-80)	24.0	149.00	4180
														CONT RUN COMPLETION STRING AS PER PROGRAM & TALLY SHEET: CONT RUN 3-1/2" X 4-1/2" COMPLETION STRING TO 3470M MEANWHILE PRESS TEST COMPLETION STRING @ 3100M. OK., CONT RUN COMPLETION STRING TO 3810M, M/U 4 1/2" DHSV ASSY & CONNECT 1/4" C/L TO DHSV PORT, APPLY PRESS IN C/L TO 10000PSI & PRESS TEST. OK., KEEP 5000PSI IN C/L, RIH W/ 1JT 4 1/2" TBG TO 3827M, PERFORM DHSV INFLOW TEST, OK, RIH 4 JTS 4-1/2" TBG TO 3867M. APPLY 5200PSI & 5500PSI PRESS IN CLR1&2 AND RUPTURE CIVR1&2 RUPTURE DISK, M/U 4-1/2" FLUTED SWAGE & TBG HGR, M/U 4-1/2" RUNNING & PULLING TOOLS FOR TBG HGR ON HGR. PASS CILS &	24.0	150.00	4180
														PRESS TEST COMPLETION STRING, TBG HGR & L/J W/ 7000 PSI; OK. INSTALL GOLPA. FLANGE & 4-1/16" GATE VALVE ON COMPLETION STRING. R/U SLICK LINE EQUIP. RIH & SET 3.437" PROTECTION SLEEVE IN TRSSV. RETRIEVE 2.75" WFB CHECK VALVE FROM SSD. RIH W/ 2.562" PLUG & 2" PRONG TO NO-GO.NIPPLE DEPTH & SET THEM (2 RUN). RUN 2.8" SHIFTING TOOLS TO CONFIRM SSD IS CLOSE. R/D SLICK LINE EQUIPMENT. L/D GOLPA. FLANGE. SPACE-OUT STRING (1.5M) ABOVE THS. PERFORM SETTING 7" PERMANENT PKR. @ 3861M W/ APPLY PRESS GRADUALLY TO MAX.3500SI AS PER PROGRAM (OBS SET PKR INDICATION) & INCREASE PRESS TO 7000PSI TO TEST	24.0	151.00	4180
														N/D 13-5/8" 10K BOP STACK, 5K ANN PREVENTER & SPACER SPOOL. INSTALL FS SEAL (METAL SEAL) INSIDE TBG HGR NECK, R/U & INSTALL 11" * 4 1/16" 10K B.M.V (MSP DRILEX). PASS 3/8" CILs & 1/4" C/L & CONNECT TO EXIT CAP, L/U PUMP TRUCK & PRESS TEST METAL SEAL & 2WCV W/ 8000/10000 PSI 15/5MIN, OK., PRESS TEST CAVITY W/	24.0	152.00	4180
														8000PSI, OK. PRESS TEST BETWEEN O-RING TBG HGR NECK W/ 8000PSI, OK. PRESS TEST 3/8" CILs W/ 2000 PSI, "OK"., PRESS TEST C/L W/ 10000 PSI, "OK"., INSTALL 4 1/16" 10K SOLID BLOCK, BODY PRESS TEST SAME W/ 8000PSI 15MIN, OK., RET. 4" 10K 2WCV, R/U SLICK LINE & INSTALL LUBRICATOR & BOP'S, INSTALL 3.437" PROTECTION			


Activity Breakdown Table

IADC CODE	OPERATIONS	Actual Hours	Percentage
1	Rig Up/Tear Down/Move	14.00	0.38%
2	Drilling	914.50	24.90%
3	Reaming	226.50	6.17%
4	Coring	0.50	0.01%
5	Circulate & Condition	154.00	4.19%
6	Trips	958.00	26.09%
7	Service/ Maintain Rig	11.00	0.30%
8	Repair Rig	59.00	1.61%
9	Replacing Drill Line	13.00	0.35%
10	Deviation Survey	7.50	0.20%
11	Logging	65.50	1.78%
12	Run Casing/ Liner	171.00	4.66%
13	Cementing	70.50	1.92%
14	Wait on Cement	17.50	0.48%
15	Rig Up/Down BOP	43.00	1.17%
16	Test BOP	33.50	0.91%
17	Drill Stem Test	88.50	2.41%
18	Fishing	228.00	6.21%
19	Specialized Directional Work	231.00	6.29%
20	Operation Status (Waiting)	188.00	5.12%
21	Safety	0.00	0.00%
22	Perforating	40.50	1.10%
23	Completion\ XMT	94.00	2.56%
24	Treating	0.00	0.00%
25	Swabbing	0.00	0.00%
26	Surface Testing	0.00	0.00%
27	Well Control	27.00	0.74%
28	Other	16.00	0.44%
29	Subsea Operation	0.00	0.00%
	Total	3643.00	100.00%

Activity Breakdown Chart

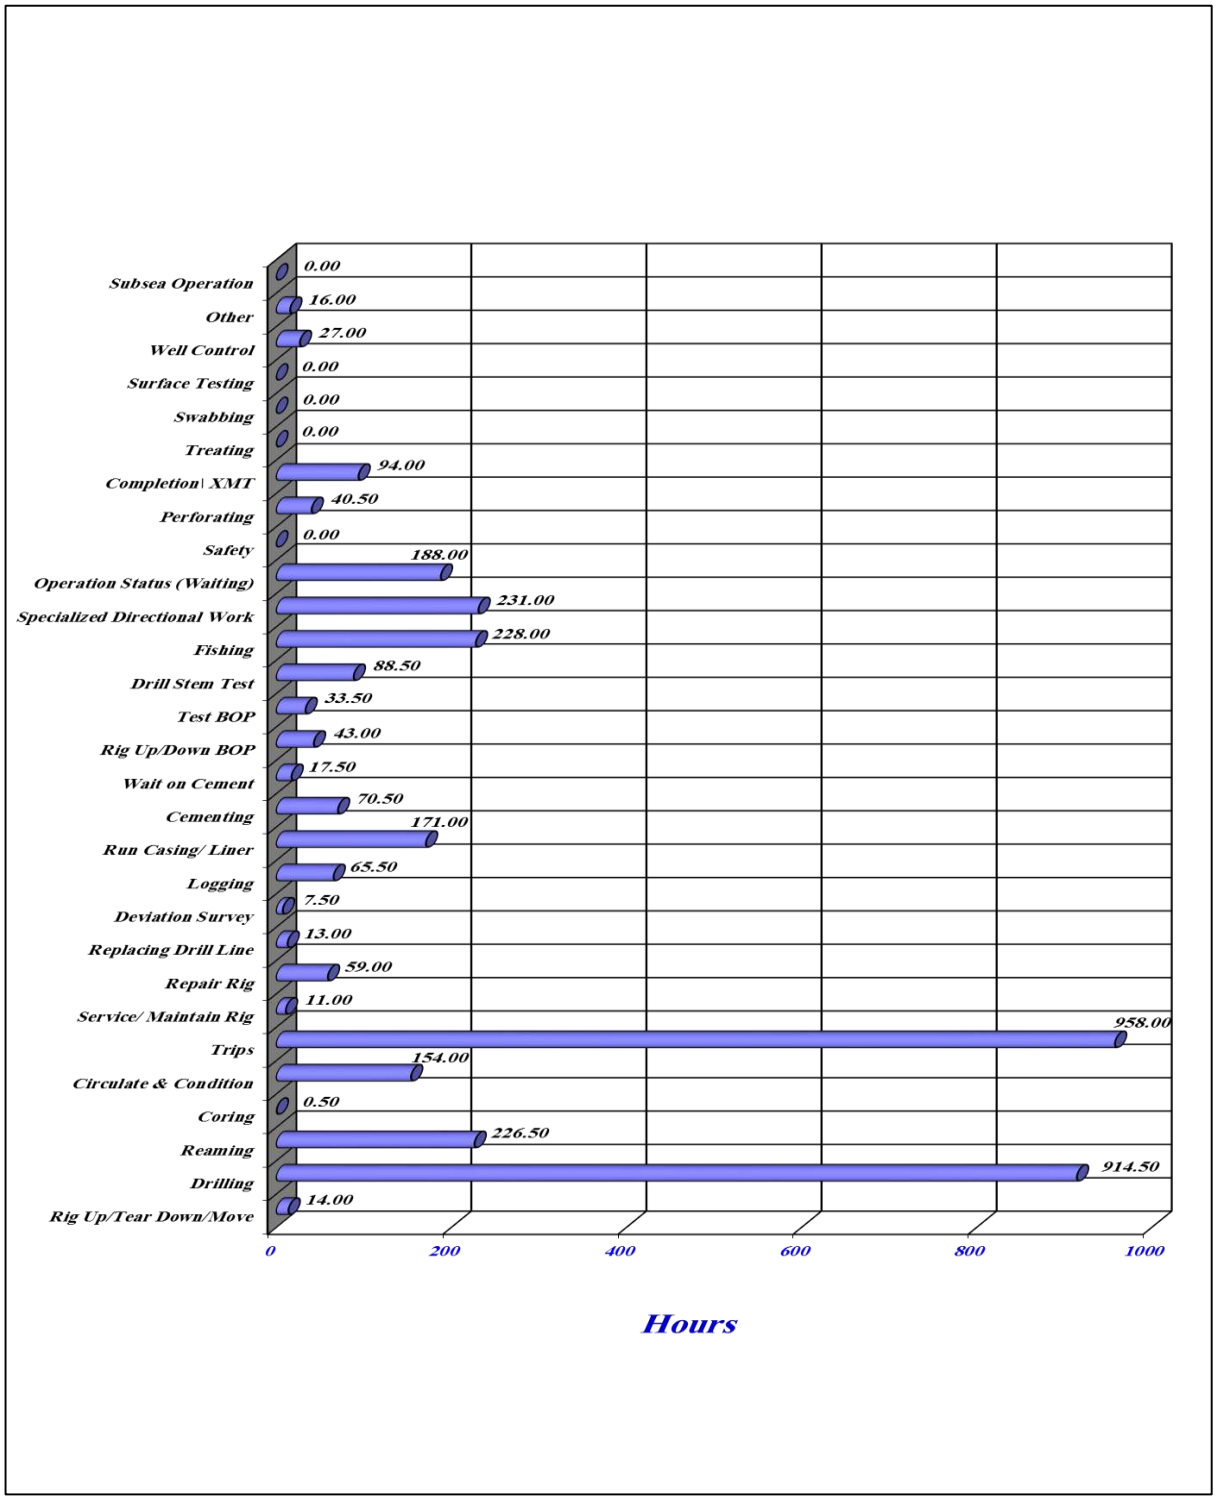

Activity Break down Plot

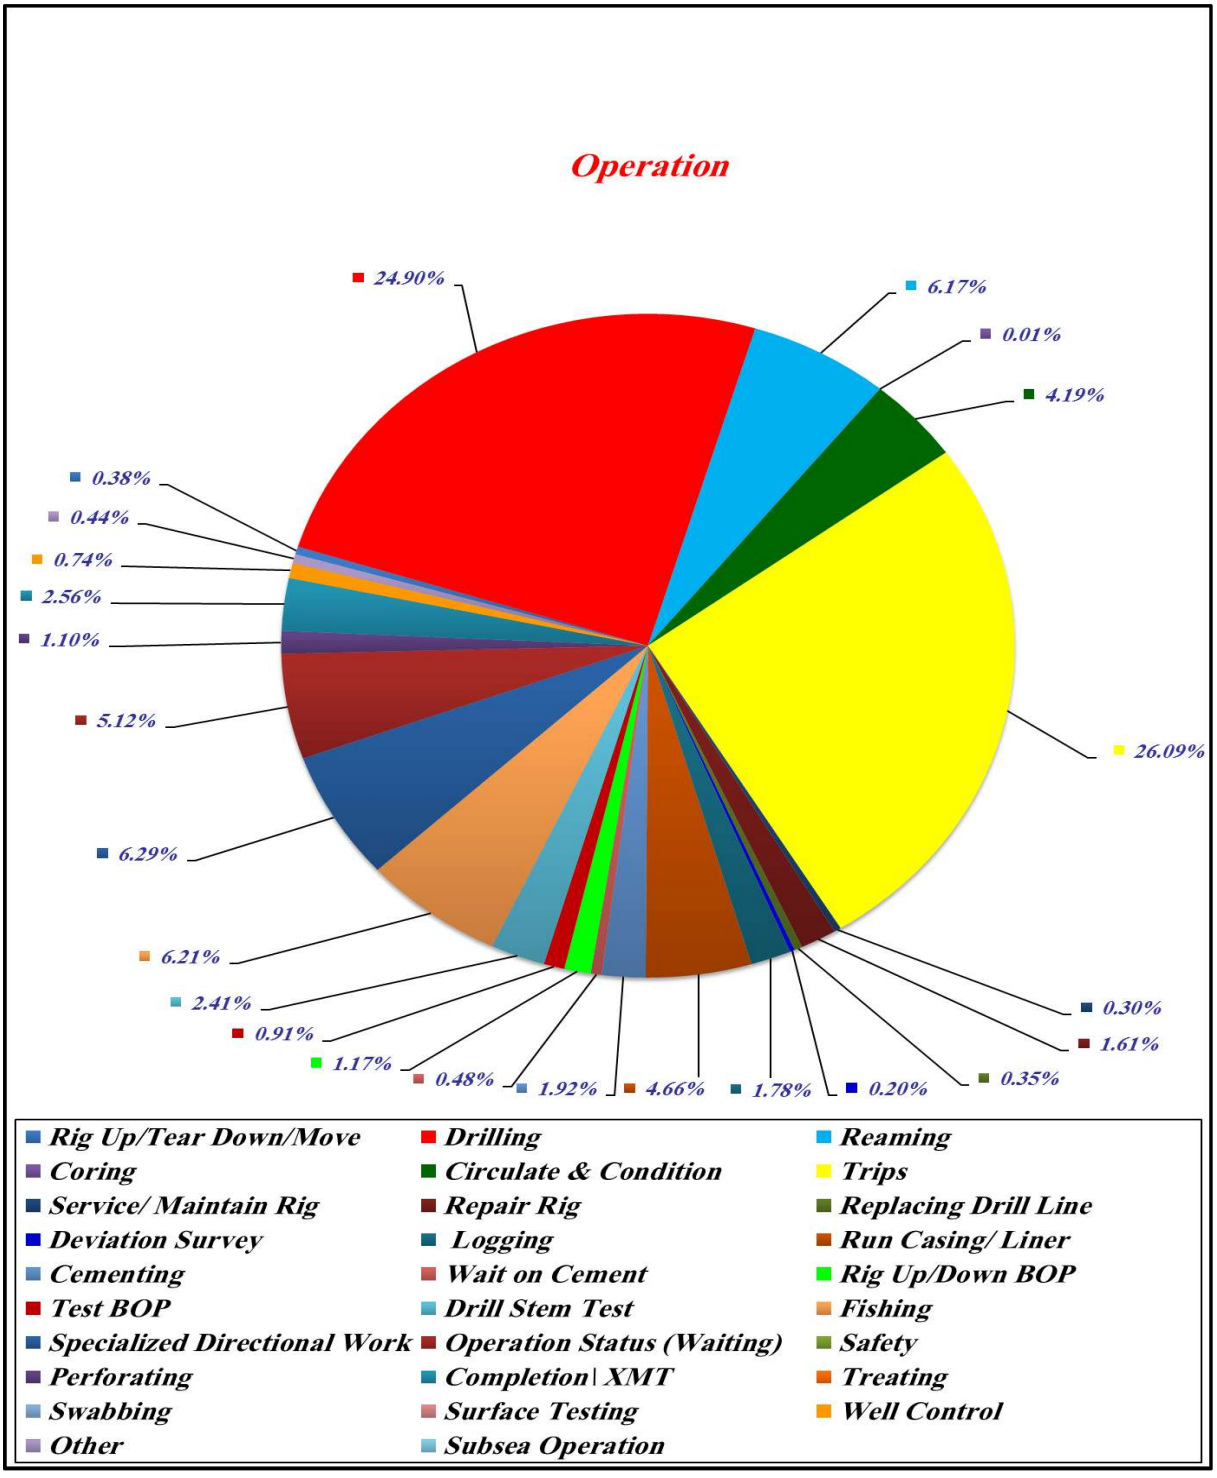

3.3 NPT Break-Down

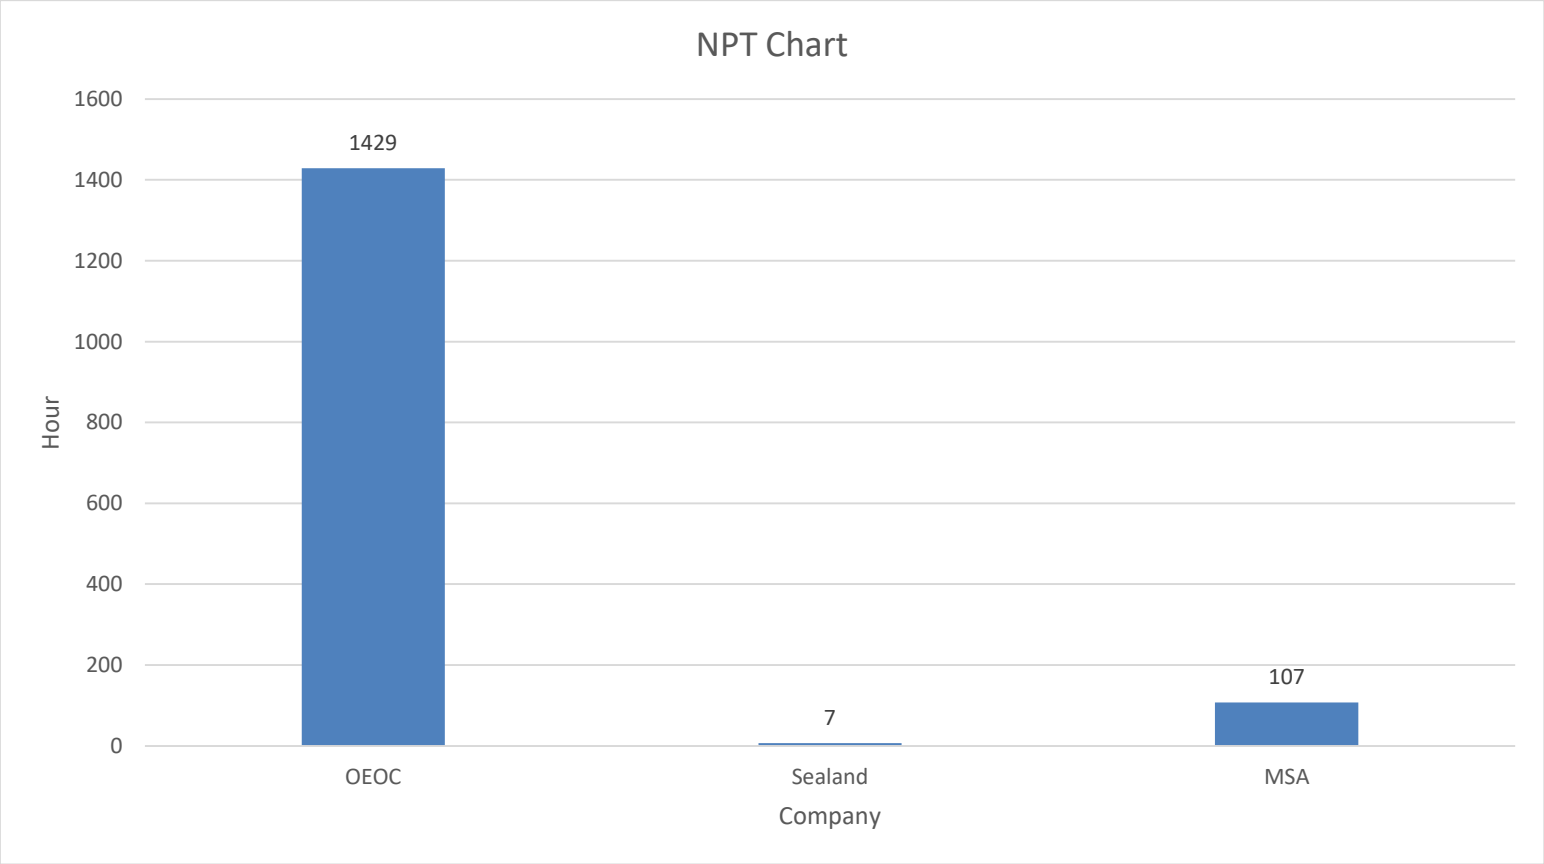


Figure 3-2: AZNS-207 NPT Break-Down Chart

Section	Description	Co.	NPT (hr)	Date
26" Hole Section	DUE TO LOW ROP	OEOC	5.0	1403.07.27
17.5" Hole Section	DUE TO WORK ON TDS	OEOC	4.0	1403.08.08
	LEFT IN HOLE, FISHING	OEOC / MSA	18.0	1403.08.10
	LEFT IN HOLE, FISHING	OEOC / MSA	24.0	1403.08.11
	LEFT IN HOLE, FISHING	OEOC / MSA	24.0	1403.08.12
	LEFT IN HOLE, FISHING	OEOC / MSA	7.0	1403.08.13
	POOH (OUT OF PROGRAM) W/ HARD B/R & SEVERAL TIGHT SPOT (TIGHT HOLE & BAD CONDITION)	MSA	10.0	1403.08.14
	POOH (OUT OF PROGRAM) W/ HARD B/R (TIGHT HOLE & BAD CONDITION)	MSA	8.0	1403.08.15
	RIH (OUT OF PROGRAM) W/ HARD W/R (TIGHT HOLE & BAD CONDITION)	MSA	5.0	
	WORK ON TDS	OEOC	6.0	
	RIH (OUT OF PROGRAM) W/ HARD W/R (TIGHT HOLE & BAD CONDITION)	MSA	5.0	
	RIH (OUT OF PROGRAM) W/ HARD W/R (TIGHT HOLE & BAD HOLE CONDITION)	MSA	24.0	1403.08.16
	TRIP (OUT OF PROGRAM) W/ TIGHT HOLE & BAD HOLE CONDITION	MSA	24.0	1403.08.17
	TIGHT HOLE & BAD HOLE CONDITION (NOT USING KCL IN DRLG MUD)	MSA	24.0	1403.08.18
	TIGHT HOLE & BAD HOLE CONDITION (NOT USING KCL IN DRLG MUD)	OEOC-MSA	24.0	1403.08.19
	LEFT IN HOLE, FISHING	OEOC-MSA	24.0	1403.08.20
	WORK ON FISHING F/ 1531M TO 1539M "NO SUCC"	OEOC-MSA	24.0	1403.08.21
	IN ORDER TAG TOF RIH W/ 17 1/2" B.BIT	OEOC-MSA	24.0	1403.08.22
	IN ORDER TAG TOF RIH W/ 17 1/2" B.BIT	OEOC-MSA	24.0	1403.08.23
	IN ORDER TAG TOF RIH W/ 17 1/2" B.BIT	OEOC-MSA	24.0	1403.08.24
	POOH TO SURF & RIH W/ FISHING TOOLS	OEOC-MSA	24.0	1403.08.25
	RIH W/ 11 3/4" OVERSHOT	OEOC-MSA	24.0	1403.08.26
	RIH W/ 11 3/4" OVERSHOT & POOH TO SURF, RIH 17 1/2" TAPER MILL	OEOC-MSA	24.0	1403.08.27
	RIH 17 1/2" TAPER MILL TO 700M, DUE TO CHANGE PROGRAM POOH TO SURF	OEOC-MSA	24.0	1403.08.28

RIH 8 3/8"C.CUT BIT TO PERFORM CMT PLUG JOB	OEOC-MSA	24.0	1403.08.29
PERFORM REPEAT CMT BALANCE PLUG JOB	OEOC-MSA	24.0	1403.08.30
D/O CMT BALANCE PLUG	OEOC-MSA	24.0	1403.09.01
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.02
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.03
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.04
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.05
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.06
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.07
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.08
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.09
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	24.0	1403.09.10
LEFT IN HOLE, INABILITY TO CATCH FISH, LEAD TO SIDE TRACKING THE WELL	OEOC-MSA	19.0	1403.09.11
DUE TO VERY LOW ROP AGAINST THE PLAN	OEOC-MSA	14.0	1403.09.12
DUE TO OUT OF PROGRAM TRIPPING	OEOC-MSA	6.0	1403.09.12
TRIP DUE TO LOW ROP & DRLG DUE TO LOW ROP	OEOC-MSA	24.0	1403.09.13
DUE TO OBS GRADUALLY DEC PRESS (80 PSI) STOP DRLG, DECIDED TO POOH	OEOC-MSA	2.0	1403.09.14
DUE TO DEC PRESS(80PSI) DECIDED POOH TO SURF & RUN BACK TO BTM	OEOC-MSA	21.5	1403.09.15
DUE TO LOW ROP	OEOC-MSA	20.5	1403.09.16
DELAY IN OPERATION (13 3/8" CSG CMT JOB)	OEOC-MSA	15.0	1403.09.20
DELAY IN OPERATION (13 3/8" CSG CMT JOB)	OEOC-MSA	7.0	1403.09.21
DELAY IN OPERATION	OEOC-MSA	1.0	1403.09.22
DUE TO LOW ROP	OEOC-MSA	6.0	1403.09.24
DUE TO LOW ROP	OEOC-MSA	2.0	
WORK ON IBOP	OEOC-MSA	9.0	1403.09.25

	WORK ON HOLE CONDITION (LOSSES)	OEOC-MSA	23.0	1403.09.29
	WORK ON HOLE CONDITION (LOSSES)	OEOC-MSA	24.0	1403.09.30
	WORK ON HOLE CONDITION (LOSSES)	OEOC-MSA	24.0	1403.10.01
	LOW ROP	OEOC-MSA	11.0	1403.10.03
12 1/4"Hole Section	WAIT ON REC DRLG JAR	OEOC-MSA	24.0	1403.10.04
	WAIT ON REC DRLG JAR + LEAKAGE FROM 4-1/16" STAND PIPE MANIFOLD	OEOC-MSA	16.0	1403.10.05
	DROP 300 PSI SPP	OEOC-RIG	6.0	1403.10.11
	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	24.0	1403.10.12
	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	24.0	1403.10.13
	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	5.0	1403.10.14
	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	10.0	1403.10.17
	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	24.0	1403.10.18
8 1/2" HOLE SECTION	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	24.0	1403.10.19
	DUE TO TWIST OFF FROM TOP OF 12-1/4" S.STAB & LEFT IN HOLE	OEOC-RIG	13.0	1403.10.20
	DUE TO BURST ON THE UPPER IBOP.	OEOC-RIG	17.5	1403.10.21
	DUE TO LEFT IN HOLE (FISHING)	OEOC	21.5	1403.10.26
	DELAY IN OPERATION DUE TO LEFT IN HOLE (FISHING)	OEOC	24.0	1403.10.27
	DELAY IN OPERATION DUE TO LEFT IN HOLE (FISHING)	OEOC	11.0	1403.10.28
	DELAY IN OPERATION DUE TO LOW ROP & LEFT IN HOLE (BROKEN CUTTER BIT) LEAD TO RUN JUNK SUB	OEOC	19.0	1403.10.29
	DELAY IN OPERATION DUE TO LEFT IN HOLE (BROKEN CUTTER BIT) LEAD TO RUN JUNK SUB & WORK ON J.SUB (UNPLANNED)	OEOC	24.0	1403.10.30
	DELAY IN OPERATION DUE TO LEFT IN HOLE (BROKEN PDC BIT CUTTER) LEAD TO RUN JUNK SUB & RUN RCJB (UNPLANNED, FISHING)	OEOC	24.0	1403.11.01
	DELAY IN OPERATION DUE TO LEFT IN HOLE (BROKEN PDC BIT CUTTER) LEAD TO RUN JUNK SUB & RUN RCJB (UNPLANNED, FISHING)	OEOC	24.0	1403.11.02

DELAY IN OPERATION DUE TO LEFT IN HOLE (BROKEN PDC BIT CUTTER) LEAD TO RUN JUNK SUB & RUN RCJB (UNPLANNED, FISHING)	OEOC	14.0	1403.11.03
DELAY IN OPERATION DUE TO OBS DEC. SPP & RETURN MW 82PCF (CIRC. TO BALANCE MW TO 83PCF)	OEOC	1.0	1403.11.08
CHANGE WASH PIPE	OEOC	2.5	1403.11.10
CHANGE WASH PIPE	OEOC	2.0	1403.11.11
WASH OUT IBOP BODY CHANGE SAME	OEOC	7.0	1403.11.14
NPT DUE TO PLUGGED BIT NOZZLES	OEOC	11.5	1403.11.15
NPT DUE TO PLUGGED BIT NOZZLES	OEOC	10.5	1403.11.15
NPT DUE TO PLUGGED BIT NOZZLES	OEOC	20.0	1403.11.16
INCREASE LOSSES	OEOC	2.0	1403.11.16
LOSSES CONTROL	OEOC	24.0	1403.11.17
INCREASE LOSSES	OEOC	24.0	1403.11.18
INCREASE LOSSES	OEOC	10.0	1403.11.19
UNPLUG STRG	OEOC	2.0	1403.11.19
DELAY IN BOP PRESS TEST (RECTIFY SEVERAL LEAKAGES)	OEOC	3.0	1403.11.24
DELAY IN OPERATION DUE TO WORK ON LEAKAGE FROM TDS SAVER SUB	OEOC	2.0	1403.11.25
WORK ON TDS DUE TO INABILITY TO DESIRED ROTATION (TORQUE FLUCTUATION PROBLEM)	OEOC	10.0	1403.11.26
DUE TO OBS INCREASE LOSS FORMATION & LACK OF MUD MATERIAL	OEOC	11.0	1403.11.27
DELAY IN OPERATION DUE FAILURE OF LOGGING TOOLS	THE THIRD PARTY (SEALAND) / OEOC	7.0	1403.12.02
1 HOUR NPT CONSIDERED FOR OEOC DUE TO EXCEED PLANNED TIME FOR CHANGE RAMS & BOP TESTING.	OEOC	1.0	1403.12.07
2 HOURS NPT CONSIDERED FOR OEOC DUE TO DELAY IN OPERATION.	OEOC	2.0	1403.12.07
3 HOURS NPT DUE TO STOP OPERATION SLIP & CUT D.L.	OEOC	3.0	1403.12.11
8.5 HOURS NPT DUE TO LOGGING TRY TO PASS F/ 3772M "NO SUCC".	OEOC	8.5	1403.12.13
DUE TO NOT PASS LOGGING TOOLS F/ 3772M, RUN 4 1/2" BLANK GUN AS DUMMY RUN NO PASS, FINALLY COND. TRIP (DELAY IN OPERATION)	OEOC	24.0	1403.12.14

	DUE TO NOT PASS LOGGING TOOLS F/ 3772M, RUN 4 1/2" BLANK GUN AS DUMMY RUN NO PASS, FINALLY COND. TRIP (DELAY IN OPERATION)	OEOC	9.0	1403.12.15
	WAIT ON DAY LIGHT	OEOC	6.0	1403.12.15
	WAIT ON DAY LIGHT	OEOC	6.0	1403.12.16
	WAIT ON DAY LIGHT	OEOC	5.0	
	WAIT ON DAY LIGHT	OEOC	6.0	1403.12.17
	WAIT ON DAY LIGHT	OEOC	5.0	
	WAIT ON DAY LIGHT	OEOC	6.0	1403.12.18
	WAIT ON DAY LIGHT	OEOC	5.0	
	WAIT ON DAY LIGHT	OEOC	6.0	1403.12.19
	B/O & L/D COMPLETION TOOLS OF DE-COMPLETED FROM AZNS-122 (NOT PLANNED)	MSA	3.0	1403.12.22
	B/O & L/D COMPLETION TOOLS OF DE-COMPLETED FROM AZNS-122 (NOT PLANNED)	MSA	4.0	1403.12.23

Table 3-1: AZNS-207 NPT Time Break – Down (Based on Client's Order and Information)

4. Geological & Logging Reports

4.1 Geological Report

stratigraphy

- **Aghajari Formation**

  This Formation consists of a repetition of brown to grey calcareous sandstones, chert debris and gypsum-veined red marl. A fauna of brackish to freshwater was observed, together with more marine fauna.

- **Gachsaran Formation**

  This formation begins with white, glassy, soft, medium, hard anhydrite and off white, light gray to gray, soft to medium hard, dolomitic limestone. Comprises of anhydrite interbedded with gray marl and red marl, salt beds of variable thickness and some thin limestone beds. This formation in type section not divided to another member. The Anhydrite is white off white, milky, soft, and partly crystalline to crystalline, medium hard to hard. The Gray marl is gray to light gray, soft. The Red marl is red brown to brown, soft, sticky. The Limestone is gray to light gray, buff to buff gray, hard, and slightly dolomitic.

- **Asmari Formation**

  The Asmari Formation in Azadegan Field developed a massive sandstone interval, with a few thin argillaceous limestones in the upper sections. Sandstone is clear, fine to medium-sorted, and poorly consolidated. On the other hand, the lower sections consist of intercalation of sandy, chalky, slightly dolomitic high-energy limestone with sandstone layers.

- **Pabdeh /Jahrum Formation**

  The Cenozoic era is started by the Jahrum Formation and its lateral equivalent the Pabdeh Formation in SW Iran. In the Azadegan Field, this argillaceous Formation is mainly comprised of argillaceous limestone at its top, which becomes more calcareous in the lower part. The Pabdeh Formation conformably is overlain by the Asmari Formation and disconformably rests on the Gurpi Formation. According to some index microfauna that are related to planktonic foraminifera,

the Pabdeh Formation is possibly deposited in deeper marine settings and the Jahrum interval is deposited in shallower marine condition. The Jahrum Formation just extends in the southern part of the Azadegan Field which in the northern part of the field is replaced by Pabdeh Formation.

- **Pabdeh Formation**

Pabdeh Formation is divided into two parts in the Azadegan field. The upper part is made of grey to dark- brown argillaceous limestone and marl. Planktonic fauna dates that this part was deposited in Oligocene. The lower part is composed of dark-brown, slightly argillaceous limestone. Pelagic fauna, mostly Globigerina and Globorotalia, indicates that this part was formed during late Paleocene to late Eocene in age. It seems that no early Paleocene formation exists in the Azadegan area.

- **Gurpi Formation**

This formation consists of three main units: a) Upper Gurpi Member b) Tarbour Member c) Lower Gurpi Member.

➢ **Upper Gurpi Member**

This member begins with light gray, gray, off white, soft to medium, sticky argillaceous limestone. The Upper Gurpi Member is mostly consisting of gray buff to gray with of trace partly buff gray, dark gray, medium hard to hard argillaceous, high argillaceous graded to marl argillaceous limestone interbedded with anhydrite marl and chalky limestone beds. The anhydritic marl is light gray to gray, soft, sticky, graded to high argillaceous calcareous. The chalky limestone is light gray to buff gray, medium hard to soft, chalky. II, a slightly argillaceous.

➢ **Tarbur Member**

In the western Abadan Plain about 50 meters thick chalky limestone was encountered in the middle part of the Gurpi Formation, which contains abundant fragments of bioclasts, suggesting very shallow depositional environment. This interval is equivalent to the Tarbur Formation with reservoir quality in other regions.

➢ **Lower Gurpi Member**

This Member begins with off white, cream, soft to medium hard argillaceous limestone and light gray to gray, soft, sticky marl. The Member consisting of dark

gray to gray, light gray, soft to medium hard argillaceous limestone and light cream and soft. II, A. chalky limestone beds.

- **Ilam Formation**

This formation is mostly consisting of limestone interbedded with shale and claystone beds. The Limestone is cream, buff to buff gray, light brown, soft to medium hard, chalky, II, A, oil stained partly slightly argillaceous. The Shale is green gray to light green gray, mostly brown gray, medium hard, pyritic, slightly calcareous. The Claystone is green gray to light green gray and soft, slightly calcareous.

- **Laffan Member**

The Laffan Member is mostly consisting of greenish-grey pyritic shale layer with ostracods fauna interbedded with Claystone beds that capping the Sarvak Formation.

- **Sarvak Formation**

The Sarvak Formation developed a carbonate unit, which was gradually overlying the Kazhdumi Formation, and it is abruptly terminated by an erosion phase, covered by a various late Cretaceous sediment. The lithology of Sarvak consists of the dark grey fine grained nodular argillaceous limestone interbedded with thin marls in the bottom. The Limestone graded upward into a white-to-buff massive chalky limestone with siliceous nodules; developed a very massive tan-to-brown limestone containing abundant rudist debris in the middle part. In the upper part is made up of rubbly limestone with red staining and leached zones of breccia and the top of Sarvak Formation is very ferruginous. For the layering scheme of the reservoir section, sequence stratigraphic concept was applied to the Azadegan wells. Judging from the characteristics of gamma ray and other wireline logs, relative sea- level change during the deposition of the reservoir sections were interpreted in terms of sequence stratigraphic context. Based upon the sea-level change inferred, the sections were interpreted as vertical accumulation of a number of zones, each of which is geologically termed as a depositional sequence, implicitly representing a genetically related body of sedimentary sequence. The formation was divided totally into thirteen zones by interpreting.

- **Kazhdumi Formation**

This formation is start with dark brown to dark green gray, medium hard to hard, soft to medium, high bituminous, calcareous shale interbedded with argillaceous limestone, sandy claystone, claystone, marl, sandy limestone, limestone beds. the middle part developed light-grey, micritic to chalky limestone, the low part, is around 40-60m in thickness clean channel sands interbedded with argillaceous sands with streaks of shale.

- **Dariyan Formation**

In the Azadegan Field, the average thickness of the Dariyan Formation is 183.5 m; its greatest thickness is 197.5 m in well AZN-1. This formation overlies the Gadvan Formation conformably and is overlain disconformably by the Kazhdumi Formation. Dariyan Formation starts with white-to-white cream grey clean limestone type I/II, I. Base of Dariyan Formation appears grey, green pyritic shale interbedded with argillaceous limestone. This zone called transition zone and thickness is 16m. after last grey limestone indicates of Gadvan Formation.

- **Gadvan Formation**

In this formation a variety of lithological rock types such as carbonates, rich organic shales and sandstones were deposited in various environments. The lower part of the Gadvan Formation is composed of low- energy, but not very deep, micritic, often argillaceous limestone with echinoids and algal fragments. Two sandstone units were defined in the Gadvan Formation lateral changes and especially discontinuity of the sandstone layers which are consist of fine clastic (shales and siltstones) may be expected The Gadvan formation divided to three parts:

  - **Upper Gadvan**

The upper part appears with occurrence of terrigenous rock. The lithology is composed of grey claystone and some shale.

  - **Khalij Member**

The Khalij Member appear with pure limestone, cream, light brown and in some intervals oil stain.

  - **Lower Gadvan**

The lower part consisting of alternating of marl, argillaceous limestone, limestone, claystone, sandy claystone and sandstone beds. The Marl is green gray, soft, sticky, slightly calcareous. The Argillaceous Limestone is gray white gray medium hard to soft, partly pyritic. The Limestone is white, white to light gray, hard. The Claystone is light gray, soft, sticky. The Sandy Claystone is light gray, soft, sticky, fine sand grained. The Sandstone is brown to gray, partly white buff, gray, friable, sorted, sub rounded, medium quartz grained, partly calcareous. This sandstone which occurs in Zone-3 and Zone-5 are the reservoir of this formation and in this part is equivalent with Kushk Member.

- **Fahliyan Formation**

This formation is start with light gray, light green gray, soft Limestone interbedded with green gray, soft, sticky Marl, green gray, light gray, soft, Argillaceous Limestone and dark green gray, soft, sticky Clay stone beds. This formation at continue is consisting of buff white light gray, light brown, brown, medium hard, hard, densely, slightly argillaceous limestone and off white, white gray, medium hard chalky limestone beds.

Lithostratigraphic Unit	Formation Tops (m)				TVD Thickness	Difference	Casing & Liner Data	
	Forecast	MD (Sample)	MD (Log)	TVDss		($MD_{Forecast}$-MD_{Log})	Size	Depth
	(m)	(m)	(m)	(m)	(m)	(m)	(Inch)	(m)
Original Hole								
Aghajari	Surface	Surface	Surface	Surface	1009.5	-	20	149
Gachsaran	1021	1020	-	-1005.5	348	-		
Asmari	1368	1368	-	-1353.5	217.7	-		
SideTrack Hole								
K.O.P. at 1435m (inside of Asmari Formation)								
Pabdeh or Pd./Ja.	1583	1584	1586.86	-1571.2	97.45	3.86		
Jahrum	1685	1684	1684.84	-1668.7	312.39	-0.16	13 3/8	1648
Pabdeh	1994	1991	1997.78	-1981.4	184.12	3.78		
U. Gurpi	2178	2178	2182.11	-2165.7	162.47	4.11		
Tarbur	2343	2346	2344.72	-2328.3	76.46	1.72		
L. Gurpi	2418	2423	2421.23	-2404.8	142.34	3.23		
Ilam	2560	2563	2563.64	-2547.2	67.98	3.64		
Laffan	2629	2633	2631.64	-2615.2	6.08	2.64		
Sarvak (Sar.-1)	2635	2639	2637.73	-2621.3	21.69	2.73		
Sar.-2	-	-	2659.42	-2643	8.32	-		
Sar.-3	-	-	2667.75	-2651.3	25.58	-		
Sar.-4-6	-	-	2693.33	-2676.9	84.41	-		
Sar.-7	-	-	2777.76	-2761.4	15.58	-		
Sar.-8	-	-	2793.34	-2776.9	59.86	-		
Sar.-9	-	-	2853.21	-2836.8	48.14	-		
Sar.-10	-	-	2901.36	-2885	24.63	-		
Sar.-11	-	-	2925.99	-2909.6	19.05	-		
Sar.-12	-	-	2945.04	-2928.6	88.91	-		
Sar.-Intra	-	-	3033.95	-3017.5	242.41	-		
Kazhdumi	3270	3266	3276.37	-3259.9	136.12	6.37		
Kaz.-1-Shale	-	-	3412.5	-3396.1	10.8	-		
Kaz.-2-Sand	-	-	3423.3	-3406.9	26.45	-		
Kaz.-3-Shale	-	-	3449.76	-3433.3	5.7	-		
Kaz.-4-Sand	-	-	3455.46	-3439	5.56	-		
Kaz.-5-Shale	-	-	3461.02	-3444.6	10.43	-		
Dariyan	3464	3467	3471.45	-3455	157.1	7.45		
Gadvan (Gad.-1)	3622	3626	3628.56	-3612.1	10.43	6.56		
Gad.-2u	-	-	3638.99	-3622.6	54.39	-		
Khalij Mbr.	-	3692	3693.39	-3677	9.39	-		
Gad.-2l	-	-	3702.78	-3686.3	3.71	-		
Gad.-3	-	-	3706.49	-3690	8.86	-		
Gad.-4	-	-	3715.35	-3698.9	14.95	-		
Gad.-5a	-	-	3730.3	-3713.9	10.45	-		
Gad.-5b	-	-	3740.75	-3724.3	2.38	-		
Gad.-5c	-	-	3743.13	-3726.7	10.83	-		
Gad.-6	-	-	3753.96	-3737.5	22.76	-		
Gad.-7	-	-	3776.72	-3760.3	21.43	-		
Gad.-8	-	-	3798.15	-3781.7	130.19	-	9 5/8	3895
Fahliyan	3915	3954	3928.34	-3911.9	41.06	13.34		
Fah.-1a	3955	-	3969.4	-3953	13.58	14.4		
Fah.-1b	3971	-	3982.98	-3966.5	12.23	11.98		
Fah.-1c	3982	-	3995.21	-3978.8	33.6	13.21		
Fah.-2a	4016	-	4028.81	-4012.4	16.55	12.81		
Fah.-2b	4033	-	4045.36	-4028.9	11.69	12.36		
Fah.-3a	4046	-	4057.05	-4040.6	4.77	11.05		
Fah.-3b	4053	-	4061.82	-4045.4	12.96	8.82		
Fah.-4a	4066	-	4074.78	-4058.3	11.64	8.78		
Fah.-4b	4076	-	4086.42	-4070	25.14	10.42		
Fah.-5a	4103	-	4111.56	-4095.1	25.4	8.56		
Fah.-5b	4127	-	4136.96	-4120.5	43.03	9.96		
T.D.	4180	4180	4180	-4162.6		0	7 L.	3786 - 4179.5

Table 4-1: AZNS-207 Formation & Reservoir Sub Layer Tops

Well General Data			Formation and Reservoir Sub Layer Tops			
Area	Abadan Plain, Block-III		Lithostratigraphic Units	MD	TVDss (mc)	Thickness (TVD)
Field	South Azadegan		Original Hole (Based on Sample)			
Pad No.	93		Aghajari	Surface	Surface	1009.5
Rig No.	OEOC-208		Gachsaran	1020	-1005.5	348
Well No.	AZNS-207 S.T.-1		Asmari	1368	-1353.5	217.7
Well Type	Development		SideTrack Hole (Based on Log)			
Total Depth/Formation	4180m (-4162.62mc)/Fahliyan		K.O.P. at 1435m (inside of Asmari Formation)			
Wellhead Coordinates	WGS-1984	E: 192,581m	Pabdeh or Pd./Ja.	1586.86	-1571.2	97.45
		N: 3,441,012m	Jahrum	1684.84	-1668.7	312.39
E. Point in Fahliyan Fm.	WGS-1984	E: 192,676.96m	Pabdeh	1997.78	-1981.4	184.12
		N: 3,441,009.35m	U. Gurpi	2182.11	-2165.7	162.47
T.D. Coordinates	WGS-1984	E: 192,676.53m	Tarbur	2344.72	-2328.3	76.46
		N: 3,441,007.63m	L. Gurpi	2421.23	-2404.8	142.34
Elevation	R.T.E.	14.45m	Ilam	2563.64	-2547.2	67.98
	G.L.E.	3.95m	Laffan	2631.64	-2615.2	6.08
Spudded Rig Date:	17-Oct-24		Sarvak (Sar.-1)	2637.73	-2621.3	21.69
Released Rig Date:	17-Mar-25		Sar.-2	2659.42	-2643	8.32
Start of Drilling Date:	17-Oct-24		Sar.-3	2667.75	-2651.3	25.58
End of Drilling Date:	17-Feb-25		Sar.-4-6	2693.33	-2676.9	84.41
Casing & Liner			Sar.-7	2777.76	-2761.4	15.58
Size (inch)	Depth (m)	Remarks	Sar.-8	2793.34	-2776.9	59.86
	From / To		Sar.-9	2853.21	-2836.8	48.14
20	- / 149	Set inside of Aghajari Fm.	Sar.-10	2901.36	-2885	24.63
13 3/8	- / 1648	Set inside of Pd. or Pd./Ja. Fm.	Sar.-11	2925.99	-2909.6	19.05
9 5/8	- / 3895	Set inside of Gadvan Fm.	Sar.-12	2945.04	-2928.6	88.91
7	3786 / 4179.5	Set Off Bottom	Sar.-Intra	3033.95	-3017.5	242.41
Mud Properties			Kazhdumi	3276.37	-3259.9	136.12
Hole Size (inch)	Mud Type & Weight		Kaz.-1-Shale	3412.5	-3396.1	10.8
26	Bentonite Mud (66-70pcf)		Kaz.-2-Sand	3423.3	-3406.9	26.45
17 1/2	Bentonite Mud (70-73pcf) / (KCL) Polymer Mud (73-85pcf)		Kaz.-3-Shale	3449.76	-3433.3	5.7
12 1/4	KCL Polymer Mud (73-85pcf)		Kaz.-4-Sand	3455.46	-3439	5.56
8 3/8	KCL Polymer Mud (80-103pcf)		Kaz.-5-Shale	3461.02	-3444.6	10.43
Electrical Logs			Dariyan	3471.45	-3455	157.1
Log / Company / Hole Size / Run No. / Depth Interval (m) / Date			Gadvan (Gad.-1)	3628.56	-3612.1	10.43
Resistivity/Sonic/CDR-GR / Sealand / 8 3/8" / 1 / 3815 - 4176 / 2025.02.19			Gad.-2u	3638.99	-3622.6	54.39
			Khalij Mbr.	3693.39	-3677	9.39
			Gad.-2l	3702.78	-3686.3	3.71
LDT/CNT/NGS / Sealand / 8 3/8" / 2 / 3820 - 4173 / 2025.02.19			Gad.-3	3706.49	-3690	8.86
			Gad.-4	3715.35	-3698.9	14.95
			Gad.-5a	3730.3	-3713.9	10.45
SBT/CCL/VDL-GR / Sealand / 12 1/4" / 3 / 1648 - 3887 / 2025.02.20			Gad.-5b	3740.75	-3724.3	2.38
			Gad.-5c	3743.13	-3726.7	10.83
			Gad.-6	3753.96	-3737.5	22.76
SBT/CCL/VDL-GR / Sealand / 8 3/8" / 1 / 3786 - 4140 / 2025.03.05			Gad.-7	3776.72	-3760.3	21.43
			Gad.-8	3798.15	-3781.7	130.19
			Fahliyan	3928.34	-3911.9	41.06
26" Hole Section Summary			Fah.-1a	3969.4	-3953	13.58
This section drilling started with Bentonite Mud (66-70pcf) from Surface to 150m. Ran 20" CSG to 149m and cemented.			Fah.-1b	3982.98	-3966.5	12.23
			Fah.-1c	3995.21	-3978.8	33.6
17 1/2" Hole Section Summary			Fah.-2a	4028.81	-4012.4	16.55
This section drilling started with Bentonite Mud (70-73pcf) and (KCL) Polymer Mud (73-85pcf) from 151m to 1648.5m. Ran 13 3/8" CSG to 1648m and cemented.			Fah.-2b	4045.36	-4028.9	11.69
			Fah.-3a	4057.05	-4040.6	4.77
12 1/4" Hole Section Summary			Fah.-3b	4061.82	-4045.4	12.96
This section drilling started with KCL Polymer Mud (73-85pcf) from 1648.5m to 3895m. Ran 9 5/8" CSG to 3895m and cemented.			Fah.-4a	4074.78	-4058.3	11.64
			Fah.-4b	4086.42	-4070	25.14
8 3/8" Hole Section Summary			Fah.-5a	4111.56	-4095.1	25.4
This section drilling started with KCL Polymer Mud (80-103pcf) from 3895m to4180m. Ran 7" LNR to 4179.5m and cemented.			Fah.-5b	4136.96	-4120.5	43.03
			T.D.	4180	-4162.62	
Perforation Data: 7" Liner (4 1/2" Gun - WCP Method)						
Perforation Intervals: 4082-4074.5m / 4070.5-4067.5 m / 4066-4063 m / 4061.4-4057 m / 4045-4029m / 4019.5-4015.5m (Totally 37.9m)						

Table 4-2: AZNS-207 Well Data Summary

Open Hole (Inch)	Formation/Member	Interval From (m)	Interval To (m)	Mud Properties	Casing and Liner Size (Inch)	Casing and Liner Depth (m)
Original Hole						
26	Aghajari	Surface	151	Bentonite Mud (66-70pcf)	20	149
17 1/2	Aghajari	151	1020	Bentonite Mud (70-73pcf)/ Polymer Mud (74pcf)		
	Gachsaran	1020	1368	Polymer Mud (74pcf)		
	Asmari	1368	1564	KCL Polymer Mud (74-85pcf)		
SideTrack Hole						
17 1/2	Asmari	1435	1586.86	KCL Polymer Mud (74-85pcf)		
	Pd. or Pd./Ja.	1586.86	1648.5	KCL Polymer Mud (73-85pcf)	13 3/8	1648
12 1/4	Pd. or Pd./Ja.	1648.5	1684	KCL Polymer Mud (73-85pcf)		
	Jahrum	1684	1997.78	KCL Polymer Mud (73-74pcf)		
	Pabdeh	1997.78	2182.11	KCL Polymer Mud (75-77pcf)		
	U.Gurpi	2182.11	2344.72	KCL Polymer Mud (77pcf)		
	Tarbur	2344.72	2421.23	KCL Polymer Mud (78pcf)		
	L.Gurpi	2421.23	2563.64	KCL Polymer Mud (78pcf)		
	Ilam	2563.64	2631.64	KCL Polymer Mud (78pcf)		
	Laffan	2631.64	2637.73	KCL Polymer Mud (78pcf)		
	Sarvak	2637.73	3276.37	KCL Polymer Mud (78-81pcf)		
	Kazhdumi	3276.37	3471.45	KCL Polymer Mud (82pcf)		
	Dariyan	3471.45	3628.56	KCL Polymer Mud (83pcf)		
	Gadvan	3628.56	3895	KCL Polymer Mud (81-85pcf)	9 5/8	3895
8 3/8	Gadvan	3895	3928.34	KCL Polymer Mud (80-102pcf)		
	Fahliyan	3928.34	4180	KCL Polymer Mud (103pcf)	7 L.	3786-4179.5

Table 4-3: AZNS-207 Open Hole, Casing & Mud Properties

Hole Type	Date	Formation/Member	From (m)	To (m)	Mud Type	Mud Weight (pcf)	Loss (BPD)	Gain (BPD)
Original Hole	17/10/2024	Aghajari	14	31	Bentonite Mud	69	NL	NG
	18/10/2024		31	151		70	NL	NG
	21/10/2024		151	155		70	NL	NG
	22/10/2024		155	225		71	NL	NG
	23/10/2024		225	495		71	NL	NG
	24/10/2024		495	730	Polymer Mud	73	NL	NG
	25/10/2024		730	800		74	NL	NG
	26/10/2024	Aghajari - Gachsaran	800	1073		74	NL	NG
	27/10/2024	Gachsaran	1073	1227		74	NL	NG
	28/10/2024		1227	1356		74	NL	NG
	29/10/2024	Gachsaran - Asmari	1356	1373		74	NL	NG
	30/10/2024	Asmari	1373	1450		76	NL	NG
	31/10/2024		1450	1480		76	61	NG
	01/11/2024		1480	1480		76	24	NG
	03/11/2024		1480	1548		76	694	NG
	04/11/2024		1548	1562		76	510	NG
	07/11/2024		1562	1564.5		76	150	NG
SideTrack Hole	25/11/2024	Asmari	1429	1439.5	KCL Polymer Mud	85	72	NG
	26/11/2024		1439..5	1447		85	60	NG
	27/11/2024		1447	1472		85	96	NG
	28/11/2024		1472	1507		85	100	NG
	29/11/2024		1507	1552		85	84	NG
	30/11/2024		1552	1571		85	48	NG
	02/12/2024	Asmari - Pabdeh/Jahrum	1571	1592.9		85	27	NG
	03/12/2024	Pabdeh/Jahrum	1592.9	1594		85	38	NG
	04/12/2024		1594	1616		85	36	NG
	05/12/2024		1616	1617.5		85	30	NG
	06/12/2024		1617.5	1636		85	36	NG
	07/12/2024		1636	1648.5		85	36	NG
	14/12/2024		1648.5	1654		73	NL	NG
	15/12/2024	Pabdeh/Jahrum - Jahrum	1654	1713		73	100	NG
	16/12/2024	Jahrum	1713	1828		73	360	NG
	17/12/2024		1828	1861		74	108	NG
	18/12/2024	Jahrum - Pabdeh	1861	1994		75	75	NG
	19/12/2024	Pabdeh	1994	2000		75	160	NG
	22/12/2024		2000	2114		77	48	NG
	23/12/2024		2114	2150		77	38	NG
	25/12/2024	Pabdeh - U.Gurpi	2150	2189		77	40	NG
	26/12/2024	U. Gurpi	2189	2339		77	72	NG
	27/12/2024	Tarbur & L. Gurpi	2339	2509		78	96	NG
	28/12/2024	Illam & Laffan & Sarvak	2509	2686		78	55	NG
	29/12/2024	Sarvak	2686	2696.5		78	18	NG
	30/12/2024		2696.5	2737		78	45	NG
	31/12/2024		2737	2810		78	48	NG
	03/01/2025		2810	2868		79	65	NG
	04/01/2025		2868	2870		79	65	NG
	05/01/2025		2870	2941		79	55	NG
	06/01/2025		2941	3006.7		79	55	NG
	09/01/2025		3006.7	3017.5		80	45	NG
	10/01/2025		3017.5	3023.5		80	28	NG
	11/01/2025		3023.5	3027		80	40	NG
	12/01/2025		3027	3054		80	54	NG
	13/01/2025		3054	3140		80.5	90	NG
	14/01/2025		3140	3236		81	96	NG
	15/01/2025		3236	3240		81.5	192	NG
	17/01/2025	Sarvak - Kazhdumi	3240	3274		82	60	NG
	18/01/2025	Kazhdumi	3274	3275		82	48	NG
	19/01/2025		3275	3284.4		82	60	NG
	21/01/2025		3284.4	3285		82	78	NG
	22/01/2025		3285	3315		82	96	NG
	23/01/2025		3515	3427		82	96	NG
	24/01/2025	Kazhdumi - Dariyan	3427	3535		83	96	NG
	25/01/2025	Dariyan	3535	3620		83	72	NG
	26/01/2025	Dariyan- Gadvan	3620	3671		83	72	NG
	27/01/2025	Gadvan	3671	3741		83	72	NG
	28/01/2025		3741	3790		84	68	NG
	29/01/2025		3790	3820		85	72	NG
	30/01/2025		3820	3846		84	168	NG
	31/01/2025		3846	3872		84	190	NG
	02/02/2025		3872	3891		82.5	472	NG
	04/02/2025		3891	3895		80	960	NG
	13/02/2025		3895	3910		80	NL	NG
	14/02/2025		3910	3928		100	NL	NG
	15/02/2025		3928	3964		102.5	24	NG
	16/02/2025	Fahliyan	3964	4076		103	36	NG
	17/02/2025		4076	4180		103	36	NG

Table 4-4: AZNS-207 Mud Loss & Gain

No.	Depth	Formation	Thickness	Shows
1	1756 - 1762	Jahrum	6	Fair
2	2700 - 2794	Sarvak	94	Weak
3	3046 - 3050		4	Weak
4	3080		1	Weak
5	3422 - 3452	Kazhdumi	30	Weak
6	3644	Gadvan	1	Weak
7	3708		1	Weak -Fair
8	3709 - 3714		5	Fair
9	3722 - 3736		14	Weak
10	3748		1	Weak
11	3934	Fahliyan	1	Weak
12	3956 - 3962		6	Weak
13	3982 - 3988		6	Weak
14	4028 - 4042		14	Weak
15	4058 - 4062		4	Weak
16	4070 - 4082		12	Weak
17	4086 - 4102		16	Weak-Fair
18	4106 - 4180		74	Weak

Table 4-5: AZNS-207 Hydrocarbon Shows

Intervals (m)		Thickness (m)	Method	Size	Company
From	To				
4082	4074.5	7.5	WCP	7"	Sealand
4070.5	4067.5	3			
4066	4063	3			
4061.4	4057	4.4			
4045	4029	16			
4019.5	4015.5	4			

Table 4-6: AZNS-207 Perforation Data

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
1	14	29	Aghajari	Good	52	327	340	Aghajari	Good
2	29	31	Aghajari	Good	53	340	350	Aghajari	Good
3	31	33	Aghajari	Good	54	350	360	Aghajari	Good
4	33	35	Aghajari	Good	55	360	365	Aghajari	Good
5	35	45	Aghajari	Good	56	365	370	Aghajari	Good
6	45	56	Aghajari	Good	57	370	375	Aghajari	Good
7	56	70	Aghajari	Good	58	375	380	Aghajari	Good
8	70	73	Aghajari	Good	59	380	385	Aghajari	Good
9	73	80	Aghajari	Good	60	385	390	Aghajari	Good
10	80	95	Aghajari	Good	61	390	400	Aghajari	Good
11	95	100	Aghajari	Good	62	400	405	Aghajari	Good
12	100	105	Aghajari	Good	63	405	410	Aghajari	Good
13	105	110	Aghajari	Good	64	410	415	Aghajari	Good
14	110	115	Aghajari	Good	65	415	420	Aghajari	Good
15	115	120	Aghajari	Good	66	420	425	Aghajari	Good
16	120	125	Aghajari	Good	67	425	430	Aghajari	Good
17	125	140	Aghajari	Good	68	430	435	Aghajari	Good
18	140	145	Aghajari	Good	69	435	440	Aghajari	Good
19	145	151	Aghajari	Good	70	440	450	Aghajari	Good
20	151	155	Aghajari	Good	71	450	460	Aghajari	Good
21	155	159	Aghajari	Good	72	460	465	Aghajari	Good
22	159	165	Aghajari	Good	73	465	475	Aghajari	Good
23	165	166	Aghajari	Good	74	475	485	Aghajari	Good
24	166	167	Aghajari	Good	75	485	490	Aghajari	Good
25	167	170	Aghajari	Good	76	490	495	Aghajari	Good
26	170	178	Aghajari	Good	77	495	505	Aghajari	Good
27	178	183	Aghajari	Good	78	505	515	Aghajari	Good
28	183	185	Aghajari	Good	79	515	525	Aghajari	Good
29	185	189	Aghajari	Good	80	525	535	Aghajari	Good
30	189	197	Aghajari	Good	81	535	540	Aghajari	Good
31	197	207	Aghajari	Good	82	540	545	Aghajari	Good
32	207	212	Aghajari	Good	83	545	560	Aghajari	Good
33	212	217	Aghajari	Good	84	560	585	Aghajari	Good
34	217	222	Aghajari	Good	85	585	590	Aghajari	Good
35	222	225	Aghajari	Good	86	590	595	Aghajari	Good
36	225	232	Aghajari	Good	87	595	600	Aghajari	Good
37	232	237	Aghajari	Good	88	600	605	Aghajari	Good
38	237	242	Aghajari	Good	89	605	610	Aghajari	Good
39	242	247	Aghajari	Good	90	610	615	Aghajari	Good
40	247	252	Aghajari	Good	91	615	620	Aghajari	Good
41	252	257	Aghajari	Good	92	620	630	Aghajari	Good
42	257	262	Aghajari	Good	93	630	635	Aghajari	Good
43	262	272	Aghajari	Good	94	635	645	Aghajari	Good
44	272	282	Aghajari	Good	95	645	650	Aghajari	Good
45	282	292	Aghajari	Good	96	650	655	Aghajari	Good
46	292	297	Aghajari	Good	97	655	660	Aghajari	Good
47	297	302	Aghajari	Good	98	660	670	Aghajari	Good
48	302	307	Aghajari	Good	99	670	675	Aghajari	Good
49	307	312	Aghajari	Good	100	675	690	Aghajari	Good
50	312	317	Aghajari	Good	101	690	700	Aghajari	Good
51	317	327	Aghajari	Good	102	700	705	Aghajari	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
103	705	710	Aghajari	Good	154	1021	1024	Gachsaran	Good
104	710	730	Aghajari	Good	155	1024	1026	Gachsaran	Good
105	730	735	Aghajari	Good	156	1026	1030	Gachsaran	Good
106	735	740	Aghajari	Good	157	1030	1034	Gachsaran	Good
107	740	750	Aghajari	Good	158	1034	1038	Gachsaran	Good
108	750	755	Aghajari	Good	159	1038	1040	Gachsaran	Good
109	755	760	Aghajari	Good	160	1040	1042	Gachsaran	Good
110	760	770	Aghajari	Good	161	1042	1046	Gachsaran	Good
111	770	775	Aghajari	Good	162	1046	1048	Gachsaran	Good
112	775	780	Aghajari	Good	163	1048	1058	Gachsaran	Good
113	780	795	Aghajari	Good	164	1058	1060	Gachsaran	Good
114	795	800	Aghajari	Good	165	1060	1062	Gachsaran	Good
115	800	805	Aghajari	Good	166	1062	1066	Gachsaran	Good
116	805	810	Aghajari	Good	167	1066	1070	Gachsaran	Good
117	810	815	Aghajari	Good	168	1070	1072	Gachsaran	Good
118	815	825	Aghajari	Good	169	1072	1074	Gachsaran	Good
119	825	830	Aghajari	Good	170	1074	1078	Gachsaran	Good
120	830	835	Aghajari	Good	171	1078	1080	Gachsaran	Good
121	835	840	Aghajari	Good	172	1080	1082	Gachsaran	Good
122	840	845	Aghajari	Good	173	1082	1084	Gachsaran	Good
123	845	850	Aghajari	Good	174	1084	1086	Gachsaran	Good
124	850	860	Aghajari	Good	175	1086	1088	Gachsaran	Good
125	860	865	Aghajari	Good	176	1088	1091	Gachsaran	Good
126	865	870	Aghajari	Good	177	1091	1096	Gachsaran	Good
127	870	875	Aghajari	Good	178	1096	1104	Gachsaran	Good
128	875	880	Aghajari	Good	179	1104	1106	Gachsaran	Good
129	880	885	Aghajari	Good	180	1106	1114	Gachsaran	Good
130	885	890	Aghajari	Good	181	1114	1125	Gachsaran	Good
131	890	895	Aghajari	Good	182	1125	1128	Gachsaran	Good
132	895	900	Aghajari	Good	183	1128	1137	Gachsaran	Good
133	900	905	Aghajari	Good	184	1137	1149	Gachsaran	Good
134	905	910	Aghajari	Good	185	1149	1155	Gachsaran	Good
135	910	915	Aghajari	Good	186	1155	1167	Gachsaran	Good
136	915	925	Aghajari	Good	187	1167	1173	Gachsaran	Good
137	925	930	Aghajari	Good	188	1173	1179	Gachsaran	Good
138	930	940	Aghajari	Good	189	1179	1181	Gachsaran	Good
139	940	950	Aghajari	Good	190	1181	1191	Gachsaran	Good
140	950	955	Aghajari	Good	191	1191	1194	Gachsaran	Good
141	955	960	Aghajari	Good	192	1194	1200	Gachsaran	Good
142	960	970	Aghajari	Good	193	1200	1202	Gachsaran	Good
143	970	975	Aghajari	Good	194	1202	1204	Gachsaran	Good
144	975	980	Aghajari	Good	195	1204	1207	Gachsaran	Good
145	980	985	Aghajari	Good	196	1207	1212	Gachsaran	Good
146	985	990	Aghajari	Good	197	1212	1216	Gachsaran	Good
147	990	995	Aghajari	Good	198	1216	1218	Gachsaran	Good
148	995	1005	Aghajari	Good	199	1218	1220	Gachsaran	Good
149	1005	1010	Aghajari	Good	200	1220	1222	Gachsaran	Good
150	1010	1015	Aghajari	Good	201	1222	1227	Gachsaran	Good
151	1015	1017	Aghajari	Good	202	1227	1230	Gachsaran	Good
152	1017	1020	Aghajari	Good	203	1230	1234	Gachsaran	Good
153	1020	1021	Gachsaran	Good	204	1234	1236	Gachsaran	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
205	1236	1240	Gachsaran	Good	256	1402	1423	Asmari	Good
206	1240	1242	Gachsaran	Good	257	1423	1426	Asmari	Good
207	1242	1244	Gachsaran	Good	258	1426	1429	Asmari	Good
208	1244	1246	Gachsaran	Good	259	1429	1444	Asmari	Good
209	1246	1250	Gachsaran	Good	260	1444	1450	Asmari	Good
210	1250	1256	Gachsaran	Good	261	1450	1464	Asmari	Good
211	1256	1259	Gachsaran	Good	262	1464	1468	Asmari	Good
212	1259	1262	Gachsaran	Good	263	1468	1480	Asmari	Good
213	1262	1265	Gachsaran	Good	264	1480	1484	Asmari	Good
214	1265	1271	Gachsaran	Good	265	1484	1488	Asmari	Good
215	1271	1276	Gachsaran	Good	266	1488	1492	Asmari	Good
216	1276	1282	Gachsaran	Good	267	1492	1499	Asmari	Good
217	1282	1286	Gachsaran	Good	268	1499	1505	Asmari	Good
218	1286	1292	Gachsaran	Good	269	1505	1526	Asmari	Good
219	1292	1296	Gachsaran	Good	270	1526	1528	Asmari	Good
220	1296	1300	Gachsaran	Good	271	1528	1538	Asmari	Good
221	1300	1304	Gachsaran	Good	272	1538	1540	Asmari	Good
222	1304	1306	Gachsaran	Good	273	1540	1542	Asmari	Good
223	1306	1310	Gachsaran	Good	274	1542	1544	Asmari	Good
224	1310	1316	Gachsaran	Good	275	1544	1548	Asmari	Good
225	1316	1319	Gachsaran	Good	276	1548	1550	Asmari	Good
226	1319	1326	Gachsaran	Good	277	1550	1552	Asmari	Good
227	1326	1328	Gachsaran	Good	278	1552	1554	Asmari	Good
228	1328	1330	Gachsaran	Good	279	1554	1560	Asmari	Good
229	1330	1332	Gachsaran	Good	280	1560	1562	Asmari	Good
230	1332	1334	Gachsaran	Good	281	1430.5	1432	Asmari	Good
231	1334	1336	Gachsaran	Good	282	1432	1433	Asmari	Good
232	1336	1338	Gachsaran	Good	283	1433	1435	Asmari	Good
233	1338	1340	Gachsaran	Good	284	1435	1437	Asmari	Good
234	1340	1342	Gachsaran	Good	285	1437	1438	Asmari	Good
235	1342	1344	Gachsaran	Good	286	1438	1439	Asmari	Good
236	1344	1346	Gachsaran	Good	287	1439	1440	Asmari	Good
237	1346	1348	Gachsaran	Good	288	1440	1441	Asmari	Good
238	1348	1350	Gachsaran	Good	289	1441	1442	Asmari	Good
239	1350	1352	Gachsaran	Good	290	1442	1443	Asmari	Good
240	1352	1354	Gachsaran	Good	291	1443	1444	Asmari	Good
241	1354	1355	Gachsaran	Good	292	1444	1446	Asmari	Good
242	1355	1356	Gachsaran	Good	293	1446	1447.3	Asmari	Good
243	1356	1358	Gachsaran	Good	294	1447.3	1450	Asmari	Good
244	1358	1360	Gachsaran	Good	295	1450	1464	Asmari	Good
245	1360	1363	Gachsaran	Good	296	1464	1466	Asmari	Good
246	1363	1367	Gachsaran	Good	297	1466	1470	Asmari	Good
247	1367	13968	Gachsaran	Good	298	1470	1472	Asmari	Good
248	13968	1370	Asmari	Good	299	1472	1480	Asmari	Good
249	1370	1373	Asmari	Good	300	1480	1482	Asmari	Good
250	1373	1380	Asmari	Good	301	1482	1484	Asmari	Good
251	1380	1385	Asmari	Good	302	1484	1487	Asmari	Good
252	1385	1386	Asmari	Good	303	1487	1492	Asmari	Good
253	1386	1392	Asmari	Good	304	1492	1494	Asmari	Good
254	1392	1396	Asmari	Good	305	1494	1502	Asmari	Good
255	1396	1402	Asmari	Good	306	1502	1504	Asmari	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
307	1504	1508	Asmari	Good	358	1668	1670	Pabdeh/Jahrum	Good
308	1508	1510	Asmari	Good	359	1670	1678	Pabdeh/Jahrum	Good
309	1510	1512	Asmari	Good	360	1678	1679	Pabdeh/Jahrum	Good
310	1512	1514	Asmari	Good	361	1679	1681	Pabdeh/Jahrum	Good
311	1514	1516	Asmari	Good	362	1681	1684	Pabdeh/Jahrum	Good
312	1516	1518	Asmari	Good	363	1684	1685	Jahrum	Good
313	1518	1527	Asmari	Good	364	1685	1686	Jahrum	Good
314	1527	1530	Asmari	Good	365	1686	1688	Jahrum	Good
315	1530	1539	Asmari	Good	366	1688	1689	Jahrum	Good
316	1539	1542	Asmari	Good	367	1689	1692	Jahrum	Good
317	1542	1544	Asmari	Good	368	1692	1696	Jahrum	Good
318	1544	1546	Asmari	Good	369	1696	1698	Jahrum	Good
319	1546	1548	Asmari	Good	370	1698	1700	Jahrum	Good
320	1548	1550	Asmari	Good	371	1700	1702	Jahrum	Good
321	1550	1552	Asmari	Good	372	1702	1704	Jahrum	Good
322	1552	1554	Asmari	Good	373	1704	1706	Jahrum	Good
323	1554	1556	Asmari	Good	374	1706	171	Jahrum	Good
324	1556	1558	Asmari	Good	375	171	1712	Jahrum	Good
325	1558	1560	Asmari	Good	376	1712	1713	Jahrum	Good
326	1560	1532	Asmari	Good	377	1713	1714	Jahrum	Good
327	1532	1564	Asmari	Good	378	1714	1716	Jahrum	Good
328	1564	1571	Asmari	Good	379	1716	1724	Jahrum	Good
329	1571	1574	Asmari	Good	380	1724	1726	Jahrum	Good
330	1574	1577	Asmari	Good	381	1726	1728	Jahrum	Good
331	1577	1581	Asmari	Good	382	1728	1732	Jahrum	Good
332	1581	1585	Asmari	Good	383	1732	1736	Jahrum	Good
333	1585	1587	Pabdeh/Jahrum	Good	384	1736	1740	Jahrum	Good
334	1587	1590	Pabdeh/Jahrum	Good	385	1740	1744	Jahrum	Good
335	1590	1594	Pabdeh/Jahrum	Good	386	1744	1748	Jahrum	Good
336	1594	1596	Pabdeh/Jahrum	Good	387	1748	1754	Jahrum	Good
337	1596	1601	Pabdeh/Jahrum	Good	388	1754	1760	Jahrum	Good
338	1601	1603	Pabdeh/Jahrum	Good	389	1760	1762	Jahrum	Good
339	1603	1608	Pabdeh/Jahrum	Good	390	1762	1766	Jahrum	Good
340	1608	1616	Pabdeh/Jahrum	Good	391	1766	1768	Jahrum	Good
341	1616	1618	Pabdeh/Jahrum	Good	392	1768	1770	Jahrum	Good
342	1618	1619	Pabdeh/Jahrum	Good	393	1770	1772	Jahrum	Good
343	1619	1626	Pabdeh/Jahrum	Good	394	1772	1774	Jahrum	Good
344	1626	1627	Pabdeh/Jahrum	Good	395	1774	1776	Jahrum	Good
345	1627	1630	Pabdeh/Jahrum	Good	396	1776	1780	Jahrum	Good
346	1630	1632	Pabdeh/Jahrum	Good	397	1780	1780	Jahrum	Good
347	1632	1637	Pabdeh/Jahrum	Good	398	1780	1782	Jahrum	Good
348	1637	1642	Pabdeh/Jahrum	Good	399	1782	1784	Jahrum	Good
349	1642	1646	Pabdeh/Jahrum	Good	400	1784	1786	Jahrum	Good
350	1646	1648.5	Pabdeh/Jahrum	Good	401	1786	1788	Jahrum	Good
351	1648.5	1651	Pabdeh/Jahrum	Good	402	1788	1790	Jahrum	Good
352	1651	1653	Pabdeh/Jahrum	Good	403	1790	1798	Jahrum	Good
353	1653	1654	Pabdeh/Jahrum	Good	404	1798	1802	Jahrum	Good
354	1654	1660	Pabdeh/Jahrum	Good	405	1802	1810	Jahrum	Good
355	1660	1662	Pabdeh/Jahrum	Good	406	1810	1814	Jahrum	Good
356	1662	1664	Pabdeh/Jahrum	Good	407	1814	1818	Jahrum	Good
357	1664	1668	Pabdeh/Jahrum	Good	408	1818	1822	Jahrum	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
409	1822	1824	Jahrum	Good	460	1961	1964	Jahrum	Good
410	1824	1828	Jahrum	Good	461	1964	1966	Jahrum	Good
411	1828	1829	Jahrum	Good	462	1966	1968	Jahrum	Good
412	1829	1831	Jahrum	Good	463	1968	1970	Jahrum	Good
413	1831	1832	Jahrum	Good	464	1970	1972	Jahrum	Good
414	1832	1834	Jahrum	Good	465	1972	1974	Jahrum	Good
415	1834	1840	Jahrum	Good	466	1974	1976	Jahrum	Good
416	1840	1842	Jahrum	Good	467	1976	1978	Jahrum	Good
417	1842	1844	Jahrum	Good	468	1978	1980	Jahrum	Good
418	1844	1846	Jahrum	Good	469	1980	1982	Jahrum	Good
419	1846	1850	Jahrum	Good	470	1982	1985	Jahrum	Good
420	1850	1852	Jahrum	Good	471	1985	1988	Jahrum	Good
421	1852	1854	Jahrum	Good	472	1988	1989	Jahrum	Good
422	1854	1860	Jahrum	Good	473	1989	1991	Jahrum	Good
423	1860	1861	Jahrum	Good	474	1991	1992	Pabdeh	Good
424	1861	1862	Jahrum	Good	475	1992	1994	Pabdeh	Good
425	1862	1864	Jahrum	Good	476	1994	1996	Pabdeh	Good
426	1864	1866	Jahrum	Good	477	1996	2000	Pabdeh	Good
427	1866	1870	Jahrum	Good	478	2000	2004	Pabdeh	Good
428	1870	1880	Jahrum	Good	479	2004	2006	Pabdeh	Good
429	1880	1882	Jahrum	Good	480	2006	2010	Pabdeh	Good
430	1882	1884	Jahrum	Good	481	2010	2012	Pabdeh	Good
431	1884	1886	Jahrum	Good	482	2012	2014	Pabdeh	Good
432	1886	1888	Jahrum	Good	483	2014	2016	Pabdeh	Good
433	1888	1896	Jahrum	Good	484	2016	2018	Pabdeh	Good
434	1896	1898	Jahrum	Good	485	2018	2022	Pabdeh	Good
435	1898	1900	Jahrum	Good	486	2022	2024	Pabdeh	Good
436	1900	1902	Jahrum	Good	487	2024	2026	Pabdeh	Good
437	1902	1904	Jahrum	Good	488	2026	2028	Pabdeh	Good
438	1904	1906	Jahrum	Good	489	2028	2030	Pabdeh	Good
439	1906	1908	Jahrum	Good	490	2030	2032	Pabdeh	Good
440	1908	1910	Jahrum	Good	491	2032	2034	Pabdeh	Good
441	1910	1914	Jahrum	Good	492	2034	2036	Pabdeh	Good
442	1914	1918	Jahrum	Good	493	2036	2042	Pabdeh	Good
443	1918	1924	Jahrum	Good	494	2042	2048	Pabdeh	Good
444	1924	1932	Jahrum	Good	495	2048	2050	Pabdeh	Good
445	1932	1934	Jahrum	Good	496	2050	2052	Pabdeh	Good
446	1934	1936	Jahrum	Good	497	2052	2054	Pabdeh	Good
447	1936	1942	Jahrum	Good	498	2054	2058	Pabdeh	Good
448	1942	1944	Jahrum	Good	499	2058	2062	Pabdeh	Good
449	1944	1946	Jahrum	Good	500	2062	2064	Pabdeh	Good
450	1946	1948	Jahrum	Good	501	2064	2066	Pabdeh	Good
451	1948	1950	Jahrum	Good	502	2066	2070	Pabdeh	Good
452	1950	1952	Jahrum	Good	503	2070	2072	Pabdeh	Good
453	1952	1953	Jahrum	Good	504	2072	2076	Pabdeh	Good
454	1953	1955	Jahrum	Good	505	2076	2086	Pabdeh	Good
455	1955	1957	Jahrum	Good	506	2086	2090	Pabdeh	Good
456	1957	1958	Jahrum	Good	507	2090	2094	Pabdeh	Good
457	1958	1959	Jahrum	Good	508	2094	2099	Pabdeh	Good
458	1959	1960	Jahrum	Good	509	2099	2105	Pabdeh	Good
459	1960	1961	Jahrum	Good	510	2105	2112	Pabdeh	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
511	2112	2114	Pabdeh	Good	562	2337	2339	U. Gurpi	Good
512	2114	2118	Pabdeh	Good	563	2339	2342.5	U. Gurpi	Good
513	2118	2122	Pabdeh	Good	564	2342.5	2344	U. Gurpi	Good
514	2122	2124	Pabdeh	Good	565	2344	2344.5	U. Gurpi	Good
515	2124	2126	Pabdeh	Good	566	2344.5	2346	U. Gurpi	Good
516	2126	2132	Pabdeh	Good	567	2346	2353	Tarbur	Good
517	2132	2134	Pabdeh	Good	568	2353	2355	Tarbur	Good
518	2134	2136	Pabdeh	Good	569	2355	2356	Tarbur	Good
519	2136	2138	Pabdeh	Good	570	2356	2358	Tarbur	Good
520	2138	2140	Pabdeh	Good	571	2358	2362	Tarbur	Good
521	2140	2142	Pabdeh	Good	572	2362	2366	Tarbur	Good
522	2142	2144	Pabdeh	Good	573	2366	2370	Tarbur	Good
523	2144	2146	Pabdeh	Good	574	2370	2374	Tarbur	Good
524	2146	2150	Pabdeh	Good	575	2374	2376	Tarbur	Good
525	2150	2178	Pabdeh	Good	576	2376	2382	Tarbur	Good
526	2178	2181	U. Gurpi	Good	577	2382	2386	Tarbur	Good
527	2181	2182	U. Gurpi	Good	578	2386	2388	Tarbur	Good
528	2182	2184	U. Gurpi	Good	579	2388	2390	Tarbur	Good
529	2184	2188	U. Gurpi	Good	580	2390	2398	Tarbur	Good
530	2188	2192	U. Gurpi	Good	581	2398	2404	Tarbur	Good
531	2192	2200	U. Gurpi	Good	582	2404	2408	Tarbur	Good
532	2200	2206	U. Gurpi	Good	583	2408	2414	Tarbur	Good
533	2206	2210	U. Gurpi	Good	584	2414	2416	Tarbur	Good
534	2210	2216	U. Gurpi	Good	585	2416	2419	Tarbur	Good
535	2216	2220	U. Gurpi	Good	586	2419	2421	Tarbur	Good
536	2220	2222	U. Gurpi	Good	587	2421	2423	Tarbur	Good
537	2222	2226	U. Gurpi	Good	588	2423	2426	L. Gurpi	Good
538	2226	2230	U. Gurpi	Good	589	2426	2430	L. Gurpi	Good
539	2230	2234	U. Gurpi	Good	590	2430	2436	L. Gurpi	Good
540	2234	2236	U. Gurpi	Good	591	2436	2454	L. Gurpi	Good
541	2236	2238	U. Gurpi	Good	592	2454	2466	L. Gurpi	Good
542	2238	2242	U. Gurpi	Good	593	2466	2490	L. Gurpi	Good
543	2242	2244	U. Gurpi	Good	594	2490	2509	L. Gurpi	Good
544	2244	2248	U. Gurpi	Good	595	2509	2521	L. Gurpi	Good
545	2248	2252	U. Gurpi	Good	596	2521	2524	L. Gurpi	Good
546	2252	2256	U. Gurpi	Good	597	2524	2527	L. Gurpi	Good
547	2256	2260	U. Gurpi	Good	598	2527	2539	L. Gurpi	Good
548	2260	2264	U. Gurpi	Good	599	2539	2548	L. Gurpi	Good
549	2264	2268	U. Gurpi	Good	600	2548	2556	L. Gurpi	Good
550	2268	2270	U. Gurpi	Good	601	2556	2563	L. Gurpi	Good
551	2270	2274	U. Gurpi	Good	602	2563	2566	Ilam	Good
552	2274	2276	U. Gurpi	Good	603	2566	2567	Ilam	Good
553	2276	2280	U. Gurpi	Good	604	2567	2568	Ilam	Good
554	2280	2290	U. Gurpi	Good	605	2568	2569	Ilam	Good
555	2290	2294	U. Gurpi	Good	606	2569	2573	Ilam	Good
556	2294	2296	U. Gurpi	Good	607	2573	2580	Ilam	Good
557	2296	2300	U. Gurpi	Good	608	2580	2584	Ilam	Good
558	2300	2316	U. Gurpi	Good	609	2584	2586	Ilam	Good
559	2316	2322	U. Gurpi	Good	610	2586	2590	Ilam	Good
560	2322	2332	U. Gurpi	Good	611	2590	2598	Ilam	Good
561	2332	2337	U. Gurpi	Good	612	2598	2602	Ilam	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
613	2602	2606	Ilam	Good	663	2860	2862	Sarvak	Good
614	2606	2616	Ilam	Good	664	2862	2864	Sarvak	Good
615	2616	2625	Ilam	Good	665	2864	2866	Sarvak	Good
616	2625	2633	Ilam	Good	666	2866	2868	Sarvak	Good
617	2633	2634	Laffan	Good	667	2868	2870	Sarvak	Good
618	2634	2635	Laffan	Good	668	2870	2872	Sarvak	Good
619	2635	2636	Laffan	Good	669	2872	2878	Sarvak	Good
620	2636	2637	Laffan	Good	670	2878	2884	Sarvak	Good
621	2637	2639	Laffan	Good	671	2884	2888	Sarvak	Good
622	2639	2640	Sarvak	Good	672	2888	2896	Sarvak	Good
623	2640	2641	Sarvak	Good	673	2896	2900	Sarvak	Good
624	2641	2642	Sarvak	Good	674	2900	2902	Sarvak	Good
625	2642	2650	Sarvak	Good	675	2902	2914	Sarvak	Good
626	2650	2652	Sarvak	Good	676	2914	2918	Sarvak	Good
627	2652	2658	Sarvak	Good	677	2918	2926	Sarvak	Good
628	2658	2659	Sarvak	Good	678	2926	2928	Sarvak	Good
629	2659	2660	Sarvak	Good	679	2928	2930	Sarvak	Good
630	2660	2662	Sarvak	Good	680	2930	2934	Sarvak	Good
631	2662	2664	Sarvak	Good	681	2934	2938	Sarvak	Good
632	2664	2666	Sarvak	Good	682	2938	2940	Sarvak	Good
633	2666	2668	Sarvak	Good	683	2940	2944	Sarvak	Good
634	2668	2670	Sarvak	Good	684	2944	2950	Sarvak	Good
635	2670	2672	Sarvak	Good	685	2950	2958	Sarvak	Good
636	2672	2674	Sarvak	Good	686	2958	2968	Sarvak	Good
637	2674	2686	Sarvak	Good	687	2968	2974	Sarvak	Good
638	2686	2689	Sarvak	Good	688	2974	2978	Sarvak	Good
639	2689	2691	Sarvak	Good	689	2978	2980	Sarvak	Good
640	2691	2694	Sarvak	Good	690	2980	2992	Sarvak	Good
641	2694	2696	Sarvak	Good	691	2992	2994	Sarvak	Good
642	2696	2700	Sarvak	Good	692	2994	2996	Sarvak	Good
643	2700	2702	Sarvak	Good	693	2996	2998	Sarvak	Good
644	2702	2704	Sarvak	Good	694	2998	3000	Sarvak	Good
645	2704	2716	Sarvak	Good	695	3000	3004	Sarvak	Good
646	2716	2718	Sarvak	Good	696	3004	3007	Sarvak	Good
647	2718	2730	Sarvak	Good	697	3007	3008	Sarvak	Good
648	2730	2738	Sarvak	Good	698	3008	3012	Sarvak	Good
649	2738	2746	Sarvak	Good	699	3012	3016	Sarvak	Good
650	2746	2754	Sarvak	Good	700	3016	3019	Sarvak	Good
651	2754	2764	Sarvak	Good	701	3019	3024	Sarvak	Good
652	2764	2770	Sarvak	Good	702	3024	3025	Sarvak	Good
653	2770	2788	Sarvak	Good	703	3025	3027	Sarvak	Good
654	2788	2807	Sarvak	Good	704	3027	3032	Sarvak	Good
655	2807	2810	Sarvak	Good	705	3032	3044	Sarvak	Good
656	2810	2814	Sarvak	Good	706	3044	3056	Sarvak	Good
657	2814	2818	Sarvak	Good	707	3056	3058	Sarvak	Good
658	2818	2822	Sarvak	Good	708	3058	3060	Sarvak	Good
659	2822	2836	Sarvak	Good	709	3060	3072	Sarvak	Good
660	2836	2840	Sarvak	Good	710	3072	3078	Sarvak	Good
661	2840	2854	Sarvak	Good	711	3078	3084	Sarvak	Good
662	2854	2858	Sarvak	Good	712	3084	3086	Sarvak	Good
663	2858	2860	Sarvak	Good	713	3086	3092	Sarvak	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
714	3092	3102	Sarvak	Good	765	3370	3374	Kazhdumi	Good
715	3102	3106	Sarvak	Good	766	3374	3378	Kazhdumi	Good
716	3106	3110	Sarvak	Good	767	3378	3382	Kazhdumi	Good
717	3110	3112	Sarvak	Good	768	3382	3386	Kazhdumi	Good
718	3112	3114	Sarvak	Good	769	3386	3392	Kazhdumi	Good
719	3114	3118	Sarvak	Good	770	3392	3396	Kazhdumi	Good
720	3118	3122	Sarvak	Good	771	3396	3400	Kazhdumi	Good
721	3122	3130	Sarvak	Good	772	3400	3404	Kazhdumi	Good
722	3130	3138	Sarvak	Good	773	3404	3406	Kazhdumi	Good
723	3138	3146	Sarvak	Good	774	3406	3409	Kazhdumi	Good
724	3146	3152	Sarvak	Good	775	3409	3413	Kazhdumi	Good
725	3152	3156	Sarvak	Good	776	3413	3415	Kazhdumi	Good
726	3156	3188	Sarvak	Good	777	3415	3419	Kazhdumi	Good
727	3188	3190	Sarvak	Good	778	3419	3421	Kazhdumi	Good
728	3190	3208	Sarvak	Good	779	3421	3422	Kazhdumi	Good
729	3208	3222	Sarvak	Good	780	3422	3423	Kazhdumi	Good
730	3222	3226	Sarvak	Good	781	3423	3425	Kazhdumi	Good
731	3226	3232	Sarvak	Good	782	3425	3427	Kazhdumi	Good
732	3232	3240	Sarvak	Good	783	3427	3428	Kazhdumi	Good
733	3240	3244	Sarvak	Good	784	3428	3430	Kazhdumi	Good
734	3244	3250	Sarvak	Good	785	3430	3432	Kazhdumi	Good
735	3250	3252	Sarvak	Good	786	3432	3436	Kazhdumi	Good
736	3252	3256	Sarvak	Good	787	3436	3438	Kazhdumi	Good
737	3256	3266	Sarvak	Good	788	3438	3442	Kazhdumi	Good
738	3266	3267	Kazhdumi	Good	789	3442	3446	Kazhdumi	Good
739	3267	3268	Kazhdumi	Good	790	3446	3448	Kazhdumi	Good
740	3268	3269	Kazhdumi	Good	791	3448	3452	Kazhdumi	Good
741	3269	3274	Kazhdumi	Good	792	3452	3462	Kazhdumi	Good
742	3274	3276	Kazhdumi	Good	793	3462	3467	Kazhdumi	Good
743	3276	3278	Kazhdumi	Good	794	3467	3470	Dariyan	Good
744	3278	3285	Kazhdumi	Good	795	3470	3473	Dariyan	Good
745	3285	3289	Kazhdumi	Good	796	3473	3476	Dariyan	Good
746	3289	3290	Kazhdumi	Good	797	3476	3484	Dariyan	Good
747	3290	3294	Kazhdumi	Good	798	3484	3492	Dariyan	Good
748	3294	3306	Kazhdumi	Good	799	3492	3506	Dariyan	Good
749	3306	3308	Kazhdumi	Good	800	3506	3508	Dariyan	Good
750	3308	3312	Kazhdumi	Good	801	3508	3535	Dariyan	Good
751	3312	3314	Kazhdumi	Good	802	3535	3540	Dariyan	Good
752	3314	3315	Kazhdumi	Good	803	3540	3562	Dariyan	Good
753	3315	3316	Kazhdumi	Good	804	3562	3564	Dariyan	Good
754	3316	33185	Kazhdumi	Good	805	3564	3570	Dariyan	Good
755	33185	3318	Kazhdumi	Good	806	3570	3582	Dariyan	Good
756	3318	3326	Kazhdumi	Good	807	3582	3586	Dariyan	Good
757	3326	3328	Kazhdumi	Good	808	3586	3592	Dariyan	Good
758	3328	3340	Kazhdumi	Good	809	3592	3612	Dariyan	Good
759	3340	3342	Kazhdumi	Good	810	3612	3614	Dariyan	Good
760	3342	3344	Kazhdumi	Good	811	3614	3617	Dariyan	Good
761	3344	3360	Kazhdumi	Good	812	3617	3620	Dariyan	Good
762	3360	3364	Kazhdumi	Good	813	3620	3621	Dariyan	Good
763	3364	3366	Kazhdumi	Good	814	3621	3622	Dariyan	Good
764	3366	3370	Kazhdumi	Good	815	3622	3625	Dariyan	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
816	3625	3626	Dariyan	Good	867	3752	3754	Khalij	Good
817	3626	3628	Gadvan	Good	868	3754	3755	Khalij	Good
818	3628	3630	Gadvan	Good	869	3755	3757	Khalij	Good
819	3630	3631	Gadvan	Good	870	3757	3759	Khalij	Good
820	3631	3632	Gadvan	Good	871	3759	3762	Khalij	Good
821	3632	3638	Gadvan	Good	872	3762	3764	Khalij	Good
822	3638	3640	Gadvan	Good	873	3764	3766	Khalij	Good
823	3640	3644	Gadvan	Good	874	3766	3768	Khalij	Good
824	3644	3654	Gadvan	Good	875	3768	3770	Khalij	Good
825	3654	3658	Gadvan	Good	876	3770	3772	Khalij	Good
826	3658	3660	Gadvan	Good	877	3772	3773	Khalij	Good
827	3660	3662	Gadvan	Good	878	3773	3774	Khalij	Good
828	3662	3666	Gadvan	Good	879	3774	3775	Khalij	Good
829	3666	3671	Gadvan	Good	880	3775	3776	Khalij	Good
830	3671	3675	Gadvan	Good	881	3776	3778	Khalij	Good
831	3675	3676	Gadvan	Good	882	3778	3779	Khalij	Good
832	3676	3678	Gadvan	Good	883	3779	3781	Khalij	Good
833	3678	3680	Gadvan	Good	884	3781	3783	Khalij	Good
834	3680	3685	Gadvan	Good	885	3783	3786	Khalij	Good
835	3685	3686	Gadvan	Good	886	3786	3789	Khalij	Good
836	3686	3692	Gadvan	Good	887	3789	3790	Khalij	Good
837	3692	3695	Khalij	Good	888	3790	3791	Khalij	Good
838	3695	3697	Khalij	Good	889	3791	3793	Khalij	Good
839	3697	3701	Khalij	Good	890	3793	3794	Khalij	Good
840	3701	3702	Khalij	Good	891	3794	3795	Khalij	Good
841	3702	3703	Khalij	Good	892	3795	3796	Khalij	Good
842	3703	3704	Khalij	Good	893	3796	3798	Khalij	Good
843	3704	3705	Khalij	Good	894	3798	3800	Khalij	Good
844	3705	3707	Khalij	Good	895	3800	3808	Khalij	Good
845	3707	3708	Khalij	Good	896	3808	3810	Khalij	Good
846	3708	3710	Khalij	Good	897	3810	3813	Khalij	Good
847	3710	3713	Khalij	Good	898	3813	3814	Khalij	Good
848	3713	3714	Khalij	Good	899	3814	3816	Khalij	Good
849	3714	3715	Khalij	Good	900	3816	3820	Khalij	Good
850	3715	3716	Khalij	Good	901	3820	3830	Khalij	Good
851	3716	3720	Khalij	Good	902	3830	3834	Khalij	Good
852	3720	3724	Khalij	Good	903	3834	3835	Khalij	Good
853	3724	3726	Khalij	Good	904	3835	3836	Khalij	Good
854	3726	3730	Khalij	Good	905	3836	3838	Khalij	Good
855	3730	3732	Khalij	Good	906	3838	3839	Khalij	Good
856	3732	3734	Khalij	Good	907	3839	3840	Khalij	Good
857	3734	3737	Khalij	Good	908	3840	3849	Khalij	Good
858	3737	3739	Khalij	Good	909	3849	3854	Khalij	Good
859	3739	3741	Khalij	Good	910	3854	3855	Khalij	Good
860	3741	3742	Khalij	Good	911	3855	3856	Khalij	Good
861	3742	3743	Khalij	Good	912	3856	3857	Khalij	Good
862	3743	3745	Khalij	Good	913	3857	3858	Khalij	Good
863	3745	3746	Khalij	Good	914	3858	3859	Khalij	Good
864	3746	3748	Khalij	Good	915	3859	3860	Khalij	Good
865	3748	3750	Khalij	Good	916	3860	3861	Khalij	Good
866	3750	3752	Khalij	Good	917	3861	3863	Khalij	Good

No.	Sample Interval		Formation/ Member	Sample Quality	No.	Sample Interval		Formation/ Member	Sample Quality
	From	To				From	To		
918	3863	3864	Khalij	Good	969	4084	4090	Fahliyan	Good
919	3864	3865	Khalij	Good	970	4090	4098	Fahliyan	Good
920	3865	3866	Khalij	Good	971	4098	4110	Fahliyan	Good
921	3866	3867	Khalij	Good	972	4110	4114	Fahliyan	Good
922	3867	3868	Khalij	Good	973	4114	4126	Fahliyan	Good
923	3868	3870	Khalij	Good	974	4126	4136	Fahliyan	Good
924	3870	3872	Khalij	Good	975	4136	4144	Fahliyan	Good
925	3872	3874	Khalij	Good	976	4144	4166	Fahliyan	Good
926	3874	3875	Khalij	Good	977	4166	4172	Fahliyan	Good
927	3875	3876	Khalij	Good	978	4172	4176	Fahliyan	Good
928	3876	3878	Khalij	Good	979	4176	4180	Fahliyan	Good
929	3878	3880	Khalij	Good					
930	3880	3881	Khalij	Good					
931	3881	3883	Khalij	Good					
932	3883	3884	Khalij	Good					
933	3884	3890	Khalij	Good					
934	3890	3891	Khalij	Good					
935	3891	3895	Khalij	Good					
936	3895	3899	Khalij	Good					
937	3899	3903	Khalij	Good					
938	3903	3905	Khalij	Good					
939	3905	3908	Khalij	Good					
940	3908	3910	Khalij	Good					
941	3910	3912	Khalij	Good					
942	3912	3914	Khalij	Good					
943	3914	3921	Khalij	Good					
944	3921	3922	Khalij	Good					
945	3922	3926	Khalij	Good					
946	3926	3928	Khalij	Good					
947	3928	3946	Khalij	Good					
948	3946	3954	Khalij	Good					
949	3954	3963	Fahliyan	Good					
950	3963	3964	Fahliyan	Good					
951	3964	3968	Fahliyan	Good					
952	3968	3980	Fahliyan	Good					
953	3980	3990	Fahliyan	Good					
954	3990	3994	Fahliyan	Good					
955	3994	4006	Fahliyan	Good					
956	4006	4008	Fahliyan	Good					
957	4008	4018	Fahliyan	Good					
958	4018	4025	Fahliyan	Good					
959	4025	4027	Fahliyan	Good					
960	4027	4029	Fahliyan	Good					
961	4029	4032	Fahliyan	Good					
962	4032	4040	Fahliyan	Good					
963	4040	4042	Fahliyan	Good					
964	4042	4054	Fahliyan	Good					
965	4054	4058	Fahliyan	Good					
966	4058	4076	Fahliyan	Good					
967	4076	4080	Fahliyan	Good					
968	4080	4084	Fahliyan	Good					

Table 4-7: AZNS-207 Sample Interval & Quality (Cutting Collection)

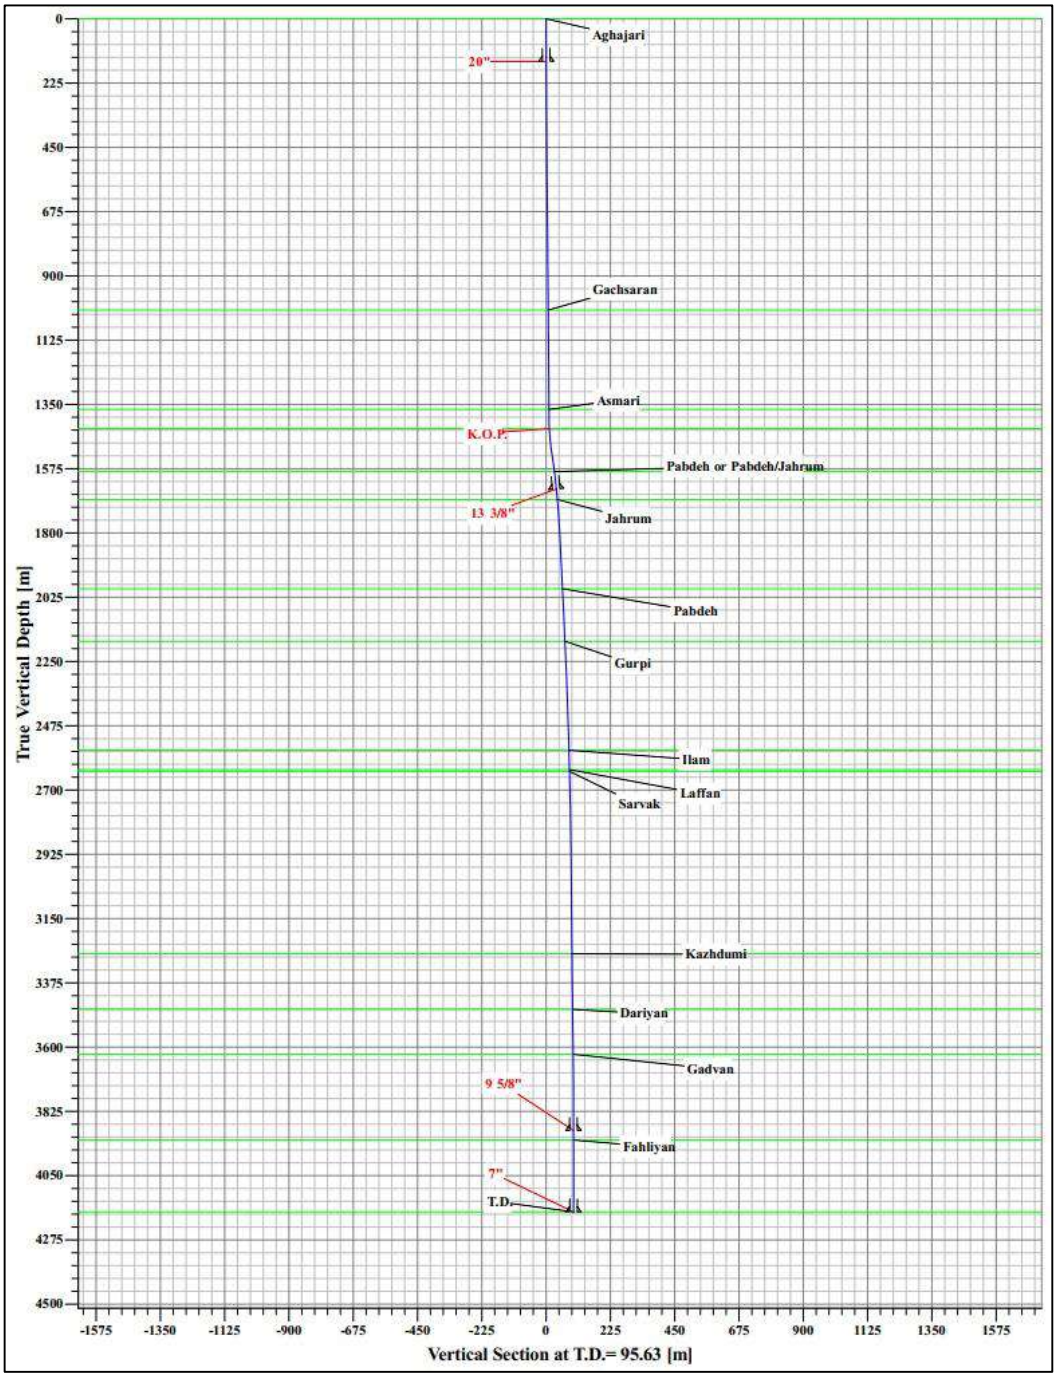


Figure 4-1: AZNS-207 Side – Track Cross Section

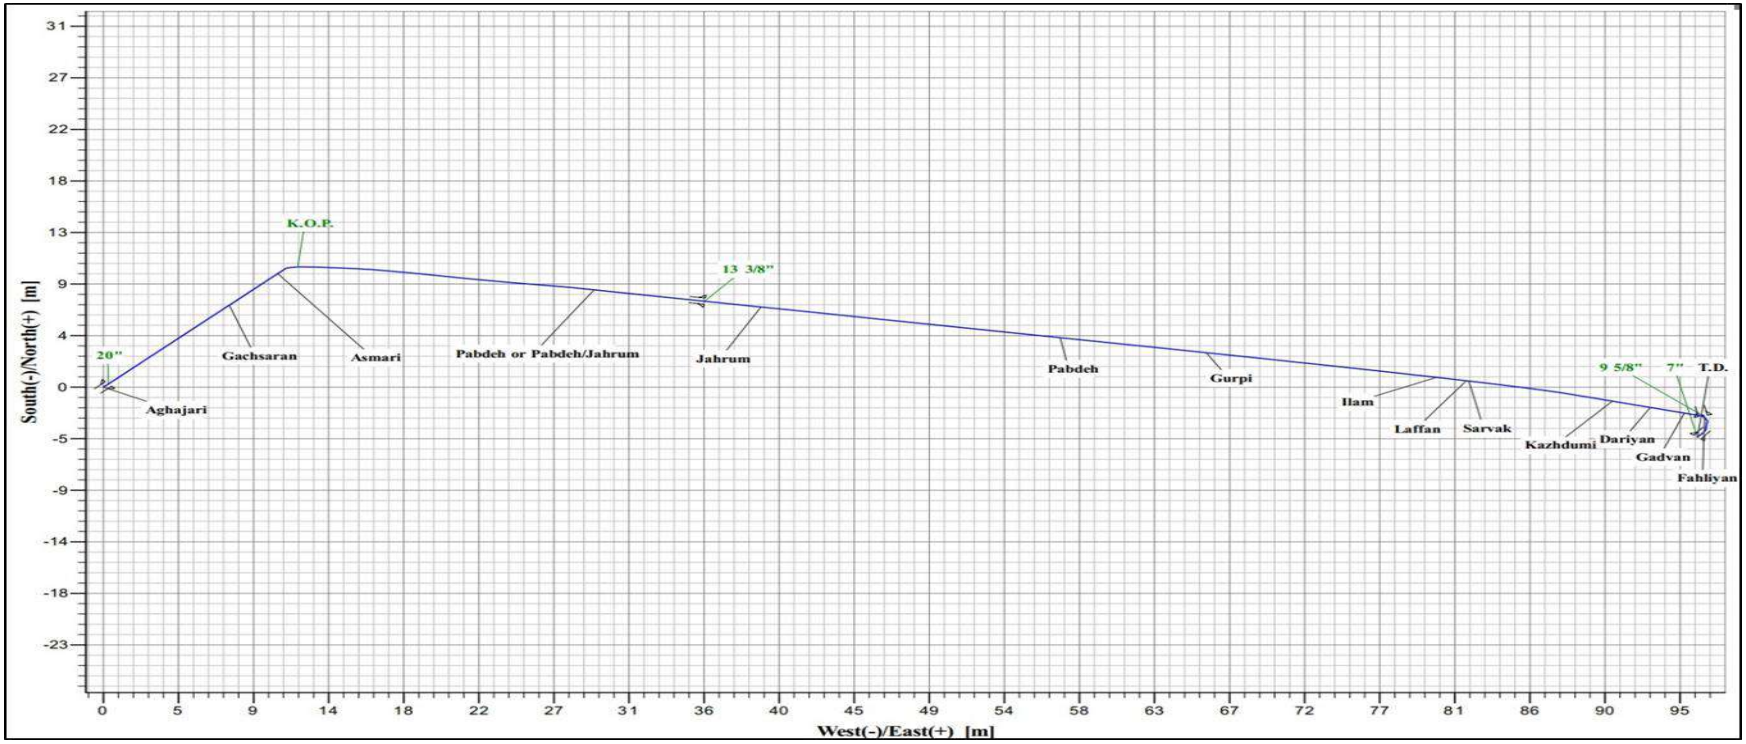


Figure 4-2: AZNS-207 Side – Track Plan View

4.2 Logging and Testing Reports

Wireline Logging Reports

The elaborative Logging Data in Well AZNS-207 are as below:

Log	Company	Hole Size (inch)	Run No.	Depth Interval (m)	Date
Resistivity/Sonic/CDR-GR	Sealand	8 3/8	1	3815 - 4176	2025.02.19
LDT/CNT/NGS	Sealand	8 3/8	2	3820 - 4173	2025.02.19
SBT/CCL/VDL-GR	Sealand	12 1/4	3	1648 - 3887	2025.02.20
SBT/CCL/VDL-GR	Sealand	8 3/8	1	3786 - 4140	2025.03.05

Table 4-8: AZNS-207 List of Electrical Logs

4.3 9-5/8" Casing Cement Evaluation Log Result

Top Depth	Bottom Depth	Interval (M)	Min (dB/ft)	Avg (dB/ft)	Max (dB/ft)	Bonded	Derivative	Channel Risk Pass	Formation	Isolated
1556.65	1648.70	92.05	0.00	6.25	22.10	✓	–	✓	✗	
1648.70	1650.00	1.30	7.31	9.57	11.43	✓	–	✓	✓	
1650.00	1675.80	25.80	4.03	7.67	22.96	✗	–	–	✓	
1675.80	1677.30	1.50	4.78	10.40	18.47	✗	–	–	✗	
1677.30	1677.40	0.10	6.21	8.60	11.80	✓	–	✓	✗	
1677.40	1689.20	11.80	4.30	6.50	14.75	✗	–	–	✗	
1689.20	1689.30	0.10	6.04	7.99	9.66	✓	–	✓	✗	
1689.30	1690.40	1.10	5.17	6.61	8.50	✗	–	–	✗	
1690.40	1700.80	10.40	4.43	7.54	20.25	✗	–	–	✓	
1700.80	1701.00	0.20	7.27	11.13	16.22	✓	–	✓	✓	
1701.00	1724.80	23.80	3.50	6.95	19.45	✗	–	–	✓	
1724.80	1724.90	0.10	7.11	9.64	12.63	✓	–	✓	✓	
1724.90	1760.50	35.60	4.11	7.05	21.38	✗	–	–	✓	
1760.50	1760.60	0.10	6.40	11.01	15.42	✓	–	✓	✓	
1760.60	1772.50	11.90	3.97	7.10	19.89	✗	–	–	✓	
1772.50	1772.60	0.10	6.87	10.33	13.35	✓	–	✓	✓	
1772.60	1799.80	27.20	4.18	7.58	17.53	✗	–	–	✓	
1799.80	1800.00	0.20	7.50	8.69	10.99	✓	–	✓	✓	
1800.00	1800.30	0.30	7.38	8.67	11.20	✗	–	–	✓	
1800.30	1800.60	0.30	7.56	8.68	11.20	✓	–	✓	✓	
1800.60	1801.10	0.50	7.37	8.52	11.22	✗	–	–	✓	
1801.10	1801.40	0.30	7.47	8.56	10.61	✓	–	✓	✓	
1801.40	1802.20	0.80	6.55	8.55	11.19	✗	–	–	✓	
1802.20	1802.30	0.10	7.46	8.64	10.37	✓	–	✓	✓	
1802.30	1808.80	6.50	5.34	8.41	18.84	✗	–	–	✓	
1808.80	1808.90	0.10	6.22	9.24	13.46	✓	–	✓	✓	
1808.90	1855.80	46.90	4.72	7.85	18.20	✗	–	–	✓	
1855.80	1855.90	0.10	6.52	8.99	12.96	✓	–	✓	✓	
1855.90	1868.00	12.10	4.23	7.60	16.43	✗	–	–	✓	
1868.00	1868.10	0.10	7.25	8.42	10.55	✓	–	✓	✓	
1868.10	1927.80	59.70	4.04	7.57	19.95	✗	–	–	✓	
1927.80	1927.90	0.10	6.49	8.73	11.39	✓	–	✓	✓	
1927.90	1952.00	24.10	3.88	7.45	18.39	✗	–	–	✓	
1952.00	1952.10	0.10	6.67	8.25	10.64	✓	–	✓	✓	
1952.10	1964.00	11.90	5.06	7.42	15.97	✗	–	–	✓	
1964.00	1964.10	0.10	6.76	9.24	12.79	✓	–	✓	✓	
1964.10	1976.00	11.90	5.04	7.71	13.90	✗	–	–	✓	
1976.00	1976.20	0.20	6.26	9.37	12.30	✓	–	✓	✓	
1976.20	1989.70	13.50	4.88	8.02	18.01	✗	–	–	✓	
1989.70	1989.80	0.10	7.44	8.45	9.53	✓	–	✓	✓	
1989.80	2012.30	22.50	4.75	7.64	19.10	✗	–	–	✓	
2012.30	2012.40	0.10	5.78	7.70	9.26	✓	–	✓	✓	
2012.40	2025.60	13.20	4.69	7.86	17.89	✗	–	–	✓	
2025.60	2025.70	0.10	7.28	8.34	9.62	✓	–	✓	✓	
2025.70	2039.70	14.00	4.69	8.13	17.94	✗	–	–	✓	
2039.70	2040.10	0.40	7.16	8.45	10.07	✓	–	✓	✓	
2040.10	2041.00	0.90	6.67	7.98	10.06	✗	–	–	✓	
2041.00	2041.10	0.10	7.47	8.30	8.97	✓	–	✓	✓	
2041.10	2042.30	1.20	6.39	7.88	8.98	✗	–	–	✓	

2042.30	2042.50	0.20	7.20	7.98	8.81	✓	–	✓	✓	
2042.50	2042.80	0.30	7.20	8.11	9.01	✗	–	–	✓	
2042.80	2042.90	0.10	7.44	8.16	9.01	✓	–	✓	✓	
2042.90	2043.60	0.70	6.64	8.05	9.21	✗	–	–	✓	
2043.60	2043.80	0.20	7.51	8.06	8.64	✓	–	✓	✓	
2043.80	2044.40	0.60	6.79	8.22	9.53	✗	–	–	✓	
2044.40	2044.60	0.20	7.18	8.31	9.55	✓	–	✓	✓	
2044.60	2052.60	8.00	5.41	8.22	16.77	✗	–	–	✓	
2052.60	2052.80	0.20	7.35	8.81	10.47	✓	–	✓	✓	
2052.80	2054.90	2.10	6.48	8.61	11.77	✗	–	–	✓	
2054.90	2055.50	0.60	7.56	8.90	10.09	✓	–	✓	✓	
2055.50	2055.70	0.20	7.56	8.95	10.09	✗	–	–	✓	
2055.70	2056.90	1.20	7.57	8.79	10.55	✓	–	✓	✓	
2056.90	2057.30	0.40	7.55	8.65	10.62	✗	–	–	✓	
2057.30	2058.20	0.90	7.19	8.64	10.22	✓	–	✓	✓	
2058.20	2071.70	13.50	4.94	8.12	18.58	✗	–	–	✓	
2071.70	2071.80	0.10	7.38	10.67	15.19	✓	–	✓	✓	
2071.80	2088.80	17.00	5.22	7.64	17.93	✗	–	–	✓	
2088.80	2089.50	0.70	7.62	8.20	9.27	✓	–	✓	✓	
2089.50	2119.40	29.90	3.41	8.06	24.64	✗	–	–	✓	
2119.40	2119.50	0.10	7.15	8.52	10.47	✓	–	✓	✓	
2119.50	2153.50	34.00	5.09	7.44	19.29	✗	–	–	✓	
2153.50	2155.20	1.70	6.02	9.60	17.00	✗	–	–	✗	
2155.20	2155.30	0.10	7.10	10.59	13.71	✓	–	✓	✗	
2155.30	2167.20	11.90	4.27	6.79	18.32	✗	–	–	✗	
2167.20	2167.30	0.10	6.51	8.96	12.18	✓	–	✓	✗	
2167.30	2179.20	11.90	4.09	6.44	14.59	✗	–	–	✗	
2179.20	2179.30	0.10	6.31	9.69	13.35	✓	–	✓	✗	
2179.30	2191.00	11.70	4.19	6.51	22.43	✗	–	–	✗	
2191.00	2191.10	0.10	6.43	12.51	19.84	✓	–	✓	✗	
2191.10	2275.00	83.90	3.64	6.18	23.36	✗	–	–	✗	
2275.00	2275.10	0.10	5.99	8.87	12.35	✓	–	✓	✗	
2275.10	2299.20	24.10	3.87	6.17	18.13	✗	–	–	✗	
2299.20	2299.30	0.10	5.77	8.96	12.85	✓	–	✓	✗	
2299.30	2323.20	23.90	3.88	6.14	19.50	✗	–	–	✗	
2323.20	2323.30	0.10	6.92	11.16	18.78	✓	–	✓	✗	
2323.30	2347.80	24.50	4.27	6.16	16.75	✗	–	–	✗	
2347.80	2352.10	4.30	4.45	6.56	10.41	✗	–	–	✓	
2352.10	2356.20	4.10	7.62	9.84	14.35	✓	–	✓	✓	
2356.20	2357.50	1.30	5.04	8.51	11.47	✗	–	–	✓	
2357.50	2361.40	3.90	6.88	11.85	19.89	✓	–	✓	✓	
2361.40	2361.50	0.10	7.60	9.97	12.46	✗	–	–	✓	
2361.50	2365.30	3.80	7.53	11.08	15.84	✓	–	✓	✓	
2365.30	2365.40	0.10	7.53	10.56	14.02	✗	–	–	✓	
2365.40	2365.60	0.20	7.51	10.30	13.47	✓	–	✓	✓	
2365.60	2367.00	1.40	6.56	9.81	13.64	✗	–	–	✓	
2367.00	2368.00	1.00	7.11	10.53	14.63	✓	–	✓	✓	
2368.00	2368.50	0.50	6.92	10.75	14.84	✗	–	–	✓	
2368.50	2369.20	0.70	6.80	11.10	17.72	✓	–	✓	✓	
2369.20	2370.50	1.30	5.65	12.18	19.71	✗	–	–	✓	

2370.50	2370.60	0.10	7.32	12.51	17.58	✓	–	✓	✓	
2370.60	2370.70	0.10	7.32	10.62	14.93	✗	–	–	✓	
2370.70	2371.40	0.70	7.32	10.11	14.93	✓	–	✓	✓	
2371.40	2379.60	8.20	3.87	6.65	12.35	✗	–	–	✓	
2379.60	2382.50	2.90	4.41	7.69	15.34	✗	–	–	✗	
2382.50	2382.60	0.10	7.13	11.86	15.34	✓	–	✓	✗	
2382.60	2396.30	13.70	4.14	6.24	15.56	✗	–	–	✗	
2396.30	2404.60	8.30	4.50	6.49	9.68	✗	–	–	✓	
2404.60	2406.20	1.60	5.75	9.20	14.70	✗	–	–	✗	
2406.20	2406.30	0.10	7.20	11.00	14.61	✓	–	✓	✗	
2406.30	2431.30	25.00	4.06	6.22	15.83	✗	–	–	✗	
2431.30	2435.40	4.10	5.03	6.71	8.35	✗	–	–	✓	
2435.40	2442.70	7.30	4.33	6.75	15.72	✗	–	–	✗	
2442.70	2446.70	4.00	4.69	6.88	10.65	✗	–	–	✓	
2446.70	2453.50	6.80	4.27	6.85	17.66	✗	–	–	✗	
2453.50	2453.60	0.10	7.01	10.63	15.55	✓	–	✓	✗	
2453.60	2489.20	35.60	3.65	6.32	19.40	✗	–	–	✗	
2489.20	2489.30	0.10	6.25	11.15	16.39	✓	–	✓	✗	
2489.30	2547.90	58.60	3.72	6.25	18.45	✗	–	–	✗	
2547.90	2548.00	0.10	6.59	8.38	10.45	✓	–	✓	✗	
2548.00	2559.90	11.90	4.33	6.49	17.32	✗	–	–	✗	
2559.90	2560.00	0.10	5.98	9.06	12.61	✓	–	✓	✗	
2560.00	2608.20	48.20	4.21	6.54	23.32	✗	–	–	✗	
2608.20	2608.30	0.10	7.28	11.33	16.80	✓	–	✓	✗	
2608.30	2631.90	23.60	3.74	6.26	20.00	✗	–	–	✗	
2631.90	2632.00	0.10	6.72	10.50	15.49	✓	–	✓	✗	
2632.00	2640.90	8.90	4.40	5.79	8.97	✗	–	–	✗	
2640.90	2643.70	2.80	4.22	7.15	16.44	✗	–	–	✓	
2643.70	2643.80	0.10	6.08	10.59	16.44	✓	–	✓	✓	
2643.80	2645.80	2.00	4.20	6.64	10.66	✗	–	–	✓	
2645.80	2646.50	0.70	7.46	9.54	11.06	✓	–	✓	✓	
2646.50	2666.40	19.90	3.88	6.60	17.29	✗	–	–	✓	
2666.40	2666.50	0.10	7.00	8.24	10.69	✓	–	✓	✓	
2666.50	2669.40	2.90	5.05	9.03	17.08	✓	–	✓	✓	
2669.40	2811.20	141.80	3.14	6.37	20.57	✗	–	–	✗	
2811.20	2811.30	0.10	6.30	8.79	11.48	✓	–	✓	✗	
2811.30	2871.80	60.50	3.78	6.13	19.26	✗	–	–	✗	
2871.80	2873.60	1.80	5.12	7.17	10.82	✗	–	–	✓	
2873.60	2873.70	0.10	7.31	9.67	11.28	✓	–	✓	✓	
2873.70	2874.90	1.20	5.58	9.65	13.15	✗	–	–	✓	
2874.90	2888.80	13.90	7.62	13.17	20.87	✓	–	✓	✓	
2888.80	2891.40	2.60	4.96	10.95	17.90	✗	–	–	✓	
2891.40	2892.10	0.70	6.89	13.00	19.34	✓	–	✓	✓	
2892.10	2892.60	0.50	5.28	9.67	15.72	✗	–	–	✓	
2892.60	2895.50	2.90	5.47	13.13	20.70	✓	–	✓	✓	
2895.50	2898.10	2.60	4.34	6.48	12.30	✗	–	–	✓	
2898.10	2899.40	1.30	7.27	12.13	14.71	✓	–	✓	✓	
2899.40	2900.70	1.30	5.19	7.76	12.35	✗	–	–	✓	
2900.70	2900.80	0.10	7.33	9.08	12.35	✓	–	✓	✓	
2900.80	2901.90	1.10	5.62	7.80	12.09	✗	–	–	✓	

2901.90	2905.00	3.10	7.29	11.38	15.36	✓	–	✓	✓	
2905.00	2919.70	14.70	4.54	7.91	19.26	✗	–	–	✓	
2919.70	2920.30	0.60	7.27	10.82	14.13	✓	–	✓	✓	
2920.30	2920.60	0.30	7.07	10.28	14.40	✗	–	–	✓	
2920.60	2920.80	0.20	7.57	10.22	14.40	✓	–	✓	✓	
2920.80	2920.90	0.10	7.57	9.67	13.55	✗	–	–	✓	
2920.90	2921.00	0.10	6.89	9.12	12.57	✓	–	✓	✓	
2921.00	2921.30	0.30	6.46	9.25	13.75	✗	–	–	✓	
2921.30	2924.20	2.90	7.25	10.52	14.74	✓	–	✓	✓	
2924.20	2924.40	0.20	7.25	9.40	11.58	✗	–	–	✓	
2924.40	2925.20	0.80	7.07	9.47	12.86	✓	–	✓	✓	
2925.20	2925.80	0.60	6.34	8.64	11.72	✗	–	–	✓	
2925.80	2925.90	0.10	6.88	8.35	11.18	✓	–	✓	✓	
2925.90	2931.70	5.80	4.89	8.59	22.89	✗	–	–	✓	
2931.70	2931.90	0.20	6.95	11.75	18.51	✓	–	✓	✓	
2931.90	2932.60	0.70	5.84	8.56	11.70	✗	–	–	✓	
2932.60	2932.90	0.30	7.51	8.50	9.64	✓	–	✓	✓	
2932.90	2942.00	9.10	4.11	7.60	13.77	✗	–	–	✓	
2942.00	2942.30	0.30	6.97	10.15	13.51	✓	–	✓	✓	
2942.30	2943.70	1.40	5.29	11.88	20.61	✗	–	–	✓	
2943.70	2943.80	0.10	6.85	11.44	17.02	✓	–	✓	✓	
2943.80	2959.90	16.10	4.12	6.73	17.60	✗	–	–	✓	
2959.90	2960.00	0.10	7.43	8.77	11.28	✓	–	✓	✓	
2960.00	2967.70	7.70	4.80	7.31	21.66	✗	–	–	✓	
2967.70	2967.80	0.10	7.15	13.35	21.66	✓	–	✓	✓	
2967.80	2989.70	21.90	4.38	6.84	15.09	✗	–	–	✓	
2989.70	3009.50	19.80	4.20	7.34	18.44	✗	–	–	✗	
3009.50	3027.20	17.70	5.13	7.82	21.11	✗	–	–	✓	
3027.20	3027.30	0.10	7.50	11.37	16.11	✓	–	✓	✓	
3027.30	3038.90	11.60	4.09	8.25	18.42	✗	–	–	✓	
3038.90	3039.00	0.10	7.57	9.98	11.86	✓	–	✓	✓	
3039.00	3049.00	10.00	5.88	8.36	11.86	✗	–	–	✓	
3049.00	3049.20	0.20	7.26	9.08	11.71	✓	–	✓	✓	
3049.20	3049.50	0.30	6.99	8.89	11.71	✗	–	–	✓	
3049.50	3050.80	1.30	6.74	12.10	18.66	✓	–	✓	✓	
3050.80	3062.70	11.90	5.03	8.14	19.46	✗	–	–	✓	
3062.70	3063.20	0.50	7.16	10.24	17.76	✓	–	✓	✓	
3063.20	3073.20	10.00	5.58	8.03	11.34	✗	–	–	✓	
3073.20	3074.90	1.70	7.18	12.60	24.39	✓	–	✓	✓	
3074.90	3076.20	1.30	5.88	8.05	10.76	✗	–	–	✓	
3076.20	3076.40	0.20	7.46	8.36	9.66	✓	–	✓	✓	
3076.40	3076.60	0.20	7.45	8.71	10.01	✗	–	–	✓	
3076.60	3076.80	0.20	7.60	8.63	10.01	✓	–	✓	✓	
3076.80	3076.90	0.10	7.60	8.51	10.15	✗	–	–	✓	
3076.90	3077.10	0.20	7.39	8.51	10.31	✓	–	✓	✓	
3077.10	3077.40	0.30	7.39	8.63	10.45	✗	–	–	✓	
3077.40	3077.60	0.20	7.62	9.17	11.37	✓	–	✓	✓	
3077.60	3077.70	0.10	7.62	9.16	11.37	✗	–	–	✓	
3077.70	3078.50	0.80	7.54	8.81	11.37	✓	–	✓	✓	
3078.50	3081.20	2.70	6.61	8.32	10.84	✗	–	–	✓	

3081.20	3081.50	0.30	7.24	8.60	11.10	✓	–	✓	✓	
3081.50	3081.70	0.20	7.19	8.61	11.35	✗	–	–	✓	
3081.70	3082.00	0.30	7.19	8.78	11.35	✓	–	✓	✓	
3082.00	3082.40	0.40	6.95	8.96	11.58	✗	–	–	✓	
3082.40	3083.00	0.60	7.57	8.73	10.98	✓	–	✓	✓	
3083.00	3083.10	0.10	7.57	8.45	10.98	✗	–	–	✓	
3083.10	3083.20	0.10	7.56	8.32	10.32	✓	–	✓	✓	
3083.20	3083.30	0.10	7.56	8.42	10.36	✗	–	–	✓	
3083.30	3084.90	1.60	6.59	8.84	11.63	✓	–	✓	✓	
3084.90	3085.50	0.60	6.32	8.49	10.97	✗	–	–	✓	
3085.50	3087.00	1.50	6.46	10.44	16.52	✓	–	✓	✓	
3087.00	3091.10	4.10	5.72	7.83	10.57	✗	–	–	✓	
3091.10	3091.20	0.10	7.34	8.44	10.84	✓	–	✓	✓	
3091.20	3091.60	0.40	6.63	8.52	10.84	✗	–	–	✓	
3091.60	3092.20	0.60	7.10	8.38	9.39	✓	–	✓	✓	
3092.20	3093.70	1.50	5.95	8.01	10.12	✗	–	–	✓	
3093.70	3094.00	0.30	7.53	8.40	9.53	✓	–	✓	✓	
3094.00	3094.40	0.40	6.65	8.11	9.26	✗	–	–	✓	
3094.40	3095.00	0.60	7.51	9.04	10.43	✓	–	✓	✓	
3095.00	3095.80	0.80	6.73	9.16	11.13	✗	–	–	✓	
3095.80	3097.40	1.60	7.28	8.92	10.92	✓	–	✓	✓	
3097.40	3098.00	0.60	6.90	8.04	9.30	✗	–	–	✓	
3098.00	3099.00	1.00	7.33	12.05	17.83	✓	–	✓	✓	
3099.00	3110.50	11.50	3.97	6.92	21.10	✗	–	–	✓	
3110.50	3110.60	0.10	6.40	12.95	19.85	✓	–	✓	✓	
3110.60	3134.20	23.60	3.60	7.17	18.96	✗	–	–	✓	
3134.20	3134.30	0.10	6.19	10.48	15.70	✓	–	✓	✓	
3134.30	3140.10	5.80	4.12	6.20	9.87	✗	–	–	✓	
3140.10	3148.80	8.70	3.82	7.25	17.38	✗	–	–	✗	
3148.80	3158.20	9.40	4.99	7.43	18.40	✗	–	–	✓	
3158.20	3158.30	0.10	6.22	9.94	14.86	✓	–	✓	✓	
3158.30	3165.60	7.30	4.97	7.45	9.82	✗	–	–	✓	
3165.60	3165.80	0.20	7.07	8.49	10.18	✓	–	✓	✓	
3165.80	3167.80	2.00	5.91	8.69	10.95	✗	–	–	✓	
3167.80	3168.00	0.20	7.56	9.17	10.30	✓	–	✓	✓	
3168.00	3175.80	7.80	4.28	7.79	17.08	✗	–	–	✓	
3175.80	3175.90	0.10	7.52	8.47	9.17	✓	–	✓	✓	
3175.90	3176.50	0.60	6.97	8.49	10.18	✗	–	–	✓	
3176.50	3180.80	4.30	7.33	9.89	12.30	✓	–	✓	✓	
3180.80	3181.00	0.20	7.55	10.39	13.67	✗	–	–	✓	
3181.00	3181.10	0.10	7.55	10.62	14.62	✓	–	✓	✓	
3181.10	3182.30	1.20	1.72	9.30	15.16	✗	–	–	✓	
3182.30	3183.30	1.00	7.56	10.60	12.78	✓	–	✓	✓	
3183.30	3183.70	0.40	7.45	10.25	12.82	✗	–	–	✓	
3183.70	3183.90	0.20	7.35	10.30	13.53	✓	–	✓	✓	
3183.90	3192.30	8.40	4.91	7.83	13.63	✗	–	–	✓	
3192.30	3192.40	0.10	7.79	9.45	12.09	✓	–	✓	✓	
3192.40	3199.20	6.80	5.20	8.93	22.82	✗	–	–	✓	
3199.20	3199.40	0.20	7.21	9.08	11.18	✓	–	✓	✓	
3199.40	3199.80	0.40	6.58	8.54	11.16	✗	–	–	✓	

3199.80	3200.40	0.60	7.20	9.12	11.73	✓	–	✓	✓	
3200.40	3200.90	0.50	6.47	9.15	11.82	✗	–	–	✓	
3200.90	3201.20	0.30	7.53	8.90	11.37	✓	–	✓	✓	
3201.20	3202.10	0.90	7.22	8.65	12.52	✗	–	–	✓	
3202.10	3202.20	0.10	7.46	9.01	12.52	✓	–	✓	✓	
3202.20	3214.40	12.20	5.02	7.88	18.34	✗	–	–	✓	
3214.40	3214.50	0.10	7.59	8.90	10.31	✓	–	✓	✓	
3214.50	3214.70	0.20	7.53	8.90	10.31	✗	–	–	✓	
3214.70	3215.00	0.30	7.53	9.08	10.78	✓	–	✓	✓	
3215.00	3230.90	15.90	5.07	7.83	18.73	✗	–	–	✓	
3230.90	3231.70	0.80	7.45	9.04	11.86	✓	–	✓	✓	
3231.70	3232.00	0.30	7.30	9.25	12.22	✗	–	–	✓	
3232.00	3232.40	0.40	7.46	9.28	12.75	✓	–	✓	✓	
3232.40	3232.60	0.20	7.57	9.28	12.93	✗	–	–	✓	
3232.60	3233.00	0.40	7.44	9.59	12.93	✓	–	✓	✓	
3233.00	3234.40	1.40	6.59	8.98	12.85	✗	–	–	✓	
3234.40	3234.50	0.10	7.60	9.06	11.42	✓	–	✓	✓	
3234.50	3235.00	0.50	6.80	8.74	11.42	✗	–	–	✓	
3235.00	3239.80	4.80	7.11	9.60	15.13	✓	–	✓	✓	
3239.80	3240.00	0.20	7.48	9.31	12.72	✗	–	–	✓	
3240.00	3243.20	3.20	7.51	10.31	18.80	✓	–	✓	✓	
3243.20	3243.70	0.50	6.78	8.35	9.53	✗	–	–	✓	
3243.70	3251.80	8.10	7.23	9.81	12.28	✓	–	✓	✓	
3251.80	3251.90	0.10	7.56	8.47	10.03	✗	–	–	✓	
3251.90	3257.90	6.00	7.59	10.69	20.84	✓	–	✓	✓	
3257.90	3258.00	0.10	7.59	9.36	10.44	✗	–	–	✓	
3258.00	3260.00	2.00	7.20	9.57	10.77	✓	–	✓	✓	
3260.00	3260.80	0.80	6.85	9.38	10.66	✗	–	–	✓	
3260.80	3261.80	1.00	7.50	9.69	11.04	✓	–	✓	✓	
3261.80	3261.90	0.10	7.50	9.88	11.04	✗	–	–	✓	
3261.90	3262.40	0.50	7.49	9.71	10.91	✓	–	✓	✓	
3262.40	3262.60	0.20	7.49	9.67	10.79	✗	–	–	✓	
3262.60	3264.30	1.70	7.52	9.59	11.22	✓	–	✓	✓	
3264.30	3265.40	1.10	7.52	14.26	25.46	✓	–	✓	✓	
3265.40	3265.60	0.20	7.39	9.89	10.91	✓	–	✓	✓	
3265.60	3266.20	0.60	7.05	9.28	10.88	✗	–	–	✓	
3266.20	3266.40	0.20	7.42	9.04	10.27	✓	–	✓	✓	
3266.40	3267.30	0.90	7.04	9.20	11.56	✗	–	–	✓	
3267.30	3271.60	4.30	7.49	10.17	13.34	✓	–	✓	✓	
3271.60	3276.10	4.50	5.00	7.10	11.55	✗	–	–	✓	
3276.10	3288.40	12.30	7.69	12.07	18.50	✓	–	✓	✓	
3288.40	3291.30	2.90	4.76	9.38	16.32	✗	–	–	✓	
3291.30	3295.30	4.00	7.12	10.01	14.74	✓	–	✓	✓	
3295.30	3296.00	0.70	6.69	10.32	14.43	✗	–	–	✓	
3296.00	3296.10	0.10	7.50	10.41	14.11	✓	–	✓	✓	
3296.10	3296.30	0.20	7.50	10.29	13.71	✗	–	–	✓	
3296.30	3296.70	0.40	7.43	10.46	14.71	✓	–	✓	✓	
3296.70	3297.30	0.60	7.23	10.42	14.71	✗	–	–	✓	
3297.30	3298.70	1.40	7.36	10.57	14.47	✓	–	✓	✓	
3298.70	3299.00	0.30	7.24	9.98	12.80	✗	–	–	✓	

3299.00	3309.20	10.20	6.96	11.20	23.93	✓	–	✓	✓	
3309.20	3309.50	0.30	6.62	9.90	14.05	✗	–	–	✓	
3309.50	3310.00	0.50	7.09	9.99	13.01	✓	–	✓	✓	
3310.00	3310.90	0.90	6.74	9.09	12.35	✗	–	–	✓	
3310.90	3311.30	0.40	7.42	8.98	10.99	✓	–	✓	✓	
3311.30	3311.60	0.30	7.21	9.12	11.30	✗	–	–	✓	
3311.60	3323.80	12.20	7.38	11.38	18.68	✓	–	✓	✓	
3323.80	3324.00	0.20	7.35	10.70	14.30	✗	–	–	✓	
3324.00	3326.10	2.10	7.35	12.15	19.77	✓	–	✓	✓	
3326.10	3326.20	0.10	7.60	10.30	12.41	✗	–	–	✓	
3326.20	3326.60	0.40	7.53	10.19	12.56	✓	–	✓	✓	
3326.60	3328.20	1.60	7.42	10.20	12.60	✗	–	–	✓	
3328.20	3357.80	29.60	7.56	10.79	16.20	✓	–	✓	✓	
3357.80	3358.40	0.60	7.21	10.01	11.73	✗	–	–	✓	
3358.40	3374.20	15.80	7.62	11.11	16.76	✓	–	✓	✓	
3374.20	3374.50	0.30	7.57	10.58	12.79	✗	–	–	✓	
3374.50	3408.30	33.80	7.56	11.54	19.32	✓	–	✓	✓	
3408.30	3408.50	0.20	7.53	9.68	12.16	✗	–	–	✓	
3408.50	3429.30	20.80	7.53	11.33	16.77	✓	–	✓	✓	
3429.30	3430.80	1.50	6.21	9.76	12.44	✗	–	–	✓	
3430.80	3431.90	1.10	6.87	13.36	17.88	✓	–	✓	✓	
3431.90	3433.40	1.50	5.36	9.13	13.62	✗	–	–	✓	
3433.40	3435.10	1.70	7.48	10.79	14.38	✓	–	✓	✓	
3435.10	3435.60	0.50	7.32	11.07	14.02	✗	–	–	✓	
3435.60	3436.20	0.60	7.50	11.41	13.65	✓	–	✓	✓	
3436.20	3437.10	0.90	6.76	10.79	12.85	✗	–	–	✓	
3437.10	3480.30	43.20	7.46	12.63	18.69	✓	–	✓	✓	
3480.30	3481.30	1.00	6.39	11.44	13.71	✗	–	–	✓	
3481.30	3486.90	5.60	7.36	12.43	13.90	✓	–	✓	✓	
3486.90	3487.40	0.50	6.91	11.70	13.57	✗	–	–	✓	
3487.40	3494.60	7.20	7.43	13.08	21.16	✓	–	✓	✓	
3494.60	3495.60	1.00	6.88	10.97	13.73	✗	–	–	✓	
3495.60	3508.40	12.80	7.52	11.91	16.89	✓	–	✓	✓	
3508.40	3516.70	8.30	5.10	8.51	15.09	✗	–	–	✓	
3516.70	3517.00	0.30	7.59	9.97	11.68	✓	–	✓	✓	
3517.00	3517.20	0.20	7.54	10.01	11.71	✗	–	–	✓	
3517.20	3518.70	1.50	7.19	10.62	12.90	✓	–	✓	✓	
3518.70	3529.10	10.40	4.82	7.99	15.99	✗	–	–	✓	
3529.10	3532.60	3.50	7.26	11.42	13.76	✓	–	✓	✓	
3532.60	3533.80	1.20	6.10	8.07	11.55	✗	–	–	✓	
3533.80	3534.00	0.20	7.43	9.64	11.79	✓	–	✓	✓	
3534.00	3539.50	5.50	5.97	10.36	19.11	✗	–	–	✓	
3539.50	3539.70	0.20	6.91	11.92	16.00	✓	–	✓	✓	
3539.70	3547.90	8.20	3.57	7.50	12.99	✗	–	–	✓	
3547.90	3551.80	3.90	7.27	11.02	16.22	✓	–	✓	✓	
3551.80	3567.80	16.00	4.57	9.12	16.04	✗	–	–	✓	
3567.80	3568.60	0.80	7.46	11.07	14.50	✓	–	✓	✓	
3568.60	3574.70	6.10	4.98	9.79	14.50	✗	–	–	✓	
3574.70	3574.80	0.10	7.32	11.13	13.69	✓	–	✓	✓	
3574.80	3576.90	2.10	7.35	11.88	15.79	✗	–	–	✓	

3576.90	3581.00	4.10	7.03	11.62	14.09	✓	–	✓	✓	
3581.00	3582.30	1.30	5.69	10.13	13.80	✗	–	–	✓	
3582.30	3587.90	5.60	7.45	12.99	19.51	✓	–	✓	✓	
3587.90	3590.90	3.00	5.22	9.54	14.07	✗	–	–	✓	
3590.90	3592.10	1.20	7.58	11.42	13.88	✓	–	✓	✓	
3592.10	3594.10	2.00	4.70	10.18	14.37	✗	–	–	✓	
3594.10	3595.30	1.20	7.28	12.31	14.46	✓	–	✓	✓	
3595.30	3595.60	0.30	7.26	12.06	14.35	✗	–	–	✓	
3595.60	3601.50	5.90	7.28	13.25	19.23	✓	–	✓	✓	
3601.50	3602.90	1.40	4.89	9.59	13.87	✗	–	–	✓	
3602.90	3608.30	5.40	7.07	11.93	13.71	✓	–	✓	✓	
3608.30	3609.70	1.40	5.19	9.02	13.11	✗	–	–	✓	
3609.70	3610.60	0.90	7.20	11.56	14.12	✓	–	✓	✓	
3610.60	3611.00	0.40	6.58	10.68	14.12	✗	–	–	✓	
3611.00	3614.00	3.00	7.00	12.53	16.29	✓	–	✓	✓	
3614.00	3615.10	1.10	6.54	10.28	13.20	✗	–	–	✓	
3615.10	3619.60	4.50	7.21	11.87	13.88	✓	–	✓	✓	
3619.60	3621.90	2.30	4.65	10.71	13.88	✗	–	–	✓	
3621.90	3622.90	1.00	7.66	10.61	14.19	✓	–	✓	✓	
3622.90	3631.40	8.50	4.17	11.80	18.27	✗	–	–	✓	
3631.40	3636.20	4.80	7.00	12.44	19.18	✓	–	✓	✓	
3636.20	3637.20	1.00	6.02	9.95	14.45	✗	–	–	✓	
3637.20	3638.20	1.00	7.35	11.37	14.90	✓	–	✓	✓	
3638.20	3638.60	0.40	7.26	11.48	14.70	✗	–	–	✓	
3638.60	3644.50	5.90	6.52	13.26	15.52	✓	–	✓	✓	
3644.50	3648.60	4.10	3.96	8.60	17.01	✗	–	–	✓	
3648.60	3651.30	2.70	7.46	12.38	15.24	✓	–	✓	✓	
3651.30	3651.50	0.20	7.36	10.39	12.41	✗	–	–	✓	
3651.50	3661.10	9.60	6.30	13.45	17.95	✓	–	✓	✓	
3661.10	3662.30	1.20	3.28	9.53	14.15	✗	–	–	✓	
3662.30	3662.80	0.50	6.76	11.35	14.27	✓	–	✓	✓	
3662.80	3664.00	1.20	5.38	7.90	12.16	✗	–	–	✓	
3664.00	3664.10	0.10	6.75	9.83	12.60	✓	–	✓	✓	
3664.10	3667.00	2.90	4.12	8.02	13.74	✗	–	–	✓	
3667.00	3675.20	8.20	7.47	13.19	17.96	✓	–	✓	✓	
3675.20	3676.20	1.00	6.99	12.43	15.92	✗	–	–	✓	
3676.20	3681.10	4.90	6.76	14.11	17.35	✓	–	✓	✓	
3681.10	3682.40	1.30	6.07	11.17	15.20	✗	–	–	✓	
3682.40	3698.60	16.20	7.19	13.00	17.48	✓	–	✓	✓	
3698.60	3700.60	2.00	3.48	7.76	12.64	✗	–	–	✓	
3700.60	3718.60	18.00	5.87	12.72	17.53	✓	–	✓	✓	
3718.60	3719.80	1.20	3.66	6.55	10.71	✗	–	–	✓	
3719.80	3754.50	34.70	6.90	13.19	17.55	✓	–	✓	✓	
3754.50	3757.00	2.50	4.33	8.03	13.26	✗	–	–	✓	
3757.00	3760.90	3.90	7.42	11.66	14.45	✓	–	✓	✓	
3760.90	3763.00	2.10	5.18	8.32	13.26	✗	–	–	✓	
3763.00	3774.70	11.70	7.49	13.41	18.04	✓	–	✓	✓	
3774.70	3775.90	1.20	4.46	8.34	11.92	✗	–	–	✓	
3775.90	3776.50	0.60	7.38	10.47	12.20	✓	–	✓	✓	
3776.50	3776.80	0.30	6.98	10.66	12.82	✗	–	–	✓	

3776.80	3781.80	5.00	6.79	12.43	14.99	✓	–	✓	✓	
3781.80	3782.30	0.50	6.26	11.80	14.07	✗	–	–	✓	
3782.30	3790.60	8.30	6.57	12.73	19.17	✓	–	✓	✓	
3790.60	3791.10	0.50	6.05	11.11	15.68	✗	–	–	✓	
3791.10	3794.60	3.50	7.17	11.86	14.90	✓	–	✓	✓	
3794.60	3795.10	0.50	6.52	9.37	11.77	✗	–	–	✓	
3795.10	3796.50	1.40	7.20	11.08	13.58	✓	–	✓	✓	
3796.50	3796.80	0.30	7.12	10.49	12.82	✗	–	–	✓	
3796.80	3801.30	4.50	7.26	12.12	14.77	✓	–	✓	✓	
3801.30	3801.80	0.50	6.77	9.08	11.49	✗	–	–	✓	
3801.80	3804.50	2.70	7.21	12.64	16.84	✓	–	✓	✓	
3804.50	3804.80	0.30	7.14	11.13	13.00	✗	–	–	✓	
3804.80	3808.60	3.80	7.55	13.20	15.17	✓	–	✓	✓	
3808.60	3808.90	0.30	7.24	10.26	12.61	✗	–	–	✓	
3808.90	3818.80	9.90	6.97	13.07	19.41	✓	–	✓	✓	
3818.80	3819.60	0.80	6.14	8.13	11.24	✗	–	–	✓	
3819.60	3820.50	0.90	7.53	9.82	12.47	✓	–	✓	✓	
3820.50	3825.10	4.60	5.02	8.67	12.23	✗	–	–	✓	
3825.10	3828.60	3.50	7.61	12.98	17.10	✓	–	✓	✓	
3828.60	3829.30	0.70	5.81	9.14	13.07	✗	–	–	✓	
3829.30	3837.50	8.20	6.27	12.49	14.83	✓	–	✓	✓	
3837.50	3838.70	1.20	5.22	11.04	16.29	✗	–	–	✓	
3838.70	3847.00	8.30	6.84	12.60	15.69	✓	–	✓	✓	
3847.00	3847.50	0.50	6.56	9.23	11.27	✗	–	–	✓	
3847.50	3848.00	0.50	7.46	9.86	12.50	✓	–	✓	✓	
3848.00	3848.50	0.50	6.95	9.35	12.69	✗	–	–	✓	
3848.50	3848.90	0.40	7.17	8.75	11.14	✓	–	✓	✓	
3848.90	3851.50	2.60	5.10	9.99	15.67	✗	–	–	✓	
3851.50	3854.20	2.70	7.29	9.89	13.35	✓	–	✓	✓	
3854.20	3854.80	0.60	7.03	8.60	12.36	✗	–	–	✓	
3854.80	3860.70	5.90	7.20	10.95	13.76	✓	–	✓	✓	
3860.70	3862.00	1.30	6.26	8.56	11.84	✗	–	–	✓	
3862.00	3863.20	1.20	7.16	11.99	16.92	✓	–	✓	✓	
3863.20	3864.30	1.10	5.58	9.33	12.42	✗	–	–	✓	
3864.30	3865.60	1.30	7.60	9.18	10.56	✓	–	✓	✓	
3865.60	3866.00	0.40	7.43	9.13	10.29	✗	–	–	✓	
3866.00	3868.80	2.80	7.26	10.35	13.63	✓	–	✓	✓	
3868.80	3870.30	1.50	4.69	7.69	10.62	✗	–	–	✓	
3870.30	3870.70	0.40	6.68	8.99	10.70	✓	–	✓	✓	
3870.70	3871.40	0.70	6.12	7.95	9.92	✗	–	–	✓	
3871.40	3877.40	6.00	7.55	10.87	16.47	✓	–	✓	✓	
3877.40	3889.95	12.55	3.75	6.07	13.88	✗	–	–	✓	

Figure 4-3: AZNS-207 9-5/8" CMT Evaluation Log

4.4 7" Liner Cement Evaluation Log Result

Top Depth	Bottom Depth	Interval (M)	Min (dB/ft)	Avg (dB/ft)	Max (dB/ft)	Bonded	Derivative	Channel Risk Pass	Formation	Isolated
3895.00	3902.25	7.25	0.00	8.35	24.12	✓	–	✓	✗	
3902.25	3906.55	4.30	8.78	13.21	15.51	✓	–	✓	✓	
3906.55	3939.45	32.90	3.03	7.47	19.77	✗	–	–	✓	
3939.45	3943.55	4.10	4.50	7.21	12.43	✗	–	–	✗	
3943.55	3950.75	7.20	3.19	7.12	14.01	✗	–	–	✓	
3950.75	3951.15	0.40	7.59	11.09	13.13	✓	–	✓	✓	
3951.15	3952.55	1.40	4.67	8.03	12.13	✗	–	–	✓	
3952.55	3955.85	3.30	7.77	12.37	15.40	✓	–	✓	✓	
3955.85	3957.65	1.80	5.61	10.16	16.86	✗	–	–	✓	
3957.65	3957.75	0.10	6.81	10.10	13.75	✓	–	✓	✓	
3957.75	3959.05	1.30	4.18	8.54	12.02	✗	–	–	✓	
3959.05	3959.15	0.10	7.74	10.41	12.07	✓	–	✓	✓	
3959.15	3959.25	0.10	7.74	10.71	12.47	✗	–	–	✓	
3959.25	3959.85	0.60	6.59	11.68	13.95	✓	–	✓	✓	
3959.85	3959.95	0.10	6.59	10.31	12.67	✗	–	–	✓	
3959.95	3960.25	0.30	6.59	10.99	13.52	✓	–	✓	✓	
3960.25	3961.15	0.90	6.42	8.89	12.42	✗	–	–	✓	
3961.15	3961.95	0.80	7.31	11.57	15.31	✓	–	✓	✓	
3961.95	3962.25	0.30	7.68	10.21	12.07	✗	–	–	✓	
3962.25	3962.65	0.40	7.68	10.55	12.51	✓	–	✓	✓	
3962.65	3962.95	0.30	7.78	10.03	12.92	✗	–	–	✓	
3962.95	3963.45	0.50	8.79	10.95	13.01	✓	–	✓	✓	
3963.45	3965.25	1.80	5.30	8.45	13.46	✗	–	–	✓	
3965.25	3966.05	0.80	8.60	12.14	14.93	✓	–	✓	✓	
3966.05	3966.85	0.80	6.52	9.65	12.72	✗	–	–	✓	
3966.85	3967.45	0.60	6.67	11.40	13.88	✓	–	✓	✓	
3967.45	3967.65	0.20	6.95	10.33	12.97	✗	–	–	✓	
3967.65	3967.95	0.30	6.95	10.30	12.59	✓	–	✓	✓	
3967.95	3968.55	0.60	6.76	9.72	12.36	✗	–	–	✓	
3968.55	3968.65	0.10	6.49	9.71	11.99	✓	–	✓	✓	
3968.65	3977.95	9.30	5.07	8.15	14.66	✗	–	–	✓	
3977.95	3979.65	1.70	7.97	11.97	14.00	✓	–	✓	✓	
3979.65	3979.75	0.10	7.85	10.38	12.23	✗	–	–	✓	
3979.75	3980.65	0.90	7.48	11.95	15.08	✓	–	✓	✓	
3980.65	3981.35	0.70	5.64	9.18	12.61	✗	–	–	✓	
3981.35	3981.45	0.10	9.01	9.68	10.32	✓	–	✓	✓	
3981.45	3983.45	2.00	5.73	10.90	19.19	✗	–	–	✓	
3983.45	3987.85	4.40	7.12	12.52	15.64	✓	–	✓	✓	
3987.85	3988.15	0.30	9.10	10.21	12.43	✗	–	–	✓	
3988.15	3988.65	0.50	9.28	10.72	12.50	✓	–	✓	✓	
3988.65	3988.95	0.30	8.47	10.63	12.61	✗	–	–	✓	
3988.95	3989.55	0.60	7.98	10.78	12.81	✓	–	✓	✓	
3989.55	3990.05	0.50	8.96	10.49	13.00	✗	–	–	✓	
3990.05	3990.45	0.40	9.01	11.10	13.39	✓	–	✓	✓	
3990.45	3990.65	0.20	8.74	11.10	13.39	✗	–	–	✓	
3990.65	3990.85	0.20	8.25	10.68	13.01	✓	–	✓	✓	
3990.85	3992.65	1.80	5.85	9.68	12.95	✗	–	–	✓	
3992.65	3993.05	0.40	8.51	10.79	12.54	✓	–	✓	✓	
3993.05	3993.35	0.30	8.01	11.10	13.68	✗	–	–	✓	

3993.35	3993.75	0.40	8.01	11.92	14.83	✓	–	✓	✓	
3993.75	3995.15	1.40	8.34	12.41	18.82	✗	–	▪	✓	
3995.15	3995.65	0.50	7.59	10.87	14.27	✓	–	✓	✓	
3995.65	4007.45	11.80	4.46	8.17	18.70	✗	–	▪	✓	
4007.45	4010.15	2.70	9.03	12.74	16.05	✓	–	✓	✓	
4010.15	4010.45	0.30	8.23	11.12	14.83	✗	–	▪	✓	
4010.45	4012.35	1.90	7.87	12.83	16.15	✓	–	✓	✓	
4012.35	4030.15	17.80	4.11	7.68	16.54	✗	–	▪	✓	
4030.15	4030.55	0.40	7.79	11.05	13.60	✓	–	✓	✓	
4030.55	4031.25	0.70	6.18	8.80	13.05	✗	–	▪	✓	
4031.25	4033.25	2.00	6.89	13.40	18.70	✓	–	✓	✓	
4033.25	4043.65	10.40	4.24	6.77	13.74	✗	–	▪	✓	
4043.65	4043.75	0.10	5.28	10.98	13.74	✓	–	✓	✓	
4043.75	4053.25	9.50	3.06	9.51	18.15	✗	–	▪	✓	
4053.25	4054.15	0.90	7.24	12.56	15.86	✓	–	✓	✓	
4054.15	4054.45	0.30	8.05	11.69	14.48	✗	–	▪	✓	
4054.45	4055.65	1.20	9.02	12.63	16.21	✓	–	✓	✓	
4055.65	4055.85	0.20	6.80	11.85	14.59	✗	–	▪	✓	
4055.85	4056.05	0.20	6.00	11.27	14.38	✓	–	✓	✓	
4056.05	4056.15	0.10	6.00	11.27	14.72	✗	–	▪	✓	
4056.15	4057.65	1.50	6.00	11.46	16.70	✓	–	✓	✓	
4057.65	4062.85	5.20	3.01	6.28	12.48	✗	–	▪	✓	
4062.85	4063.05	0.20	8.72	10.73	12.28	✓	–	✓	✓	
4063.05	4066.55	3.50	3.34	7.05	11.86	✗	–	▪	✓	
4066.55	4070.95	4.40	7.40	13.01	17.52	✓	–	✓	✓	
4070.95	4080.75	9.80	3.03	7.51	13.92	✗	–	▪	✓	
4080.75	4081.25	0.50	7.89	11.41	13.42	✓	–	✓	✓	
4081.25	4082.65	1.40	6.37	11.61	18.95	✗	–	▪	✓	
4082.65	4082.95	0.30	7.44	11.39	14.92	✓	–	✓	✓	
4082.95	4083.25	0.30	7.43	10.64	13.61	✗	–	▪	✓	
4083.25	4085.35	2.10	7.83	13.19	16.96	✓	–	✓	✓	
4085.35	4101.15	15.80	2.82	7.60	19.75	✗	–	▪	✓	
4101.15	4102.05	0.90	5.17	11.29	13.80	✓	–	✓	✓	
4102.05	4102.55	0.50	4.92	10.71	13.96	✗	–	▪	✓	
4102.55	4102.85	0.30	6.34	9.92	13.48	✓	–	✓	✓	
4102.85	4103.15	0.30	6.34	9.58	12.66	✗	–	▪	✓	
4103.15	4103.95	0.80	7.68	11.67	14.89	✓	–	✓	✓	
4103.95	4109.45	5.50	3.38	9.19	17.51	✗	–	▪	✓	
4109.45	4109.95	0.50	8.77	11.68	13.82	✓	–	✓	✓	
4109.95	4110.55	0.60	6.39	9.99	12.84	✗	–	▪	✓	
4110.55	4111.85	1.30	6.89	11.28	14.28	✓	–	✓	✓	
4111.85	4117.85	6.00	3.96	8.17	12.92	✗	–	▪	✓	
4117.85	4118.35	0.50	7.31	11.00	12.98	✓	–	✓	✓	
4118.35	4118.75	0.40	8.37	11.31	13.82	✗	–	▪	✓	
4118.75	4118.95	0.20	8.85	11.23	13.77	✓	–	✓	✓	

4118.95	4125.35	6.40	4.00	8.52	16.85	✗	–	-	✓	
4125.35	4125.65	0.30	7.43	10.73	13.07	✓	–	✓	✓	
4125.65	4127.45	1.80	6.78	9.31	12.54	✗	–	-	✓	
4127.45	4127.65	0.20	8.69	10.36	12.59	✓	–	✓	✓	
4127.65	4128.75	1.10	5.77	10.39	14.79	✗	–	-	✓	
4128.75	4129.25	0.50	8.41	11.40	14.02	✓	–	✓	✓	
4129.25	4129.35	0.10	8.21	11.65	14.14	✗	–	-	✓	
4129.35	4130.25	0.90	6.33	11.79	15.59	✓	–	✓	✓	
4130.25	4130.45	0.20	8.45	11.59	14.09	✗	–	-	✓	
4130.45	4130.95	0.50	9.37	11.44	13.86	✓	–	✓	✓	
4130.95	4133.15	2.20	3.88	9.97	19.51	✗	–	-	✓	
4133.15	4133.55	0.40	7.56	11.67	14.65	✓	–	✓	✓	
4133.55	4133.65	0.10	7.56	10.22	12.13	✗	–	-	✓	
4133.65	4134.65	1.00	7.33	11.44	14.02	✓	–	✓	✓	
4134.65	4135.45	0.80	4.85	8.93	12.48	✗	–	-	✓	
4135.45	4135.55	0.10	8.43	10.09	11.29	✓	–	✓	✓	
4135.55	4140.55	5.00	5.42	8.77	11.55	✗	–	-	✓	
4140.55	4141.00	0.45	5.45	8.82	11.50	✗	–	-	✗	

Figure 4-4: AZNS-207 7" CMT Evaluation Log

5. Bottom Hole Assembly Record

This is a record of the bottom hole assemblies (BHA) used to drill the various sections of this well.

Each assembly has been treated for every bit run in the hole and besides the listing of the components of the drilling assembly, it also includes additional information of interest pertaining to that run such as the drilling and mud parameters, casing details, highlights of the run, discharge to RPM ratios of down hole motors, hydraulic inferences such as bit efficiencies, annular and impact velocities, ECD, circulating hours that are all inclusive for the bit run, a record of met rage and Bit life for that run and the cumulative life and met rage produced where bits are re-run, tripping times and any other data that might be considered relevant or interesting. The bit data in the BHA record is supplementary to the exclusive listing of the bits used in this well, which can be perused in the BIT RECORD, which precedes this chapter.

Date: 21.10.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #2	Length	Cum Lgth
17 ½" M.T. Bit	0.41	0.41
9 ½" Bit Sub	1.23	1.64
3 × 9 ½" DC	26.74	28.38
XOS	0.98	29.36
TOTAL BHA		**29.36**

Bit Data

Bit #	2
Size	17 ½"
Type	GAT135G (M.T. Bit)
Mfgr	King Dream
Serial No.	2306181JH
Nozzles	3 × 18/32"
IADC Code	135
Depth In	151
Depth Out	165
Metrage	14
Hours Run	7
Av. ROP	2.00
Condition	--

Performance Record :

Total Revolution On Bit : *14.7* krev

This Run (14m) : *7* hrs

Cumulative Bit Life (14m) : *7* hrs

Drilling & Mud Parameters :

WOB (klb)	5-8
RPM (rpm)	30-40
TOR (lbf.ft)	1-1.5
SPP (psi)	600-650
FLOW (gpm)	550-600
MW (pcf)	70
FV (sec)	35
PV / YP	11/18
Gel 0 / 10	8/11
Alk. / HPHT	10.5
FLT °C	P.CH

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 7.087" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 22.10.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #3	Length	Cum Lgth
17 ½" M.T. Bit	0.41	0.41
9 ½" Bit Sub	1.23	1.64
2 × 9 ½" DC	18.04	19.68
17 ½" S.S.T.	2.55	22.23
4 × 9 ½" DC	34.44	56.67
XOS	0.78	57.45
6 × 8 ½" DC	49.60	107.05
XOS	0.95	108.00
6 × 5" HWDP	55.33	163.33
TOTAL BHA		**163.33**

Bit Data

Bit #	2 run#2
Size	17 ½"
Type	GAT135G (M.T. Bit)
Mfgr	King Dream
Serial No.	2306181JH
Nozzles	2 × Open + 1 × 18/32"
IADC Code	135
Depth In	165
Depth Out	793
Metrage	628
Hours Run	45.4
Av. ROP	13.80
Condition	1-1-BU-A-E-1/16"-WO- BHA

Performance Record :

Total Revolution On Bit : *301* krev

This Run (628m) : *45.4* hrs

Cumulative Bit Life (642m) : *52.4* hrs

Drilling & Mud Parameters :

WOB (klb)	25-35
RPM (rpm)	100-110
TOR (lbf.ft)	2-6
SPP (psi)	600-1100
FLOW (gpm)	800-1000
MW (pcf)	70-73
FV (sec)	35-37
PV / YP	11-12/18-11
Gel 0 / 10	8-3/11-5
Alk. / HPHT	10.5-9.4
FLT °C	P.CH

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.693" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 25.10.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #4	Length	Cum Lgth
17 ½" PDC Bit	0.42	0.42
9 ½" Bit Sub	1.23	1.65
2 × 9 ½" DC	18.04	19.69
17 ½" S.S.T.	2.55	22.24
4 × 9 ½" DC	34.44	56.68
XOS	0.78	57.46
6 × 8 ½" DC	49.60	107.06
XOS	0.95	108.01
6 × 5" HWDP	55.33	163.34
TOTAL BHA		163.34

Bit Data

Bit #	3
Size	17 ½"
Type	PDC
Mfgr	Haliburton
Serial No.	16FX65S
Nozzles	9 × 14/32"
IADC Code	S323
Depth In	793
Depth Out	1373.8
Metrage	580.8
Hours Run	62
Av. ROP	9.40
Condition	3-6-BT-(N,T)-X-I-(CT,BU)-PR

Performance Record :

Total Revolution On Bit : 558 krev

This Run (580.8m) : 62 hrs

Cumulative Bit Life (580.8m) : 62 hrs

Drilling & Mud Parameters :

WOB (klb)	10-35
RPM (rpm)	100-180
TOR (lbf.ft)	2-10
SPP (psi)	600-1950
FLOW (gpm)	800-1000
MW (pcf)	73-74
FV (sec)	37-40
PV / YP	10-13
Gel 0 / 10	3-4/5-6
Alk. / HPHT	9.5
FLT °C	P.CH

Reason for POOH :

POOH due to low ROP.

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 30.10.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #5	Length	Cum Lgth
17 ½" PDC Bit	0.46	0.46
9 ½" Bit Sub	1.23	1.69
2 × 9 ½" DC	18.04	19.73
17 ½" S.S.T.	2.55	22.28
4 × 9 ½" DC	34.44	56.72
XOS	0.78	57.50
6 × 8 ½" DC	49.60	107.09
XOS	0.95	108.04
6 × 5" HWDP	55.33	163.37
TOTAL BHA		163.37

Bit Data

Bit #	4
Size	17 ½"
Type	PDC
Mfgr	Haliburton
Serial No.	FSX643Z
Nozzles	2 × 14/32"+7 × 16/32"
IADC Code	S234
Depth In	1373.8
Depth Out	1480.3
Metrage	106.5
Hours Run	10.5
Av. ROP	10.20
Condition	2-1-CT-N-X-I-BU/BT-TW

Performance Record :

Total Revolution On Bit : 85 krev

This Run (106.5m) : 10.5 hrs

Cumulative Bit Life (106.5m) : 10 hrs

Drilling & Mud Parameters :

WOB (klb)	5-15
RPM (rpm)	90-180
TOR (lbf.ft)	2-8
SPP (psi)	2000
FLOW (gpm)	900
MW (pcf)	74-76
FV (sec)	39-41
PV / YP	10-11/10-12
Gel 0 / 10	3-4/5-6
Alk. / HPHT	9.3-9.5
FLT °C	P.CH

Reason for POOH :

POOH due to twist off string.

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 31.10.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #6	Length	Cum Lgth
12 ¾" Overshot	1.17	1.17
1 × 8 ½" DC	8.29	9.46
8" Fishing Jar	4.53	13.99
1 × 8 ½" DC	8.40	22.39
XOS	0.95	23.34
6 × 5" HWDP	55.33	78.67
TOTAL BHA		78.67

Bit Data

Bit #	--
Size	12 ¾"
Type	Overshot
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	1480.3
Depth Out	1480.3
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	41
PV / YP	11/12
Gel 0 / 10	4/6
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 01.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #7	Length	Cum Lgth
11 ¾" Overshot	3.00	3.00
1 × 8 ½" DC	8.29	11.29
8" Fishing Jar	4.53	15.82
1 × 8 ½" DC	8.40	24.22
XOS	0.95	25.17
6 × 5" HWDP	55.33	80.50
TOTAL BHA		80.50

Bit Data

Bit #	--
Size	11 ¾"
Type	Overshot
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	1480.3
Depth Out	1480.3
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	41
PV / YP	11/12
Gel 0 / 10	4/6
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 02.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #8	Length	Cum Lgth
17 ½" PDC Bit	0.46	0.46
9 ½" Bit Sub	1.14	1.60
2 × 9 ½" DC	18.33	19.93
17 ½" S.S.T.	2.48	22.41
4 × 9 ½" DC	36.25	58.66
XOS	0.91	59.57
6 × 8 ½" DC	51.90	111.47
XOS	0.79	112.26
6 × 5" HWDP	55.33	167.59
TOTAL BHA		167.59

Bit Data

Bit #	4run#2
Size	17 ½"
Type	PDC
Mfgr	Haliburton
Serial No.	FSX643Z
Nozzles	2 × 14/32"+7 × 16/32"
IADC Code	S234
Depth In	1480.3
Depth Out	1562
Metrage	81.7
Hours Run	18.5
Av. ROP	4.42
Condition	5-8-LD-A-X-1/8-BU-PR

Performance Record :

Total Revolution On Bit : 183.15 krev

This Run (81.7m) : 18.5 hrs

Cumulative Bit Life (188.2m) : 29 hrs

Drilling & Mud Parameters :

WOB (klb)	5-15
RPM (rpm)	160-170
TOR (lbf.ft)	6000-11000
SPP (psi)	1800-1950
FLOW (gpm)	850-900
MW (pcf)	76
FV (sec)	39-41
PV / YP	9-10/11-13
Gel 0 / 10	3-7/5-9
Alk. / HPHT	8.3-9.5
FLT °C	P.CH

Reason for POOH :

POOH due to low ROP.

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 05.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #9	Length	Cum Lgth
17 ½" R.Bit	0.41	0.41
12⅝" Junk Sub	1.18	1.59
9 ½" Bit Sub	1.14	2.73
2 × 9 ½" DC	18.33	21.06
17 ½" S.S.T.	2.48	23.54
4 × 9 ½" DC	36.25	59.79
XOS	0.98	60.77
6 × 5" HWDP	55.33	116.10
		116.10
TOTAL BHA		116.10

Bit Data

Bit #	2run#3
Size	17 ½"
Type	GAT135G (M.T. Bit)
Mfgr	King Dream
Serial No.	2306181JH
Nozzles	3 × 18/32"
IADC Code	135
Depth In	1562
Depth Out	1564.5
Metrage	2.5
Hours Run	3
Av. ROP	0.83
Condition	1-1-WT-A-E-I-1/16-BU/WO-BHA

Performance Record :

Total Revolution On Bit : 330 krev

This Run (2.5m) : 3.5 hrs

Cumulative Bit Life (644.5m) : 55.4 hrs

Drilling & Mud Parameters :

WOB (klb)	2-19
RPM (rpm)	45-80
TOR (lbf.ft)	1000-8000
SPP (psi)	950-1000
FLOW (gpm)	750
MW (pcf)	76
FV (sec)	39
PV / YP	9/11
Gel 0 / 10	4/6
Alk. / HPHT	9.5
FLT °C	P.CH

Reason for POOH :

POOH Due to Change BHA.

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 08.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #10	Length	Cum Lgth
17 ½" PDC Bit	0.44	0.44
9 ½" Bit Sub	1.14	1.58
2 × 9 ½" DC	18.33	19.91
17 ½" S.S.T.	2.48	22.39
4 × 9 ½" DC	36.25	58.64
XOS	0.91	59.55
6 × 8 ½" DC	51.90	111.45
8"Jar + Flex	11.05	122.50
3 × 8 ½" DC	25.36	147.86
XOS	0.79	148.65
6 × 5" HWDP	55.33	203.98
TOTAL BHA		203.98

Bit Data

Bit #	5
Size	17 ½"
Type	PDC
Mfgr	Reed Hycalog
Serial No.	222691
Nozzles	7 × 16/32"
IADC Code	TFR 716
Depth In	1564.5
Depth Out	1564.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	39
PV / YP	8/9
Gel 0 / 10	2/3
Alk. / HPHT	10.3
FLT °C	--

Reason for POOH :

POOH due to twist off string.

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 10.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #11	Length	Cum Lgth
11 ¾" Overshot	3.00	3.00
1 × 8 ½" DC	8.46	11.46
8" Fishing Jar	4.53	15.99
1 × 8 ½" DC	8.29	24.28
XOS	0.95	25.23
6 × 5" HWDP	55.33	80.56
TOTAL BHA		80.56

Bit Data

Bit #	--
Size	11 ¾"
Type	Overshot
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	1564.5
Depth Out	1564.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	76
FV (sec)	39
PV / YP	8/9
Gel 0 / 10	2/3
Alk. / HPHT	10.3
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 12.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #12	Length	Cum Lgth
17 ½" B. Bit	0.42	0.42
9 ½" Bit Sub	1.16	1.58
2 × 9 ½" DC	17.65	19.23
17 ½" S.S.T.	2.48	21.71
1 × 9 ½" DC	9.20	30.91
XOS	0.91	31.82
6 × 8 ½" DC	51.90	83.72
XOS	0.79	84.51
6 × 5" HWDP	55.33	139.84
TOTAL BHA		**139.84**

Bit Data

Bit #	6
Size	17 ½"
Type	B.Bit
Mfgr	King Dream
Serial No.	2205166JH
Nozzles	3 × 18/32 + center jet
IADC Code	415
Depth In	1564.5
Depth Out	1564.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-3-BT-G-E-I-BU-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	83
FV (sec)	43
PV / YP	14/12
Gel 0 / 10	3/5
Alk. / HPHT	9
FLT °C	P.CH

Reason for POOH :

POOH due to change BHA.

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 15.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #13	Length	Cum Lgth
11 ¾" Overshot	1.18	1.18
1 × 8 ½" DC	9.32	10.50
8" Fishing Jar	4.21	14.71
1 × 8 ½" DC	9.33	24.04
XOS	1.09	25.13
6 × 5" HWDP	55.33	80.46
TOTAL BHA		**80.46**

Bit Data

Bit #	--
Size	11 ¾"
Type	Overshot
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	1564.5
Depth Out	1564.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	83
FV (sec)	43
PV / YP	14/12
Gel 0 / 10	3/5
Alk. / HPHT	9
FLT °C	P.CH

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.693 " Q = 5.21 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 17.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #14	Length	Cum Lgth
Taper Mill	1.38	1.38
9 ½" Bit Sub	1.22	2.60
XOS	0.98	3.58
1 × 5" HWDP	9.06	12.64
XOS	0.80	13.44
9 × 8 ½" DC	82.02	95.45
XOS	1.09	96.54
9 × 5" HWDP	82.71	179.25
TOTAL BHA		**179.25**

Bit Data

Bit #	--
Size	17 ½"
Type	Taper Mill
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	1564.5
Depth Out	1564.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	85
FV (sec)	42
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to Change BHA

PUMP DATA

Pump 1: 7.087" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 21.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #15	Length	Cum Lgth
17 ½" B. Bit	0.42	0.42
9 ½" Bit Sub	1.22	1.64
2 × 9 ½" DC	18.26	19.90
17 ½" S.S.T.	2.48	22.38
1 × 9 ½" DC	9.13	31.51
XOS	1.08	32.59
3 × 8 ½" DC	27.98	60.56
XOS	1.09	61.65
9 × 5" HWDP	82.71	144.36
TOTAL BHA		**144.36**

Bit Data

Bit #	6 run#2
Size	17 ½"
Type	B.Bit
Mfgr	King Dream
Serial No.	2205166JH
Nozzles	3 × 18/32 + 1 × 16/32 center jet
IADC Code	415
Depth In	1564.5
Depth Out	1564.5
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-3-BT-G-E-I-BU-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	85
FV (sec)	42
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to Change BHA

PUMP DATA

Pump 1: 7.087" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 23.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #16	Length	Cum Lgth
17 ½" R. Bit	0.41	0.41
9 ⅝" PDM	8.04	8.45
9 ⅝" Float Sub	0.46	8.91
9 ½" UBHO	1.15	10.06
9 ½" NMDC	9.32	19.38
X.O.S	1.08	20.46
3 × 8 ½" DC	27.98	48.44
8"Jar + Flex	10.04	58.48
3 × 8 ½" DC	28.00	86.48
X.O.S	1.09	87.57
3 × 5" HWDP	27.38	114.95
TOTAL BHA		114.95

Bit Data

Bit #	2run#4
Size	17 ½"
Type	GAT135G (M.T. Bit)
Mfgr	King Dream
Serial No.	2306181JH
Nozzles	3 × Open
IADC Code	135
Depth In	1435
Depth Out	1447
Metrage	12
Hours Run	20
Av. ROP	0.60
Condition	1-1-WT-A-E-1/8"-BU/WO-BHA

Performance Record :

Total Revolution On Bit : 500 krev

This Run (12m) : 20 hrs

Cumulative Bit Life (656.5m) : 75.4 hrs

Drilling & Mud Parameters :

WOB (klb)	2-12
RPM (rpm)	-- (92-96)
TOR (lbf.ft)	--
SPP (psi)	1480-1780
FLOW (gpm)	700-730
MW (pcf)	85
FV (sec)	42
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to Change BHA

PUMP DATA

Pump 1: 7.087" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 26.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #17	Length	Cum Lgth
17 ½" B. Bit	0.42	0.42
9 ⅝" PDM	8.04	8.46
9 ⅝" Float Sub	0.46	8.92
9 ½" UBHO	1.15	10.07
9 ½" NMDC	9.32	19.39
3 × 9 ½" DC	27.39	46.78
X.O.S	1.08	47.86
3 × 8 ½" DC	27.98	75.84
8"Jar + Flex	10.04	85.88
3 × 8 ½" DC	28.00	113.88
X.O.S	1.09	114.97
9× 5" HWDP	82.71	197.68
TOTAL BHA		197.68

Bit Data

Bit #	7
Size	17 ½"
Type	HJT517GL
Mfgr	King Dream
Serial No.	2301490JH
Nozzles	3 × 22
IADC Code	517
Depth In	1447
Depth Out	1552
Metrage	105
Hours Run	55
Av. ROP	1.90
Condition	1-1-WT-A-E-I-No-PR

Performance Record :

Total Revolution On Bit : 321 krev

This Run (105m) : 55 hrs

Cumulative Bit Life (105m) : 55 hrs

Drilling & Mud Parameters :

WOB (klb)	5-27
RPM (rpm)	30 + (92-96)
TOR (lbf.ft)	2000-3000
SPP (psi)	1500-2300
FLOW (gpm)	600-750
MW (pcf)	85
FV (sec)	42
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 7.087" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 30.11.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #18	Length	Cum Lgth
17 ½" PDC Bit	0.42	0.42
9 ⅝" PDM	8.04	8.46
9 ⅝" Float Sub	0.46	8.92
9 ½" UBHO	1.15	10.07
9 ½" NMDC	9.32	19.39
3 × 9 ½" DC	27.39	46.78
X.O.S	1.08	47.86
3 × 8 ½" DC	27.98	75.84
8"Jar + Flex	10.04	85.88
3 × 8 ½" DC	28.00	113.88
X.O.S	1.09	114.97
9× 5" HWDP	82.71	197.68
TOTAL BHA		197.68

Performance Record :

Total Revolution On Bit : *214* krev

This Run (40.9m) : *24.5* hrs

Cumulative Bit Life (40.9m) : *24.5* hrs

Reason for POOH :

POOH due to penetration rate

Bit Data

Bit #	8
Size	17 ½"
Type	PDC
Mfgr	Geo Diamond
Serial No.	20106
Nozzles	5 × 20 + 3 × 18
IADC Code	16MM
Depth In	1552
Depth Out	1592.9
Metrage	40.9
Hours Run	24.5
Av. ROP	1.70
Condition	6-8-RO-N/S/G-X-1/8"-BF-PR

Drilling & Mud Parameters :

WOB (klb)	5-27
RPM (rpm)	30-40 + (96-107)
TOR (lbf.ft)	1000-9000
SPP (psi)	1800-2400
FLOW (gpm)	700-800
MW (pcf)	85
FV (sec)	42
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 03.12.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #19	Length	Cum Lgth
17 ½" B. Bit	0.42	0.42
9 ½" Bit Sub	1.22	1.64
2 × 9 ½" DC	18.26	19.90
17" String Stabilizer	2.73	22.63
1 × 9 ½" DC	9.13	31.76
X.O.S	1.08	32.84
5× 8 ½" DC	46.64	79.48
8"Jar + Flex	10.04	89.52
3 × 8 ½" DC	9.34	98.85
X.O.S	1.09	99.94
9× 5" HWDP	82.71	182.65
TOTAL BHA		182.65

Performance Record :

Total Revolution On Bit : *473* krev

This Run (23.1m) : *18* hrs

Cumulative Bit Life (128m) : *75* hrs

Reason for POOH :

POOH due to decrease pump pressure

Bit Data

Bit #	7run#2
Size	17 ½"
Type	HJT517GL
Mfgr	King Dream
Serial No.	2301490JH
Nozzles	3 × 22
IADC Code	517
Depth In	1592.9
Depth Out	1616
Metrage	23.1
Hours Run	20
Av. ROP	1.15
Condition	1-1-WT-A-E-I-No-PP

Drilling & Mud Parameters :

WOB (klb)	2-15
RPM (rpm)	60-150
TOR (lbf.ft)	2000-5000
SPP (psi)	2100-2300
FLOW (gpm)	700-850
MW (pcf)	85
FV (sec)	42
PV / YP	15/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 05.12.2024

20" Csing Shoe @ 149m ; ID: 19.125" ; Weight: 94lb/ft

Phase Diameter : 17 ½"

BHA #20	Length	Cum Lgth
17 ½" B. Bit	0.42	0.42
9 ½" Bit Sub	1.22	1.64
2 × 9 ½" DC	18.26	19.90
17" String Stabilizer	2.73	22.63
1 × 9 ½" DC	9.13	31.76
X.O.S	1.08	32.84
5× 8 ½" DC	46.64	79.48
8"Jar + Flex	10.04	89.52
3 × 8 ½" DC	9.34	98.85
X.O.S	1.09	99.94
9× 5" HWDP	82.71	182.65
TOTAL BHA		182.65

Bit Data

Bit #	7run#3
Size	17 ½"
Type	HJT517GL
Mfgr	King Dream
Serial No.	2301490JH
Nozzles	3 × 22
IADC Code	517
Depth In	1616
Depth Out	1648.5
Metrage	32.5
Hours Run	55
Av. ROP	0.59
Condition	2-3-WT-A-I-F-BT-TD

Performance Record :

Total Revolution On Bit :	*800*	krev
This Run (32.5m) :	*55*	hrs
Cumulative Bit Life (160.5m) :	*130*	hrs

Drilling & Mud Parameters :

WOB (klb)	2-30
RPM (rpm)	50-150
TOR (lbf.ft)	2000-5000
SPP (psi)	1250-1900
FLOW (gpm)	600-750
MW (pcf)	85
FV (sec)	40
PV / YP	14/9
Gel 0 / 10	3/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to reach casing point

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)
Pump 2: 7.087" Q = 5.84 gal/stk (95%)
Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 13.12.2024

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #21	Length	Cum Lgth
12 ¼" PDC Bit	0.260	0.260
8 ½" Bit Sub	1.105	1.37
2 × 8 ½" DC	18.67	20.04
12 ¼" Stabilizer	1.49	21.52
7 × 8 ½" DC	65.31	86.83
8" Flex JT	3.55	90.38
8"Jar	7.52	97.90
1 × 8 ½" DC	8.27	106.17
X.O.S	1.09	107.26
9 × 5" HWDP	83.41	190.67
TOTAL BHA		190.67

Bit Data

Bit #	9
Size	12 ¼"
Type	PDC
Mfgr	ReedHycalog
Serial No.	--
Nozzles	6 × 15
IADC Code	--
Depth In	1648.5
Depth Out	1831
Metrage	182.5
Hours Run	46.5
Av. ROP	3.90
Condition	8-8-RO-A-X-I-WT-PR

Performance Record :

Total Revolution On Bit :	*404*	krev
This Run (182.5m) :	*46.5*	hrs
Cumulative Bit Life (182.5m) :	*46.5*	hrs

Drilling & Mud Parameters :

WOB (klb)	10-30
RPM (rpm)	160
TOR (lbf.ft)	2000-12000
SPP (psi)	470-570
FLOW (gpm)	380-420
MW (pcf)	73-74
FV (sec)	39
PV / YP	13/10
Gel 0 / 10	2/4
Alk. / HPHT	9.1
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)
Pump 2: 7.087" Q = 5.84 gal/stk (95%)
Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 17.12.2024

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #22	Length	Cum Lgth
12 ¼" B. Bit	0.30	0.30
8 ½" Bit Sub	1.105	1.40
2 × 8 ½" DC	18.67	20.07
12 ¼" Stabilizer	1.49	21.56
7 × 8 ½" DC	65.31	86.87
8" Flex JT	3.55	90.41
8"Jar	7.52	97.93
1 × 8 ½" DC	8.27	106.20
X.O.S	1.09	107.29
9 × 5" HWDP	83.41	190.70
TOTAL BHA		190.70

Bit Data

Bit #	10
Size	12 ¼"
Type	B.Bit
Mfgr	King dream
Serial No.	2304290JH
Nozzles	3 × Open
IADC Code	537
Depth In	1831
Depth Out	2000
Metrage	169
Hours Run	24
Av. ROP	7.0
Condition	1-1-WT-A-E-I-NO-BHA

Performance Record :

Total Revolution On Bit : *182* krev

This Run (169m) : *24* hrs

Cumulative Bit Life (169m) : *24* hrs

Drilling & Mud Parameters :

WOB (klb)	10-20
RPM (rpm)	70-110
TOR (lbf.ft)	2000-7000
SPP (psi)	350-760
FLOW (gpm)	400-600
MW (pcf)	75
FV (sec)	39
PV / YP	12/11
Gel 0 / 10	2/4
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 20.12.2024

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #23	Length	Cum Lgth
12 ¼" B. Bit	0.30	0.30
8 ½" Bit Sub	1.105	1.40
2 × 8 ½" DC	18.67	20.07
12 ¼" Stabilizer	1.49	21.56
7 × 8 ½" DC	65.31	86.87
8" Flex JT	3.55	90.41
8"Jar	7.52	97.93
1 × 8 ½" DC	8.27	106.20
X.O.S	1.09	107.29
9 × 5" HWDP	83.41	190.70
TOTAL BHA		190.70

Bit Data

Bit #	10 run#2
Size	12 ¼"
Type	B.Bit
Mfgr	King dream
Serial No.	2304290JH
Nozzles	3 × Open
IADC Code	537
Depth In	2000
Depth Out	2150
Metrage	150
Hours Run	33.5
Av. ROP	4.47
Condition	1-2-BT-G-E-I-No-WT-PR

Performance Record :

Total Revolution On Bit : *410* krev

This Run (150m) : *33.5* hrs

Cumulative Bit Life (319m) : *57.5* hrs

Drilling & Mud Parameters :

WOB (klb)	5-30
RPM (rpm)	70-160
TOR (lbf.ft)	3000-5000
SPP (psi)	350-1300
FLOW (gpm)	400-600
MW (pcf)	75
FV (sec)	39
PV / YP	12/11
Gel 0 / 10	2/4
Alk. / HPHT	9.2
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 24.12.2024

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #24	Length	Cum Lgth
12 ¼" PDC	0.365	0.365
8 ½" Bit Sub	1.105	1.47
2 × 8 ½" DC	18.67	20.14
12 ¼" Stabilizer	1.49	21.63
7 × 8 ½" DC	65.31	86.94
8" Flex JT	2.84	89.78
8"Jar	7.01	96.79
1 × 8 ½" DC	8.27	105.06
X.O.S	1.09	106.15
9 × 5" HWDP	83.41	189.56
TOTAL BHA		190.70

Bit Data

Bit #	11
Size	12 ¼"
Type	PDC
Mfgr	Best
Serial No.	220799
Nozzles	2 × 14 + 5 × 13 + 2 × 12
IADC Code	M423
Depth In	2150
Depth Out	2696.5
Metrage	545.5
Hours Run	66
Av. ROP	8.30
Condition	4-4-LT-N/C-X-I-WT-PR

Performance Record :

Total Revolution On Bit : 609 krev

This Run (545.5m) : 66 hrs

Cumulative Bit Life (545.5m) : 66 hrs

Drilling & Mud Parameters :

WOB (klb)	10-20
RPM (rpm)	110-180
TOR (lbf.ft)	4000-11000
SPP (psi)	1750 2250
FLOW (gpm)	600 - 750
MW (pcf)	75-77
FV (sec)	39-40
PV / YP	12/11
Gel 0 / 10	3/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 29.12.2024

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #25	Length	Cum Lgth
12 ¼" PDC	0.365	0.365
8 ½" Bit Sub	1.105	1.47
2 × 8 ½" DC	18.67	20.14
12 ¼" Stabilizer	1.49	21.63
7 × 8 ½" DC	65.31	86.94
8" Flex JT	2.84	89.78
8"Jar	7.01	96.79
1 × 8 ½" DC	8.27	105.06
X.O.S	1.09	106.15
9 × 5" HWDP	83.41	189.56
TOTAL BHA		190.70

Bit Data

Bit #	12
Size	12 ¼"
Type	PDC
Mfgr	Best
Serial No.	220798
Nozzles	4 × 14 + 5 × 13
IADC Code	M423
Depth In	2696.5
Depth Out	2810
Metrage	113.5
Hours Run	29
Av. ROP	3.90
Condition	1-1-WT-A-X-I-NO-LIH

Performance Record :

Total Revolution On Bit : 225 krev

This Run (113.5m) : 29 hrs

Cumulative Bit Life (113.5m) : 29 hrs

Drilling & Mud Parameters :

WOB (klb)	10-15
RPM (rpm)	60-180
TOR (lbf.ft)	4000-7000
SPP (psi)	2100-2450
FLOW (gpm)	600-800
MW (pcf)	77+-78
FV (sec)	40
PV / YP	12/11
Gel 0 / 10	3/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to left in hole

PUMP DATA

Pump 1: 7.087 " Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 01.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #26	Length	Cum Lgth
10 ⅛" Over shot	0.950	0.950
1 × 8 ½" DC	8.27	9.22
8"Jar	4.26	13.48
1 × 8 ½" DC	8.36	21.84
X.O.S	1.09	22.93
9 × 5" HWDP	83.41	106.34
TOTAL BHA		**190.70**

Bit Data

Bit #	Over Shot
Size	--
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	2810
Depth Out	2810
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	78
FV (sec)	40
PV / YP	12/11
Gel 0 / 10	3/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 7.087" Q = 5.84 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 02.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #27	Length	Cum Lgth
12 ¼" PDC	0.365	0.365
8 ½" Bit Sub	1.22	1.59
2 × 8 ½" DC	18.67	20.26
12 ¼" Stabilizer	2.04	22.30
7 × 8 ½" DC	64.24	86.54
8" Flex JT	2.84	89.38
8"Jar	7.01	96.39
1 × 8 ½" DC	8.36	104.75
X.O.S	1.10	105.85
9 × 5" HWDP	83.41	189.26
TOTAL BHA		**190.70**

Bit Data

Bit #	12 run#2
Size	12 ¼"
Type	PDC
Mfgr	Best
Serial No.	220798
Nozzles	4 × 14 + 5 × 13
IADC Code	M423
Depth In	2810
Depth Out	2868
Metrage	58
Hours Run	14.65
Av. ROP	3.90
Condition	6-2-NT-L-X-I-BT-PR

Performance Record :

Total Revolution On Bit : 348 krev

This Run (58m) : 14.65 hrs

Cumulative Bit Life (171.5m) : 43.65 hrs

Drilling & Mud Parameters :

WOB (klb)	10-15
RPM (rpm)	60-180
TOR (lbf.ft)	4000-7000
SPP (psi)	2100-2450
FLOW (gpm)	600-800
MW (pcf)	79
FV (sec)	40
PV / YP	13/11
Gel 0 / 10	3/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 6.69" Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 04.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #28	Length	Cum Lgth
12 ¼" PDC	0.360	0.360
8 ½" Bit Sub	1.22	1.58
2 × 8 ½" DC	18.67	20.25
12 ¼" Stabilizer	2.04	22.29
7 × 8 ½" DC	64.24	86.53
8" Flex JT	2.84	89.37
8"Jar	7.01	96.38
1 × 8 ½" DC	8.36	104.74
X.O.S	1.10	105.84
9 × 5" HWDP	83.41	189.25
TOTAL BHA		189.25

Bit Data

Bit #	13
Size	12 ¼"
Type	PDC
Mfgr	Best
Serial No.	220796
Nozzles	4 × 14 + 5 × 13
IADC Code	M423
Depth In	2868
Depth Out	3006.7
Metrage	138.7
Hours Run	32
Av. ROP	4.30
Condition	1-2-LT-N-X-I-PN-LIH

Performance Record :

Total Revolution On Bit :	*307*	krev
This Run (138.7m) :	*32*	hrs
Cumulative Bit Life (138.7m) :	*32*	hrs

Drilling & Mud Parameters :

WOB (klb)	10-17
RPM (rpm)	140-160
TOR (lbf.ft)	4000-8000
SPP (psi)	2300-2550
FLOW (gpm)	780-800
MW (pcf)	79
FV (sec)	40
PV / YP	13/11
Gel 0 / 10	2/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to left in hole

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)
Pump 2: 7.087" Q = 5.84 gal/stk (95%)
Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 07.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #29	Length	Cum Lgth
10⅛" O.Shot	0.950	0.950
1 × 8 ½" DC	8.27	9.22
8" Jar	4.26	13.48
X.O.S	1.09	14.57
9 × 5" HWDP	83.41	97.98
TOTAL BHA		97.98

Bit Data

Bit #	Over Shot
Size	--
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3006.7
Depth Out	3006.7
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	79
FV (sec)	40
PV / YP	13/11
Gel 0 / 10	2/5
Alk. / HPHT	9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)
Pump 2: 7.087" Q = 5.84 gal/stk (95%)
Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 08.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #30	Length	Cum Lgth
12 ¼" PDC	0.360	0.360
8 ½" Bit Sub	1.22	1.58
2 × 8 ½" DC	18.66	20.24
12 ¼" Stabilizer	2.04	22.28
7 × 8 ½" DC	65.30	87.58
8" Flex JT	2.84	90.42
8"Jar	7.01	97.43
1 × 8 ½" DC	9.33	106.76
X.O.S	1.10	107.86
9 × 5" HWDP	83.41	191.27
TOTAL BHA		191.27

Bit Data

Bit #	13 Run#2
Size	12 ¼"
Type	PDC
Mfgr	Best
Serial No.	220796
Nozzles	4 × 14 + 5 × 13
IADC Code	M423
Depth In	3006.7
Depth Out	3027.21
Metrage	20.51
Hours Run	22
Av. ROP	0.90
Condition	3-8-RO-N-X-I-(BT,CT)-PR

Performance Record :

Total Revolution On Bit : 185 krev

This Run (20.5m) : 22 hrs

Cumulative Bit Life (159.2m) : 54 hrs

Drilling & Mud Parameters :

WOB (klb)	8-25
RPM (rpm)	100-180
TOR (lbf.ft)	3-7
SPP (psi)	2000-2600
FLOW (gpm)	700-780
MW (pcf)	79-80
FV (sec)	40
PV / YP	13/11
Gel 0 / 10	2/5
Alk. / HPHT	9.4-9.5
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 11.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #31	Length	Cum Lgth
12 ¼" PDC	0.360	0.360
8 ½" Bit Sub	1.22	1.58
2 × 8 ½" DC	18.66	20.24
12 ¼" Stabilizer	2.04	22.28
7 × 8 ½" DC	65.30	87.58
8" Flex JT	2.84	90.42
8"Jar	7.01	97.43
1 × 8 ½" DC	9.33	106.76
X.O.S	1.10	107.86
9 × 5" HWDP	83.41	191.27
TOTAL BHA		191.27

Bit Data

Bit #	14
Size	12 ¼"
Type	PDC
Mfgr	Best
Serial No.	--
Nozzles	4 × 14 + 5 × 13
IADC Code	M423
Depth In	3027.2
Depth Out	3240
Metrage	212.8
Hours Run	49.5
Av. ROP	4.30
Condition	5-3-LT-N/S-X-1/16"-BT-WO

Performance Record :

Total Revolution On Bit : 475 krev

This Run (212.8m) : 49.5 hrs

Cumulative Bit Life (212.8m) : 49.5 hrs

Drilling & Mud Parameters :

WOB (klb)	10-20
RPM (rpm)	160
TOR (lbf.ft)	4-9
SPP (psi)	2600-2750
FLOW (gpm)	750-780
MW (pcf)	80-81
FV (sec)	43-44
PV / YP	11/14
Gel 0 / 10	2/5
Alk. / HPHT	9.4-9.5
FLT °C	--

Reason for POOH :

POOH due to wash out drill string

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 15.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #32	Length	Cum Lgth
10⅛" O.Shot	2.150	2.150
1 × 8 ½" DC	8.44	10.59
X.O.S	1.08	11.67
3 × 5" HWDP	27.76	39.43
		39.43
TOTAL BHA		**39.43**

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Reason for POOH :

POOH due to change BHA

Bit Data

Bit #	Over Shot
Size	10⅛"
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3240.6
Depth Out	3240.6
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	81
FV (sec)	44
PV / YP	15/12
Gel 0 / 10	2/4
Alk. / HPHT	9.4
FLT °C	--

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 16.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #33	Length	Cum Lgth
12 ¼" PDC	0.380	0.380
8 ½" Bit Sub	1.22	1.60
2 × 8 ½" DC	18.66	20.26
12 ¼" Stabilizer	2.04	22.30
7 × 8 ½" DC	65.30	87.60
8"Jar	9.57	97.17
1 × 8 ½" DC	9.33	106.50
X.O.S	1.10	107.60
9 × 5" HWDP	84.10	191.70
		191.70
TOTAL BHA		**191.70**

Performance Record :

Total Revolution On Bit : *121.8* krev

This Run (35m) : *14* hrs

Cumulative Bit Life (35m) : *14* hrs

Reason for POOH :

POOH due to penetration rate

Bit Data

Bit #	15
Size	12 ¼"
Type	PDC
Mfgr	SMITH
Serial No.	M88VPXX
Nozzles	8 × 16
IADC Code	M424
Depth In	3240
Depth Out	3275
Metrage	35
Hours Run	14
Av. ROP	2.50
Condition	6-7-B Blade-N-X-1/8"-BT/LT-PR

Drilling & Mud Parameters :

WOB (klb)	10-25
RPM (rpm)	120-170
TOR (lbf.ft)	3-5
SPP (psi)	2600-2700
FLOW (gpm)	750-780
MW (pcf)	81-82
FV (sec)	44-46
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.4-9.5
FLT °C	--

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 18.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #34	Length	Cum Lgth
12 ¼" B. Bit	0.290	0.290
9 ½" Junk Sub	1.10	1.39
8 ½" Bit Sub	1.22	2.61
2 × 8 ½" DC	18.66	21.27
12 ¼" Stabilizer	2.04	23.31
7 × 8 ½" DC	65.30	88.61
8"Jar	9.57	98.18
1 × 8 ½" DC	9.33	107.51
X.O.S	1.10	108.61
9 × 5" HWDP	84.10	192.71
TOTAL BHA		192.71

Bit Data

Bit #	10 run#3
Size	12 ¼"
Type	B.Bit
Mfgr	King dream
Serial No.	2304290JH
Nozzles	3 × 20
IADC Code	537
Depth In	3275
Depth Out	3284.4
Metrage	9.4
Hours Run	11
Av. ROP	0.90
Condition	2-4-BT-G-E-I-WT-PR

Performance Record :

Total Revolution On Bit : 442 krev

This Run (9.4m) : 11 hrs

Cumulative Bit Life (328.4m) : 68.5 hrs

Drilling & Mud Parameters :

WOB (klb)	10-20
RPM (rpm)	40-90
TOR (lbf.ft)	3-5
SPP (psi)	90-2850
FLOW (gpm)	400-750
MW (pcf)	82
FV (sec)	46-49
PV / YP	19/14
Gel 0 / 10	4/6
Alk. / HPHT	9.4-9.5
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 20.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #35	Length	Cum Lgth
10 1/8" RCJB	1.395	1.395
6 × 8 ½" DC	55.96	57.36
XOS	1.10	58.46
9 × 5" HWDP	84.10	142.56
TOTAL BHA		142.56

Bit Data

Bit #	--
Size	--
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3284.4
Depth Out	3284.9
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	3-5
RPM (rpm)	10-25
TOR (lbf.ft)	3-6
SPP (psi)	800-1000
FLOW (gpm)	400-450
MW (pcf)	82
FV (sec)	46-47
PV / YP	19/14
Gel 0 / 10	4/6
Alk. / HPHT	9.4-9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 22.01.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #36	Length	Cum Lgth
12 ¼" PDC	0.380	0.380
8 ½" Bit Sub	1.22	1.60
2 × 8 ½" DC	18.66	20.26
12 ¼" Stabilizer	2.04	22.30
7 × 8 ½" DC	65.30	87.60
8"Jar	9.57	97.17
1 × 8 ½" DC	9.33	106.50
X.O.S	1.10	107.60
9 × 5" HWDP	84.10	191.70
		191.70
TOTAL BHA		191.70

Bit Data

Bit #	16
Size	12 ¼"
Type	PDC
Mfgr	Beste
Serial No.	M1664
Nozzles	9 × 13
IADC Code	M424
Depth In	3285
Depth Out	3872
Metrage	587
Hours Run	166.5
Av. ROP	3.53
Condition	2-2-WT-A-X-I-LT-PR

Performance Record :

Total Revolution On Bit :	*1599*	krev
This Run (587m) :	*166.5*	hrs
Cumulative Bit Life (587m) :	*166.5*	hrs

Drilling & Mud Parameters :

WOB (klb)	8-25
RPM (rpm)	150-170
TOR (lbf.ft)	5-10
SPP (psi)	2600-2800
FLOW (gpm)	670-725
MW (pcf)	82-84
FV (sec)	44-46
PV / YP	16/13
Gel 0 / 10	3/5
Alk. / HPHT	9.4-9.5
FLT °C	--

Reason for POOH :

POOH due to penetration rate

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 01.02.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #37	Length	Cum Lgth
12 ¼" PDC	0.370	0.370
8 ½" Bit Sub	1.22	1.59
2 × 8 ½" DC	18.66	20.25
12 ¼" Stabilizer	2.04	22.29
7 × 8 ½" DC	65.30	87.59
8"Jar	9.57	97.16
1 × 8 ½" DC	9.33	106.49
X.O.S	1.10	107.59
9 × 5" HWDP	84.09	191.68
TOTAL BHA		191.68

Bit Data

Bit #	17
Size	12 ¼"
Type	PDC
Mfgr	Burintekh
Serial No.	4263
Nozzles	6 × 15
IADC Code	M323
Depth In	3872
Depth Out	3891
Metrage	19
Hours Run	7
Av. ROP	2.71
Condition	--

Performance Record :

Total Revolution On Bit :	*69.3*	krev
This Run (19m) :	*7*	hrs
Cumulative Bit Life (19m) :	*7*	hrs

Drilling & Mud Parameters :

WOB (klb)	5-25
RPM (rpm)	160-170
TOR (lbf.ft)	5-10
SPP (psi)	2450-2810
FLOW (gpm)	670-725
MW (pcf)	82.5-84
FV (sec)	45
PV / YP	16/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4-9.5
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 04.02.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #38	Length	Cum Lgth
12 ¼" PDC	0.370	0.370
8 ½" Bit Sub	1.22	1.59
2 × 8 ½" DC	18.66	20.25
7 × 8 ½" DC	65.30	85.55
8"Jar	9.57	95.12
1 × 8 ½" DC	9.33	104.45
X.O.S	1.10	105.55
9 × 5" HWDP	84.09	189.64
TOTAL BHA		189.64

Bit Data

Bit #	17 Run2
Size	12 ¼"
Type	PDC
Mfgr	Burintekh
Serial No.	4263
Nozzles	6 × 15
IADC Code	M323
Depth In	3891
Depth Out	3895
Metrage	4
Hours Run	2
Av. ROP	2.00
Condition	1-1-WT-A-X-I-NO-HP

Performance Record :

Total Revolution On Bit :	*87.3*	krev
This Run (4m) :	*2*	hrs
Cumulative Bit Life (23m) :	*9*	hrs

Drilling & Mud Parameters :

WOB (klb)	15-25
RPM (rpm)	140-160
TOR (lbf.ft)	6-9
SPP (psi)	1350-1750
FLOW (gpm)	450-550
MW (pcf)	80-81
FV (sec)	44-45
PV / YP	15/11-16/12
Gel 0 / 10	2/4-3/5
Alk. / HPHT	9.3-9.4
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 06.02.2025

13 ⅜" Csing Shoe @ 1648m ; ID: 12.415"; Weight: 68lb/ft

Phase Diameter : 12 ¼"

BHA #39	Length	Cum Lgth
6 ½" C.C.Bit	0.120	0.120
6 ½" Bit Sub	1.22	1.34
399 × 5" DP	3809.11	3810.45
TOTAL BHA		3810.45

Bit Data

Bit #	18
Size	6 ½"
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	3895
Depth Out	3895
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit :	--	krev
This Run (m) :	--	hrs
Cumulative Bit Life (m) :	--	hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	80
FV (sec)	43-44
PV / YP	14/10-15/11
Gel 0 / 10	2/4-3/5
Alk. / HPHT	9-9.3
FLT °C	--

Reason for POOH :

POOH due to run casing 9 ⅝"

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 12.02.2025

9 ⅝" Csing Shoe @ 3895m ; ID: 8.535"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #40	Length	Cum Lgth
8 ⅜" PDC	0.270	0.270
8 ½" Bit Sub	1.22	1.49
2 × 6 ½" DC	18.52	20.01
8 ⅜" Stabilizer	1.41	21.42
10 × 6 ½" DC	90.74	110.75
6 ½"Jar	7.11	117.86
3 × 6 ½" DC	26.83	144.69
9 × 5" HWDP	84.09	228.78
TOTAL BHA		**230.19**

Bit Data

Bit #	18
Size	8 ⅜"
Type	PDC
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M433
Depth In	3895
Depth Out	4180
Metrage	285
Hours Run	57
Av. ROP	5.00
Condition	1-1-WT-A-X-I-BT-TD

Performance Record :

Total Revolution On Bit : 393.3 krev

This Run (285m) : 57 hrs

Cumulative Bit Life (285m) : 57 hrs

Drilling & Mud Parameters :

WOB (klb)	10-20
RPM (rpm)	80-150
TOR (lbf.ft)	9-11
SPP (psi)	1450-2600
FLOW (gpm)	350-500
MW (pcf)	100-103
FV (sec)	43-55
PV / YP	18/10-26/12
Gel 0 / 10	3/5-4/6
Alk. / HPHT	9.1-9.4
FLT °C	--

Reason for POOH :

POOH due to reach to total depth.

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 20.02.2025

9 ⅝" Csing Shoe @ 3895m ; ID: 8.535"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #41	Length	Cum Lgth
8 ⅜" PDC	0.270	0.270
8 ½" Bit Sub	1.22	1.49
2 × 6 ½" DC	18.52	20.01
8 ⅜" Stabilizer	1.41	21.42
10 × 6 ½" DC	90.74	110.75
3 × 6 ½" DC	26.83	137.58
9 × 5" HWDP	84.09	221.67
TOTAL BHA		**223.08**

Bit Data

Bit #	18 Run2
Size	8 ⅜"
Type	PDC
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M433
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-1-WT-A-X-I-BT-TD

Performance Record :

Total Revolution On Bit : 393.3 krev

This Run (m) : -- hrs

Cumulative Bit Life (285m) : 57 hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103
FV (sec)	50
PV / YP	24/14
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to run 7" liner

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 23.02.2025

7" Liner Shoe @ 4179.5m ; ID: 6.004"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #42	Length	Cum Lgth
8 ⅜" PDC	0.270	0.270
8 ½" Bit Sub	1.22	1.49
6 × 6 ½" DC	18.52	82.00
9 × 5" HWDP	84.09	166.09
TOTAL BHA		**104.10**

Bit Data

Bit #	18 Run3
Size	8 ⅜"
Type	PDC
Mfgr	Best
Serial No.	220852
Nozzles	7 × 14
IADC Code	M433
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	1-3-BT-G-X-I-WT-BHA

Performance Record :

Total Revolution On Bit : 57 krev

This Run (m) : -- hrs

Cumulative Bit Life (285m) : 57 hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103
FV (sec)	50
PV / YP	24/14
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 25.02.2025

7" Liner Shoe @ 4179.5m ; ID: 6.004"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #43	Length	Cum Lgth
5 ⅞" Rock Bit	0.170	0.170
4 ¾" Bit Sub	1.00	1.17
15 × 4 ¾" DC	135.25	136.42
9 × 3 ½" HWDP	82.30	218.72
30 × 3 ½" DP	290.23	508.95
X.O.S	0.96	509.91
TOTAL BHA		**509.91**

Bit Data

Bit #	19
Size	5 ⅞"
Type	Rock Bit
Mfgr	Kingdream
Serial No.	2204638JH
Nozzles	3 × Open
IADC Code	--
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-BT-A-E-I-LT-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103
FV (sec)	50
PV / YP	24/14
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 27.02.2025

7" Liner Shoe @ 4179.5m ; ID: 6.004"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #44	Length	Cum Lgth
5 ⅞" Rock Bit	0.170	0.170
7" Scraper	1.01	1.18
4 ¾" Bit Sub	1.00	2.18
6 × 4 ¾" DC	54.17	56.35
9 × 3 ½" HWDP	82.30	138.65
27 × 3 ½" DP	261.47	400.12
X.O.S	0.96	401.08
D.Pin	0.31	401.39
9 5/8" Scraper	1.38	402.77
Bit Sub	1.22	403.99
9 × 5" HWDP	84.09	488.08
TOTAL BHA		488.08

Bit Data

Bit #	19 Run2
Size	5 ⅞"
Type	Rock Bit
Mfgr	Kingdream
Serial No.	2204638JH
Nozzles	3 × Open
IADC Code	--
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-BT-A-F-I-LT-BHA

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103
FV (sec)	50
PV / YP	24/14
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to change BHA

PUMP DATA

Pump 1: 6.69" Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 28.02.2025

7" Liner Shoe @ 4179.5m ; ID: 6.004"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #45	Length	Cum Lgth
Bottom B.T	1.260	1.260
Anchor pipe	1.53	2.79
X.O.S	0.80	3.59
Middle Packer element	1.33	4.92
Above Packer 9 5/8	0.76	5.68
X.O.S	1.00	6.68
X.O.S	0.40	7.08
RH Release safety joint	0.73	7.81
Hydraulic JAR	1.00	8.81
Middle B.T	1.25	10.06
Hydrospring	1.56	11.62
D.C.I.P	1.64	13.26
X.O.S	0.25	13.51
5" DP	9.52	23.03
REVERS SUB	0.40	23.43
12 × 6 1/2" DC	109.26	132.69
TOTAL BHA		132.69

Bit Data

Bit #	--
Size	--
Type	--
Mfgr	--
Serial No.	--
Nozzles	--
IADC Code	--
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103
FV (sec)	47
PV / YP	19/10-12
Gel 0 / 10	3/5
Alk. / HPHT	9.2-9.6
FLT °C	--

Reason for POOH :

POOH due to run log

PUMP DATA

Pump 1: 6.69" Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 04.03.2025

7" Liner Shoe @ 4179.5m ; ID: 6.004"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #46	Length	Cum Lgth
5 ⅞" Rock Bit	0.170	0.170
4 ¾" Bit Sub	1.00	1.17
15× 4 ¾" DC	135.25	136.42
9 × 3 ½" HWDP	82.30	218.72
30 × 3 ½" DP	290.23	508.95
X.O.S	0.96	509.91
TOTAL BHA		509.91

Bit Data

Bit #	19 Run3
Size	5 ⅞"
Type	HAT217G
Mfgr	Kingdream
Serial No.	2204638JH
Nozzles	3 × Open
IADC Code	217
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	2-2-BT-A-F-I-LT-LOG.

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103
FV (sec)	50
PV / YP	20/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to run log

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

Date : 10.03.2025

7" Liner Shoe @ 4179.5m ; ID: 6.004"; Weight: 53.5lb/ft

Phase Diameter : 8 ⅜"

BHA #47	Length	Cum Lgth
5 ⅞"Junk Mill	0.618	0.618
4 ¾" Bit Sub	1.00	1.62
15× 4 ¾" DC	135.25	136.87
9 × 3 ½" HWDP	82.30	219.17
30 × 3 ½" DP	290.23	509.40
X.O.S	0.96	510.36
TOTAL BHA		510.36

Bit Data

Bit #	Junk Mill
Size	5 ⅞"
Type	--
Mfgr	CylanderSazi
Serial No.	--
Nozzles	5 × 12
IADC Code	--
Depth In	4180
Depth Out	4180
Metrage	--
Hours Run	--
Av. ROP	--
Condition	--

Performance Record :

Total Revolution On Bit : -- krev

This Run (m) : -- hrs

Cumulative Bit Life (m) : -- hrs

Drilling & Mud Parameters :

WOB (klb)	--
RPM (rpm)	--
TOR (lbf.ft)	--
SPP (psi)	--
FLOW (gpm)	--
MW (pcf)	103-104
FV (sec)	50
PV / YP	21/12
Gel 0 / 10	3/5
Alk. / HPHT	9.4
FLT °C	--

Reason for POOH :

POOH due to completion String.

PUMP DATA

Pump 1: 6.69 " Q = 5.20 gal/stk (95%)

Pump 2: 7.087" Q = 5.84 gal/stk (95%)

Pump 3: 7.087" Q = 5.84 gal/stk (95%)

6. Casing Information

6.1 20” Casing

20” Casing Report

Casing Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012		N
RIG	208	WSS	Gh.Kadivar / A.Eyvazi		192,581		E
DATE	1403.07.28	HOLE DEPTH	151 m MD		MUD WT.	70	PCF
HOLE SIZE	26" inches		151 m TVD		MUD TYPE	Bent. Mud	

PREVIOUS CASING	DEPTH metres	O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS
	NA	NA	NA	NA	NA	

LNR STRING COMPOSITION

Qty.	O.D. in	I.D.	ITEM DESCRIPTION / MANUFACTURER	Wt. lb/ft	GRADE	CONNECTION	Make Up Torque	LENGTH m	DEPTH m MD
1	20"	19.125	26" F.SHOE	94	K-55	BTC	Base on Triangle	0.900	149.00
2	20"	19.125	CSG	94	K-55	BTC	Base on Triangle	148.100	148.10

FINAL SHOE DEPTH	149.00 m		CSG WEIGHT IN AIR	46.5	klbs
TOTAL LENGTH OF LNR RUN	149.00 m		CSG WEIGHT IN MUD	40.0	klbs

PERFORMANCE	DATE/TIME
STARTED RUNNING LNR	19-Oct-2024, 05:30
FINISHED RUNNING LNR	19-Oct-2024, 11:00
TOTAL TIME (hours)	5.5
DOWNTIME (hours)	-

REASON(S) FOR DOWNTIME:

CASING RUNNING COMPANY:	OEOC

CENTRALISER / SCRATCHER PLACEMENT

MANUFACTURER	KTK
TYPE	20" X 26" Centralizer
PLACEMENT	Install as per CSG Tally.

COMMENTS:

R/U 20" CSG Running Equipment (OEOC Co), HPJSM.P/U 20" Float shoe (Welded on JT)+ 1Jt 20" CSG (94#, K55, BTC) and Cont. Run 20" CSG to 149m (Totally 13 Jts), F/U each Jt while running & Install 20 × 26" centralizer as per program.
M/U 20" Swage and Circ thru CSG; OK.M/U 5" Stinger (Dress w/ 5 No. O-Ring) on Pup Jt & Install 5" X 20" Bow Centralizer, RIH w/ 5" DPs thru CSG to 20" CSG Shoe depth and sting in stinger to float shoe. Establish Circ. thru DPs and check stinger sealing; OK.

20” Casing Tally

MSA

Field :	Azadegan	Well NO:	AZNS-207	Rig NO:	208 OEOC	Drlg CO:	OEOC

20" Casing

Grade	ID "	Drift "	Weight lb/ft	Burst psi	Collaspse psi	Tensile Strenght Klbs	Coupling OD in	TQ ft x lb	Nominal Dia. OD
TP110SS	19.125	19	94.0	2,110	520	1,480		Base on Triangl	20

Total Dept	151.0 m	Formation Name :	Aghajari	Hook Weight :	58 k lb
Shoe Dept	149.0	Formation Top :		STRG CAP (bbl):	175
Float Colla				Mud Weight (pcf) :	70

Number on jt	Grade	Order No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	STRG CAP. (bbl)	Remarks	
								Centralizers	IN / OUT
					149.00	58.00	0.00		
Float Shoe	20" Stab in Float Shoe		0.90	0.90	148.10	58.24	1.05		
1	20" CSG, 94#,K55, BTC	1	11.59	12.49	136.51	61.33	14.56	Bow	
2	20" CSG, 94#,K55, BTC	2	11.39	23.88	125.12	64.38	27.84		
3	20" CSG, 94#,K55, BTC	3	11.51	35.39	113.61	67.45	41.25		
4	20" CSG, 94#,K55, BTC	4	11.40	46.78	102.22	70.49	54.54	Bow	
5	20" CSG, 94#,K55, BTC	5	11.71	58.49	90.51	73.62	68.19		
6	20" CSG, 94#,K55, BTC	6	12.20	70.69	78.31	76.88	82.41		
7	20" CSG, 94#,K55, BTC	7	11.43	82.12	66.88	79.93	95.73	Bow	
8	20" CSG, 94#,K55, BTC	8	11.31	93.43	55.57	82.95	108.92		
9	20" CSG, 94#,K55, BTC	-	11.22	93.43	OUT	82.95	108.92		Out
10	20" CSG, 94#,K55, BTC	9	11.41	104.84	44.16	86.00	122.22		
11	20" CSG, 94#,K55, BTC	-	10.52	104.84	OUT	86.00	122.22		Out
12	20" CSG, 94#,K55, BTC	10	11.20	116.04	32.96	89.00	135.28	Bow	
13	20" CSG, 94#,K55, BTC	11	11.11	127.15	21.85	91.96	148.23		
14	20" CSG, 94#,K55, BTC	12	11.64	138.79	10.21	95.07	161.80	Bow	
15	20" CSG, 94#,K55, BTC	13	11.49	150.28	-1.28	98.14	175.20		
16	20" CSG, 94#,K55, BTC	-	11.48	150.28	OUT	98.14	175.20	Pin Damage	Out

6.2 13 – 3/8" Casing

13-3/8" Casing Report

Casing Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012		N
RIG	208	WSS	A.Moradi / P.Bakhshi		192,581		E
DATE	1403.07.28	HOLE DEPTH	1,648 m MD		MUD WT.	85	PCF
HOLE SIZE	17-1/2" inches		1,648 m TVD		MUD TYPE	KCl Poly Mud	

	DEPTH metres	O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS
PREVIOUS CASING	149.0	20"	94	K-55	BTC	

CSG STRING COMPOSITION

Qty.	O.D. in	I.D.	ITEM DESCRIPTION / MANUFACTURER	Wt. lb/ft	GRADE	CONNECTION	Make Up Torque	LENGTH m
1	13-3/8"	12.415	13 3/8" Float Shoe,68# N-80, BTC	68	N-80	BTC	Base on Triangle	0.580
2	13-3/8"	12.415	13 3/8" CSG 68#, N-80, BTC	68	N-80	BTC	Base on Triangle	22.774
1	13-3/8"	12.415	13 3/8" Float Collar,68# N-80, BTC	68	N-80	BTC	Base on Triangle	0.480
143	13-3/8"	12.415	13 3/8" CSG 68#, N-80, BTC	68	N-80	BTC	Base on Triangle	1626.691

FINAL SHOE DEPTH	1648.00 m		CSG WEIGHT IN AIR	367.7	klbs
TOTAL LENGTH OF CSG. RUN	1648.00 m		CSG WEIGHT IN MUD	303.8	klbs

PERFORMANCE	DATE/TIME
STARTED RUNNING LNR	8-Dec-2024, 16:30
FINISHED RUNNING LNR	9-Dec-2024, 23:00
TOTAL TIME (hours)	30.5
DOWNTIME (hours)	-

REASON(S) FOR DOWNTIME:

CASING RUNNING COMPANY: OEOC

CENTRALISER / SCRATCHER PLACEMENT

MANUFACTURER	IDC
TYPE	17-1/2" X 13-3/8" Bow Centralizer & 20" X 13-3/8" Rigid Centralizer
PLACEMENT	Install as per CSG Tally.

COMMENTS:

Held P.J.S.M, P/U & M/U shoe track as: 13 3/8" F.Shoe + 2 Jts 13-3/8" CSG (68#, N-80, BTC) + 13 3/8" F.Collar. M/U swage, Check F.Shoe & F.Collar function; OK. M/U circ. Swage, Change TDS Links to 500-T, M/U fill up tools and spider elevator (slips type). Cont. RIH 13-3/8" CSG (68#, N-80, BTC) f/ 400m to 1648.5m, Tag BTM, Pull out STRG to 1648m(0.5mT Off BTM) with 1-2BPH Loss.
>> Fill up & break circ. every 5 Jts.
>> Used centralizer as per program.

13-3/8" Casing Tally

13 3/8" Casing Tally

Field :	Azadegan	Well NO:		AZNS207	Rig :	208 OEOC		Drlg CO:	MSA
Grade	ID (inch)	Drift (inch)	Weight (lb/ft)	Burst (psi)	Collaspse (psi)	Yield (klbs)	Coupling (cm)	TQ (lb.ft)	Nominal Dia. OD (inch)
N-80	12.415	12.259	68.0		2260	5020	27		13 3/8

Total Depth :	1648.50	Formation Name :	Pabdeh/Ja	Hook Weight :	55
Shoe Depth :	1648.00	Formation Top :		VOLUME (TOTAL)	810.77
Float Collar :	1624.17			Mud Weight (pcf) :	85

Number on jt	Grade	Run In No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	VOL(BBL)	Centralizers	IN / OUT
					1648.00	55.00			
Float Shoe	13 3/8" Float Shoe,68# N-80, BTC		0.580	0.58	1647.42	55.11	0.285		
1	13 3/8" CSG 68#, N-80, BTC	1	11.457	12.04	1635.96	57.22	5.913	BOW	
2	13 3/8" CSG 68#, N-80, BTC	2	11.317	23.35	1624.65	59.31	11.472	BOW	
Float Collar	13 3/8" Float Collar,68# N-80, BTC		0.480	23.83	1624.17	59.40	11.708		
3	13 3/8" CSG, 68#, N-80, BTC	3	11.197	35.03	1612.97	61.46	17.208		
4	13 3/8" CSG, 68#, N-80, BTC	4	11.383	46.41	1601.59	63.56	22.800		
5	13 3/8" CSG, 68#, N-80, BTC	5	11.462	57.88	1590.12	65.67	28.430		
6	13 3/8" CSG, 68#, N-80, BTC	6	11.472	69.35	1578.65	67.79	34.065		
7	13 3/8" CSG, 68#, N-80, BTC	7	11.289	80.64	1567.36	69.87	39.611	BOW	
8	13 3/8" CSG, 68#, N-80, BTC	8	11.348	91.99	1556.02	71.97	45.185		
9	13 3/8" CSG, 68#, N-80, BTC	9	11.452	103.44	1544.56	74.08	50.810		
10	13 3/8" CSG, 68#, N-80, BTC	10	11.242	114.68	1533.32	76.15	56.333		
11	13 3/8" CSG, 68#, N-80, BTC	11	11.317	126.00	1522.00	78.24	61.892		
12	13 3/8" CSG, 68#, N-80, BTC	12	11.467	137.46	1510.54	80.35	67.525		
13	13 3/8" CSG, 68#, N-80, BTC	13	11.322	148.79	1499.22	82.44	73.086	BOW	
14	13 3/8" CSG, 68#, N-80, BTC	14	11.317	160.10	1487.90	84.53	78.646		
15	13 3/8" CSG, 68#, N-80, BTC	15	11.457	171.56	1476.44	86.64	84.273		
16	13 3/8" CSG, 68#, N-80, BTC	16	11.417	182.98	1465.02	88.75	89.882		
17	13 3/8" CSG, 68#, N-80, BTC	17	11.100	194.08	1453.92	90.80	95.334		
18	13 3/8" CSG, 68#, N-80, BTC	18	11.465	205.54	1442.46	92.91	100.966		
19	13 3/8" CSG, 68#, N-80, BTC	19	11.482	217.02	1430.98	95.03	106.606	BOW	
20	13 3/8" CSG, 68#, N-80, BTC	20	11.482	228.51	1419.50	97.15	112.247		
21	13 3/8" CSG, 68#, N-80, BTC	21	11.447	239.95	1408.05	99.26	117.870		
22	13 3/8" CSG, 68#, N-80, BTC	22	11.451	251.40	1396.60	101.37	123.495		
23	13 3/8" CSG, 68#, N-80, BTC	23	11.712	263.12	1384.89	103.53	129.248		
24	13 3/8" CSG, 68#, N-80, BTC	24	11.706	274.82	1373.18	105.69	134.998		
25	13 3/8" CSG, 68#, N-80, BTC	25	11.454	286.28	1361.73	107.80	140.624	BOW	
26	13 3/8" CSG, 68#, N-80, BTC	26	11.317	297.59	1350.41	109.89	146.184		
27	13 3/8" CSG, 68#, N-80, BTC	27	11.390	308.98	1339.02	111.99	151.779		
28	13 3/8" CSG, 68#, N-80, BTC	28	11.440	320.42	1327.58	114.10	157.398		
29	13 3/8" CSG, 68#, N-80, BTC	29	11.312	331.73	1316.27	116.19	162.955		
30	13 3/8" CSG, 68#, N-80, BTC	30	11.342	343.08	1304.92	118.28	168.526		
31	13 3/8" CSG, 68#, N-80, BTC	31	11.429	354.51	1293.50	120.39	174.140	BOW	
32	13 3/8" CSG, 68#, N-80, BTC	32	11.453	365.96	1282.04	122.50	179.766		
33	13 3/8" CSG, 68#, N-80, BTC	33	11.465	377.42	1270.58	124.61	185.398		
34	13 3/8" CSG, 68#, N-80, BTC	34	11.457	388.88	1259.12	126.73	191.026		
35	13 3/8" CSG, 68#, N-80, BTC	35	11.458	400.34	1247.66	128.84	196.655		
36	13 3/8" CSG, 68#, N-80, BTC	36	11.467	411.81	1236.20	130.96	202.287		
37	13 3/8" CSG, 68#, N-80, BTC	37	10.992	422.80	1225.20	132.98	207.687	BOW	
38	13 3/8" CSG, 68#, N-80, BTC	38	11.162	433.96	1214.04	135.04	213.170		
39	13 3/8" CSG, 68#, N-80, BTC	39	10.900	444.86	1203.14	137.05	218.524		
40	13 3/8" CSG, 68#, N-80, BTC	40	11.486	456.35	1191.66	139.17	224.166		
41	13 3/8" CSG, 68#, N-80, BTC	41	11.327	467.67	1180.33	141.26	229.731		
42	13 3/8" CSG, 68#, N-80, BTC	42	11.467	479.14	1168.86	143.37	235.363		
43	13 3/8" CSG, 68#, N-80, BTC	43	11.385	490.52	1157.48	145.47	240.956	BOW	
44	13 3/8" CSG, 68#, N-80, BTC	44	11.272	501.80	1146.20	147.55	246.493		
45	13 3/8" CSG, 68#, N-80, BTC	45	11.472	513.27	1134.73	149.67	252.128		
46	13 3/8" CSG, 68#, N-80, BTC	46	11.217	524.49	1123.52	151.74	257.638		
47	13 3/8" CSG, 68#, N-80, BTC	47	11.450	535.94	1112.07	153.85	263.263		
48	13 3/8" CSG, 68#, N-80, BTC	48	11.431	547.37	1100.63	155.96	268.878		
49	13 3/8" CSG, 68#, N-80, BTC	49	11.381	558.75	1089.25	158.06	274.469	BOW	

50	13 3/8" CSG, 68#, N-80, BTC	**50**	11.333	570.08	**1077.92**	**160.15**	280.036		
51	13 3/8" CSG, 68#, N-80, BTC	**51**	11.327	581.41	**1066.59**	**162.24**	285.600		
52	13 3/8" CSG, 68#, N-80, BTC	**51**	11.059	581.41	**OUT**	**162.24**	285.600		**OUT**
53	13 3/8" CSG, 68#, N-80, BTC	**51**	11.055	581.41	**OUT**	**162.24**	285.600		**OUT**
54	13 3/8" CSG, 68#, N-80, BTC	**52**	11.438	592.85	**1055.16**	**164.35**	291.218		
55	13 3/8" CSG, 68#, N-80, BTC	**53**	11.427	604.27	**1043.73**	**166.45**	296.831		
56	13 3/8" CSG, 68#, N-80, BTC	**54**	10.997	615.27	**1032.73**	**168.48**	302.233		
57	13 3/8" CSG, 68#, N-80, BTC	**55**	10.872	626.14	**1021.86**	**170.49**	307.574	BOW	
58	13 3/8" CSG, 68#, N-80, BTC	**56**	11.049	637.19	**1010.81**	**172.53**	313.001		
59	13 3/8" CSG, 68#, N-80, BTC	**56**	10.682	637.19	**OUT**	**172.53**	313.001		**OUT**
60	13 3/8" CSG, 68#, N-80, BTC	**57**	11.322	648.51	**999.49**	**174.61**	318.563		
61	13 3/8" CSG, 68#, N-80, BTC	**58**	11.475	659.99	**988.01**	**176.73**	324.200		
62	13 3/8" CSG, 68#, N-80, BTC	**59**	11.467	671.45	**976.55**	**178.85**	329.833		
63	13 3/8" CSG, 68#, N-80, BTC	**60**	11.472	682.93	**965.07**	**180.96**	335.468		
64	13 3/8" CSG, 68#, N-80, BTC	**61**	11.402	694.33	**953.67**	**183.07**	341.069	BOW	
65	13 3/8" CSG, 68#, N-80, BTC	**62**	11.400	705.73	**942.27**	**185.17**	346.669		
66	13 3/8" CSG, 68#, N-80, BTC	**63**	11.474	717.20	**930.80**	**187.28**	352.305		
67	13 3/8" CSG, 68#, N-80, BTC	**64**	11.427	728.63	**919.37**	**189.39**	357.918		
68	13 3/8" CSG, 68#, N-80, BTC	**65**	11.334	739.96	**908.04**	**191.48**	363.486		
69	13 3/8" CSG, 68#, N-80, BTC	**66**	11.340	751.30	**896.70**	**193.57**	369.056		
70	13 3/8" CSG, 68#, N-80, BTC	**67**	11.445	762.75	**885.25**	**195.69**	374.678	BOW	
71	13 3/8" CSG, 68#, N-80, BTC	**68**	11.484	774.23	**873.77**	**197.80**	380.319		
72	13 3/8" CSG, 68#, N-80, BTC	**69**	11.215	785.45	**862.55**	**199.87**	385.828		
73	13 3/8" CSG, 68#, N-80, BTC	**70**	11.184	796.63	**851.37**	**201.93**	391.322		
74	13 3/8" CSG, 68#, N-80, BTC	**71**	11.322	807.95	**840.05**	**204.02**	396.884		
75	13 3/8" CSG, 68#, N-80, BTC	**72**	11.317	819.27	**828.73**	**206.11**	402.443		
76	13 3/8" CSG, 68#, N-80, BTC	**73**	11.149	830.42	**817.58**	**208.17**	407.920	BOW	
77	13 3/8" CSG, 68#, N-80, BTC	**74**	11.492	841.91	**806.09**	**210.29**	413.565		
78	13 3/8" CSG, 68#, N-80, BTC	**75**	11.397	853.31	**794.69**	**212.39**	419.163		
79	13 3/8" CSG, 68#, N-80, BTC	**76**	11.407	864.72	**783.29**	**214.49**	424.767		
80	13 3/8" CSG, 68#, N-80, BTC	**76**	10.973	864.72	**OUT**	**214.49**	424.767		**OUT**
81	13 3/8" CSG, 68#, N-80, BTC	**77**	11.407	876.12	**771.88**	**216.60**	430.370		
82	13 3/8" CSG, 68#, N-80, BTC	**78**	11.407	887.53	**760.47**	**218.70**	435.973		
83	13 3/8" CSG, 68#, N-80, BTC	**79**	11.474	899.00	**749.00**	**220.82**	441.610	BOW	
84	13 3/8" CSG, 68#, N-80, BTC	**80**	11.451	910.45	**737.55**	**222.93**	447.235		
85	13 3/8" CSG, 68#, N-80, BTC	**81**	11.465	921.92	**726.08**	**225.04**	452.866		
86	13 3/8" CSG, 68#, N-80, BTC	**82**	11.472	933.39	**714.61**	**227.16**	458.502		
87	13 3/8" CSG, 68#, N-80, BTC	**83**	11.192	944.58	**703.42**	**229.22**	463.999		
88	13 3/8" CSG, 68#, N-80, BTC	**84**	11.506	956.09	**691.91**	**231.35**	469.651		
89	13 3/8" CSG, 68#, N-80, BTC	**85**	11.462	967.55	**680.45**	**233.46**	475.282	BOW	
90	13 3/8" CSG, 68#, N-80, BTC	**86**	11.462	979.01	**668.99**	**235.57**	480.912		
91	13 3/8" CSG, 68#, N-80, BTC	**87**	11.313	990.33	**657.67**	**237.66**	486.469		
92	13 3/8" CSG, 68#, N-80, BTC	**87**	10.557	990.33	**OUT**	**237.66**	486.469		**OUT**
93	13 3/8" CSG, 68#, N-80, BTC	**88**	11.457	1001.78	**646.22**	**239.77**	492.097		
94	13 3/8" CSG, 68#, N-80, BTC	**89**	11.427	1013.21	**634.79**	**241.88**	497.710		
95	13 3/8" CSG, 68#, N-80, BTC	**89**	11.074	1013.21	**OUT**	**241.88**	497.710		**OUT**
96	13 3/8" CSG, 68#, N-80, BTC	**90**	11.181	1024.39	**623.61**	**243.94**	503.203		
97	13 3/8" CSG, 68#, N-80, BTC	**91**	11.452	1035.84	**612.16**	**246.06**	508.828	BOW	
98	13 3/8" CSG, 68#, N-80, BTC	**92**	11.487	1047.33	**600.67**	**248.17**	514.471		
99	13 3/8" CSG, 68#, N-80, BTC	**93**	11.487	1058.82	**589.18**	**250.29**	520.114		
100	13 3/8" CSG, 68#, N-80, BTC	**94**	11.716	1070.53	**577.47**	**252.45**	525.869		
101	13 3/8" CSG, 68#, N-80, BTC	**94**	11.045	1070.53	**OUT**	**252.45**	525.869		**OUT**
102	13 3/8" CSG, 68#, N-80, BTC	**95**	11.187	1081.72	**566.28**	**254.52**	531.364		
103	13 3/8" CSG, 68#, N-80, BTC	**96**	11.321	1093.04	**554.96**	**256.61**	536.925		
104	13 3/8" CSG, 68#, N-80, BTC	**97**	11.462	1104.50	**543.50**	**258.72**	542.556	BOW	
105	13 3/8" CSG, 68#, N-80, BTC	**98**	11.470	1115.97	**532.03**	**260.84**	548.190		
106	13 3/8" CSG, 68#, N-80, BTC	**98**	10.962	1115.97	**OUT**	**260.84**	548.190		**OUT**
107	13 3/8" CSG, 68#, N-80, BTC	**99**	11.248	1127.22	**520.78**	**262.91**	553.715		
108	13 3/8" CSG, 68#, N-80, BTC	**100**	11.485	1138.71	**509.29**	**265.03**	559.357		
109	13 3/8" CSG, 68#, N-80, BTC	**101**	11.477	1150.18	**497.82**	**267.15**	564.995		
110	13 3/8" CSG, 68#, N-80, BTC	**102**	11.208	1161.39	**486.61**	**269.21**	570.500		
111	13 3/8" CSG, 68#, N-80, BTC	**103**	11.489	1172.88	**475.12**	**271.33**	576.144	BOW	
112	13 3/8" CSG, 68#, N-80, BTC	**104**	11.169	1184.05	**463.95**	**273.39**	581.630		
113	13 3/8" CSG, 68#, N-80, BTC	**105**	11.323	1195.37	**452.63**	**275.48**	587.192		
114	13 3/8" CSG, 68#, N-80, BTC	**105**	10.739	1195.37	**OUT**	**275.48**	587.192		**OUT**
115	13 3/8" CSG, 68#, N-80, BTC	**105**	10.842	1195.37	**OUT**	**275.48**	587.192		**OUT**
116	13 3/8" CSG, 68#, N-80, BTC	**105**	11.145	1195.37	**OUT**	**275.48**	587.192		**OUT**
117	13 3/8" CSG, 68#, N-80, BTC	**106**	11.145	1206.52	**441.48**	**277.54**	592.667		
118	13 3/8" CSG, 68#, N-80, BTC	**107**	11.165	1217.68	**430.32**	**279.60**	598.151		
119	13 3/8" CSG, 68#, N-80, BTC	**108**	11.482	1229.16	**418.84**	**281.71**	603.792		

120	13 3/8" CSG, 68#, N-80, BTC	109	11.352	1240.52	407.48	283.81	609.368	BOW	
121	13 3/8" CSG, 68#, N-80, BTC	110	11.468	1251.98	396.02	285.92	615.001		
122	13 3/8" CSG, 68#, N-80, BTC	111	11.314	1263.30	384.70	288.01	620.559		
123	13 3/8" CSG, 68#, N-80, BTC	112	11.485	1274.78	373.22	290.13	626.201		
124	13 3/8" CSG, 68#, N-80, BTC	113	11.459	1286.24	361.76	292.24	631.830		
125	13 3/8" CSG, 68#, N-80, BTC	114	11.492	1297.73	350.27	294.36	637.475		
126	13 3/8" CSG, 68#, N-80, BTC	115	11.419	1309.15	338.85	296.47	643.084	BOW	
127	13 3/8" CSG, 68#, N-80, BTC	116	11.417	1320.57	327.43	298.57	648.692		
128	13 3/8" CSG, 68#, N-80, BTC	117	11.484	1332.05	315.95	300.69	654.333		
129	13 3/8" CSG, 68#, N-80, BTC	118	11.433	1343.49	304.51	302.80	659.950		
130	13 3/8" CSG, 68#, N-80, BTC	119	11.455	1354.94	293.06	304.91	665.577		
131	13 3/8" CSG, 68#, N-80, BTC	120	11.287	1366.23	281.77	306.99	671.121		
132	13 3/8" CSG, 68#, N-80, BTC	121	11.432	1377.66	270.34	309.10	676.737	BOW	
133	13 3/8" CSG, 68#, N-80, BTC	122	11.292	1388.95	259.05	311.19	682.283		
134	13 3/8" CSG, 68#, N-80, BTC	123	11.317	1400.27	247.73	313.27	687.843		
135	13 3/8" CSG, 68#, N-80, BTC	124	11.462	1411.73	236.27	315.39	693.473		
136	13 3/8" CSG, 68#, N-80, BTC	125	11.432	1423.16	224.84	317.50	699.089		
137	13 3/8" CSG, 68#, N-80, BTC	125	11.067	1423.16	OUT	317.50	699.089		OUT
138	13 3/8" CSG, 68#, N-80, BTC	126	11.414	1434.58	213.42	319.60	704.695		
139	13 3/8" CSG, 68#, N-80, BTC	127	11.232	1445.81	202.19	321.67	710.213	BOW	
140	13 3/8" CSG, 68#, N-80, BTC	128	11.040	1456.85	191.15	323.71	715.636		
141	13 3/8" CSG, 68#, N-80, BTC	129	11.457	1468.31	179.69	325.82	721.264		
142	13 3/8" CSG, 68#, N-80, BTC	130	11.363	1479.67	168.33	327.92	726.846		
143	13 3/8" CSG, 68#, N-80, BTC	131	11.487	1491.16	156.84	330.04	732.488		
144	13 3/8" CSG, 68#, N-80, BTC	132	11.357	1502.51	145.49	332.13	738.067		
145	13 3/8" CSG, 68#, N-80, BTC	133	11.347	1513.86	134.14	334.22	743.641	RIGID	
146	13 3/8" CSG, 68#, N-80, BTC	134	11.415	1525.28	122.72	336.33	749.248		
147	13 3/8" CSG, 68#, N-80, BTC	135	11.217	1536.49	111.51	338.40	754.758		
148	13 3/8" CSG, 68#, N-80, BTC	136	11.451	1547.94	100.06	340.51	760.383		
149	13 3/8" CSG, 68#, N-80, BTC	137	11.324	1559.27	88.73	342.60	765.946		
150	13 3/8" CSG, 68#, N-80, BTC	138	11.471	1570.74	77.26	344.72	771.581		
151	13 3/8" CSG, 68#, N-80, BTC	139	11.457	1582.20	65.80	346.83	777.209	RIGID	
152	13 3/8" CSG, 68#, N-80, BTC	140	11.454	1593.65	54.35	348.94	782.835		
153	13 3/8" CSG, 68#, N-80, BTC	141	11.469	1605.12	42.88	351.06	788.469		
154	13 3/8" CSG, 68#, N-80, BTC	142	11.407	1616.53	31.47	353.16	794.072	RIGID	
155	13 3/8" CSG, 68#, N-80, BTC	143	11.106	1627.63	20.37	355.21	799.528		
156	13 3/8" CSG, 68#, N-80, BTC	144	11.434	1639.07	8.93	357.32	805.144		
157	13 3/8" CSG, 68#, N-80, BTC	145	11.459	1650.53	-2.53	359.43	810.773		

6.3 9-5/8" Casing

9-5/8" Casing Report

Casing Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012		N
RIG	208	WSS	A.Moradi / A.Eyvazi		192,581		E
DATE	1403.11.19	HOLE DEPTH	3,895 m MD		MUD WT.	80	PCF
HOLE SIZE	12-1/4" inches		3,895 m TVD		MUD TYPE	KCl Poly Mud	

	DEPTH metres	O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS
PREVIOUS CASING	1648.0	13-3/8"	68	N-80	BTC	

CSG STRING COMPOSITION

Qty.	O.D. in	I.D.	ITEM DESCRIPTION / MANUFACTURER	Wt. lb/ft	GRADE	CONNECTION	Make Up Torque	LENGTH m	
1	9-5/8"	8.535	9 5/8" Float Shoe,53.5# T-95, N.Vam	53.5	T-95	New Vam	20875-23141-25426	0.610	
1	9-5/8"	8.535	9 5/8" CSG 53.5#, 110SS, (Box: HSM-3, Pin: N.Vam)	53.5	110SS	B:HSM-3 P: N.Vam	20875-23141-25426	11.243	
1	9-5/8"	8.535	9 5/8" CSG 53.5#, 110SS, HSM-3	53.5	110SS	HSM-3	20875-23141-25426	12.047	
1	9-5/8"	8.535	9 5/8" Float Collar,53.5# T-95, HSM-3	53.5	110SS	HSM-3	20875-23141-25426	0.610	
	9-5/8"	8.535	9 5/8" CSG 53.5#, 110SS, HSM-3	53.5	110SS	HSM-3	20875-23141-25426	3962.610	

FINAL SHOE DEPTH	3895.00 m	CSG WEIGHT IN AIR		683.7	klbs
TOTAL LENGTH OF CSG. RUN	3895.00 m	CSG WEIGHT IN MUD		572.0	klbs

PERFORMANCE	DATE/TIME
STARTED RUNNING CSG	7-Feb-2025, 10:00
FINISHED RUNNING CSG	10-Feb-2025, 12:00
TOTAL TIME (hours)	74
DOWNTIME (hours)	-

REASON(S) FOR DOWNTIME:

CASING RUNNING COMPANY:	OEOC

CENTRALISER / SCRATCHER PLACEMENT

MANUFACTURER	IDC
TYPE	12-1/4" X 9-5/8" Bow Centralizer & 13-3/8" X 9-5/8" Rigid Centralizer
PLACEMENT	Install as per CSG Tally.

COMMENTS:

Retrieved 13-5/8"wear bushing. Close Shear/Blind Rams. Change Top rams to 9-5/8" fix, Meanwhile Circ.thru C/M; 30 BPH losses. Perform Pres test Top Rams; "Ok". R/U OEOC CSG Running equipment. Set Jam System. Held PJSM. P/U 1 Jt 9-5/8" CSG (53.5#, 110SS, Pin: N.Vam Box: HSM-3), M/U 9-5/8" F.Shoe (53.5#, T-95, N.Vam, Double Valve) on shoe Jt. M/U 1 Jt 9-5/8" CSG (53.5#, 110SS, HSM-3), F/U String & check flow pass thru; Ok. M/U 9-5/8" Float Collar (53.5#, 110SS, HSM-3) below 1 Jt 9-5/8" CSG (53.5#, 110SS, HSM-3) & RIH to 400m (Totally: 34 Jts). Meanwhile F/U string every 10 Jts, Break Circ. Every 20 Jts and Circ. Across wellhead all the time; 35-20 BPHL.

Cont. Run 9-5/8" CSG (53.5#, 110SS, HSM-3) to 3700 m meanwhile F/U string & Break Circ. Every 10 Jts. Wash Dn w/ 9-5/8" CSG string f/ 3700 to 3895 m. (Totally: 327 Jts) Tag BTM w/ 10 Klb Wt; 5-2 BPHL.Slow circulate mud Thru CSG string meanwhile R/D CSG handling equpment.

Install 12-1/4" X 9-5/8" Bow Centralizer & 13-3/8" X 9-5/8" Rigid Centralizer as per tally.

9-5/8" Casing Tally

9 5/8" Casing Tally

Field :	Azadegan	Well NO:		AZNS207	Rig :	208 OEOC		Drlg CO:	MSA
Grade	ID (inch)	Drift (inch)	Weight (lb/ft)	Burst (psi)	Collaspse (psi)	Yield (klbs)	Coupling (cm)	TQ (lb.ft)	Nominal Dia. OD (inch)
110SS	8.535	8.5	53.5	10900	7950	1710	33.7	23141	9 5/8

Total Depth :	3895	Formation Name :	Gadvan	Hook Weight :	55
Shoe Depth :	3895	Formation Top :	3626.00	VOLUME (TOTAL)	904.76
Float Collar :	3870.49			Mud Weight (pcf) :	80.00

Number on jt	Grade	Run In No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	VOL(BBL)	Centralizers	IN / OUT
					3895.00	55.00			
Float Shoe	9 5/8" Float Shoe,53.5# T-95, New Vam		0.610	0.61	3894.39	55.09	0.142		
1	9 5/8" CSG 53.5#, 110SS, (Box: HSM-3, Pin: N.Vam)	1	11.243	11.85	3883.15	56.74	2.752	BOW	
2	9 5/8" CSG 53.5#, 110SS, HSM-3	2	12.047	23.90	3871.10	58.51	5.549	BOW	
Float Collar	9 5/8" Float Collar,53.5# 110SS, HSM-3		0.610	24.51	3870.49	58.60	5.690		
3	9 5/8" CSG 53.5#, 110SS, HSM-3	2	12.084	24.51	OUT	58.60	5.690		OUT
4	9 5/8" CSG 53.5#, 110SS, HSM-3	3	12.095	36.61	3858.40	60.38	8.498		
5	9 5/8" CSG 53.5#, 110SS, HSM-3	4	12.064	48.67	3846.33	62.15	11.299		
6	9 5/8" CSG 53.5#, 110SS, HSM-3	5	12.039	60.71	3834.29	63.92	14.094		
7	9 5/8" CSG 53.5#, 110SS, HSM-3	6	11.753	72.46	3822.54	65.64	16.823		
8	9 5/8" CSG 53.5#, 110SS, HSM-3	7	12.068	84.53	3810.47	67.42	19.624	BOW	
9	9 5/8" CSG 53.5#, 110SS, HSM-3	8	12.077	96.61	3798.39	69.19	22.428		
10	9 5/8" CSG 53.5#, 110SS, HSM-3	9	12.077	108.68	3786.32	70.97	25.232		
11	9 5/8" CSG 53.5#, 110SS, HSM-3	10	12.066	120.75	3774.25	72.74	28.033		
12	9 5/8" CSG 53.5#, 110SS, HSM-3	11	12.084	132.83	3762.17	74.51	30.839		
13	9 5/8" CSG 53.5#, 110SS, HSM-3	12	12.073	144.91	3750.09	76.29	33.642		
14	9 5/8" CSG 53.5#, 110SS, HSM-3	13	11.755	156.66	3738.34	78.01	36.371	BOW	
15	9 5/8" CSG 53.5#, 110SS, HSM-3	14	12.074	168.74	3726.27	79.79	39.174		
16	9 5/8" CSG 53.5#, 110SS, HSM-3	15	12.070	180.81	3714.20	81.56	41.976		
17	9 5/8" CSG 53.5#, 110SS, HSM-3	16	12.075	192.88	3702.12	83.33	44.779		
18	9 5/8" CSG 53.5#, 110SS, HSM-3	17	12.068	204.95	3690.05	85.11	47.581		
19	9 5/8" CSG 53.5#, 110SS, HSM-3	18	12.072	217.02	3677.98	86.88	50.384		
20	9 5/8" CSG 53.5#, 110SS, HSM-3	19	11.898	228.92	3666.08	88.63	53.146	BOW	
21	9 5/8" CSG 53.5#, 110SS, HSM-3	20	11.432	240.35	3654.65	90.31	55.800		
22	9 5/8" CSG 53.5#, 110SS, HSM-3	21	11.455	251.81	3643.20	91.99	58.460		
23	9 5/8" CSG 53.5#, 110SS, HSM-3	22	11.502	263.31	3631.69	93.68	61.130		
24	9 5/8" CSG 53.5#, 110SS, HSM-3	23	12.078	275.39	3619.62	95.46	63.934		
25	9 5/8" CSG 53.5#, 110SS, HSM-3	24	12.072	287.46	3607.54	97.23	66.737		
26	9 5/8" CSG 53.5#, 110SS, HSM-3	25	12.062	299.52	3595.48	99.00	69.537	BOW	
27	9 5/8" CSG 53.5#, 110SS, HSM-3	26	12.069	311.59	3583.41	100.77	72.339		
28	9 5/8" CSG 53.5#, 110SS, HSM-3	26	12.062	311.59	OUT	100.77	72.339		OUT
29	9 5/8" CSG 53.5#, 110SS, HSM-3	27	12.060	323.65	3571.35	102.55	75.139		
30	9 5/8" CSG 53.5#, 110SS, HSM-3	28	12.040	335.69	3559.31	104.31	77.934		
31	9 5/8" CSG 53.5#, 110SS, HSM-3	29	11.782	347.47	3547.53	106.04	80.669		
32	9 5/8" CSG 53.5#, 110SS, HSM-3	30	12.078	359.55	3535.45	107.82	83.473		
33	9 5/8" CSG 53.5#, 110SS, HSM-3	31	12.066	371.61	3523.39	109.59	86.275	BOW	
34	9 5/8" CSG 53.5#, 110SS, HSM-3	32	12.023	383.64	3511.36	111.36	89.066		
35	9 5/8" CSG 53.5#, 110SS, HSM-3	33	12.057	395.69	3499.31	113.13	91.865		
36	9 5/8" CSG 53.5#, 110SS, HSM-3	34	11.853	407.55	3487.45	114.87	94.617		
37	9 5/8" CSG 53.5#, 110SS, HSM-3	35	12.069	419.62	3475.38	116.64	97.419		
38	9 5/8" CSG 53.5#, 110SS, HSM-3	36	11.713	431.33	3463.67	118.36	100.138		
39	9 5/8" CSG 53.5#, 110SS, HSM-3	37	11.668	443.00	3452.00	120.08	102.847	BOW	
40	9 5/8" CSG 53.5#, 110SS, HSM-3	37	11.763	443.00	OUT	120.08	102.847		OUT
41	9 5/8" CSG 53.5#, 110SS, HSM-3	38	12.080	455.08	3439.92	121.85	105.652		
42	9 5/8" CSG 53.5#, 110SS, HSM-3	39	12.073	467.15	3427.85	123.63	108.454		
43	9 5/8" CSG 53.5#, 110SS, HSM-3	40	12.076	479.23	3415.77	125.40	111.258		
44	9 5/8" CSG 53.5#, 110SS, HSM-3	41	11.675	490.90	3404.10	127.12	113.968		
45	9 5/8" CSG 53.5#, 110SS, HSM-3	42	11.776	502.68	3392.32	128.85	116.702		
46	9 5/8" CSG 53.5#, 110SS, HSM-3	43	11.699	514.38	3380.62	130.56	119.418	BOW	
47	9 5/8" CSG 53.5#, 110SS, HSM-3	44	12.039	526.42	3368.59	132.33	122.213		
48	9 5/8" CSG 53.5#, 110SS, HSM-3	45	12.018	538.43	3356.57	134.10	125.004		
49	9 5/8" CSG 53.5#, 110SS, HSM-3	46	11.881	550.31	3344.69	135.84	127.762		
50	9 5/8" CSG 53.5#, 110SS, HSM-3	46	12.061	550.31	OUT	135.84	127.762		OUT
51	9 5/8" CSG 53.5#, 110SS, HSM-3	47	11.545	561.86	3333.14	137.54	130.442		
52	9 5/8" CSG 53.5#, 110SS, HSM-3	48	11.859	573.72	3321.28	139.28	133.195		
53	9 5/8" CSG 53.5#, 110SS, HSM-3	49	11.917	585.64	3309.37	141.03	135.962	BOW	
54	9 5/8" CSG 53.5#, 110SS, HSM-3	50	12.073	597.71	3297.29	142.81	138.765		
55	9 5/8" CSG 53.5#, 110SS, HSM-3	51	12.065	609.77	3285.23	144.58	141.566		
56	9 5/8" CSG 53.5#, 110SS, HSM-3	52	12.061	621.83	3273.17	146.35	144.366		
57	9 5/8" CSG 53.5#, 110SS, HSM-3	53	12.070	633.90	3261.10	148.12	147.168		
58	9 5/8" CSG 53.5#, 110SS, HSM-3	54	12.064	645.97	3249.03	149.90	149.969		
59	9 5/8" CSG 53.5#, 110SS, HSM-3	55	11.482	657.45	3237.55	151.58	152.635	BOW	
60	9 5/8" CSG 53.5#, 110SS, HSM-3	56	11.760	669.21	3225.79	153.31	155.365		
61	9 5/8" CSG 53.5#, 110SS, HSM-3	57	12.056	681.27	3213.73	155.08	158.164		
62	9 5/8" CSG 53.5#, 110SS, HSM-3	57	12.054	681.27	OUT	155.08	158.164		OUT

63	9 5/8" CSG 53.5#, 110SS, HSM-3	58	12.072	693.34	3201.66	156.85	160.967		
64	9 5/8" CSG 53.5#, 110SS, HSM-3	59	12.090	705.43	3189.57	158.63	163.773		
65	9 5/8" CSG 53.5#, 110SS, HSM-3	60	11.451	716.88	3178.12	160.31	166.432		
66	9 5/8" CSG 53.5#, 110SS, HSM-3	61	12.030	728.91	3166.09	162.08	169.225	BOW	
67	9 5/8" CSG 53.5#, 110SS, HSM-3	62	11.823	740.73	3154.27	163.82	171.970		
68	9 5/8" CSG 53.5#, 110SS, HSM-3	63	11.921	752.65	3142.35	165.57	174.737		
69	9 5/8" CSG 53.5#, 110SS, HSM-3	64	12.070	764.72	3130.28	167.34	177.540		
70	9 5/8" CSG 53.5#, 110SS, HSM-3	65	11.722	776.45	3118.56	169.06	180.261		
71	9 5/8" CSG 53.5#, 110SS, HSM-3	66	11.896	788.34	3106.66	170.81	183.023		
72	9 5/8" CSG 53.5#, 110SS, HSM-3	67	11.546	799.89	3095.11	172.51	185.703	BOW	
73	9 5/8" CSG 53.5#, 110SS, HSM-3	68	12.046	811.93	3083.07	174.28	188.500		
74	9 5/8" CSG 53.5#, 110SS, HSM-3	69	12.074	824.01	3070.99	176.05	191.303		
75	9 5/8" CSG 53.5#, 110SS, HSM-3	70	12.068	836.08	3058.93	177.82	194.105		
76	9 5/8" CSG 53.5#, 110SS, HSM-3	71	12.067	848.14	3046.86	179.60	196.906		
77	9 5/8" CSG 53.5#, 110SS, HSM-3	72	11.758	859.90	3035.10	181.32	199.636		
78	9 5/8" CSG 53.5#, 110SS, HSM-3	73	11.611	871.51	3023.49	183.03	202.332	BOW	
79	9 5/8" CSG 53.5#, 110SS, HSM-3	74	11.956	883.47	3011.53	184.78	205.107		
80	9 5/8" CSG 53.5#, 110SS, HSM-3	75	11.620	895.09	2999.91	186.49	207.805		
81	9 5/8" CSG 53.5#, 110SS, HSM-3	76	11.872	906.96	2988.04	188.24	210.561		
82	9 5/8" CSG 53.5#, 110SS, HSM-3	77	11.871	918.83	2976.17	189.98	213.317		
83	9 5/8" CSG 53.5#, 110SS, HSM-3	78	12.058	930.89	2964.11	191.75	216.117		
84	9 5/8" CSG 53.5#, 110SS, HSM-3	79	11.873	942.76	2952.24	193.50	218.873	BOW	
85	9 5/8" CSG 53.5#, 110SS, HSM-3	80	12.079	954.84	2940.16	195.27	221.677		
86	9 5/8" CSG 53.5#, 110SS, HSM-3	81	12.060	966.90	2928.10	197.04	224.477		
87	9 5/8" CSG 53.5#, 110SS, HSM-3	82	12.071	978.97	2916.03	198.81	227.280		
88	9 5/8" CSG 53.5#, 110SS, HSM-3	83	12.073	991.04	2903.96	200.59	230.083		
89	9 5/8" CSG 53.5#, 110SS, HSM-3	84	12.031	1003.08	2891.93	202.36	232.876		
90	9 5/8" CSG 53.5#, 110SS, HSM-3	85	11.726	1014.80	2880.20	204.08	235.598	BOW	
91	9 5/8" CSG 53.5#, 110SS, HSM-3	86	12.050	1026.85	2868.15	205.85	238.396		
92	9 5/8" CSG 53.5#, 110SS, HSM-3	87	12.066	1038.92	2856.08	207.62	241.197		
93	9 5/8" CSG 53.5#, 110SS, HSM-3	88	12.071	1050.99	2844.01	209.39	243.999		
94	9 5/8" CSG 53.5#, 110SS, HSM-3	89	12.070	1063.06	2831.94	211.17	246.802		
95	9 5/8" CSG 53.5#, 110SS, HSM-3	90	12.060	1075.12	2819.88	212.94	249.601		
96	9 5/8" CSG 53.5#, 110SS, HSM-3	91	12.060	1087.18	2807.82	214.71	252.401	BOW	
97	9 5/8" CSG 53.5#, 110SS, HSM-3	92	12.063	1099.24	2795.76	216.48	255.202		
98	9 5/8" CSG 53.5#, 110SS, HSM-3	93	11.839	1111.08	2783.92	218.22	257.950		
99	9 5/8" CSG 53.5#, 110SS, HSM-3	93	11.790	1111.08	OUT	218.22	257.950		OUT
100	9 5/8" CSG 53.5#, 110SS, HSM-3	93	12.080	1111.08	OUT	218.22	257.950		OUT
101	9 5/8" CSG 53.5#, 110SS, HSM-3	93	12.070	1111.08	OUT	218.22	257.950		OUT
102	9 5/8" CSG 53.5#, 110SS, HSM-3	94	12.069	1123.15	2771.85	220.00	260.752		
103	9 5/8" CSG 53.5#, 110SS, HSM-3	95	12.059	1135.21	2759.79	221.77	263.552		
104	9 5/8" CSG 53.5#, 110SS, HSM-3	96	12.021	1147.23	2747.77	223.53	266.343		
105	9 5/8" CSG 53.5#, 110SS, HSM-3	97	11.913	1159.14	2735.86	225.28	269.109	BOW	
106	9 5/8" CSG 53.5#, 110SS, HSM-3	98	11.725	1170.87	2724.13	227.01	271.831		
107	9 5/8" CSG 53.5#, 110SS, HSM-3	99	12.066	1182.93	2712.07	228.78	274.632		
108	9 5/8" CSG 53.5#, 110SS, HSM-3	100	11.898	1194.83	2700.17	230.53	277.394		
109	9 5/8" CSG 53.5#, 110SS, HSM-3	101	11.727	1206.56	2688.44	232.25	280.117		
110	9 5/8" CSG 53.5#, 110SS, HSM-3	102	11.840	1218.40	2676.60	233.99	282.866		
111	9 5/8" CSG 53.5#, 110SS, HSM-3	103	11.866	1230.26	2664.74	235.73	285.620	BOW	
112	9 5/8" CSG 53.5#, 110SS, HSM-3	103	11.773	1230.26	OUT	235.73	285.620		OUT
113	9 5/8" CSG 53.5#, 110SS, HSM-3	104	12.057	1242.32	2652.68	237.50	288.420		
114	9 5/8" CSG 53.5#, 110SS, HSM-3	105	12.039	1254.36	2640.64	239.27	291.215		
115	9 5/8" CSG 53.5#, 110SS, HSM-3	106	11.895	1266.26	2628.75	241.02	293.976		
116	9 5/8" CSG 53.5#, 110SS, HSM-3	107	11.694	1277.95	2617.05	242.74	296.691		
117	9 5/8" CSG 53.5#, 110SS, HSM-3	108	11.868	1289.82	2605.18	244.48	299.446		
118	9 5/8" CSG 53.5#, 110SS, HSM-3	109	12.073	1301.89	2593.11	246.25	302.249	BOW	
119	9 5/8" CSG 53.5#, 110SS, HSM-3	110	12.092	1313.98	2581.02	248.03	305.057		
120	9 5/8" CSG 53.5#, 110SS, HSM-3	111	12.064	1326.05	2568.95	249.80	307.857		
121	9 5/8" CSG 53.5#, 110SS, HSM-3	112	12.077	1338.12	2556.88	251.58	310.661		
122	9 5/8" CSG 53.5#, 110SS, HSM-3	113	12.047	1350.17	2544.83	253.35	313.458		
123	9 5/8" CSG 53.5#, 110SS, HSM-3	114	12.039	1362.21	2532.79	255.11	316.253		
124	9 5/8" CSG 53.5#, 110SS, HSM-3	115	11.886	1374.10	2520.91	256.86	319.012	BOW	
125	9 5/8" CSG 53.5#, 110SS, HSM-3	116	11.065	1385.16	2509.84	258.49	321.581		L.JOINT
126	9 5/8" CSG 53.5#, 110SS, HSM-3	117	11.361	1396.52	2498.48	260.15	324.219		
127	9 5/8" CSG 53.5#, 110SS, HSM-3	118	11.676	1408.20	2486.80	261.87	326.930		
128	9 5/8" CSG 53.5#, 110SS, HSM-3	119	11.493	1419.69	2475.31	263.56	329.598		
129	9 5/8" CSG 53.5#, 110SS, HSM-3	120	11.771	1431.46	2463.54	265.29	332.331		
130	9 5/8" CSG 53.5#, 110SS, HSM-3	121	11.817	1443.28	2451.72	267.02	335.074	BOW	
131	9 5/8" CSG 53.5#, 110SS, HSM-3	122	12.030	1455.31	2439.69	268.79	337.867		
132	9 5/8" CSG 53.5#, 110SS, HSM-3	123	11.591	1466.90	2428.10	270.49	340.558		
133	9 5/8" CSG 53.5#, 110SS, HSM-3	124	11.876	1478.78	2416.22	272.24	343.315		
134	9 5/8" CSG 53.5#, 110SS, HSM-3	125	11.908	1490.68	2404.32	273.99	346.080		
135	9 5/8" CSG 53.5#, 110SS, HSM-3	125	12.066	1490.68	OUT	273.99	346.080		OUT
136	9 5/8" CSG 53.5#, 110SS, HSM-3	125	12.082	1490.68	OUT	273.99	346.080		OUT
137	9 5/8" CSG 53.5#, 110SS, HSM-3	126	11.893	1502.58	2392.42	275.73	348.841		
138	9 5/8" CSG 53.5#, 110SS, HSM-3	127	11.882	1514.46	2380.54	277.48	351.599	BOW	
139	9 5/8" CSG 53.5#, 110SS, HSM-3	128	11.768	1526.23	2368.77	279.21	354.332		
140	9 5/8" CSG 53.5#, 110SS, HSM-3	129	12.043	1538.27	2356.73	280.98	357.127		
141	9 5/8" CSG 53.5#, 110SS, HSM-3	129	11.827	1538.27	OUT	280.98	357.127		OUT
142	9 5/8" CSG 53.5#, 110SS, HSM-3	130	11.608	1549.88	2345.12	282.68	359.822		

143	9 5/8" CSG 53.5#, 110SS, HSM-3	131	12.076	1561.95	2333.05	284.46	362.626		
144	9 5/8" CSG 53.5#, 110SS, HSM-3	131	12.065	1561.95	OUT	284.46	362.626		OUT
145	9 5/8" CSG 53.5#, 110SS, HSM-3	132	11.771	1573.72	2321.28	286.19	365.359		
146	9 5/8" CSG 53.5#, 110SS, HSM-3	133	11.757	1585.48	2309.52	287.91	368.088	BOW	
147	9 5/8" CSG 53.5#, 110SS, HSM-3	133	12.083	1585.48	OUT	287.91	368.088		OUT
148	9 5/8" CSG 53.5#, 110SS, HSM-3	133	12.056	1585.48	OUT	287.91	368.088		OUT
149	9 5/8" CSG 53.5#, 110SS, HSM-3	134	12.080	1597.56	2297.44	289.69	370.893		
150	9 5/8" CSG 53.5#, 110SS, HSM-3	134	12.058	1597.56	OUT	289.69	370.893		OUT
151	9 5/8" CSG 53.5#, 110SS, HSM-3	134	11.900	1597.56	OUT	289.69	370.893		OUT
152	9 5/8" CSG 53.5#, 110SS, HSM-3	135	11.918	1609.48	2285.52	291.44	373.660		
153	9 5/8" CSG 53.5#, 110SS, HSM-3	136	12.061	1621.54	2273.46	293.21	376.460		
154	9 5/8" CSG 53.5#, 110SS, HSM-3	137	12.079	1633.62	2261.38	294.99	379.264		
155	9 5/8" CSG 53.5#, 110SS, HSM-3	138	12.047	1645.67	2249.33	296.76	382.061		
156	9 5/8" CSG 53.5#, 110SS, HSM-3	139	12.058	1657.72	2237.28	298.53	384.860	BOW	
157	9 5/8" CSG 53.5#, 110SS, HSM-3	140	12.089	1669.81	2225.19	300.30	387.667		
158	9 5/8" CSG 53.5#, 110SS, HSM-3	141	11.770	1681.58	2213.42	302.03	390.400		
159	9 5/8" CSG 53.5#, 110SS, HSM-3	142	12.024	1693.61	2201.39	303.80	393.191		
160	9 5/8" CSG 53.5#, 110SS, HSM-3	143	12.047	1705.65	2189.35	305.57	395.988		
161	9 5/8" CSG 53.5#, 110SS, HSM-3	144	11.874	1717.53	2177.47	307.31	398.745		
162	9 5/8" CSG 53.5#, 110SS, HSM-3	145	11.684	1729.21	2165.79	309.03	401.457	BOW	
163	9 5/8" CSG 53.5#, 110SS, HSM-3	145	12.072	1729.21	OUT	309.03	401.457		OUT
164	9 5/8" CSG 53.5#, 110SS, HSM-3	146	12.063	1741.28	2153.72	310.80	404.258		
165	9 5/8" CSG 53.5#, 110SS, HSM-3	147	11.907	1753.18	2141.82	312.55	407.022		
166	9 5/8" CSG 53.5#, 110SS, HSM-3	148	11.705	1764.89	2130.11	314.27	409.740		
167	9 5/8" CSG 53.5#, 110SS, HSM-3	149	12.070	1776.96	2118.04	316.04	412.542		
168	9 5/8" CSG 53.5#, 110SS, HSM-3	150	12.091	1789.05	2105.95	317.82	415.349		
169	9 5/8" CSG 53.5#, 110SS, HSM-3	151	12.065	1801.11	2093.89	319.59	418.150	BOW	
170	9 5/8" CSG 53.5#, 110SS, HSM-3	152	11.547	1812.66	2082.34	321.29	420.831		
171	9 5/8" CSG 53.5#, 110SS, HSM-3	153	11.900	1824.56	2070.44	323.04	423.593		
172	9 5/8" CSG 53.5#, 110SS, HSM-3	154	12.061	1836.62	2058.38	324.81	426.393		
173	9 5/8" CSG 53.5#, 110SS, HSM-3	155	12.050	1848.67	2046.33	326.58	429.191		
174	9 5/8" CSG 53.5#, 110SS, HSM-3	156	11.795	1860.47	2034.53	328.31	431.929		
175	9 5/8" CSG 53.5#, 110SS, HSM-3	157	11.524	1871.99	2023.01	330.00	434.605	BOW	
176	9 5/8" CSG 53.5#, 110SS, HSM-3	158	12.064	1884.05	2010.95	331.78	437.406		
177	9 5/8" CSG 53.5#, 110SS, HSM-3	159	11.828	1895.88	1999.12	333.51	440.152		
178	9 5/8" CSG 53.5#, 110SS, HSM-3	160	12.068	1907.95	1987.05	335.29	442.953		
179	9 5/8" CSG 53.5#, 110SS, HSM-3	161	12.070	1920.02	1974.98	337.06	445.756		
180	9 5/8" CSG 53.5#, 110SS, HSM-3	162	12.044	1932.06	1962.94	338.83	448.552		
181	9 5/8" CSG 53.5#, 110SS, HSM-3	163	12.052	1944.12	1950.88	340.60	451.350		
182	9 5/8" CSG 53.5#, 110SS, HSM-3	163	12.058	1944.12	OUT	340.60	451.350		OUT
183	9 5/8" CSG 53.5#, 110SS, HSM-3	163	12.060	1944.12	OUT	340.60	451.350		OUT
184	9 5/8" CSG 53.5#, 110SS, HSM-3	164	12.043	1956.16	1938.84	342.37	454.146	BOW	
185	9 5/8" CSG 53.5#, 110SS, HSM-3	165	12.041	1968.20	1926.80	344.14	456.941		
186	9 5/8" CSG 53.5#, 110SS, HSM-3	166	12.062	1980.26	1914.74	345.91	459.741		
187	9 5/8" CSG 53.5#, 110SS, HSM-3	167	12.082	1992.34	1902.66	347.68	462.546		
188	9 5/8" CSG 53.5#, 110SS, HSM-3	168	12.032	2004.38	1890.62	349.45	465.340		
189	9 5/8" CSG 53.5#, 110SS, HSM-3	169	11.933	2016.31	1878.69	351.20	468.110		
190	9 5/8" CSG 53.5#, 110SS, HSM-3	170	11.899	2028.21	1866.79	352.95	470.873	BOW	
191	9 5/8" CSG 53.5#, 110SS, HSM-3	171	11.845	2040.05	1854.95	354.69	473.623		
192	9 5/8" CSG 53.5#, 110SS, HSM-3	172	12.073	2052.13	1842.87	356.47	476.425		
193	9 5/8" CSG 53.5#, 110SS, HSM-3	172	12.054	2052.13	OUT	356.47	476.425		OUT
194	9 5/8" CSG 53.5#, 110SS, HSM-3	173	11.653	2063.78	1831.22	358.18	479.131		
195	9 5/8" CSG 53.5#, 110SS, HSM-3	174	11.632	2075.41	1819.59	359.89	481.831		
196	9 5/8" CSG 53.5#, 110SS, HSM-3	175	11.631	2087.04	1807.96	361.60	484.532		
197	9 5/8" CSG 53.5#, 110SS, HSM-3	176	12.058	2099.10	1795.90	363.37	487.331		
198	9 5/8" CSG 53.5#, 110SS, HSM-3	177	12.020	2111.12	1783.88	365.13	490.122	BOW	
199	9 5/8" CSG 53.5#, 110SS, HSM-3	178	12.035	2123.16	1771.84	366.90	492.916		
200	9 5/8" CSG 53.5#, 110SS, HSM-3	179	12.078	2135.23	1759.77	368.67	495.720		
201	9 5/8" CSG 53.5#, 110SS, HSM-3	180	12.068	2147.30	1747.70	370.45	498.522		
202	9 5/8" CSG 53.5#, 110SS, HSM-3	181	11.753	2159.05	1735.95	372.17	501.250		
203	9 5/8" CSG 53.5#, 110SS, HSM-3	181	11.563	2159.05	OUT	372.17	501.250		OUT
204	9 5/8" CSG 53.5#, 110SS, HSM-3	182	11.776	2170.83	1724.17	373.90	503.984	BOW	
205	9 5/8" CSG 53.5#, 110SS, HSM-3	183	12.075	2182.91	1712.09	375.68	506.787		
206	9 5/8" CSG 53.5#, 110SS, HSM-3	184	12.053	2194.96	1700.04	377.45	509.586		
207	9 5/8" CSG 53.5#, 110SS, HSM-3	185	11.904	2206.86	1688.14	379.20	512.349		
208	9 5/8" CSG 53.5#, 110SS, HSM-3	186	11.639	2218.50	1676.50	380.91	515.051		
209	9 5/8" CSG 53.5#, 110SS, HSM-3	187	11.853	2230.35	1664.65	382.65	517.803		
210	9 5/8" CSG 53.5#, 110SS, HSM-3	188	11.862	2242.22	1652.78	384.39	520.557	BOW	
211	9 5/8" CSG 53.5#, 110SS, HSM-3	189	11.886	2254.10	1640.90	386.14	523.317		
212	9 5/8" CSG 53.5#, 110SS, HSM-3	190	12.051	2266.15	1628.85	387.91	526.114		
213	9 5/8" CSG 53.5#, 110SS, HSM-3	191	11.879	2278.03	1616.97	389.65	528.872		
214	9 5/8" CSG 53.5#, 110SS, HSM-3	192	11.547	2289.58	1605.42	391.35	531.553		
215	9 5/8" CSG 53.5#, 110SS, HSM-3	193	12.084	2301.66	1593.34	393.12	534.358		
216	9 5/8" CSG 53.5#, 110SS, HSM-3	194	11.720	2313.38	1581.62	394.85	537.079	RIGID	
217	9 5/8" CSG 53.5#, 110SS, HSM-3	195	12.011	2325.39	1569.61	396.61	539.868		
218	9 5/8" CSG 53.5#, 110SS, HSM-3	196	12.009	2337.40	1557.60	398.37	542.656		
219	9 5/8" CSG 53.5#, 110SS, HSM-3	197	11.749	2349.15	1545.85	400.10	545.384		
220	9 5/8" CSG 53.5#, 110SS, HSM-3	198	12.026	2361.18	1533.82	401.87	548.176		
221	9 5/8" CSG 53.5#, 110SS, HSM-3	199	12.068	2373.25	1521.75	403.64	550.977		
222	9 5/8" CSG 53.5#, 110SS, HSM-3	200	12.072	2385.32	1509.68	405.41	553.780	RIGID	

223	9 5/8" CSG 53.5#, 110SS, HSM-3	201	12.065	2397.38	1497.62	407.19	556.581		
224	9 5/8" CSG 53.5#, 110SS, HSM-3	201	11.738	2397.38	OUT	407.19	556.581		OUT
225	9 5/8" CSG 53.5#, 110SS, HSM-3	202	12.059	2409.44	1485.56	408.96	559.381		
226	9 5/8" CSG 53.5#, 110SS, HSM-3	202	11.689	2409.44	OUT	408.96	559.381		OUT
227	9 5/8" CSG 53.5#, 110SS, HSM-3	203	12.057	2421.50	1473.50	410.73	562.180		
228	9 5/8" CSG 53.5#, 110SS, HSM-3	204	11.769	2433.27	1461.73	412.46	564.912		
229	9 5/8" CSG 53.5#, 110SS, HSM-3	205	11.584	2444.85	1450.15	414.16	567.602		
230	9 5/8" CSG 53.5#, 110SS, HSM-3	206	12.086	2456.94	1438.06	415.93	570.407		
231	9 5/8" CSG 53.5#, 110SS, HSM-3	207	12.038	2468.98	1426.02	417.70	573.202	RIGID	
232	9 5/8" CSG 53.5#, 110SS, HSM-3	208	11.700	2480.68	1414.32	419.42	575.918		
233	9 5/8" CSG 53.5#, 110SS, HSM-3	209	11.603	2492.28	1402.72	421.13	578.612		
234	9 5/8" CSG 53.5#, 110SS, HSM-3	210	11.688	2503.97	1391.03	422.84	581.326		
235	9 5/8" CSG 53.5#, 110SS, HSM-3	210	11.388	2503.97	OUT	422.84	581.326		OUT
236	9 5/8" CSG 53.5#, 110SS, HSM-3	210	11.732	2503.97	OUT	422.84	581.326		OUT
237	9 5/8" CSG 53.5#, 110SS, HSM-3	211	12.059	2516.03	1378.97	424.61	584.125		
238	9 5/8" CSG 53.5#, 110SS, HSM-3	212	12.023	2528.05	1366.95	426.38	586.917		
239	9 5/8" CSG 53.5#, 110SS, HSM-3	213	12.085	2540.13	1354.87	428.16	589.722	RIGID	
240	9 5/8" CSG 53.5#, 110SS, HSM-3	214	12.087	2552.22	1342.78	429.93	592.528		
241	9 5/8" CSG 53.5#, 110SS, HSM-3	215	12.084	2564.31	1330.69	431.71	595.334		
242	9 5/8" CSG 53.5#, 110SS, HSM-3	216	12.070	2576.38	1318.62	433.48	598.136		
243	9 5/8" CSG 53.5#, 110SS, HSM-3	217	12.046	2588.42	1306.58	435.25	600.933		
244	9 5/8" CSG 53.5#, 110SS, HSM-3	218	11.761	2600.18	1294.82	436.98	603.663		
245	9 5/8" CSG 53.5#, 110SS, HSM-3	219	12.042	2612.22	1282.78	438.75	606.459	RIGID	
246	9 5/8" CSG 53.5#, 110SS, HSM-3	219	11.605	2612.22	OUT	438.75	606.459		OUT
247	9 5/8" CSG 53.5#, 110SS, HSM-3	219	11.472	2612.22	OUT	438.75	606.459		OUT
248	9 5/8" CSG 53.5#, 110SS, HSM-3	220	12.078	2624.30	1270.70	440.52	609.263		
249	9 5/8" CSG 53.5#, 110SS, HSM-3	221	12.072	2636.37	1258.63	442.29	612.066		
250	9 5/8" CSG 53.5#, 110SS, HSM-3	222	11.892	2648.27	1246.73	444.04	614.826		
251	9 5/8" CSG 53.5#, 110SS, HSM-3	223	11.576	2659.84	1235.16	445.74	617.514		
252	9 5/8" CSG 53.5#, 110SS, HSM-3	224	11.733	2671.58	1223.42	447.47	620.238	RIGID	
253	9 5/8" CSG 53.5#, 110SS, HSM-3	225	11.735	2683.31	1211.69	449.19	622.962		
254	9 5/8" CSG 53.5#, 110SS, HSM-3	226	12.058	2695.37	1199.63	450.96	625.762		
255	9 5/8" CSG 53.5#, 110SS, HSM-3	227	12.088	2707.46	1187.54	452.74	628.568		
256	9 5/8" CSG 53.5#, 110SS, HSM-3	228	12.056	2719.51	1175.49	454.51	631.367		
257	9 5/8" CSG 53.5#, 110SS, HSM-3	229	11.731	2731.24	1163.76	456.23	634.091		
258	9 5/8" CSG 53.5#, 110SS, HSM-3	230	12.099	2743.34	1151.66	458.01	636.900	RIGID	
259	9 5/8" CSG 53.5#, 110SS, HSM-3	231	11.734	2755.08	1139.92	459.73	639.624		
260	9 5/8" CSG 53.5#, 110SS, HSM-3	232	11.568	2766.64	1128.36	461.43	642.309		
261	9 5/8" CSG 53.5#, 110SS, HSM-3	233	11.748	2778.39	1116.61	463.16	645.037		
262	9 5/8" CSG 53.5#, 110SS, HSM-3	234	11.625	2790.02	1104.98	464.87	647.736		
263	9 5/8" CSG 53.5#, 110SS, HSM-3	235	11.602	2801.62	1093.38	466.57	650.429		
264	9 5/8" CSG 53.5#, 110SS, HSM-3	236	11.733	2813.35	1081.65	468.29	653.153	RIGID	
265	9 5/8" CSG 53.5#, 110SS, HSM-3	237	11.450	2824.80	1070.20	469.98	655.811		
266	9 5/8" CSG 53.5#, 110SS, HSM-3	238	12.051	2836.85	1058.15	471.75	658.609		
267	9 5/8" CSG 53.5#, 110SS, HSM-3	239	12.082	2848.94	1046.06	473.52	661.414		
268	9 5/8" CSG 53.5#, 110SS, HSM-3	240	12.060	2861.00	1034.00	475.29	664.214		
269	9 5/8" CSG 53.5#, 110SS, HSM-3	241	12.057	2873.05	1021.95	477.06	667.013		
270	9 5/8" CSG 53.5#, 110SS, HSM-3	242	12.058	2885.11	1009.89	478.83	669.813		
271	9 5/8" CSG 53.5#, 110SS, HSM-3	243	11.879	2896.99	998.01	480.58	672.570	RIGID	
272	9 5/8" CSG 53.5#, 110SS, HSM-3	244	12.085	2909.07	985.93	482.36	675.376		
273	9 5/8" CSG 53.5#, 110SS, HSM-3	245	12.076	2921.15	973.85	484.13	678.180		
274	9 5/8" CSG 53.5#, 110SS, HSM-3	246	12.027	2933.18	961.82	485.90	680.972		
275	9 5/8" CSG 53.5#, 110SS, HSM-3	247	11.896	2945.07	949.93	487.64	683.734		
276	9 5/8" CSG 53.5#, 110SS, HSM-3	248	11.916	2956.99	938.01	489.39	686.500		
277	9 5/8" CSG 53.5#, 110SS, HSM-3	249	12.071	2969.06	925.94	491.17	689.303	RIGID	
278	9 5/8" CSG 53.5#, 110SS, HSM-3	250	11.498	2980.56	914.44	492.86	691.972		
279	9 5/8" CSG 53.5#, 110SS, HSM-3	251	11.861	2992.42	902.58	494.60	694.726		
280	9 5/8" CSG 53.5#, 110SS, HSM-3	252	11.796	3004.22	890.78	496.33	697.464		
281	9 5/8" CSG 53.5#, 110SS, HSM-3	253	11.857	3016.07	878.93	498.07	700.217		
282	9 5/8" CSG 53.5#, 110SS, HSM-3	254	11.851	3027.92	867.08	499.81	702.968		
283	9 5/8" CSG 53.5#, 110SS, HSM-3	255	11.849	3039.77	855.23	501.56	705.719	RIGID	
284	9 5/8" CSG 53.5#, 110SS, HSM-3	256	11.500	3051.27	843.73	503.24	708.389		
285	9 5/8" CSG 53.5#, 110SS, HSM-3	257	11.879	3063.15	831.85	504.99	711.147		
286	9 5/8" CSG 53.5#, 110SS, HSM-3	258	12.085	3075.24	819.76	506.77	713.953		
287	9 5/8" CSG 53.5#, 110SS, HSM-3	259	11.772	3087.01	807.99	508.49	716.686		
288	9 5/8" CSG 53.5#, 110SS, HSM-3	260	11.691	3098.70	796.30	510.21	719.400		
289	9 5/8" CSG 53.5#, 110SS, HSM-3	261	11.896	3110.60	784.40	511.96	722.162	RIGID	
290	9 5/8" CSG 53.5#, 110SS, HSM-3	262	11.702	3122.30	772.70	513.68	724.878		
291	9 5/8" CSG 53.5#, 110SS, HSM-3	263	11.739	3134.04	760.96	515.40	727.604		
292	9 5/8" CSG 53.5#, 110SS, HSM-3	264	11.626	3145.66	749.34	517.11	730.303		
293	9 5/8" CSG 53.5#, 110SS, HSM-3	265	11.719	3157.38	737.62	518.83	733.024		
294	9 5/8" CSG 53.5#, 110SS, HSM-3	266	11.261	3168.64	726.36	520.49	735.638		
295	9 5/8" CSG 53.5#, 110SS, HSM-3	267	12.081	3180.72	714.28	522.26	738.443	RIGID	
296	9 5/8" CSG 53.5#, 110SS, HSM-3	268	12.055	3192.78	702.22	524.03	741.241		
297	9 5/8" CSG 53.5#, 110SS, HSM-3	269	11.729	3204.51	690.49	525.76	743.964		
298	9 5/8" CSG 53.5#, 110SS, HSM-3	270	11.917	3216.42	678.58	527.51	746.731		
299	9 5/8" CSG 53.5#, 110SS, HSM-3	271	11.897	3228.32	666.68	529.25	749.493		
300	9 5/8" CSG 53.5#, 110SS, HSM-3	272	11.774	3240.10	654.90	530.98	752.227		
301	9 5/8" CSG 53.5#, 110SS, HSM-3	273	11.532	3251.63	643.37	532.68	754.904	RIGID	
302	9 5/8" CSG 53.5#, 110SS, HSM-3	274	11.861	3263.49	631.51	534.42	757.658		

303	9 5/8" CSG 53.5#, 110SS, HSM-3	275	12.062	3275.55	619.45	536.19	760.458		
304	9 5/8" CSG 53.5#, 110SS, HSM-3	276	11.885	3287.44	607.56	537.94	763.217		
305	9 5/8" CSG 53.5#, 110SS, HSM-3	277	12.079	3299.51	595.49	539.71	766.021		
306	9 5/8" CSG 53.5#, 110SS, HSM-3	278	12.074	3311.59	583.41	541.49	768.825		
307	9 5/8" CSG 53.5#, 110SS, HSM-3	279	11.906	3323.49	571.51	543.24	771.589	RIGID	
308	9 5/8" CSG 53.5#, 110SS, HSM-3	279	11.734	3323.49	OUT	543.24	771.589		OUT
309	9 5/8" CSG 53.5#, 110SS, HSM-3	280	12.065	3335.56	559.44	545.01	774.390		
310	9 5/8" CSG 53.5#, 110SS, HSM-3	281	12.072	3347.63	547.37	546.78	777.192		
311	9 5/8" CSG 53.5#, 110SS, HSM-3	282	12.066	3359.70	535.30	548.55	779.994		
312	9 5/8" CSG 53.5#, 110SS, HSM-3	282	11.432	3359.70	OUT	548.55	779.994		OUT
313	9 5/8" CSG 53.5#, 110SS, HSM-3	283	12.082	3371.78	523.22	550.33	782.799		
314	9 5/8" CSG 53.5#, 110SS, HSM-3	283	11.739	3371.78	OUT	550.33	782.799		OUT
315	9 5/8" CSG 53.5#, 110SS, HSM-3	284	12.085	3383.86	511.14	552.10	785.604		
316	9 5/8" CSG 53.5#, 110SS, HSM-3	285	12.040	3395.90	499.10	553.87	788.400	RIGID	
317	9 5/8" CSG 53.5#, 110SS, HSM-3	286	12.028	3407.93	487.07	555.64	791.192		
318	9 5/8" CSG 53.5#, 110SS, HSM-3	287	12.036	3419.97	475.03	557.41	793.986		
319	9 5/8" CSG 53.5#, 110SS, HSM-3	288	11.902	3431.87	463.13	559.16	796.749		
320	9 5/8" CSG 53.5#, 110SS, HSM-3	289	11.718	3443.59	451.41	560.88	799.470		
321	9 5/8" CSG 53.5#, 110SS, HSM-3	290	11.894	3455.48	439.52	562.62	802.231		
322	9 5/8" CSG 53.5#, 110SS, HSM-3	291	11.855	3467.34	427.66	564.37	804.984	RIGID	
323	9 5/8" CSG 53.5#, 110SS, HSM-3	292	11.796	3479.13	415.87	566.10	807.722		
324	9 5/8" CSG 53.5#, 110SS, HSM-3	293	11.740	3490.87	404.13	567.82	810.448		
325	9 5/8" CSG 53.5#, 110SS, HSM-3	294	12.055	3502.93	392.07	569.59	813.246		
326	9 5/8" CSG 53.5#, 110SS, HSM-3	295	12.022	3514.95	380.05	571.36	816.037		
327	9 5/8" CSG 53.5#, 110SS, HSM-3	296	11.702	3526.65	368.35	573.08	818.754		
328	9 5/8" CSG 53.5#, 110SS, HSM-3	297	11.752	3538.40	356.60	574.81	821.483	RIGID	
329	9 5/8" CSG 53.5#, 110SS, HSM-3	298	11.842	3550.25	344.75	576.55	824.232		
330	9 5/8" CSG 53.5#, 110SS, HSM-3	299	11.925	3562.17	332.83	578.30	827.000		
331	9 5/8" CSG 53.5#, 110SS, HSM-3	299	11.722	3562.17	OUT	578.30	827.000		OUT
332	9 5/8" CSG 53.5#, 110SS, HSM-3	300	12.076	3574.25	320.75	580.07	829.804		
333	9 5/8" CSG 53.5#, 110SS, HSM-3	301	12.045	3586.29	308.71	581.84	832.600		
334	9 5/8" CSG 53.5#, 110SS, HSM-3	302	11.911	3598.20	296.80	583.59	835.366		
335	9 5/8" CSG 53.5#, 110SS, HSM-3	303	12.089	3610.29	284.71	585.37	838.172	RIGID	
336	9 5/8" CSG 53.5#, 110SS, HSM-3	304	12.062	3622.35	272.65	587.14	840.973		
337	9 5/8" CSG 53.5#, 110SS, HSM-3	305	11.857	3634.21	260.79	588.88	843.725		
338	9 5/8" CSG 53.5#, 110SS, HSM-3	306	12.072	3646.28	248.72	590.65	846.528		
339	9 5/8" CSG 53.5#, 110SS, HSM-3	307	12.079	3658.36	236.64	592.43	849.332		
340	9 5/8" CSG 53.5#, 110SS, HSM-3	308	12.059	3670.42	224.58	594.20	852.132		
341	9 5/8" CSG 53.5#, 110SS, HSM-3	309	11.627	3682.05	212.95	595.91	854.831	RIGID	
342	9 5/8" CSG 53.5#, 110SS, HSM-3	310	11.543	3693.59	201.41	597.60	857.511		
343	9 5/8" CSG 53.5#, 110SS, HSM-3	310	11.904	3693.59	OUT	597.60	857.511		OUT
344	9 5/8" CSG 53.5#, 110SS, HSM-3	311	12.074	3705.67	189.33	599.38	860.314		
345	9 5/8" CSG 53.5#, 110SS, HSM-3	312	12.088	3717.75	177.25	601.15	863.121		
346	9 5/8" CSG 53.5#, 110SS, HSM-3	313	11.763	3729.52	165.48	602.88	865.852		
347	9 5/8" CSG 53.5#, 110SS, HSM-3	313	11.538	3729.52	OUT	602.88	865.852		OUT
348	9 5/8" CSG 53.5#, 110SS, HSM-3	313	12.015	3729.52	OUT	602.88	865.852		OUT
349	9 5/8" CSG 53.5#, 110SS, HSM-3	314	12.040	3741.56	153.44	604.65	868.647		
350	9 5/8" CSG 53.5#, 110SS, HSM-3	315	11.718	3753.27	141.73	606.37	871.367	RIGID	
351	9 5/8" CSG 53.5#, 110SS, HSM-3	316	12.074	3765.35	129.65	608.15	874.170		
352	9 5/8" CSG 53.5#, 110SS, HSM-3	317	11.815	3777.16	117.84	609.88	876.913		
353	9 5/8" CSG 53.5#, 110SS, HSM-3	318	11.923	3789.09	105.91	611.63	879.681		
354	9 5/8" CSG 53.5#, 110SS, HSM-3	318	11.456	3789.09	OUT	611.63	879.681		OUT
355	9 5/8" CSG 53.5#, 110SS, HSM-3	318	11.863	3789.09	OUT	611.63	879.681		OUT
356	9 5/8" CSG 53.5#, 110SS, HSM-3	318	11.840	3789.09	OUT	611.63	879.681		OUT
357	9 5/8" CSG 53.5#, 110SS, HSM-3	319	12.073	3801.16	93.84	613.41	882.484		
358	9 5/8" CSG 53.5#, 110SS, HSM-3	320	12.082	3813.24	81.76	615.18	885.289		
359	9 5/8" CSG 53.5#, 110SS, HSM-3	321	12.071	3825.31	69.69	616.95	888.092	RIGID	
360	9 5/8" CSG 53.5#, 110SS, HSM-3	322	12.081	3837.39	57.61	618.73	890.896		
361	9 5/8" CSG 53.5#, 110SS, HSM-3	323	12.071	3849.46	45.54	620.50	893.699		
632	9 5/8" CSG 53.5#, 110SS, HSM-3	324	11.600	3861.06	33.94	622.21	896.392	RIGID	
363	9 5/8" CSG 53.5#, 110SS, HSM-3	325	11.900	3872.96	22.04	623.95	899.155		
364	9 5/8" CSG 53.5#, 110SS, HSM-3	326	12.071	3885.04	9.96	625.73	901.957		
365	9 5/8" CSG 53.5#, 110SS, HSM-3	327	12.089	3897.12	-2.12	627.50	904.764		
Pup Jt # 1	9 5/8" CSG 53.5#, 110SS, HSM-3	327	1.660	3897.124	OUT	627.50	904.76		OUT
Pup Jt # 2	9 5/8" CSG 53.5#, 110SS, HSM-3	327	3.860	3897.12	OUT	627.50	904.764		OUT

6.4 7" Liner

7" Liner Report

Casing Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012		N
RIG	208	WSS	A.Seifii / P.Bakhshi		192,581		E
DATE	1403.12.04	HOLE DEPTH	4,180 m MD	MUD WT.	103	PCF	
HOLE SIZE	8-3/8" inches		4,180 m TVD	MUD TYPE	Poly Mud		

	DEPTH metres	O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS
PREVIOUS CASING	3895.0	9-5/8"	53.5	110SS	HSM-3	

CSG STRING COMPOSITION

Qty.	O.D. in	I.D. in	ITEM DESCRIPTION / MANUFACTURER	Wt. lb/ft	GRADE	CONNECTION	Make Up Torque	LENGTH m
1	7	6.004	7" REAMER F.SHOE (35#,110SS, TPCQ) PPA	35	110SS	TPCQ	14340-15770	0.570
2	7	6.004	7" LNR, 35 #, TP110S, TPCQ THD	35	110SS	TPCQ	14340-15770	24.740
1	7	6.004	7" F.Collar (35#, 110SS, TPCQ) PPA	35	110SS	TPCQ	14340-15770	0.280
1	7	6.004	7" LNR, 35 #, TP110S, TPCQ THD	35	110SS	TPCQ	14340-15770	12.662
1	7	6.004	7" LDC (35#, 110SS, TPCQ) PPA	35	110SS	TPCQ	14340-15770	0.280
28	7	6.004	7" LNR, 35 #, TP110S, TPCQ THD	35	110SS	TPCQ	14340-15770	350.504
1	7		7"Rotational Hyd HGR assembly (PPA)	35	110SS	TPCQ	14340-15770	5.07

FINAL SHOE DEPTH	4180.00 m	CSG WEIGHT IN AIR		45.2	klbs
TOTAL LENGTH OF CSG. RUN	394.106 m	CSG WEIGHT IN MUD		35.7	klbs

PERFORMANCE	DATE/TIME
STARTED RUNNING CSG	22-Feb-2025, 03:30
FINISHED RUNNING CSG	23-Feb-2025, 24:00
TOTAL TIME (hours)	44.5
DOWNTIME (hours)	-

REASON(S) FOR DOWNTIME:

CASING RUNNING COMPANY: OEOC

CENTRALIZER / SCRATCHER PLACEMENT

MANUFACTURER	
TYPE	9-5/8" X 7" Bow Centralizer 9-5/8" X 7" Rigid Centralizer
PLACEMENT	Install as per liner Tally.

COMMENTS:

R/U 7" liner running equipment. M/U 7" Reamer F.shoe, RIH 2 Jts 7" liner (35#, TP110SS, TPCQ), M/U 7" F.Collar, RIH 1 Jt 7" liner (35#, TP110SS, TPCQ), M/U 7" LDC and cont. RIH 27 Jts 7" liner (35#, TP110SS, TPCQ), P/U & M/U 7" Rot. Hyd. Liner hanger assembly to 4180m, tag btm while pass drift thru all drill pipes, Establish circ. Record WT up & downward. Set liner hanger position (0.5m off btm). Dropped ball and circ. Till ball seat in LDC. Set hanger. Shear LDC by applly 2700psi with rig pump. turn string 27 rounds clockwise and released setting tools. check string WT, confirmed set liner hanger. M/U cement manifold (loaded dart), prepare & make cmt solution & spacer (chemical wash) meanwhile circ. mud thru string as 1.5 cap of string, L/U cmt line & press. test same w/ 3000psi, OK, pump 15bbl chemical wash as spacer, pump cmt slurry (S.V: 52bbl, S.W: 118pcf), release dart & disp. cmt slurry w/ totally 253bbl drlg fluid 103pcf, obs shearing (213bbl & 3000psi) & bumping (253bbl & 2700psi), during cementing & disp. same obs 3bbl loss), disconnected cmt line, pull out dog sub from PBR & slack off 40kips weight on the lap of tie-back to set top PKR (obs shock string on weight indicator). POOH with liner hanger setting tools to 3552m (8std & the first 3std. wet), flush the string cont. POOH to 3322m, CBU, cont. POOH to surf. L/D liner hanger setting tools.

7” Liner Tally

7" LNR Tally

Field:	SOUTH AZADEGAN	**Well NO:**	SAZN-207	**Rig NO:**	OEOC 208	**Drlg CO:**	MSA		
Client:	PETRO PARS	**Job:**	7" Liner			**Date:**	10-Dec-25		

Grade	ID "	Drift "	Weight lb/ft	Burst psi	Collaspse psi	Yield klbs	Coupling OD in	TQ ft x lb	Nominal Dia. OD
T110S	6.004	5.879	35	13,690	13,020	1,119	7.717	14340-15770	7

Total Depth :	4180.0 m	**Formation Name:**	Fahliyan	**Hook Weight :**	58 k lb
Shoe Depth :	4179.50	**Formation Top:**	3969 mt	**STRG CAP (bbl):**	261
LDC :	4141.47	**Rig Floor to Spool:**		**Mud Weight (pcf) :**	103
L.LNR	3788. 89	**0. LAP:**	109.11		

Number on jt	Grade	Order No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	STRG CAP. (bbl)	Remarks	
								Centralizers	IN / OUT
					4,180.000	58.000	0.000		
Float Shoe	7" REAMER F.SHOE (35#,110SS, TPCQ) PPA	-	0.570	0.570	4179.43	58.052	0.065		
1	7" LNR, 35 #, TP110S, TPCQ THD	1	12.258	12.828	4167.172	59.175	1.474	Bow Centeralizer	
2	7" LNR, 35 #, TP110S, TPCQ THD	2	12.482	25.310	4154.69	60.319	2.908	Bow Centeralizer	
FLOAT COLLAR	7" F.Collar (35#, 110SS, TPCQ) PPA	-	0.280	25.590	4154.41	60.356	2.940		
3	7" LNR, 35 #, TP110S, TPCQ THD	3	12.662	38.252	4141.748	61.517	4.395	Bow Centeralizer	
LDC	7" LDC (35#, 110SS, TPCQ) PPA	-	0.280	38.532	4141.468	61.554	4.427		
4	7" LNR, 35 #, TP110S, TPCQ THD	4	12.508	51.040	4128.96	62.700	5.864	Bow Centeralizer	
5	7" LNR, 35 #, TP110S, TPCQ THD	5	12.667	63.707	4116.293	63.861	7.320		
6	7" LNR, 35 #, TP110S, TPCQ THD	6	12.660	76.367	4103.633	65.021	8.774		
7	7" LNR, 35 #, TP110S, TPCQ THD	7	12.464	88.831	4091.169	66.163	10.206		
8	7" LNR, 35 #, TP110S, TPCQ THD	8	12.629	101.460	4078.54	67.320	11.657	Bow Centeralizer	
9	7" LNR, 35 #, TP110S, TPCQ THD	9	12.388	113.848	4066.152	68.455	13.081		
10	7" LNR, 35 #, TP110S, TPCQ THD	10	12.660	126.508	4053.492	69.615	14.535		
11	7" LNR, 35 #, TP110S, TPCQ THD	11	12.659	139.167	4040.833	70.775	15.990		
12	7" LNR, 35 #, TP110S, TPCQ THD	12	12.278	151.445	4028.555	71.901	17.400	Bow Centeralizer	
13	7" LNR, 35 #, TP110S, TPCQ THD	13	12.558	164.003	4015.997	73.051	18.843		
14	7" LNR, 35 #, TP110S, TPCQ THD	14	12.668	176.671	4003.329	74.212	20.299		
15	7" LNR, 35 #, TP110S, TPCQ THD	15	12.305	188.976	3991.024	75.340	21.713		
16	7" LNR, 35 #, TP110S, TPCQ THD	16	12.404	201.380	3978.62	76.477	23.138	Bow Centeralizer	
17	7" LNR, 35 #, TP110S, TPCQ THD	17	12.353	213.733	3966.267	77.609	24.557		
18	7" LNR, 35 #, TP110S, TPCQ THD	18	12.657	226.390	3953.61	78.768	26.011		
19	7" LNR, 35 #, TP110S, TPCQ THD	19	12.661	239.051	3940.949	79.928	27.466		
20	7" LNR, 35 #, TP110S, TPCQ THD	20	12.505	251.556	3928.444	81.074	28.903	Bow Centeralizer	
21	7" LNR, 35 #, TP110S, TPCQ THD	21	12.381	263.937	3916.063	82.209	30.325		
22	7" LNR, 35 #, TP110S, TPCQ THD	22	12.507	276.444	3903.556	83.355	31.762		
23	7" LNR, 35 #, TP110S, TPCQ THD	23	12.247	288.691	3891.309	84.478	33.169		
24	7" LNR, 35 #, TP110S, TPCQ THD	24	12.647	301.338	3878.662	85.636	34.622	Rigid Centralizers	
25	7" LNR, 35 #, TP110S, TPCQ THD	25	12.316	313.654	3866.346	86.765	36.037	Rigid Centralizers	
26	7" LNR, 35 #, TP110S, TPCQ THD	26	12.737	326.391	3853.609	87.932	37.501		
27	7" LNR, 35 #, TP110S, TPCQ THD	27	12.201	338.592	3841.408	89.050	38.903		
28	7" LNR, 35 #, TP110S, TPCQ THD	28	12.657	351.249	3828.751	90.210	40.357	Rigid Centralizers	
29	7" LNR, 35 #, TP110S, TPCQ THD	29	12.465	363.714	3816.286	91.352	41.789		
30	7" LNR, 35 #, TP110S, TPCQ THD	30	12.657	376.371	3803.629	92.512	43.243		
31	7" LNR, 35 #, TP110S, TPCQ THD	31	12.665	389.036	3790.964	93.672	44.699	Rigid Centralizers	
32	7" LNR, 35 #, TP110S, TPCQ THD	32	12.104	389.036	OUT	93.672	44.699		OUT
33	7" LNR, 35 #, TP110S, TPCQ THD	33	12.653	389.036	OUT	93.672	44.699		OUT
34	7" LNR, 35 #, TP110S, TPCQ THD	34	12.662	389.036	OUT	93.672	44.699		OUT
35	7" LNR, 35 #, TP110S, TPCQ THD	35	12.391	389.036	OUT	93.672	44.699		OUT
36	7" LNR, 35 #, TP110S, TPCQ THD	36	12.651	389.036	OUT	93.672	44.699		OUT
37	7" LNR, 35 #, TP110S, TPCQ THD	37	12.343	389.036	OUT	93.672	44.699		OUT
38	7" LNR, 35 #, TP110S, TPCQ THD	38	12.436	389.036	OUT	93.672	44.699		OUT
39	7" LNR, 35 #, TP110S, TPCQ THD	39	12.653	389.036	OUT	93.672	44.699		OUT
40	7" LNR, 35 #, TP110S, TPCQ THD	40	13.280	389.036	OUT	93.672	44.699		OUT
41	7" LNR, 35 #, TP110S, TPCQ THD	41	12.383	389.036	OUT	93.672	44.699		OUT
42	7" LNR, 35 #, TP110S, TPCQ THD	42	12.419	389.036	OUT	93.672	44.699		OUT
43	7" LNR, 35 #, TP110S, TPCQ THD	43	12.402	389.036	OUT	93.672	44.699		OUT
44	7" LNR, 35 #, TP110S, TPCQ THD	44	12.452	389.036	OUT	93.672	44.699		OUT
45	7" LNR, 35 #, TP110S, TPCQ THD	45	12.665	389.036	OUT	93.672	44.699		OUT
46	7" LNR, 35 #, TP110S, TPCQ THD	46	12.657	389.036	OUT	93.672	44.699		OUT
47	7" LNR, 35 #, TP110S, TPCQ THD	47	12.294	389.036	OUT	93.672	44.699		OUT
48	7" LNR, 35 #, TP110S, TPCQ THD	48	12.496	389.036	OUT	93.672	44.699		OUT
Rotational Hyd HGR	7" Rotational Hyd HGR (PPA)	-	1.800	390.836	3789.164	93.836	44.905		
POB	7" Pack off bushing (PPA)	-	0.400	391.236	3788.764	93.872	44.951		
LG & Top packer	7" LG & Top packer (PPA)	-	0.750	391.986	3788.014	93.940	45.037		
Tie back (PBR)	7" Tie back sleeve (PPA)	-	2.120	394.106	3785.894	94.132	45.281		
ools neck	setting tools neck	-	3.370	397.476	3782.524	94.323	45.472		
5" DP STD	132STD	-	3,780.350	4,177.826	2.174	311.528	260.615		
5" Pup joint DP	5" Pup joint DP	-	4.600	4,182.426	-2.426	311.706	260.877		

7. Cement Reports

7.1 20” Casing Cement Report

Cement Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012	N	
RIG	208	WSS	Gh.Kadivar / A.Eyvazi		192,581	E	
DATE	1403.07.28	HOLE DEPTH	3,891 m MD	MUD WT.	70	PCF	
HOLE SIZE	26" inches		3,889 m TVD	MUD TYPE	Bent. Mud		
CEMENTING CONTRACTOR	SPAD Energy Co.						

TYPE OF CEMENT JOB (casing, liner, squeeze, plug etc)	CASING	LINER INFORMATION				
		SHOE DEPTH:	149.00 m	HANGER:		m
PLUGS		DEPTH m	O.D. in	I.D. in	WEIGHT lb/ft	GRADE
CEMENT PLACEMENT TOP	m	149	20"	19.125"	94	K-55
BOTTOM	m					
CEMENT PLACEMENT TOP	m					
BOTTOM	m					

PREVIOUS CASING	DEPTH m	O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS

Cement Job	VOL bbl	WT. pcf	Cement Sx.	RECIPE	Additive
Spacer	50	62.4		FRESH WATER	-
First Stage					
Cement Slurry	210	118	868	CLASS "G" DELIJAN, CaCl2, AntiFoam	868 SXS CMT CLASS "G" DELIJAN, 1300 LB CaCl2, 40 GAL ANTI-FOAM AGENT
Total Pumped	210				

Operational Comments / Time Breakdown

OPERATION	TIME / DATE
L/U CMT LINE & TEST IT	17:00-17:30/1403.07.28
PUMP SPACER	17:00-17:30/1403.07.28
PUMP CMT	17:30-18:20/1403.07.28
DISPLACMENT	18:20-18:30/1403.07.28

REASON(S) FOR DOWNTIME:

LACEMENT

RATE bbl/min	VOL bbl	PRESS psi	MP (Yes/No, N/A) Top	Int.	Bttm	FINAL PRESS psi
4-5	210	100-200				

DOWNTIME hrs

BACKFLOW (Yes/No): No

POST JOB INFORMATION					
CEMENT TAGGED @	m	CEMENT EXPECTED @	m		
CEMENT DRILLED @	m/hr	TIME SINCE PLACEMENT	hrs		

COMMENTS:

L/U CMT line to string, press test to 3000psi, OK. Pump 50bbl fresh water as spacer. Mix and pump 868 sxs CMT "G" Delijan (S.V: 210bbl, S.W: 118pcf). After pumping 180bbl got contaminated CMT on surface. Totally dump 20bbl contaminated and 10bbl net slurry. Displace CMT w/ 6bbl fresh water (2bbl short). Check for back flow; Negative. Sting out f/ float shoe.

7.2 13-3/8" Casing Cement Report

Cement Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012	N	
RIG	208	WSS	A.Moradi / P.Bakhshi		192,581	E	
DATE	1403.07.28	HOLE DEPTH	1,648 m MD	MUD WT.	85	PCF	
HOLE SIZE	17-1/2" inches		1,648 m TVD	MUD TYPE	KCl Poly Mud		
CEMENTING CONTRACTOR	SPAD Energy Co.						

TYPE OF CEMENT JOB (casing, liner, squeeze, plug etc)	CASING	LINER INFORMATION				
		SHOE DEPTH:	1648.00 m	HANGER:		m
PLUGS		DEPTH m	O.D. in	I.D. in	WEIGHT lb/ft	GRADE
CEMENT PLACEMENT TOP	1623 m	1648	13-3/8"	12.415"	68	N-80
CEMENT PLACEMENT BOTTOM	1624 m					
CEMENT PLACEMENT TOP	m					
CEMENT PLACEMENT BOTTOM	m					

	DEPTH m		O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS
PREVIOUS CASING	149.0	20"	94	K-55	BTC		

Cement Job	VOL bbl	WT. pcf	Cement Sx.	Additive
Chemical Wash	20	62.4		796 Gal Fresh Water, 100 Gal Chemical Wash, 4 Gal Anti-Foam
Spacer	130	95.0		4550 Gal Fresh Water, 1300 Gal Chemical Spacer, 16250 sxs NaCl, 13 Gal Anti-Foam, 260 Gal Surfactant, 31850 sxs Barite
First Stage				
Lead Cement Slurry	1202	94	2760	17365.18 lb Micro Silica, 868.26 lb Retarder, 868.26 lb Dispersant, 130 Gal Liquid Friction Reducer, 130 Gal Anti Foam.
Tail Cement Slurry	135.5	118	563.42	155.36 lb Retarder, 15.55 Gal Liquid Friction Reducer, 23.30 Gal Anti Foam.
Total Pumped	1337.5			

Operational Comments / Time Breakdown

OPERATION	TIME / DATE	REASON(S) FOR DOWNTIME:
L/U CMT LINE & TEST IT	18:00-23:00/1403.08.20	
PUMP CHEMICAL WASH & SPACER	23:00-24:00/1403.08.20	
PUMP CMT & DISPLACMENT	00:00-07:30/1403.08.21	

DOWNTIME	hrs	BACKFLOW (Yes/No):	No

POST JOB INFORMATION					
CEMENT TAGGED @	m	CEMENT EXPECTED @	m
CEMENT DRILLED @	m/hr	TIME SINCE PLACEMENT	hrs

COMMENTS:

L/up cmt line on csg strg & established circ. While P/up strg weight by spider elevator & L/D side door slips . Perform press test cmt line with 500/1500psi for 10 min; OK.
Mix and pump 20 bbl Ch. Wash w/ pump truck. Pump 100 bbl Spacer w/ rig pump, 1-2 BPH Loss.
PUMP 1202 BBL CMT SLURRY (94PCF, "G" DELIJAN, 2780 SXS) AS LEAD CMT, PUMP 135.5 BBL CMT SLURRY (118 PCF, "G" DELIJAN, 555 SXS) AS TAIL CMT, DROP TOP PLUG, DISPLACE CMT W/ 795 BBL MUD (85PCF), OBS BUMPING & PERFORM CIT W/ 1500PSI FOR 15MIN "OK".

7.3 9-5/8" Casing Cement Report

Cement Report

General Data

FIELD	AZNS	**WELL NO.**	207	**LOCATION**	3,441,012	**N**	
RIG	208	**WSS**	A.Moradi / A.Eyvazi		192,581	**E**	
DATE	1403.11.22	**HOLE DEPTH**	3,895 m MD	**MUD WT.**	80	PCF	
HOLE SIZE	12-1/4" inches		3,895 m TVD	**MUD TYPE**	KCl Poly Mud		
CEMENTING CONTRACTOR	SPAD Energy Co.						

TYPE OF CEMENT JOB (casing, liner, squeeze, plug etc)	CASING	**/ LINER INFORMATION**				
		SHOE DEPTH:	1648.00 m	**HANGER:**		m

PLUGS				**DEPTH m**	**O.D. in**	**I.D. in**	**IGHT lb/ft**	**GRADE**
CEMENT PLACEMENT	**TOP**	3870	m	3895	9-5/8"	8.535"	53 1/2	110SS
	BOTTOM	3870	m					
CEMENT PLACEMENT	**TOP**		m					
	BOTTOM		m					

	DEPTH m		**O.D.** in	**WEIGHT** lb/ft	**GRADE**	**CONNECTION TYPE**	**COMMENTS**
PREVIOUS CASING	1648.0	13-3/8"	68	N-80	BTC		

Cement Job	**VOL** bbl	**WT.** pcf	**Cement** Sx.	**Additive**
Chemical Wash	40	62.4		1742 Gal Fresh Water, 200 Gal Chemical Wash, 8 Gal Anti-Foam
Spacer	60	90.0		3150 Gal Fresh Water, 900 Gal Chemical Spacer, 11250 lb NaCl, 9 Gal Anti-Foam, 180 Gal Surfactant, 16650 lb Barite
First Stage				
Lead Cement Slurry	1108	95	2600	14223.49 lb Micro Silica, 1706.82 lb Retarder, 1137.88 lb FLC, 284.47 gal Dispersant, 85.34 Gal Anti Foam.
Tail Cement Slurry	116	118	371.00	13611.87 lb Silica Flour, 271.30 lb Retarder, 217.04 lb FLC, 108.52 lb Micro Silica, 54.26 gal Dispersant, 108.52 gal Anti-Gas, 16.28 Gal Anti Foam.
Total Pumped	1224			

Operational Comments / Time Breakdown

OPERATION	**TIME / DATE**	**REASON(S) FOR DOWNTIME:**
L/U CMT LINE & TEST IT	12:00-19:00/1403.11.22	
PUMP CHEMICAL WASH & SPACER	19:00-19:30/1403.11.22	
PUMP CMT	19:30-00:00/1403.11.22	
DISPLACMENT	00:00-01:00/1403.11.23	

DOWNTIME	hrs	**BACKFLOW (Yes/No):**	No

POST JOB INFORMATION					
CEMENT TAGGED @		m	CEMENT EXPECTED @		m
CEMENT DRILLED @		m/hr	TIME SINCE PLACEMENT		hrs

COMMENTS:

Cont. Run 9-5/8" CSG (53.5#, 110SS, HSM-3) f/ 3440 to 3700 m meanwhile F/U string & Break Circ. Every 10 Jts. Wash Dn w/ 9-5/8" CSG string f/ 3700 to 3895 m. (Totally: 327 Jts) Tag BTM w/ 10 Klb Wt; 5-2 BPHL; Install Centralizer as per tally. Meanwhile prepare 1000 bbl CMT Solution & Transfer to CMT solution tanks. Slow circulate mud Thru CSG string meanwhile R/D CSG handling equpment. while prepare CMT spacer.
R/U 9-5/8" CMT head, Plug already loaded. L/U CMT head. Held PJSM. L/U CMT line to CMT head, Press test CMT line to 500/3000 psi; OK. Pump 40 bbl 62.4 pcf Chemical wash, 60 bbl 90 pcf Spacer ahead. Mix & Pump 2600 sxs CMT G Delijan (SV: 1108 bbl, SW: 95pcf) as lead slurry, Mix & Pump 371 sxs CMT G Delijan blended w/ 36.66 lb/sxs Silica Flour (SV: 116 bbl, SW: 118 pcf) as tail slurry; 2-3 BPHL, Drop top plug. Displace w/ totally 903 bbl 80 pcf mud; Observe bumping w/ 2000psi (80% Burst Press). Check back flow; OK. Got 230 bbl Contaminated CMT (80-90 pcf) & 170 bbl Green CMT slurry (95 pcf) on return & Totally 30 bbl losses during displace.

7" Liner Cement Report

Cement Report

General Data

FIELD	AZNS	WELL NO.	207	LOCATION	3,441,012	N	
RIG	208	WSS	A.Seifi / P.Bakhshi		192,581	E	
DATE	1403.12.05	HOLE DEPTH	4,180 m MD	MUD WT.	103	PCF	
HOLE SIZE	8-3/8" inches		4,180 m TVD	MUD TYPE	Poly Mud		
CEMENTING CONTRACTOR	SPAD Energy Co.						

TYPE OF CEMENT JOB (casing, liner, squeeze, plug etc)	Liner	CASING / LINER INFORMATION					
		SHOE DEPTH:	4180.00 m	HANGER:	3786 m		
PLUGS		DEPTH m	O.D. in	I.D. in	WEIGHT lb/ft	GRADE	
CEMENT PLACEMENT TOP	3870 m	4180	7.000	6004.000	35	110SS	
CEMENT PLACEMENT BOTTOM	3870 m						
CEMENT PLACEMENT TOP	m						
CEMENT PLACEMENT BOTTOM	m						

	DEPTH m	O.D. in	WEIGHT lb/ft	GRADE	CONNECTION TYPE	COMMENTS
PREVIOUS CASING	3895.0	9 5/8	53.5	110SS	HSM-3	

Cement Job	VOL bbl	WT. pcf	Cement Sx.	Additive
Chemical Wash	15	62.4		552 Gal Fresh Water, 75 Gal Chemical Wash, 3 Gal Anti-Foam
Spacer				
First Stage				
Lead Cement Slurry	51.89	118	800	134.39 lb Micro Silica, 134.39 lb Retarder, 33.60 lb FLC, 26.88 gal Dispersant, 67.20 Gal Anti Gas Migration, 10.08 Gal Anti Foam.
Total Pumped	51.89			

Operational Comments / Time Breakdown

OPERATION	TIME / DATE	REASON(S) FOR DOWNTIME:
L/U CMT LINE & TEST IT	06:30-07:30/1403.12.05	
PUMP CHEMICAL WASH	07:30-08:00/1403.12.05	
PUMP CMT	08:00-09:00/1403.12.05	
DISPLACMENT	09:00-10:30/1403.12.05	

DOWNTIME	hrs	BACKFLOW (Yes/No):	No

POST JOB INFORMATION					
CEMENT TAGGED @	3650	m	CEMENT EXPECTED @		m
CEMENT DRILLED @	4-7	m/hr	TIME SINCE PLACEMENT		hrs

COMMENTS:

Establish circ. Record WT up & downward. Set liner hanger position (0.5m off btm). Dropped ball and circ. Till ball seat in LDC. Set hanger. Shear LDC by applly 2700psi with rig pump. turn string 27 rounds clockwise and released setting tools. check string WT, confirmed set liner hanger. M/U cement manifold (loaded dart), prepare & make cmt solution & spacer (chemical wash) meanwhile circ. mud thru string as 1.5 cap of string, L/U cmt line & press. test same w/ 3000psi, OK, pump 15bbl chemical wash as spacer, pump cmt slurry (S.V: 52bbl, S.W: 118pcf), release dart & disp. cmt slurry w/ totally 253bbl drlg fluid 103pcf, obs shearing (213bbl & 3000psi) & bumping (253bbl & 2700psi), during cementing & disp. same obs 3bbl loss), disconnected cmt line, pull out dog sub from PBR & slack off 40kips weight on the lap of tie-back to set top PKR (obs shock string on weight indicator). POOH with liner hanger setting tools to 3552m (8std & the first 3std. wet), flush the string cont. POOH to 3322m, CBU, cont. POOH to surf. L/D liner hanger setting tools.

8. Completion Report

8.1 Tubing Information

Tubing Size(in)	Weight (ppf)	Grade	Ultimate Strengths	Connection	Collapse Pressure (psi)	Burst Pressure (psi)	Interval (m)
4-1/2	18.9	L-80	233 klb	HSM3	13830	13380	0 – 3732.15
3-1/2	10.2	L-80	440 klbs	HSM3	12120	11560	3732.15 – 3879.27

Table 8-1: AZNS-207 Completion Tubing Information

8.2 Completion Tools Specification Checklist

Item	Equipment Description	
1	**CONTROL LINE "WEIQIXIN":**	
	THINKNESS:	0.065"
	WORK PRESSURE:	15000 PSI
	O.D.:	0.25"
	TYPE:	SEAMLESS
	MATERIAL:	INC 825
	LENGTH:	120m/Roll
2	**UPPER FLOW COUPLING " WEIQIXIN" :**	
	OD:	**5.5"**
	ID:	3.640"
	THREADS:	4-1/2" 18.9 PPF, HSM3
	WORKING PRESSURE:	10000 PSI
	LENGTH:	6 FT
	MATERIAL:	13CR-110KSI
	LOWER FLOW COUPLING " WEIQIXIN" :	
	OD:	5.550"
	ID:	3.640"
	THREADS:	4-1/2" 18.9 PPF, HSM3
	WORKING PRESSURE:	10000 PSI
	LENGTH:	4 FT
	MATERIAL:	13CR-110KSI
3	**TUBING RETRIEVABL SAFETY VALVE " WEIQIXIN" :**	
	SETTING DEPTH:	62.40m
	WORKING PRESSURE:	10000 PSI

Item	Equipment Description	
	TEMPERATURE:	325 DEG F
	MAX O.D.:	7.5"
	MIN. I.D.:	3.437"
	PROFILE:	AF
	SELF-EQUALIZING FEATURE	HYDRAULIC CONTROL
	MATERIAL:	13CR-110KSI
	THREADS:	4-1/2" 18.9 PPF HSM3
	PROTECTION SLEEVE	
	PROFILE	AF
	MIN ID	2.9"
4	**TRAVELING JOINT " WEIQIXIN" :**	
	STROKE LENGTH	10 FT
	SHEAR PIN SET:	15000LB
	ELASTOMER:	AFLAS
	WORKING PRESSURE:	10000 psi
	TEMPERATURE:	300 DEG F
	TOOL OD:	5.315"
	TOOL ID:	2.922"
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	13CR-110KSI
	TRANSFER TORQUE FEATURE	YES
5	**SLIDING SIDE DOOR " WEIQIXIN" :**	
	PROFILE:	X
	MAX.OD:	4.551"
	MIN ID:	2.750"
	PRESSURE RATING:	10000 PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	13CR-110KSI
	OPEN METHOD	DOWNWARD OPEN
6	**COMPLETION PACKER " WEIQIXIN" :**	
	TYPE:	PERMANENT
	CASING :	7" 32 PPF
	OD:	5.689"
	ID:	2.922"
	WORKING PRESSURE:	10000 PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	MATERIAL:	13CR-110KSI
	ELEMENT MATERIAL:	AFLAS
	4.0" ANCHOR SEAL	
	MAX OD (PACKING):	4"
	ID:	2.922"

Item	Equipment Description	
	WORKING PRESSURE:	10000PSI
	TEMPERATURE:	300 DEG F
	THREADS:	3-1/2" 10.20 PPF HSM3 B
	TYPE:	RATCH LATCH
7	**LANDING NIPPLE " WEIQIXIN" :**	
	PROFILE TYPE:	R
	WORKING PRESSURE:	10000 PSI
	MAX O.D.:	4.5"
	SEAL BORE:	2.562”
	MIN ID:	2.441"
	THREADS:	3-1/2" 10.20 PPF HSM3 B*P
	TEMPERATURE:	300 DEG F
	MATERIAL:	13CR-110KSI
8	**RE-ENTRY GUIDE SHOE " WEIQIXIN" :**	
	OD:	4.5"
	MIN ID:	2.922"
	TOP CONNECTION	3-1/2" 10.20 PPF HSM3 BOX
	MATERIAL:	13CR-110KSI
9	**3-1/2" CHEMICAL INJECTION" WEIQIXIN" :**	
	TYPE	TUBING RETRIVABLE
	MAX OD	5.00"
	MIN ID	2.922"
	MATERIAL:	13CR-110KSI
	TEMPERATURE	300 DEG F
	CONNECTION	3-1/2" 10.20 PPF HSM3 B*P
	CIV CONNECTION	NPT 3/8" BOX FOR CIV
	1.00"CIV VALVE	
	TYPE	DUAL CHECK VALVE WITH RUPTURE DISC
	WORKING PRESSURE	15000PSI
	MARERIAL	13CR-110KSI
	TEMPERATURE:	300 DEG F
	TOP CONNECTION	3/8" AUTOCLAVE
	BOTTOM CONNECTION	3/8" NPT
	RUPTURE DISC PRESSURE	6000PSI

Item	Name	Description
1	**Tubing Hanger**	11" BOWL x 4-1/2" 18.9 PPF BOX TPCQ-EX CONNECTION BOTTOM & 4-1/2" 4-2G ACME BOX TOP WITH 4-1/2" EXTENDED NECK, WITH ONE CONTINUOUS 1/4" NPT C.LINE EXIT FOR SSSV, ONE 1/4" LINE EXIT FOR DHPG, INSTALLATION COMPLETE WITH RELATED FITTINGS AND PLUGS, WITH TWO CHANNEL FOR 3/8" CHEMICAL, C/W ALIGNMENT PREPATION FOR ESP. BPV: 4" TYPE H THREAD PREPARATION, THREE FS SEAL TO PACK OFF THE UPPER NECK AND TWO S SEAL TO PACK OFF THE BODY OF HANGER, MATERIAL: 410SS. M.C: FF-0.5 T.C: U PSL:3G PR:2 COMPANY: MSP
2	**Fluted Adaptor**	4 1/2" 18.9 PPF, L-80 HSM3 PIN * TPCQ EX PIN, OD: 5.5'' ID: 3.64'' SLOTS: 6 * 1 INCH WIDTH


Table 8-2: AZNS-207 Tools Specification

8.3 Assembling Test Report

WEIQIXIN PETROLEUM MACHINERY(TIANJIN)CO.LTD

惟其信 WEIQIXIN


SCSSV Test Report




Type:	210W 343-AF04	
Serial Number:	08/24 24104-02	
Connection Size:	4-1/2" 18.90 PPF HSM3 BOX × PIN	
Working Pressure	10,000Psi	
OD:	7.500"	
ID:	3.437"	
Length:	1.785 m	
Material:	S13CR-110 KSI	
Hydraulic Control Pressure	Full Open	Full Closed
	1800 Psi	800 Psi
8,000 Psi Hydraulic Control Pressure No Drop in 15 Minutes	ok	
8,000 Psi Pressure No Drop in 15 Minutes	ok	
8,000 Psi flapper Pressure No Drop in 15 Minutes	ok	
Top Connection	Length:	1.620 m
Top Flow Coupling:	Serial Number:	08/24 Y240712-01
	Length:	1.725 m
Bottom Flow Coupling:	Serial Number:	09/24 Y240713-01
	Length:	1.116 m
Bottom Connection:	Length:	1.621 m
Well Name and Location:	AZNS-207	
MSA Project Manager: Name/Title: Date:		
WQX: Name/Title: Date: 2025.3.15		

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:

Figure 8-1: AZNS-207 TRSSSV Test Report

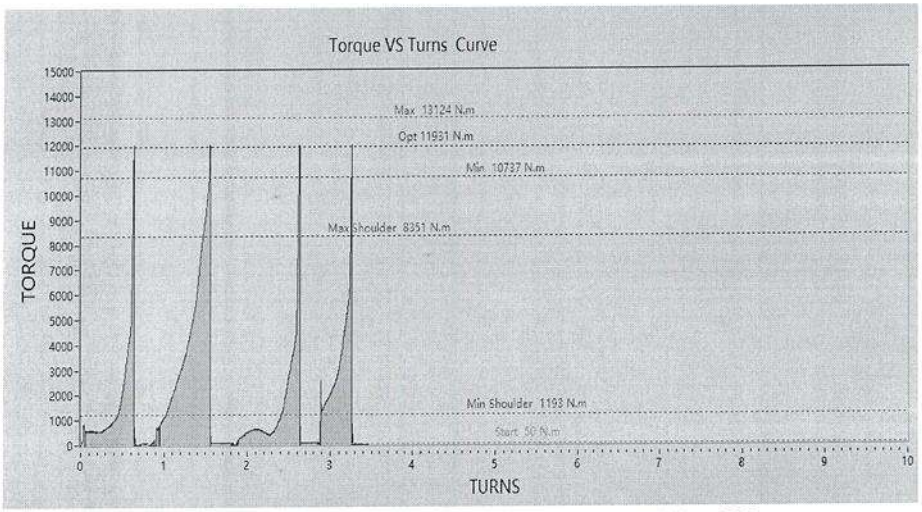

Top pup joint – top flow coupling – 3SV, Bottom flow coupling – bottom pup joint – 3SV

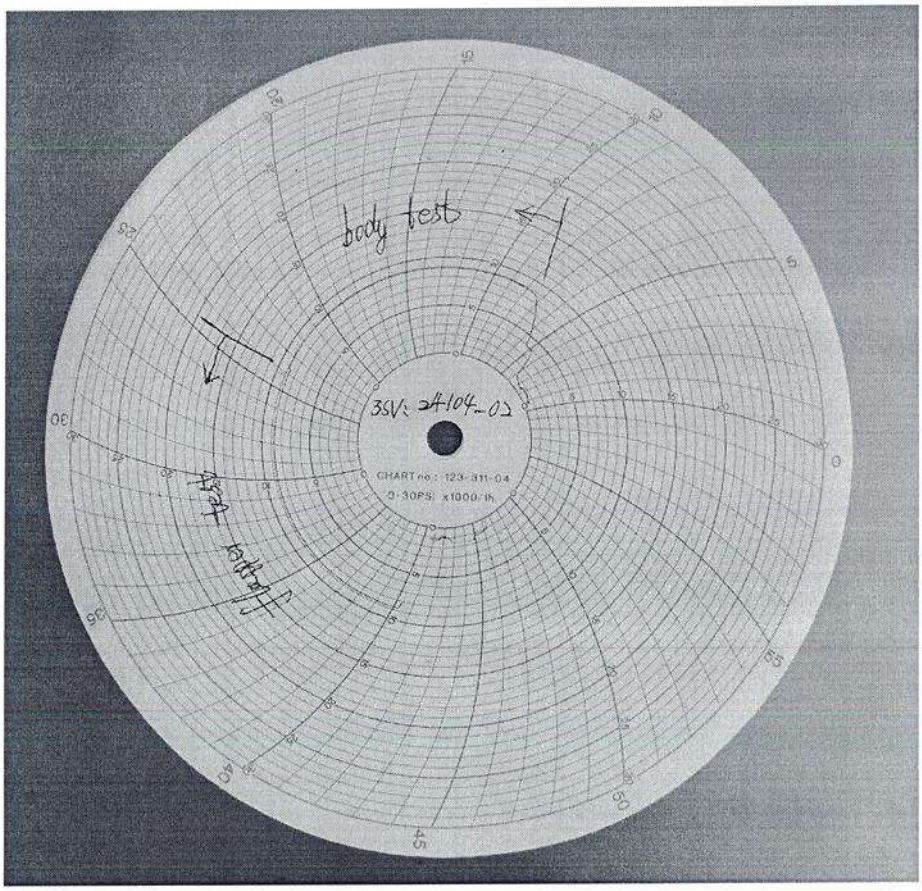


Pressure test curve

Figure 8-2: AZNS-207 TRSSSV Connections Graph

WEIQIXIN PETROLEUM MACHINERY(TIANJIN)CO.LTD

WSDP Hydraulic Set Permanent Packer Test Report

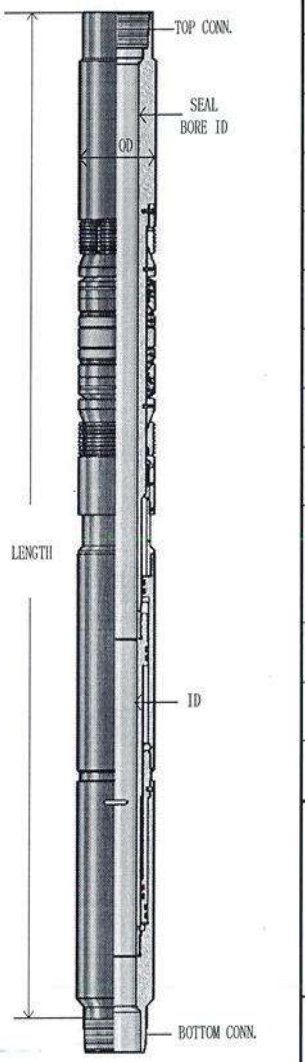

Type:	336W144-002	
Serial Number:	08/24 24139-01	
Connection Size:	LEFT HAND X 3-1/2" 10.20 PPF HSM3 PIN	
Working Pressure	10,000 Psi	
OD:	5.689"	
ID:	2.922"	
Length:	4.571m	
Material:	S13CR-110KSI	
Temperature:	300 DEG F	
Element :	Aflas	
Setting Pressure:	3,500 Psi	
Seal Bore Size:	Upper Seal Bore ID:4.00" & Lower Seal Bore ID:2.922"	
Top Connection:	Length:	1.916 m
Bottom Connection:	Length:	2.036 m
Well Name and Location:	AZNS-207	

MSA Project Manager:
Name/Title:
Date:

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:


WQX:
Name/Title:
Date: 2015.3.15

Figure 8-3: AZNS-207 Permanent Packer Test Report

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

惟其信 WEIQIXIN

Model WK Anchor Tubing Seal Report

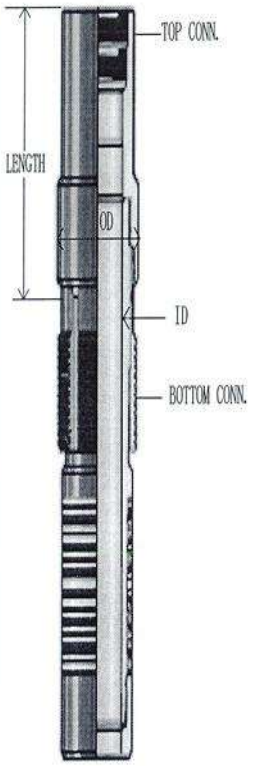


Type:	360W150-000
Serial Number:	08/24 24112-01
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX X MULE SHOE GUIDE
OD:	5.689"
ID:	2.922"
Seal OD:	4.000"
Working pressure:	10,000Psi
Length:	240 mm
Material:	S13CR-110 KSI
Well Name and Location	AZNS-207

MSA Project Manager:
Name/Title:
Date:

WQX:
Name/Title:
Date: 2025.3.15

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:

Figure 8-4: AZNS-207 Anchor Seal Test Report

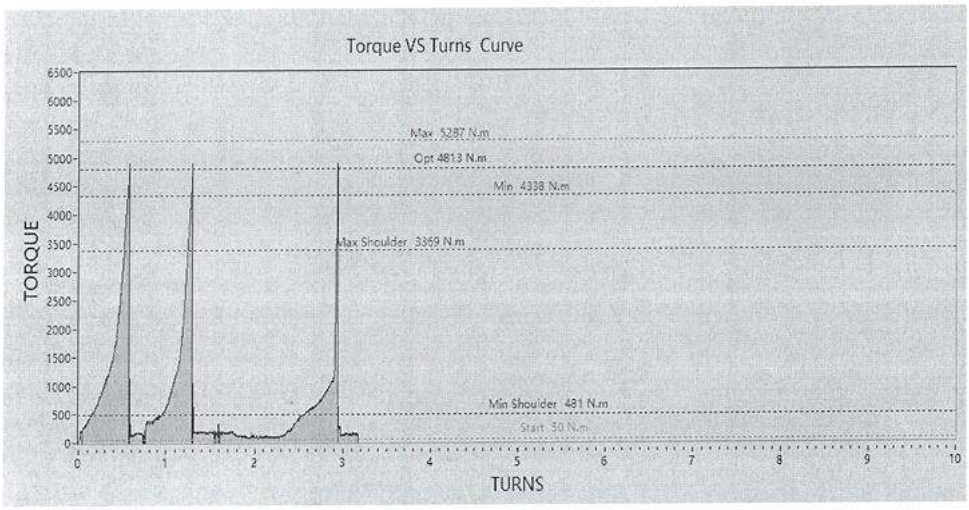

Top pup joint – anchor seal, bottom joint – coupling – Packer


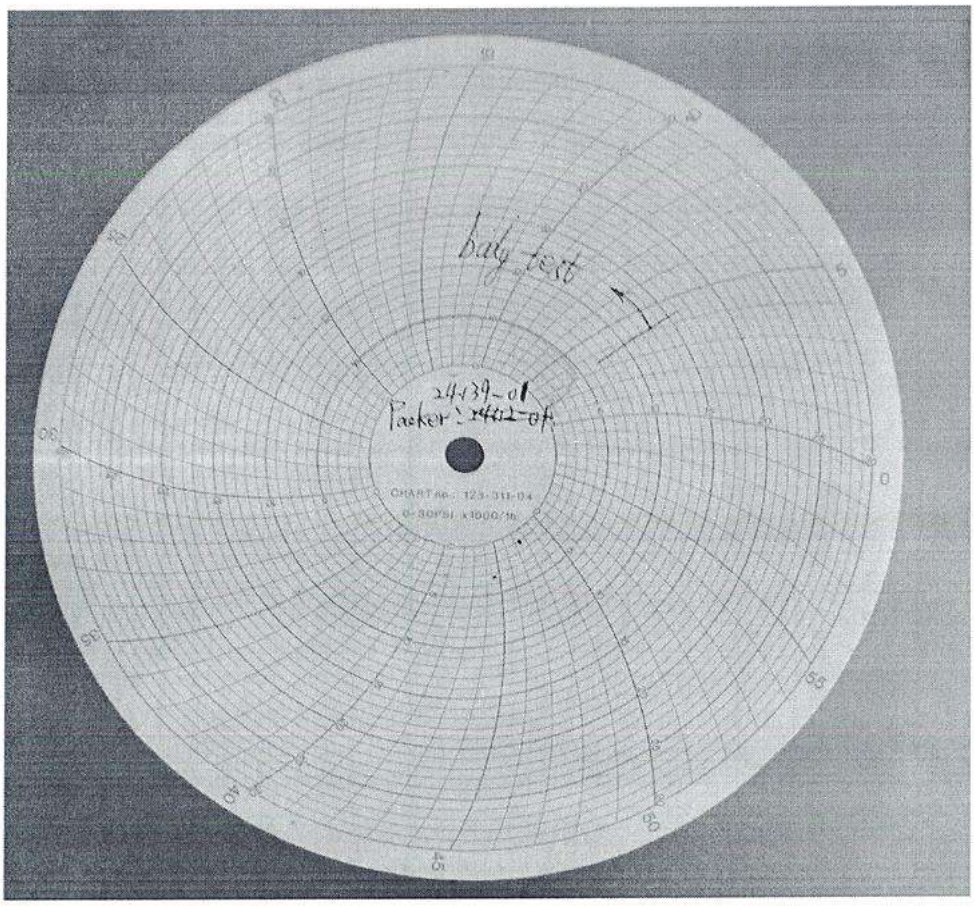


Figure 8-5: AZNS-207 Permanent Packer Connections Graph

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

惟其信 WEIQIXIN

Sliding Side Door Test Report

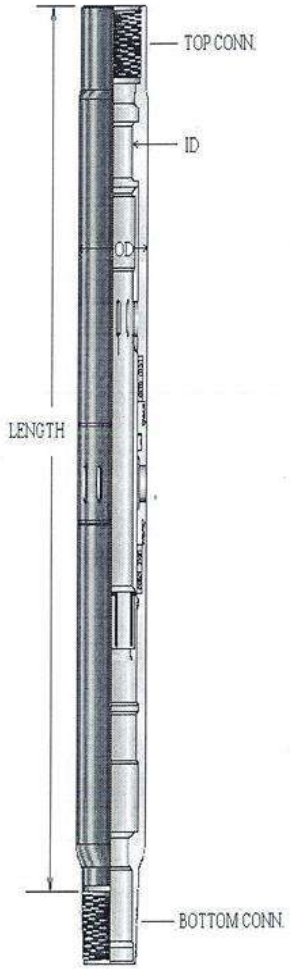

Type:	750W275-X39	
Serial Number:	08/24 24141-02	
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX × PIN	
Working Pressure	10,000 Psi	
OD:	4.551"	
ID:	2.750"	
Seal Bore ID :	2.750"	
Length:	1.196 m	
Temperature	300 DEG F	
Material:	S13CR-110KSI	
Profile:	X	
Shifting Direction:	DOWNWARD OPEN	
Top Connection:	Length:	2.023 m
Bottom Connection:	Length:	2.015 m
8,000 Psi Pressure No Drop in 15 Minutes	Ok	
8,000 Psi blanking plug Pressure No Drop in 15 Minutes	Ok	
Well Name and Location:	AZNS-207	


ماهان صنعت آزیا

MSA Project Manager:
Name/Title:
Date:

Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:

WQX:
Name/Title:
Date: 2015, 3, 15

Figure 8-6: AZNS-207 SSD Test Report

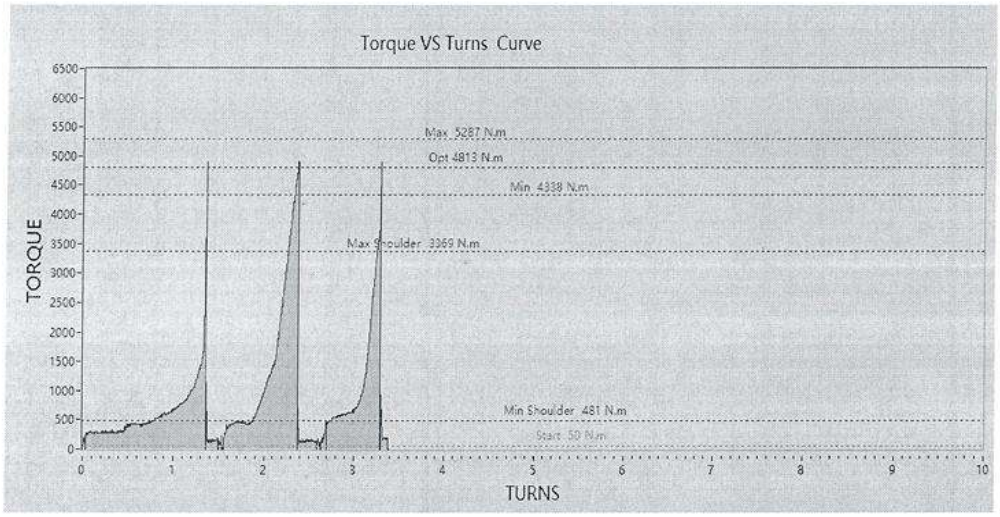

Top pup joint – SSD, Bottom joint – coupling – SSD


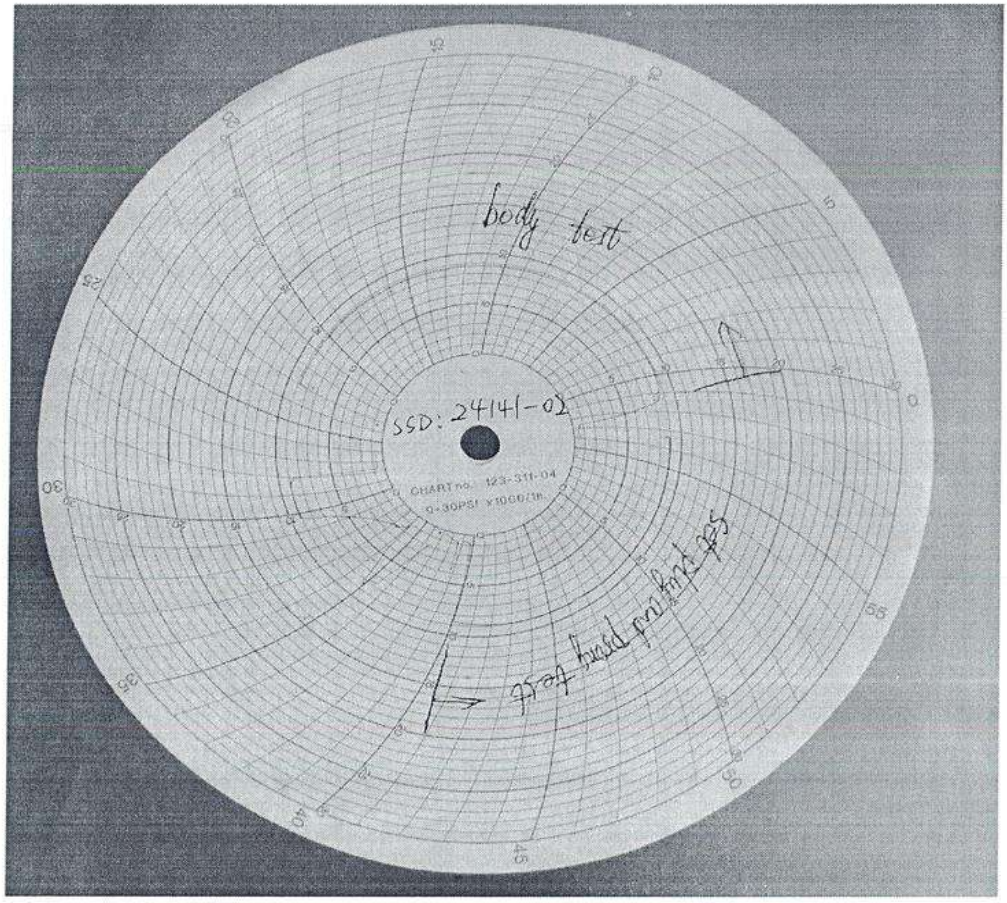


Figure 8-7: AZNS-207 SSD Connection & Pressure Test Graph

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

惟其信 WEIQIXIN

Expansion Joint Test Report

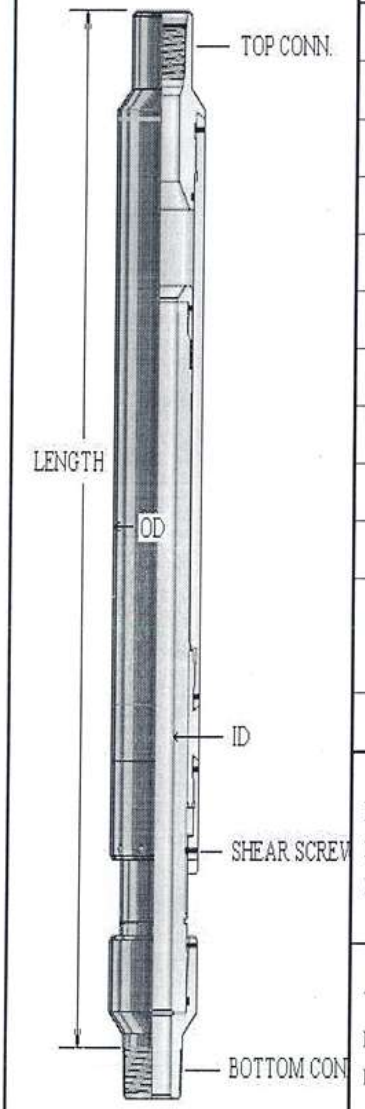


Type:	370W350-030	
Serial Number:	09/24 24107-02	
Connection Size:	3-1/2" 10.20 PPF HSM3 BOX× PIN	
Working Pressure	10,000 Psi	
OD:	5.315"	
ID:	2.922"	
Length:	7.308 m	
Material	S13CR-110KSI	
Share Screw:	3	
Top Connection:	Length:	2.002 m
Bottom Connection:	Length:	2.025 m
8,000 Psi Pressure No Drop in 15 Minutes	ok	
Well Name and Location:	AZNS-207	

MSA Project Manager:
Name/Title:
Date:

Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:

WQX:
Name/Title:
Date: 2015. 3. 15

Figure 8-8: AZNS-207 Expansion Joint Test Report

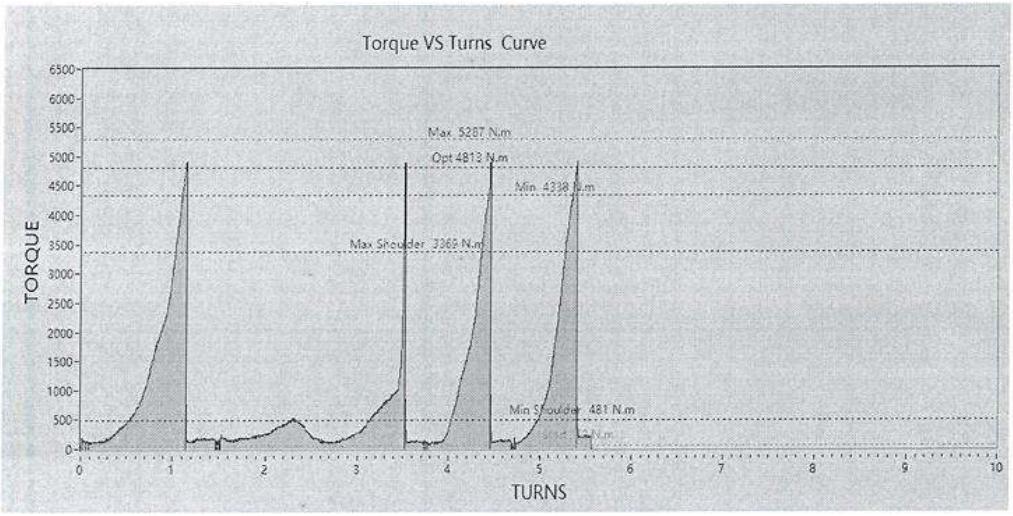

Top joint – coupling – EX.J, Bottom joint – coupling – EX.J


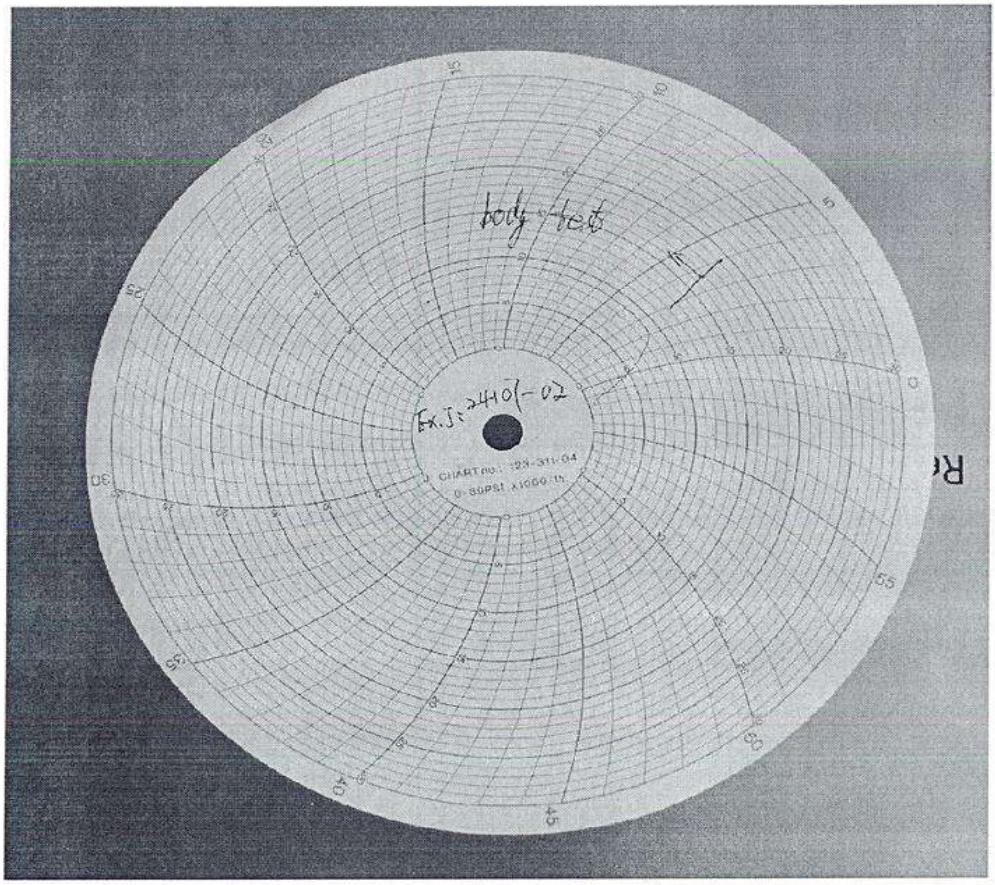


Figure 8-9: AZNS-207 Expansion Joint Connection & Pressure Test Graph

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

维其信 WEIQIXIN

Landing Nipple Test Report

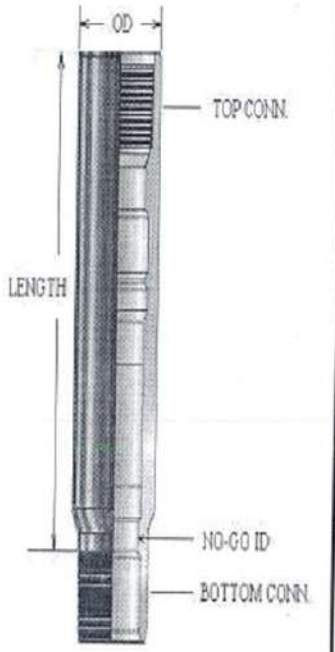


Type:	706W256-N18	
Serial Number:	08/24 Y240714-01	
Connection Size:	3-1/2"10.22 PPF HSM3 BOX × PIN	
OD:	4.500"	
ID:	2.562" R Profile	
NO-GO ID:	2.442"	
Length:	0.393 m	
Material:	S13CR-110 KSI	
Top Connection:	Length:	1.912 m
8,000 Psi blanking plug Pressure No Drop in 15 Minutes	Ok	
Well Name and Location: هاهان صنعت آریا AZNS-207		

Drilling Supervisor
MSA Project Manager:
South Azadegan Project
Name/Title:
Date:
Rig No:
EPDS CONTRACTOR Date:

WQX:
Name/Title:
Date: 2025.8.15

Figure 8-10: AZNS-207 Landing Nipple Test Report

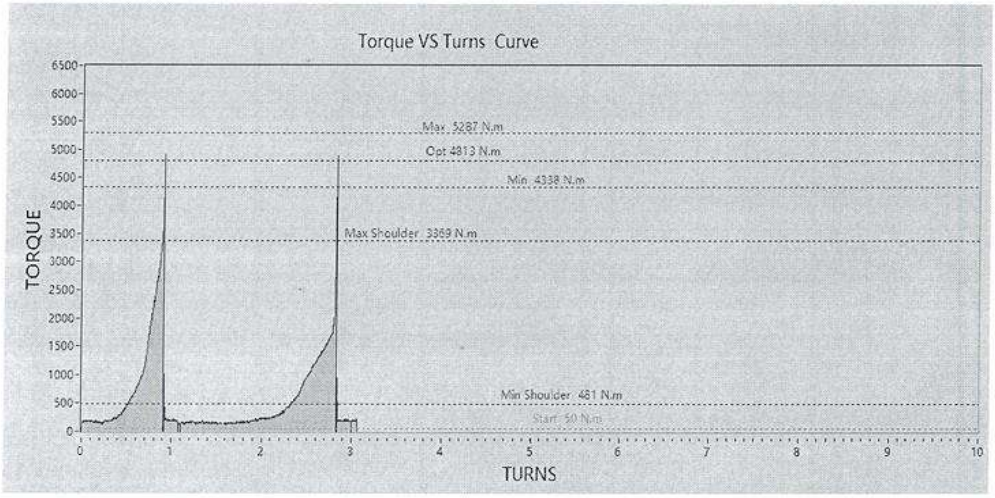

Top pup joint – L.N – Mule shoe

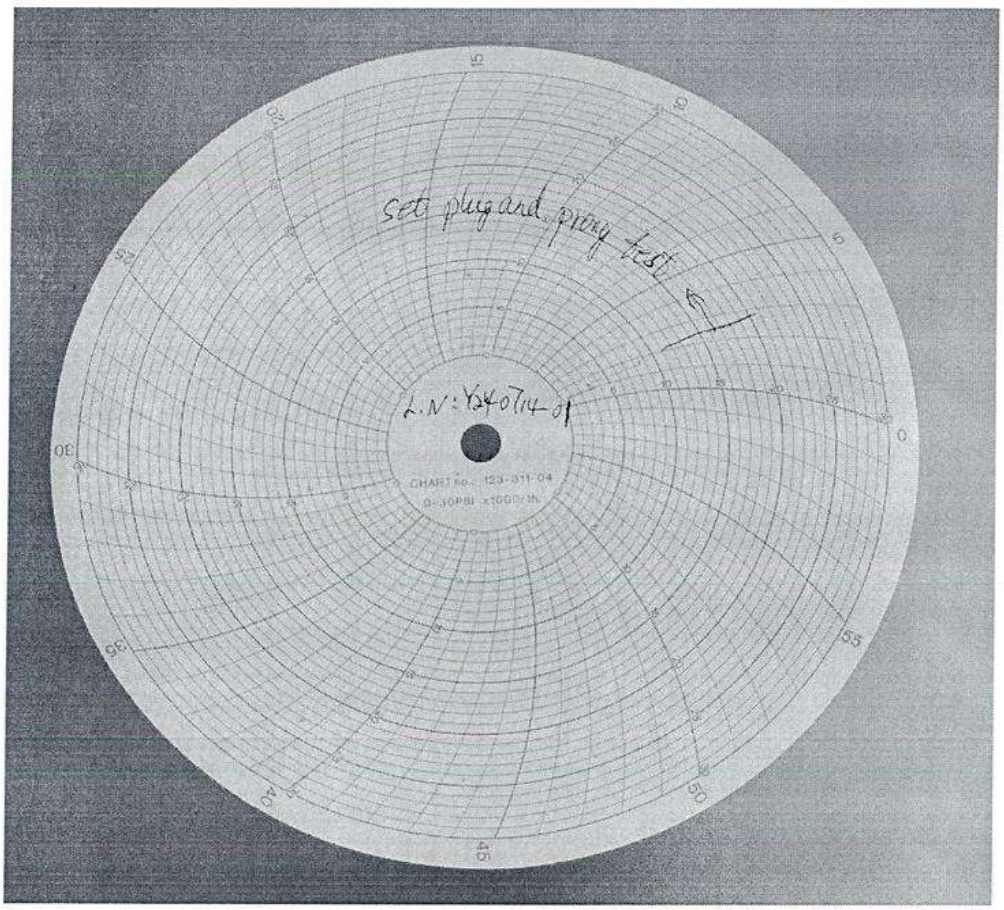


Figure 8-11: AZNS-207 Landing Nipple Connection & Pressure Test Graph

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

惟其信 WEIQIXIN

Chemical Injection Valve Test Report



Type:	802W100-601
Serial Number:	09/24 24129-02
Connection Size:	3/8" JAM NUT BOX x 3/8" NPT PIN
OD:	1"
ID:	0.299"
Rupture DISK:	6000Psi
Spring open pressure:	500Psi
Length:	310mm
Material:	S13CR-110 KSI
8,000 Psi Pressure No Drop in 15 Minutes	Ok
Well Name and location	AZNS-207

ماهان صنعت آریا

MSA Project Manager:
Name/Title:
Date:


Drilling Supervisor
South Azadegan Project
Rig No: -
EPDS CONTRACTOR Date:

WQX:
Name/Title:
Date: 2025.3.15

Figure 8-12: AZNS-207 First CIV Test Report

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

Chemical Injection Mandrel Test Report




Type:	800W350-028	
Serial Number:	09/24 Y240720-02	
Connection Size:	3-1/2" 10.2PPF HSM3 BOX × PIN	
OD:	5.000"	
ID:	2.922"	
Working pressure:	15,000Psi	
Temperature:	300 DEG F	
Length:	0.728 m	
Top Connection:	Length:	1.910 m
Bottom Connection:	Length:	1.906 m
Material:	S13CR-110KSI	
8,000 Psi Pressure No Drop in 15 Minutes	Ok	
Well Name and Location	ماهان صنعت آریا AZNS-207	

MSA Project Manager:
Name/Title: Drilling Supervisor
Date: South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:

WQX:
Name/Title:
Date: 2015.3.15

Figure 8-13: AZNS-207 First CIM Test Report

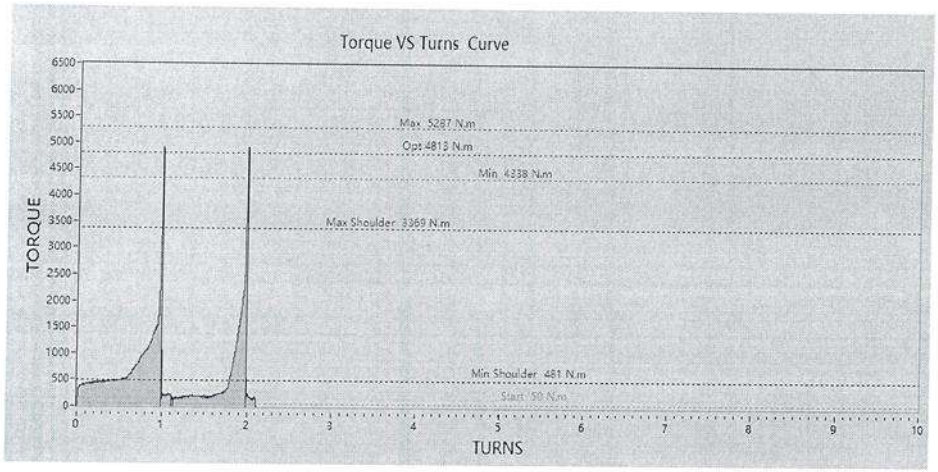

Top pup joint – CIM – bottom pup joint

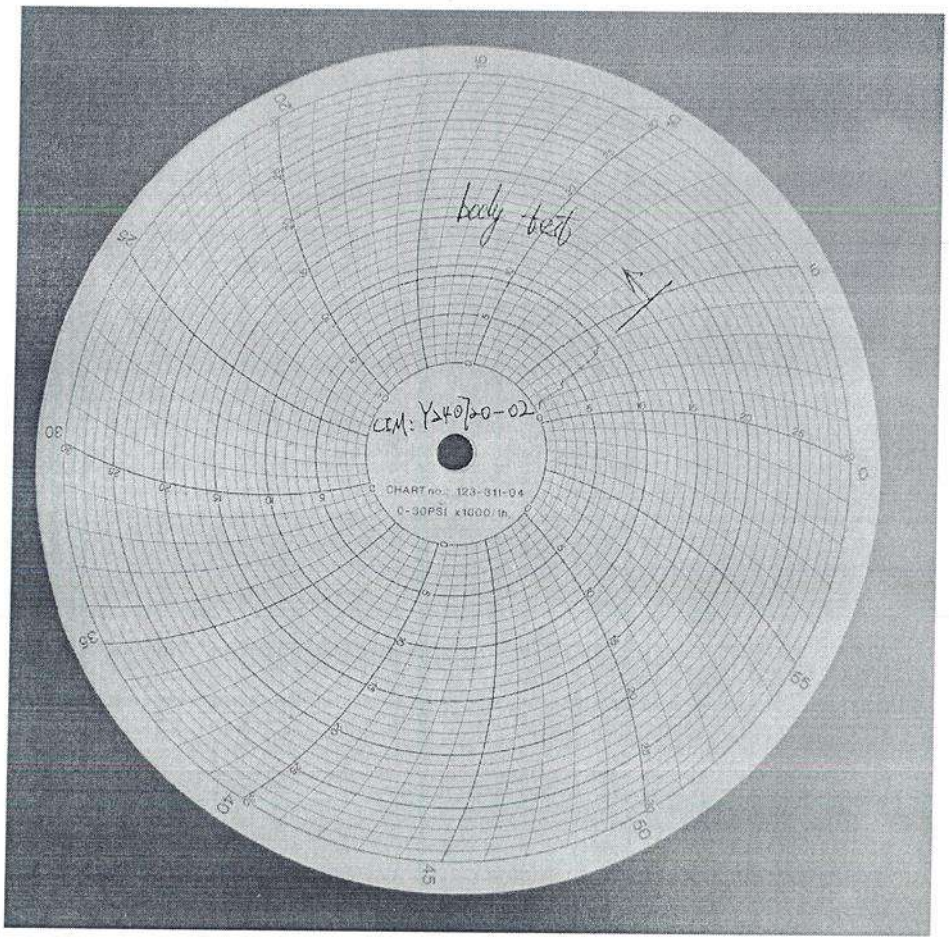


Figure 8-14: AZNS-207 First CIM Connection & Pressure Test Graph

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD

惟其信 WEIQIXIN

Chemical Injection Valve Test Report



Type:	802W100-601
Serial Number:	09/24 24129-04
Connection Size:	3/8" JAM NUT BOX x 3/8" NPT PIN
OD:	1"
ID:	0.299"
Rupture DISK:	6000Psi
Spring open pressure:	500Psi
Length:	310mm
Material:	S13CR-110 KSI
8,000 Psi Pressure No Drop in 15 Minutes	Ok
Well Name and Location	AZNS-207

MSA Project Manager:
Name/Title:
Date:

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No:
MSA
DRDS CONTRACTOR Date:


WEQX:
Name/Title:
Date: 2015.3.15

Figure 8-15: AZNS-207 Second CIV Test Report

WEIQIXIN PETROLEUM MACHINERY(TIANJIN) CO.LTD


惟其信 WEIQIXIN

Chemical Injection Mandrel Test Report



Type:	800W350-028	
Serial Number:	09/24 Y240720-04	
Connection Size:	3-1/2" 10.2PPF HSM3 BOX × PIN	
OD:	5.000"	
ID:	2.922"	
Working pressure:	15,000Psi	
Temperature:	300 DEG F	
Length:	0.728 m	
Top Connection:	Length:	1.962 m
Bottom Connection:	Length:	1.914 m
Material:	S13CR-110KSI	
8,000 Psi Pressure No Drop in 15 Minutes	Ok	
Well Name and Location:		AZNS-207
MSA Project Manager: Name/Title: Date:	ماهان صنعت آریا Drilling Supervisor South Azadegan Project Rig No: EPDS CONTRACTOR Date:	
WQX: Name/Title: Date:	2014.3.15	

Figure 8-16: AZNS-207 Second CIM Test Report

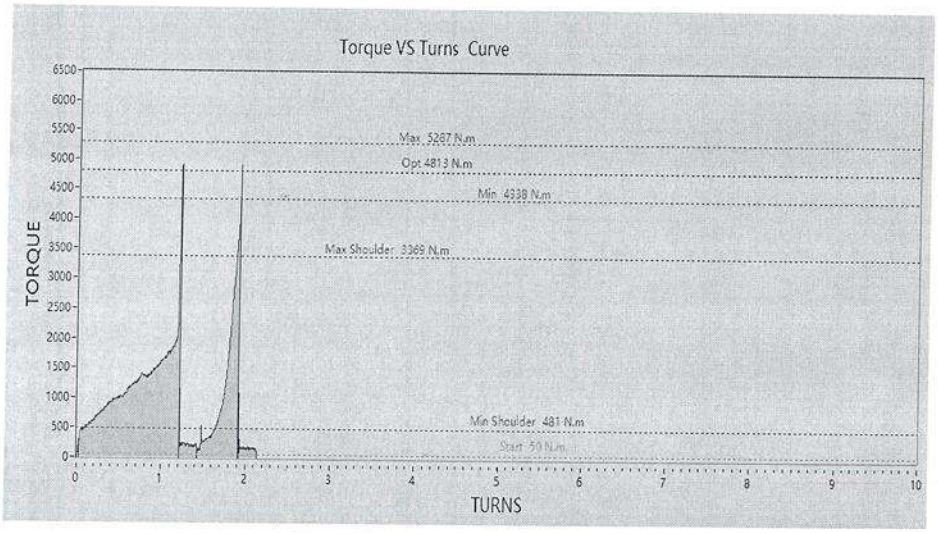

Top pup joint – CIM – bottom pup joint

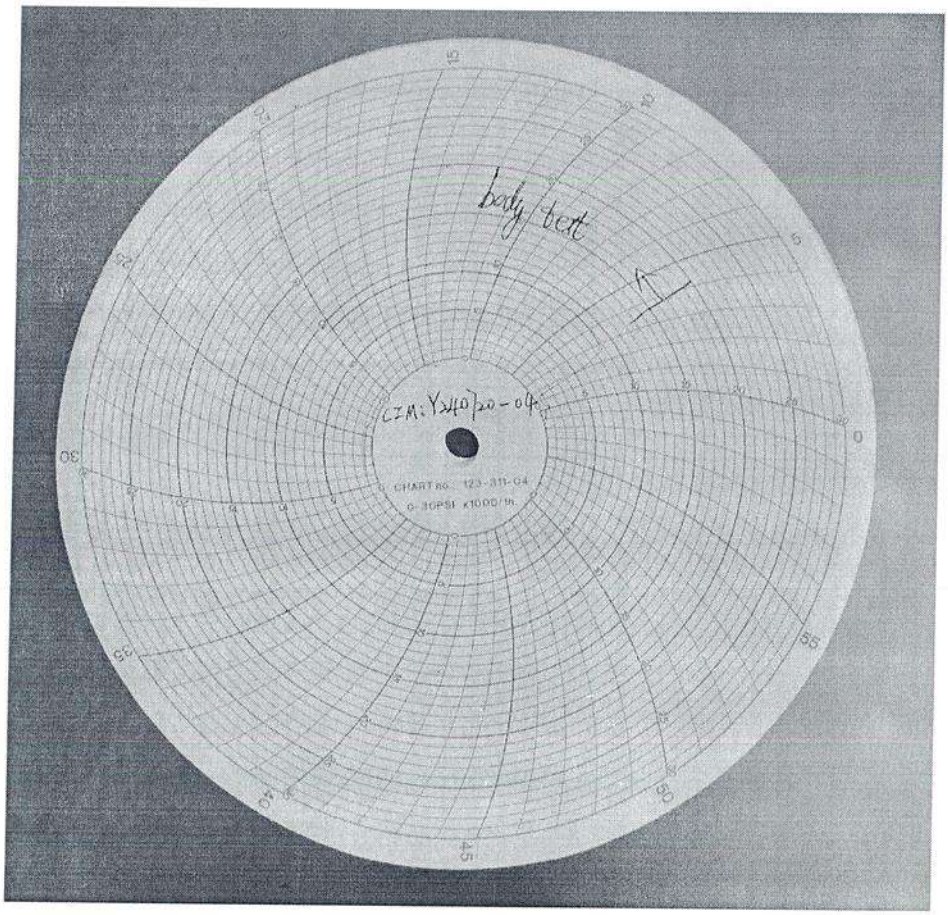


Figure 8-17: AZNS-207 Second CIM Connection & Pressure Test Graph

8.4 Completion Operation Checklist

Item	Operation Name	Remark	Check Mark✓
1	Scraper Trip	Packer depth should be scraped	√
2	Pre-job preparation	Pre-connection All Down Hole Equipment With Upper & Lower Pup Joints On Confirmed Thread-makeup at Workshop, And Pressure Test Prior To Being Transported To Well Site.	√
		Retrieve Wear Bushing, M/U Jet Sub And Flush Bop Stack & Well Head With Fresh Water.	√
		All Crossovers, Pup Joints For Space Out Measured Put In Right Place.	√
		Lift Control Line And Protectors On Rig Floor.	√
		Hold A Pre-Job Safety Meeting For Running Upper Completion String.	√
3	Assembling and RIH	M/U 3-1/2" Re-entry Guide Shoe And 3-1/2" BTM No Go Landing Nipple	√
		Check The Conditions Landing Nipple To Make Sure There Is No Damage, Observe There Is No Any Trash Trapped Inside.	√
		Assemble Landing Nipple.	√
		RIH 1 Joint Tubing As Per Tally	√
		P/U And M/U Hydraulic-Set PERMANENT Production Packer.	√
		Much More Care Should Be Taken When Packer Is Passing Well Head And Liner Hanger While RIH,	√
		Assemble Ratch Latch If Packer	-
		Slack Off Packer Assembly, Double Check The Quantity Of Shear Pins,	√

		Remove The Tape On The Element, Check If Any Damages On It.	
		RIH 1 Joint Tubing As Per Tally	√
		M/U Pup Joint And SSD (close Position) To Tubing String With check valve Inside.	√
		Pressure Test Tubing String 7000psi/15min Every 50 JTs.	√
		RIH Completion String and M/U traveling joint as per running tally.	√
		M/U 2 NO. CIV as per running tally& Press Test to 2000 Psi.	-
		Cont. Running Tubing as per Tally while Install Cross protector for the 2 NO. 3/8”control line.	-
		M/U TRSSSV	√
		Install control line to TRSSSV and pressure test control line 8000psi x 15mins. And then keep 5000psi pressure while running to ensure TRSSSV open. Install TRSSSV protector for the 1/4” control line. Continue to run 4-1/2” tubing as per running tally.	√
4	M/U and Space out Tubing Hanger	Pick up & M/U tubing hanger with double pin crossover. M/U landing joint. Check string weight upward and downward.	√
		Roughly cut control line about 2 meters above tubing hanger, wrap 2-3 turns and then feed through Tubing Hanger.	√
		Check string weight upward and downward and Space out Tubing Hanger 1.5 m (Half stroke) above tubing head spool	√

Item	Operation Name	Remark	Check Mark✓
5	Set production	R/Up Slick Line. Remove Check valve inside SSD	√
		RIH and Set check vlve in Landing Nipple. POOH to surface.	√

	packer	Pressurize inside tubing to 500psi to ensure traveling joint is full open. Increase Pressure gradually to SET PACKER. Increase pressure to 7000 Psi to Test String.	√
6	Land Tubing hanger	Move down completion string and apply required weight to shear traveling joint load pins and Land Tubing hanger in T.H.S. Slack off completely & Record the weight.	√
		Drain the BOP stack through the gate valves of tubing head before landing hanger in THS. Leave the valves open.	√
		Tie Down Screws on THS should be fully open before Operation	√
7	N/D BOP & N/U X-mas tree	Tighten tie down screws.	√
		Test inside string w/ 5000 psi, 15 min.	√
		R/Up Slick Line. RIH with slick line and Ret. Check valve from Landing Nipple. POOH to surface.	√
		Test Annulus w/ 2000 Psi 15min.	√
		Close BOP ram and test above tubing hanger (annulus between BOP and landing joint) to 1000psi.	√
		B/O & L/D landing joint.	√
		Set 4” 2Way in TBG Hanger & Test it, Back off and L/D Running Tool.	√
		N/D BOP.	√
		Feed control line, through head bonnet.	√
		Check hanger for any damage and pressure test control line to 5000psi	√
		Pressure test chemical injection line & rapture the disc after installing	-

		Bonnet.	
		N/U x-mass tree as program.(Bottom Master)	√
		Perform required tests for X-mass tree. (Bottom Master)	√
		Connect from X-mass tree production valve to the pump unit & well test choke manifold with T-type connection & test all lines to 7500 Psi.	√
		Remove 4" two way, install 4" one way	√
		Close TRSSSV	√
		Release the rig. Clean the well site.	√

Table 8-3: AZNS-207 Operation Checklist

8.5 Well Head and X-mass tree Specification (installed)

Well Type	Specification	Check and Remark
Well Head 10000 Psi for Fahliyan Wells	**TUBING HEAD ADAPTOR** BOTTOM STUDDED FLANGE 11", 10000 PSI, BX158 TOP STUDDED FLANGE 4-1/16" 10000 PSI BX155 FULL BORE PREPARED WITH TWO S-SEAL AND ONE METAL TO METAL SEAL TO PACK TOP NECK OF TUBING HANGER C/W RELATED TEST AND INJECTION PORTS PREPARTION. C/W TWO CONTINUOUS FEED THROUGH TYPE 1/4" NPT CONTROL LINE EXITS PREPARTION (ONE FOR 1/4" TRSSSV CL AND ONE FOR 1/4" DOWNHOLE PRESSURE GAUGE) AND TWO 3/8" NPT CONTINUOUS FEED THROUGH TYPE LINE PORTS FOR CHEMCIAL INJECTION LINE EXIT INCLUDING RELATED SWAGE LOCK FITTINGS C/WITH ONE 4-1/16", 10K WP FULL BORE MANUAL GATE VALVE FORGED BODY AND BONNET, ALLOY STAINLESS STEEL 410SS GATE & SEAT AISI 410 COATED WITH TUNGSTEN CARBIDE USING HVOF METHOD STEM: INCONEL 718 WITH BACK SEAT CAPABILITY, NON RISING STEM METAL TO METAL SEAL BETWEEN SEAT AND GATE C/W HAND WHEEL FORGED BODY ALLOY STEEL AISI 410 MAXIMUM HEIGHT: 800MM M/C: FF-0.5 T/C: U PSL:3G PR:2 CROSS T-TYPE SOLID BLOCK CROSS T-TYPE SOLID BLOCK, BOTTOM FLANGED 4-1/16" API 10000 PSI WP TOP FLANGED STUDDED 4-1/16" API 10000 PSI WP FOR TREE CAP WITH TWO STUDDED SIDE OUTLETS 4-1/16" 10000PSI WP ELEVATED AT 900 DEG AND TWO 4-1/16", 10000 PSI MANUAL GATE VALVE AT THE TOP AND BOTTOM AND ONE 4-1/16", 10000 PSI WP SAFETY VALVE EQUIPPED WITH HYDRAULIC WIRE CUT ACTUATOR AS UPPER MASTER VALVE MATERIAL OF BODY, BONNET: AISI 410 SEAT, GATE: AISI 410SS HARD FACED WITH TUNGSTEN CARBIDE UASING HVOP METHOD MATERIAL OF STEM: INCONEL 718 M/C: FF-0.5 T/C: U PSL:3G PR:2G. MANUAL GATE VALVE API 4-1/16" 10000 PSI WP. FLANGED ENDS AND FULL BORE METAL TO METAL SEAL BETWEEN BODY/SEAT/GATE WITH BACK SEAT CAPABILITY, NON RISING STEM C/W HANDWHEELS MATERIAL OF BODY, BONNET, SEAT, GATE: AISI 410SS MATERIAL OF STEM: INCONEL 718 GATE&SEAT HARD FACED WITH TUNGSTEN CARBIDE BY HOVF METHOD M/C: FF-0.5 T/C: U PSL:3G PR:2 X-MAS TREE CAP 4-1/16" API 10000 PSI WP, FLANGED BOTTOM (4-1/16", BORE) 8-3/8"-4ACME-2G THREAD TOP, BLANKING PLUG TAPPED WITH 1/2" NPT THREAD, FORGED BODY, MATERIAL: STAINLESS STEEL 410 M/C:FF-0.5 T/C:U PSL:3G PR:2	

8.6 Completion Sketch

AZNS-207 Completion Sketch

Contractor	MSA / OEOC	Liner & Tubing Data					Client	PEDEC / PPL
Field	AZADEGAN	Description	7"Liner	3 1/2" Tubing	4 1/2" Tubing	Tubing		
Well Number:	AZNS-207	OD[in]	7.00	3.50	4.50		7'' Liner Lap:	3786
Rig :	208-OEOC	Nominal weight [lb/ft]	35.00	10.20	18.90		7'' Liner Shoe:	4179.5
RTE-GLE	14.45	Grade	TP110SS	L-80	L-80			
RTE-THF	11.33	Thread	TPCQ	HSM3	HSM3		Total Depth:	4180
Rig Spudded Date :		Inside diameter [in]	6.004	2.915	3.640		X-mass Tree:	MSP
End of Operation		API Drift Diameter	5.879	2.797	3.515		Size & Rating:	4-1/16" 10K


Schematic		Description	Max OD	Min ID	Length(m)	BTM(m)	TOP(m)
	1	Elevation (Floor - TBG Head Flange)			11.234	10.320	-0.914
		TBG HGR Running Tools			0.230	10.550	10.320
	2	TBG HANGER MSP, 10K, 11" * 4 1/2'' ACME Box up * 4 1/2'' TPCQ-EX Box Down , M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type ''H'' Two Way	5.118	3.64	0.560	11.110	10.550
	3	4-1/2" FLUTED SWAGE ADAPTER D/P, 18.9# TPCQ-EX PIN ON TOP X HSM3 PIN ON DOWN* SUPER 13CR-110KSI, WEIQIXIN Co	6.1	3.64	1.019	12.129	11.110
	4	5 JOINTs TUBING 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	46.931	59.060	12.129
	5	PUP JOINT 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	1.623	60.683	59.060
	6	4-1/2" FLOW COUPLING,18.9#,SUPER 13CR-110KSI,HSM3 , 6 FT, WEIQIXIN Co	5.5	3.64	1.725	62.408	60.683
	7	TRSSV-10 Tubing Retrievable Saftey Valve, 4 1/2", 18.9# W/ 3.437" Seal bore,HSM3 , SUPER 13CR-110KSI, 10K WP With AF Profile, Flapper Type, WEIQIXIN Co	7.5	3.437	1.785	64.193	62.408
	8	4-1/2" FLOW COUPLING, 18.9#,SUPER 13CR-110KSI,HSM3 , 4' FT, WEIQIXIN Co	5.5	3.64	1.117	65.310	64.193
	9	PUP JOINT 4 1/2",HSM3 ,18.9#, L-80, Type-1	5.118	3.64	1.623	66.933	65.310
	10	381 JOINTs TUBING 4-1/2"HSM3 18.9#, L-80	5.118	3.64	3665.223	3732.156	66.933
	11	X-over 4-1/2"HSM3, 18.9# BOX * 3-1/2"HSM3 , 10.2# PIN,	5.118	2.922	1.100	3733.256	3732.156
	12	7 JOINTs TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	64.646	3797.902	3733.256
	13	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.910	3799.812	3797.902
	14	3 1/2" CIV TUBING RETRIEVABLE CHEMICAL INJECTION MANDRELHSM3 , 10.2#,SUPER 13CR-110KSI W/CHECK VALVE, DUAL TYPE & RUPTURE DISC, WEIQIXIN Co	5	2.922	0.624	3800.436	3799.812
	15	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.880	3802.316	3800.436
	16	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.256	3811.572	3802.316
	17	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.960	3813.532	3811.572
	18	3 1/2" CIV TUBING RETRIEVABLE CHEMICAL INJECTION MANDRELHSM3 , 10.2#,SUPER 13CR-110KSI W/CHECK VALVE, DUAL TYPE & RUPTURE DISC, WEIQIXIN Co	5	2.922	0.724	3814.256	3813.532
	19	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.891	3816.147	3814.256
	20	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.172	3825.319	3816.147
	21	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	2.000	3827.319	3825.319
	22	3-1/2" EXP. JOINT,HSM3 , SUPER 13CR-110KSI, 10'STK (Half Open) Splind Rotational Lock System Any Position, Shear Pin Set 20,000 LBS, WEIQIXIN Co	5.135	2.922	5.760	3833.079	3827.319
	23	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	2.001	3835.080	3833.079
	24	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.247	3844.327	3835.080
	25	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	2.023	3846.350	3844.327
	26	3-1/2" NON-ELASTOMERIC SLIDING SIDE DOOR, SUPER 13CR-110KSI, HSM3 With Type X Selective Profile (PROFILE: 2.750" X, DOWNWARD OPEN), WEIQIXIN Co	4.551	2.75	1.198	3847.548	3846.350
	27	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.990	3849.538	3847.548
	28	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.229	3858.767	3849.538
	29	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.916	3860.683	3858.767
	30	3-1/2" ANCHOR SEAL ASSEMBLY,HSM3, 10.2#,SUPER 13CR-110KSI, 4" PACKING OD, WEIQIXIN Co	4/00	2.922	0.234	3860.917	3860.683
	31	7'' HYDRAULIC SET PERMANENT PRODUCTION PACKER, MODEL WSDP TO BE RUN IN 7.00" 29-35 PPF CASING, SUPER 13CR-110KSI, UPPER SEAL BORE: 4", WEIQIXIN Co	5//689	2.922	4.571	3865.488	3860.917
	33	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.250	2.922	2.012	3867.500	3865.488
	34	1 JOINT TUBING 3-1/2"HSM3 , 10.2#, L-80.Type-1	4.25	2.922	9.229	3876.729	3867.500
	35	3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	4.25	2.922	1.911	3878.640	3876.729
	36	13-1/2" BOTTOM NO-GO LANDING,HSM3 , 10.2#, SUPER 13CR-110KSI W/ Seal Bore 2.560" TYPE XN, WEIQIXIN Co	4.5	2.562	0.394	3879.034	3878.640
	37	3-1/2" WIRLINE RE-ENTRY GUIDE, 10.2 #,HSM3 Con,SUPER 13CR-110KSI, WEIQIXIN Co	4.25	2.922	0.241	3879.275	3879.034
		END OF COMPLETION STRING					3879.275

Figure 8-18: AZNS-207 Completion Sketch

8.7 Completion Tally

MSA / OEOC

Field :	Azadegan		Well NO:	AZNS207	Rig NO:	OEOC208	Drlg CO:		OEOC
PEDEC, PPL			Completion String						
Grade	ID "	Drift "	Weight lb/ft	Burst psi	Collaspse psi	Yield klbs	Coupling "	TQ ft x lb	Nominal Dia. OD
L-80	2.922	2.8	10.2	11,560.0	12,120.0	233	3.962	3200-3550-3900	3-1/2"
L-80	3.640	3.5	18.9	13,380.0	13,820.0	440	5.137	7920-8800-9680	4-1/2"
BTM NO GO Depth:	3878.64		Formation Name :		Fahliyan	Hook Weight :			58 k lb
BTM of String	3879.28		Formation Top :		3968	VOLUME (TOTAL)			161.65
Packer Depth :	3860.92					Mud Weight (pcf) :			104
Rig Floor to THS:	10.7								

Number on jt	Grade	Run In No.	Jt Length (m)	Cum Length (m)	Dist to RT (m)	M/D weight (Klbs)	VOL(BBL)	Remarks	
								joint no	IN / OUT
					3879.275	58.00			
3-1/2" WIRLINE RE-ENTRY GUIDE, 10.2 #,HSM3 Con,SUPER 13CR-110KSI, WEIQIXIN Co	3-1/2" Mule Shoe		0.241	0.24	3879.034	58.01	0.01		
13-1/2" BOTTOM NO-GO LANDING,HSM3 , 10.2#, SUPER 13CR-110KSI W/ Seal Bore 2.560" TYPE XN, WEIQIXIN Co	3-1/2" BTM NO GO		0.394	0.64	3878.640	58.02	0.02		
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.911	2.55	3876.729	58.07	0.07		
1	TUBING 3-1/2", 10.2#, L-80,HSM3	1	9.229	11.78	3867.500	58.31	0.32	1	
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		2.012	13.79	3865.488	58.36	0.38		
7" HYDRAULIC SET PERMANENT PRODUCTION PACKER, MODEL WSDP TO BE RUN IN 7.00" 29-35 PPF CASING, SUPER 13CR-110KSI, UPPER SEAL BORE: 4", WEIQIXIN Co	PKR		4.571	18.36	3860.917	58.48	0.50		
3-1/2" ANCHOR SEAL ASSEMBLY,HSM3, 10.2#,SUPER 13CR-110KSI, 4" PACKING OD, WEIQIXIN Co	Ratch Lach		0.234	18.59	3860.683	58.49	0.51		
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.916	20.51	3858.767	58.54	0.56		
2	TUBING 3-1/2", 10.2#, L-80,HSM3	2	9.229	29.74	3849.538	58.78	0.81	2	G.ring
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.990	31.73	3847.548	58.84	0.86		
3-1/2" NON-ELASTOMERIC SLIDING SIDE DOOR, SUPER 13CR-110KSI, HSM3 With Type X Selective Profile (PROFILE: 2.750" X, DOWNWARD OPEN), WEIQIXIN Co	SSD		1.198	32.93	3846.350	58.87	0.90		
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		2.023	34.95	3844.327	58.92	0.95		
3	TUBING 3-1/2", 10.2#, L-80,HSM3	3	9.247	44.20	3835.080	59.16	1.20	3	
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		2.001	46.20	3833.079	59.22	1.26		
3-1/2" EXP. JOINT,HSM3 , SUPER 13CR-110KSI, 10'STK (Half Open) Splind Rotational Lock System Any Position, Shear Pin Set 20,000 LBS, WEIQIXIN Co	Traveling Jt		5.760	51.96	3827.319	59.37	1.41		
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		2.000	53.96	3825.319	59.42	1.47		
4	TUBING 3-1/2", 10.2#, L-80,HSM3	4	9.172	63.13	3816.147	59.66	1.72	4	
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.891	65.02	3814.256	59.71	1.77		
3 1/2" CIV TUBING RETRIEVABLE CHEMICAL INJECTION MANDRELHSM3 , 10.2#,SUPER 13CR-110KSI W/CHECK VALVE, DUAL TYPE & RUPTURE DISC, WEIQIXIN Co	CIV		0.724	65.74	3813.532	59.73	1.79		
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.960	67.70	3811.572	59.78	1.84		
5	TUBING 3-1/2", 10.2#, L-80,HSM3	5	9.256	76.96	3802.316	60.03	2.09	5	
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.880	78.84	3800.436	60.08	2.15		
3 1/2" CIV TUBING RETRIEVABLE CHEMICAL INJECTION MANDRELHSM3 , 10.2#,SUPER 13CR-110KSI W/CHECK VALVE, DUAL TYPE & RUPTURE DISC, WEIQIXIN Co	CIV		0.624	79.46	3799.812	60.09	2.16		
3-1/2" PUP JOINT,HSM3 , 10.2#, L-80, Type-1	Pup Joint 3-1/2", 10.2#,HSM3		1.910	81.37	3797.902	60.14	2.21		Protector
6	TUBING 3-1/2", 10.2#, L-80,HSM3	6	9.243	90.62	3788.659	60.39	2.47	6	Protector
7	TUBING 3-1/2", 10.2#, L-80,HSM3	7	9.241	99.86	3779.418	60.63	2.72	7	Protector
8	TUBING 3-1/2", 10.2#, L-80,HSM3	8	9.249	109.11	3770.169	60.87	2.97	8	Protector
9	TUBING 3-1/2", 10.2#, L-80,HSM3	9	9.222	118.33	3760.947	61.12	3.22	9	Protector
10	TUBING 3-1/2", 10.2#, L-80,HSM3	10	9.216	127.54	3751.731	61.36	3.47	10	Protector
11	TUBING 3-1/2", 10.2#, L-80,HSM3	11	9.245	136.79	3742.486	61.60	3.72	11	Protector
12	TUBING 3-1/2", 10.2#, L-80,HSM3	12	9.230	146.02	3733.256	61.85	3.97	12	Protector

X-over 4-1/2"HSM3, 18.9# BOX * 3-1/2"HSM3 , 10.2# PIN,	XOS 4-1/2", HSM3 B X 3-1/2" HSM3, P	0	1.100	147.12	3732.156	61.90	4.00		
25	TUBING 4-1/2", 18.9#, L-80,HSM3	13	9.531	156.65	3722.625	62.37	4.41	13	Protector
26	TUBING 4-1/2", 18.9#, L-80,HSM3	14	9.530	166.18	3713.095	62.83	4.81	14	Press Test/G.ring
27	TUBING 4-1/2", 18.9#, L-80,HSM3	15	9.530	175.71	3703.565	63.30	5.21	15	Protector
28	TUBING 4-1/2", 18.9#, L-80,HSM3	16	9.528	185.24	3694.037	63.76	5.61	16	Protector
29	TUBING 4-1/2", 18.9#, L-80,HSM3	17	9.528	194.77	3684.509	64.23	6.02	17	Protector
30	TUBING 4-1/2", 18.9#, L-80,HSM3	18	9.529	204.30	3674.980	64.69	6.42	18	Protector
31	TUBING 4-1/2", 18.9#, L-80,HSM3	19	9.533	213.83	3665.447	65.16	6.82	19	Protector
32	TUBING 4-1/2", 18.9#, L-80,HSM3	20	9.527	223.36	3655.920	65.62	7.22	20	Protector
33	TUBING 4-1/2", 18.9#, L-80,HSM3	21	9.530	232.89	3646.390	66.09	7.63	21	Protector
34	TUBING 4-1/2", 18.9#, L-80,HSM3	22	9.531	242.42	3636.859	66.55	8.03	22	Protector
35	TUBING 4-1/2", 18.9#, L-80,HSM3	23	9.534	251.95	3627.325	67.02	8.43	23	Protector
36	TUBING 4-1/2", 18.9#, L-80,HSM3	24	9.531	261.48	3617.794	67.48	8.83	24	Protector
37	TUBING 4-1/2", 18.9#, L-80,HSM3	25	9.530	271.01	3608.264	67.95	9.24	25	Protector
38	TUBING 4-1/2", 18.9#, L-80,HSM3	26	9.532	280.54	3598.732	68.42	9.64	26	Protector
39	TUBING 4-1/2", 18.9#, L-80,HSM3	27	9.529	290.07	3589.203	68.88	10.04	27	Protector
40	TUBING 4-1/2", 18.9#, L-80,HSM3	28	9.528	299.60	3579.675	69.35	10.44	28	Protector
41	TUBING 4-1/2", 18.9#, L-80,HSM3	29	9.527	309.13	3570.148	69.81	10.85	29	Protector
42	TUBING 4-1/2", 18.9#, L-80,HSM3	30	9.529	318.66	3560.619	70.28	11.25	30	Protector
43	TUBING 4-1/2", 18.9#, L-80,HSM3	31	9.530	328.19	3551.089	70.74	11.65	31	Protector
44	TUBING 4-1/2", 18.9#, L-80,HSM3	32	9.186	337.37	3541.903	71.19	12.04	32	Protector
45	TUBING 4-1/2", 18.9#, L-80,HSM3	33	9.528	346.90	3532.375	71.65	12.44	33	Protector
46	TUBING 4-1/2", 18.9#, L-80,HSM3	34	9.528	356.43	3522.847	72.12	12.84	34	Protector
47	TUBING 4-1/2", 18.9#, L-80,HSM3	35	9.528	365.96	3513.319	72.59	13.25	35	Protector
48	TUBING 4-1/2", 18.9#, L-80,HSM3	36	9.522	375.48	3503.797	73.05	13.65	36	Protector
49	TUBING 4-1/2", 18.9#, L-80,HSM3	37	9.530	385.01	3494.267	73.52	14.05	37	Protector
50	TUBING 4-1/2", 18.9#, L-80,HSM3	38	9.522	394.53	3484.745	73.98	14.45	38	Protector
51	TUBING 4-1/2", 18.9#, L-80,HSM3	39	9.522	404.05	3475.223	74.45	14.85	39	Protector
52	TUBING 4-1/2", 18.9#, L-80,HSM3	40	9.530	413.58	3465.693	74.91	15.26	40	Protector
53	TUBING 4-1/2", 18.9#, L-80,HSM3	41	9.534	423.12	3456.159	75.38	15.66	41	Protector
54	TUBING 4-1/2", 18.9#, L-80,HSM3	42	9.536	432.65	3446.623	75.84	16.06	42	Protector
55	TUBING 4-1/2", 18.9#, L-80,HSM3	43	9.541	442.19	3437.082	76.31	16.46	43	Protector
56	TUBING 4-1/2", 18.9#, L-80,HSM3	44	9.536	451.73	3427.546	76.77	16.87	44	Protector
57	TUBING 4-1/2", 18.9#, L-80,HSM3	45	9.533	461.26	3418.013	77.24	17.27	45	Protector
58	TUBING 4-1/2", 18.9#, L-80,HSM3	46	9.539	470.80	3408.474	77.70	17.67	46	Protector
59	TUBING 4-1/2", 18.9#, L-80,HSM3	47	9.533	480.33	3398.941	78.17	18.08	47	Protector
60	TUBING 4-1/2", 18.9#, L-80,HSM3	48	9.526	489.86	3389.415	78.63	18.48	48	Protector
61	TUBING 4-1/2", 18.9#, L-80,HSM3	49	9.528	499.39	3379.887	79.10	18.88	49	Protector
62	TUBING 4-1/2", 18.9#, L-80,HSM3	50	9.524	508.91	3370.363	79.56	19.28	50	Protector
63	TUBING 4-1/2", 18.9#, L-80,HSM3	51	9.529	518.44	3360.834	80.03	19.68	51	Protector
64	TUBING 4-1/2", 18.9#, L-80,HSM3	52	8.958	527.40	3351.876	80.47	20.06	52	Protector
65	TUBING 4-1/2", 18.9#, L-80,HSM3	53	9.527	536.93	3342.349	80.93	20.47	53	Protector
66	TUBING 4-1/2", 18.9#, L-80,HSM3	54	9.527	546.45	3332.822	81.40	20.87	54	Protector
67	TUBING 4-1/2", 18.9#, L-80,HSM3	55	9.531	555.98	3323.291	81.86	21.27	55	Protector
68	TUBING 4-1/2", 18.9#, L-80,HSM3	56	9.544	565.53	3313.747	82.33	21.67	56	Protector
69	TUBING 4-1/2", 18.9#, L-80,HSM3	57	9.556	575.08	3304.191	82.80	22.08	57	Protector
70	TUBING 4-1/2", 18.9#, L-80,HSM3	58	9.556	584.64	3294.635	83.26	22.48	58	Protector
71	TUBING 4-1/2", 18.9#, L-80,HSM3	59	9.531	594.17	3285.104	83.73	22.88	59	Protector
72	TUBING 4-1/2", 18.9#, L-80,HSM3	60	9.529	603.70	3275.575	84.19	23.28	60	Protector
73	TUBING 4-1/2", 18.9#, L-80,HSM3	61	9.528	613.23	3266.047	84.66	23.69	61	Protector
74	TUBING 4-1/2", 18.9#, L-80,HSM3	62	9.531	622.76	3256.516	85.12	24.09	62	Protector
75	TUBING 4-1/2", 18.9#, L-80,HSM3	63	9.533	632.29	3246.983	85.59	24.49	63	Protector
76	TUBING 4-1/2", 18.9#, L-80,HSM3	64	9.535	641.83	3237.448	86.05	24.90	64	Protector
77	TUBING 4-1/2", 18.9#, L-80,HSM3	65	9.532	651.36	3227.916	86.52	25.30	65	Protector
78	TUBING 4-1/2", 18.9#, L-80,HSM3	66	9.532	660.89	3218.384	86.98	25.70	66	Protector
79	TUBING 4-1/2", 18.9#, L-80,HSM3	67	9.530	670.42	3208.854	87.45	26.10	67	Protector
80	TUBING 4-1/2", 18.9#, L-80,HSM3	68	9.529	679.95	3199.325	87.92	26.50	68	Protector
81	TUBING 4-1/2", 18.9#, L-80,HSM3	69	9.542	689.49	3189.783	88.38	26.91	69	Protector
82	TUBING 4-1/2", 18.9#, L-80,HSM3	70	9.545	699.04	3180.238	88.85	27.31	70	Protector
83	TUBING 4-1/2", 18.9#, L-80,HSM3	71	9.570	708.61	3170.668	89.31	27.72	71	Protector
84	TUBING 4-1/2", 18.9#, L-80,HSM3	72	9.539	718.15	3161.129	89.78	28.12	72	Protector
85	TUBING 4-1/2", 18.9#, L-80,HSM3	73	9.536	727.68	3151.593	90.25	28.52	73	Protector
86	TUBING 4-1/2", 18.9#, L-80,HSM3	74	9.546	737.23	3142.047	90.71	28.92	74	Protector
87	TUBING 4-1/2", 18.9#, L-80,HSM3	75	9.535	746.76	3132.512	91.18	29.33	75	Protector
88	TUBING 4-1/2", 18.9#, L-80,HSM3	76	9.529	756.29	3122.983	91.64	29.73	76	Protector
89	TUBING 4-1/2", 18.9#, L-80,HSM3	77	9.524	765.82	3113.459	92.11	30.13	77	Protector
90	TUBING 4-1/2", 18.9#, L-80,HSM3	78	9.529	775.35	3103.930	92.57	30.53	78	Protector
91	TUBING 4-1/2", 18.9#, L-80,HSM3	79	9.528	784.87	3094.402	93.04	30.94	79	Protector
92	TUBING 4-1/2", 18.9#, L-80,HSM3	80	9.526	794.40	3084.876	93.50	31.34	80	Protector
93	TUBING 4-1/2", 18.9#, L-80,HSM3	81	9.530	803.93	3075.346	93.97	31.74	81	Protector

94	TUBING 4-1/2", 18.9#, L-80,HSM3	82	9.528	813.46	3065.818	94.43	32.14	82	Protector
95	TUBING 4-1/2", 18.9#, L-80,HSM3	83	9.527	822.98	3056.291	94.90	32.55	83	Protector
96	TUBING 4-1/2", 18.9#, L-80,HSM3	84	9.525	832.51	3046.766	95.36	32.95	84	Protector
97	TUBING 4-1/2", 18.9#, L-80,HSM3	85	9.529	842.04	3037.237	95.83	33.35	85	Protector
98	TUBING 4-1/2", 18.9#, L-80,HSM3	86	9.531	851.57	3027.706	96.29	33.75	86	Protector
99	TUBING 4-1/2", 18.9#, L-80,HSM3	87	9.529	861.10	3018.177	96.76	34.15	87	Protector
100	TUBING 4-1/2", 18.9#, L-80,HSM3	88	9.530	870.63	3008.647	97.22	34.56	88	Protector
101	TUBING 4-1/2", 18.9#, L-80,HSM3	89	9.525	880.15	2999.122	97.69	34.96	89	Protector
102	TUBING 4-1/2", 18.9#, L-80,HSM3	90	9.535	889.69	2989.587	98.16	35.36	90	Protector
103	TUBING 4-1/2", 18.9#, L-80,HSM3	91	9.531	899.22	2980.056	98.62	35.76	91	Protector
104	TUBING 4-1/2", 18.9#, L-80,HSM3	92	9.536	908.76	2970.520	99.09	36.17	92	Protector
105	TUBING 4-1/2", 18.9#, L-80,HSM3	93	9.532	918.29	2960.988	99.55	36.57	93	Protector
106	TUBING 4-1/2", 18.9#, L-80,HSM3	94	9.531	927.82	2951.457	100.02	36.97	94	Protector
107	TUBING 4-1/2", 18.9#, L-80,HSM3	95	9.533	937.35	2941.924	100.48	37.38	95	Protector
108	TUBING 4-1/2", 18.9#, L-80,HSM3	96	9.531	946.88	2932.393	100.95	37.78	96	Protector
109	TUBING 4-1/2", 18.9#, L-80,HSM3	97	9.528	956.41	2922.865	101.41	38.18	97	Protector
110	TUBING 4-1/2", 18.9#, L-80,HSM3	98	9.529	965.94	2913.336	101.88	38.58	98	Protector
111	TUBING 4-1/2", 18.9#, L-80,HSM3	99	9.529	975.47	2903.807	102.34	38.98	99	Protector
112	TUBING 4-1/2", 18.9#, L-80,HSM3	100	9.525	984.99	2894.282	102.81	39.39	100	Protector
113	TUBING 4-1/2", 18.9#, L-80,HSM3	101	9.522	994.52	2884.760	103.27	39.79	101	Protector
114	TUBING 4-1/2", 18.9#, L-80,HSM3	102	9.184	1003.70	2875.576	103.72	40.18	102	Protector
115	TUBING 4-1/2", 18.9#, L-80,HSM3	103	9.530	1013.23	2866.046	104.19	40.58	103	Protector
116	TUBING 4-1/2", 18.9#, L-80,HSM3	104	9.529	1022.76	2856.517	104.65	40.98	104	Protector
117	TUBING 4-1/2", 18.9#, L-80,HSM3	105	9.532	1032.29	2846.985	105.12	41.38	105	Press test/Protector
118	TUBING 4-1/2", 18.9#, L-80,HSM3	106	9.530	1041.82	2837.455	105.58	41.79	106	Protector
119	TUBING 4-1/2", 18.9#, L-80,HSM3	107	9.527	1051.35	2827.928	106.05	42.19	107	Protector
120	TUBING 4-1/2", 18.9#, L-80,HSM3	108	9.527	1060.87	2818.401	106.51	42.59	108	Protector
121	TUBING 4-1/2", 18.9#, L-80,HSM3	109	9.531	1070.41	2808.870	106.98	42.99	109	Protector
122	TUBING 4-1/2", 18.9#, L-80,HSM3	110	9.526	1079.93	2799.344	107.44	43.40	110	Protector
123	TUBING 4-1/2", 18.9#, L-80,HSM3	111	9.542	1089.47	2789.802	107.91	43.80	111	Protector
124	TUBING 4-1/2", 18.9#, L-80,HSM3	112	9.598	1099.07	2780.204	108.38	44.20	112	Protector
125	TUBING 4-1/2", 18.9#, L-80,HSM3	113	9.527	1108.60	2770.677	108.84	44.61	113	Protector
126	TUBING 4-1/2", 18.9#, L-80,HSM3	114	9.530	1118.13	2761.147	109.31	45.01	114	Protector
127	TUBING 4-1/2", 18.9#, L-80,HSM3	115	9.530	1127.66	2751.617	109.77	45.41	115	Protector
128	TUBING 4-1/2", 18.9#, L-80,HSM3	116	9.522	1137.18	2742.095	110.24	45.81	116	Protector
129	TUBING 4-1/2", 18.9#, L-80,HSM3	117	9.521	1146.70	2732.574	110.70	46.22	117	Protector
130	TUBING 4-1/2", 18.9#, L-80,HSM3	118	9.524	1156.23	2723.050	111.17	46.62	118	Protector
131	TUBING 4-1/2", 18.9#, L-80,HSM3	119	9.529	1165.75	2713.521	111.63	47.02	119	Protector
132	TUBING 4-1/2", 18.9#, L-80,HSM3	120	9.530	1175.28	2703.991	112.10	47.42	120	Protector
133	TUBING 4-1/2", 18.9#, L-80,HSM3	121	9.568	1184.85	2694.423	112.57	47.83	121	Protector
134	TUBING 4-1/2", 18.9#, L-80,HSM3	122	9.569	1194.42	2684.854	113.03	48.23	122	Protector
135	TUBING 4-1/2", 18.9#, L-80,HSM3	123	9.572	1203.99	2675.282	113.50	48.64	123	Protector
136	TUBING 4-1/2", 18.9#, L-80,HSM3	124	9.565	1213.56	2665.717	113.97	49.04	124	Protector
137	TUBING 4-1/2", 18.9#, L-80,HSM3	125	9.570	1223.13	2656.147	114.43	49.44	125	Protector
138	TUBING 4-1/2", 18.9#, L-80,HSM3	126	9.545	1232.67	2646.602	114.90	49.85	126	Protector
139	TUBING 4-1/2", 18.9#, L-80,HSM3	127	9.567	1242.24	2637.035	115.37	50.25	127	Protector
140	TUBING 4-1/2", 18.9#, L-80,HSM3	128	9.543	1251.78	2627.492	115.83	50.65	128	Protector
141	TUBING 4-1/2", 18.9#, L-80,HSM3	129	9.412	1261.20	2618.080	116.29	51.05	129	Protector
142	TUBING 4-1/2", 18.9#, L-80,HSM3	130	9.546	1270.74	2608.534	116.76	51.45	130	Protector
143	TUBING 4-1/2", 18.9#, L-80,HSM3	131	9.571	1280.31	2598.963	117.23	51.86	131	Protector
144	TUBING 4-1/2", 18.9#, L-80,HSM3	132	9.568	1289.88	2589.395	117.69	52.26	132	Protector
145	TUBING 4-1/2", 18.9#, L-80,HSM3	133	9.543	1299.42	2579.852	118.16	52.67	133	Protector
146	TUBING 4-1/2", 18.9#, L-80,HSM3	134	9.537	1308.96	2570.315	118.63	53.07	134	Protector
147	TUBING 4-1/2", 18.9#, L-80,HSM3	135	9.533	1318.49	2560.782	119.09	53.47	135	Protector
148	TUBING 4-1/2", 18.9#, L-80,HSM3	136	9.535	1328.03	2551.247	119.56	53.87	136	Protector
149	TUBING 4-1/2", 18.9#, L-80,HSM3	137	9.536	1337.56	2541.711	120.02	54.28	137	Protector
150	TUBING 4-1/2", 18.9#, L-80,HSM3	138	9.420	1346.98	2532.291	120.48	54.67	138	Protector
151	TUBING 4-1/2", 18.9#, L-80,HSM3	139	9.545	1356.53	2522.746	120.95	55.08	139	Protector
152	TUBING 4-1/2", 18.9#, L-80,HSM3	140	9.528	1366.06	2513.218	121.41	55.48	140	Protector
153	TUBING 4-1/2", 18.9#, L-80,HSM3	141	9.528	1375.59	2503.690	121.88	55.88	141	Protector
154	TUBING 4-1/2", 18.9#, L-80,HSM3	142	9.527	1385.11	2494.163	122.34	56.28	142	Protector
155	TUBING 4-1/2", 18.9#, L-80,HSM3	143	9.527	1394.64	2484.636	122.81	56.69	143	Protector
156	TUBING 4-1/2", 18.9#, L-80,HSM3	144	9.528	1404.17	2475.108	123.27	57.09	144	Protector
157	TUBING 4-1/2", 18.9#, L-80,HSM3	145	9.528	1413.70	2465.580	123.74	57.49	145	Protector
158	TUBING 4-1/2", 18.9#, L-80,HSM3	146	9.524	1423.22	2456.056	124.20	57.89	146	Protector
159	TUBING 4-1/2", 18.9#, L-80,HSM3	147	9.525	1432.74	2446.531	124.67	58.30	147	Protector
160	TUBING 4-1/2", 18.9#, L-80,HSM3	148	9.527	1442.27	2437.004	125.13	58.70	148	Protector
161	TUBING 4-1/2", 18.9#, L-80,HSM3	149	9.391	1451.66	2427.613	125.59	59.09	149	Protector
162	TUBING 4-1/2", 18.9#, L-80,HSM3	150	9.544	1461.21	2418.069	126.06	59.50	150	Protector
163	TUBING 4-1/2", 18.9#, L-80,HSM3	151	9.543	1470.75	2408.526	126.52	59.90	151	Protector

164	TUBING 4-1/2", 18.9#, L-80,HSM3	152	9.536	1480.29	2398.990	126.99	60.30	152	Protector
165	TUBING 4-1/2", 18.9#, L-80,HSM3	153	9.529	1489.81	2389.461	127.45	60.71	153	Protector
166	TUBING 4-1/2", 18.9#, L-80,HSM3	154	9.423	1499.24	2380.038	127.91	61.10	154	Protector
167	TUBING 4-1/2", 18.9#, L-80,HSM3	155	9.527	1508.76	2370.511	128.38	61.51	155	Protector
168	TUBING 4-1/2", 18.9#, L-80,HSM3	156	9.566	1518.33	2360.945	128.85	61.91	156	Protector
169	TUBING 4-1/2", 18.9#, L-80,HSM3	157	9.531	1527.86	2351.414	129.31	62.31	157	Protector
170	TUBING 4-1/2", 18.9#, L-80,HSM3	158	9.529	1537.39	2341.885	129.78	62.71	158	Protector
171	TUBING 4-1/2", 18.9#, L-80,HSM3	159	9.528	1546.92	2332.357	130.24	63.12	159	Protector
172	TUBING 4-1/2", 18.9#, L-80,HSM3	160	9.543	1556.46	2322.814	130.71	63.52	160	Protector
173	TUBING 4-1/2", 18.9#, L-80,HSM3	161	9.528	1565.99	2313.286	131.17	63.92	161	Protector
174	TUBING 4-1/2", 18.9#, L-80,HSM3	162	9.543	1575.53	2303.743	131.64	64.33	162	Protector
175	TUBING 4-1/2", 18.9#, L-80,HSM3	163	9.556	1585.09	2294.187	132.11	64.73	163	Protector
176	TUBING 4-1/2", 18.9#, L-80,HSM3	164	9.558	1594.65	2284.629	132.57	65.13	164	Protector
177	TUBING 4-1/2", 18.9#, L-80,HSM3	165	9.559	1604.21	2275.070	133.04	65.54	165	Protector
178	TUBING 4-1/2", 18.9#, L-80,HSM3	166	9.554	1613.76	2265.516	133.51	65.94	166	Protector
179	TUBING 4-1/2", 18.9#, L-80,HSM3	167	9.555	1623.31	2255.961	133.97	66.34	167	Protector
180	TUBING 4-1/2", 18.9#, L-80,HSM3	168	9.554	1632.87	2246.407	134.44	66.75	168	Protector
181	TUBING 4-1/2", 18.9#, L-80,HSM3	169	9.534	1642.40	2236.873	134.90	67.15	169	Protector
182	TUBING 4-1/2", 18.9#, L-80,HSM3	170	9.534	1651.94	2227.339	135.37	67.55	170	Protector
183	TUBING 4-1/2", 18.9#, L-80,HSM3	171	9.537	1661.47	2217.802	135.84	67.95	171	Protector
184	TUBING 4-1/2", 18.9#, L-80,HSM3	172	9.534	1671.01	2208.268	136.30	68.36	172	Protector
185	TUBING 4-1/2", 18.9#, L-80,HSM3	173	9.531	1680.54	2198.737	136.77	68.76	173	Protector
186	TUBING 4-1/2", 18.9#, L-80,HSM3	174	9.534	1690.07	2189.203	137.23	69.16	174	Protector
187	TUBING 4-1/2", 18.9#, L-80,HSM3	175	9.533	1699.61	2179.670	137.70	69.56	175	Protector
188	TUBING 4-1/2", 18.9#, L-80,HSM3	176	9.531	1709.14	2170.139	138.16	69.97	176	Protector
189	TUBING 4-1/2", 18.9#, L-80,HSM3	177	9.533	1718.67	2160.606	138.63	70.37	177	Protector
190	TUBING 4-1/2", 18.9#, L-80,HSM3	178	9.534	1728.20	2151.072	139.09	70.77	178	Protector
191	TUBING 4-1/2", 18.9#, L-80,HSM3	179	9.529	1737.73	2141.543	139.56	71.18	179	Protector
192	TUBING 4-1/2", 18.9#, L-80,HSM3	180	9.528	1747.26	2132.015	140.02	71.58	180	Protector
193	TUBING 4-1/2", 18.9#, L-80,HSM3	181	9.531	1756.79	2122.484	140.49	71.98	181	Protector
194	TUBING 4-1/2", 18.9#, L-80,HSM3	182	9.533	1766.32	2112.951	140.95	72.38	182	Protector
195	TUBING 4-1/2", 18.9#, L-80,HSM3	183	9.528	1775.85	2103.423	141.42	72.78	183	Protector
196	TUBING 4-1/2", 18.9#, L-80,HSM3	184	9.525	1785.38	2093.898	141.88	73.19	184	Protector
197	TUBING 4-1/2", 18.9#, L-80,HSM3	185	9.533	1794.91	2084.365	142.35	73.59	185	Protector
198	TUBING 4-1/2", 18.9#, L-80,HSM3	186	9.529	1804.44	2074.836	142.82	73.99	186	Protector
199	TUBING 4-1/2", 18.9#, L-80,HSM3	187	9.530	1813.97	2065.306	143.28	74.39	187	Protector
200	TUBING 4-1/2", 18.9#, L-80,HSM3	188	9.529	1823.50	2055.777	143.75	74.80	188	Protector
201	TUBING 4-1/2", 18.9#, L-80,HSM3	189	9.528	1833.03	2046.249	144.21	75.20	189	Protector
202	TUBING 4-1/2", 18.9#, L-80,HSM3	190	9.527	1842.55	2036.722	144.68	75.60	190	Protector
203	TUBING 4-1/2", 18.9#, L-80,HSM3	191	9.533	1852.09	2027.189	145.14	76.00	191	Protector
204	TUBING 4-1/2", 18.9#, L-80,HSM3	192	9.525	1861.61	2017.664	145.61	76.41	192	Protector
205	TUBING 4-1/2", 18.9#, L-80,HSM3	193	9.533	1871.14	2008.131	146.07	76.81	193	Protector
206	TUBING 4-1/2", 18.9#, L-80,HSM3	194	9.530	1880.67	1998.601	146.54	77.21	194	Protector
207	TUBING 4-1/2", 18.9#, L-80,HSM3	195	9.534	1890.21	1989.067	147.00	77.61	195	Protector
208	TUBING 4-1/2", 18.9#, L-80,HSM3	196	9.529	1899.74	1979.538	147.47	78.02	196	Protector
209	TUBING 4-1/2", 18.9#, L-80,HSM3	197	9.536	1909.27	1970.002	147.93	78.42	197	Protector
210	TUBING 4-1/2", 18.9#, L-80,HSM3	198	9.529	1918.80	1960.473	148.40	78.82	198	Protector
211	TUBING 4-1/2", 18.9#, L-80,HSM3	199	9.535	1928.34	1950.938	148.86	79.22	199	Protector
212	TUBING 4-1/2", 18.9#, L-80,HSM3	200	9.531	1937.87	1941.407	149.33	79.63	200	Protector
213	TUBING 4-1/2", 18.9#, L-80,HSM3	201	9.540	1947.41	1931.867	149.80	80.03	201	Protector
214	TUBING 4-1/2", 18.9#, L-80,HSM3	202	9.532	1956.94	1922.335	150.26	80.43	202	Protector
215	TUBING 4-1/2", 18.9#, L-80,HSM3	203	9.536	1966.48	1912.799	150.73	80.83	203	Protector
216	TUBING 4-1/2", 18.9#, L-80,HSM3	204	9.531	1976.01	1903.268	151.19	81.24	204	Protector
217	TUBING 4-1/2", 18.9#, L-80,HSM3	205	9.532	1985.54	1893.736	151.66	81.64	205	Protector
218	TUBING 4-1/2", 18.9#, L-80,HSM3	206	9.531	1995.07	1884.205	152.12	82.04	206	Protector
219	TUBING 4-1/2", 18.9#, L-80,HSM3	207	9.536	2004.61	1874.669	152.59	82.45	207	Protector
220	TUBING 4-1/2", 18.9#, L-80,HSM3	208	9.532	2014.14	1865.137	153.05	82.85	208	Press test/Protector
221	TUBING 4-1/2", 18.9#, L-80,HSM3	209	9.532	2023.67	1855.605	153.52	83.25	209	Protector
222	TUBING 4-1/2", 18.9#, L-80,HSM3	210	9.531	2033.20	1846.074	153.98	83.65	210	Protector
223	TUBING 4-1/2", 18.9#, L-80,HSM3	211	9.527	2042.73	1836.547	154.45	84.06	211	Protector
224	TUBING 4-1/2", 18.9#, L-80,HSM3	212	9.530	2052.26	1827.017	154.91	84.46	212	Protector
225	TUBING 4-1/2", 18.9#, L-80,HSM3	213	9.533	2061.79	1817.484	155.38	84.86	213	Protector
226	TUBING 4-1/2", 18.9#, L-80,HSM3	214	9.534	2071.33	1807.950	155.85	85.26	214	Protector
227	TUBING 4-1/2", 18.9#, L-80,HSM3	215	9.535	2080.86	1798.415	156.31	85.67	215	Protector
228	TUBING 4-1/2", 18.9#, L-80,HSM3	216	9.530	2090.39	1788.885	156.78	86.07	216	Protector
229	TUBING 4-1/2", 18.9#, L-80,HSM3	217	9.533	2099.92	1779.352	157.24	86.47	217	Protector
230	TUBING 4-1/2", 18.9#, L-80,HSM3	218	9.529	2109.45	1769.823	157.71	86.87	218	Protector
231	TUBING 4-1/2", 18.9#, L-80,HSM3	219	9.530	2118.98	1760.293	158.17	87.28	219	Protector


233	TUBING 4-1/2", 18.9#, L-80,HSM3	220	9.523	2128.51	1750.770	158.64	87.68	220	Protector
234	TUBING 4-1/2", 18.9#, L-80,HSM3	221	9.543	2138.05	1741.227	159.10	88.08	221	Protector
235	TUBING 4-1/2", 18.9#, L-80,HSM3	222	9.536	2147.58	1731.691	159.57	88.48	222	Protector
236	TUBING 4-1/2", 18.9#, L-80,HSM3	223	9.530	2157.11	1722.161	160.03	88.89	223	Protector
237	TUBING 4-1/2", 18.9#, L-80,HSM3	224	9.552	2166.67	1712.609	160.50	89.29	224	Protector
238	TUBING 4-1/2", 18.9#, L-80,HSM3	225	9.534	2176.20	1703.075	160.97	89.69	225	Protector
239	TUBING 4-1/2", 18.9#, L-80,HSM3	226	9.554	2185.75	1693.521	161.43	90.10	226	Protector
240	TUBING 4-1/2", 18.9#, L-80,HSM3	227	9.541	2195.30	1683.980	161.90	90.50	227	Protector
241	TUBING 4-1/2", 18.9#, L-80,HSM3	228	9.543	2204.84	1674.437	162.36	90.90	228	Protector
242	TUBING 4-1/2", 18.9#, L-80,HSM3	229	9.540	2214.38	1664.897	162.83	91.30	229	Protector
243	TUBING 4-1/2", 18.9#, L-80,HSM3	230	9.553	2223.93	1655.344	163.30	91.71	230	Protector
244	TUBING 4-1/2", 18.9#, L-80,HSM3	231	9.524	2233.46	1645.820	163.76	92.11	231	Protector
245	TUBING 4-1/2", 18.9#, L-80,HSM3	232	9.525	2242.98	1636.295	164.23	92.51	232	Protector
246	TUBING 4-1/2", 18.9#, L-80,HSM3	233	9.523	2252.50	1626.772	164.69	92.91	233	Protector
247	TUBING 4-1/2", 18.9#, L-80,HSM3	234	9.528	2262.03	1617.244	165.16	93.32	234	Protector
248	TUBING 4-1/2", 18.9#, L-80,HSM3	235	9.523	2271.55	1607.721	165.62	93.72	235	Protector
249	TUBING 4-1/2", 18.9#, L-80,HSM3	236	9.528	2281.08	1598.193	166.09	94.12	236	Protector
250	TUBING 4-1/2", 18.9#, L-80,HSM3	237	9.523	2290.61	1588.670	166.55	94.52	237	Protector
251	TUBING 4-1/2", 18.9#, L-80,HSM3	238	9.530	2300.14	1579.140	167.02	94.93	238	Protector
252	TUBING 4-1/2", 18.9#, L-80,HSM3	239	9.533	2309.67	1569.607	167.48	95.33	239	Protector
253	TUBING 4-1/2", 18.9#, L-80,HSM3	240	9.532	2319.20	1560.075	167.95	95.73	240	Protector
254	TUBING 4-1/2", 18.9#, L-80,HSM3	241	9.527	2328.73	1550.548	168.41	96.13	241	Protector
255	TUBING 4-1/2", 18.9#, L-80,HSM3	242	9.532	2338.26	1541.016	168.88	96.54	242	Protector
256	TUBING 4-1/2", 18.9#, L-80,HSM3	243	9.534	2347.79	1531.482	169.34	96.94	243	Protector
257	TUBING 4-1/2", 18.9#, L-80,HSM3	244	9.531	2357.32	1521.951	169.81	97.34	244	Protector
258	TUBING 4-1/2", 18.9#, L-80,HSM3	245	9.530	2366.85	1512.421	170.27	97.74	245	Protector
259	TUBING 4-1/2", 18.9#, L-80,HSM3	246	9.523	2376.38	1502.898	170.74	98.15	246	Protector
260	TUBING 4-1/2", 18.9#, L-80,HSM3	247	9.531	2385.91	1493.367	171.20	98.55	247	Protector
261	TUBING 4-1/2", 18.9#, L-80,HSM3	248	9.543	2395.45	1483.824	171.67	98.95	248	Protector
262	TUBING 4-1/2", 18.9#, L-80,HSM3	249	9.552	2405.00	1474.272	172.14	99.35	249	Protector
263	TUBING 4-1/2", 18.9#, L-80,HSM3	250	9.530	2414.53	1464.742	172.60	99.76	250	Protector
264	TUBING 4-1/2", 18.9#, L-80,HSM3	251	9.530	2424.06	1455.212	173.07	100.16	251	Protector
265	TUBING 4-1/2", 18.9#, L-80,HSM3	252	9.529	2433.59	1445.683	173.53	100.56	252	Protector
266	TUBING 4-1/2", 18.9#, L-80,HSM3	253	9.533	2443.13	1436.150	174.00	100.96	253	Protector
267	TUBING 4-1/2", 18.9#, L-80,HSM3	254	9.551	2452.68	1426.599	174.46	101.37	254	Protector
268	TUBING 4-1/2", 18.9#, L-80,HSM3	255	9.538	2462.21	1417.061	174.93	101.77	255	Protector
269	TUBING 4-1/2", 18.9#, L-80,HSM3	256	9.536	2471.75	1407.525	175.40	102.17	256	Protector
270	TUBING 4-1/2", 18.9#, L-80,HSM3	257	9.525	2481.28	1398.000	175.86	102.57	257	Protector
271	TUBING 4-1/2", 18.9#, L-80,HSM3	258	9.555	2490.83	1388.445	176.33	102.98	258	Protector
272	TUBING 4-1/2", 18.9#, L-80,HSM3	259	9.530	2500.36	1378.915	176.79	103.38	259	Protector
273	TUBING 4-1/2", 18.9#, L-80,HSM3	260	9.536	2509.90	1369.379	177.26	103.78	260	Protector
274	TUBING 4-1/2", 18.9#, L-80,HSM3	261	9.539	2519.44	1359.840	177.72	104.19	261	Protector
275	TUBING 4-1/2", 18.9#, L-80,HSM3	262	9.538	2528.97	1350.302	178.19	104.59	262	Protector
276	TUBING 4-1/2", 18.9#, L-80,HSM3	263	9.536	2538.51	1340.766	178.65	104.99	263	Protector
277	TUBING 4-1/2", 18.9#, L-80,HSM3	264	9.526	2548.04	1331.240	179.12	105.39	264	Protector
278	TUBING 4-1/2", 18.9#, L-80,HSM3	265	9.528	2557.56	1321.712	179.58	105.80	265	Protector
279	TUBING 4-1/2", 18.9#, L-80,HSM3	266	9.524	2567.09	1312.188	180.05	106.20	266	Protector
280	TUBING 4-1/2", 18.9#, L-80,HSM3	267	9.537	2576.62	1302.651	180.52	106.60	267	Protector
281	TUBING 4-1/2", 18.9#, L-80,HSM3	268	9.530	2586.15	1293.121	180.98	107.00	268	Protector
282	TUBING 4-1/2", 18.9#, L-80,HSM3	269	9.534	2595.69	1283.587	181.45	107.41	269	Protector
283	TUBING 4-1/2", 18.9#, L-80,HSM3	270	9.534	2605.22	1274.053	181.91	107.81	270	Protector
284	TUBING 4-1/2", 18.9#, L-80,HSM3	271	9.533	2614.76	1264.520	182.38	108.21	271	Protector
285	TUBING 4-1/2", 18.9#, L-80,HSM3	272	9.532	2624.29	1254.988	182.84	108.61	272	Protector
286	TUBING 4-1/2", 18.9#, L-80,HSM3	273	9.543	2633.83	1245.445	183.31	109.02	273	Protector
287	TUBING 4-1/2", 18.9#, L-80,HSM3	274	9.203	2643.03	1236.242	183.76	109.41	274	Protector
288	TUBING 4-1/2", 18.9#, L-80,HSM3	275	9.533	2652.57	1226.709	184.22	109.81	275	Protector
289	TUBING 4-1/2", 18.9#, L-80,HSM3	276	9.531	2662.10	1217.178	184.69	110.21	276	Protector
290	TUBING 4-1/2", 18.9#, L-80,HSM3	277	9.537	2671.63	1207.641	185.15	110.61	277	Protector
291	TUBING 4-1/2", 18.9#, L-80,HSM3	278	9.531	2681.17	1198.110	185.62	111.02	278	Protector
292	TUBING 4-1/2", 18.9#, L-80,HSM3	279	9.535	2690.70	1188.575	186.09	111.42	279	Protector
293	TUBING 4-1/2", 18.9#, L-80,HSM3	280	9.534	2700.23	1179.041	186.55	111.82	280	Protector
294	TUBING 4-1/2", 18.9#, L-80,HSM3	281	9.533	2709.77	1169.508	187.02	112.22	281	Protector
295	TUBING 4-1/2", 18.9#, L-80,HSM3	282	9.524	2719.29	1159.984	187.48	112.63	282	Protector
296	TUBING 4-1/2", 18.9#, L-80,HSM3	283	9.525	2728.82	1150.459	187.95	113.03	283	Protector
297	TUBING 4-1/2", 18.9#, L-80,HSM3	284	9.528	2738.34	1140.931	188.41	113.43	284	Protector
298	TUBING 4-1/2", 18.9#, L-80,HSM3	285	9.567	2747.91	1131.364	188.88	113.83	285	Protector
299	TUBING 4-1/2", 18.9#, L-80,HSM3	286	9.528	2757.44	1121.836	189.34	114.24	286	Protector
300	TUBING 4-1/2", 18.9#, L-80,HSM3	287	9.524	2766.96	1112.312	189.81	114.64	287	Protector
301	TUBING 4-1/2", 18.9#, L-80,HSM3	288	9.535	2776.50	1102.777	190.27	115.04	288	Protector
302	TUBING 4-1/2", 18.9#, L-80,HSM3	289	9.534	2786.03	1093.243	190.74	115.44	289	Protector


	303	TUBING 4-1/2", 18.9#, L-80,HSM3	290	9.531	2795.56	1083.712	191.20	115.85	290	Protector
	304	TUBING 4-1/2", 18.9#, L-80,HSM3	291	9.530	2805.09	1074.182	191.67	116.25	291	Protector
	305	TUBING 4-1/2", 18.9#, L-80,HSM3	292	9.531	2814.62	1064.651	192.14	116.65	292	Protector
	306	TUBING 4-1/2", 18.9#, L-80,HSM3	293	9.524	2824.15	1055.127	192.60	117.05	293	Protector
	307	TUBING 4-1/2", 18.9#, L-80,HSM3	294	9.545	2833.69	1045.582	193.07	117.46	294	Protector
	308	TUBING 4-1/2", 18.9#, L-80,HSM3	295	9.530	2843.22	1036.052	193.53	117.86	295	Protector
	309	TUBING 4-1/2", 18.9#, L-80,HSM3	296	9.529	2852.75	1026.523	194.00	118.26	296	Protector
	310	TUBING 4-1/2", 18.9#, L-80,HSM3	297	9.528	2862.28	1016.995	194.46	118.66	297	Protector
	311	TUBING 4-1/2", 18.9#, L-80,HSM3	298	9.528	2871.81	1007.467	194.93	119.07	298	Protector
	312	TUBING 4-1/2", 18.9#, L-80,HSM3	299	9.223	2881.03	998.244	195.38	119.46	299	Protector
	313	TUBING 4-1/2", 18.9#, L-80,HSM3	300	9.528	2890.56	988.716	195.84	119.86	300	Protector
	314	TUBING 4-1/2", 18.9#, L-80,HSM3	301	9.529	2900.09	979.187	196.31	120.26	301	Protector
	315	TUBING 4-1/2", 18.9#, L-80,HSM3	302	9.527	2909.62	969.660	196.77	120.66	302	Protector
	316	TUBING 4-1/2", 18.9#, L-80,HSM3	303	9.206	2918.82	960.454	197.22	121.05	303	Protector
	317	TUBING 4-1/2", 18.9#, L-80,HSM3	304	9.527	2928.35	950.927	197.69	121.45	304	Protector
	318	TUBING 4-1/2", 18.9#, L-80,HSM3	305	9.529	2937.88	941.398	198.15	121.86	305	Protector
	319	TUBING 4-1/2", 18.9#, L-80,HSM3	306	9.529	2947.41	931.869	198.62	122.26	306	Protector
	320	TUBING 4-1/2", 18.9#, L-80,HSM3	307	9.532	2956.94	922.337	199.08	122.66	307	Protector
	321	TUBING 4-1/2", 18.9#, L-80,HSM3	308	9.530	2966.47	912.807	199.55	123.06	308	Protector
	322	TUBING 4-1/2", 18.9#, L-80,HSM3	309	9.530	2976.00	903.277	200.01	123.47	309	Protector
	323	TUBING 4-1/2", 18.9#, L-80,HSM3	310	9.530	2985.53	893.747	200.48	123.87	310	Protector
	324	TUBING 4-1/2", 18.9#, L-80,HSM3	311	9.532	2995.06	884.215	200.94	124.27	311	Protector
	325	TUBING 4-1/2", 18.9#, L-80,HSM3	312	9.528	3004.59	874.687	201.41	124.67	312	Protector
	326	TUBING 4-1/2", 18.9#, L-80,HSM3	313	9.519	3014.11	865.168	201.87	125.08	313	Protector
	327	TUBING 4-1/2", 18.9#, L-80,HSM3	314	9.524	3023.63	855.644	202.34	125.48	314	Protector
	328	TUBING 4-1/2", 18.9#, L-80,HSM3	315	9.528	3033.16	846.116	202.80	125.88	315	Protector
	329	TUBING 4-1/2", 18.9#, L-80,HSM3	316	9.524	3042.68	836.592	203.27	126.28	316	Protector
	330	TUBING 4-1/2", 18.9#, L-80,HSM3	317	9.532	3052.22	827.060	203.74	126.69	317	Protector
	331	TUBING 4-1/2", 18.9#, L-80,HSM3	318	9.529	3061.74	817.531	204.20	127.09	318	Protector
	332	TUBING 4-1/2", 18.9#, L-80,HSM3	319	9.532	3071.28	807.999	204.67	127.49	319	Protector
	333	TUBING 4-1/2", 18.9#, L-80,HSM3	320	9.201	3080.48	798.798	205.11	127.88	320	Protector
	334	TUBING 4-1/2", 18.9#, L-80,HSM3	321	9.531	3090.01	789.267	205.58	128.28	321	Protector
	335	TUBING 4-1/2", 18.9#, L-80,HSM3	322	9.536	3099.54	779.731	206.05	128.68	322	Pres Test/Protector
	336	TUBING 4-1/2", 18.9#, L-80,HSM3	323	9.534	3109.08	770.197	206.51	129.09	323	Protector
	337	TUBING 4-1/2", 18.9#, L-80,HSM3	324	9.533	3118.61	760.664	206.98	129.49	324	Protector
	338	TUBING 4-1/2", 18.9#, L-80,HSM3	325	9.536	3128.15	751.128	207.44	129.89	325	Protector
	339	TUBING 4-1/2", 18.9#, L-80,HSM3	326	9.192	3137.34	741.936	207.89	130.28	326	Protector
	340	TUBING 4-1/2", 18.9#, L-80,HSM3	327	9.528	3146.87	732.408	208.36	130.68	327	Protector
	341	TUBING 4-1/2", 18.9#, L-80,HSM3	328	9.527	3156.39	722.881	208.82	131.09	328	Protector
	342	TUBING 4-1/2", 18.9#, L-80,HSM3	329	9.531	3165.93	713.350	209.29	131.49	329	Protector
	343	TUBING 4-1/2", 18.9#, L-80,HSM3	330	9.529	3175.45	703.821	209.75	131.89	330	Protector
	344	TUBING 4-1/2", 18.9#, L-80,HSM3	331	9.527	3184.98	694.294	210.22	132.29	331	Protector
	345	TUBING 4-1/2", 18.9#, L-80,HSM3	332	9.528	3194.51	684.766	210.68	132.69	332	Protector
	346	TUBING 4-1/2", 18.9#, L-80,HSM3	333	9.196	3203.71	675.570	211.13	133.08	333	Protector
	347	TUBING 4-1/2", 18.9#, L-80,HSM3	334	9.533	3213.24	666.037	211.60	133.49	334	Protector
	348	TUBING 4-1/2", 18.9#, L-80,HSM3	335	9.535	3222.77	656.502	212.06	133.89	335	Protector
	349	TUBING 4-1/2", 18.9#, L-80,HSM3	336	9.534	3232.31	646.968	212.53	134.29	336	Protector
	350	TUBING 4-1/2", 18.9#, L-80,HSM3	337	9.533	3241.84	637.435	212.99	134.69	337	Protector
	351	TUBING 4-1/2", 18.9#, L-80,HSM3	338	9.534	3251.37	627.901	213.46	135.10	338	Protector
	352	TUBING 4-1/2", 18.9#, L-80,HSM3	339	9.534	3260.91	618.367	213.92	135.50	339	Protector
	353	TUBING 4-1/2", 18.9#, L-80,HSM3	340	9.535	3270.44	608.832	214.39	135.90	340	Protector
	354	TUBING 4-1/2", 18.9#, L-80,HSM3	341	9.536	3279.98	599.296	214.86	136.30	341	Protector
	355	TUBING 4-1/2", 18.9#, L-80,HSM3	342	9.552	3289.53	589.744	215.32	136.71	342	Protector
	356	TUBING 4-1/2", 18.9#, L-80,HSM3	343	9.534	3299.07	580.210	215.79	137.11	343	Protector
	357	TUBING 4-1/2", 18.9#, L-80,HSM3	344	9.537	3308.60	570.673	216.25	137.51	344	Protector
	358	TUBING 4-1/2", 18.9#, L-80,HSM3	345	9.540	3318.14	561.133	216.72	137.92	345	Protector
	359	TUBING 4-1/2", 18.9#, L-80,HSM3	346	9.531	3327.67	551.602	217.18	138.32	346	Protector
	360	TUBING 4-1/2", 18.9#, L-80,HSM3	347	9.527	3337.20	542.075	217.65	138.72	347	Protector
	361	TUBING 4-1/2", 18.9#, L-80,HSM3	348	9.527	3346.73	532.548	218.11	139.12	348	Protector
	362	TUBING 4-1/2", 18.9#, L-80,HSM3	349	9.528	3356.26	523.020	218.58	139.53	349	Protector
	363	TUBING 4-1/2", 18.9#, L-80,HSM3	350	9.531	3365.79	513.489	219.04	139.93	350	Protector
	364	TUBING 4-1/2", 18.9#, L-80,HSM3	351	9.527	3375.31	503.962	219.51	140.33	351	Protector
	365	TUBING 4-1/2", 18.9#, L-80,HSM3	352	9.530	3384.84	494.432	219.97	140.73	352	Protector
	366	TUBING 4-1/2", 18.9#, L-80,HSM3	353	9.531	3394.37	484.901	220.44	141.13	353	Protector
	367	TUBING 4-1/2", 18.9#, L-80,HSM3	354	9.535	3403.91	475.366	220.91	141.54	354	Protector
	368	TUBING 4-1/2", 18.9#, L-80,HSM3	355	9.530	3413.44	465.836	221.37	141.94	355	Protector
	369	TUBING 4-1/2", 18.9#, L-80,HSM3	356	9.525	3422.96	456.311	221.84	142.34	356	Protector
	370	TUBING 4-1/2", 18.9#, L-80,HSM3	357	9.532	3432.50	446.779	222.30	142.74	357	Protector
	371	TUBING 4-1/2", 18.9#, L-80,HSM3	358	9.829	3442.33	436.950	222.78	143.16	358	Protector
	372	TUBING 4-1/2", 18.9#, L-80,HSM3	359	9.201	3451.53	427.749	223.23	143.55	359	Protector
	373	TUBING 4-1/2", 18.9#, L-80,HSM3	360	9.531	3461.06	418.218	223.70	143.95	360	Protector
	374	TUBING 4-1/2", 18.9#, L-80,HSM3	361	9.525	3470.58	408.693	224.16	144.35	361	Protector
	375	TUBING 4-1/2", 18.9#, L-80,HSM3	362	9.528	3480.11	399.165	224.63	144.76	362	Protector
	376	TUBING 4-1/2", 18.9#, L-80,HSM3	363	9.526	3489.64	389.639	225.09	145.16	363	Protector
	377	TUBING 4-1/2", 18.9#, L-80,HSM3	364	9.402	3499.04	380.237	225.55	145.55	364	Protector
	378	TUBING 4-1/2", 18.9#, L-80,HSM3	365	9.415	3508.45	370.822	226.01	145.95	365	Protector
	379	TUBING 4-1/2", 18.9#, L-80,HSM3	366	9.410	3517.86	361.412	226.47	146.35	366	Protector
	380	TUBING 4-1/2", 18.9#, L-80,HSM3	367	9.521	3527.38	351.891	226.93	146.75	367	Protector
	381	TUBING 4-1/2", 18.9#, L-80,HSM3	368	9.526	3536.91	342.365	227.40	147.15	368	Protector
	383	TUBING 4-1/2", 18.9#, L-80,HSM3	369	9.526	3546.44	332.839	227.86	147.56	369	Protector
	386	TUBING 4-1/2", 18.9#, L-80,HSM3	370	9.527	3555.96	323.312	228.33	147.96	370	Protector
	387	TUBING 4-1/2", 18.9#, L-80,HSM3	371	9.533	3565.50	313.779	228.79	148.36	371	Protector
	388	TUBING 4-1/2", 18.9#, L-80,HSM3	372	9.535	3575.03	304.244	229.26	148.76	372	Protector
	391	TUBING 4-1/2", 18.9#, L-80,HSM3	373	9.182	3584.21	295.062	229.71	149.15	373	Protector


396	TUBING 4-1/2", 18.9#, L-80,HSM3	374	9.142	3593.36	285.920	230.15	149.54	374	Protector
397	TUBING 4-1/2", 18.9#, L-80,HSM3	375	9.527	3602.88	276.393	230.62	149.94	375	Protector
398	TUBING 4-1/2", 18.9#, L-80,HSM3	376	9.534	3612.42	266.859	231.09	150.34	376	Protector
399	TUBING 4-1/2", 18.9#, L-80,HSM3	377	9.542	3621.96	257.317	231.55	150.75	377	Protector
400	TUBING 4-1/2", 18.9#, L-80,HSM3	378	9.535	3631.49	247.782	232.02	151.15	378	Protector
401	TUBING 4-1/2", 18.9#, L-80,HSM3	379	9.536	3641.03	238.246	232.48	151.55	379	Protector
402	TUBING 4-1/2", 18.9#, L-80,HSM3	380	9.529	3650.56	228.717	232.95	151.95	380	Protector
403	TUBING 4-1/2", 18.9#, L-80,HSM3	381	9.531	3660.09	219.186	233.41	152.36	381	Protector
404	TUBING 4-1/2", 18.9#, L-80,HSM3	382	9.533	3669.62	209.653	233.88	152.76	382	Protector
405	TUBING 4-1/2", 18.9#, L-80,HSM3	383	9.559	3679.18	200.094	234.35	153.16	383	Protector
406	TUBING 4-1/2", 18.9#, L-80,HSM3	384	9.528	3688.71	190.566	234.81	153.56	384	Protector
410	TUBING 4-1/2", 18.9#, L-80,HSM3	385	9.532	3698.24	181.034	235.28	153.97	385	Protector
414	TUBING 4-1/2", 18.9#, L-80,HSM3	386	9.531	3707.77	171.503	235.74	154.37	386	Protector
415	TUBING 4-1/2", 18.9#, L-80,HSM3	387	9.529	3717.30	161.974	236.21	154.77	387	Protector
418	TUBING 4-1/2", 18.9#, L-80,HSM3	388	9.529	3726.83	152.445	236.67	155.17	388	Protector
419	TUBING 4-1/2", 18.9#, L-80,HSM3	389	9.527	3736.36	142.918	237.14	155.58	389	Protector
421	TUBING 4-1/2", 18.9#, L-80,HSM3	390	9.287	3745.64	133.631	237.59	155.97	390	Protector
422	TUBING 4-1/2", 18.9#, L-80,HSM3	391	9.526	3755.17	124.105	238.06	156.37	391	Protector
423	TUBING 4-1/2", 18.9#, L-80,HSM3	392	9.527	3764.70	114.578	238.52	156.77	392	Protector
424	TUBING 4-1/2", 18.9#, L-80,HSM3	393	9.530	3774.23	105.048	238.99	157.18	393	Protector
425	TUBING 4-1/2", 18.9#, L-80,HSM3	394	9.528	3783.76	95.520	239.45	157.58	394	Protector
426	TUBING 4-1/2", 18.9#, L-80,HSM3	395	9.533	3793.29	85.987	239.92	157.98	395	Protector
434	TUBING 4-1/2", 18.9#, L-80,HSM3	396	9.528	3802.82	76.459	240.38	158.38	396	Protector
435	TUBING 4-1/2", 18.9#, L-80,HSM3	397	9.526	3812.34	66.933	240.85	158.79	397	Protector
PUP JOINT 4 1/2",HSM3 ,18.9#, L-80, Type-1	PUP JOINT 4 1/2",HSM3		1.623	3813.97	65.310	240.93	158.85		
4-1/2" FLOW COUPLING, 18.9#,SUPER 13CR-110KSI,HSM3 , 4' FT, WEIQIXIN Co	Short Flow Coupling		1.117	3815.08	64.193	240.98	158.90		
TRSSV-10 Tubing Retrievable Saftey Valve, 4 1/2", 18.9# W/ 3.437" Seal bore,HSM3 , SUPER 13CR-110KSI, 10K WP With AF Profile, Flapper Type, WEIQIXIN Co	TRSSV		1.785	3816.87	62.408	241.07	158.98		
4-1/2" FLOW COUPLING,18.9#,SUPER 13CR-110KSI,HSM3 , 6 FT, WEIQIXIN Co	Long Flow Coupling		1.725	3818.59	60.683	241.15	159.05		
PUP JOINT 4 1/2",HSM3 ,18.9#, L-80, Type-1	PUP JOINT 4 1/2",HSM3		1.623	3820.22	59.060	241.23	159.12		
457	TUBING 4-1/2", 18.9#, L-80,HSM3	398	9.406	3829.62	49.654	241.69	159.52	398	Press Test/Protector
458	TUBING 4-1/2", 18.9#, L-80,HSM3	399	9.298	3838.92	40.356	242.14	159.91	399	Protector
462	TUBING 4-1/2", 18.9#, L-80,HSM3	400	9.418	3848.34	30.938	242.60	160.31	400	Protector
463	TUBING 4-1/2", 18.9#, L-80,HSM3	401	9.531	3857.87	21.407	243.07	160.71	401	Protector
464	TUBING 4-1/2", 18.9#, L-80,HSM3	402	9.278	3867.15	12.129	243.52	161.10	402	Protector
4-1/2" FLUTED SWAGE ADAPTER D/P, 18.9# TPCQ-EX PIN ON TOP X HSM3 PIN ON DOWN* SUPER 13CR-110KSI, WEIQIXIN Co	Fluted Swage		1.019	3868.17	11.110	243.57	161.14		
TBG HANGER MSP, 10K, 11" * 4 1/2" ACME Box up * 4 1/2" TPCQ-EX Box Down , M/C: FF-0.5 T/C: UPSL: 3G PR: 2, 4" Type "H" Two Way	TBG HGR		0.560	3868.73	10.550	243.60	161.17		
Tubing Hanger Running Tool	Tubing Hanger Running Tool		0.230	3868.96	10.320	243.61	161.18		
L/Joint	L/Joint		11.234	3880.19	-0.914	244.16	161.65		Final Press Test


Figure 8-19: AZNS-207 Completion Tally

8.8 Completion String Pressure Test

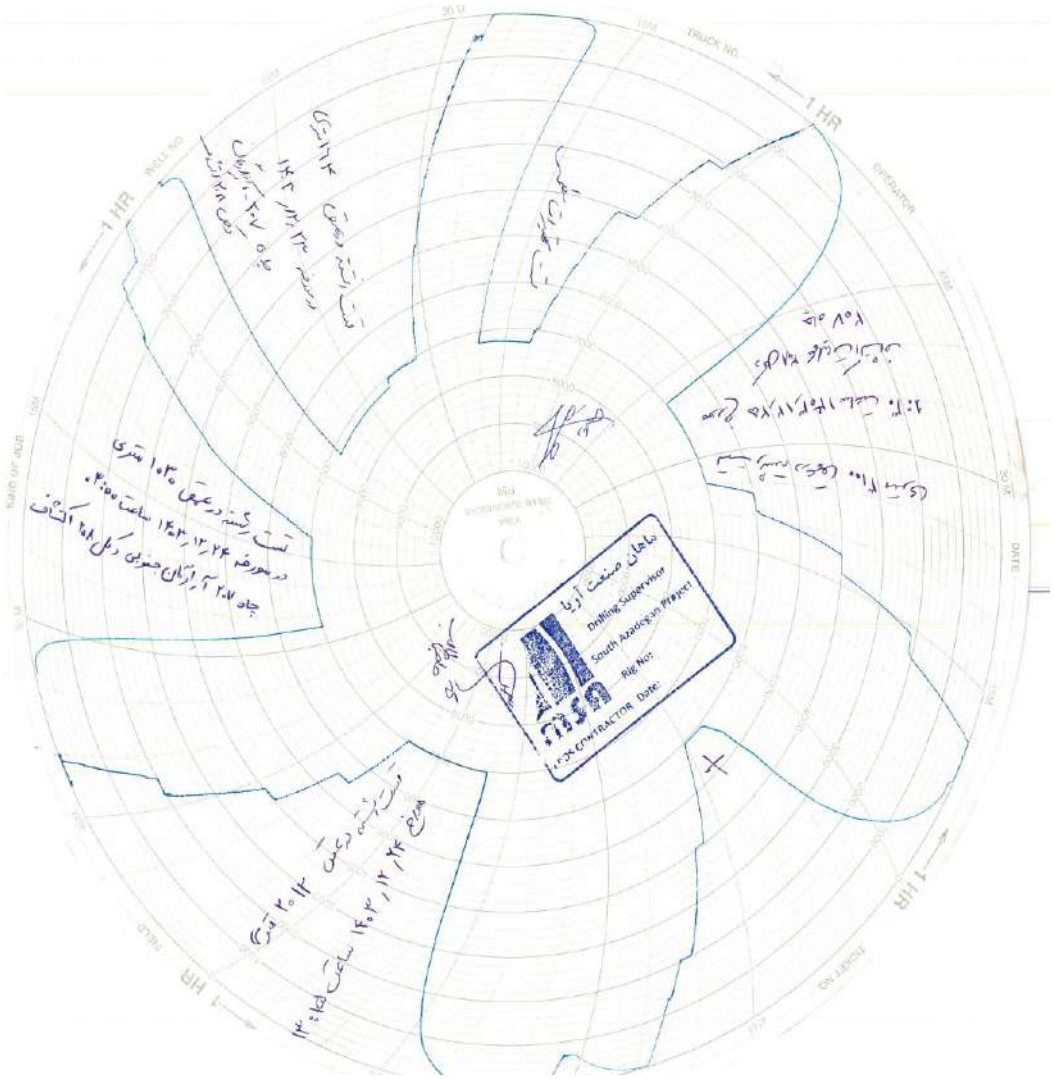

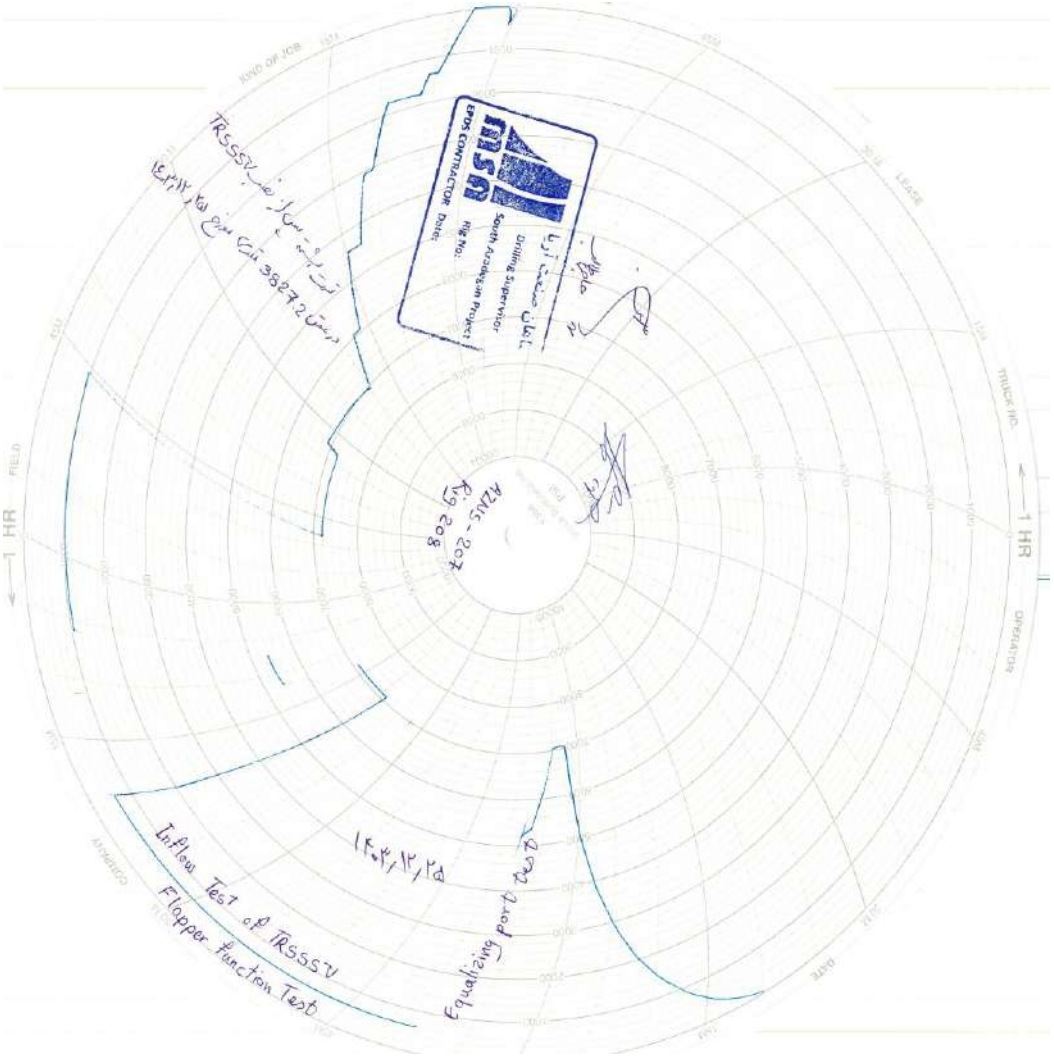
Inflow Test of TRSSSV
Flapper function Test
Equalizing port test
AZNS - 207
Rig 208
1 HR
1 HR

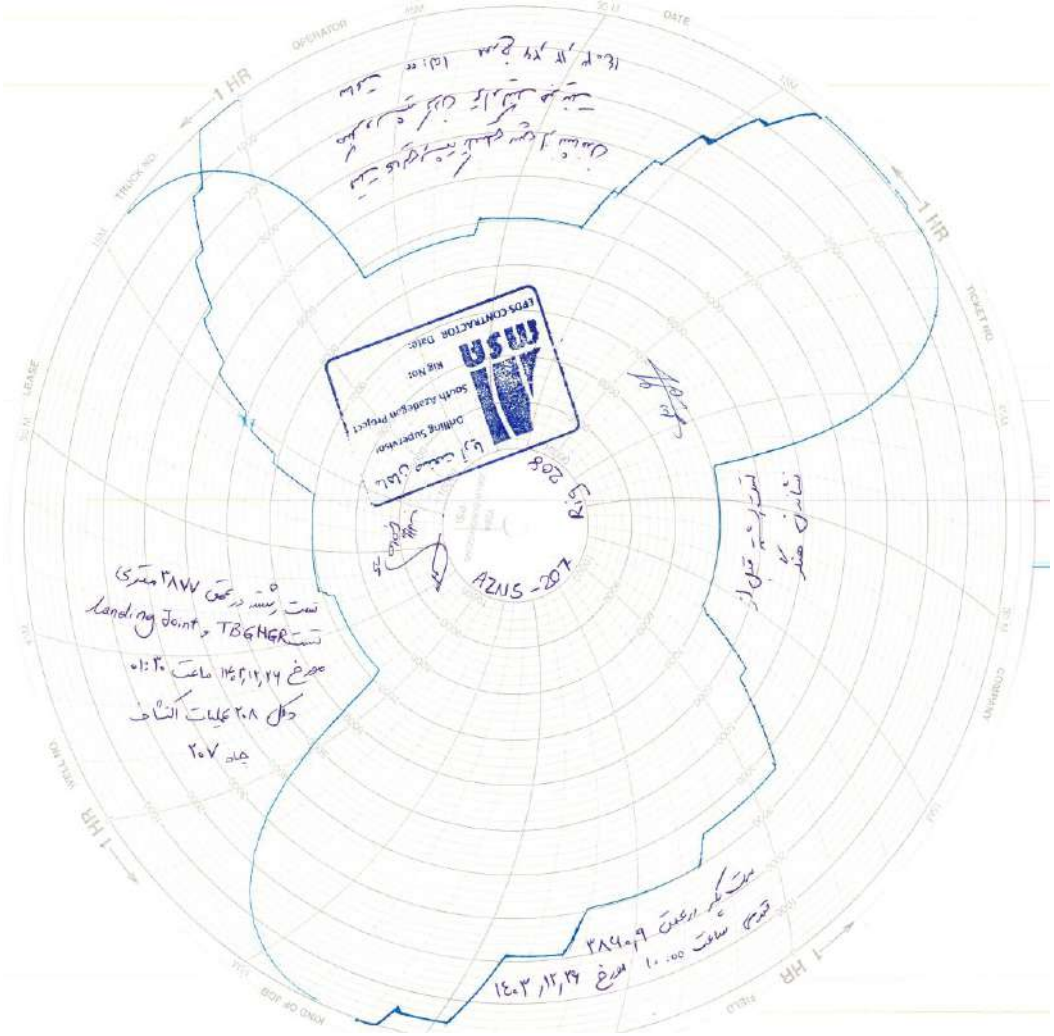
AZNS -207

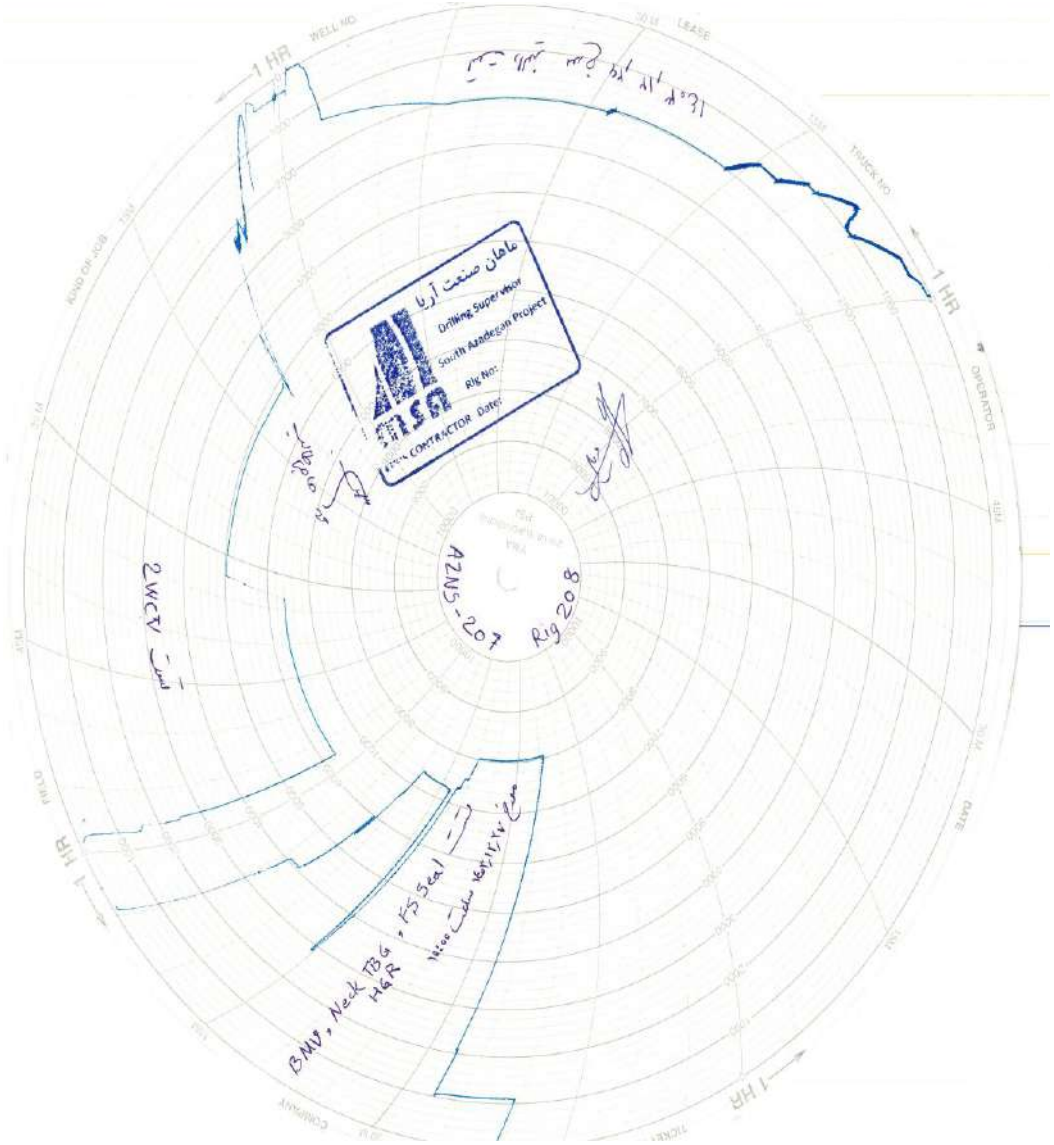
Drilling Supervisor
South Azadegan Project
Rig No:
Date:
AZNS-207
Rig 208

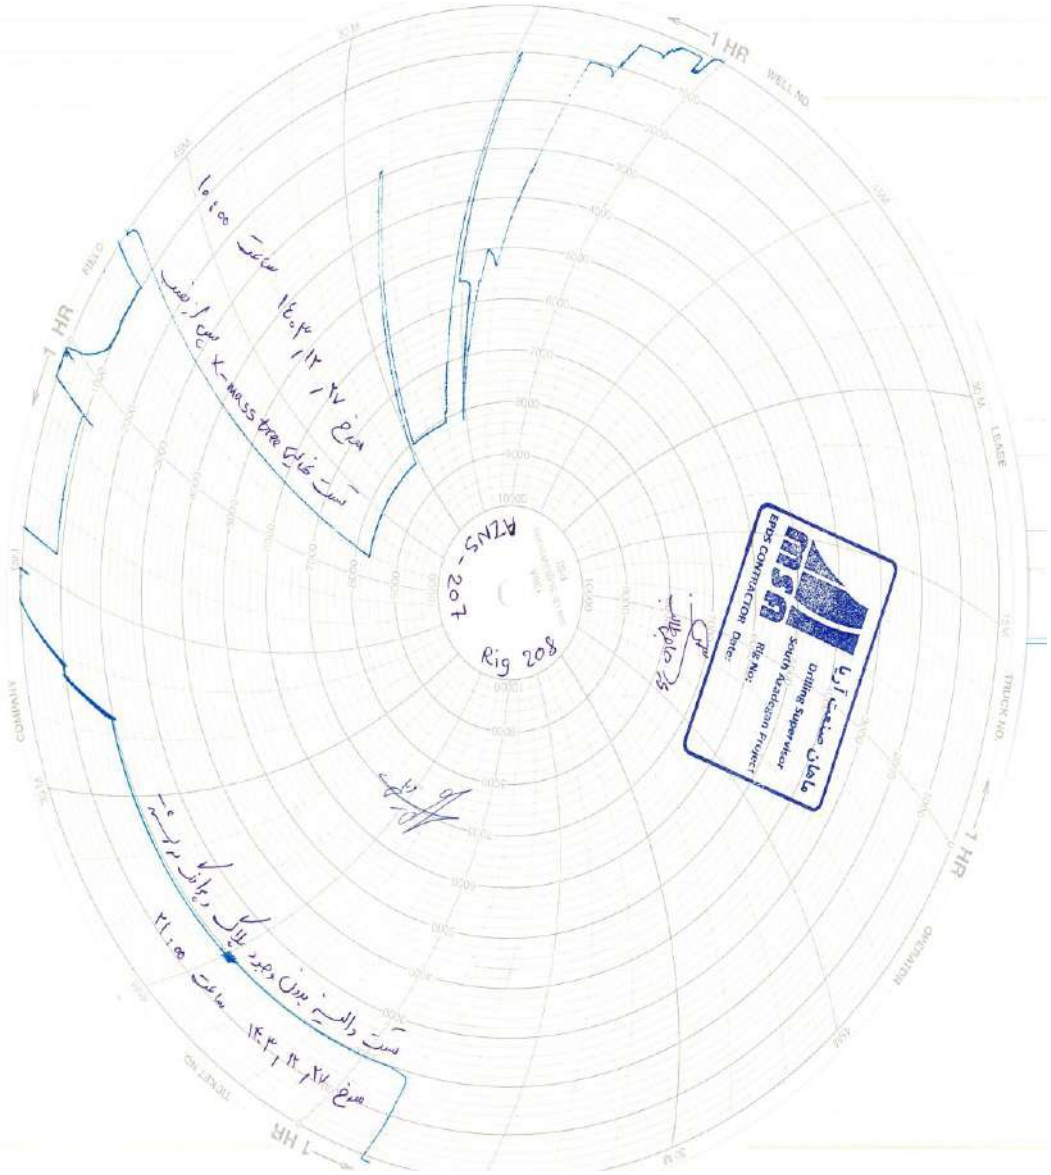


Figure 8-20: AZNS-207 Tubing Pressure Test Grap

9. Wellhead Report

9.1 Final Well Status

Well Head

Item	Specification (size, pressure rating, M/C)	Test Pressure	Test Duration
MSP C.H.H	20-3/4'' 3K, DD-0.5 PSL1, PR1	2500 psi	10 MIN
MSP C.H.S	20-3/4'' 3K * 13-5/8'' 5K , DD-0.5, PSL1, PR1	4500 psi	10 MIN
MSP T.H.S.	13-5/8'' 5K * 11''-10K, FF-0.5, PSL3, PR2	7500 psi	10 MIN
MSP X-MASS TREE(BTM)	4-1/16''-10K, FF-0.5, PSL3G, PR2	8000 psi	15 MIN

Wellbore Completion Fluids

Well bore	Fluid Type	Weight (pcf)
Cased Hole	CABR2	103-104

Well Head Pressure Record

Annulus	Pressure (psi)	Date / Time
Wellhead	0	1403.12.27
Tubing- 9 5/8"	0	1403.12.27
9 5/8" – 13 3/8"	0	1403.12.27
13 3/8" – 20"	0	1403.12.27

Barriers

Barrier Type	Depth	Pressure Test	Date Tested
Close TRSSSV	62.4 m	500 psi (inflow test after finish flow the well)	1403.12.26

Temporary Installed Equipment:

Table 9-1: AZNS-207 Status

9.2 Wellhead & X-mass tree Specification

Well Type	Specification	Check and Remark
MSP Co. Well Head 10000 Psi for Fahliyan Wells	**TUBING HEAD ADAPTOR** BOTTOM STUDDED FLANGE 11", 10000 PSI, BX158 TOP STUDDED FLANGE 4-1/16" 10000 PSI BX155 FULL BORE PREPARED WITH TWO S-SEAL AND ONE METAL TO METAL SEAL TO PACK TOP NECK OF TUBING HANGER C/W RELATED TEST AND INJECTION PORTS PREPARTION. C/W TWO CONTINUOUS FEED THROUGH TYPE 1/4" NPT CONTROL LINE EXITS PREPARTION (ONE FOR 1/4" TRSSSV CL AND ONE FOR 1/4" DOWNHOLE PRESSURE GAUGE) AND TWO 3/8" NPT CONTINUOUS FEED THROUGH TYPE LINE PORTS FOR CHEMCIAL INJECTION LINE EXIT INCLUDING RELATED SWAGE LOCK FITTINGS C/WITH ONE 4-1/16", 10K WP FULL BORE MANUAL GATE VALVE FORGED BODY AND BONNET, ALLOY STAINLESS STEEL 410SS GATE & SEAT AISI 410 COATED WITH TUNGSTEN CARBIDE USING HVOF METHOD STEM: INCONEL 718 WITH BACK SEAT CAPABILITY, NON RISING STEM METAL TO METAL SEAL BETWEEN SEAT AND GATE C/W HAND WHEEL FORGED BODY ALLOY STEEL AISI 410 MAXIMUM HEIGHT: 800MM M/C: FF-0.5 T/C: U PSL:3G PR:2 CROSS T-TYPE SOLID BLOCK CROSS T-TYPE SOLID BLOCK, BOTTOM FLANGED 4-1/16" API 10000 PSI WP TOP FLANGED STUDDED 4-1/16" API 10000 PSI WP FOR TREE CAP WITH TWO STUDDED SIDE OUTLETS 4-1/16" 10000PSI WP ELEVATED AT 900 DEG AND TWO 4-1/16", 10000 PSI MANUAL GATE VALVE AT THE TOP AND BOTTOM AND ONE 4-1/16", 10000 PSI WP SAFETY VALVE EQUIPPED WITH HYDRAULIC WIRE CUT ACTUATOR	

	AS UPPER MASTER VALVE MATERIAL OF BODY, BONNET: AISI 410 SEAT, GATE: AISI 410SS HARD FACED WITH TUNGSTEN CARBIDE UASING HVOP METHOD MATERIAL OF STEM: INCONEL 718 M/C: FF-0.5 T/C: U PSL:3G PR:2G. MANUAL GATE VALVE API 4-1/16" 10000 PSI WP. FLANGED ENDS AND FULL BORE METAL TO METAL SEAL BETWEEN BODY/SEAT/GATE WITH BACK SEAT CAPABILITY, NON RISING STEM C/W HANDWHEELS MATERIAL OF BODY, BONNET, SEAT, GATE: AISI 410SS MATERIAL OF STEM: INCONEL 718 GATE&SEAT HARD FACED WITH TUNGSTEN CARBIDE BY HOVF METHOD M/C: FF-0.5 T/C: U PSL:3G PR:2 X-MAS TREE CAP 4-1/16" API 10000 PSI WP, FLANGED BOTTOM (4-1/16", BORE) 8-3/8"-4ACME-2G THREAD TOP, BLANKING PLUG TAPPED WITH 1/2" NPT THREAD, FORGED BODY, MATERIAL: STAINLESS STEEL 410 M/C: FF-0.5 T/C: U PSL:3G PR:2	

Table 9-2: AZNS-207 Wellhead Specification

9.3 Wellhead sketch

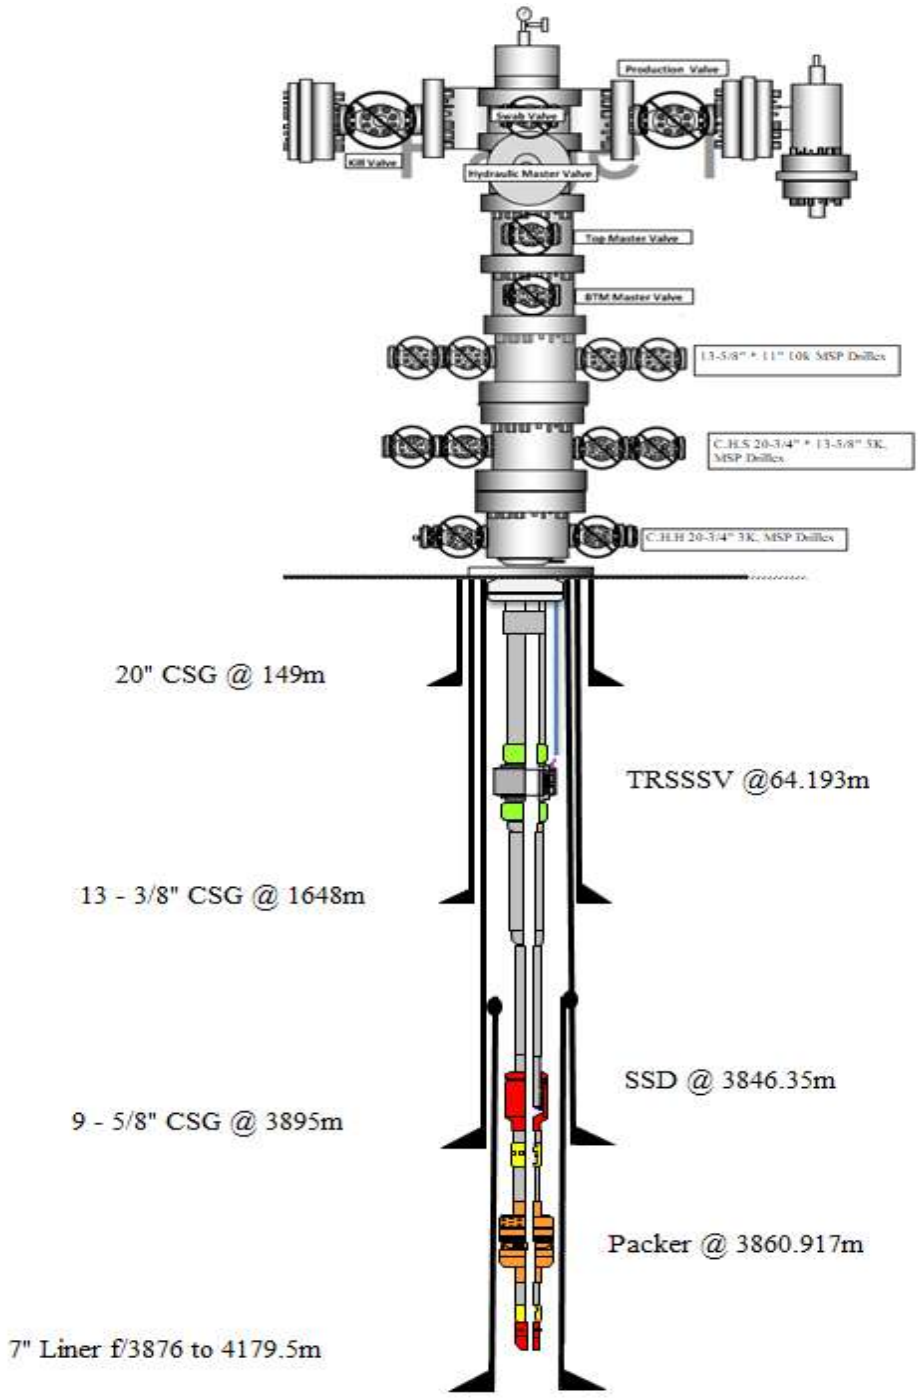


Figure 9-1: AZNS-207 Wellhead Sketch

X-mass Tree Specification (Section D)

Item	Equipment	M/C	T/C	PSL	Qty
1	BTM Master Valve 11" * 4 1/16" 10K	FF-0.5	U	3G	1
2	TOP Master Valve 4 1/16" 10K	FF-0.5	U	3G	1
3	Surface Safety Valve 4 1/16" 10K	FF-0.5	U	3G	1
4	Deeping Valve 4 1/16" 10K	FF-0.5	U	3G	1
5	Wing gate valve-1 (Kill Valve) 4 1/16" 10K	FF-0.5	U	3G	1
6	Wing gate valve-2 (production valve) 10K	FF-0.5	U	3G	1
7	41/16" Choke valve 4 1/16" 10K	FF-0.5	U	3G	1
8	X Mass Tree	FF-0.5	U	3G	1

Table 9-3: AZNS-207 Section "D" Specification

9.4 X-mass Tree Pressure Test Report (Section D – before install)

Item	Test	Check Mark and Result
1	Pressure test for the kill Valve W/ 1000 & 8000 Psi / 15 min	OK
2	Pressure test for the SSV W/ 1000 & 8000 Psi / 15 min	OK
3	Pressure test for the top master valve W/ 1000 & 8000 Psi / 15 min	OK
4	Pressure test for Swab valve W/ 1000 & 8000 Psi / 15 min	OK
5	Pressure test for the Production valve W/ 1000 & 8000 Psi / 15 min	OK

Table 9-4: AZNS-207 Section "D" Pressure Test Before Installation

9.5 X-mass Tree Pressure Test Report (Section D – after install)

Item	Test	Check mark and Result
1	Pressure test X-MAS TREE solid block and bottom section w/ 1000 & 8000 psi for 15min	OK
2	Pressure test for the SSV Exit block W/ 8000 Psi / 15 min	OK
3	Pressure test neck of tubing hanger metal seal W/1000 &8000 psi for 15min	OK

4	Pressure test for Swab valve W/ 8000 Psi / 15 min	OK
5	Pressure test for Production valve W/8000 Psi / 15 min	OK
6	Pressure test cavity of FS.seal and Ring Gasket W 8000 Psi / 15 min	OK
7	Pressure test CIV line to 2000psi	OK

Table 9-5: AZNS-207 Section "D" Pressure Test After Installation

9.6 Wellhead Related Test Report

(Tehran Energy Consultants)

Wellhead and X-Mas Tree Checklist

Well Number :	207	Well Pad Number:	93	Date:

	C.H.H	Y/N (√/ x)	INSTALL	REMARK
C.H.H (manufacturer & PR)	ONE 2 1/16" GATE VALVE	√	√	
	ONE 1 1/2" VR PLUG	X	X	
	TWO 2 1/16" COMP. FLG	√	√	
	ONE 2" BULL PLUG TAPPED THREAD 1/2" NPT	√	√	
	ONE 2" BULL PLUG (BLIND)	√	√	
	ONE N. VALVE	√	√	
	ONE PIPE PLUG	√	X	
	ONE PRESSURE GAUGE	√	√	
	ANNULUS PRESSURE			
	ALL HANDWHEELS HAVE BEEN INSTALLED IN PLACE	√	√	
	NUT AND BOLT HAVE BEEN INSTALLED IN PLACE	√	√	TOTAL NUTS & BOLTS WHICH SHOULD BE INSTALLED: ACTUAL NUTS & BOLTS WHICH HAVE BEEN INSTALLED:
	SIDE OUTLET VALVES HAVE BEEN OPERATED PROPERLY	√		

	C.H.S	Y/N (√/ x)	INSTALL	REMARK
C.H.S (manufacturer & PR)	TWO 2 1/16" GATE VALVE	√	√	
	ONE 1 1/2" VR PLUG	X	X	
	TWO 2 1/16" COMP. FLG	√	√	
	TWO 2" BULL PLUG TAPPED THREAD 1/2" NPT	√	√	
	ONE N. VALVE	√	√	
	ONE PIPE PLUG	√	√	
	ONE PRESSURE GAUGE	√	√	
	ANNULUS PRESSURE			
	ALL HANDWHEELS HAVE BEEN INSTALLED IN PLACE	√	√	
	NUT AND BOLT HAVE BEEN INSTALLED IN PLACE	√	√	TOTAL NUTS & BOLTS WHICH SHOULD BE INSTALLED: ACTUAL NUTS & BOLTS WHICH HAVE BEEN INSTALLED:
	SIDE OUTLET VALVES HAVE BEEN OPERATED PROPERLY	√		

	T.H.S	Y/N (√/ x)	INSTALL	REMARK
T.H.S (manufacturer & PR)	FOUR 2 1/16" GATE VALVE	√	√	
	ONE 1 1/2" VR PLUG	X	X	
	TWO 2 1/16" COMP FLG	√	√	
	TWO 2" BULL PLUG TAPPED THREAD 1/2" NPT	√	√	
	TWO PIPE PLUG	√	√	
	ONE 2 1/16" INSTRUMENT FLG WITH FOUR 1/2" NPT PORT & 4 PIPE PLUGS	√	√	3 No. installed & 1 No. Delivered to client.
	ONE PRESSURE GUAGE ON INSTRUMENT FLG	√	√	
	ONE N. VALVE ON INSTRUMENT FLG	√	√	
	ANNULUS PRESSURE			
	ALL HANDWHEELS HAVE BEEN INSTALLED IN PLACE	√	√	
	NUT AND BOLT HAVE BEEN INSTALLED IN PLACE	√	√	TOTAL NUTS & BOLTS WHICH SHOULD BE INSTALLED: ACTUAL NUTS & BOLTS WHICH HAVE BEEN INSTALLED:
	SIDE OUTLET VALVES HAVE BEEN OPERATED PROPERLY	√		

Signatures:

PPL Production Representative	TEC Production Operation Supervisor	Contractor Representative

South Azadegan Project Production Dept. PETROPARS

1404.05.29

ماهان صنعت آرا
Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR Date:

(Tehran Energy Consultants)

Wellhead and X-Mas Tree Checklist

Well Number :	Well Pad Number:		Date:

	X-MASS TREE	Y/N (√/x)	INSTALL	REMARK
X-MASS TREE (manufacturer & PR)	ADJUSTABLE/FIXED CHOKE VALVE	√	√	
	CHECK VALVE JUST FOR WATER DISPOSAL WELL	X	X	
	ONE COMP FLG (ON KILL LINE)	√	√	
	ONE 2" HULL PLUG TAPPED THREAD 1/2" NPT	√	√	
	ONE N. VALVE ON TREE CAP	√	√	
	ONE PRESS. GAUGE ON TREE CAP	√	√	
	ONE PIPE PLUG	√	X	
	4 1/16 INSTRUMENT FLG (BEFORE CHOKE VALVE WITH FOUR 1/2" NPT PORT & 4 PIPE PLUGS)	√	√	
	ONE PRESSURE GUAGE ON INSTRUMENT FLG	√	√	
	ONE NEEDLE VALVE ON INSTRUMENT FLG	√	√	
	4 1/16" WELD NECK FLG	√	√	
	1/4" FITTING (FOR CT) SWAGELOK	√	√	
	ONE 1/2" FITTING FOR TREE CAP	√	√	
	WELLHEAD PRESSURE			
	ALL HANDWHEELS HAVE BEEN INSTALLED IN PLACE	√	√	
	ALL NUT AND BOLT HAVE BEEN INSTALLED IN PLACE	√	√	TOTAL NUTS & BOLTS WHICH SHOULD BE INSTALLED: ACTUAL NUTS & BOLTS WHICH HAVE BEEN INSTALLED:
	SSV CAP	√	√	W/ 1 No. 1/2" N.Valve (In Open position)
	TOP MASTER VALVE HAVE BEEN OPERATED PROPERLY	√		TURNS TO BE FULLY OPERATED:
	DIPPING VALVE HAVE BEEN OPERATED PROPERLY	√		TURNS TO BE FULLY OPERATED:
	PRODUCTION VALVE HAVE BEEN OPERATED PROPERLY	√		TURNS TO BE FULLY OPERATED:
	KILL VALVE HAVE BEEN OPERATED PROPERLY	√		TURNS TO BE FULLY OPERATED:

Remarks :

1. With 6 No. Choke bean for MSP Drillex Fix Choke. (24/64", 28/64", 32/64", 36/64", 40/64", 44/64")
2.

Signatures:

PPL Production Representative	TEC Production Operation Supervisor	Contractor Representative

1404 . 05 . 29

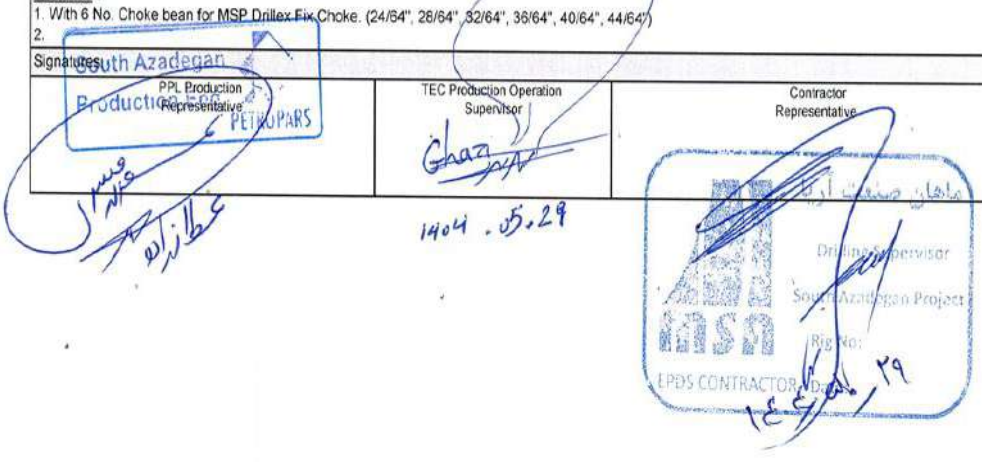


Figure 9-2: AZNS-207 Wellhead & Xmass tree Checklist

تاریخ: 1403/12/28
پیوست: دارد

بسمه تعالی

موضوع: صورتجلسه تست سطحی تاج چاه 207 آزادگان جنوبی، قبل از نصب در دکل 208 عملیات اکتشاف نفت

بدینوسیله در مورخه 1403/12/25 تست‌های سطحی تاج چاه X-Mass Tree Solid Block "T" Type 4 – 1/16" 10k, MSP DRILEX مرتبط به چاه شماره 207 آزادگان جنوبی با حضور نماینده محترم کارفرما (پتروپارس) در محل دستگاه 208 عملیات اکتشاف نفت، قبل از نصب بر روی تاج چاه به شرح ذیل انجام پذیرفت:


- Body Pressure Test of X – Mass Tree Solid Block w/ 1000^{psi}, 5min & 8000^{psi}, 15min "OK" S/N: 0269167CXC230002
- Inflow Pressure Test of 4 – 1/16" Production (WING) Valve w/ 1000^{psi}, 5min & 8000^{psi}, 15min "OK". S/N: 002929BXC230005
- Inflow Pressure Test of 4 – 1/16" Dipping (SWAB) Valve w/ 1000^{psi}, 5min & 8000^{psi}, 15min "OK". S/N: 008929KXC230002
- Inflow Pressure Test of 4 – 1/16" Kill Valve w/ 1000^{psi}, 5min & 8000^{psi}, 15min "OK" S/N: 002929BXC230001
- Inflow Pressure Test of 4 – 1/16" Surface Safety Valve w/ 1000^{psi}, 5min & 8000^{psi}, 15min "OK". S/N: XC230002
- Inflow & Out Flow Pressure Test of 4 – 1/16" Top Master Valve w/ 1000^{psi}, 5min & 8000^{psi}, 15min "OK". S/N: 008929LXC23002
- Pressure Test of 2SV Actuator w/ 2500^{psi}, 15min "OK".

– گراف مربوط به تست فشار پیوست صورتجلسه گردید.

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No:
EPDS CONTRACTOR
شرکت ماهان صنعت آریا

نماینده محترم تکمیل چاه کارفرما
شرکت نفت کیش

Figure 9-3: AZNS-207 Wellhead MOM Before Installation

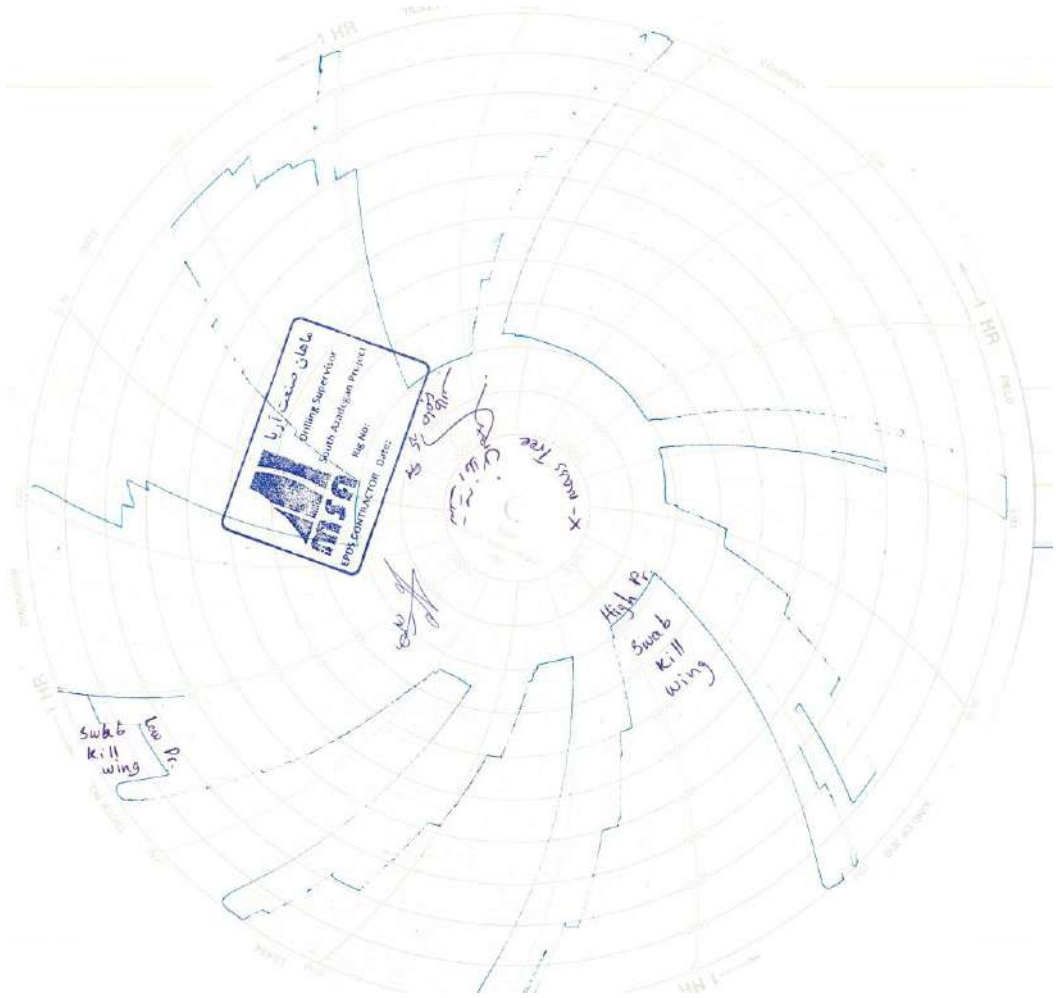
High Pr.
Swab
Kill
wing
Swab
Kill
wing

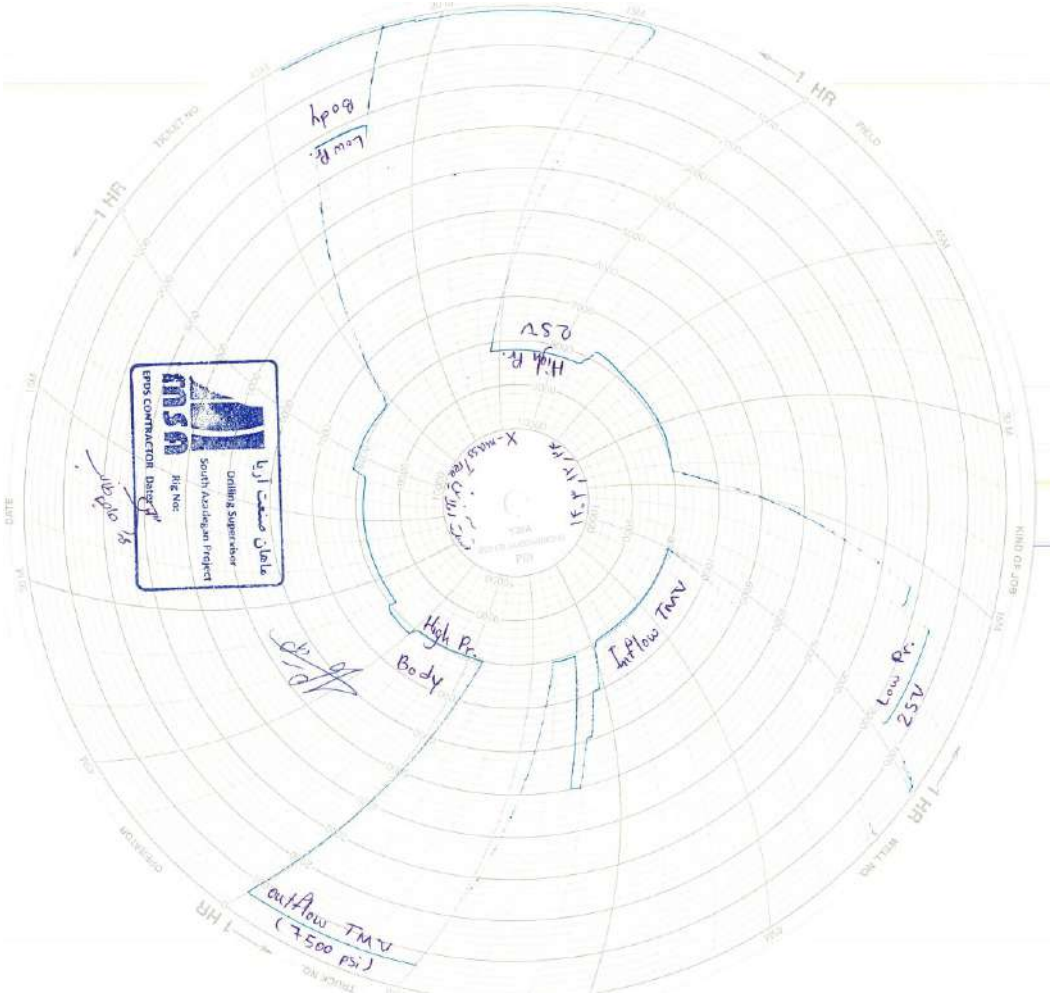


Figure 9-4: AZNS-207 X-Mass Tree Pressure Test Graph Before Installation

تاریخ: 1403/12/28
پیوست: دارد

بسمه تعالی

موضوع: صورتجلسه تست‌های پس از نصب تاج و ولهد چاه 207 آزادگان جنوبی بعد از نصب در دکل 208 عملیات اکتشاف نفت

بدینوسیله در مورخه 1403/07/28 تست‌های تاج چاه X-Mass Tree Solid Block "T" Type 4 – 1/16" 10k, MSP و ولهد چاه شماره 207 آزادگان جنوبی با حضور نماینده محترم تکمیل چاه کارفرما و نماینده عملیات حفاری ماهان DRILEX صنعت آریا در محل دستگاه حفاری 208 عملیات اکتشاف نفت بعد از نصب بر روی چاه به شرح ذیل انجام پذیرفت:

- Body Pressure Test of X – Mass Tree Solid Block w/ 10k 11" * 4 – 1/16" 10k Tubing Head Adaptor (BTM MASTER VALVE) 10k MSP/DRILEX w/ 8000psi for 15min, "OK". S/N: 0269167CXC230002
- Pressure Test TBG HGR Metal Seal to 800psi for 5min, 8000psi for 15min, "OK".
- Pressure Test F–Seal & Ring Gasket between T.H.S & Tubing Head Adaptor (BTM MASTER VALVE) to 8000psi for 15min, "OK".
- Pressure Test Neck of TBG HGR F-Seal to 8000psi for 15min, "OK".
- Pressure Test 1/4" Control Line (CL) to 8000psi for 15min, "OK".
- Pressure Test 3/8" Control Injection Lines (CIL) to 2000psi "OK".

– فشار تمامی دالیزها بررسی گردید که فشار آنها صفر بود.
– خروجی کنترل لاین شیر ایمنی درون چاهی در جهت شیر اصلی پایینی می‌باشد و همچنین CIV شماره یک در جهت ویست پیت و CIV شماره دو در خلاف جهت ویست پیت می‌باشد و همچنین بر روی دو CIV و کنترل لاین پلاگ کپ نصب گردید.
– گراف مربوط به تست فشار پیوست صورتجلسه گردید.

ماهان صنعت آریا
Drilling Supervisor
South Azadegan Project
Rig No:
Date:

نماینده محترم تکمیل چاه کارفرما
شرکت نفت کیش

شرکت ماهان صنعت آریا

Figure 9-5: AZNS-207 Wellhead MOM After Installation

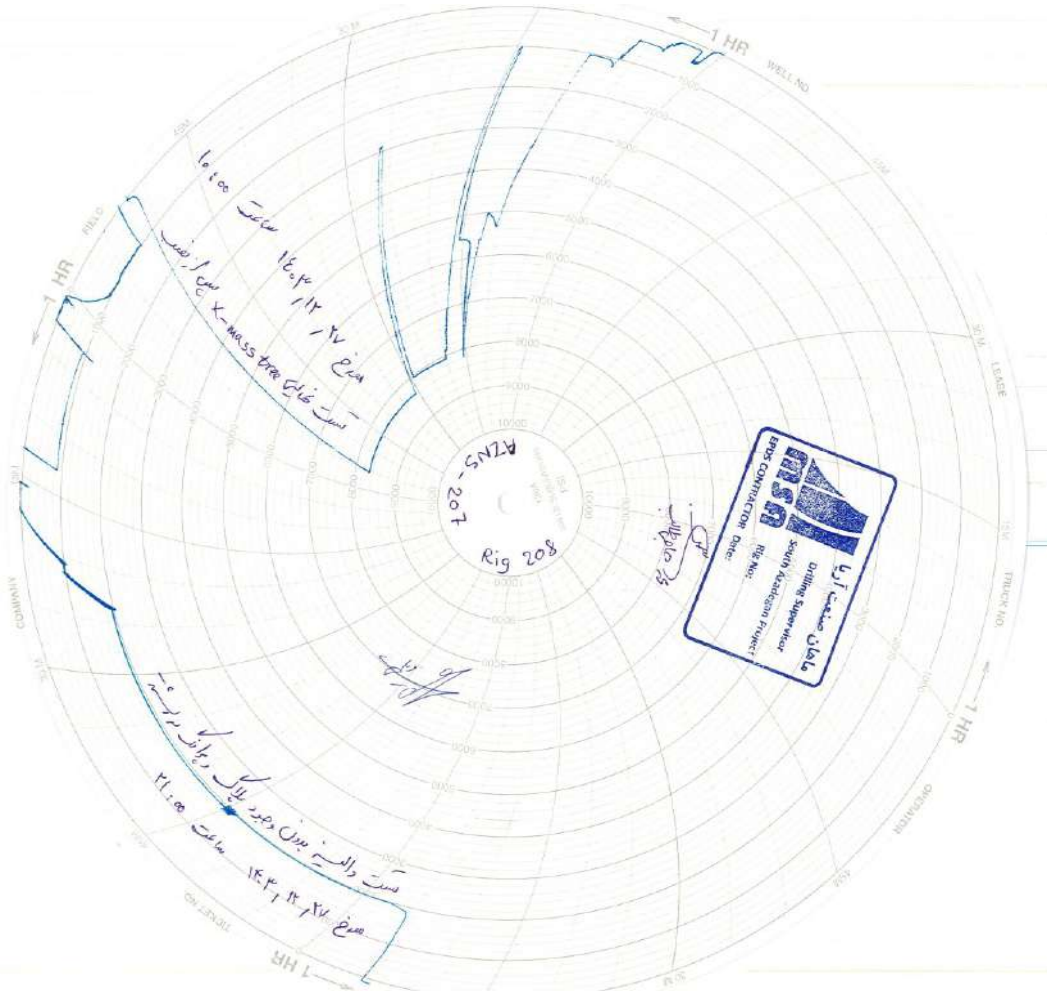


Figure 9-6: AZNS-207 Body & Metal Seal of X-Mass Tree Pressure Test Graph

10. Drilling Fluid Information

10.1 26" Hole Section

Sections Remark:

Operation Remark: The OEOC 208 spud at 15 Oct 2024 at AZNS#207 and drilling started from surface to 151 m by using 66 - 70 PCF Bentonite mud, POOH from 151 m Surface. Rig up CSG and ran 20" CSG to as per program. pumped CMT as per program successfully.

Drilling Fluid Remark: Based on program, Bentonite mud (66 – 70 pcf and 70-40 sec/qt) was used for drilling this section. Caustic soda and soda ash were used to treat water hardness and adjust ph. Suitable amount of Bentonite was added to extend mud Rheology and cutting carrying capacity index.

Interval Information:

Interval I	Surface– 151 m	26" Hole Interval	20" Casing Set at 150 meters

Drilling Fluid Type:

FLUID PROPERTIES RECAP					
KCL Pol Mud		Drilling start	Range		Drilling End
MW (min)	pcf	66	66	70.0	70.0
Funnel Viscosity	sec/qt	70	40	70	40
PV	cps	16	11	16	11
YP	lb/100sq.ft	25	18	25	18
API Fluid loss	cc	N.C	N.C	N.C	N.C
pH		11	10	11.0	10
Solid	%	4	4	7	7
Cl (NaCl)	mg/L	1,000	1,000	7,400	7,400
Total Hardness	mg/L	260	260	360	360
Ca Hardness	mg/L	120	120	240	240

Figure 10-1: AZNS-207 Fluid Properties Recap

Interval Material Consumption Analysis:

Products	Units Used	Unit wt lbs	Total wt	Effective Concentration
Bentonite	16	2,200	35,200 lbs	30.33 ppb
Soda Ash	16	55	880 lbs	0.76 ppb
Caustic Soda	16	55	880 lbs	0.76 ppb

Initial Volume	0.0 bbl
Total Volume Built	1,160.6 bbl
Volume received	0.0 bbl
Volume Returned	0.0 bbl
Total Volume Consumed	392 bbl
Volume Transfer to Next Section	768.6 bbl
Meter Drilled	151.0 m

Figure 10-2: AZNS-207 Material Consumption Analysis

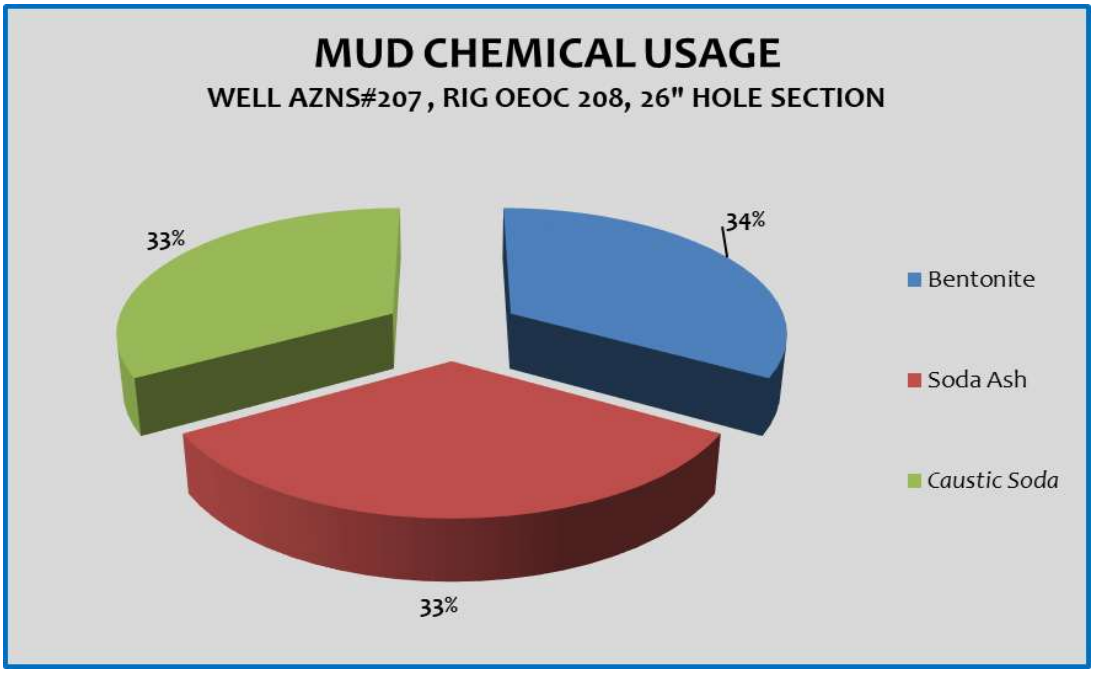


Figure 10-3: AZNS-207 Mud Chemical Usage Graph

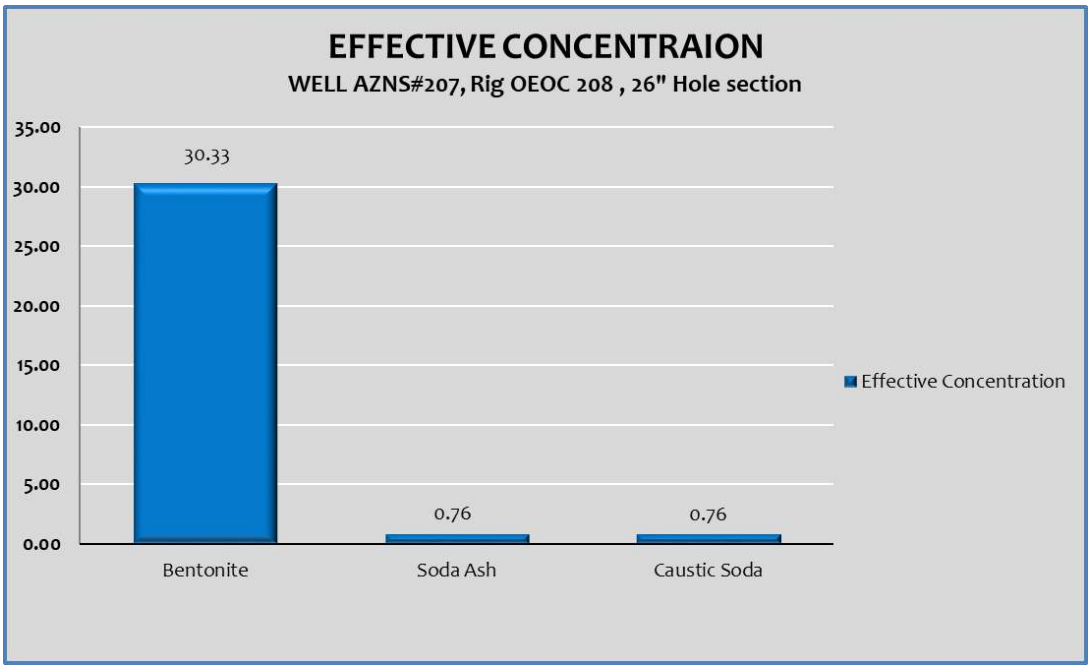


Figure 10-4: AZNS-207 Effective Concentration Chart

Interval Volume Analysis:

WELL AZNS#207, RIG OEOC 208, 26" HOLE SECTION VOLUME ANALYSIS		
Initial Volume	bbls	0.0
Received Volume	bbls	0.0
Volume Return	bbls	0.0
Volume Built	bbls	1,160.6
Surface Losses/Dumped	bbls	392.0
Formation Losses	bbls	0.0
Total Losses	bbls	392.0
Volume Transfer Out	bbls	768.6

Figure 10-5: AZNS-207 Volume Analysis Table

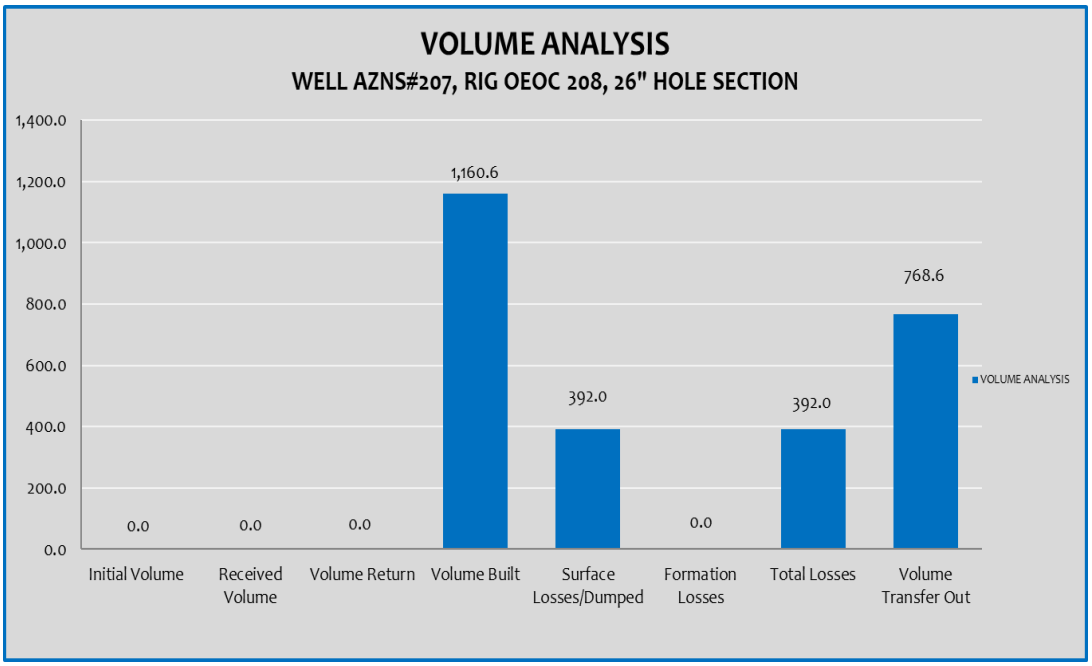


Figure 10-6: AZNS-207 Volume Analysis Chart

Interval Daily Volume Break Down:

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
15-Oct-24	01	0.0	0	0
16-Oct-24	02	492.7	0	0
17-Oct-24	03	292.5	70	0
18-Oct-24	04	375.4	286	0
19-Oct-24	05	0.0	36	0
20-Oct-24	06	0.0	0	0
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		1,160.6	392	0

Figure 10-7: AZNS-207 Daily Volume Break Down Table

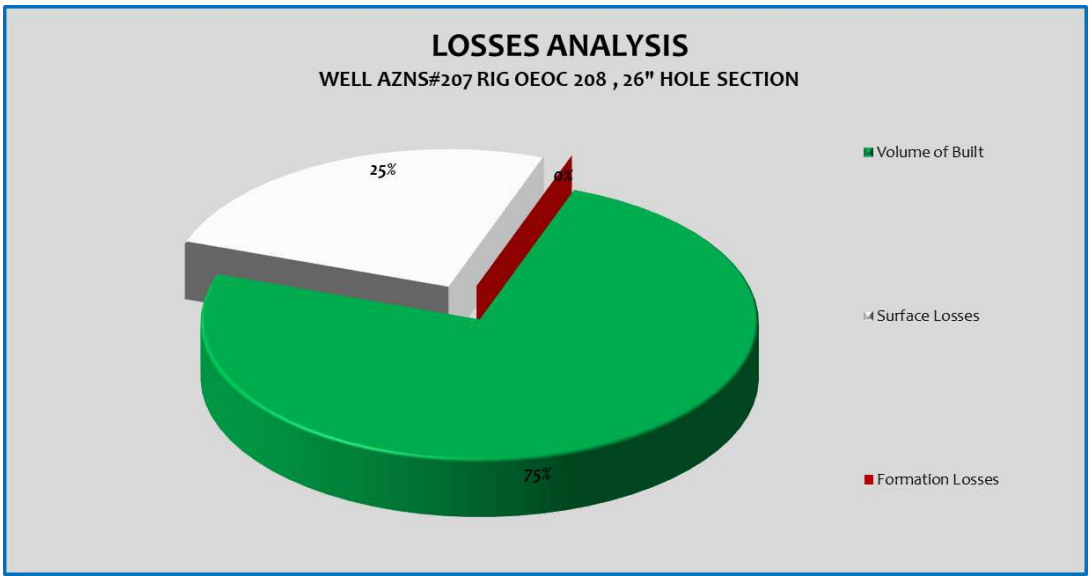


Figure 10-8: AZNS-207 Daily Volume Break Down Analysis Graph

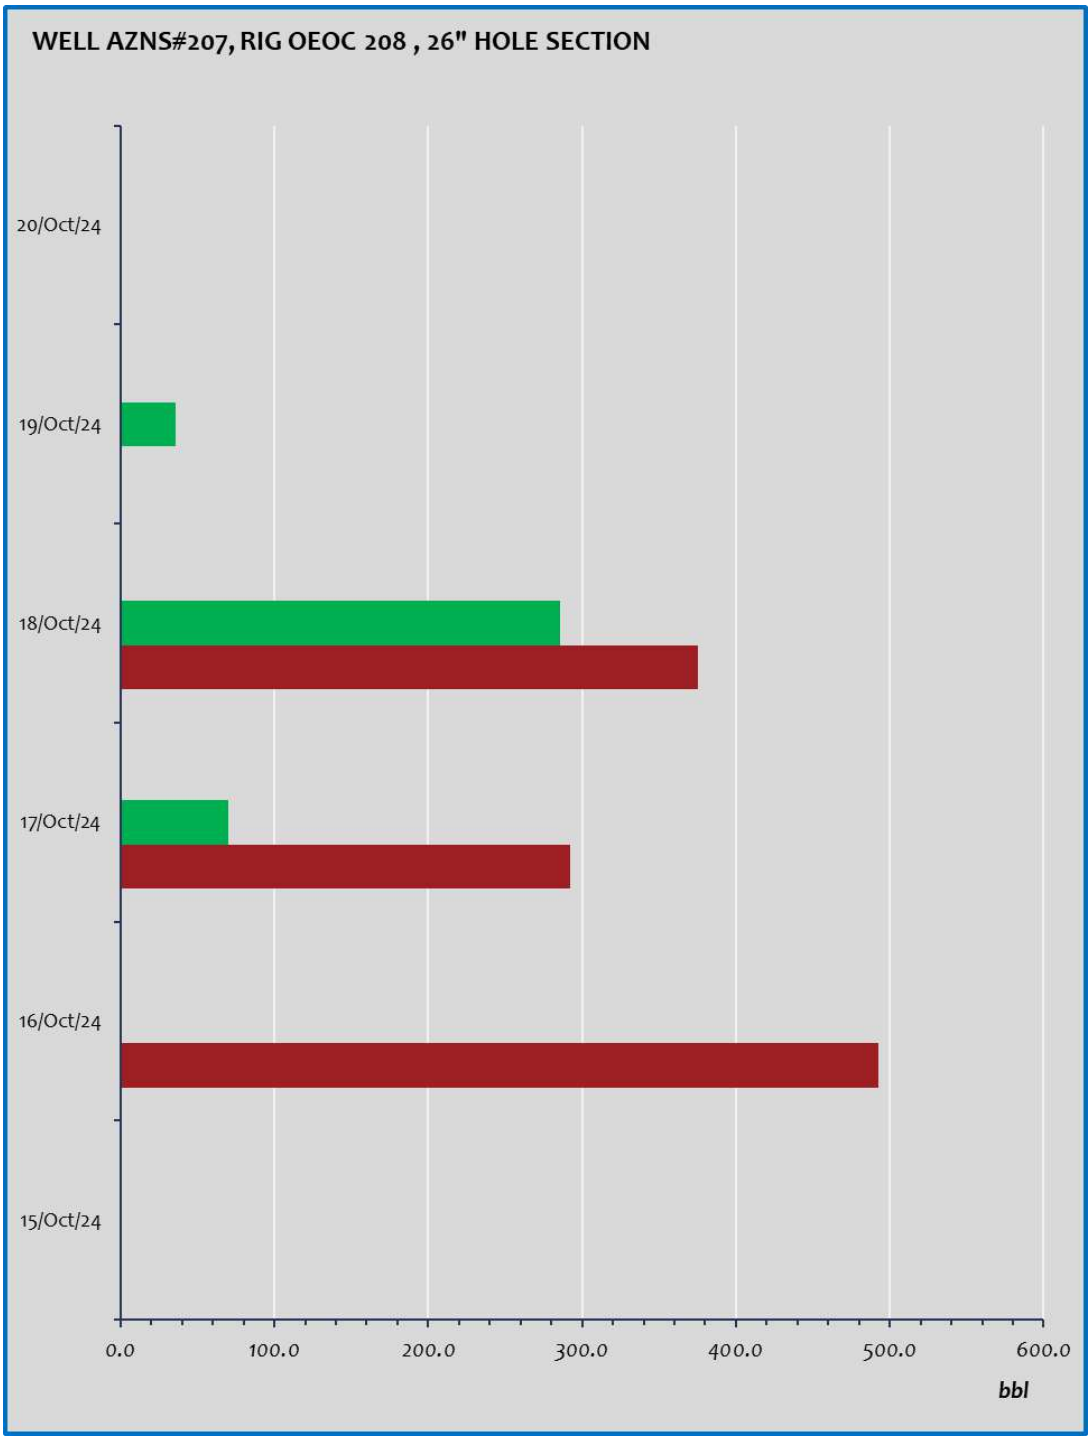


Figure 10-9: AZNS-207 Daily Volume Break Down Chart

Interval Loss Distribution:

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Mud cleaner	Trip	Pit Cleaning	Other	Formation
15-Oct-24	01	0.0	0	0	0	0	0	0	0	0	0
16-Oct-24	02	492.7	0	0	0	0	0	0	0	0	0
17-Oct-24	03	292.5	0	70	0	0	0	0	0	0	0
18-Oct-24	04	375.4	240	36	0	0	0	0	0	10	0
19-Oct-24	05	0.0	30	0	0	0	0	0	0	6	0
20-Oct-24	06	0.0	0	0	0	0	0	0	0	0	0
Total (bbl)		Volume of Built	Dump/Contaminate	Shakers	Evaporation	Centrifuge	Mud cleaner	Trip	Pit Cleaning	Other	Formation
		1,160.6	270	106	0	0	0	0	0	16	0

Figure 10-10: AZNS-207 Loss Distribution Table

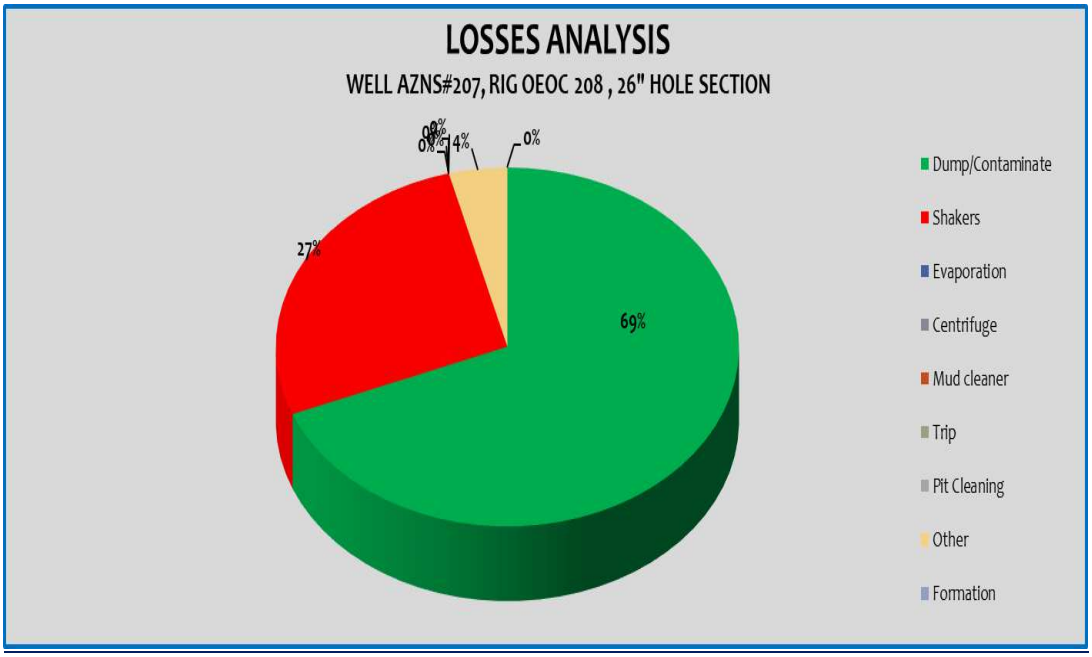


Figure 10-11: AZNS-207 Loss Analysis Graph

Interval Fluid Properties Recap:

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	Solid %	Chloride	Calcium	Total Hardness	Mud Type
15-Oct-24												
16-Oct-24	0	66	70	16	25	N.C	11	4	1000	120	260	Gel Mud
17-Oct-24	31	69	49	12	22	N.C	10	5	7400	240	360	Gel Mud
18-Oct-24	151	70	40	11	18	N.C	10	7	7400	240	360	Gel Mud
19-Oct-24	151	70	40	11	18	N.C	10.5	7	7400	240	360	Gel Mud
20-Oct-24	151	70	40	11	18	N.C	10.5	7	7400	240	360	Gel Mud
Drilling Start												
Drilling End												

Figure 10-12: AZNS-207 Interval Fluid Properties Recap

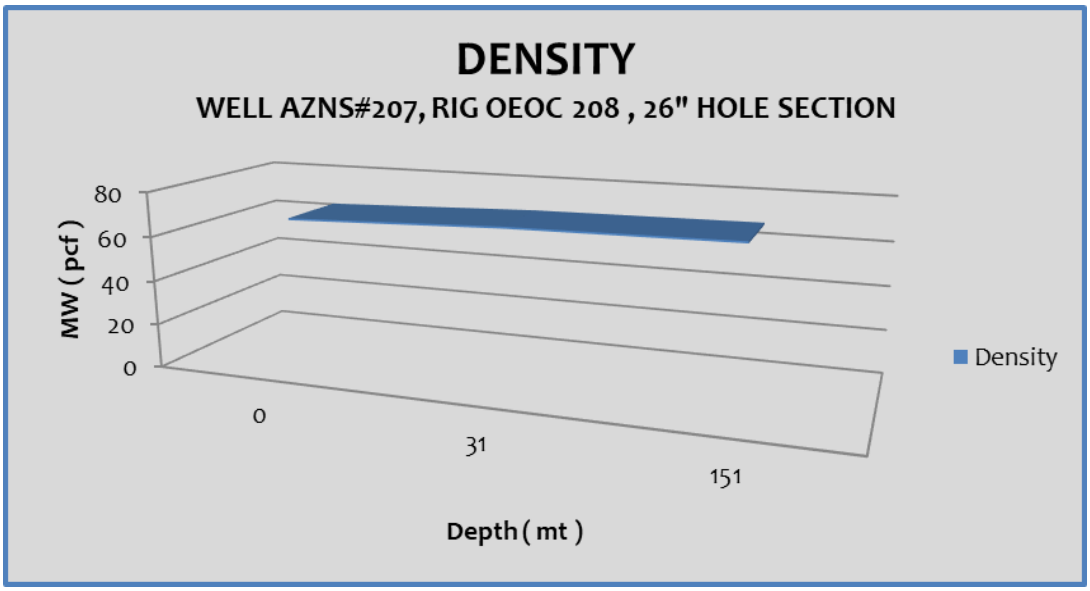


Figure 10-13: AZNS-207 Density Chart

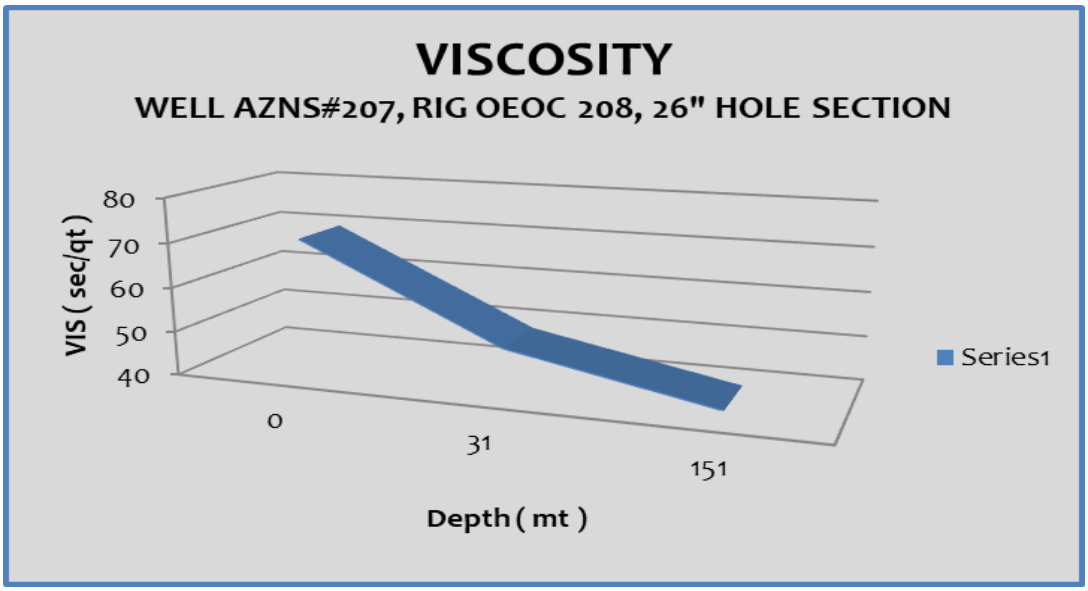


Figure 10-14: AZNS-207 Viscosity Chart

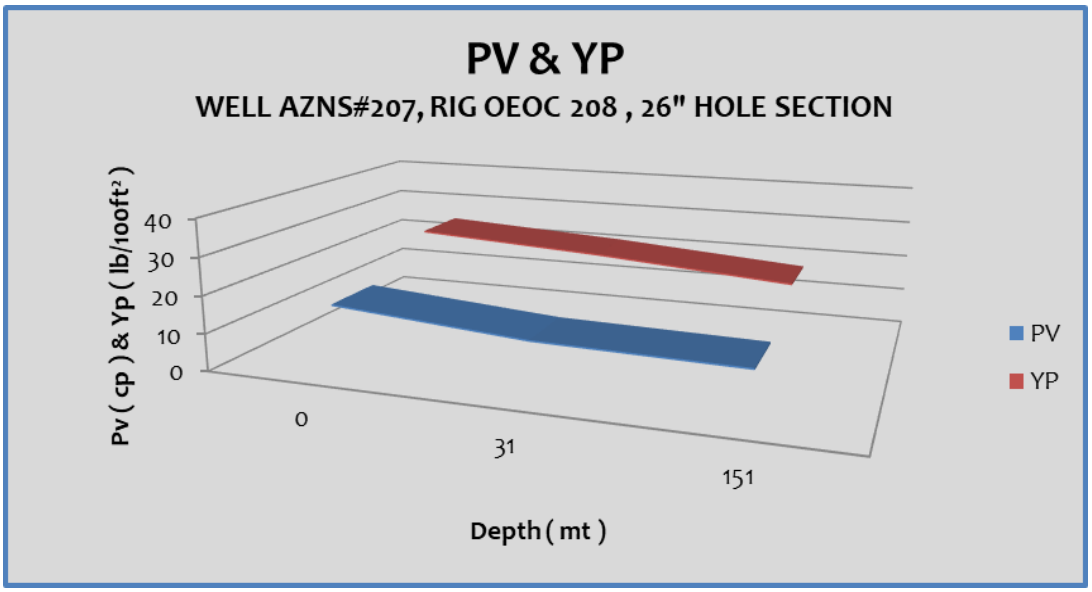


Figure 10-15: AZNS-207 PV & YP Chart

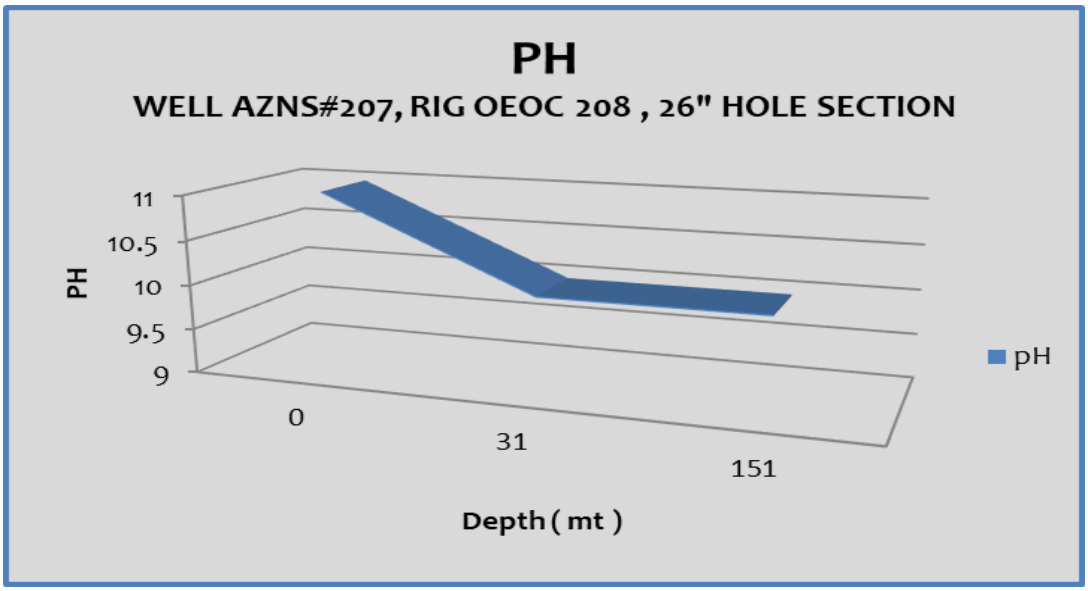


Figure 10-16: AZNS-207 PH Chart

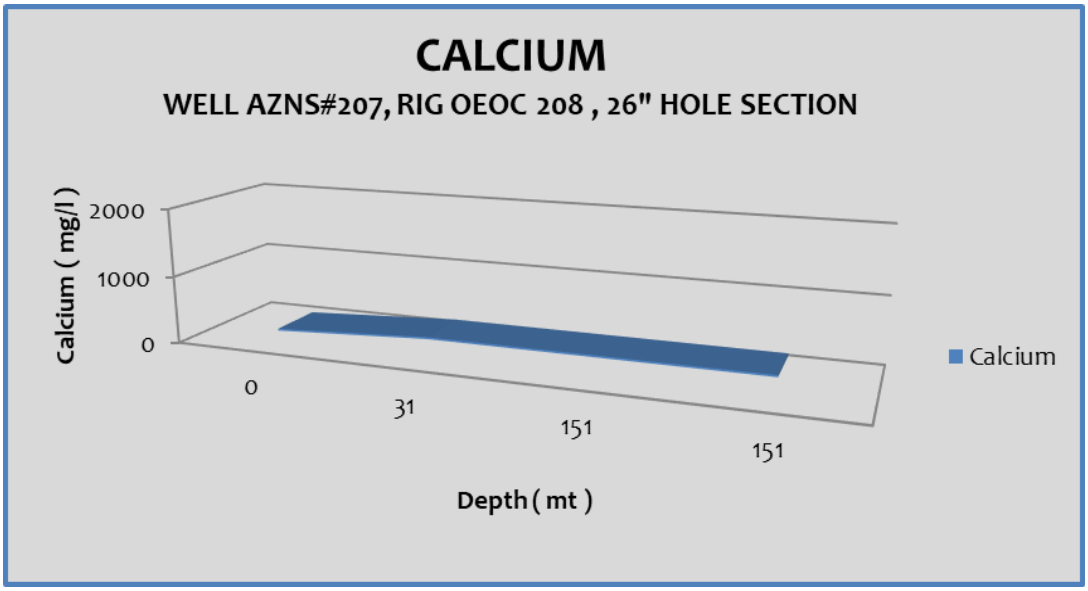


Figure 10-17: AZNS-207 Calcium Chart

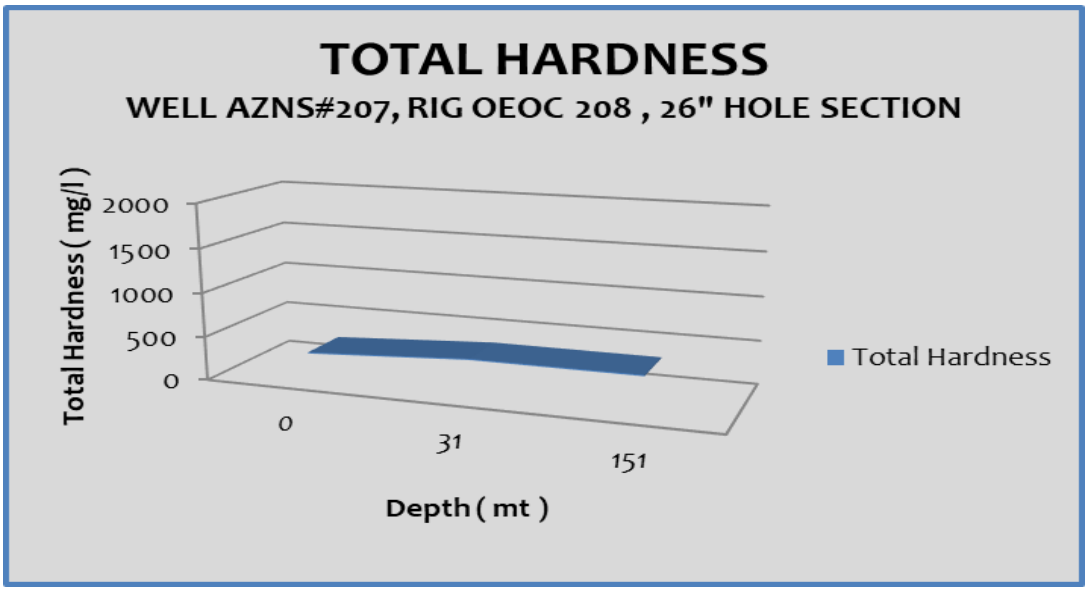


Figure 10-18: AZNS-207 Total Hardness Chart

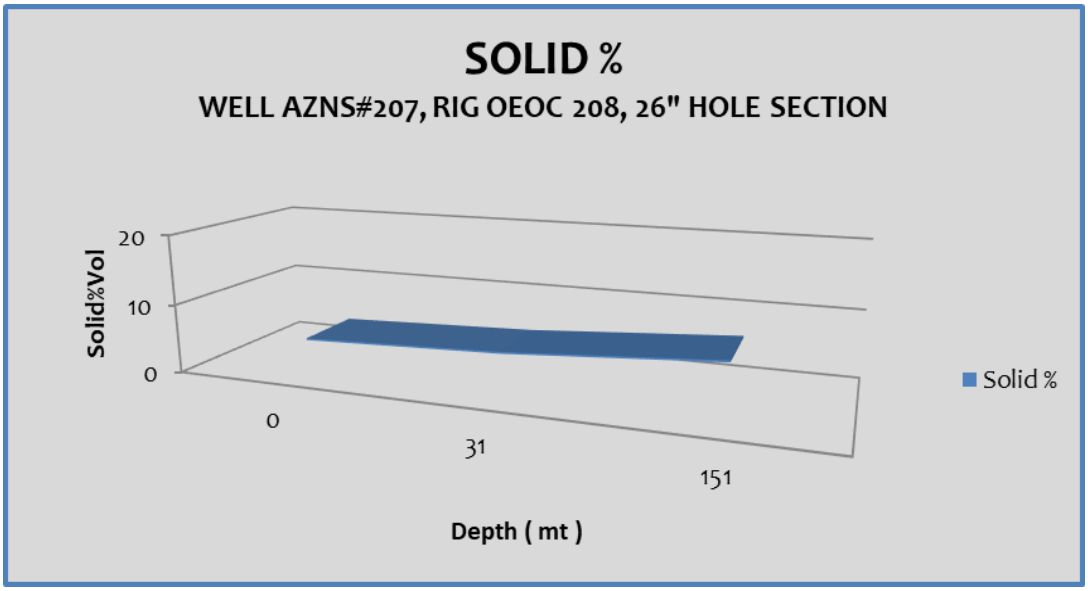


Figure 10-19: AZNS-207 Solid Percentage Chart

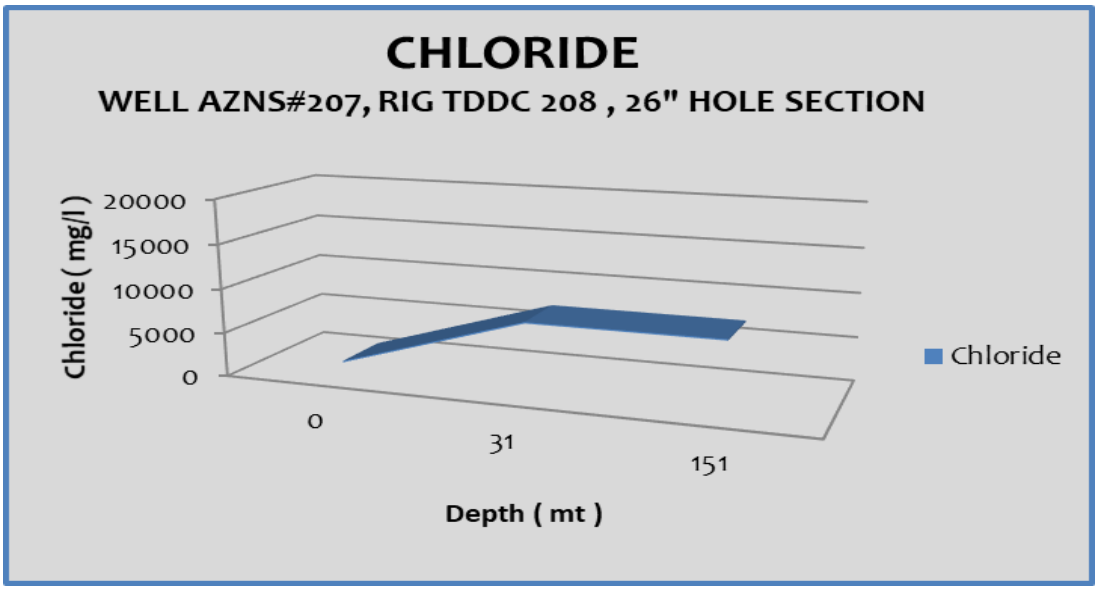


Figure 10-20: AZNS-207 Chloride Chart

Interval Solids Control Discussion:

Rig OEOC 208 has 3 shale shakers were dressed with:

- **Shaker#1**: 80 - 100 Mesh Screen
- **Shaker#2**: 80 - 100 Mesh Screen
- **Shaker#3: 80 - 100 Mesh Screen**

WELL AZNS#207. RIG OEOC 208 , 26" HOLE SECTION Solid Control Equipment Working Hr.s	
Shaker # 01	44
Shaker # 02	68
Shaker # 03	54
Mud Cleaner	0
Centrifuge	0

Figure 10-21: AZNS-207 Solid Control Table

10.2 17-1/2" Hole Section

Sections Remark:

Operation Remark: After the 20'' casing was set and performed cementing as per program successfully then made up 17 ½'' BHA after that RIH to 149m then started drill out cement and float equipment after that started drilling formation as 17 ½'' hole section to 165m then POOH due to bit nozzles washed out.

Made up 17 ½'' drilling BHA and RIH to 165m and commenced drilling to 495m then wiper trip was performed from depth of 495m to 225m with good hole condition then continued drilling to 590m and displaced Bentonite mud with Salt.Poly mud after that continued drilling to 793m then POOH due to changing bit and continued drilling to 1107m. Wiper trip was performed from depth of 1107m to 792m and with good hole condition and continued drilling to 1356m with NL-NG, Commenced drilling to 1373.8m and POOH to surface due to TDS problem.

Made up BHA and RIH to 1373.8m then continued drilling to 1479m, at this point pumped LCM pill due to 40-50 BPH loss and resumed drilling to 1480.3m, suddenly pressure dropped so POOH to surface and observed twist off from top of first 9-1/2" Drill Collar, therefor, made up fishing assembly and RIH to 1469.78m that was top of the fish and worked on catching the fish with 12-3/4" Over shot but this job had no success then POOH to surface.

Made up 11-3/4" fishing assembly and RIH to 1469m then performed fishing operation and POOH to surface After that observed fish was recovered completely, made up 17-1/2" BHA and RIH to 1480.3m, at this point pumped high viscosity pill and circulated and bottoms up then Resumed drilling to 1548m meanwhile pumped LCM pill several time POOH to surface due to low ROP with 5-15 BPH loss.

Made up 17-1/2" BHA and Junk sub then RIH to 1562m and commenced drilling from 1562m to 1564.5m then pumped 100 bbl. LCM pill and circulation job was perfumed after that POOH to 1460m with 5-20 BPH loss and continued POOH to surface.

Made up 17-1/2" BHA and RIH to 1515.5m while pumping high viscosity pill periodically in depth of 1200m to 1515.5m, suddenly pressure dropped in stand pipe so POOH surface for checking string with 2-8 BPH loss.

Made up 11-3/4" Over shot and RIH with fishing BHA to 1495.6m while wash down last stand and observed that dropped the fish so wash down to 1531m and took weight therefor worked on fishing with 4-6 BPH but fishing was no success so POOH to surface.

Made up 17-1/2" BHA and RIH to 1542.4m (top of fish) then circulated out high viscosity pill therefor POOH to surface, made up and assembled 11-3/4" Over shot with 3-6 BHP loss then RIH to 1539m then circulated out high viscosity pill with hard wash and ream down to 1541.2m with 6-8 BPH loss after that Continued hard wash and ream down from 1540.5m to 1541.4m with 2-3 BPH after that POOH to surface with 4-6 BPH.

Made up 17-1/2" taper mill and RIH to 700m and POOH to surface, made up 8-3/8" center cut bit and RIH to 1536m then Cement plug job was performed as per program after that POOH to 960m and wait on cement then commenced POOH to surface.

Made up 7-7/8" center cut bit and RIH to 960m then commenced drilling to 1486m and circulation job was performed in 1330m then cement plug job was performed as per program then POOH with 7-7/8" center cut bit to 130m and POOH to surface.

Made up 17-1/2" BHA and RIH to 1407m then drilled out cement to 1429m and circulation job was performed after that POOH to surface.

SIDE TRACKING

Made up directional BHA and RIH to 142m, at this point shallow test of DHM and MWD was performed meanwhile changed mud tools and leakage D. jar therefor, was waiting to receive another D. jar with 3-5 BPH loss after that continued RIH with 17-1/2" directional BHA from 142m to 1419m then wash down with 17-1/2" directional BHA from 1419m to 1429.4m. commenced directional drilling of hole section 17-1/2" from 1429.4m to 1649.5m.

Drilling Fluid Remark: Based on VIRA recommendation the carried bentonite mud from 26" hole section and added water to decreased MW to use for started this section up to 590 m and then the hole was displaced with fresh 71 pcf S. Saturated/KCL/Polymer mud was employ to drilling this section.

It was tried to reach optimum inhibition by using KCl as main shale inhibitor to stabilize active formation by decreasing the tendency of to absorb, swell and slough-off in HV-pills. Chloride of active system kept to 170000-180000 ml/lit to improve hole condition.

It was tried to control FL by adding Green Starch. The MW increased by adding barite& limestone up to 85 pcf.

SCE such as Shakers, mud cleaner and centrifuges were running to discard LGS while drilling this section. Several batches of premix/fresh mud were prepared occasionally and added to into active system intermittently in order to maintain recommended mud properties & surface Vol.

Beside that active circulation volume was treated frequently with essential chemical such Lime and caustic soda as Alkalinity controller to adjust pH, Soda Ash for control hardness, Starch lv as Fluid loss controller and KCl as shale inhibitor. In addition, Barite used to increase MW up to 91 pcf during drilling this section.

Also it was tried to extend hole cleaning by using HV Pill in different stage of operation.

Interval Information:

Interval II	155 – 1648 m	17 ½" Hole Interval	13 3/8" Casing Set at 1648 m

Drilling Fluid Types (main hole):

FLUID PROPERTIES RECAP					
KCL Pol Mud		Drilling start	Range		Drilling End
MW (min)	pcf	71	71	76.0	76.0
Funnel Viscosity	sec/qt	33	33	42	35
PV	cps	7	7	12	8
YP	lb/100sq.ft	15	10	15	10
API Fluid loss	cc	N.C	6	8	6.5
pH		10.5	9	10.5	10.3
Solid	%	8	8	14	14
MBT	lb/bbl	_	2.5	12.5	7.5
Cl (NaCl)	mg/L	7,400	7,400	140,000	140,000
Total Hardness	mg/L	400	400	2,320	2,040
Ca Hardness	mg/L	320	320	2,200	1,800

Figure 10-22: AZNS-207 17-1/2" (main hole) Fluid Properties Recap Table

Drilling Fluid Types (side track):

FLUID PROPERTIES RECAP					
KCL Pol Mud		Drilling start	Range		Drilling End
MW (min)	pcf	85	85	85.0	85.0
Funnel Viscosity	sec/qt	40	40	42	40
PV	cps	12	12	15	14
YP	lb/100sq.ft	10	9	10	9
API Fluid loss	cc	4	2	4	2
pH		9.6	9.4	9.7	9.5
Solid	%	19	19	19	19
MBT	lb/bbl	7.5	7.5	7.5	7.5
Cl (NaCl)	mg/L	180,000	180,000	180,000	180,000
Total Hardness	mg/L	3,200	3,200	3,200	3,200
Ca Hardness	mg/L	3,000	3,000	3,000	3,000

Figure 10-23: AZNS-207 17-1/2" (side track) Fluid Properties Recap Table

Material Consumption Analysis (main hole):

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Barite	75	3,300	247,500	lbs	17.68	ppb
Caustic Soda	156	55	8,580	lbs	0.61	ppb
Defoamer	1	55	55	gal	0.004	gpb
Limestone	48	2,200	105,600	lbs	7.54	ppb
PHPA	5	11	55	lbs	0.004	ppb
Salt (NACL)	531	2,200	1,168,200	lbs	83.46	ppb
Soda Ash	185	55	10,175	lbs	0.73	ppb
Starch LV/G	2,354	55	129,470	lbs	9.25	ppb
Xanthan Gum	60	55	3,300	lbs	0.24	ppb
Starch HT	408	55	22,440	lbs	1.60	ppb
KCL	8	2,200	17,600	lbs	1.26	ppb
Lime	494	55	27,170	lbs	1.94	ppb
MICA M	154	55	8,470	lbs	0.61	ppb
KWIK SEAL M	144	55	7,920	lbs	0.57	ppb
MICA F	18	55	990	lbs	0.07	ppb

Initial Volume	769.0	bbl
Total Volume Built	13,996.9	bbl
Volume received	0.0	bbl
Volume Returned	0.0	bbl
Total Volume Consumed	12,068	bbl
Volume Transfer to Next Section	2,697.9	bbl
Meter Drilled	1,409.0	m

Figure 10-24: AZNS-207 17-1/2" (main hole) Material Consumption Analysis Table

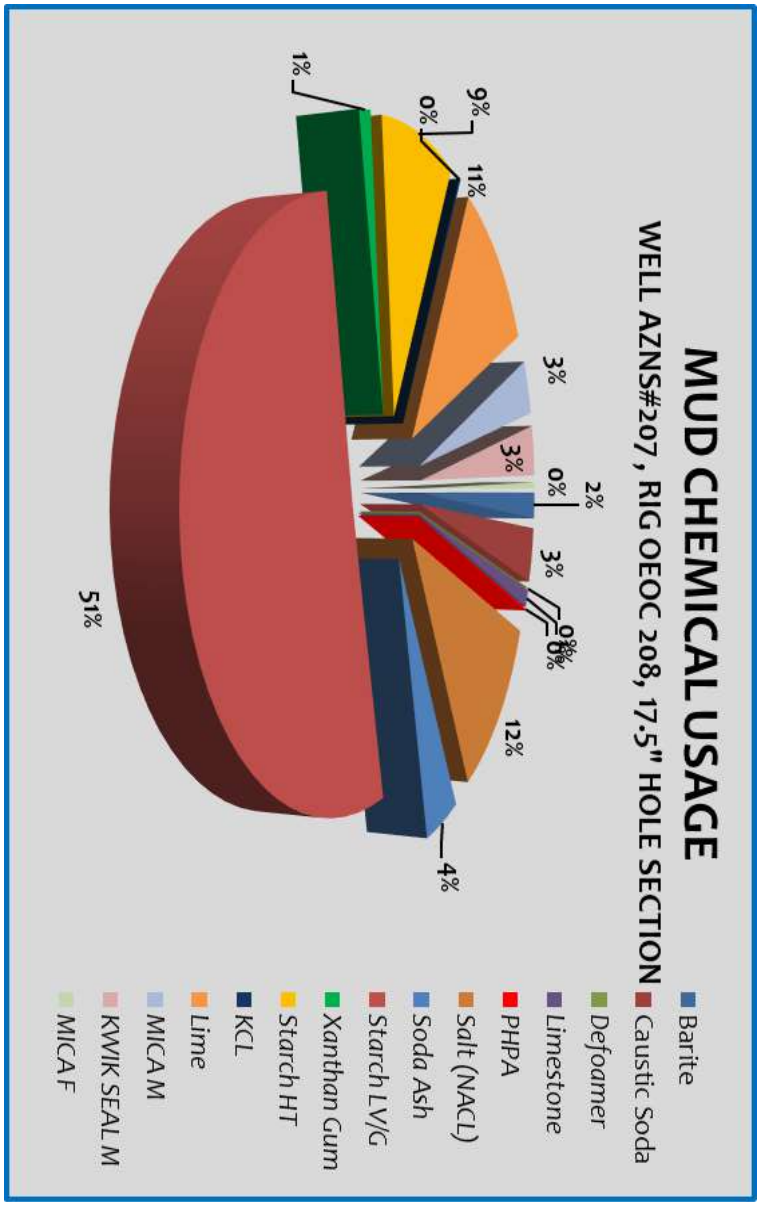


Figure 10-25: AZNS-207 17-1/2" (main hole) Mud Chemical Usage Graph

Material Consumption Analysis (side track):

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Barite	60	3,300	198,000	lbs	70.06	ppb
Caustic Soda	22	55	1,210	lbs	0.43	gpb
PHPA	5	55	275	lbs	0.097	ppb
Salt (NACL)	105	2,200	231,000	lbs	81.74	ppb
Soda Ash	43	55	2,365	lbs	0.84	ppb
Sodium Bicarbonate	20	55	1,100	lbs	0.39	ppb
Starch LV/G	606	55	33,330	lbs	11.79	ppb
Xanthan Gum	37	55	2,035	lbs	0.72	ppb
KCL	23	2,200	50,600	lbs	17.91	ppb
Lime	112	55	6,160	lbs	2.18	ppb
Limestone Chips F	134	55	7,370	lbs	2.61	ppb
Limestone Chips F	4	2,200	8,800	lbs	3.11	ppb

Initial Volume	2,699.0	bbl
Total Volume Built	2,826.0	bbl
Volume received	0.0	bbl
Volume Returned	0.0	bbl
Total Volume Consumed	3,294	bbl
Volume Transfer to Next Section	2,231.0	bbl
Meter Drilled	219.0	m

Figure 10-26: AZNS-207 17-1/2" (side track) Material Consumption Analysis Table

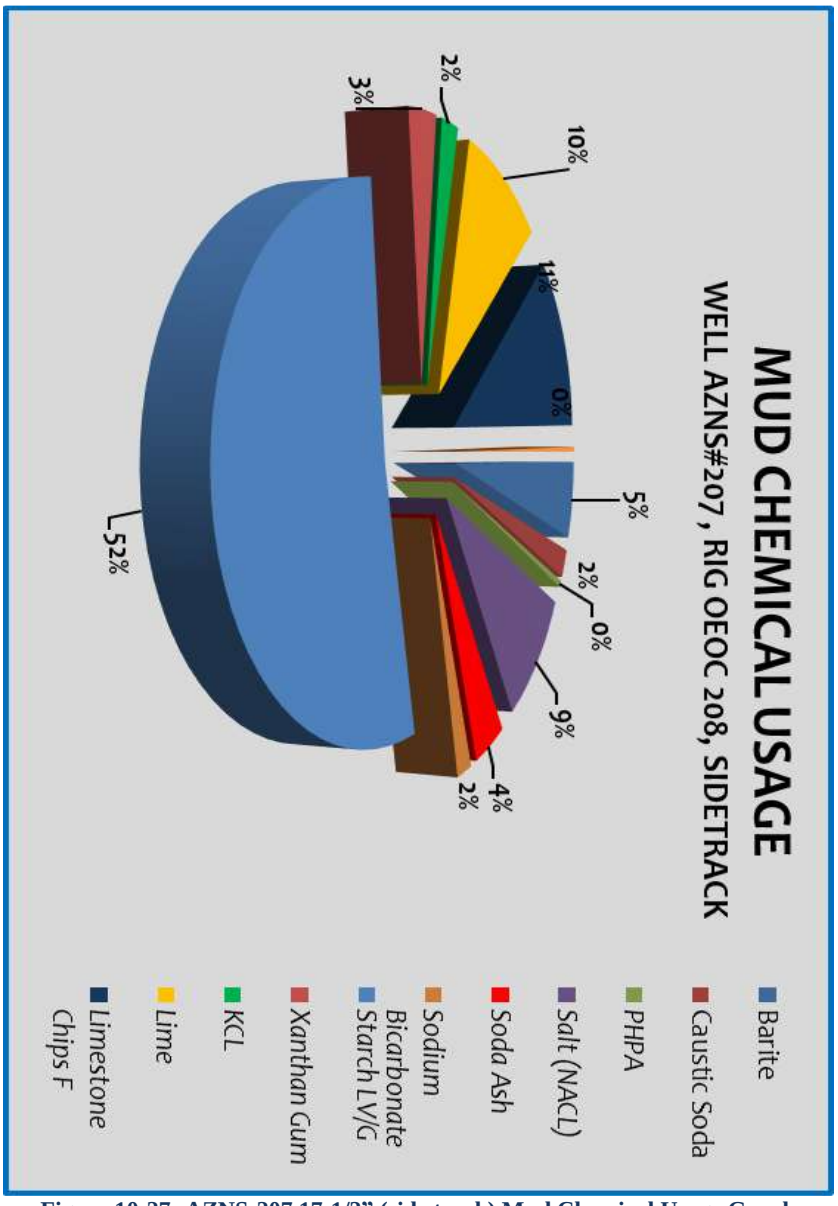


Figure 10-27: AZNS-207 17-1/2" (side track) Mud Chemical Usage Graph

Volume Analysis (main hole):

WELL AZNS#193, RIG TDDC 301, 17.5" HOLE SECTION VOLUME ANALYSIS		
Initial Volume	bbls	769.0
Received Volume	bbls	0.0
Volume Return	bbls	0.0
Volume Built	bbls	13,996.9
Surface Losses/Dumped	bbls	8,772.0
Formation Losses	bbls	3,295.0
Total Losses	bbls	12,067.0
Volume Transfer Out	bbls	2,699

Figure 10-28: AZNS-207 17-1/2" (main hole) Volume Analysis Table

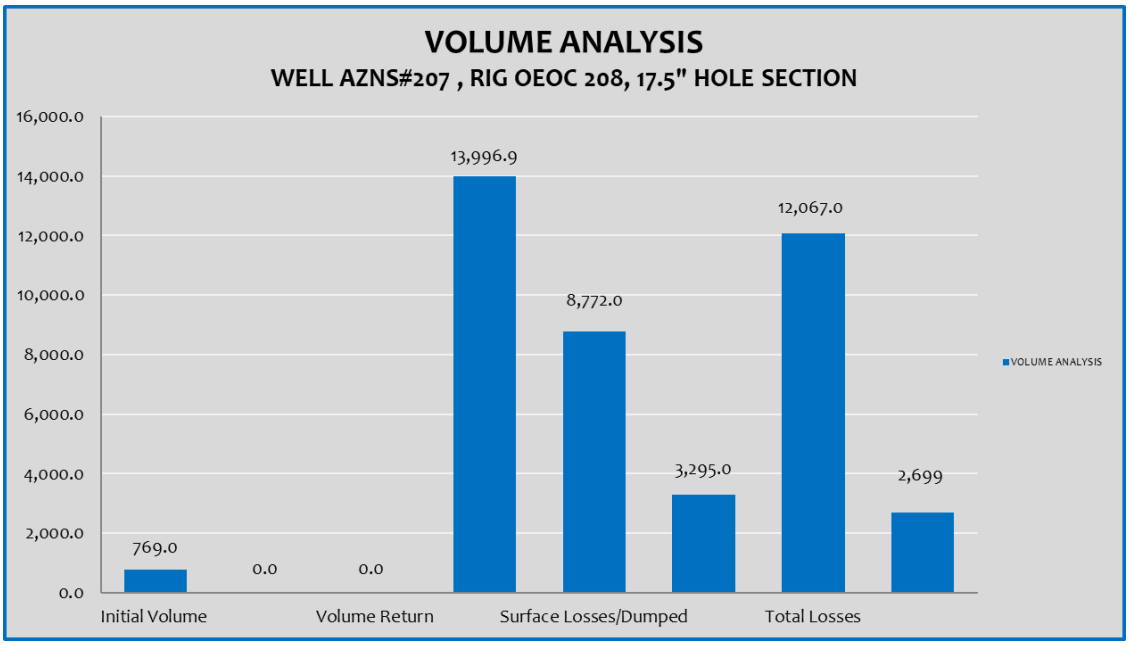


Figure 10-29: AZNS-207 17-1/2" (main hole) Volume Analysis Chart

Volume Analysis (side track):

WELL AZNS#207 , RIG OEOC 208, SIDETRACK VOLUME ANALYSIS		
Initial Volume	bbls	2,698.0
Received Volume	bbls	0.0
Volume Return	bbls	0.0
Volume Built	bbls	2,825.6
Surface Losses/Dumped	bbls	2,249.0
Formation Losses	bbls	1,044.0
Total Losses	bbls	3,293.0
Volume Transfer Out	bbls	2,231

Figure 10-30: AZNS-207 17-1/2" (side track) Volume Analysis Table

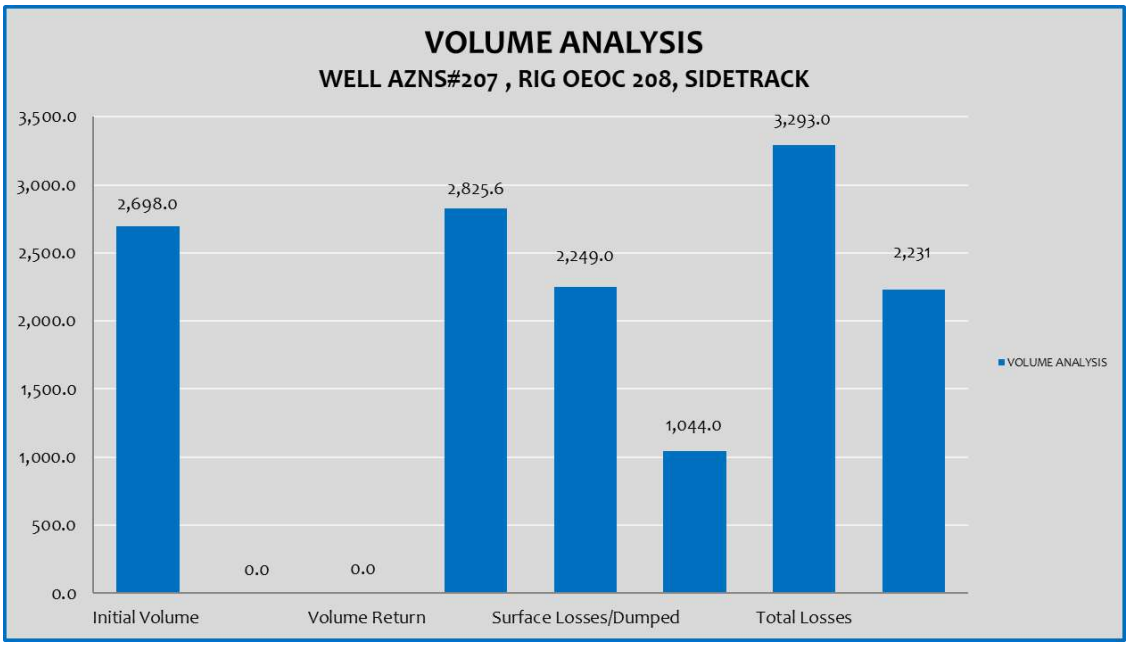


Figure 10-31: AZNS-207 17-1/2" (side track) Volume Analysis Chart

Daily Volume Break Down (main hole):

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
21-Oct-24	7	837.0	30	0
22-Oct-24	8	236.2	154	0
23-Oct-24	9	1,347.3	788	0
24-Oct-24	10	1,649.8	1,905	0
25-Oct-24	11	375.3	464	0
26-Oct-24	12	813.5	447	0
27-Oct-24	13	782.4	534	0
28-Oct-24	14	663.5	415	0
29-Oct-24	15	654.0	585	0
30-Oct-24	16	724.7	559	0
31-Oct-24	17	344.4	166	61
1-Nov-24	18	149.9	70	24
2-Nov-24	19	111.7	134	24
3-Nov-24	20	874.0	172	694
4-Nov-24	21	289.5	140	361
5-Nov-24	22	427.2	55	221
6-Nov-24	23	773.9	350	343
7-Nov-24	24	584.3	79	150
8-Nov-24	25	54.1	218	40
9-Nov-24	26	314.8	310	82
10-Nov-24	27	126.2	35	85
11-Nov-24	28	31.4	42	144
12-Nov-24	29	139.0	89	135
13-Nov-24	30	193.2	60	138
14-Nov-24	31	563.3	137	220
15-Nov-24	32	353.8	204	120
16-Nov-24	33	166.5	116	170
17-Nov-24	34	208.3	69	87
18-Nov-24	35	18.4	262	48
19-Nov-24	36	0.0	47	52
20-Nov-24	37	74.0	12	24
21-Nov-24	38	115.3	124	72
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		13,997	8,772	3,295

Figure 10-32: AZNS-207 17-1/2" (main hole) Daily Volume Break Down Table

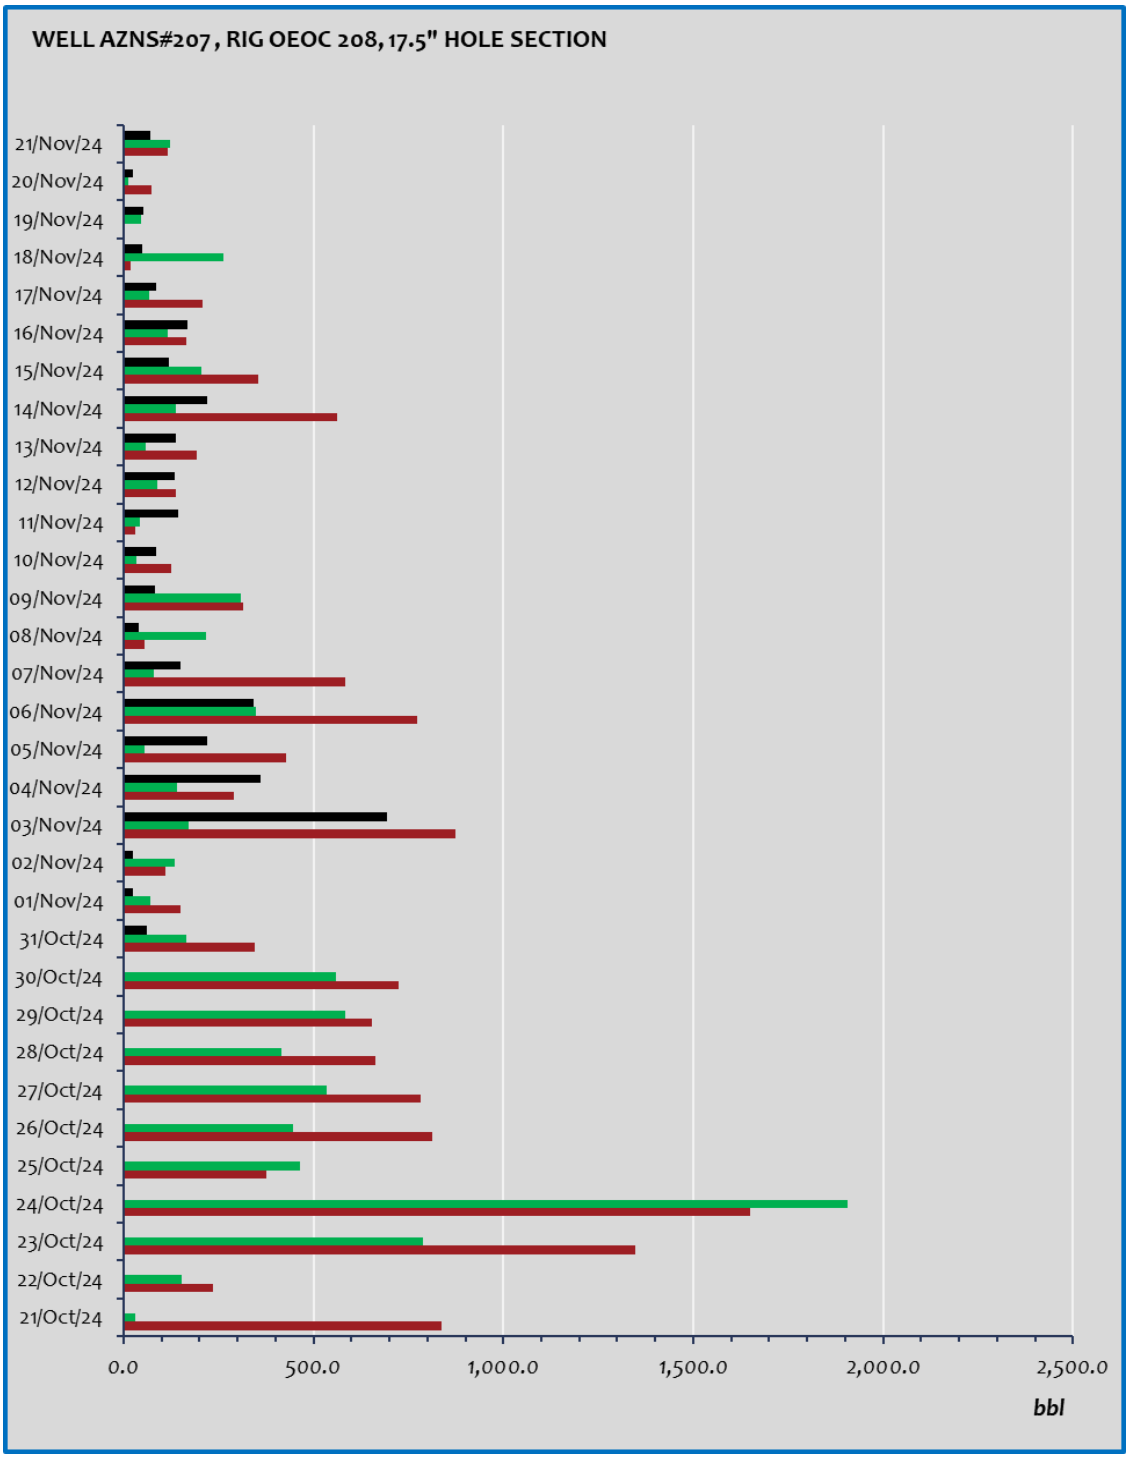


Figure 10-33: AZNS-207 17-1/2" (main hole) Daily Volume Break Down Chart

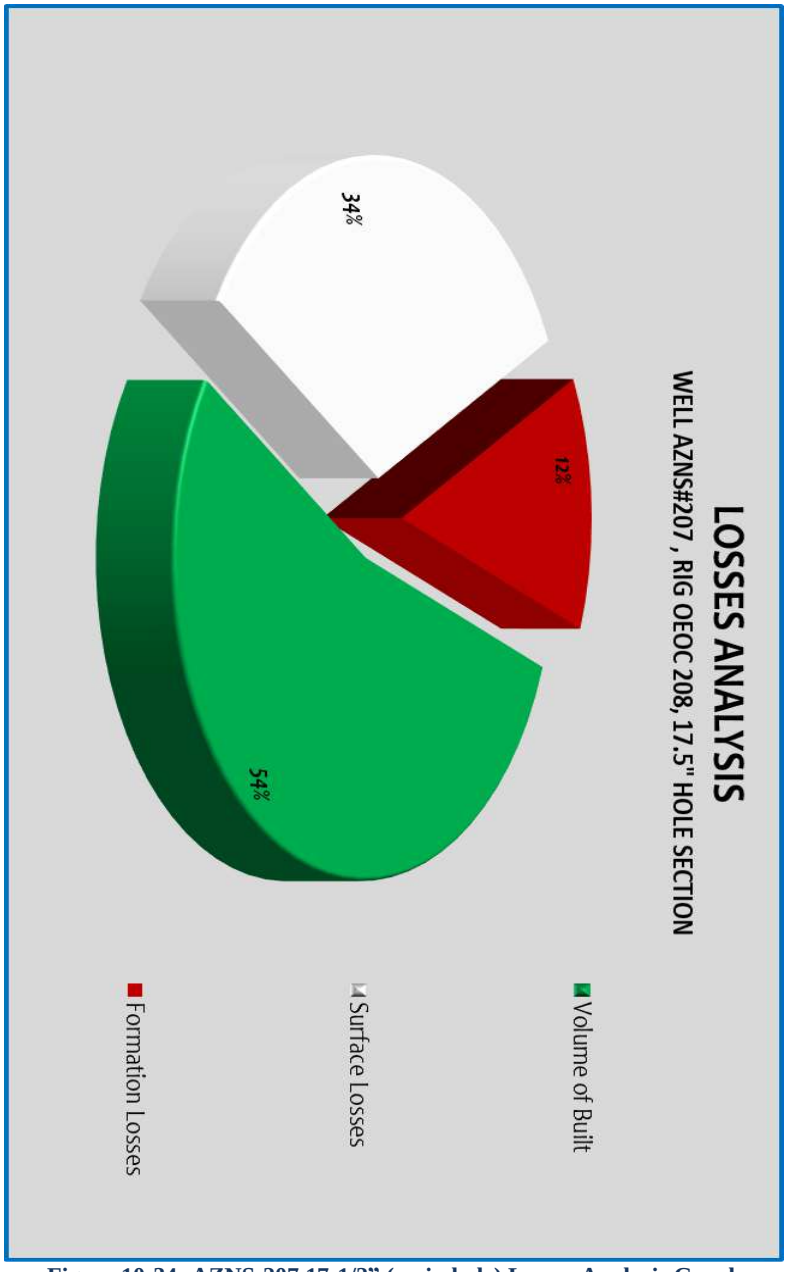


Figure 10-34: AZNS-207 17-1/2" (main hole) Losses Analysis Graph

Daily Volume Break Down (side track):

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
22-Nov-24	7	753.1	767	64
23-Nov-24	8	171.2	34	72
24-Nov-24	9	186.9	33	60
25-Nov-24	10	242.1	136	72
26-Nov-24	11	202.0	224	60
27-Nov-24	12	480.0	36	96
28-Nov-24	13	200.1	63	100
29-Nov-24	14	190.3	36	84
30-Nov-24	15	0.0	88	43
1-Dec-24	16	6.2	30	48
2-Dec-24	17	3.8	133	27
3-Dec-24	18	139.5	75	36
4-Dec-24	19	1.4	24	36
5-Dec-24	20	101.1	40	30
6-Dec-24	21	0.9	56	36
7-Dec-24	22	108.1	64	36
8-Dec-24	23	0.0	256	32
9-Dec-24	24	0.0	110	36
10-Dec-24	25	38.9	32	36
11-Dec-24	26	0.0	12	40
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		2,826	2,249	1,044

Figure 10-35: AZNS-207 17-1/2" (side track) Daily Volume Break Down Table

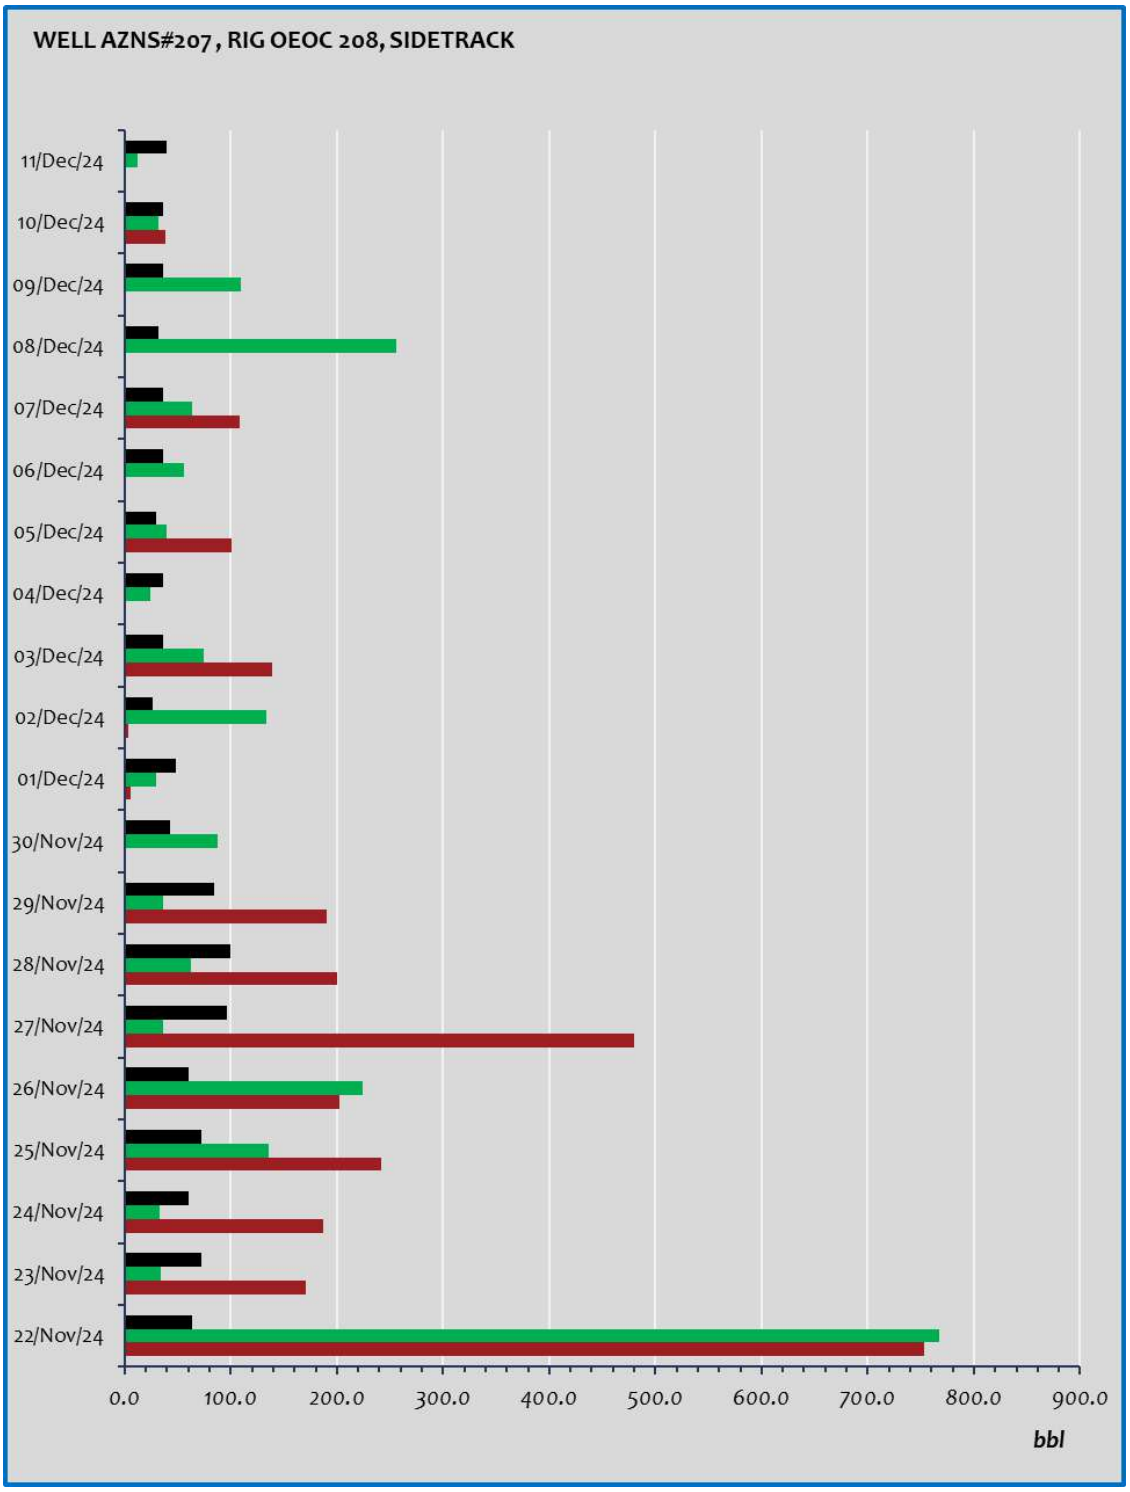


Figure 10-36: AZNS-207 17-1/2" (side track) Daily Volume Break Down Chart

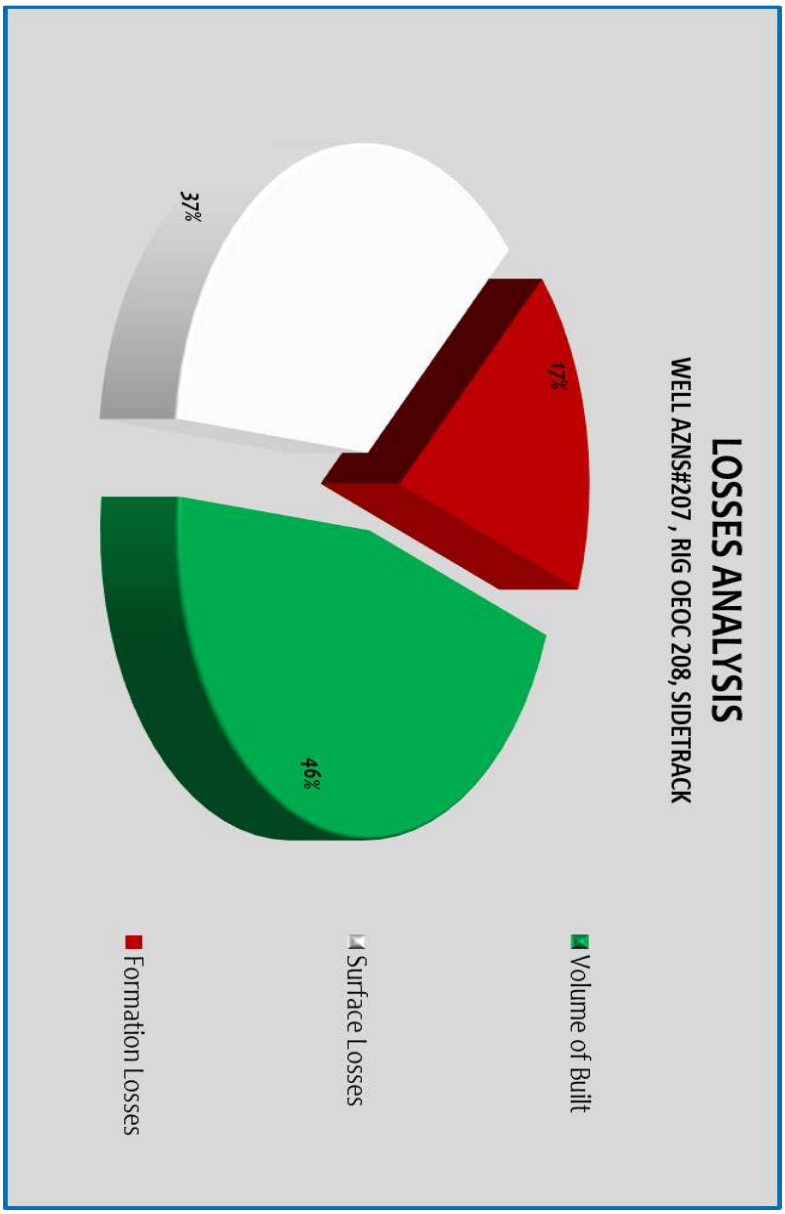


Figure 10-37: AZNS-207 17-1/2" (side track) Daily Volume Break Down Analysis Graph

Loss Distribution (main hole):

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
21-Oct-24	7	837.0	0	10	0	0	0	0	20	0	0
22-Oct-24	8	236.2	118	36	0	0	0	0	0	0	0
23-Oct-24	9	1,347.3	720	48	0	0	0	0	0	0	20
24-Oct-24	10	1,649.8	1,730	80	0	25	0	40	0	0	30
25-Oct-24	11	375.3	240	84	0	60	0	35	0	0	45
26-Oct-24	12	813.5	0	90	0	92	0	200	0	0	65
27-Oct-24	13	782.4	40	72	0	92	0	300	0	0	30
28-Oct-24	14	663.5	77	36	0	72	0	200	0	0	30
29-Oct-24	15	654.0	230	48	0	72	0	200	0	0	35
30-Oct-24	16	724.7	140	96	0	48	0	180	0	0	95
31-Oct-24	17	344.4	0	90	0	16	60	0	0	61	0
1-Nov-24	18	149.9	0	15	0	10	45	0	0	24	0
2-Nov-24	19	111.7	60	0	0	20	40	14	0	24	0
3-Nov-24	20	874.0	0	80	0	20	0	32	0	694	40
4-Nov-24	21	289.5	40	40	0	0	30	0	0	361	30
5-Nov-24	22	427.2	0	40	0	0	15	0	0	221	0
6-Nov-24	23	773.9	180	96	0	22	0	0	22	343	30
7-Nov-24	24	584.3	0	40	0	24	0	0	0	150	15
8-Nov-24	25	54.1	40	38	0	120	0	0	0	40	20
9-Nov-24	26	314.8	60	30	0	120	0	100	0	82	0
10-Nov-24	27	126.2	0	20	0	15	0	0	0	85	0
11-Nov-24	28	31.4	0	42	0	0	0	0	0	144	0
12-Nov-24	29	139.0	0	34	0	0	20	0	0	135	35
13-Nov-24	30	193.2	0	37	0	0	0	0	0	138	23
14-Nov-24	31	563.3	55	42	0	0	0	0	0	220	40
15-Nov-24	32	353.8	120	34	0	0	15	0	20	120	15
16-Nov-24	33	166.5	60	36	0	0	0	0	0	170	20
17-Nov-24	34	208.3	30	24	0	0	0	0	0	87	15
18-Nov-24	35	18.4	223	24	0	0	0	0	15	48	0
19-Nov-24	36	0.0	0	12	0	0	0	0	20	52	15
20-Nov-24	37	74.0	0	12	0	0	0	0	0	24	0
21-Nov-24	38	115.3	100	24	0	0	0	0	0	72	0
Total (bbl)		Volume of Built	Dump/Contaminate	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
		13,996.9	4,263	1,410	0	828	225	1,301	97	3,295	648.0

Figure 10-38: AZNS-207 17-1/2" (main hole) Loss Distribution Table

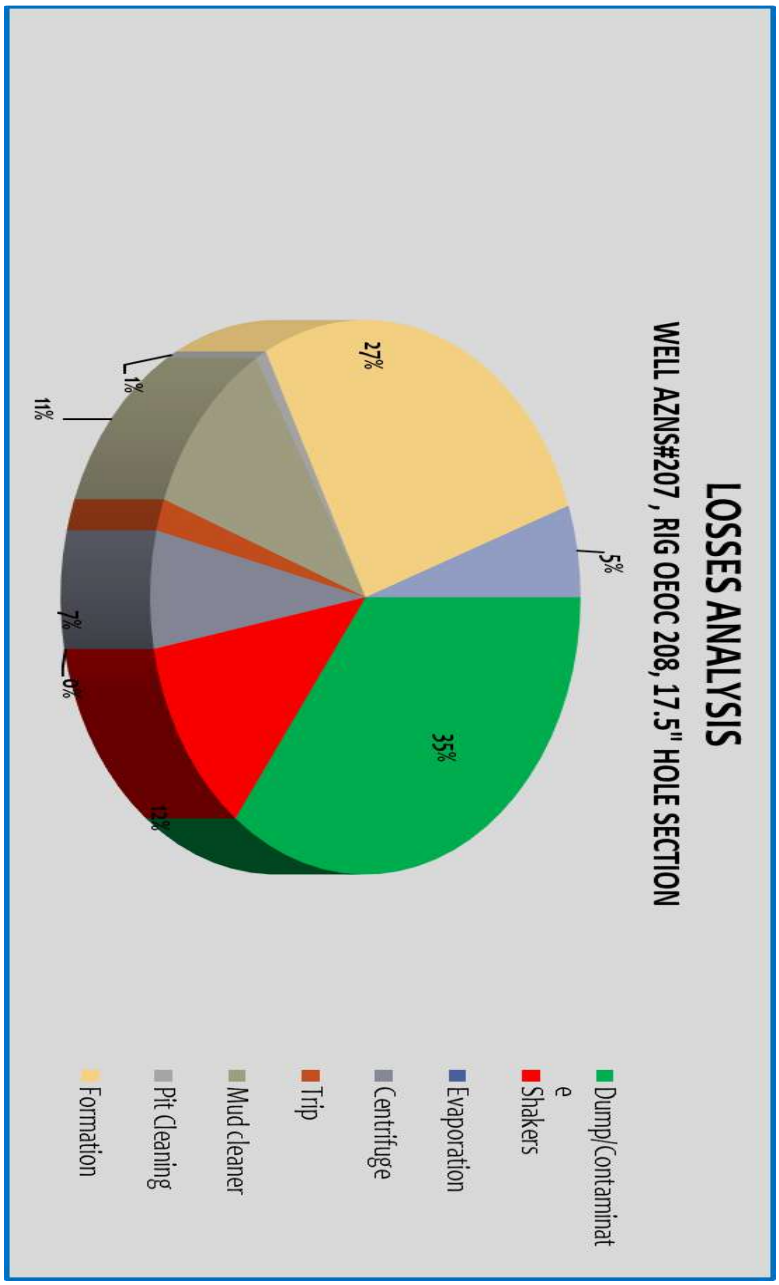


Figure 10-39: AZNS-207 17-1/2" (main hole) Loss Analysis Graph

Fluid Properties Recap (main hole):

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	MBT	Solid %	Chloride	Calcium	Total Hardness	Mud Type
21-Oct-24	155	70	36	7	19	N.C	11		7	7400	320	400	PHG Mud
22-Oct-24	225	71	33	7	15	N.C	10.5		8	7400	320	400	PHG Mud
23-Oct-24	495	71	33	8	15	N.C	10.2		8	7400	320	400	PHG Mud
24-Oct-24	730	73	35	12	11	6	9.5	2.5	9	120000	800	1000	SALT/POL MUD
25-Oct-24	800	74	37	10	12	6	9.5	12.5	10	140000	1280	1400	SALT/POL MUD
26-Oct-24	1073	74	40	12	13	8	9.5	12.5	12	140000	1800	2000	SALT/POL MUD
27-Oct-24	1227	74	40	12	10	8	9.5	12.5	12	140000	1800	2000	SALT/POL MUD
28-Oct-24	1356	74	40	11	10	8	9.5	12.5	12	140000	1800	2000	SALT/POL MUD
29-Oct-24	1373	74	39	11	10	8	9.5	12.5	12	140000	1800	2000	SALT/POL MUD
30-Oct-24	1450	76	42	10	12	8	9.5	10	14	140000	1800	2000	SALT/POL MUD
31-Oct-24	1480	76	41	10	12	8	9.3	10	14	140000	1800	2000	SALT/POL MUD
1-Nov-24	1480	76	41	10	12	8	9.3	10	14	140000	1800	2000	SALT/POL MUD
2-Nov-24	1480	76	39	9	11	8	9.3	7.5	14	140000	1800	2000	SALT/POL MUD
3-Nov-24	1480	76	40	10	13	30	9.3	7.5	14	140000	2200	2320	SALT/POL MUD
4-Nov-24	1562	76	39	9	12	30	9	7.5	14	140000	2000	2120	SALT/POL MUD
5-Nov-24	1562	76	39	9	12	20	9.2	7.5	14	140000	2000	2120	SALT/POL MUD
6-Nov-24	1562	76	39	9	11	20	9.5	7.5	14	140000	1800	2040	SALT/POL MUD
7-Nov-24	1564	76	35	8	10	6.5	10.3	7.5	14	140000	1800	2040	SALT/POL MUD
8-Nov-24	1564	76	39	8	9	6.5	10.4	7.5	14	181000	1800	2040	SALT/POL MUD
9-Nov-24	1564	76	39	8	9	25	10.4	7.5	14	171000	3480	3800	SALT/POL MUD
10-Nov-24	1564	76	38	8	9	25	10.3	7.5	14	171000	3480	3800	SALT/POL MUD
11-Nov-24	1564	79	39	8	10	7.5	9.2	7.5	15	171000	3400	3620	SALT/POL MUD
12-Nov-24	1564	81	41	8	10	25	9.1	7.5	17	171000	3400	3620	SALT/POL MUD
13-Nov-24	1564	83	42	13	10	25	9.4	7.5	18	171000	3400	3620	SALT/POL MUD
14-Nov-24	1564	83	43	14	12	9	9.4	7.5	18	170000	2600	2920	SALT/POL MUD
15-Nov-24	1564	83	43	14	12	6	9.4	7.5	18	170000	2520	2760	SALT/POL MUD
16-Nov-24	1564	83	43	14	12	4	9.3	7.5	18	176000	2520	2760	KCL/POL MUD
17-Nov-24	1564	85	42	15	12	5	9.4	7.5	19	176000	2600	2800	KCL/POL MUD
18-Nov-24	1564	85	42	14	12	4	9.4	7.5	19	176000	2600	2800	KCL/POL MUD
19-Nov-24	1564	85	43	14	12	4	9.3	7.5	19	176000	2600	2800	KCL/POL MUD
20-Nov-24	1564	85	40	13	10	6	9.5	7.5	19	176000	2800	3000	KCL/POL MUD
21-Nov-24	1564	85	43	15	12	7	9.4	7.5	19	176000	4000	4200	KCL/POL MUD

Drilling Start
Drilling End

Figure 10-40: AZNS-207 17-1/2" (main hole) Fluid Properties Recap Table

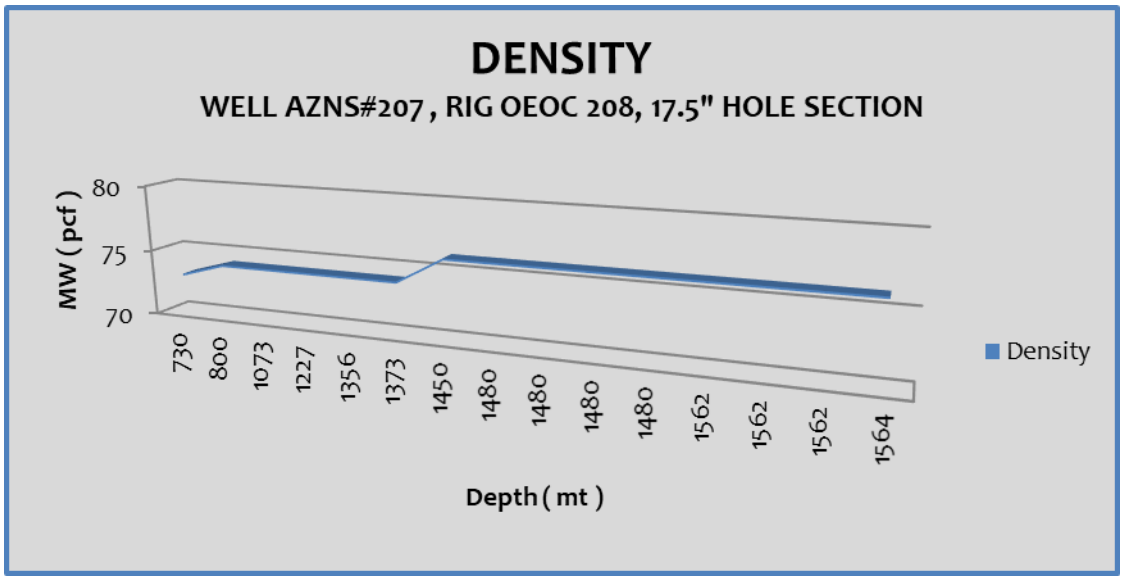


Figure 10-41: AZNS-207 17-1/2" (main hole) Density Chart

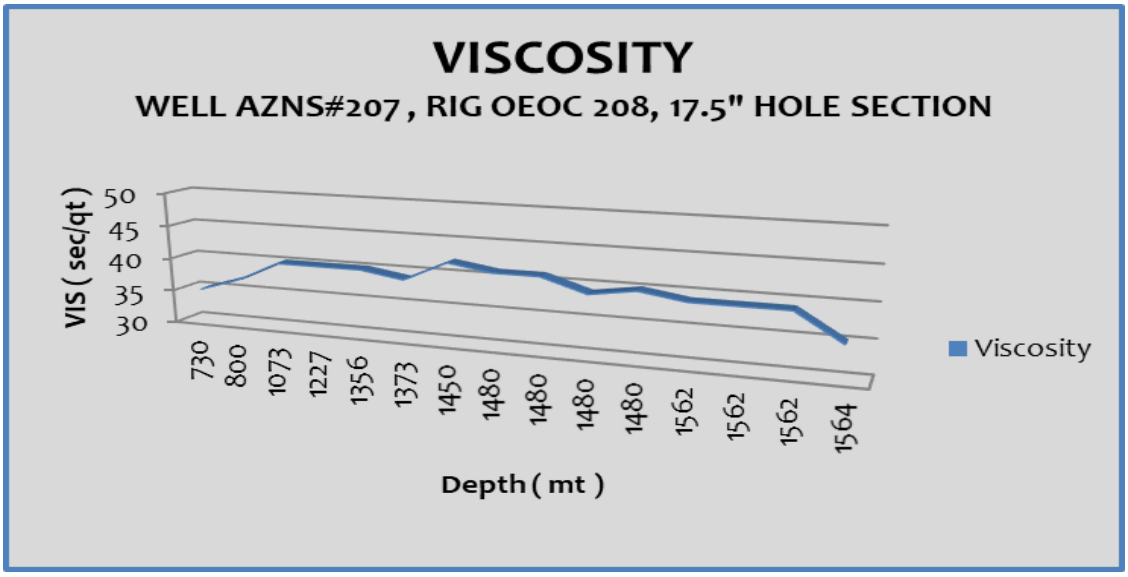


Figure 10-42: AZNS-207 17-1/2" (main hole) Viscosity Chart

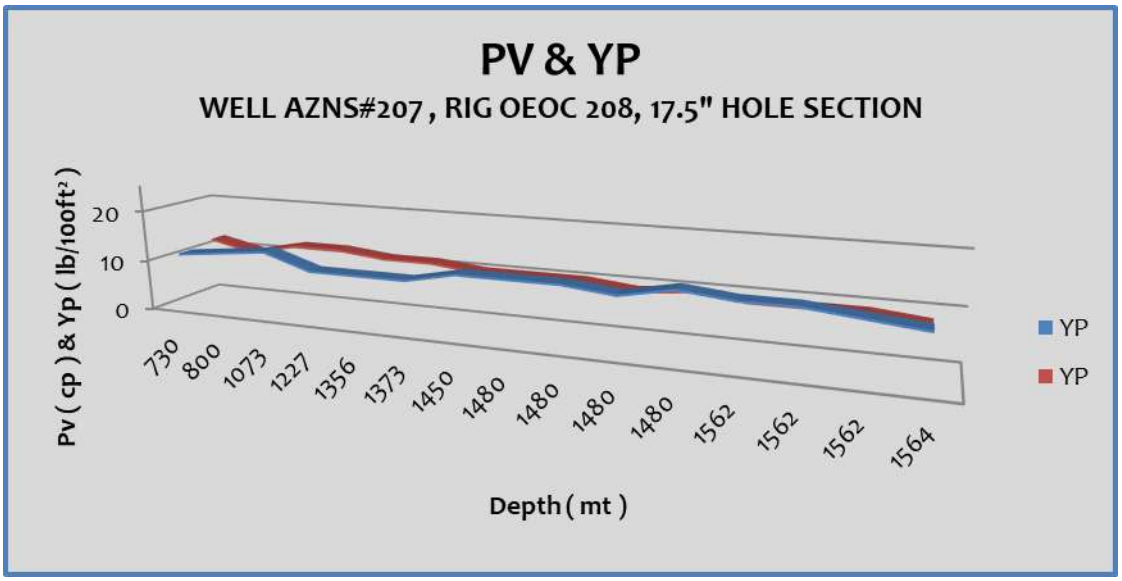


Figure 10-43: AZNS-207 17-1/2" (main hole) PV & YP Chart

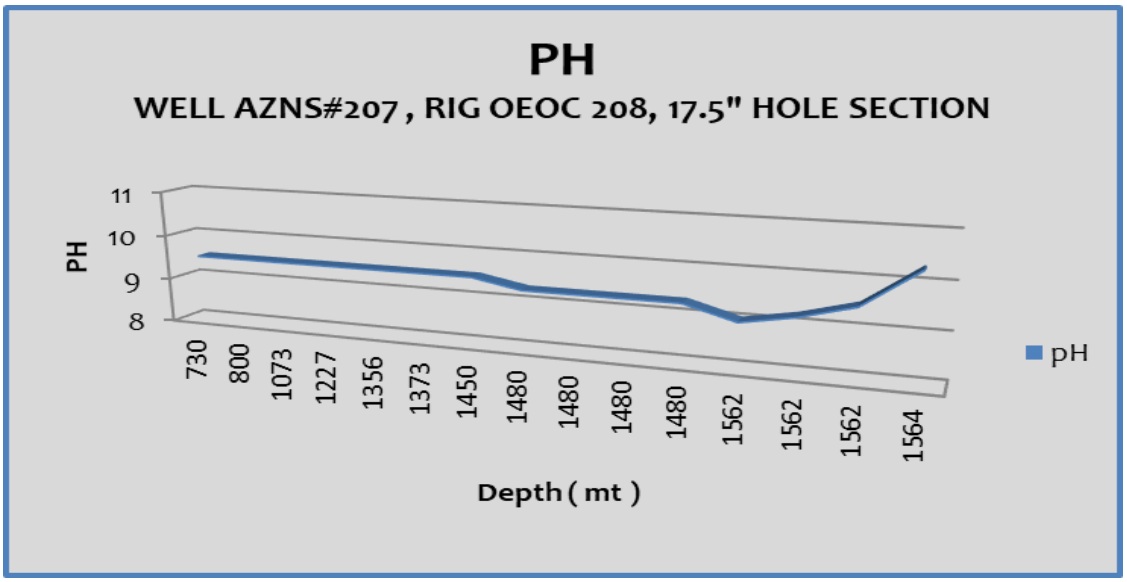


Figure 10-44: AZNS-207 17-1/2" (main hole) PH Chart

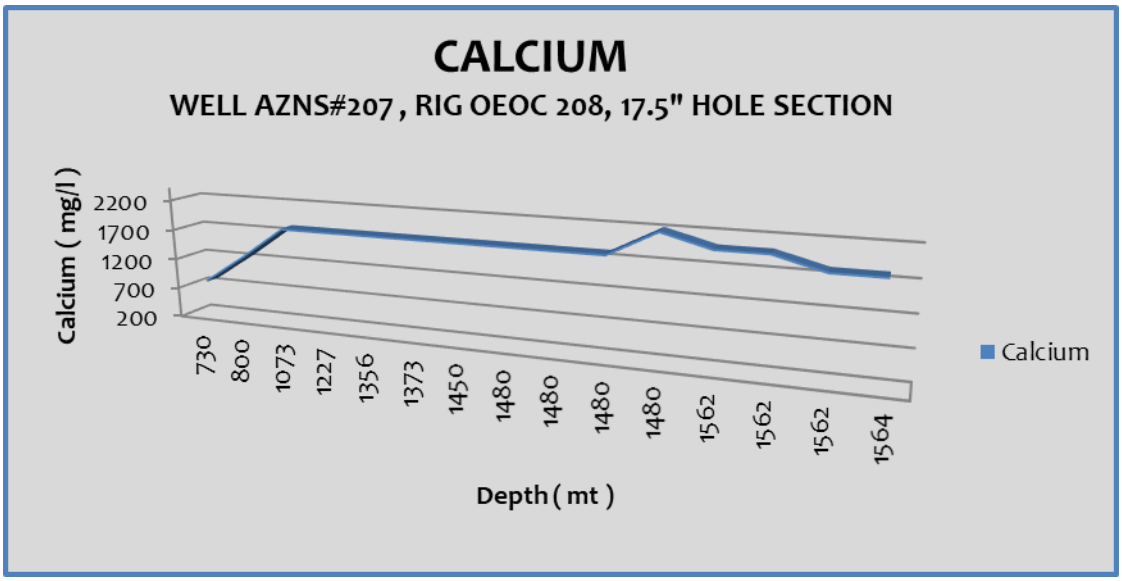


Figure 10-45: AZNS-207 17-1/2" (main hole) Calcium Chart

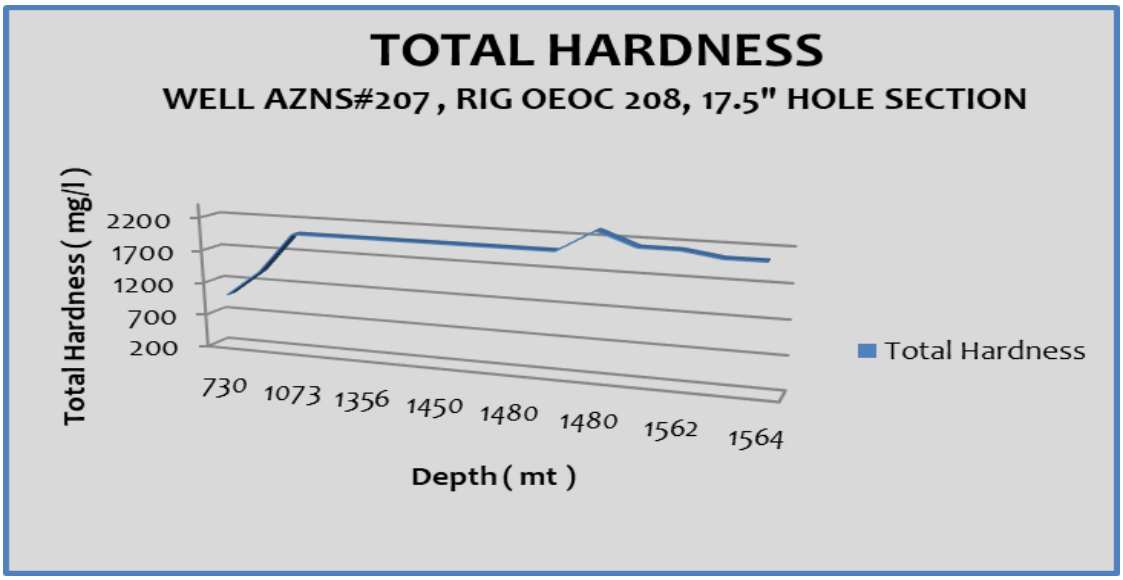


Figure 10-46: AZNS-207 17-1/2" (main hole) Total Hardness Chart

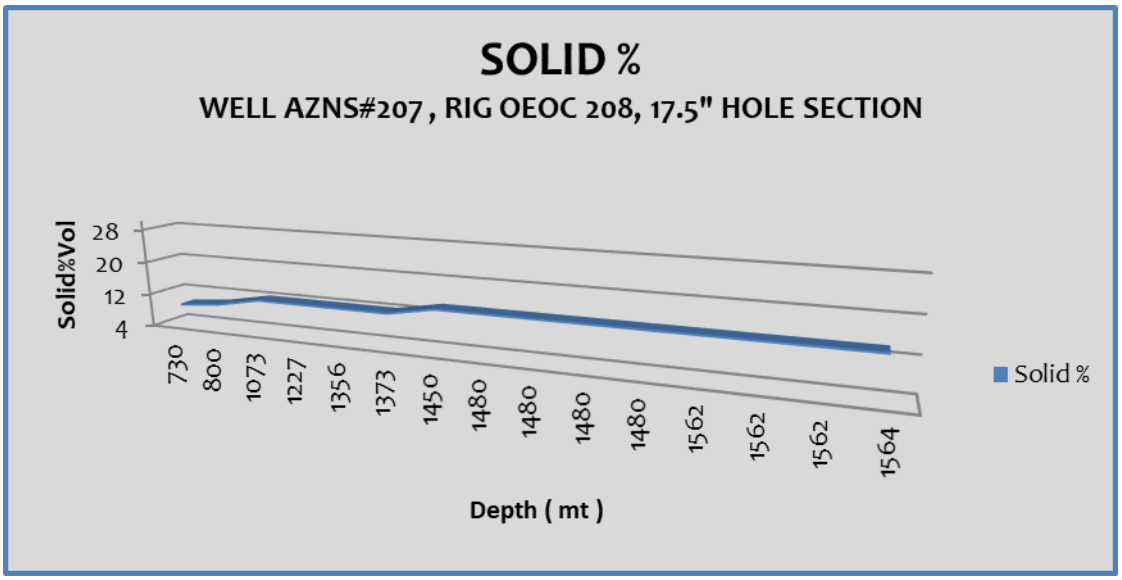


Figure 10-47: AZNS-207 17-1/2" (main hole) Solid Percentage Chart

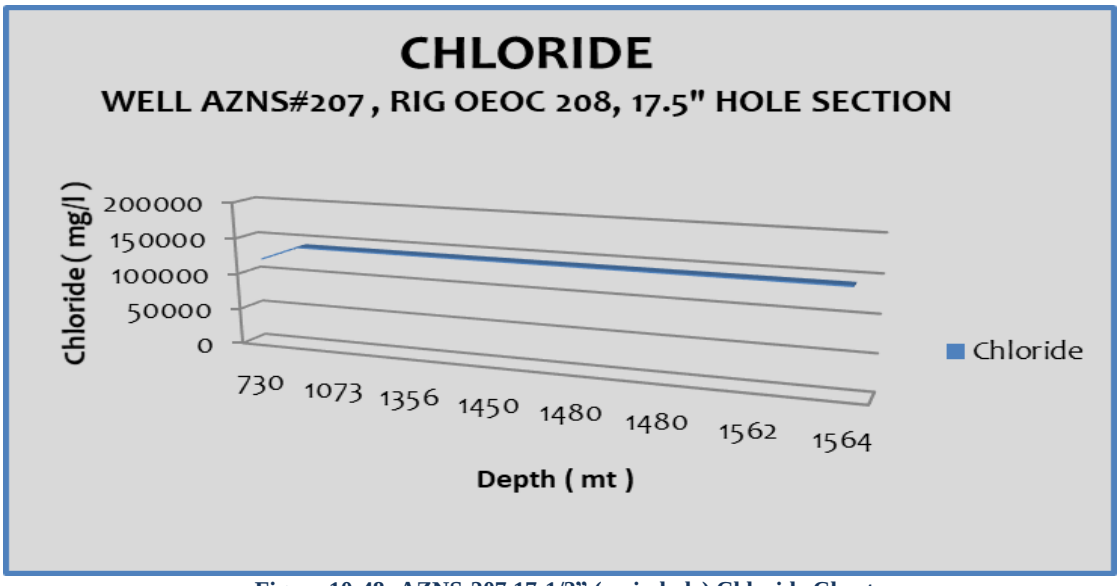


Figure 10-48: AZNS-207 17-1/2" (main hole) Chloride Chart

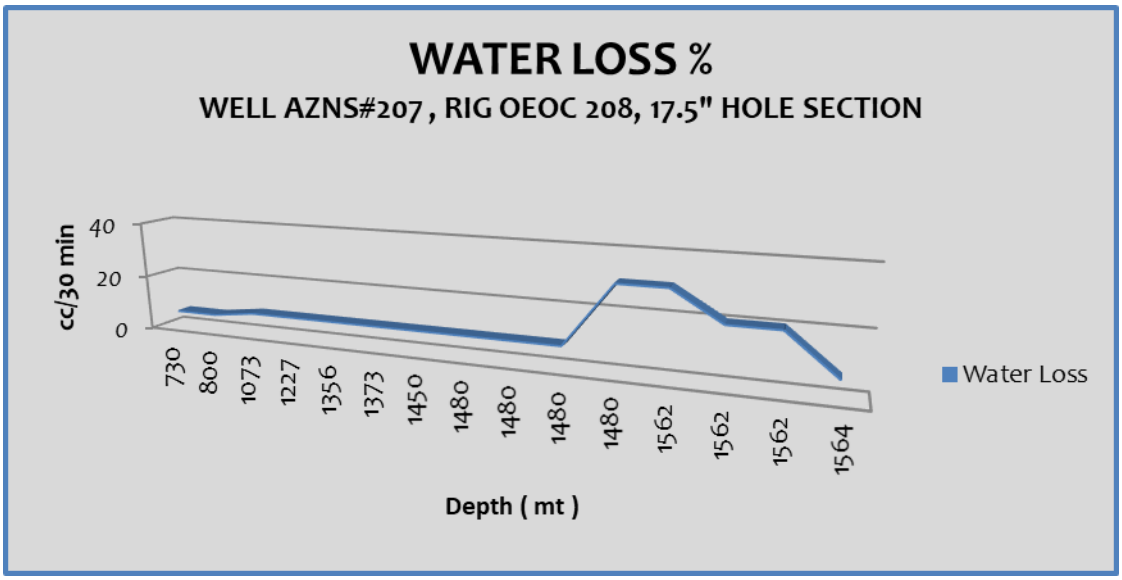


Figure 10-49: AZNS-207 17-1/2" (main hole) Waterloss Percentage Chart

Fluid Properties Recap (side track):

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	MBT	Solid %	Chloride	KCL (%Wt)	Calcium	Total Hardness	Mud Type
22-Nov-24	1429	85	42	14	12	2	9.5	7.5	19	180000	3	2800	3000	KCL/POL MUD
23-Nov-24	1429	85	42	14	12	2	9.5	7.5	19	180000	3	2800	3000	KCL/POL MUD
24-Nov-24	1429	85	41	13	11	4	9.6	7.5	11	180000	3	2800	3000	KCL/POL MUD
25-Nov-24	1440	85	40	12	10	4	9.6	7.5	19	180000	3	3000	3200	KCL/POL MUD
26-Nov-24	1447	85	40	12	10	4	9.7	7.5	19	180000	3	3000	3200	KCL/POL MUD
27-Nov-24	1472	85	40	12	10	4	9.4	7.5	19	180000	3	2880	3080	KCL/POL MUD
28-Nov-24	1507	85	40	14	10	4	9.4	7.5	19	180000	3	3000	3200	KCL/POL MUD
29-Nov-24	1552	85	40	14	10	4	9.5	7.5	19	180000	3	3000	3200	KCL/POL MUD
30-Nov-24	1552	85	40	14	10	4	9.5	7.5	19	180000	3	3000	3200	KCL/POL MUD
1-Dec-24	1571	85	41	13	10	4	9.5	7.5	19	180000	3	3000	3200	KCL/POL MUD
2-Dec-24	1592	85	42	15	10	4	9.5	7.5	19	180000	3	3000	3200	KCL/POL MUD
3-Dec-24	1594	85	41	14	10	4	9.5	7.5	19	180000	3	3000	3200	KCL/POL MUD
4-Dec-24	1616	85	41	13	10	4	9.5	7.5	19	180000	3	3000	3200	KCL/POL MUD
5-Dec-24	1617.5	85	40	14	10	3	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD
6-Dec-24	1636	85	40	14	9	3	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD
7-Dec-24	1649	85	40	14	9	2	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD
8-Dec-24	1649	85	41	15	10	2	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD
9-Dec-24	1648	85	41	15	10	2	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD
10-Dec-24	1649	85	41	15	10	2	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD
11-Dec-24	1649	85.5	41	15	10	2	9.5	7.5	19	180000	4	3000	3200	KCL/POL MUD

Drilling Start

Drilling End

Figure 10-50: AZNS-207 17-1/2" (side track) Fluid Properties Recap Table

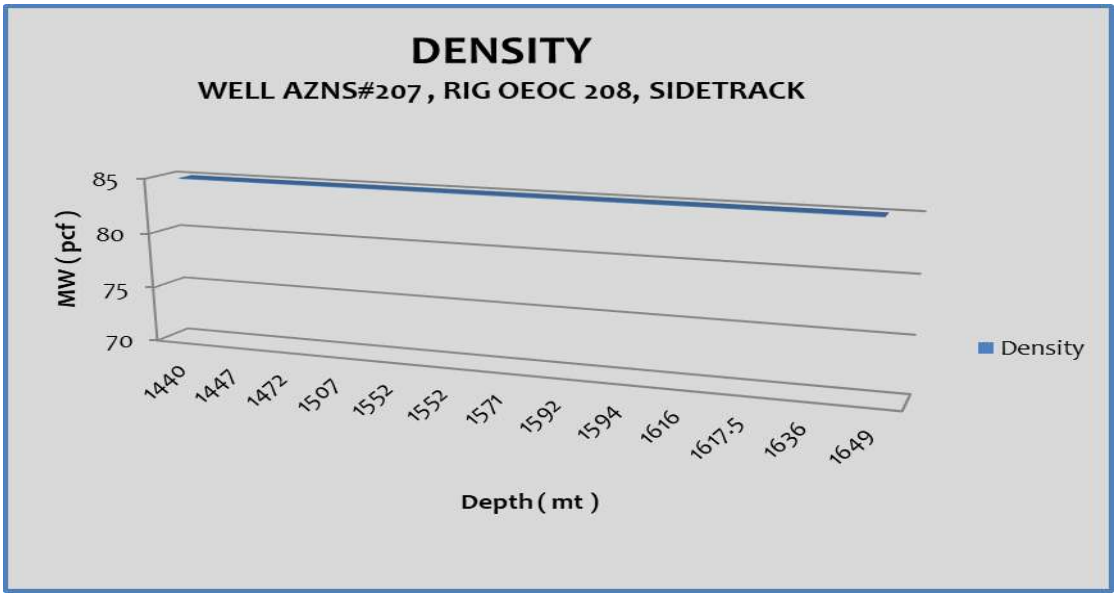


Figure 10-51: AZNS-207 17-1/2" (side track) Density Chart

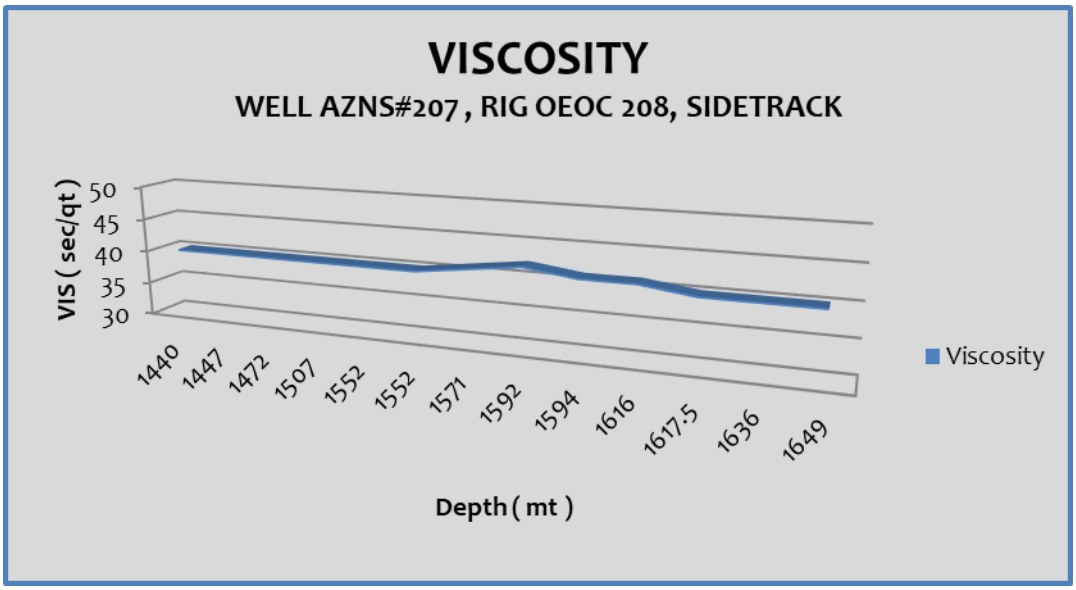


Figure 10-52: AZNS-207 17-1/2" (side track) Viscosity Chart

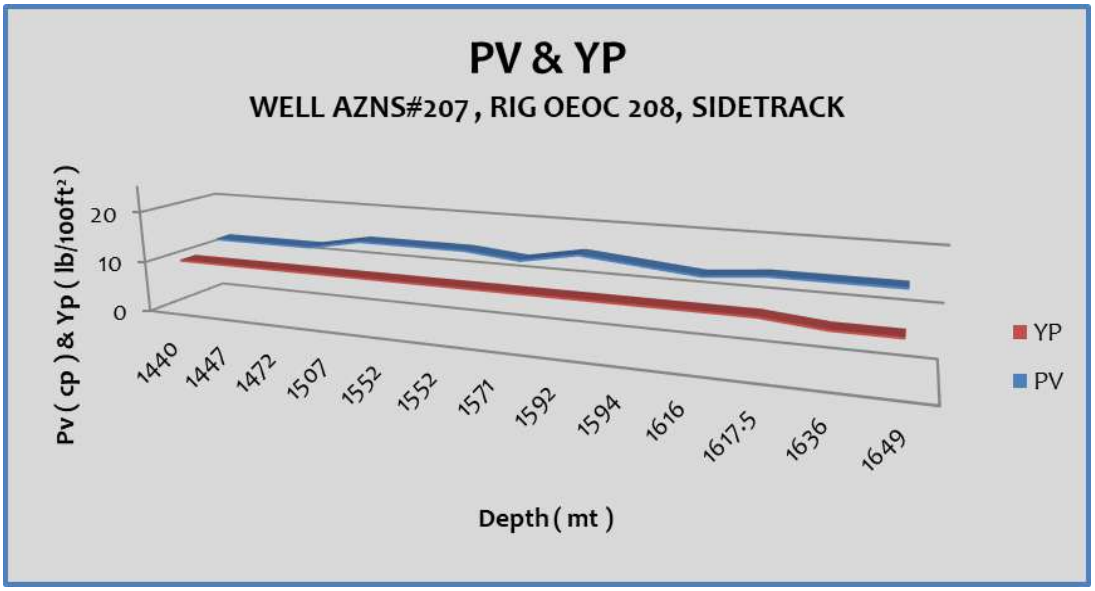


Figure 10-53: AZNS-207 17-1/2" (side track) PV & YP Chart

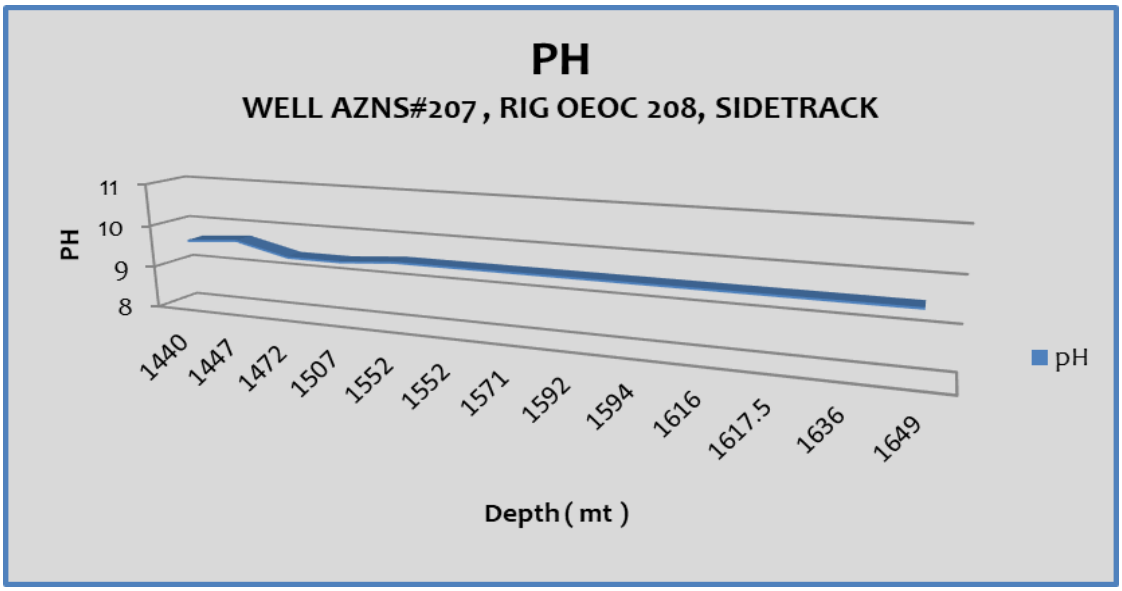


Figure 10-54: AZNS-207 17-1/2" (side track) PH Chart

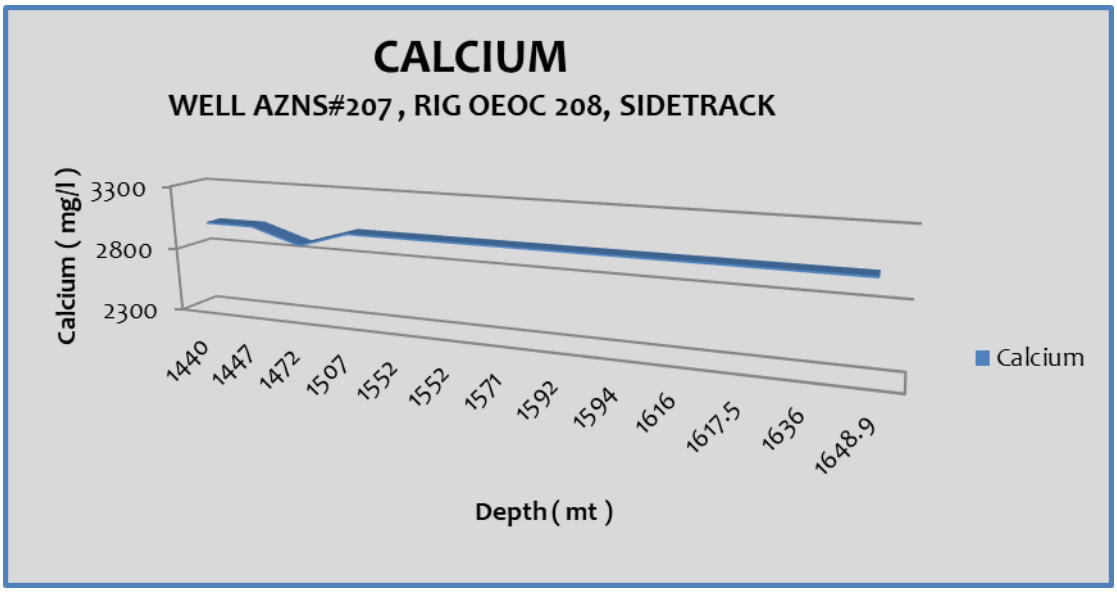


Figure 10-55: AZNS-207 17-1/2" (side track) Calcium Chart

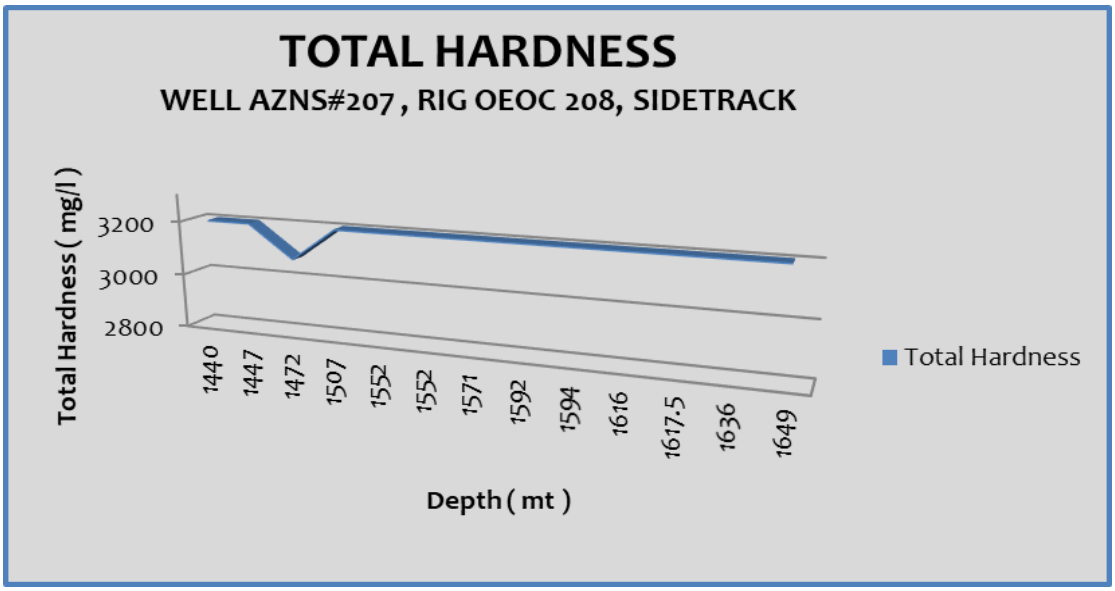


Figure 10-56: AZNS-207 17-1/2" (side track) Total Hardness Chart

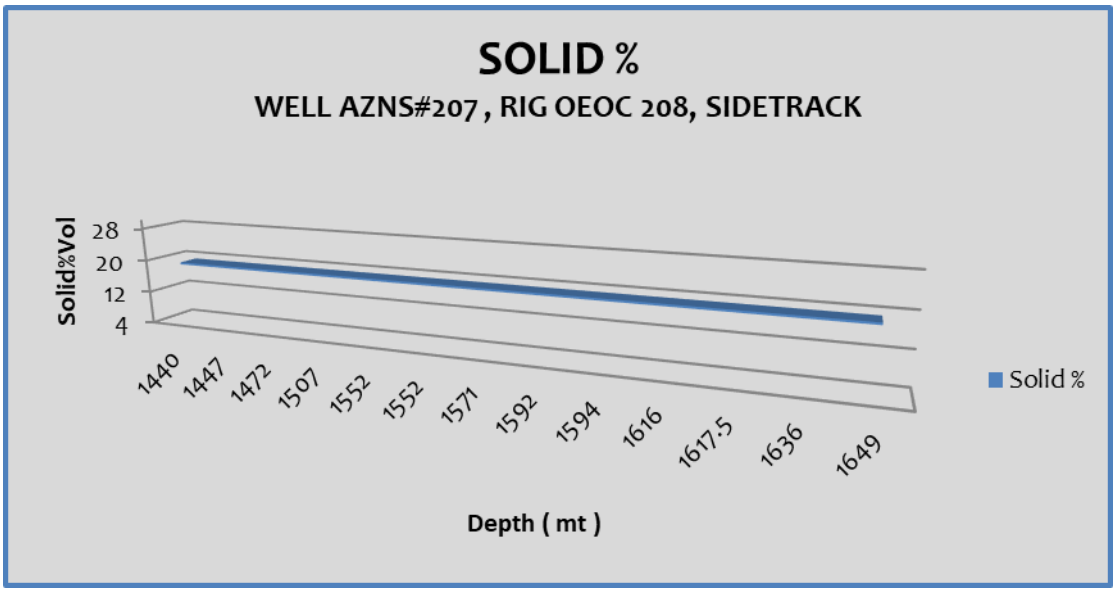


Figure 10-57: AZNS-207 17-1/2" (side track) Solid Percentage Chart

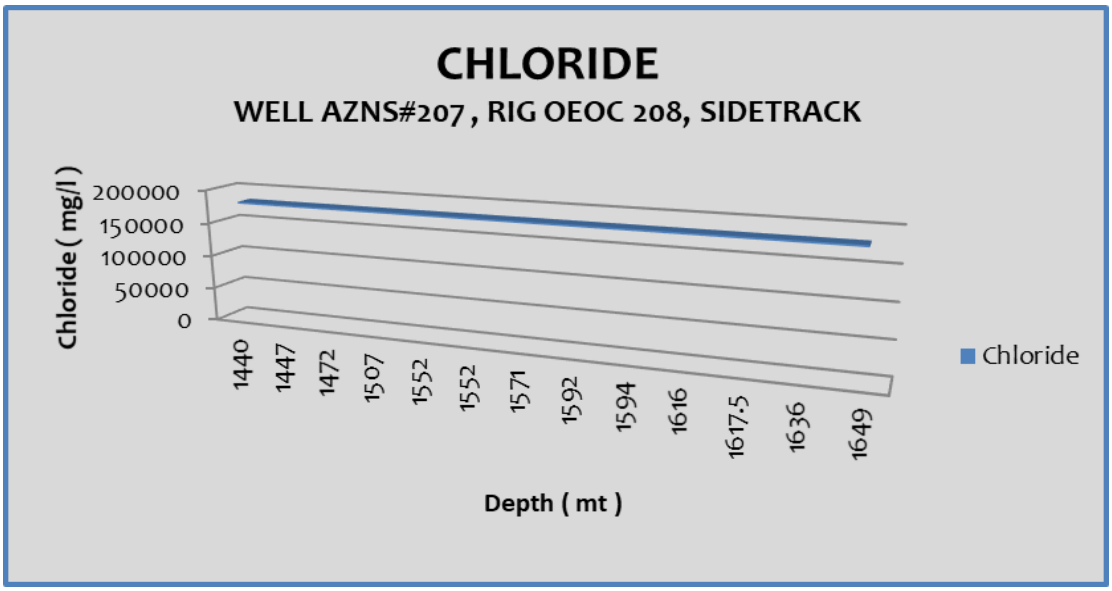


Figure 10-58: AZNS-207 17-1/2" (side track) Chloride Chart

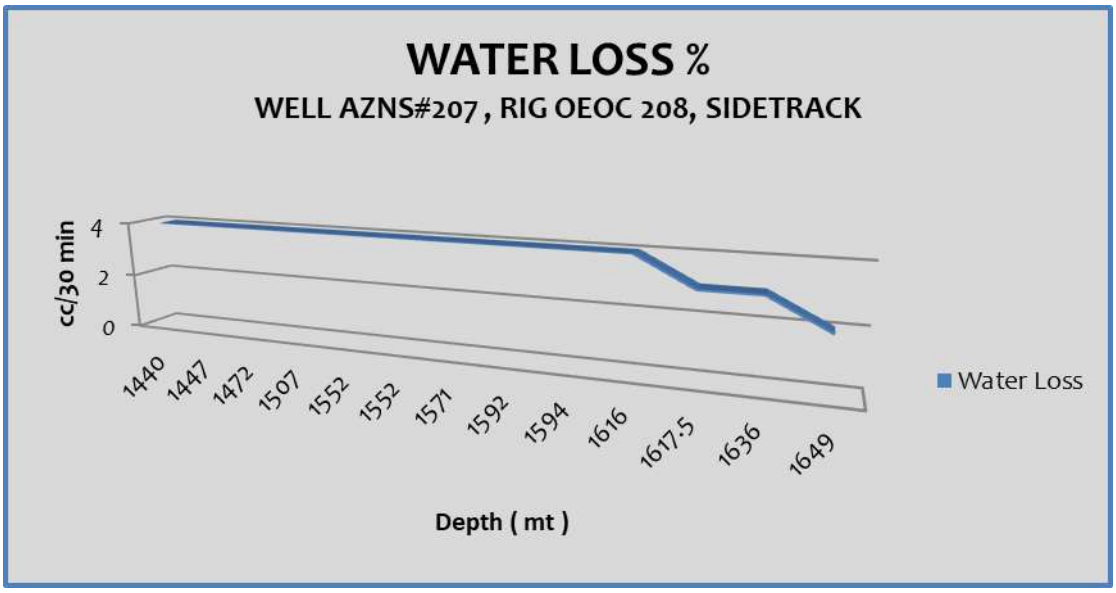


Figure 10-59: AZNS-207 17-1/2" (side track) Waterloss Percentage Chart

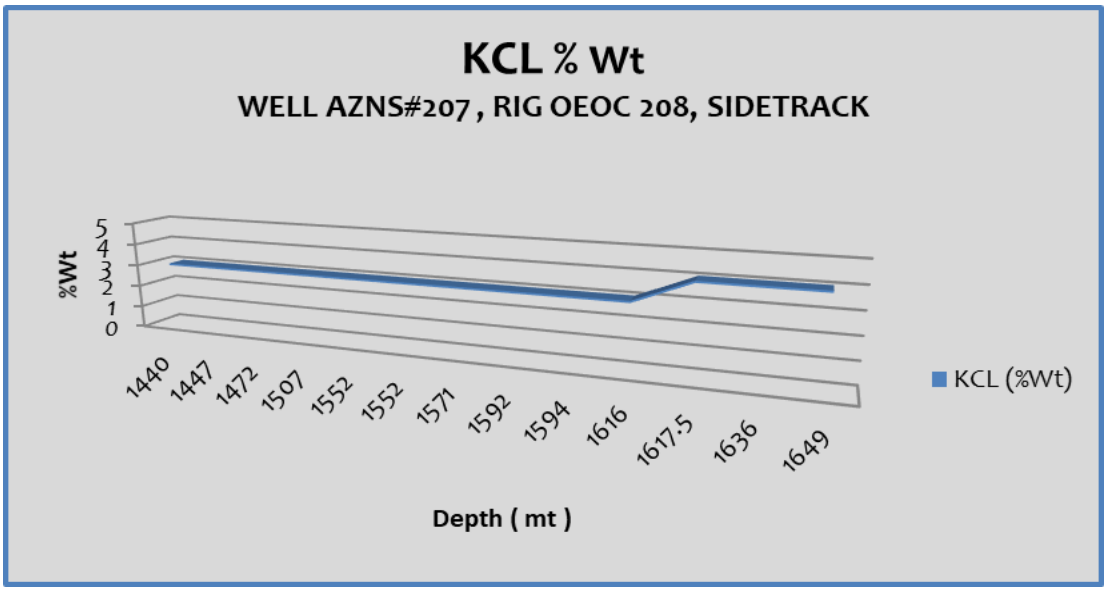


Figure 10-60: AZNS-207 17-1/2" (side track) KCl % Wt Chart

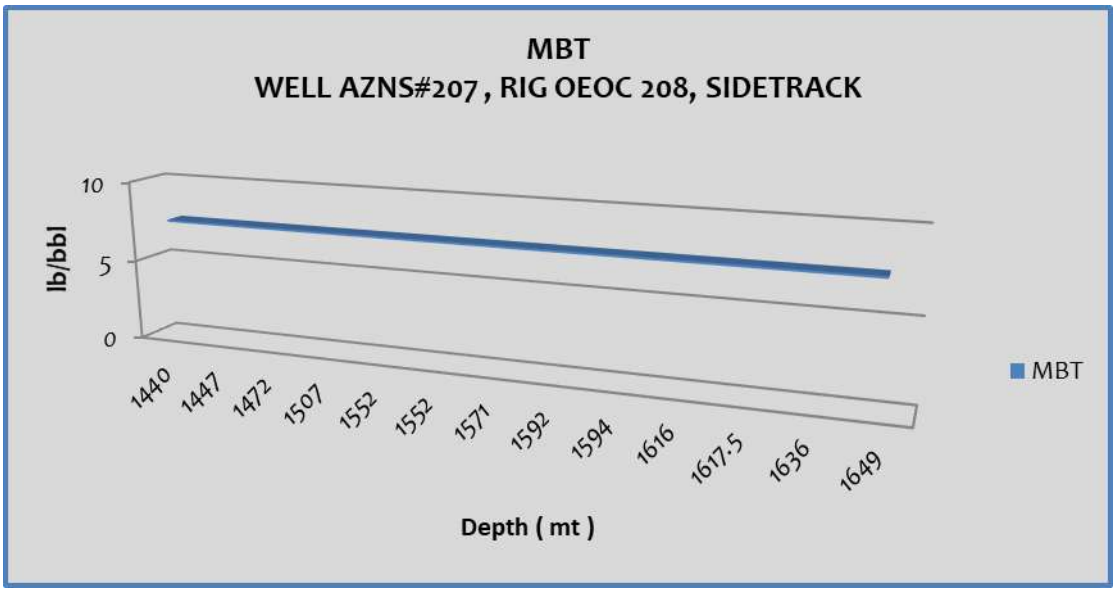


Figure 10-61: AZNS-207 17-1/2" (side track) MBT Chart

Solid Control Disscussion:

- **Shale Shakers:**

The OEOC 208 has 3 shale shakers were dressed with:

- **Shaker#1**: 140 - 200 Mesh Screen
- **Shaker#2**: 140 – 200 Mesh Screen
- **Shaker#3**: 140 - 200 Mesh Screen

Mud cleaner:

230/230/230 Mesh Screen

WELL AZNS#207 , RIG OEOC 208, SIDETRACK Solid Control Equipment Working Hr.s	
Shaker #1	1000
Shaker #2	1171
Shaker #3	976
Mud cleaner	138
Centrifuge#1	285
Centrifuge#2	187

Figure 10-62: AZNS-207 17-1/2" Solid Control Equipment Table

10.3 12-1/4" Hole Section

Sections Remark:

Operation Remark: Performed CMT Top Job.

RIH with 12 ¼" PDC Bit & D/O CMT to 1654 m and displace the well with 73 PCF KCL Poly Mud, Commenced drilling formation to 1831 with 1-15 BPH losses then POOH to surface.

RIH with new 12 ¼" new bit to bottom and cont. drilling formation to 2000 m with 1-6 BPH losses, POOH to surface.

RIH with C.Cut bit to 1890 m, spot 160 bbl. LCM pill and Performed CMT job then POOH to surface.

RIH with 12 ¼" TCI bit and D/O CMT to 1850 m and RIH to 2000 m, cont. drilling formation to 2150 m with 1-3 BPH losses and POOH to surface, meanwhile ran totco.

RIH with 12 ¼" PDC bit to bottom and resumed drilling formation to 2696.5 m, due to low progress stop drilling and POOH to surface.

RIH with new PDC bit to bottom and resumed drilling formation to 2738 m, POOH to surface due to drop spp, OBS, string twist off.

RIH with OVER-Shot to top of fish and catch same, POOH to surface.

RIH with 12 ¼" PDC bit to bottom, resumed drilling formation to 2868 m, POOH to surface with good hole condition.

RIH with 12 ¼" Bit to bottom and resumed drilling to 3006.7 with 1-4 BPH losses while increased MW to 79 PCF step by step, OBS, twist off string indication, POOH to surface.

RIH with OVER-Shot to top of fish and catch same, POOH to surface.

RIH with 12 ¼" bit to bottom, resumed drilling formation to 3027 m with 2-10 BPH losses, POOH to surface.

RIH with 12 ¼" BHA to bottom, resumed drilling formation to 3240 m with 2-8 BPH losses, OBS string twist off, POOH to surface.

RIH with OVER-Shot to top of fish and catch same, POOH to surface.

RIH with new PDC bit to bottom and drilling formation to 3620 m with 2-6 BPH losses while increased MW to 83 PCF, performed wiper trip and cont. drilling formation to 3872 m with 2-10 BPH losses while increased MW to 84 PCF and POOH to surface.

RIH with new 12 ¼" PDC bit to bottom and resumed drilling formation to 3891 m, with 25-30 BPH losses, OBS, string was plug, try to unplug string with NO SUCC, POOH to surface.

RIH with 12 ¼" PDC bit to bottom and resumed drilling to 3895 m, while decreased MW to 80 PCF, pump LCM pill and OPS, increased losses to 80-90 BPH and POOH to surface meanwhile added limestone chips F, M to active system.

RIH with C.Cut to 3100 m, Pump LCM pill and POOH to surface, while spot 140 bbl. LCM pill @ CSG shoe with 15-35 BPH losses.

Run 9 5/8" CSG & performed CMT job as per program.

Drilling Fluid Remark: Based on VIRA recommendation the carried bentonite mud from 26" hole section and added water to decreased MW to use for started this section up to 3895 m and then the hole was displaced with fresh 73 pcf S. Saturated/KCL/Polymer mud was employ to drilling this section.

It was tried to reach optimum inhibition by using KCl as main shale inhibitor to stabilize active formation by decreasing the tendency of to absorb, swell and slough-off in HV-pills. Chloride of active system kept to 170000-180000 ml/lit to improve hole condition.

It was tried to control FL by adding Green Starch. The MW increased by adding limestone up to 85 pcf.

SCE such as Shakers, mud cleaner and centrifuges were running to discard LGS while drilling this section. Several batches of premix/fresh mud were prepared occasionally and added to into active system intermittently in order to maintain recommended mud properties & surface Vol.

Beside that active circulation volume was treated frequently with essential chemical such Lime and caustic soda as Alkalinity controller to adjust pH, Soda Ash for control hardness, Starch lv as Fluid loss controller and KCl as shale inhibitor. In addition, Barite used to increase MW up to 91 pcf during drilling this section.

Also it was tried to extend hole cleaning by using HV Pill in different stage of operation.

Interval Information:

Interval III	1648.5– 3895 m	12 1/4" Hole Interval	9 5/8" Casing Set at 3895 meters

Drilling Fluid Types:

FLUID PROPERTIES RECAP					
		Drilling start	Range		Drilling End
MW (min)	pcf	73	73	85.5	80.0
Funnel Viscosity	sec/qt	39	36	49	44
PV	cps	12	8	19	15
YP	lb/100sq.ft	11	4	14	11
API Fluid loss	cc	2.3	1.4	3.4	3
pH		9.1	9	11.3	9.3
Solid	%	11	11	19	16
Cl (NaCl)	mg/L	123,000	118,000	180,000	180,000
Total Hardness	mg/L	2,400	1,560	4,600	1,600
Ca Hardness	mg/L	2,200	1,400	4,200	1,400

Figure 10-63: AZNS-207 12-1/4" Drilling Fluid Type Table

Material Consumption Analysis:

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Caustic Soda	174	55	9,570	lbs	0.54	ppb
Bentonite	1	2,200	2,200	lbs	0.124	ppb
Citric acid	18	55	990	lbs	0.056	ppb
KWIK SEAL M	2	55	110	gal	0.006	gpb
Oyster Shell F/M/C	810	55	44,550	lbs	2.512	ppb
Limestone Chips F/M/C	1,400	55	77,000	gal	4.341	gpb
Limestone	485	2,200	1,067,000	lbs	60.16	ppb
Green Starch	2,591	55	142,505	lbs	8.03	ppb
Salt (NACL)	614	55	33,770	lbs	1.90	ppb
Bicarbonate Sodium	33	55	1,815	lbs	0.10	ppb
Soda Ash	200	55	11,000	lbs	0.62	ppb
Mica F/M/C	766	55	42,130	lbs	2.38	ppb
Xanthan Gum	208	55	11,440	lbs	0.64	ppb
Wallnut shell C	238	55	13,090	lbs	0.74	ppb
KCL	90	2,200	198,000	lbs	11.16	ppb
Starch HT	40	55	2,200	lbs	0.12	ppb
Lime	533	55	29,315	lbs	1.65	ppb

Initial Volume	2,231.0	bbl
Total Volume Built	17,736.9	bbl
Volume received	415.0	bbl
Volume Returned	0.0	bbl
Total Volume Consumed	18,151	bbl
Volume Transfer to Next Section	2,232	bbl
Meter Drilled	2,246.5	m

Figure 10-64: AZNS-207 12-1/4" Material Consumption Analysis Table

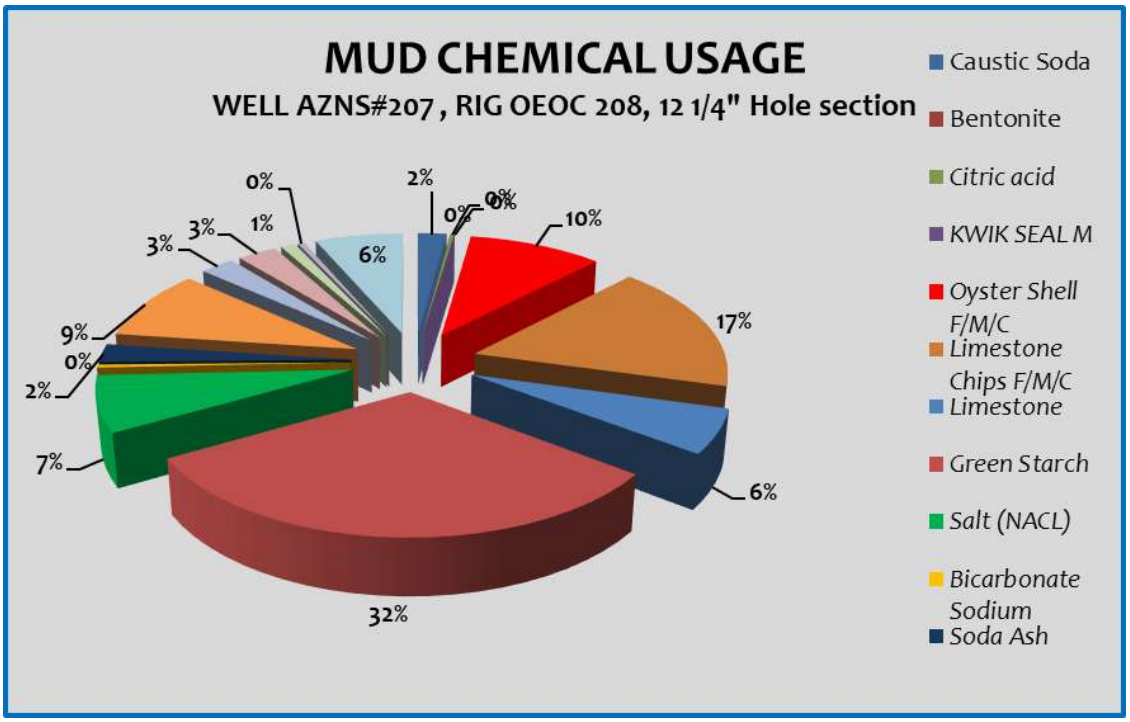


Figure 10-65: AZNS-207 12-1/4" Mud Chemical Usage Graph

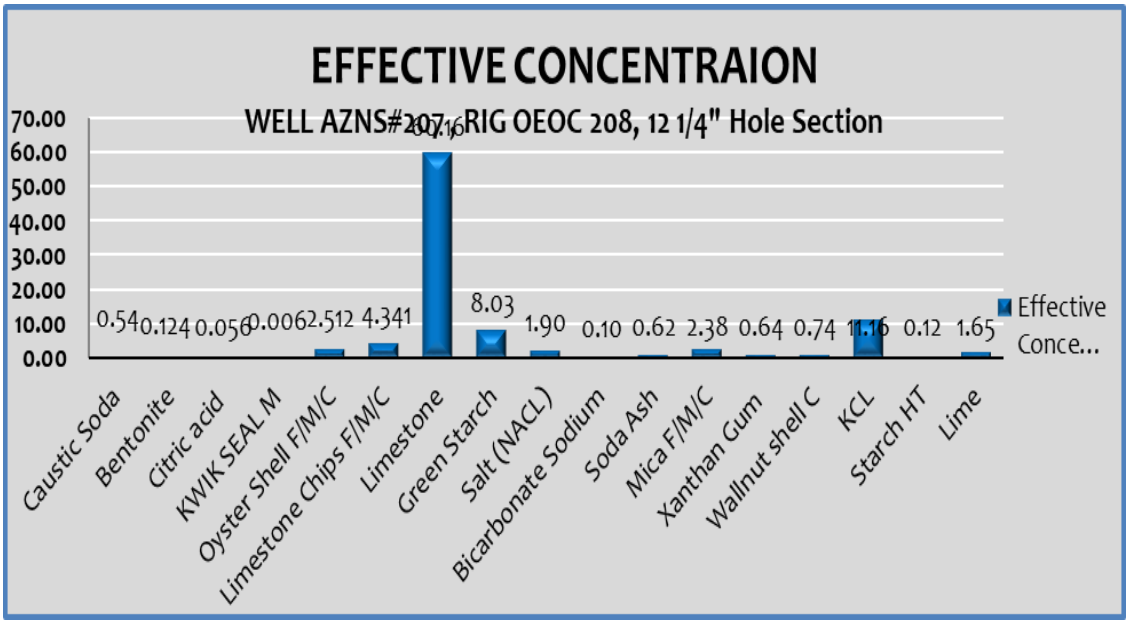


Figure 10-66: AZNS-207 12-1/4" Effective Concentration Chart

Material Consumption Analysis:

RIG: OEOC 208 , WELL: AZNS#207 , 12-1/4" Hole Section VOLUME ANALYSIS		
Initial Volume	bbls	2,231.0
Received Volume	bbls	415.0
Volume Return	bbls	0.0
Volume Built	bbls	17,736.9
Surface Losses/Dumped	bbls	7,146.0
Formation Losses	bbls	11,005.0
Total Losses	bbls	18,151.0
Volume Transfer Out	bbls	2,232

Figure 10-67: AZNS-207 12-1/4" Material Consumption Analysis Table

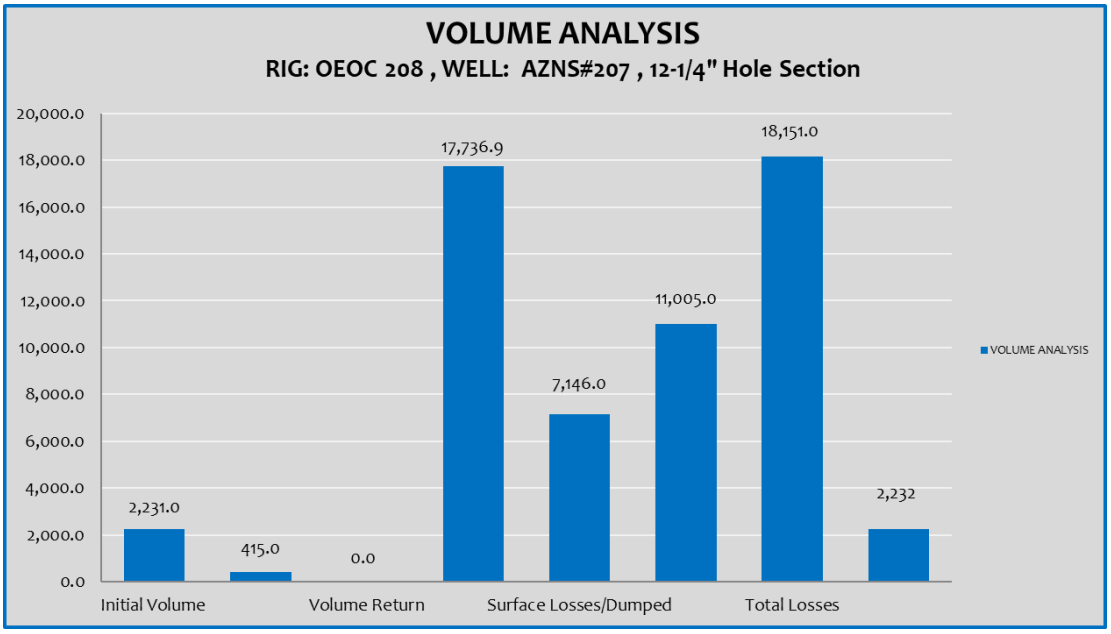


Figure 10-68: AZNS-207 12-1/4" Volume Analysis Chart

Daily Volume Break Down:

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
12-Dec-24	59	570.0	0	0
13-Dec-24	60	0.1	0	0
14-Dec-24	61	586.1	610	0
15-Dec-24	62	284.8	52	100
16-Dec-24	63	421.3	109	360
17-Dec-24	64	113.2	38	108
18-Dec-24	65	179.4	51	75
19-Dec-24	66	112.3	84	160
20-Dec-24	67	301.8	266	100
21-Dec-24	68	674.9	728	0
22-Dec-24	69	361.8	716	48
23-Dec-24	70	526.8	452	38
24-Dec-24	71	35.3	0	24
25-Dec-24	72	232.7	49	40
26-Dec-24	73	237.0	78	72
27-Dec-24	74	452.5	100	96
28-Dec-24	75	338.0	128	55
29-Dec-24	76	0.6	308	18
30-Dec-24	77	216.5	44	48
31-Dec-24	78	211.8	84	48
1-Jan-25	79	95.1	20	36
2-Jan-25	80	0.0	0	24
3-Jan-25	81	131.0	68	65
4-Jan-25	82	105.1	38	36
5-Jan-25	83	105.8	100	55
6-Jan-25	84	120.0	81	42
7-Jan-25	85	0.0	27	24
8-Jan-25	86	114.6	0	24
9-Jan-25	87	0.3	79	45
10-Jan-25	88	115.2	38	28
11-Jan-25	89	0.1	36	40
12-Jan-25	90	115.2	58	54
13-Jan-25	91	209.0	105	90
14-Jan-25	92	200.3	70	96
15-Jan-25	93	353.0	34	192

16-Jan-25	94	96.1	0	80
17-Jan-25	95	123.7	40	60
18-Jan-25	96	59.1	30	48
19-Jan-25	97	0.8	60	60
20-Jan-25	98	139.3	60	78
21-Jan-25	99	123.5	0	72
22-Jan-25	100	144.5	38	96
23-Jan-25	101	130.0	84	96
24-Jan-25	102	124.9	58	96
25-Jan-25	103	120.1	48	72
26-Jan-25	104	268.9	78	72
27-Jan-25	105	227.4	101	72
28-Jan-25	106	230.9	93	68
29-Jan-25	107	134.8	95	72
30-Jan-25	108	422.4	150	168
31-Jan-25	109	387.7	78	190
1-Feb-25	110	614.9	101	280
2-Feb-25	111	616.0	111	472
3-Feb-25	112	1,098.2	111	720
4-Feb-25	113	1,214.5	200	960
5-Feb-25	114	1,384.5	55	1,760
6-Feb-25	115	1,453.8	55	1,896
7-Feb-25	116	1,071.0	109	798
8-Feb-25	117	7.0	10	334
9-Feb-25	118	5.0	10	72
10-Feb-25	119	16.3	720	72
11-Feb-25	120	0.0	0	0
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		17,737	7,146	11,005

Figure 10-69: AZNS-207 12-1/4" Daily Volume Break Down Table

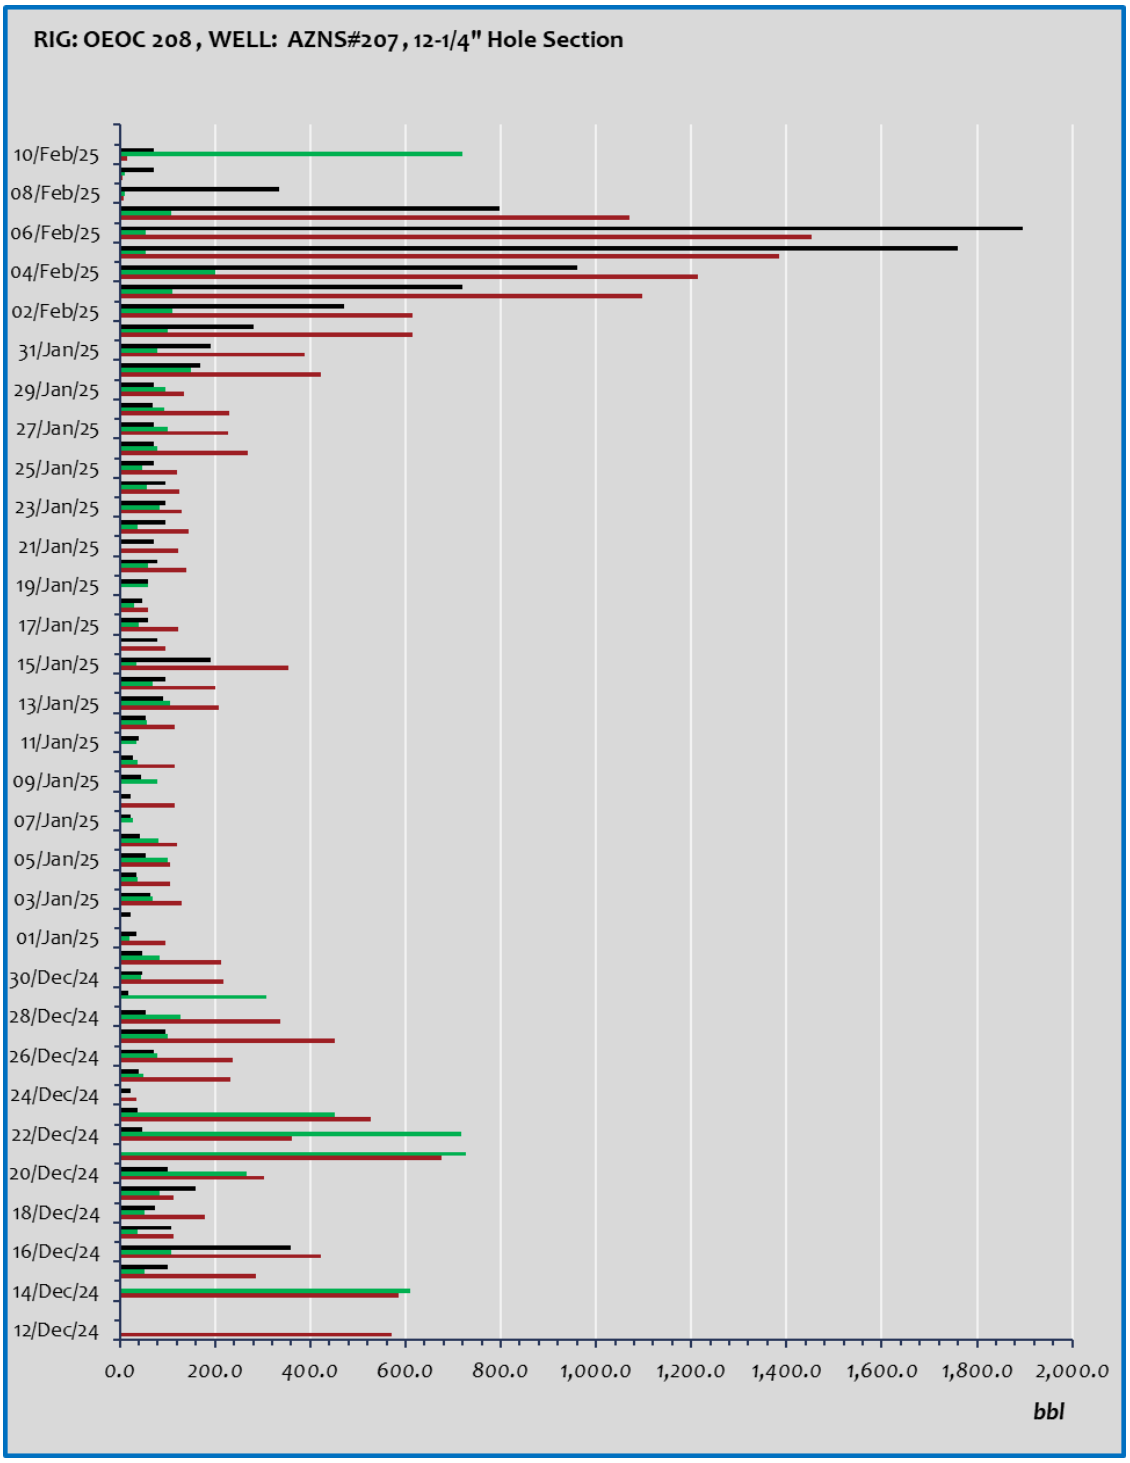


Figure 10-70: AZNS-207 12-1/4” Daily Volume Break Down Chart

Interval Loss Distribution:

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
12-Dec-24	59	570.0	0	0	0	0	0	0	0	0	0
13-Dec-24	60	0.1	0	0	0	0	0	0	0	0	0
14-Dec-24	61	586.1	500	45	0	0	0	0	35	0	30
15-Dec-24	62	284.8	40	12	0	0	0	0	0	100	0
16-Dec-24	63	421.3	37	36	0	0	0	0	0	360	36
17-Dec-24	64	113.2	0	18	0	0	0	0	0	108	20
18-Dec-24	65	179.4	0	36	0	0	0	0	0	75	15
19-Dec-24	66	112.3	0	24	0	0	0	0	30	160	30
20-Dec-24	67	301.8	170	12	0	0	25	0	0	100	59
21-Dec-24	68	674.9	550	36	0	0	0	0	32	0	110
22-Dec-24	69	361.8	650	36	0	0	0	0	0	48	30
23-Dec-24	70	526.8	375	32	0	0	15	0	0	38	30
24-Dec-24	71	35.3	0	0	0	0	0	0	0	24	0
25-Dec-24	72	232.7	0	24	0	0	0	0	10	40	15
26-Dec-24	73	237.0	0	48	0	0	0	0	0	72	30
27-Dec-24	74	452.5	25	48	0	0	0	0	0	96	27
28-Dec-24	75	338.0	25	48	0	30	0	0	0	55	25
29-Dec-24	76	0.6	260	18	0	6	0	0	24	18	0
30-Dec-24	77	216.5	0	24	0	0	0	0	0	48	20
31-Dec-24	78	211.8	0	36	0	16	0	0	12	48	20
1-Jan-25	79	95.1	20	0	0	0	0	0	0	36	0
2-Jan-25	80	0.0	0	0	0	0	0	0	0	24	0
3-Jan-25	81	131.0	10	30	0	28	0	0	0	65	0
4-Jan-25	82	105.1	15	8	0	0	0	0	0	36	15
5-Jan-25	83	105.8	0	36	0	34	0	0	10	55	20
6-Jan-25	84	120.0	10	28	0	16	0	0	12	42	15
7-Jan-25	85	0.0	15	0	0	0	0	0	12	24	0
8-Jan-25	86	114.6	0	0	0	0	0	0	0	24	0
9-Jan-25	87	0.3	15	25	0	14	0	0	0	45	25
10-Jan-25	88	115.2	15	8	0	0	0	0	15	28	0
11-Jan-25	89	0.1	0	16	0	0	10	0	10	40	0
12-Jan-25	90	115.2	0	18	0	10	0	0	0	54	30
13-Jan-25	91	209.0	0	60	0	15	0	0	0	90	30
14-Jan-25	92	200.3	0	48	0	12	0	0	0	96	10
15-Jan-25	93	353.0	10	8	0	0	16	0	0	192	0

Figure 10-71: AZNS-207 12-1/4" Interval Loss Distribution Table

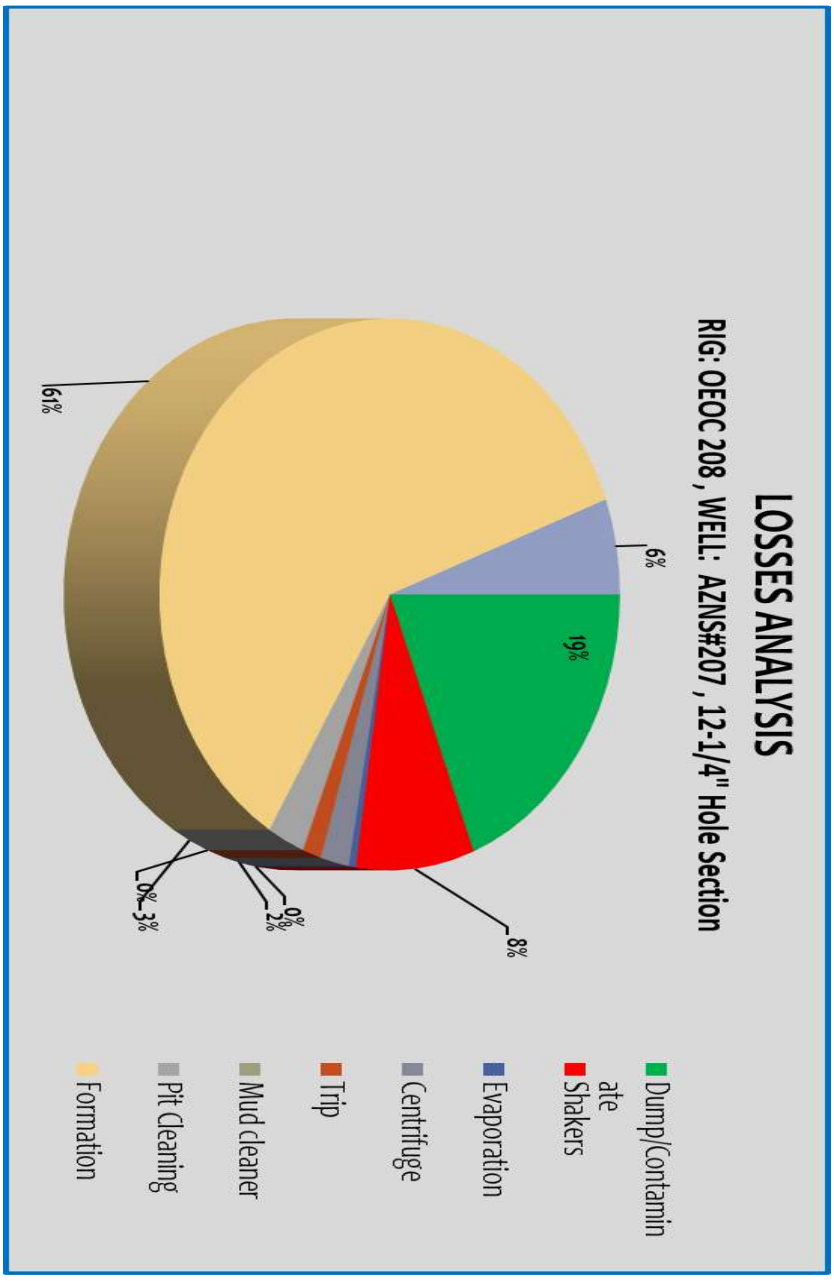


Figure 10-72: AZNS-207 12-1/4” Interval Loss Analysis Graph

Interval Fluid Properties Recap:

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	Solid %	Chloride	Calcium	Total Hardness	Mud Type
12-Dec-24	1648.9	85.5	41	15	10	2	9.5	19	180000	3000	3200	SALT/POL MUD
13-Dec-24	1648.5	85.5	41	15	10	2	9.5	19	180000	3000	3200	SALT/POL MUD
14-Dec-24	1654	73	39	12	11	2.3	9.1	11	123000	2200	2400	SALT/POL MUD
15-Dec-24	1713	73	39	13	10	3	9.1	11	123000	2200	2400	SALT/POL MUD
16-Dec-24	1828	73	39	13	11	2.8	9.2	11	122000	2200	2400	SALT/POL MUD
17-Dec-24	1861	74	39	12	11	2.8	9.2	12	122000	2200	2400	SALT/POL MUD
18-Dec-24	1994	75	40	11	9	2.8	9.3	13	120000	2480	2640	SALT/POL MUD
19-Dec-24	2000	75	40	11	9	2.8	9.3	13	120000	2560	2660	SALT/POL MUD
20-Dec-24	2000	75	39	10	9	3.4	10.1	13	120000	3120	3320	SALT/POL MUD
21-Dec-24	2000	75	36	8	4	N.C	11.3	13	118000	4200	4600	SALT/POL MUD
22-Dec-24	2114	77	38	10	9	2.5	9.5	13	138000	2680	2840	SALT/POL MUD
23-Dec-24	2150	77	38	10	9	2.5	9.5	13	144000	2680	2840	SALT/POL MUD
24-Dec-24	2150	77	38	10	8	2.5	9.5	13	140000	2640	2840	SALT/POL MUD
25-Dec-24	2189	77	39	10	9	2.5	9.5	13	143000	2640	2840	SALT/POL MUD
26-Dec-24	2339	77	40	12	11	2.5	9.5	13	147000	2200	2400	SALT/POL MUD
27-Dec-24	2509	78	40	12	11	2.5	9.5	13	150000	2200	2400	SALT/POL MUD
28-Dec-24	2685	78	40	12	11	2.4	9.5	13	160000	2200	2400	SALT/POL MUD
29-Dec-24	2696	78	40	12	11	2.4	9.5	13	160000	2200	2400	SALT/POL MUD
30-Dec-24	2737	78	40	12	11	2.4	9.5	13	164000	2120	2320	SALT/POL MUD
31-Dec-24	2810	78	40	12	11	2.4	9.5	13	164000	1920	2120	SALT/POL MUD
1-Jan-25	2810	78	40	12	11	2.4	9.5	13	164000	1920	2120	SALT/POL MUD
2-Jan-25	2810	78	40	12	11	2.4	9.5	13	164000	1920	2120	SALT/POL MUD
3-Jan-25	2868	79	40	13	11	2.4	9.5	14	166000	1840	2000	SALT/POL MUD
4-Jan-25	2870	79	40	13	11	2.2	9.5	14	166000	1840	2000	SALT/POL MUD
5-Jan-25	2941	79	40	13	11	1.4	9.5	14	168000	1800	1960	SALT/POL MUD
6-Jan-25	3006	79	40	13	11	1.8	9.5	14	170000	1800	1960	SALT/POL MUD
7-Jan-25	3006	79	40	13	11	1.8	9.5	14	170000	1800	1960	SALT/POL MUD
8-Jan-25	3006	79	41	13	11	2	9.5	14	170000	1800	1960	SALT/POL MUD
9-Jan-25	3015	80	42	14	11	1.8	9.5	15	170000	1840	2000	SALT/POL MUD
10-Jan-25	3023.5	80	42	14	11	1.8	9.4	15	170000	1840	2000	SALT/POL MUD
11-Jan-25	3027	80	42	14	11	1.8	9.4	15	170000	1840	2000	SALT/POL MUD
12-Jan-25	3054	80	43	14	11	1.7	9.5	15	172000	1840	2000	SALT/POL MUD
13-Jan-25	3140	80.5	43	14	11	1.7	9.5	15	173000	1840	2000	SALT/POL MUD
14-Jan-25	3236	81	44	15	12	1.7	9.4	16	176000	1840	2000	SALT/POL MUD
15-Jan-25	3240	81.5	44	15	12	1.7	9.4	16	176000	1840	2000	SALT/POL MUD
16-Jan-25	3240	81.5	45	15	13	1.7	9.4	16	177000	1840	2000	SALT/POL MUD
17-Jan-25	3274	82	46	16	13	1.7	9.5	17	177000	1840	2000	SALT/POL MUD
18-Jan-25	3275	82	46	16	13	1.7	9.5	17	177000	1840	2000	SALT/POL MUD
19-Jan-25	3282	82	49	19	14	1.7	9.5	17	177000	1840	2000	SALT/POL MUD

20-Jan-25	3284.4	82	49	19	14	1.7	9.5	17	178000	1840	2000	SALT/POL MUD
21-Jan-25	3284.9	82	48	18	13	1.8	9.4	17	178000	1840	2000	SALT/POL MUD
22-Jan-25	3315	82	47	17	13	1.8	9.5	17	180000	1840	2000	SALT/POL MUD
23-Jan-25	3427	82	45	16	12	1.8	9.5	17	177000	1800	2000	SALT/POL MUD
24-Jan-25	3535	83	43	15	11	1.8	9.5	18	177000	1800	2000	SALT/POL MUD
25-Jan-25	3620	83	44	16	12	1.8	9.5	18	177000	1800	2000	SALT/POL MUD
26-Jan-25	3671	83	43	16	12	1.8	9.5	18	177000	1720	1920	SALT/POL MUD
27-Jan-25	3740	83	45	16	13	1.8	9.5	18	177000	1760	1960	SALT/POL MUD
28-Jan-25	3970	84	46	17	13	1.8	9.5	19	178000	1760	1960	SALT/POL MUD
29-Jan-25	3822	85	46	17	13	1.8	9.5	20	177000	1760	1960	SALT/POL MUD
30-Jan-25	3855	84	46	17	13	1.8	9.5	19	178000	1840	2040	SALT/POL MUD
31-Jan-25	3872	84	45	16	12	1.8	9.5	19	178000	1800	2000	SALT/POL MUD
1-Feb-25	3872	84	45	16	12	1.8	9.5	19	178000	1800	2000	SALT/POL MUD
2-Feb-25	3891	82.5	45	16	12	1.8	9.5	18	178000	1840	2040	SALT/POL MUD
3-Feb-25	3891	81	45	16	12	1.8	9.4	17	178000	1720	1880	SALT/POL MUD
4-Feb-25	3895	80	44	15	11	3	9.3	16	180000	1400	1600	SALT/POL MUD
5-Feb-25	3895	80	44	15	11	3	9.3	16	180000	1400	1600	SALT/POL MUD
6-Feb-25	3895	80	43	14	10	3	9	16	175000	1400	1560	SALT/POL MUD
7-Feb-25	3895	80	44	15	11	3	9.2	16	175000	1480	1640	SALT/POL MUD
8-Feb-25	3895	80	44	15	11	3	9.4	16	175000	1520	1680	SALT/POL MUD
9-Feb-25	3895	80	43	14	11	3	9.4	16	175000	1760	1920	SALT/POL MUD
10-Feb-25	3895	80	43	14	11	3	9.4	16	175000	1760	1920	SALT/POL MUD
11-Feb-25	3895	80	43	14	11	3.2	9.4	16	175000	1760	1920	SALT/POL MUD
Drilling Start												
Drilling End												

Figure 10-73: AZNS-207 12-1/4" Interval Fluid Properties Recap Table

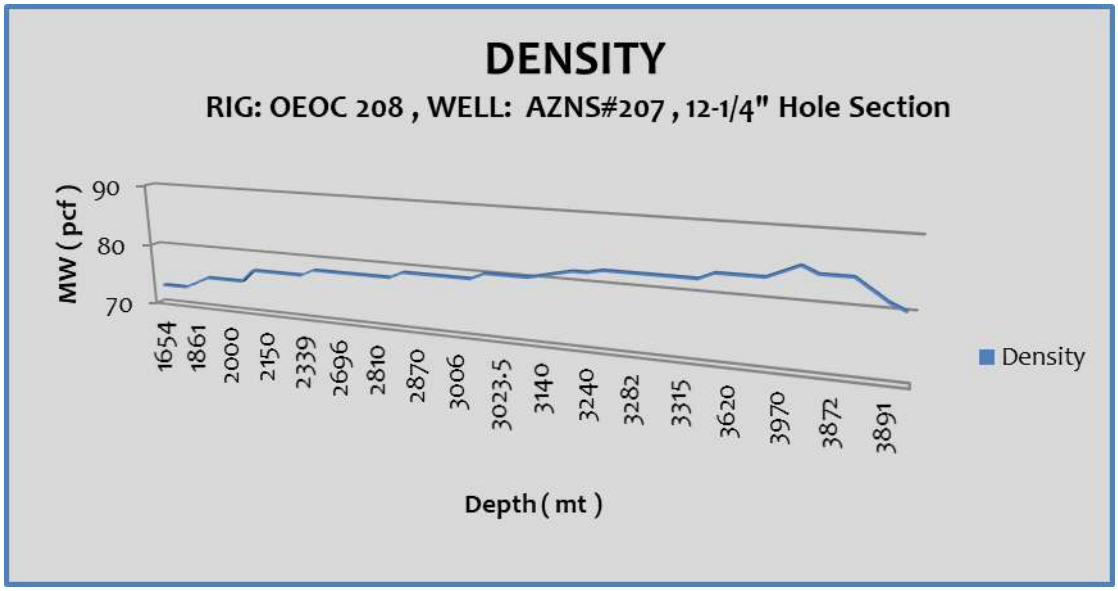


Figure 10-74: AZNS-207 12-1/4" Density Chart

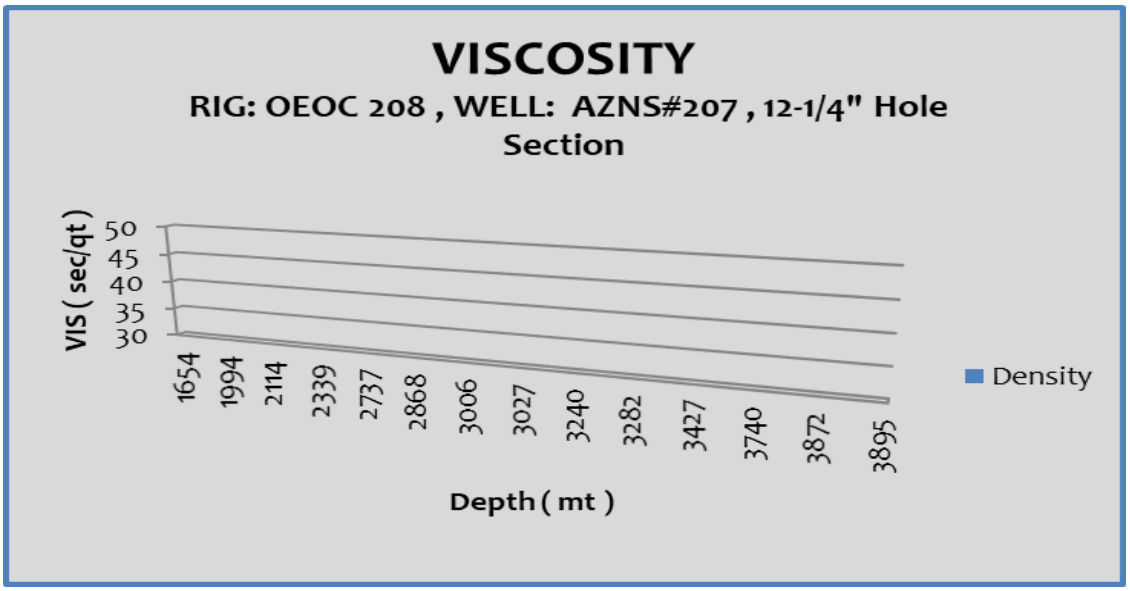


Figure 10-75: AZNS-207 12-1/4" Viscosity Chart

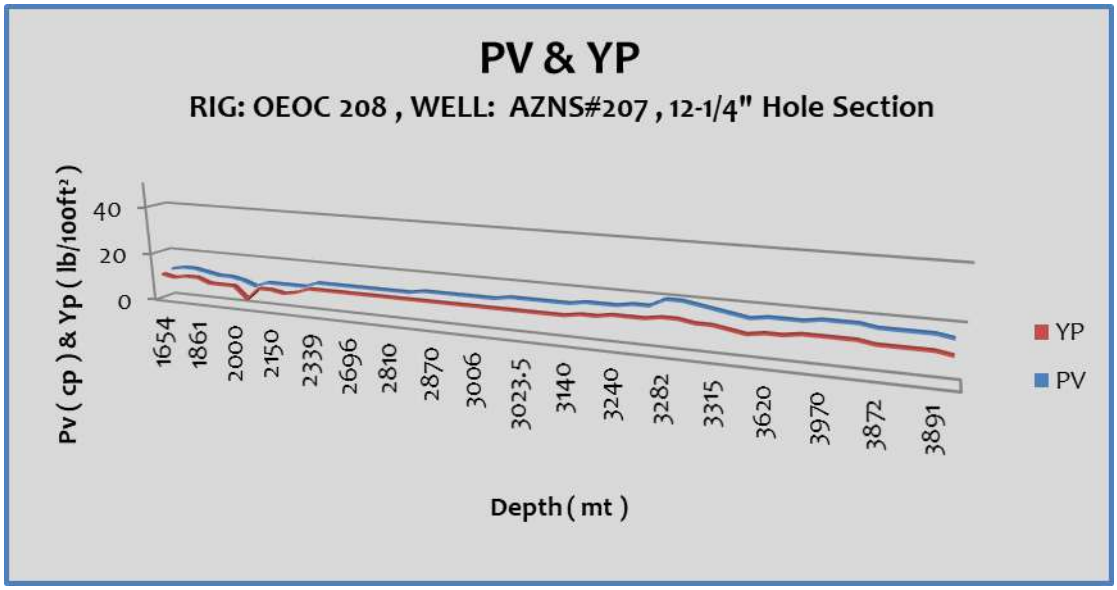


Figure 10-76: AZNS-207 12-1/4" PV & YP Chart

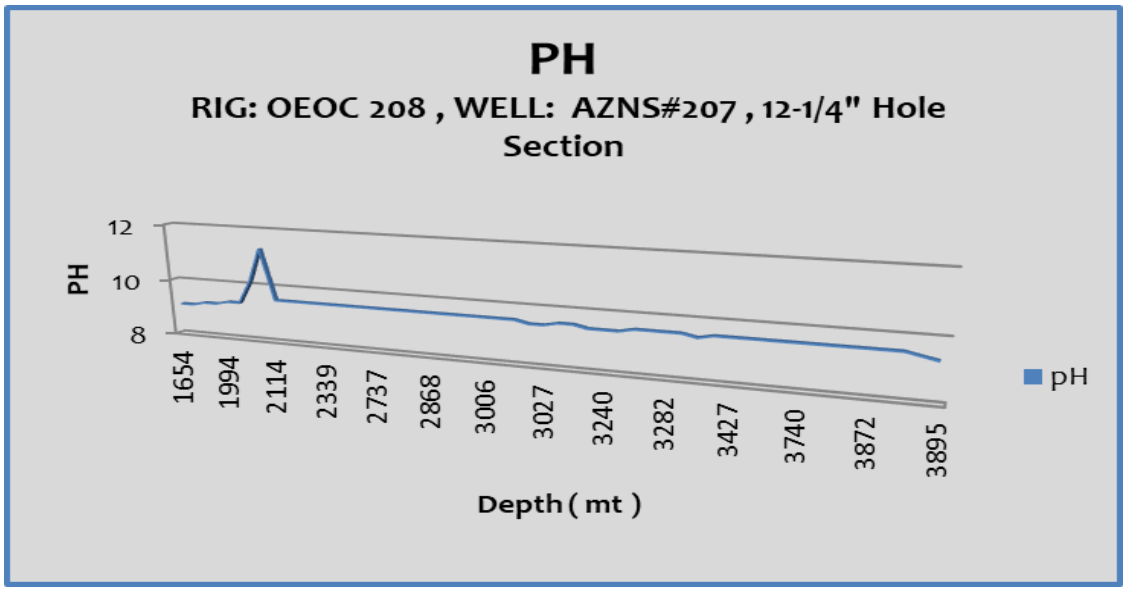


Figure 10-77: AZNS-207 12-1/4" pH Chart

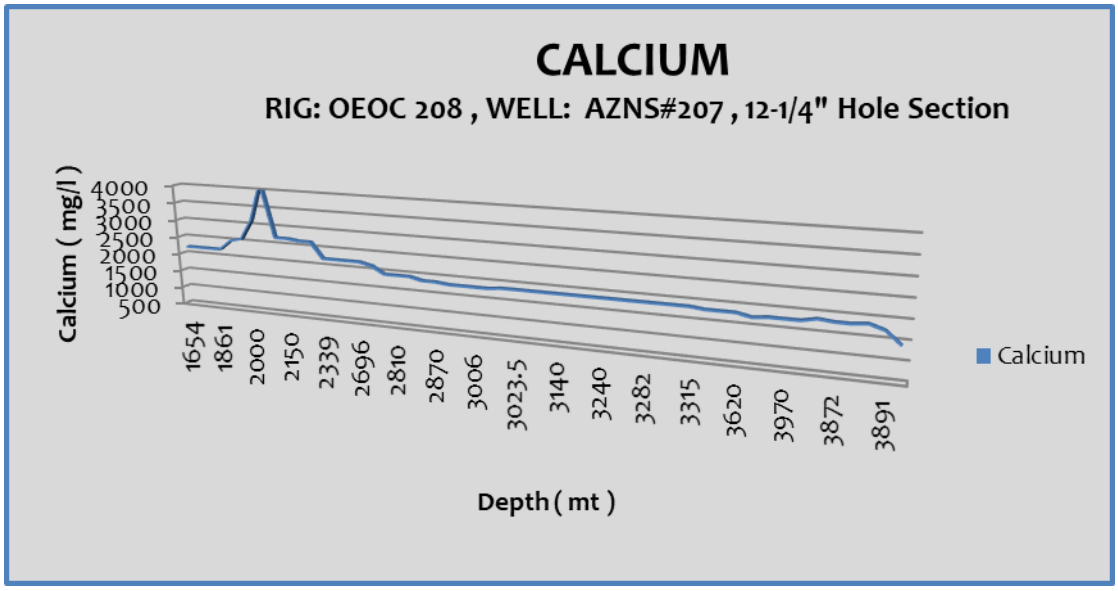


Figure 10-78: AZNS-207 12-1/4" Calcium Chart

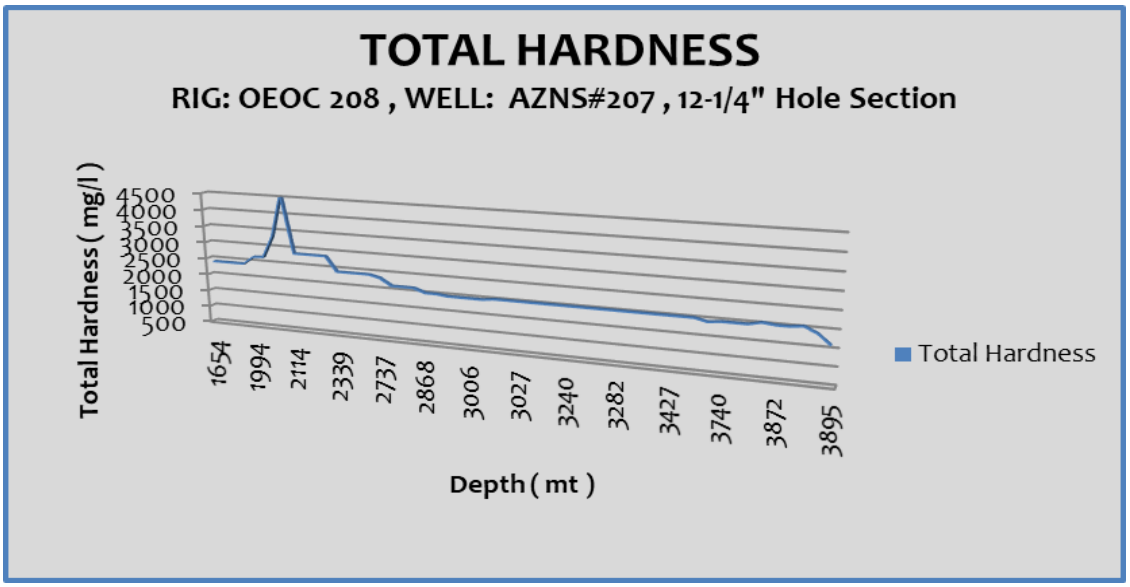


Figure 10-79: AZNS-207 12-1/4" Total Hardness Chart

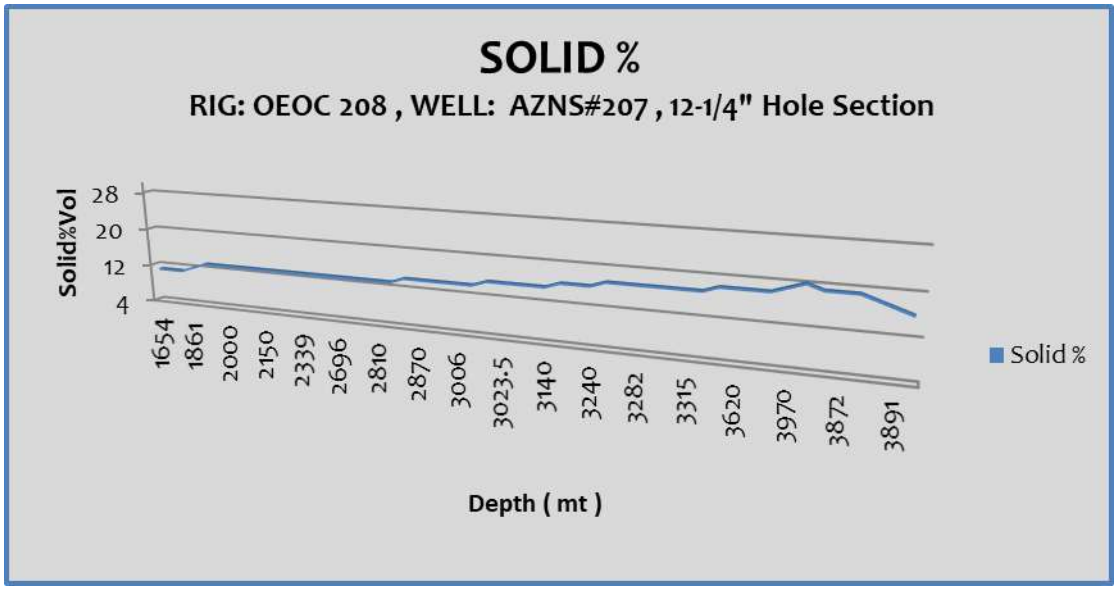


Figure 10-80: AZNS-207 12-1/4" Solid % Chart

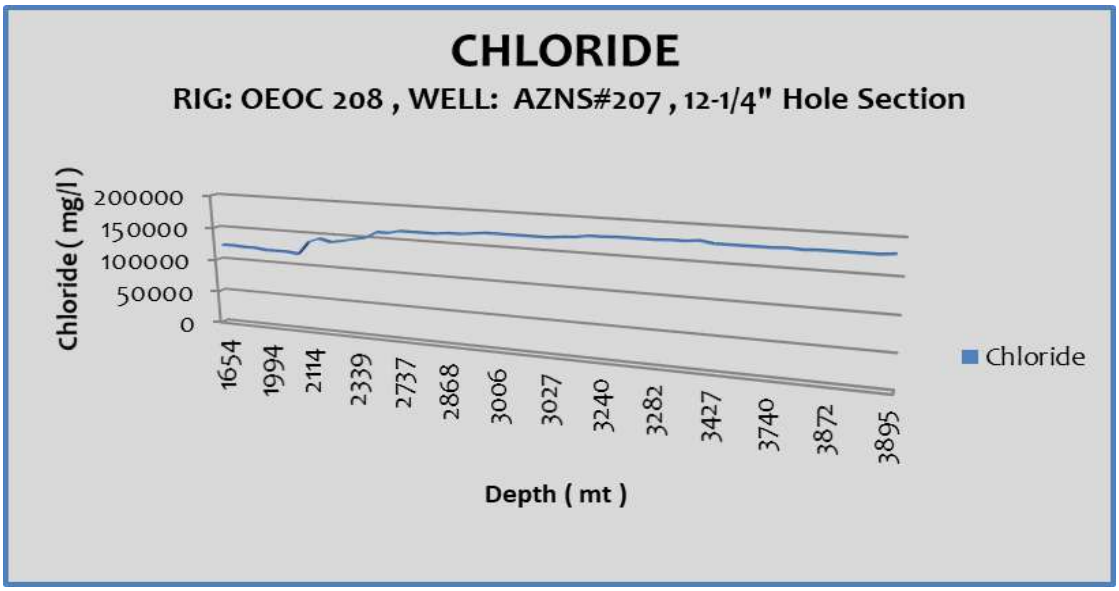


Figure 10-81: AZNS-207 12-1/4" Chloride Chart

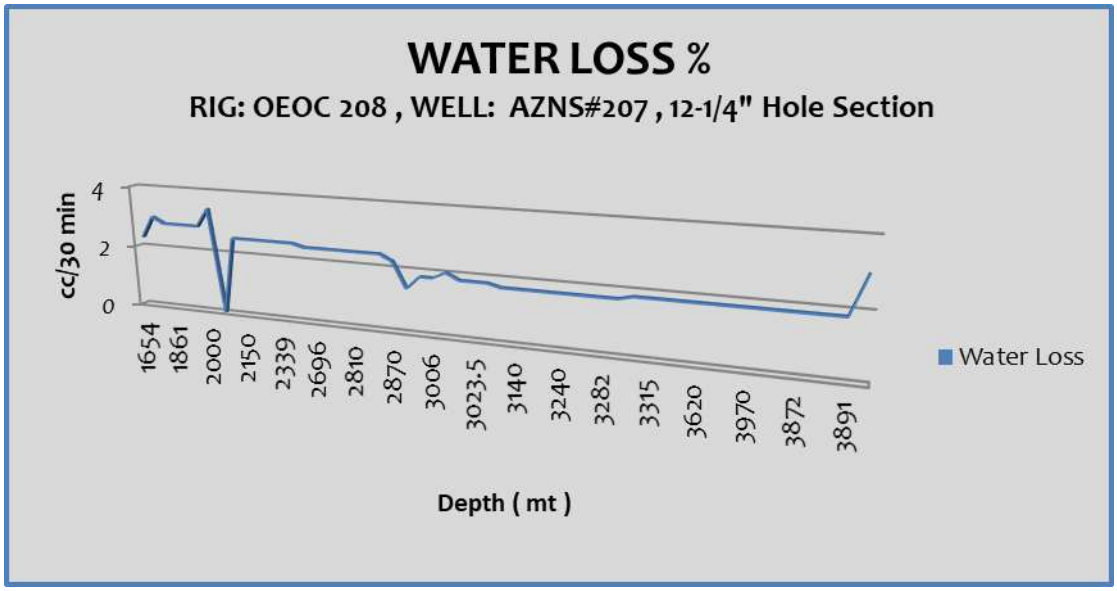


Figure 10-82: AZNS-207 12-1/4" Water Loss % Chart

Solid Control Disscusion:

• Shale Shakers:

Rig OEOC 208 has 3 shale shakers were dressed with:

- **Shaker#1**: 170-200 Mesh Screen
- **Shaker#2**: 170-200 Mesh Screen
- **Shaker#3**: 170-200 Mesh Screen

Centrifuges;

Derrick variable RPM

RIG: OEOC 208 , WELL: AZNS#207 , 12-1/4" Hole Section Solid Control Equipment Working Hr.s	
Swaco Derrick Shaker #1	1097
Swaco Derrick Shaker #2	1240
Swaco Derrick Shaker #3	872
Swaco Mud cleaner	3
Swaco Centrifuge#1	169
Chinese Centrifuge#2	22

Figure 10-83: AZNS-207 12-1/4" Solid Control Equipment Table

10.4 8-3/8" Hole Section

Sections Remark:

Operation Remark: Laid down 9 Joints 8-1/2" drill collar then RIH with HWDP 5" + D. Jar 6-1/2" + DC 6-1/2" + SST 8-3/8" to 3800m and W/D to 3867m then drilled out Medium to Hard cement, Plugs, Float Collar , Float Shoe after that drilling 8-3/8" Hole section to 3910m then due to working on TDS and Changing Saver sub Interrupted operation after that Continued drilling 8-3/8" Hole section to 3928m and circulated bottoms up then POOH to 3856m and Performed FIT to EMW 105pcf after that Worked on TDS and Ran Back to bottom then Displaced well with 100pcf mud after that Continued drilling 8-3/8" Hole section to 3964m Meanwhile Spotted 20bbl LCM Pill at 3963m then Continued drilling 8-3/8" Hole section to 4180m after that circulated bottoms up and POOH to 3980m then performed Condition trip to 3 Stands Above Shoe and Circulated slowly after that Ran Back to bottom then Pumped High Viscosity pill and Checked bottoms up Sample after that Spotted 50bbl High Viscosity Pill therefor POOH to surface.

Ran Full Suite/CDR/GR Logs Then Performed logging run #1 (Resistivity/Sonic/CDR-GR) and run #2 (Nuclear Run) LDT/CNT/NGS after that M/U logging assembly as run #3 SBT/CCL/VDL-GR then Surface checked with satisfactory results therefor RIH to 700m then R/D logging unit after that Slipped and Cut drilling line.

Made up 8-3/8" PDC bit and RIH to 4180m (bottom) then circulated after that uniformed mud Spotted 60bbl High Viscosity pill at bottom therefor POOH on elevator with good hole condition from 4180m bottom to surface.

RIH 7' Liner and assembly as per program to 4180m then tagged bottom after that Set 7" liner hanger and Performed cement as per plan therefor POOH to 3552m then Flushed string and Continued POOH to surface therefor laid down Liner hanger setting tools.

Made up 8-3/8" PDC Bit and RIH to 3650m then Commenced Drilling out cement to 3786m (7"L. Lap) after that Circulated bottoms up till shakers cleaned then POOH to surface.

Made up 5-7/8"R. Bit and RIH with cleaning out BHA joint by joint to 3789m after that drilled out & Cleaned out inside 7" liner to 4141m (Top of LDC) therefor circulated bottoms up then POOH to 3780m and Performed CIT with satisfactory result therefor Resumed POOH from 3780m to surface.

Made up and RIH by 5-7/8" Tri-Cone Bit with 7" and 9-5/8" scraper as Tandem BHA to 4141.5m (LDC depth) after that Circulated bottoms up and Spotted 30bbl CaBr2 brine in 7" liner after that POOH to 1000m then Slipped and Cut drilling line after that POOH to surface.

Made up dry test assembly and RIH to 1650m then Slipped and cut drilling line after that Resumed RIH to 3734m then Set packer and Performed 7"L. Lap dry test (3Hrs open and 6Hrs close position) therefor POOH from 3734 to surface then laid down Dry test tools.

R/U well logging tools and RIH with SBT/VDL/CCL/GR logging tools to 3772m then tried to pass but didn't succeed therefor POOH well logging tools to surface.

RIH well logging tools with 2 joints 4.5" guns as dummy run to 3772m then Tried to pass but didn't therefor POOH to surface.

RIH with 5-7/8" Bit to 4141.5m then circulated bottoms up and worked on mud after that Spotted CaBr2 therefor POOH to surface.

Drilling Fluid Remark: Based on VIRA recommendation the carried KCl Poly mud from 12 1/4" hole section + Well AZN#122 (Rig OEOC 201) and added treated with Starch LV/G, Xanthan Gum to use for started this section.

it was tried to control mud properties by using all available solid control equipment such as shale shakers was applied as per requirement in order to control MW.

The MW increased up to by adding Limestone & Hematite Powder up to 103 PCF at end of this section.

SCE such as Shakers and centrifuges were running to discard LGS while drilling this section.

Treated frequently with essential chemical such as lime as Alkalinity controller to adjust pH, Starch LV for control FL, Soda Ash for control hardness & Xanthan gum as Viscosifier.

Interval Discussion:

Interval IV	3895– 4180 m	8 3/8" Hole Interval	7" Liner Set at 285 meters

Drilling Fluid Type:

FLUID PROPERTIES RECAP					
		Drilling start	Range		Drilling End
MW (min)	pcf	80	80	103.0	103.0
Funnel Viscosity	sec/qt	36	36	45	45
PV	cps	11	11	26	23
YP	lb/100sq.ft	7	7	12	12
API Fluid loss	cc	16	4	18	4
pH		9.7	9.1	9.7	9.4
Solid	%	16	16	27	27
Cl (NaCl)	mg/L	170,000	170,000	175,000	2,400
Total Hardness	mg/L	2,600	2,600	2,800	2,600
Ca Hardness	mg/L	2,400	2,400	2,600	2,400

Figure 10-84: AZNS-207 8-3/8" Drilling Fluid Type Table

Interval Material Consumption Analysis:

Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
Caustic Soda	3	55	165	lbs	0.43	ppb
Citric acid	24	55	1,320	lbs	3.479	ppb
Hematit	15	3,300	49,500	lbs	130.469	ppb
Limestone chips	1	2,200	2,200	lbs	5.799	ppb
KCl	1	2,200	2,200	lbs	5.799	ppb
Limestone	114	2,200	250,800	lbs	661.04	ppb
Green Starch	184	55	10,120	lbs	10.33	ppb
Salt (NACL)	3	55	165	lbs	0.43	ppb
Bicarbonate Sodium	4	55	220	lbs	0.58	ppb
Soda Ash	3	110	330	lbs	0.87	ppb
Xanthan Gum	17	55	935	lbs	2.46	ppb
Lime	58	55	3,190	lbs	8.41	ppb

Note: Used Starch LV/G, Limestone, Xan.Gum and Hematite for treatment of old mud,Received mud and fresh mud.

Initial Volume	2,232.0 bbl
Total Volume Built	379.4 bbl
Volume received	600.0 bbl
Volume Returned	0.0 bbl
Total Volume Consumed	1,280 bbl
Volume Transfer to Next Section	1,931.4 bbl
Meter Drilled	285.0 m

Figure 10-85: AZNS-207 8-3/8" Material Consumption Table

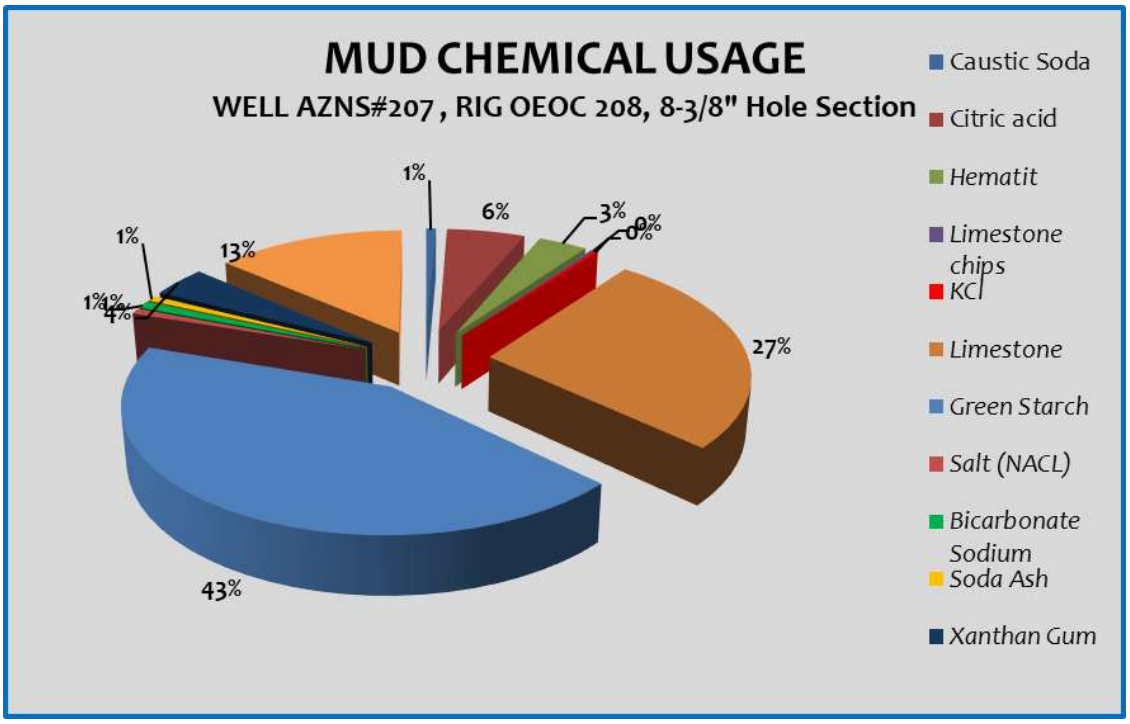


Figure 10-86: AZNS-207 8-3/8" Mud Chemical Usage Graph

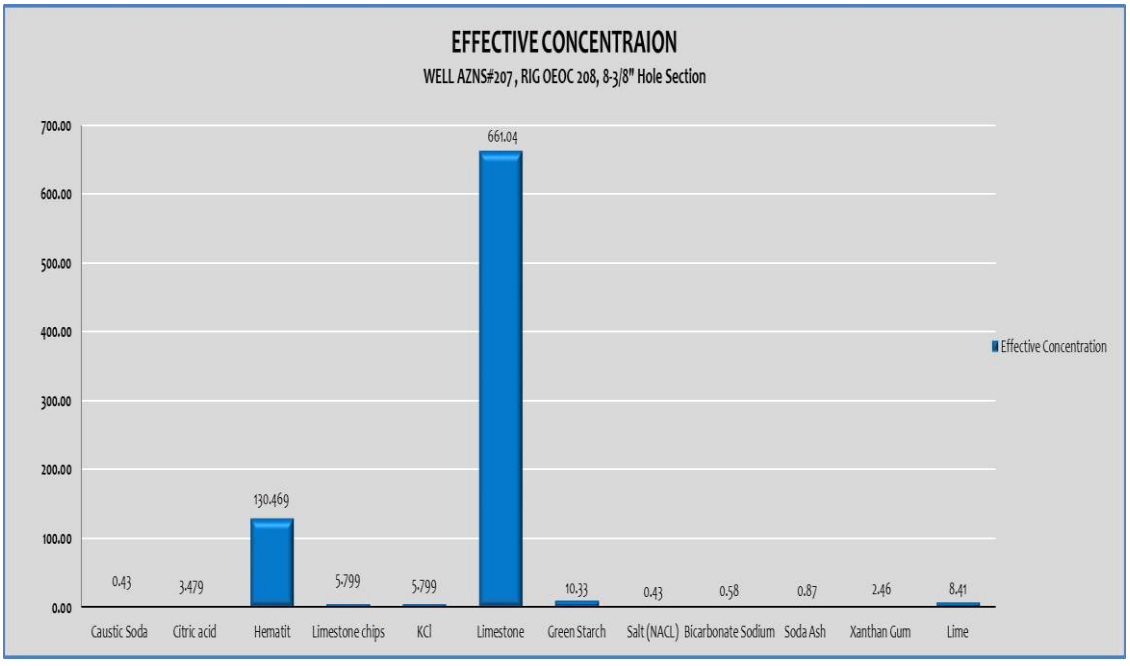


Figure 10-87: AZNS-207 8-3/8" Effective Concentration Chart

Interval Volume Analysis:

RIG: OEOC 208, WELL: AZNS#207 , 8-3/8" Hole Section VOLUME ANALYSIS		
Initial Volume	bbls	2,232.0
Received Volume	bbls	600.0
Volume Return	bbls	0.0
Volume Built	bbls	379.4
Surface Losses/Dumped	bbls	1,100.0
Formation Losses	bbls	180.0
Total Losses	bbls	1,280.0
Volume Transfer Out	bbls	1,931

Figure 10-88: AZNS-207 8-3/8" Volume Analysis Table

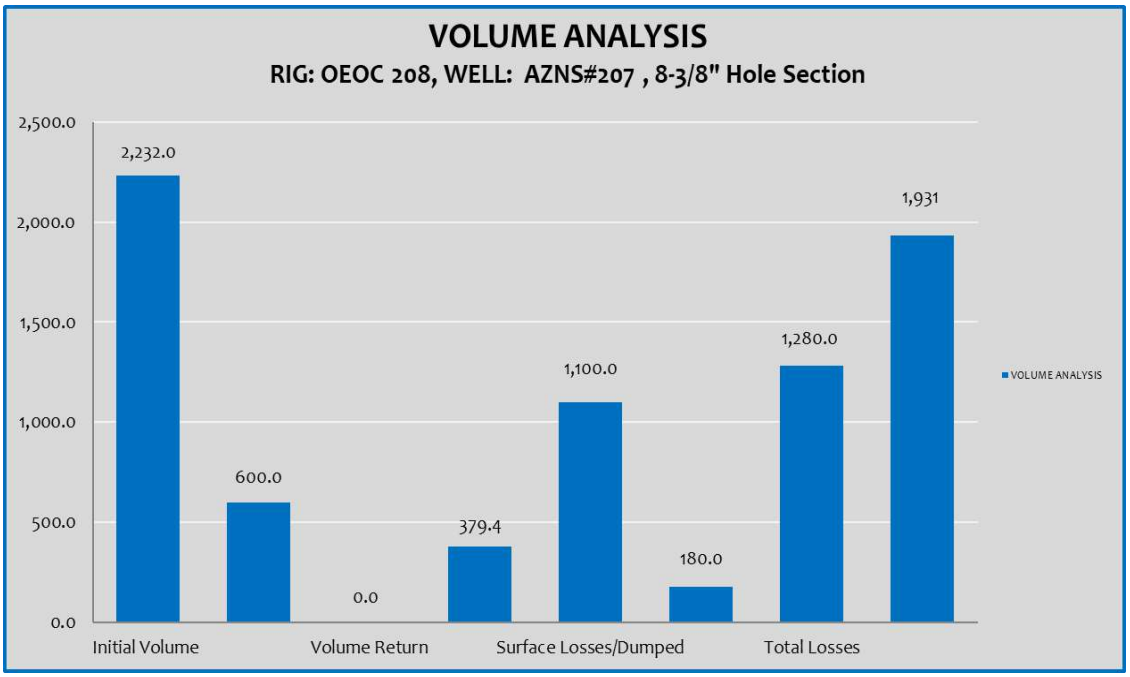


Figure 10-89: AZNS-207 8-3/8" Volume Analysis Chart

Interval Daily Volume Break Down:

Date/DMR.N		Volume of Built	Surface Losses	Formation Losses
12-Feb-25	121	0.0	0	0
13-Feb-25	122	40.7	10	0
14-Feb-25	123	146.9	515	0
15-Feb-25	124	32.1	18	24
16-Feb-25	125	17.2	60	36
17-Feb-25	126	14.2	36	36
18-Feb-25	127	0.4	27	24
19-Feb-25	128	0.1	0	12
20-Feb-25	129	105.9	0	12
21-Feb-25	130	0.9	205	12
22-Feb-25	131	0.0	0	12
23-Feb-25	132	0.0	6	12
24-Feb-25	133	1.5	28	0
25-Feb-25	134	0.0	34	0
26-Feb-25	135	0.3	30	0
27-Feb-25	136	0.1	15	0
28-Feb-25	137	0.0	42	0
1-Mar-25	138	0.0	0	0
2-Mar-25	139	0.0	25	0
3-Mar-25	140	0.0	20	0
4-Mar-25	141	19.1	17	0
5-Mar-25	142	0.0	12	0
6-Mar-25	143	0.0	0	0
7-Mar-25	144	0.0	0	0
8-Mar-25	145	0.0	0	0
Total (bbl)		Volume of Built	Surface Losses	Formation Losses
		379	1,100	180

Figure 10-90: AZNS-207 8-3/8" Daily Volume Break Down Table

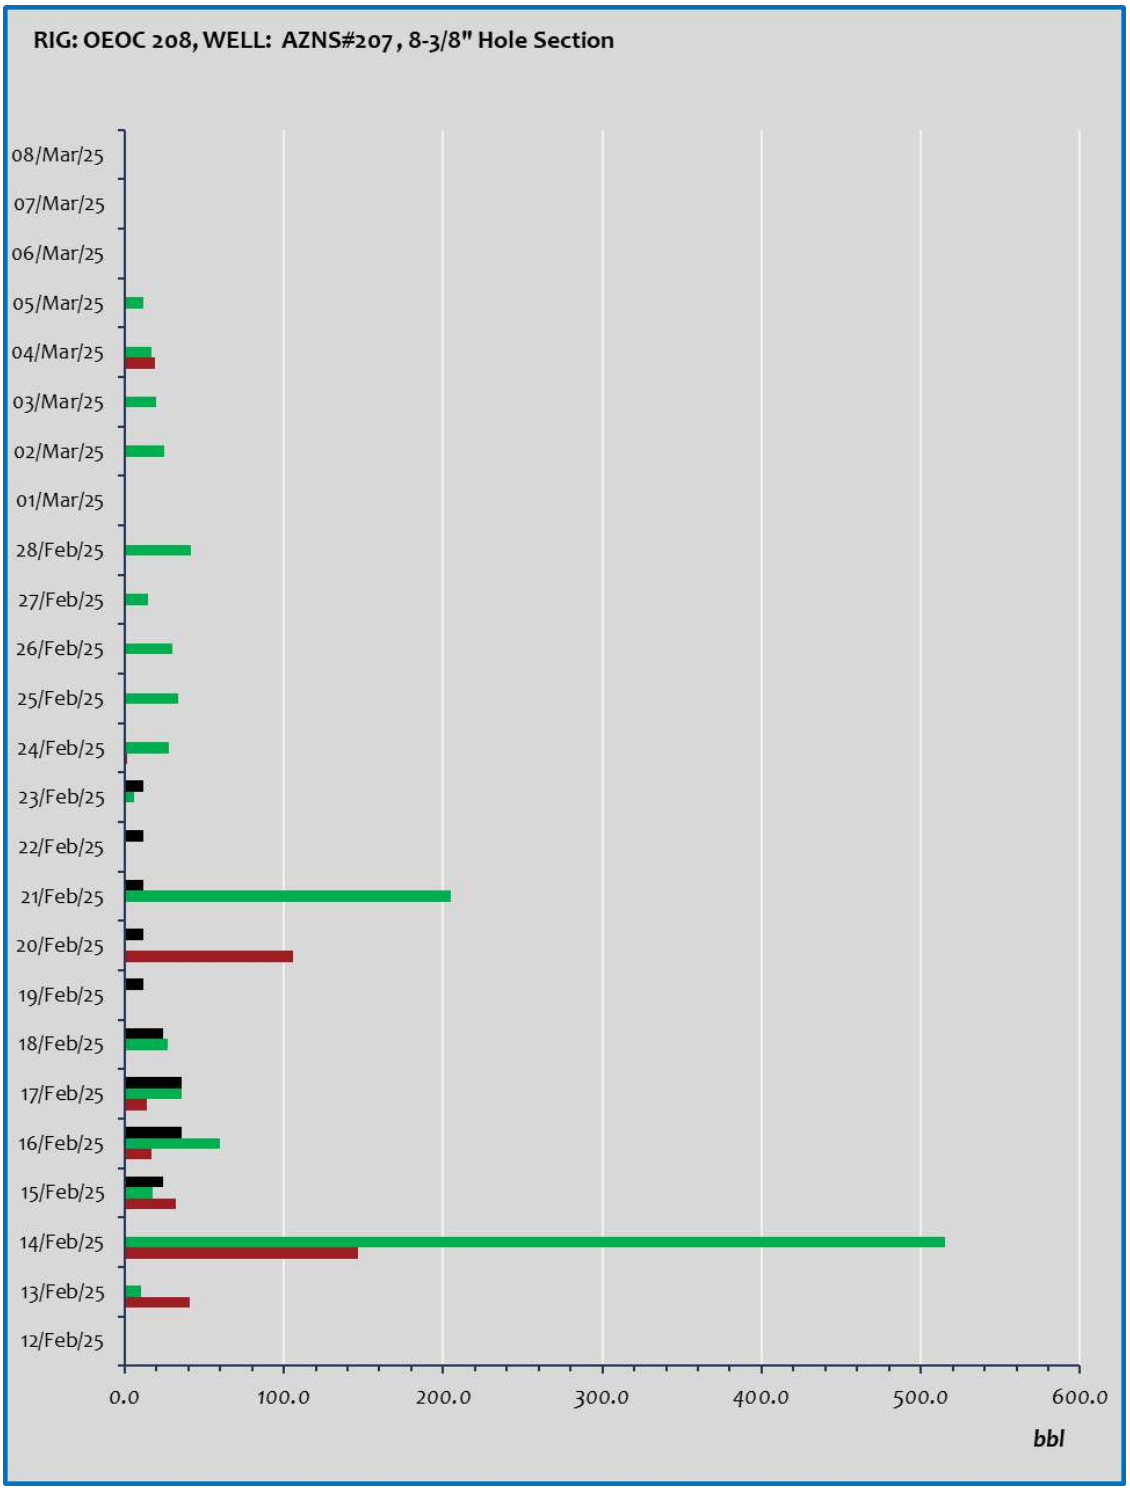


Figure 10-91: AZNS-207 8-3/8" Daily Volume Break Down Chart

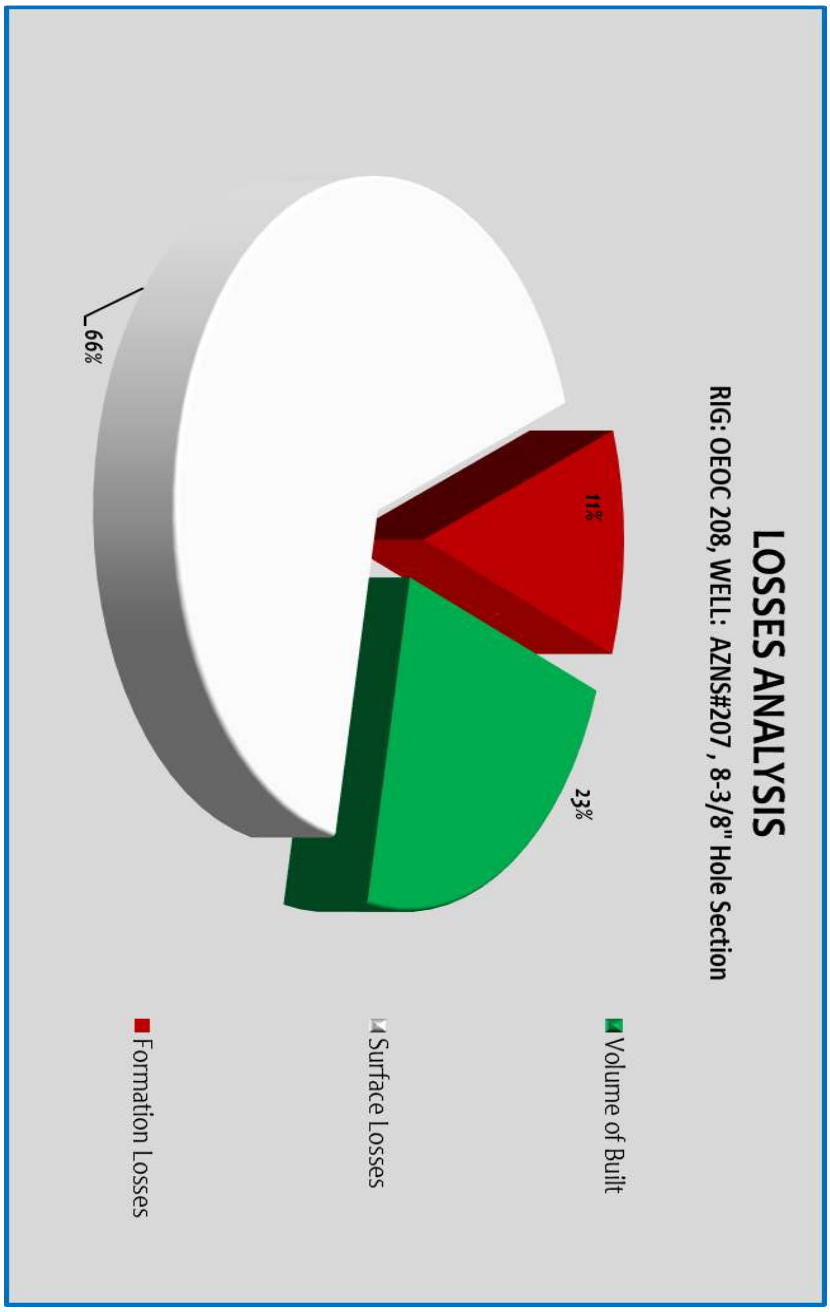


Figure 10-92: AZNS-207 8-3/8" Daily Volume Break Down Graph

Interval Loss Distribution:

Date/DMR.N		Volume of Built	Dump/Contamination	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
12-Feb-25	121	0.0	0	0	0	0	0	0	0	0	0
13-Feb-25	122	40.7	0	10	0	0	0	0	0	0	0
14-Feb-25	123	146.9	420	0	0	0	0	0	45	0	50
15-Feb-25	124	32.1	0	18	0	0	0	0	0	24	0
16-Feb-25	125	17.2	0	60	0	0	0	0	0	36	0
17-Feb-25	126	14.2	0	36	0	0	0	0	0	36	0
18-Feb-25	127	0.4	0	12	0	0	0	0	0	24	15
19-Feb-25	128	0.1	0	0	0	0	0	0	0	12	0
20-Feb-25	129	105.9	0	0	0	0	0	0	0	12	0
21-Feb-25	130	0.9	165	0	0	0	0	0	25	12	15
22-Feb-25	131	0.0	0	0	0	0	0	0	0	12	0
23-Feb-25	132	0.0	0	0	0	0	6	0	0	12	0
24-Feb-25	133	1.5	0	10	0	0	0	0	18	0	0
25-Feb-25	134	0.0	0	0	0	0	18	0	16	0	0
26-Feb-25	135	0.3	0	6	0	0	24	0	0	0	0
27-Feb-25	136	0.1	0	5	0	0	10	0	0	0	0
28-Feb-25	137	0	0	0	0	0	12	0	20	0	10
1-Mar-25	138	0	0	0	0	0	0	0	0	0	0
2-Mar-25	139	0	0	0	0	0	0	0	15	0	10
3-Mar-25	140	0	0	0	0	0	8	0	12	0	0
4-Mar-25	141	19.1	0	5	0	0	0	0	0	0	12
5-Mar-25	142	0.0	0	0	0	0	12	0	0	0	0
6-Mar-25	143	0.0	0	0	0	0	0	0	0	0	0
7-Mar-25	144	0.0	0	0	0	0	0	0	0	0	0
8-Mar-25	145	0.0	0	0	0	0	0	0	0	0	0
Total (bbl)		Volume of Built	Dump/Contaminate	Shakers	Evaporation	Centrifuge	Trip	Mud cleaner	Pit Cleaning	Formation	Other
		379.4	585	162	0	0	90	0	151	180	112.0

Figure 10-93: AZNS-207 8-3/8" Loss Distribution Table

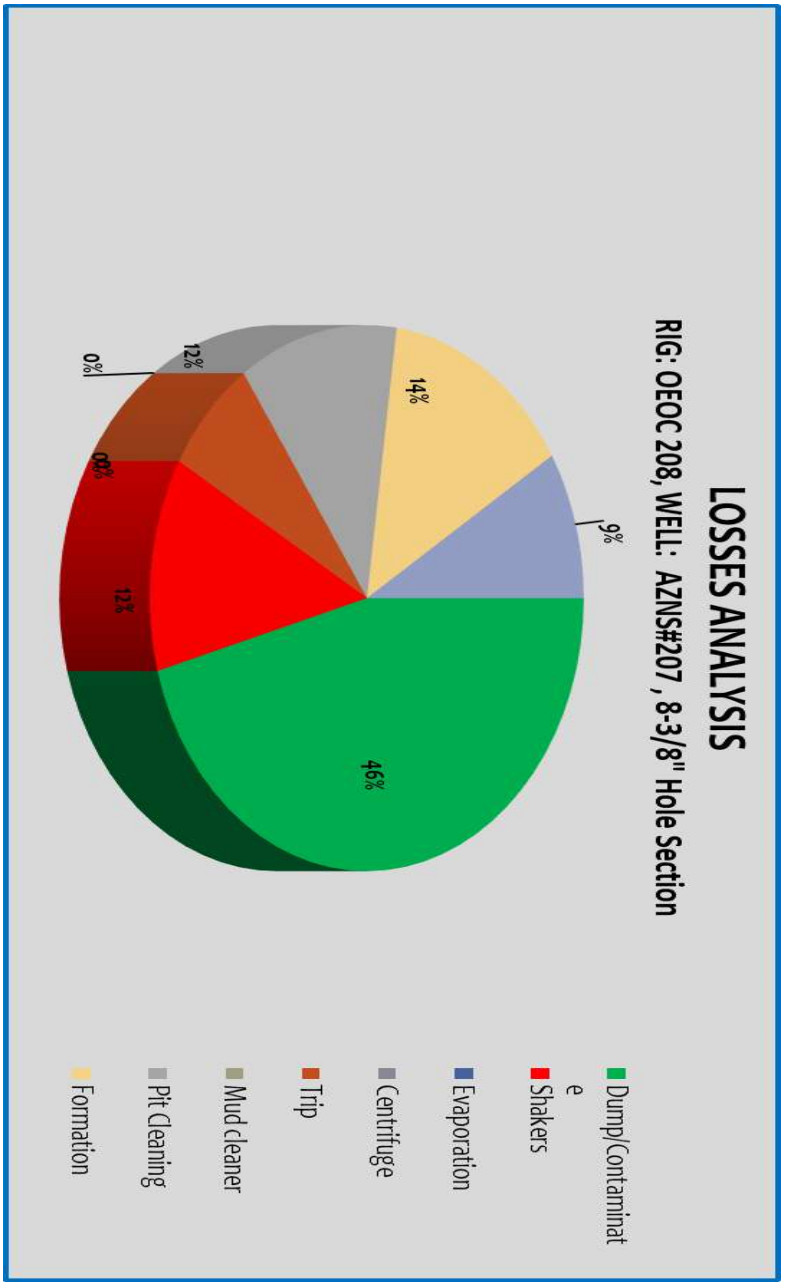


Figure 10-94: AZNS-207 8-3/8" Loss Distribution Graph

Interval Fluid Properties Recap:

Date	DEPTH	Density	VIS	PV	YP	Water Loss	pH	Solid %	Chloride	KCL (%Wt)	Calcium	Total Hardness	Mud Type
12-Feb-25	3895	80	43	14	11	3.2	9.4		175000	3	1760	1920	SALT/POL MUD
13-Feb-25	3910	80	36	11	7	16	9.7	16	170000	1	2400	2600	SALT/POL MUD
14-Feb-25	3928	100	55	26	12	18	9.1	24	175000	1	2400	2600	SALT/POL MUD
15-Feb-25	3964	102.5	43	18	10	16	9.4	25	175000	0.5	2600	2800	SALT/POL MUD
16-Feb-25	4076	103	44	23	12	4	9.3	25	175000	0.5	2400	2600	SALT/POL MUD
17-Feb-25	4180	103	45	23	12	4	9.4	27	175000	0.5	2400	2600	SALT/POL MUD
18-Feb-25	4180	103	48	24	13	4	9.4	27	175000	0.5	2400	2600	SALT/POL MUD
19-Feb-25	4180	103	50	24	14	4	9.4	27	175000	0.5	2400	2600	SALT/POL MUD
20-Feb-25	4180	103	50	24	14	4	9.4	27	175000	0.5	2400	2600	SALT/POL MUD
21-Feb-25	4180	103	49	23	13	4	9.2	27	175000	0.5	2400	2600	SALT/POL MUD
22-Feb-25	4180	103	49	23	13	4	9.2	27	175000	0.5	2400	2600	SALT/POL MUD
23-Feb-25	4180	103	47	19	12	4	9.2	27	175000	0.5	2400	2600	SALT/POL MUD
24-Feb-25	4180	103	43	18	8	10	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
25-Feb-25	4180	103	43	18	8	10	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
26-Feb-25	4180	103	47	19	10	10	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
27-Feb-25	4180	103	47	19	10	11	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
28-Feb-25	4180	103	47	19	10	11	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
1-Mar-25	4180	103	47	19	10	11	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
2-Mar-25	4180	103	47	19	10	11	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
3-Mar-25	4180	103	48	19	11	11	9.6	27	175000	0.5	2440	2720	SALT/POL MUD
4-Mar-25	4180	103	50	20	12	12	9.4	27	170000	0.5	2440	2720	SALT/POL MUD
5-Mar-25	4180	103	49	19	12	10	9.4	27	170000	0.5	2400	2720	SALT/POL MUD

Drilling Start

Drilling End

Figure 10-95: AZNS-207 8-3/8" Fluid Properties Recap Table

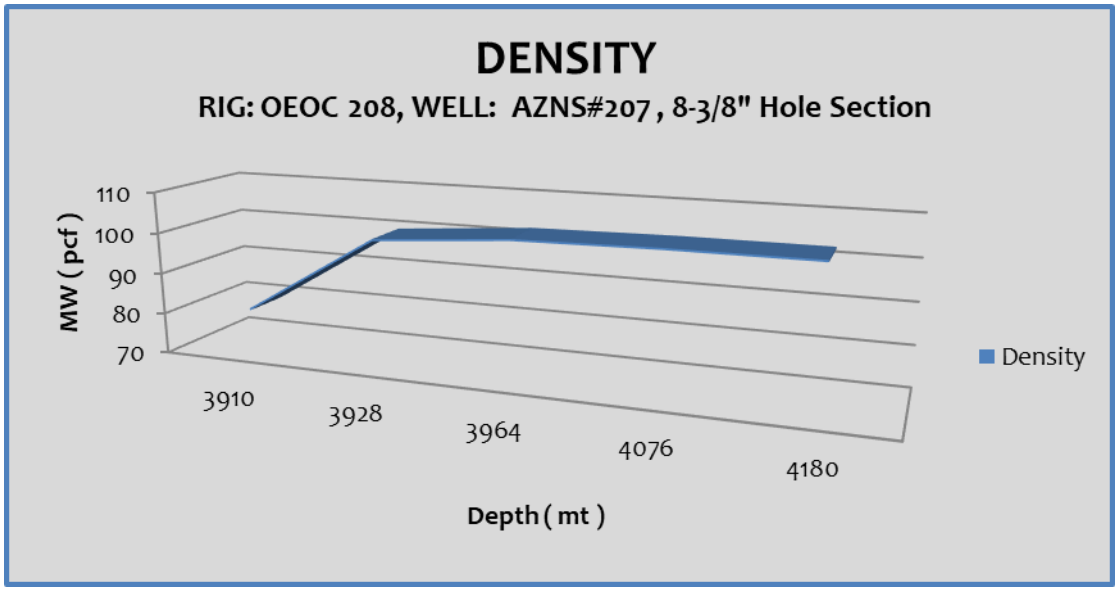


Figure 10-96: AZNS-207 8-3/8" Density Chart

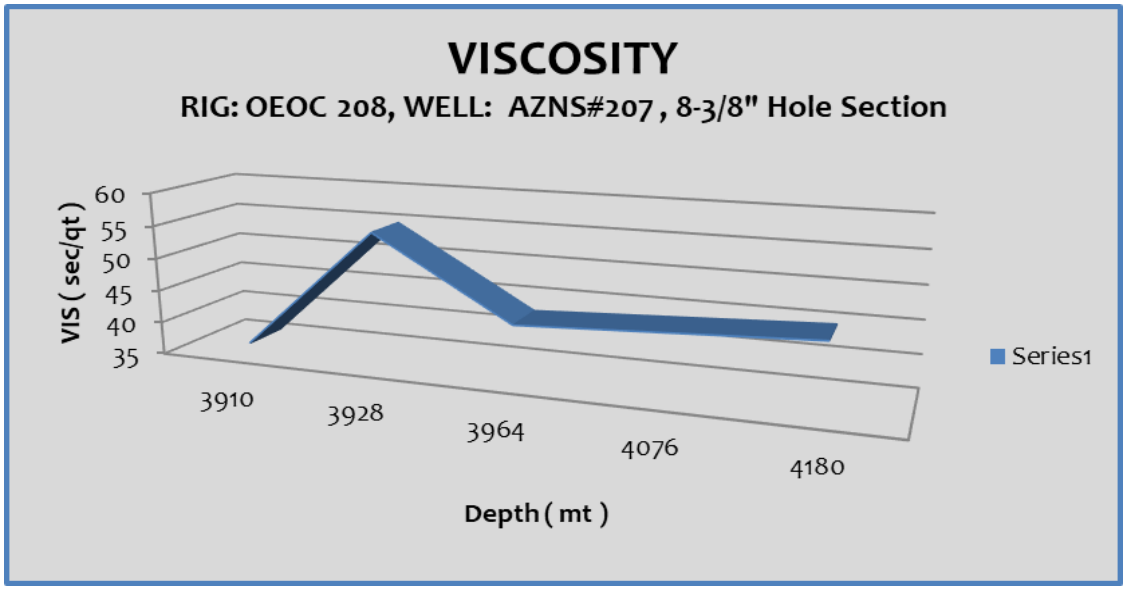


Figure 10-97: AZNS-207 8-3/8" Viscosity Chart

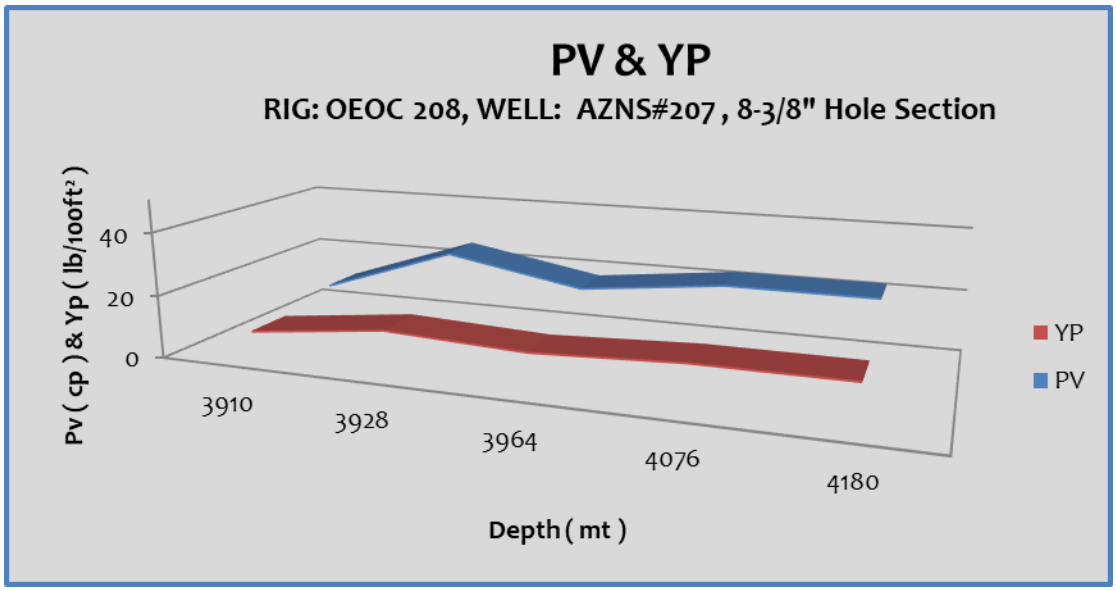


Figure 10-98: AZNS-207 8-3/8" PV & YP Chart

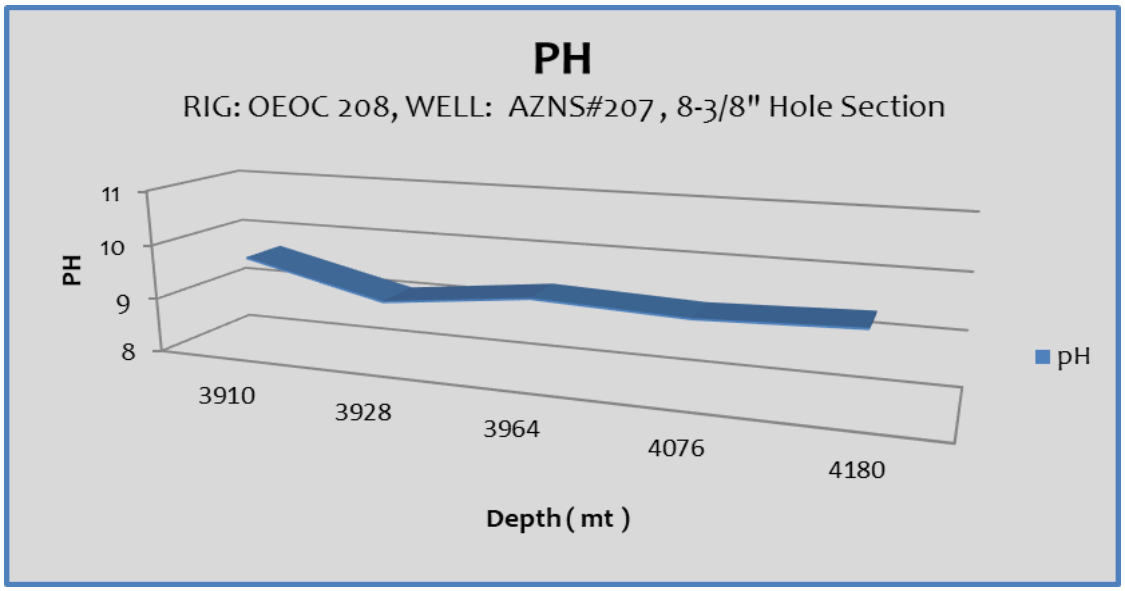


Figure 10-99: AZNS-207 8-3/8" pH Chart

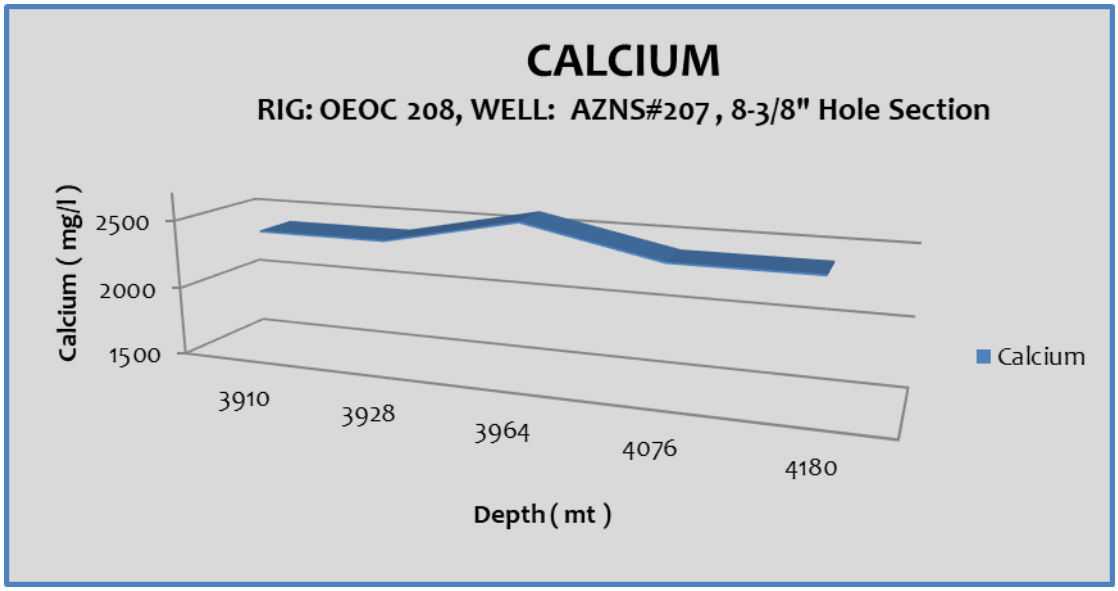


Figure 10-100: AZNS-207 8-3/8" Calcium Chart

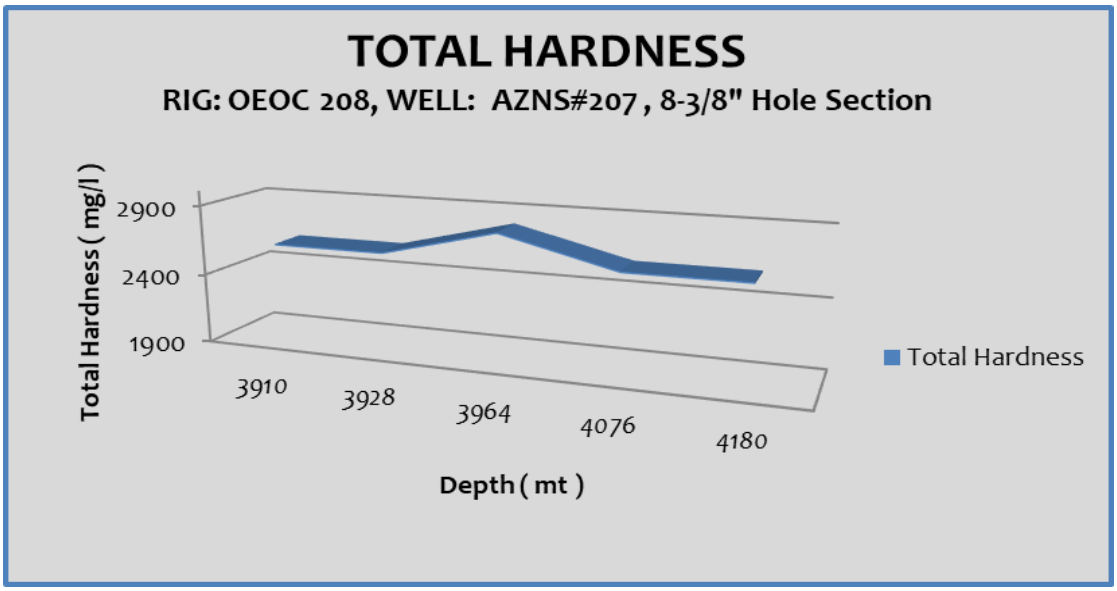


Figure 10-101: AZNS-207 8-3/8" Total Hardness Chart

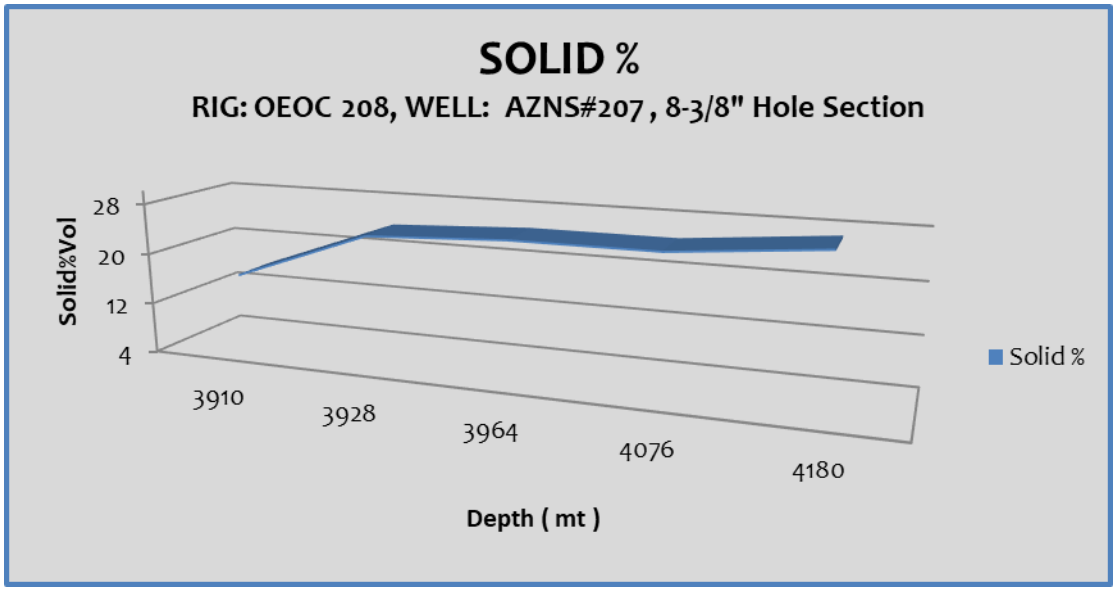


Figure 10-102: AZNS-207 8-3/8" Solid % Chart

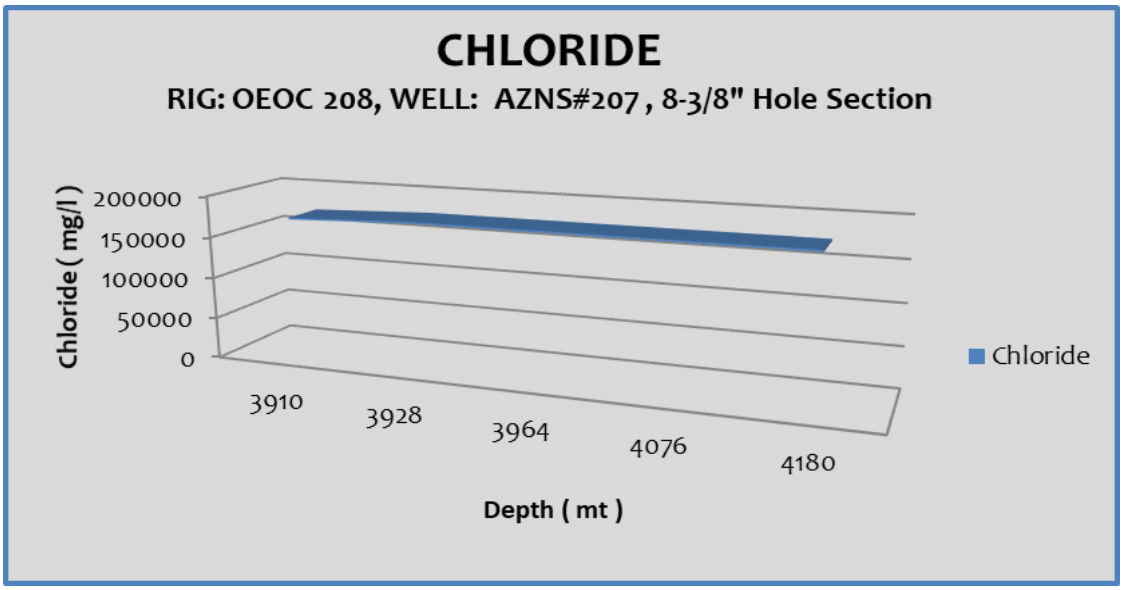


Figure 10-103: AZNS-207 8-3/8" Chloride Chart

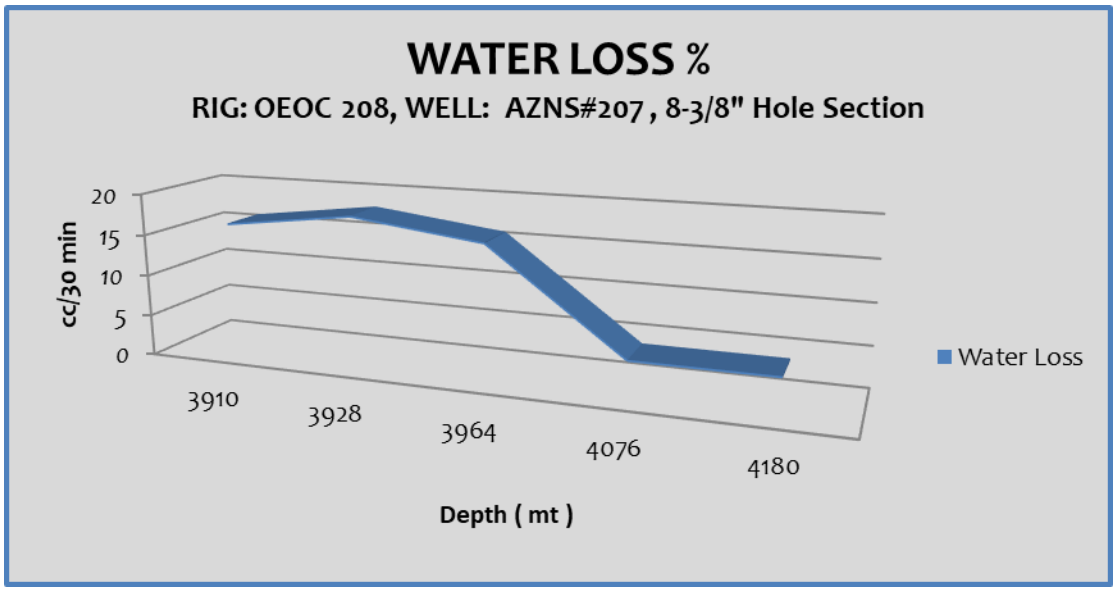


Figure 10-104: AZNS-207 8-3/8" Water Loss % Chart

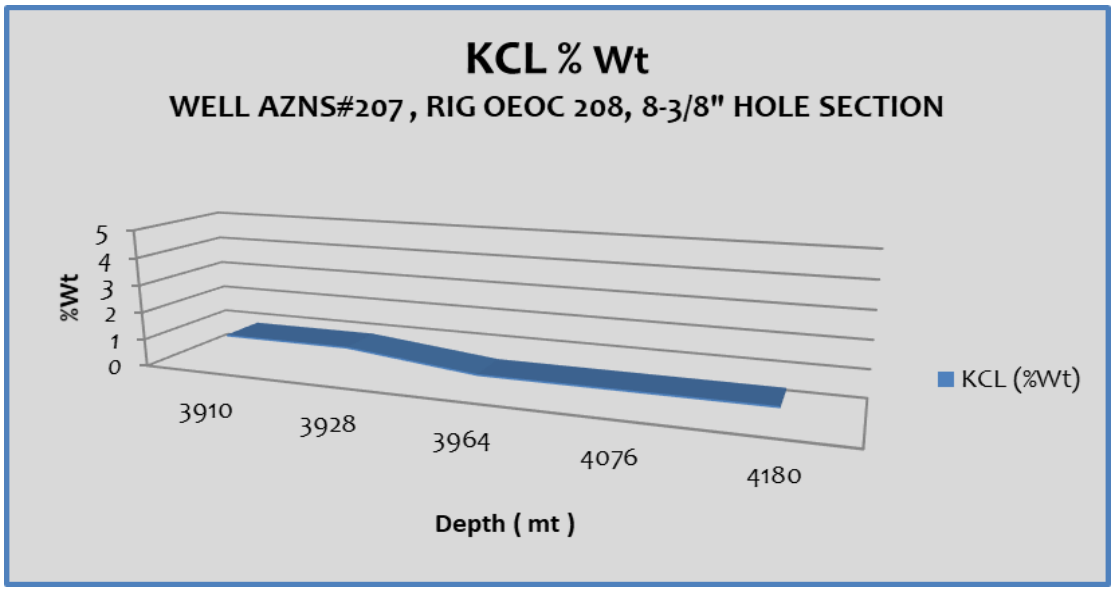


Figure 10-105: AZNS-207 8-3/8" KCl % Wt Chart

Interval Solid Control Discussion:

- **Shale Shakers:**

Rig OEOC 208 has 3 shale shakers were dressed with:

- **Shaker#1**: 200 Mesh Screen
- **Shaker#2**: 200 Mesh Screen
- **Shaker#3**: 200 Mesh Screen

Centrifuges;

Derrick variable RPM

RIG: OEOC 208, WELL: AZNS#207 , 8-3/8" Hole Section Solid Control Equipment Working Hr.s	
Swaco Shaker #1	118
Swaco Shaker #2	367
Swaco Shaker #3	185
Swaco Mud cleaner	0
Swaco Centrifuge#1	0
Chinese Centrifuge#2	0

Figure 10-106: AZNS-207 8-3/8" Solid Control Equipment

10.5 Completion Section

INHIBITED $CaBr_2$ BRINE

The completion fluid for this section will be $CaBr_2$ brine treated with a scavenger, inhibitor.

VOLUME AND MATERIAL CONSUMPTION

Completion						
Products	Units Used	Unit wt lbs	Total wt		Effective Concentration	
925 bbls CaBr2 Completion fluid has been made						
CaBr2	925	BBL	38202.5	gals	41.30	gpb
CaCl2	7	1 MT	1540	lbs	179.67	ppb
Corrision Inhibitor	4	55 Gal	220	gals	0.24	gpb
O2 Scavenger	2	55 Gal	110	gals	0.12	gpb
H2S Scavenger	2	55 Gal	110	gals	0.12	gpb
Cacl2 Brine			60.0			
MW :			104.0			*pcf*
Initial Volume :			0.0			*bbl*
Total Volume Built (Completion Fluid) :			925.0			*bbl*

Figure 10-107: AZNS-207 Completion Section Volume & Material Consupmtion

11. Waste Management Report

11.1 Waste Management Package

The required equipment's had been located on operational area, according to the employer recall, which is tabled below.

1	Dewatering unit		One	Complete with related accessories
2	Solid separation unit	Automatic filtration unit	One	Capable to filter completion fluid
3	Buffer tanks and accessories	Buffer tanks and agitators	Two	Optional/ 25 HP
4	Pumps	Centrifugal pump	One	3"x4" ,3"x6" with related accessories
5		Submersible pump	Two	4", 40-50 m^3/hr., With related accessories
6		Air diaphragm pump	Two	3", with related accessories
7		Wash down Gun	One	200 Br, with related accessories
8	Laboratory unit and waste water analysis equipment	Photo meter / ion detector	One	Complete with related accessories
9		Jar test / Centrifuge test kit	One	
10		TDS/ pH /EC /Retort kit	One	
11		Caravan including office and lab.	One	

Table 11-1: AZNS-207 Well Waste Management Information

It also, worth to be mentioned that the service personnel had been working through the pre-spud process.

11.2 Waste Management End of Well Report

26" Hole Section Information

Rig Name	208 OEOC
Start Date	Oct. 15th 2024
End Date	Oct. 20th 2024
Start Depth (m)	0
End Depth (m)	155
Duration (days)	6

Table 11-2: AZNS-207 26”" Hole Section Waste Management Information

26” Hole Section Operation’s Recap:

Solid Handling System									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Waste		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
1	15-Oct-24	0	0	0	0	0	0	0	0
2	16-Oct-24	0	0	0	0	0	0	0	0
3	17-Oct-24	31	31	137	137	0	0	0	0
4	18-Oct-24	151	120	545	681	0	0	0	0
5	19-Oct-24	151	0	36	717	0	0	0	0
6	20-Oct-24	151	0	0	717	0	0	0	0

Figure 11-1: 26" Hole Section Solid Handling System Table

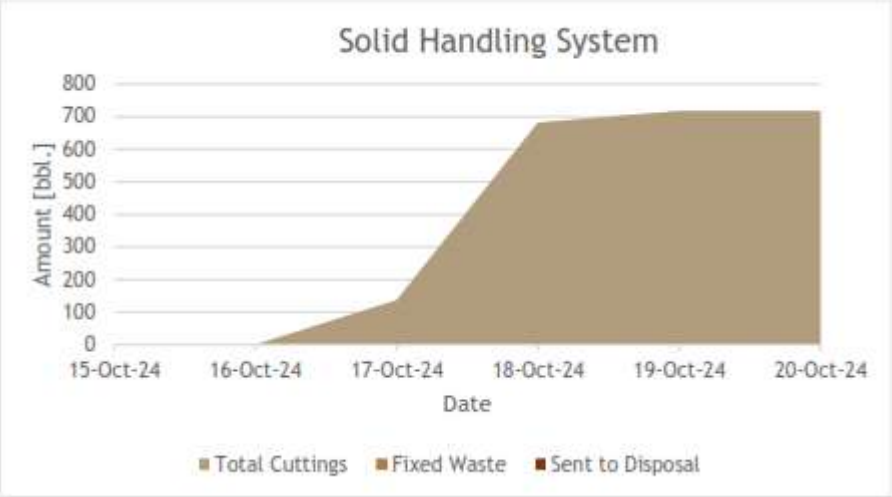


Figure 11-2: 26" Hole Section Solid Handling System Graph

Solid Handling System analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		SodSil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/M3	kg/M3	kg/M3	kg/M3
1	15-Oct-24	0	0	NA	0.000	0.000	0.000	0.000
2	16-Oct-24	0	0	NA	0.000	0.000	0.000	0.000
3	17-Oct-24	31	31	Pass	0.000	0.000	0.000	0.000
4	18-Oct-24	151	120	Pass	0.000	0.000	0.000	0.000
5	19-Oct-24	151	0	Pass	0.000	0.000	0.000	0.000
6	20-Oct-24	151	0	NA	0.000	0.000	0.000	0.000

Figure 11-3: 26" Hole Section Solid Handling System Analysis Table

Dewatering											
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
1	15-Oct-24	0	0	0	0	0	0	0	0	0	0
2	16-Oct-24	0	0	0	0	0	0	0	0	0	0
3	17-Oct-24	31	31	0	0	0	0	0	0	0	0
4	18-Oct-24	151	120	0	0	0	0	0	0	0	0
5	19-Oct-24	151	0	500	500	0	0	0	0	0	0
6	20-Oct-24	151	0	0	500	0	0	0	0	0	0

Figure 11-4: 26" Hole Section Dewatering Table

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	Al	Sulfate	Ca
				7-9	<800	<50	< 80	< 50	< 3	< 50	< 600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
1	15-Oct-24	0	0	0	0	0	0	0	0	0	0
2	16-Oct-24	0	0	0	0	0	0	0	0	0	0
3	17-Oct-24	31	31	0	0	0	0	0	0	0	0
4	18-Oct-24	151	120	0	0	0	0	0	0	0	0
5	19-Oct-24	151	0	0	0	0	0	0	0	0	0
6	20-Oct-24	151	0	0	0	0	0	0	0	0	0

Figure 11-5: 26" Hole Section Dewatering Analysis Table



Figure 11-6: 26" Hole Section Dewatering Graph

Chemical																	
No.	Date	Cement		Na_2SiO_3		Coagulant		Polymer		Lime		Soda ash		Citric acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
1	15-Oct-24	0	0	0	0	75	0	125	0	0	0	1,650	0	0	0	0	0
2	16-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
3	17-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
4	18-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
5	19-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
6	20-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Figure 11-7: 26" Hole Section Chemical Table

17 – 1/2" Hole Section Information

Rig Name	208 OEOC
Start Date	Oct. 21st 2024
End Date	Oct. 27th 2024
Start Depth (m)	155
End Depth (m)	2509
Duration (days)	68

17 – 1/2" Hole Section Operation's Recap:

Solid Handling System									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Waste		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
7	21-Oct-24	155	4	34	34	0	0	0	0
8	22-Oct-24	225	70	222	222	550	550	0	0
9	23-Oct-24	495	270	1,052	1,052	0	550	300	300
10	24-Oct-24	730	235	2,135	2,135	0	550	250	550
11	25-Oct-24	800	70	532	532	3,000	3,550	10	560
12	26-Oct-24	1,073	273	716	1,248	2,500	6,050	10	570
13	27-Oct-24	1,227	154	684	1,932	0	6,050	700	1,270
14	28-Oct-24	1,356	129	541	2,473	0	6,050	700	1,970
15	29-Oct-24	1,373	17	602	3,075	0	6,050	700	2,670

16	30-Oct-24	1,450	77	634	3,709	0	6,050	350	3,020
17	31-Oct-24	1,450	0	166	3,875	0	6,050	750	3,770
18	1-Nov-24	1,480	30	99	3,974	0	6,050	300	4,070
19	2-Nov-24	1,480	0	134	4,108	2,000	8,050	350	4,420
20	3-Nov-24	1,548	68	238	4,347	0	8,050	0	4,420
21	4-Nov-24	1,562	14	154	4,501	0	8,050	0	4,420
22	5-Nov-24	1,562	0	40	4,541	0	8,050	200	4,620
23	6-Nov-24	1,562	0	350	4,891	0	8,050	200	4,820
24	7-Nov-24	1,562	0	79	4,970	0	8,050	300	5,120
25	8-Nov-24	1,562	0	218	5,188	0	8,050	0	5,120
26	9-Nov-24	1,562	0	310	5,498	2,300	10,350	0	5,120
27	10-Nov-24	1,562	0	35	5,533	0	10,350	200	5,320
28	11-Nov-24	1,564	2	44	5,577	0	10,350	402	5,722
29	12-Nov-24	1,564	0	89	5,666	0	10,350	0	5,722
30	13-Nov-24	1,564	0	89	5,755	0	10,350	0	5,722
31	14-Nov-24	1,564	0	137	5,892	0	10,350	300	6,022
32	15-Nov-24	1,564	0	137	6,091	300	10,650	200	6,222
33	16-Nov-24	1,564	0	110	6,201	200	10,850	300	6,522
34	17-Nov-24	1,564	0	110	6,270	200	11,050	300	6,822
35	18-Nov-24	1,564	0	110	6,532	0	11,050	300	7,122
36	19-Nov-24	1,564	0	110	6,579	400	11,450	100	7,222
37	20-Nov-24	1,564	0	110	6,615	0	11,450	0	7,222
38	21-Nov-24	1,429	0	500	6,607	100	11,550	300	7,522
39	22-Nov-24	1,429	0	1,000	6,641	0	11,550	0	7,522
40	23-Nov-24	1,429	0	1,000	6,675	0	11,550	0	7,522
41	24-Nov-24	1,429	0	1,000	6,708	0	11,550	0	7,522
42	25-Nov-24	1,440	11	1,000	6,855	0	11,550	300	7,822
43	26-Nov-24	1,447	7	1,000	7,085	0	11,550	100	7,922
44	27-Nov-24	1,472	25	1,000	7,146	0	11,550	250	8,172
45	28-Nov-24	1,507	35	1,000	7,233	900	12,450	250	8,422
46	29-Nov-24	1,552	45	1,000	7,313	0	12,450	400	8,822
47	30-Nov-24	1,552	0	1,000	7,405	1,800	14,250	500	9,322
48	1-Dec-24	1,571	19	1,000	7,454	0	14,250	200	9,522
49	2-Dec-24	1,592	21	1,000	7,591	0	14,250	400	9,922
50	3-Dec-24	1,593	1	1,000	7,667	0	14,250	100	10,022
51	4-Dec-24	1,616	23	1,000	7,714	0	14,250	0	10,022
52	5-Dec-24	1,618	2	1,000	7,755	0	14,250	0	10,022
53	6-Dec-24	1,636	19	1,000	7,829	0	14,250	0	10,022
54	7-Dec-24	1,649	13	1,000	7,906	0	14,250	0	10,022
55	8-Dec-24	1,649	0	1,000	8,170	0	14,250	150	10,172
56	9-Dec-24	1,649	0	1,000	8,280	0	14,250	150	10,322
57	10-Dec-24	1,649	0	1,000	8,390	0	14,250	0	10,322
58	11-Dec-24	1,649	0	0	8,500	300	14,550	0	10,322
59	12-Dec-24	1,649	0	0	8,500	300	14,850	100	10,422
60	13-Dec-24	1,649	0	0	8,500	0	14,850	100	10,522

61	14-Dec-24	1,654	5	0	9,085	0	14,850	700	11,2
62	15-Dec-24	1,713	59	110	9,194	0	14,850	700	11,9
63	16-Dec-24	11,828	10,115	9,910	19,105	0	14,850	300	12,2
64	17-Dec-24	1,861	9,967	9,748	28,852	0	14,850	300	12,5
65	18-Dec-24	1,994	133	166	29,018	0	14,850	0	12,5
66	19-Dec-24	2,000	6	60	29,078	0	14,850	0	12,5
67	20-Dec-24	2,000	0	107	29,185	0	14,850	0	12,5
68	21-Dec-24	2,000	0	618	29,803	0	14,850	0	12,5
69	22-Dec-24	2,114	114	797	30,600	0	14,850	150	12,6
70	23-Dec-24	2,150	36	487	31,088	0	14,850	150	12,8
71	24-Dec-24	2,150	0	0	31,088	1,500	16,350	250	13,0
72	25-Dec-24	2,189	39	87	31,175	0	16,350	1,000	14,0
73	26-Dec-24	2,339	150	195	31,369	0	16,350	1,000	15,0
74	27-Dec-24	2,509	170	239	31,608	0	16,350	300	15,3

Figure 11-8: 17 – 1/2" Hole Section Solid Handling System Table

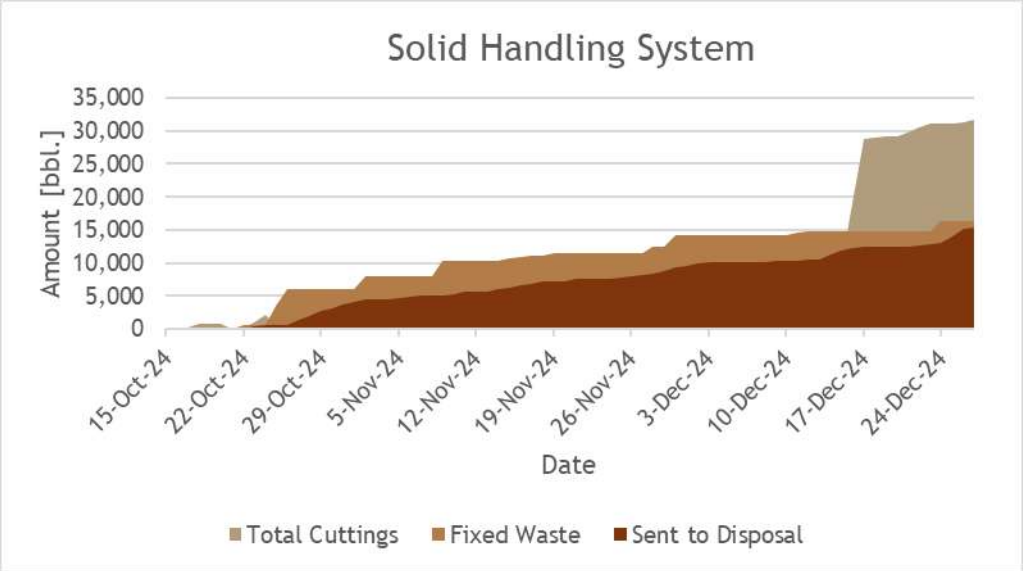


Figure 11-9: 17 – 1/2" Hole Section Solid Handling System Graph

Solid Handling System analysis

Report No.	Date	Depth	Drilled	Can test	Cement/Waste		SodSil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/M3	kg/M3	kg/M3	kg/M3
7	21-Oct-24	155	4	Pass	0.000	0.000	0.000	0.000
8	22-Oct-24	225	70	Pass	0.000	0.000	0.000	0.000
9	23-Oct-24	495	270	Pass	0.000	0.000	0.000	0.000
10	24-Oct-24	730	235	Pass	0.000	0.000	0.000	0.000
11	25-Oct-24	800	70	Pass	0.667	0.667	0.000	0.000
12	26-Oct-24	1,073	273	Pass	0.000	0.667	0.000	0.000
13	27-Oct-24	1,227	154	Pass	0.000	0.667	0.000	0.000
14	28-Oct-24	1,356	129	Pass	0.000	0.667	0.000	0.000
15	29-Oct-24	1,373	17	Pass	0.000	0.667	0.000	0.000
16	30-Oct-24	1,450	77	Pass	0.000	0.667	0.000	0.000
17	31-Oct-24	1,450	0	Pass	0.000	0.667	0.000	0.000
18	1-Nov-24	1,480	30	Pass	0.000	0.667	0.000	0.000
19	2-Nov-24	1,480	0	Pass	0.000	0.667	0.000	0.000
20	3-Nov-24	1,548	68	Pass	0.000	0.667	0.000	0.000
21	4-Nov-24	1,562	14	Pass	0.000	0.667	0.000	0.000
22	5-Nov-24	1,562	0	Pass	0.000	0.667	0.000	0.000
23	6-Nov-24	1,562	0	Pass	0.000	0.667	0.000	0.000
24	7-Nov-24	1,562	0	Pass	0.000	0.667	0.000	0.000
25	8-Nov-24	1,562	0	Pass	0.000	0.667	0.000	0.000
26	9-Nov-24	1,562	0	Pass	1.739	1.203	0.000	0.000
27	10-Nov-24	1,562	0	Pass	0.000	1.203	0.000	0.000
28	11-Nov-24	1,564	2	Pass	0.000	1.203	0.000	0.000
29	12-Nov-24	1,564	0	Pass	0.000	1.203	0.000	0.000
30	13-Nov-24	1,564	0	Pass	0.000	1.203	0.000	0.000
31	14-Nov-24	1,564	0	Pass	0.000	1.203	0.000	0.000
32	15-Nov-24	1,564	0	Pass	0.000	1.203	0.000	0.000
33	16-Nov-24	1,564	0	Pass	25.000	9.135	4.000	4.000
34	17-Nov-24	1,564	0	Pass	0.000	9.135	0.000	4.000
35	18-Nov-24	1,564	0	Pass	0.000	9.135	0.000	4.000
36	19-Nov-24	1,564	0	Pass	0.000	9.135	0.000	4.000
37	20-Nov-24	1,564	0	Pass	0.000	9.135	0.000	4.000
38	21-Nov-24	1,429	0	Pass	0.000	9.135	0.000	4.000
39	22-Nov-24	1,429	0	Pass	0.000	9.135	0.000	4.000
40	23-Nov-24	1,429	0	Pass	0.000	9.135	0.000	4.000

41	24-Nov-24	1,429	0	Pass	0.000	9.135	0.000	4.000
42	25-Nov-24	1,440	11	Pass	0.000	9.135	0.000	4.000
43	26-Nov-24	1,447	7	Pass	0.000	9.135	0.000	4.000
44	27-Nov-24	1,472	25	Pass	0.000	9.135	0.000	4.000
45	28-Nov-24	1,507	35	Pass	4.444	7.963	0.000	4.000
46	29-Nov-24	1,552	45	Pass	0.000	7.963	0.000	4.000
47	30-Nov-24	1,552	0	Pass	0.000	7.963	0.000	4.000
48	1-Dec-24	1,571	19	Pass	0.000	7.963	0.000	4.000
49	2-Dec-24	1,592	21	Pass	0.000	7.963	0.000	4.000
50	3-Dec-24	1,593	1	Pass	0.000	7.963	0.000	4.000
51	4-Dec-24	1,616	23	Pass	0.000	7.963	0.000	4.000
52	5-Dec-24	1,618	2	Pass	0.000	7.963	0.000	4.000
53	6-Dec-24	1,636	19	Pass	0.000	7.963	0.000	4.000
54	7-Dec-24	1,649	13	Pass	0.000	7.963	0.000	4.000
55	8-Dec-24	1,649	0	Pass	0.000	7.963	0.000	4.000
56	9-Dec-24	1,649	0	Pass	0.000	7.963	0.000	4.000
57	10-Dec-24	1,649	0	Pass	0.000	7.963	0.000	4.000
58	11-Dec-24	1,649	0	NA	0.000	7.963	0.000	4.000
59	12-Dec-24	1,649	0	NA	0.000	7.963	0.000	4.000
60	13-Dec-24	1,649	0	NA	0.000	7.963	0.000	4.000
61	14-Dec-24	1,654	5	NA	0.000	7.963	0.000	4.000
62	15-Dec-24	1,713	59	Pass	0.000	7.963	0.000	4.000
63	16-Dec-24	11,828	10,115	Pass	0.000	7.963	0.000	4.000
64	17-Dec-24	1,861	9,967	Pass	0.000	7.963	0.000	4.000
65	18-Dec-24	1,994	133	Pass	0.000	7.963	0.000	4.000
66	19-Dec-24	2,000	6	Pass	0.000	7.963	0.000	4.000
67	20-Dec-24	2,000	0	Pass	0.000	7.963	0.000	4.000
68	21-Dec-24	2,000	0	Pass	0.000	7.963	0.000	4.000
69	22-Dec-24	2,114	114	Pass	0.000	7.963	0.000	4.000
70	23-Dec-24	2,150	36	Pass	0.000	7.963	0.000	4.000
71	24-Dec-24	2,150	0	NA	2.667	6.903	0.000	4.000
72	25-Dec-24	2,189	39	Pass	0.000	6.903	0.000	4.000
73	26-Dec-24	2,339	150	Pass	0.000	6.903	0.000	4.000
74	27-Dec-24	2,509	170	Pass	0.000	6.903	0.000	4.000

Figure 11-10: 17 – 1/2" Hole Section Solid Handling System Analysis Table

	Dewatering											
	Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Disposed and Lost	
					Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
	-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
7	21-Oct-24	155	4	0	500	0	0	0	0	0	0	
8	22-Oct-24	225	70	700	1,200	0	0	0	0	0	0	
9	23-Oct-24	495	270	200	1,400	0	0	0	0	0	0	
10	24-Oct-24	730	235	300	1,700	0	0	0	0	0	0	
11	25-Oct-24	800	70	300	2,000	0	0	0	0	0	0	
12	26-Oct-24	1,073	273	300	2,300	0	0	0	0	0	0	
13	27-Oct-24	1,227	154	300	2,600	0	0	0	0	0	0	
14	28-Oct-24	1,356	129	300	2,900	0	0	0	0	0	0	
15	29-Oct-24	1,373	17	300	3,200	0	0	0	0	0	0	
16	30-Oct-24	1,450	77	300	3,500	0	0	0	0	0	0	
17	31-Oct-24	1,450	0	200	3,700	0	0	0	0	0	0	
18	1-Nov-24	1,480	30	200	3,900	0	0	0	0	0	0	
19	2-Nov-24	1,480	0	250	4,150	400	400	0	0	0	0	
20	3-Nov-24	1,548	68	300	4,450	0	400	150	150	0	0	
21	4-Nov-24	1,562	14	300	4,750	0	400	100	250	0	0	
22	5-Nov-24	1,562	0	300	5,050	0	400	150	400	0	0	
23	6-Nov-24	1,562	0	400	5,450	0	400	0	400	0	0	
24	7-Nov-24	1,562	0	400	5,850	400	800	150	550	0	0	
25	8-Nov-24	1,562	0	200	6,050	0	800	250	800	0	0	
26	9-Nov-24	1,562	0	200	6,250	400	1,200	0	800	0	0	
27	10-Nov-24	1,562	0	200	6,450	0	1,200	0	800	0	0	
28	11-Nov-24	1,564	2	200	6,650	0	1,200	0	800	0	0	
29	12-Nov-24	1,564	0	200	6,850	0	1,200	0	800	0	0	
30	13-Nov-24	1,564	0	200	7,050	0	1,200	0	800	0	0	
31	14-Nov-24	1,564	0	200	7,250	0	1,200	150	950	0	0	
32	15-Nov-24	1,564	0	200	7,450	400	1,600	250	1,200	0	0	
33	16-Nov-24	1,564	0	200	7,650	400	2,000	400	1,600	0	0	
34	17-Nov-24	1,564	0	200	7,850	350	2,350	350	1,950	50	50	
35	18-Nov-24	1,564	0	200	8,050	0	2,350	200	2,150	0	50	
36	19-Nov-24	1,564	0	200	8,250	400	2,750	200	2,350	50	100	
37	20-Nov-24	1,564	0	200	8,450	400	3,150	100	2,450	0	100	
38	21-Nov-24	1,429	0	200	8,650	400	3,550	400	2,850	200	300	
39	22-Nov-24	1,429	0	200	8,850	0	3,550	200	3,050	0	300	
40	23-Nov-24	1,429	0	200	9,050	0	3,550	200	3,250	0	300	

41	24-Nov-24	1,429	0	200	9,250	0	3,550	0	3,250	0	300
42	25-Nov-24	1,440	11	200	9,450	400	3,950	0	3,250	0	300
43	26-Nov-24	1,447	7	100	9,550	0	3,950	150	3,400	0	300
44	27-Nov-24	1,472	25	100	9,650	0	3,950	0	3,400	0	300
45	28-Nov-24	1,507	35	100	9,750	400	4,350	250	3,650	0	300
46	29-Nov-24	1,552	45	200	9,950	0	4,350	0	3,650	0	300
47	30-Nov-24	1,552	0	200	10,150	0	4,350	0	3,650	0	300
48	1-Dec-24	1,571	19	200	10,350	0	4,350	0	3,650	0	300
49	2-Dec-24	1,592	21	100	10,450	0	4,350	150	3,800	0	300
50	3-Dec-24	1,593	1	100	10,550	0	4,350	0	3,800	0	300
51	4-Dec-24	1,616	23	150	10,700	0	4,350	0	3,800	0	300
52	5-Dec-24	1,618	2	200	10,900	0	4,350	0	3,800	0	300
53	6-Dec-24	1,636	19	300	11,200	0	4,350	250	4,050	0	300
54	7-Dec-24	1,649	13	200	11,400	400	4,750	0	4,050	0	300
55	8-Dec-24	1,649	0	400	11,800	400	5,150	400	4,450	0	300
56	9-Dec-24	1,649	0	150	11,950	0	5,150	400	4,850	0	300
57	10-Dec-24	1,649	0	150	12,100	0	5,150	400	5,250	0	300
58	11-Dec-24	1,649	0	500	12,600	400	5,550	0	5,250	0	300
59	12-Dec-24	1,649	0	500	13,100	400	5,950	400	5,650	50	350
60	13-Dec-24	1,649	0	100	13,200	400	6,350	350	6,000	0	350
61	14-Dec-24	1,654	5	100	13,300	400	6,750	150	6,150	0	350
62	15-Dec-24	1,713	59	100	13,400	400	7,150	250	6,400	0	350
63	16-Dec-24	11,828	10,115	100	13,500	400	7,550	250	6,650	0	350
64	17-Dec-24	1,861	9,967	100	13,600	400	7,950	250	6,900	0	350
65	18-Dec-24	1,994	133	100	13,700	400	8,350	400	7,300	0	350
66	19-Dec-24	2,000	6	100	13,800	400	8,750	400	7,700	0	350
67	20-Dec-24	2,000	0	100	13,900	400	9,150	250	7,950	0	350
68	21-Dec-24	2,000	0	100	14,000	400	9,550	400	8,350	0	350
69	22-Dec-24	2,114	114	100	14,100	400	9,950	400	8,750	0	350
70	23-Dec-24	2,150	36	150	14,250	0	9,950	0	8,750	0	350
71	24-Dec-24	2,150	0	100	14,350	0	9,950	100	8,850	0	350
72	25-Dec-24	2,189	39	150	14,500	0	9,950	0	8,850	150	500
73	26-Dec-24	2,339	150	150	14,650	0	9,950	150	9,000	0	500
74	27-Dec-24	2,509	170	100	14,750	0	9,950	200	9,200	0	500

Figure 11-11: 17 – 1/2" Hole Section Dewatering Table

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	Al	Sulfate	Ca
				7-9	<800	<50	< 80	< 50	< 3	< 50	< 600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
7	21-Oct-24	155	4	0	0	0	0	0	0	0	0
8	22-Oct-24	225	70	0	0	0	0	0	0	0	0
9	23-Oct-24	495	270	0	0	0	0	0	0	0	0
10	24-Oct-24	730	235	0	0	0	0	0	0	0	0
11	25-Oct-24	800	70	0	0	0	0	0	0	0	0
12	26-Oct-24	1,073	273	0	0	0	0	0	0	0	0
13	27-Oct-24	1,227	154	0	0	0	0	0	0	0	0
14	28-Oct-24	1,356	129	0	0	0	0	0	0	0	0
15	29-Oct-24	1,373	17	0	0	0	0	0	0	0	0
16	30-Oct-24	1,450	77	0	0	0	0	0	0	0	0
17	31-Oct-24	1,450	0	0	0	0	0	0	0	0	0
18	1-Nov-24	1,480	30	0	0	0	0	0	0	0	0
19	2-Nov-24	1,480	0	7	1,200	26	42	0	1	36	1,000
20	3-Nov-24	1,548	68	7	1,200	26	42	15	1	36	1,000
21	4-Nov-24	1,562	14	7	1,200	26	42	15	1	36	1,000
22	5-Nov-24	1,562	0	7	1,200	26	42	15	1	36	1,000
23	6-Nov-24	1,562	0	0	0	0	0	0	0	0	0
24	7-Nov-24	1,562	0	7	1,200	35	56	20	1	36	1,000
25	8-Nov-24	1,562	0	7	1,200	35	56	20	1	36	1,000
26	9-Nov-24	1,562	0	0	0	0	0	0	0	0	0
27	10-Nov-24	1,562	0	0	0	0	0	0	0	0	0
28	11-Nov-24	1,564	2	0	0	0	0	0	0	0	0
29	12-Nov-24	1,564	0	0	0	0	0	0	0	0	0
30	13-Nov-24	1,564	0	0	0	0	0	0	0	0	0
31	14-Nov-24	1,564	0	0	0	0	0	0	0	0	0
32	15-Nov-24	1,564	0	7	1,100	34	54	20	1	35	1,000
33	16-Nov-24	1,564	0	0	0	0	0	0	0	0	0
34	17-Nov-24	1,564	0	7	1,000	30	48	7	3	36	700
35	18-Nov-24	1,564	0	0	0	0	0	0	0	0	0
36	19-Nov-24	1,564	0	7	1,000	26	42	30	2	37	700
37	20-Nov-24	1,564	0	0	0	0	0	0	0	0	0
38	21-Nov-24	1,429	0	0	0	0	0	0	0	0	0
39	22-Nov-24	1,429	0	0	0	0	0	0	0	0	0
40	23-Nov-24	1,429	0	0	0	0	0	0	0	0	0

41	24-Nov-24	1,429	0	0	0	0	0	0	0	0	0
42	25-Nov-24	1,440	11	0	0	0	0	0	0	0	0
43	26-Nov-24	1,447	7	0	0	0	0	0	0	0	0
44	27-Nov-24	1,472	25	0	0	0	0	0	0	0	0
45	28-Nov-24	1,507	35	0	0	0	0	0	0	0	0
46	29-Nov-24	1,552	45	0	0	0	0	0	0	0	0
47	30-Nov-24	1,552	0	0	0	0	0	0	0	0	0
48	1-Dec-24	1,571	19	0	0	0	0	0	0	0	0
49	2-Dec-24	1,592	21	0	0	0	0	0	0	0	0
50	3-Dec-24	1,593	1	0	0	0	0	0	0	0	0
51	4-Dec-24	1,616	23	0	0	0	0	0	0	0	0
52	5-Dec-24	1,618	2	0	0	0	0	0	0	0	0
53	6-Dec-24	1,636	19	0	0	0	0	0	0	0	0
54	7-Dec-24	1,649	13	0	0	0	0	0	0	0	0
55	8-Dec-24	1,649	0	0	0	0	0	0	0	0	0
56	9-Dec-24	1,649	0	0	0	0	0	0	0	0	0
57	10-Dec-24	1,649	0	0	0	0	0	0	0	0	0
58	11-Dec-24	1,649	0	7	800	25	47	7	2	35	400
59	12-Dec-24	1,649	0	7	800	25	47	7	2	35	400
60	13-Dec-24	1,649	0	7	800	25	47	7	2	35	400
61	14-Dec-24	1,654	5	7	800	25	47	7	2	35	400
62	15-Dec-24	1,713	59	7	1,000	30	48	25	2	35	900
63	16-Dec-24	11,828	10,115	7	1,000	30	48	25	2	35	900
64	17-Dec-24	1,861	9,967	7	1,000	30	48	25	2	35	900
65	18-Dec-24	1,994	133	7	1,000	30	48	25	2	35	900
66	19-Dec-24	2,000	6	7	1,000	30	48	25	2	35	900
67	20-Dec-24	2,000	0	7	1,000	30	48	25	2	35	900
68	21-Dec-24	2,000	0	7	1,000	30	48	25	2	35	900
69	22-Dec-24	2,114	114	7	1,000	30	48	25	2	35	900
70	23-Dec-24	2,150	36	7	1,000	30	48	25	2	35	900
71	24-Dec-24	2,150	0	7	1,000	30	48	25	2	35	900
72	25-Dec-24	2,189	39	7	1,000	30	48	25	2	35	900
73	26-Dec-24	2,339	150	7	1,000	30	48	25	2	35	900
74	27-Dec-24	2,509	170	7	1,000	30	48	25	2	35	900

Figure 11-12: 17 – 1/2" Hole Section Dewatering Analysis Table

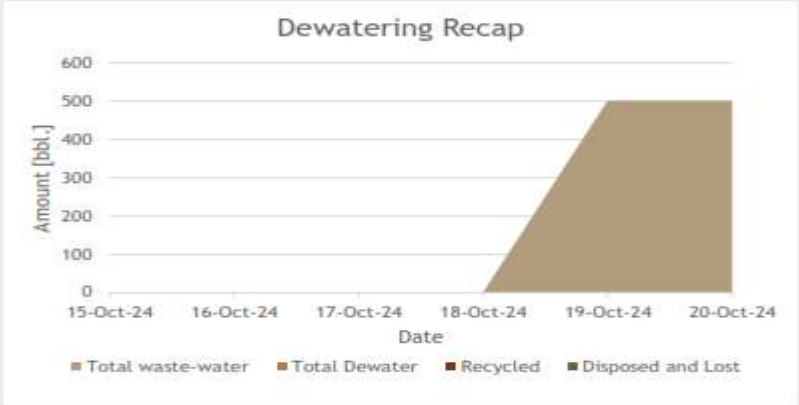


Figure 11-13: 17 – 1/2" Hole Section Dewatering Recap Graph

Chemical																			
No.	Date	Cement		Na_2SiO_3		Coagulant		Polymer		Lime		Soda ash		Citric acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
7	21-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
8	22-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
9	23-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
10	24-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
11	25-Oct-24	2,000	2,000	0	0	0	0	0	0	0	0	0	0	0	0	0	0
12	26-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
13	27-Oct-24	0	0	0	0	0	0	0	0	2,000	0	0	0	0	0	0	0
14	28-Oct-24	3,000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
15	29-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
16	30-Oct-24	4,000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
17	31-Oct-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
18	1-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
19	2-Nov-24	0	3,000	0	0	0	0	0	0	0	100	0	125	0	0	0	0
20	3-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
21	4-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
22	5-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
23	6-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
24	7-Nov-24	0	0	0	0	0	0	0	0	0	75	0	100	0	0	0	0
25	8-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
26	9-Nov-24	4,000	3,200	0	0	0	0	0	0	0	75	0	150	0	0	0	0
27	10-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
28	11-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
29	12-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
30	13-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
31	14-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
32	15-Nov-24	0	1,000	0	0	0	25	0	0	0	50	0	100	0	0	0	0
33	16-Nov-24	5,000	1,000	440	0	0	0	0	0	0	0	0	0	0	0	0	0
34	17-Nov-24	0	1,000	0	40	0	0	0	0	0	0	0	0	0	0	0	0
35	18-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
36	19-Nov-24	0	2,000	0	60	0	0	0	0	0	50	0	150	0	0	0	0
37	20-Nov-24	0	0	0	0	0	0	0	0	0	50	0	150	0	0	0	0
38	21-Nov-24	0	800	0	20	0	0	0	0	0	50	0	150	0	0	0	0
39	22-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
40	23-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
41	24-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
42	25-Nov-24	0	0	0	0	0	0	0	0	0	75	0	150	0	0	0	0
43	26-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
44	27-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
45	28-Nov-24	4,000	1,750	0	25	0	0	0	0	1,000	75	500	150	0	0	0	0
46	29-Nov-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
47	30-Nov-24	0	2,500	0	40	0	0	0	0	0	0	0	0	0	0	0	0
48	1-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
49	2-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
50	3-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

51	4-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
52	5-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
53	6-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
54	7-Dec-24	0	0	0	0	0	0	0	0	0	75	0	150	0	0	0	0
55	8-Dec-24	0	0	0	0	0	0	0	0	0	75	0	150	0	0	0	0
56	9-Dec-24	0	0	0	0	0	0	0	0	0	75	0	150	0	0	0	0
57	10-Dec-24	0	0	0	0	0	0	0	0	0	75	0	100	0	0	0	0
58	11-Dec-24	0	500	0	10	0	0	0	0	0	50	0	0	0	0	0	0
59	12-Dec-24	0	2,500	0	10	0	0	0	0	0	50	0	50	0	0	0	0
60	13-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
61	14-Dec-24	4,000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
62	15-Dec-24	4,000	0	0	0	0	0	0	1	0	50	0	50	0	0	0	0
63	16-Dec-24	0	0	0	0	0	0	0	1	0	50	0	50	0	0	0	0
64	17-Dec-24	0	0	0	0	0	0	0	1	0	50	0	50	0	0	0	0
65	18-Dec-24	0	0	0	0	0	0	0	1	0	50	0	50	0	0	0	0
66	19-Dec-24	0	0	0	0	0	0	0	1	0	50	0	50	0	0	0	0
67	20-Dec-24	0	0	0	0	0	0	0	1	0	75	0	0	0	0	0	0
68	21-Dec-24	0	0	0	0	0	0	0	2	0	75	0	0	0	0	0	0
69	22-Dec-24	0	4,000	0	0	0	0	0	2	0	75	0	0	0	0	0	0
70	23-Dec-24	0	4,000	0	0	0	0	0	2	0	75	0	0	0	0	0	0
71	24-Dec-24	4,000	2,000	0	20	0	0	0	0	0	0	0	0	0	0	0	0
72	25-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
73	26-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
74	27-Dec-24	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Figure 11-14: 17 – 1/2" Hole Section Chemical Table

12 – 1/4" Hole Section Information

Rig Name	208 OEOC
Start Date	Dec. 15th 2024
End Date	Feb. 12th 2025
Start Depth (m)	1713
End Depth (m)	3895
Duration (days)	60

12 – 1/4" Hole Section Operation's Recap

Solid Handling System									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Waste		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
62	15-Dec-24	1,713	59	0	0	0	14,850	700	12,022
63	16-Dec-24	11,828	10,115	0	0	0	14,850	300	12,322
64	17-Dec-24	1,861	9,967	0	0	0	14,850	300	12,622
65	18-Dec-24	1,994	133	600	600	0	14,850	0	12,622
66	19-Dec-24	2,000	6	600	1,200	0	14,850	0	12,622
67	20-Dec-24	2,000	0	600	1,800	0	14,850	0	12,622
68	21-Dec-24	2,000	0	600	2,400	0	14,850	0	12,622
69	22-Dec-24	2,114	114	600	3,000	0	14,850	150	12,772
70	23-Dec-24	2,150	36	0	3,000	0	14,850	150	12,922
71	24-Dec-24	2,150	0	0	3,000	1,500	16,350	250	13,172
72	25-Dec-24	2,189	39	0	3,000	0	16,350	1,000	14,172
73	26-Dec-24	2,339	150	300	3,300	300	16,650	1,000	15,172
74	27-Dec-24	2,509	170	0	3,300	0	16,650	300	15,472
75	28-Dec-24	2,685	176	0	3,300	0	16,650	0	15,472
76	29-Dec-24	2,695	10	0	3,300	0	16,650	0	15,472
77	30-Dec-24	2,737	42	0	3,300	0	16,650	0	15,472
78	31-Dec-24	2,810	73	0	3,300	0	16,650	0	15,472
79	1-Jan-25	2,810	0	0	3,300	0	16,650	1,000	16,472
80	2-Jan-25	3,007	197	1,077	4,377	2,577	19,227	1,000	17,472
81	3-Jan-25	2,868	-139	0	4,377	0	19,227	755	18,227
82	4-Jan-25	2,870	2	0	4,377	0	19,227	0	18,227
83	5-Jan-25	2,941	71	0	4,377	0	19,227	0	18,227
84	6-Jan-25	3,007	66	0	4,377	0	19,227	0	18,227
85	7-Jan-25	3,007	0	0	4,377	0	19,227	250	18,477
86	8-Jan-25	3,007	0	0	4,377	0	19,227	0	18,477
87	9-Jan-25	3,018	11	0	4,377	0	19,227	0	18,477
88	10-Jan-25	3,024	6	0	4,377	0	19,227	0	18,477
89	11-Jan-25	3,027	4	0	4,377	0	19,227	0	18,477
90	12-Jan-25	3,054	27	0	4,377	0	19,227	0	18,477
91	13-Jan-25	3,140	86	0	4,377	0	19,227	0	18,477
92	14-Jan-25	3,236	96	900	5,277	900	20,127	0	18,477
93	15-Jan-25	3,240	4	0	5,277	0	20,127	0	18,477
94	16-Jan-25	3,240	0	0	5,277	0	20,127	0	18,477
95	17-Jan-25	3,274	34	0	5,277	0	20,127	0	18,477

96	18-Jan-25	3,275	1	800	6,077	800	20,927	0	18,477
97	19-Jan-25	3,284	9	0	6,077	0	20,927	0	18,477
98	20-Jan-25	3,284	0	0	6,077	0	20,927	0	18,477
99	21-Jan-25	3,284	0	0	6,077	0	20,927	0	18,477
100	22-Jan-25	3,318	34	0	6,077	0	20,927	0	18,477
101	23-Jan-25	3,427	109	0	6,077	0	20,927	0	18,477
102	24-Jan-25	3,535	108	0	6,077	0	20,927	0	18,477
103	25-Jan-25	3,620	85	0	6,077	0	20,927	150	18,627
104	26-Jan-25	3,671	51	0	6,077	0	20,927	0	18,627
105	27-Jan-25	3,741	70	0	6,077	0	20,927	100	18,727
106	28-Jan-25	3,790	49	0	6,077	0	20,927	250	18,977
107	29-Jan-25	3,822	32	0	6,077	0	20,927	250	19,227
108	30-Jan-25	3,846	24	0	6,077	0	20,927	250	19,477
109	31-Jan-25	3,872	26	0	6,077	0	20,927	200	19,677
110	1-Feb-25	3,872	0	0	6,077	0	20,927	250	19,927
111	2-Feb-25	3,891	19	0	6,077	0	20,927	200	20,127
112	3-Feb-25	3,891	0	0	6,077	0	20,927	200	20,327
113	4-Feb-25	3,891	0	800	6,877	800	21,727	200	20,527
114	5-Feb-25	3,895	4	0	6,877	0	21,727	0	20,527
115	6-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527
116	7-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527
117	8-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527
118	9-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527
119	10-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527
120	11-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527
121	12-Feb-25	3,895	0	0	6,877	0	21,727	0	20,527

Figure 11-15: 12 – 1/4" Hole Section Solid Handling System Table

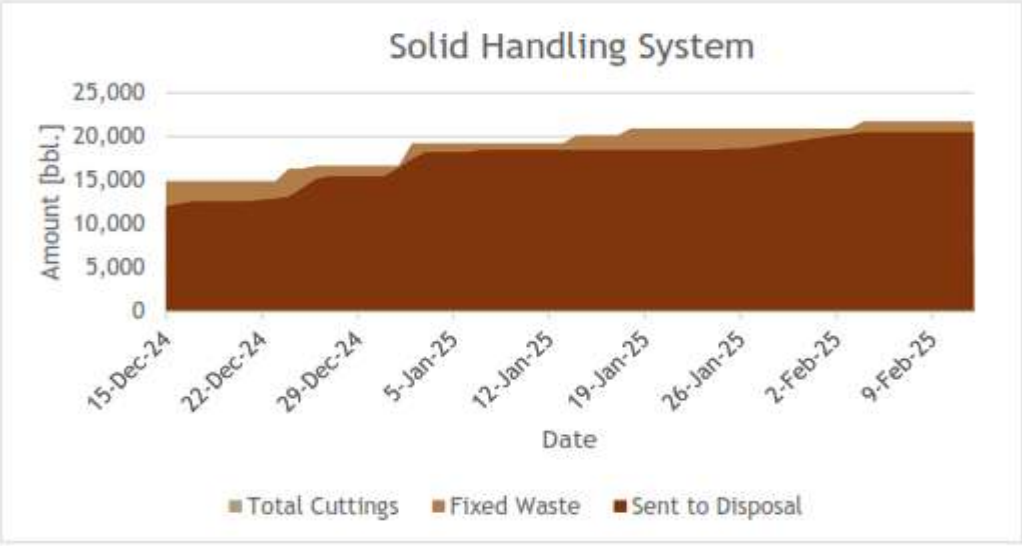


Figure 11-16: 12 – 1/4" Hole Section Solid Handling System Graph

Solid Handling System analysis

Report No.	Date	Depth	Drilled	Can test	Cement/Waste		SodSil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/M3	kg/M3	kg/M3	kg/M3
62	15-Dec-24	1,713	59	NA	0.000	0.000	0.000	0.000
63	16-Dec-24	11,828	10,115	NA	0.000	0.000	0.000	0.000
64	17-Dec-24	1,861	9,967	NA	0.000	0.000	0.000	0.000
65	18-Dec-24	1,994	133	Pass	0.000	0.000	0.000	0.000
66	19-Dec-24	2,000	6	Pass	0.000	0.000	0.000	0.000
67	20-Dec-24	2,000	0	Pass	0.000	0.000	0.000	0.000
68	21-Dec-24	2,000	0	Pass	0.000	0.000	0.000	0.000
69	22-Dec-24	2,114	114	Pass	0.000	0.000	0.000	0.000
70	23-Dec-24	2,150	36	NA	0.000	0.000	0.000	0.000
71	24-Dec-24	2,150	0	NA	1.333	1.333	0.000	0.000
72	25-Dec-24	2,189	39	NA	0.000	1.333	0.000	0.000
73	26-Dec-24	2,339	150	Pass	2.667	2.000	0.060	0.060
74	27-Dec-24	2,509	170	NA	0.000	2.000	0.000	0.060
75	28-Dec-24	2,685	176	NA	0.000	2.000	0.000	0.060
76	29-Dec-24	2,695	10	NA	0.000	2.000	0.000	0.060
77	30-Dec-24	2,737	42	NA	0.000	2.000	0.000	0.060
78	31-Dec-24	2,810	73	NA	0.000	2.000	0.000	0.060
79	1-Jan-25	2,810	0	NA	0.000	2.000	0.000	0.060
80	2-Jan-25	3,007	197	Pass	0.466	1.489	0.037	0.049
81	3-Jan-25	2,868	-139	NA	0.000	1.489	0.000	0.049
82	4-Jan-25	2,870	2	NA	0.000	1.489	0.000	0.049
83	5-Jan-25	2,941	71	NA	0.000	1.489	0.000	0.049
84	6-Jan-25	3,007	66	NA	0.000	1.489	0.000	0.049
85	7-Jan-25	3,007	0	NA	0.000	1.489	0.000	0.049
86	8-Jan-25	3,007	0	NA	0.000	1.489	0.000	0.049
87	9-Jan-25	3,018	11	NA	0.000	1.489	0.000	0.049
88	10-Jan-25	3,024	6	NA	0.000	1.489	0.000	0.049
89	11-Jan-25	3,027	4	NA	0.000	1.489	0.000	0.049
90	12-Jan-25	3,054	27	NA	0.000	1.489	0.000	0.049
91	13-Jan-25	3,140	86	NA	0.000	1.489	0.000	0.049
92	14-Jan-25	3,236	96	Pass	1.667	1.533	0.044	0.047
93	15-Jan-25	3,240	4	NA	0.000	1.533	0.000	0.047
94	16-Jan-25	3,240	0	NA	0.000	1.533	0.000	0.047
95	17-Jan-25	3,274	34	NA	0.000	1.533	0.000	0.047
96	18-Jan-25	3,275	1	Pass	1.625	1.551	0.050	0.048
97	19-Jan-25	3,284	9	NA	0.000	1.551	0.000	0.048
98	20-Jan-25	3,284	0	NA	0.000	1.551	0.000	0.048
99	21-Jan-25	3,284	0	NA	0.000	1.551	0.000	0.048
100	22-Jan-25	3,318	34	NA	0.000	1.551	0.000	0.048

101	23-Jan-25	3,427	109	NA	0.000	1.551	0.000	0.048
102	24-Jan-25	3,535	108	NA	0.000	1.551	0.000	0.048
103	25-Jan-25	3,620	85	NA	0.000	1.551	0.000	0.048
104	26-Jan-25	3,671	51	NA	0.000	1.551	0.000	0.048
105	27-Jan-25	3,741	70	NA	0.000	1.551	0.000	0.048
106	28-Jan-25	3,790	49	NA	0.000	1.551	0.000	0.048
107	29-Jan-25	3,822	32	NA	0.000	1.551	0.000	0.048
108	30-Jan-25	3,846	24	NA	0.000	1.551	0.000	0.048
109	31-Jan-25	3,872	26	NA	0.000	1.551	0.000	0.048
110	1-Feb-25	3,872	0	NA	0.000	1.551	0.000	0.048
111	2-Feb-25	3,891	19	NA	0.000	1.551	0.000	0.048
112	3-Feb-25	3,891	0	NA	0.000	1.551	0.000	0.048
113	4-Feb-25	3,891	0	Pass	1.500	1.543	0.038	0.046
114	5-Feb-25	3,895	4	NA	0.000	1.543	0.000	0.046
115	6-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046
116	7-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046
117	8-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046
118	9-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046
119	10-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046
120	11-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046
121	12-Feb-25	3,895	0	NA	0.000	1.543	0.000	0.046

Figure 11-17: 12 – 1/4" Hole Section Solid Handling System Analysis Table

Dewatering

Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
61	14-Dec-24	1,654	5	100	12,600	400	6,750	150	6,300	0	200
62	15-Dec-24	1,713	59	100	12,700	400	7,150	250	6,550	0	200
63	16-Dec-24	11,828	10,115	100	12,800	400	7,550	400	6,950	0	200
64	17-Dec-24	1,861	9,967	100	12,900	400	7,950	400	7,350	0	200
65	18-Dec-24	1,994	133	100	13,000	400	8,350	400	7,750	0	200
66	19-Dec-24	2,000	6	100	13,100	400	8,750	400	8,150	0	200
67	20-Dec-24	2,000	0	100	13,200	400	9,150	250	8,400	0	200
68	21-Dec-24	2,000	0	100	13,300	400	9,550	400	8,800	0	200
69	22-Dec-24	2,114	114	100	13,400	400	9,950	400	9,200	0	200
70	23-Dec-24	2,150	36	150	13,550	0	9,950	0	9,200	0	200
71	24-Dec-24	2,150	0	100	13,650	0	9,950	100	9,300	0	200
72	25-Dec-24	2,189	39	150	13,800	0	9,950	0	9,300	150	350
73	26-Dec-24	2,339	150	150	13,950	400	10,350	300	9,600	0	350
74	27-Dec-24	2,509	170	100	14,050	0	10,350	200	9,800	0	350
75	28-Dec-24	2,685	176	200	14,250	0	10,350	200	10,000	0	350
76	29-Dec-24	2,695	10	200	14,450	400	10,750	100	10,100	0	350
77	30-Dec-24	2,737	42	150	14,600	0	10,750	150	10,250	0	350
78	31-Dec-24	2,810	73	100	14,700	400	11,150	150	10,400	0	350
79	1-Jan-25	2,810	0	150	14,850	0	11,150	300	10,700	0	350

80	2-Jan-25	3,007	197	100	14,950	400	11,550	200	10,900	0	350
81	3-Jan-25	2,868	-139	100	15,050	0	11,550	200	11,100	0	350
82	4-Jan-25	2,870	2	150	15,200	400	11,950	200	11,300	0	350
83	5-Jan-25	2,941	71	100	15,300	0	11,950	150	11,450	0	350
84	6-Jan-25	3,007	66	100	15,400	0	11,950	150	11,600	0	350
85	7-Jan-25	3,007	0	100	15,500	0	11,950	0	11,600	0	350
86	8-Jan-25	3,007	0	100	15,600	0	11,950	0	11,600	0	350
87	9-Jan-25	3,018	11	100	15,700	0	11,950	0	11,600	0	350
88	10-Jan-25	3,024	6	100	15,800	0	11,950	0	11,600	0	350
89	11-Jan-25	3,027	4	100	15,900	0	11,950	0	11,600	0	350
90	12-Jan-25	3,054	27	50	15,950	0	11,950	100	11,700	0	350
91	13-Jan-25	3,140	86	400	16,350	500	12,450	0	11,700	0	350
92	14-Jan-25	3,236	96	400	16,750	100	12,550	100	11,800	0	350
93	15-Jan-25	3,240	4	0	16,750	0	12,550	0	11,800	0	350
94	16-Jan-25	3,240	0	0	16,750	400	12,950	400	12,200	0	350
95	17-Jan-25	3,274	34	0	16,750	0	12,950	0	12,200	0	350
96	18-Jan-25	3,275	1	0	16,750	0	12,950	0	12,200	0	350
97	19-Jan-25	3,284	9	0	16,750	0	12,950	0	12,200	0	350
98	20-Jan-25	3,284	0	50	16,800	0	12,950	50	12,250	0	350
99	21-Jan-25	3,284	0	50	16,850	0	12,950	0	12,250	0	350
100	22-Jan-25	3,318	34	50	16,900	0	12,950	50	12,300	0	350
101	23-Jan-25	3,427	109	100	17,000	0	12,950	100	12,400	0	350
102	24-Jan-25	3,535	108	150	17,150	350	13,300	200	12,600	0	350
103	25-Jan-25	3,620	85	50	17,200	0	13,300	50	12,650	0	350
104	26-Jan-25	3,671	51	50	17,250	0	13,300	0	12,650	0	350
105	27-Jan-25	3,741	70	100	17,350	0	13,300	100	12,750	0	350
106	28-Jan-25	3,790	49	100	17,450	0	13,300	100	12,850	0	350
107	29-Jan-25	3,822	32	150	17,600	400	13,700	100	12,950	0	350
108	30-Jan-25	3,846	24	200	17,800	0	13,700	200	13,150	0	350
109	31-Jan-25	3,872	26	150	17,950	400	14,100	200	13,350	0	350
110	1-Feb-25	3,872	0	100	18,050	0	14,100	100	13,450	0	350
111	2-Feb-25	3,891	19	50	18,100	0	14,100	50	13,500	0	350
112	3-Feb-25	3,891	0	50	18,150	0	14,100	0	13,500	0	350
113	4-Feb-25	3,891	0	50	18,200	0	14,100	0	13,500	0	350
114	5-Feb-25	3,895	4	50	18,250	0	14,100	150	13,650	0	350
115	6-Feb-25	3,895	0	50	18,300	400	14,500	0	13,650	0	350
116	7-Feb-25	3,895	0	200	18,500	0	14,100	0	13,650	0	350
117	8-Feb-25	3,895	0	200	18,700	400	14,500	400	14,050	0	350
118	9-Feb-25	3,895	0	200	18,900	0	14,500	0	14,050	0	350
119	10-Feb-25	3,895	0	200	19,100	400	14,900	400	14,450	0	350
120	11-Feb-25	3,895	0	200	19,300	400	15,300	400	14,850	0	350
121	12-Feb-25	3,895	0	200	19,500	400	15,700	400	15,250	0	350

Figure 11-18: 12 – 1/4" Hole Section Dewatering Table

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	Al	Sulfate	Ca
				7-9	<800	<50	< 80	< 50	< 3	< 50	< 600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
61	14-Dec-24	1,654	5	0	0	0	0	0	0	0	0
62	15-Dec-24	1,713	59	0	0	0	0	0	0	0	0
63	16-Dec-24	11,828	10,115	0	0	0	0	0	0	0	0
64	17-Dec-24	1,861	9,967	0	0	0	0	0	0	0	0
65	18-Dec-24	1,994	133	0	0	0	0	0	0	0	0
66	19-Dec-24	2,000	6	0	0	0	0	0	0	0	0
67	20-Dec-24	2,000	0	0	0	0	0	0	0	0	0
68	21-Dec-24	2,000	0	0	0	0	0	0	0	0	0
69	22-Dec-24	2,114	114	0	0	0	0	0	0	0	0
70	23-Dec-24	2,150	36	0	0	0	0	0	0	0	0
71	24-Dec-24	2,150	0	0	0	0	0	0	0	0	0
72	25-Dec-24	2,189	39	0	0	0	0	0	0	0	0
73	26-Dec-24	2,339	150	0	0	0	0	0	0	0	0
74	27-Dec-24	2,509	170	0	0	0	0	0	0	0	0
75	28-Dec-24	2,685	176	0	0	0	0	0	0	0	0
76	29-Dec-24	2,695	10	0	0	0	0	0	0	0	0
77	30-Dec-24	2,737	42	0	0	0	0	0	0	0	0
78	31-Dec-24	2,810	73	0	0	0	0	0	0	0	0
79	1-Jan-25	2,810	0	0	0	0	0	0	0	0	0
80	2-Jan-25	3,007	197	0	0	0	0	0	0	0	0
81	3-Jan-25	2,868	-139	0	0	0	0	0	0	0	0
82	4-Jan-25	2,870	2	0	0	0	0	0	0	0	0
83	5-Jan-25	2,941	71	0	0	0	0	0	0	0	0
84	6-Jan-25	3,007	66	0	0	0	0	0	0	0	0
85	7-Jan-25	3,007	0	0	0	0	0	0	0	0	0
86	8-Jan-25	3,007	0	0	0	0	0	0	0	0	0
87	9-Jan-25	3,018	11	0	0	0	0	0	0	0	0
88	10-Jan-25	3,024	6	0	0	0	0	0	0	0	0
89	11-Jan-25	3,027	4	0	0	0	0	0	0	0	0
90	12-Jan-25	3,054	27	0	0	0	0	0	0	0	0
91	13-Jan-25	3,140	86	9	1,000	40	64	50	2	40	900
92	14-Jan-25	3,236	96	9	1,000	40	64	50	2	40	900
93	15-Jan-25	3,240	4	9	1,000	40	64	50	2	40	900
94	16-Jan-25	3,240	0	7	1,000	37	59	50	3	40	800
95	17-Jan-25	3,274	34	7	1,000	37	59	50	3	40	800
96	18-Jan-25	3,275	1	7	1,000	37	59	50	3	40	800
97	19-Jan-25	3,284	9	7	1,000	37	59	50	3	40	800
98	20-Jan-25	3,284	0	7	1,000	37	59	50	3	40	800
99	21-Jan-25	3,284	0	7	1,000	37	59	50	3	40	800
100	22-Jan-25	3,318	34	7	1,000	37	59	50	3	40	800

101	23-Jan-25	3,427	109	7	1,000	37	59	50	3	40	800
102	24-Jan-25	3,535	108	7	1,000	37	59	50	3	40	800
103	25-Jan-25	3,620	85	7	1,000	37	59	50	3	40	800
104	26-Jan-25	3,671	51	0	0	0	0	0	0	0	0
105	27-Jan-25	3,741	70	0	0	0	0	0	0	0	0
106	28-Jan-25	3,790	49	0	0	0	0	0	0	0	0
107	29-Jan-25	3,822	32	7	1,200	35	56	40	3	30	1,000
108	30-Jan-25	3,846	24	7	1,200	35	56	40	3	30	1,000
109	31-Jan-25	3,872	26	8	1,000	40	64	40	3	35	800
110	1-Feb-25	3,872	0	8	1,000	40	64	40	3	35	800
111	2-Feb-25	3,891	19	8	1,000	40	64	40	3	35	800
112	3-Feb-25	3,891	0	8	1,000	40	64	40	3	35	800
113	4-Feb-25	3,891	0	8	1,000	40	64	40	3	35	800
114	5-Feb-25	3,895	4	8	1,000	40	64	40	3	35	800
115	6-Feb-25	3,895	0	7	900	40	64	35	3	40	800
116	7-Feb-25	3,895	0	7	900	40	64	35	3	40	800
117	8-Feb-25	3,895	0	7	900	40	64	35	3	40	800
118	9-Feb-25	3,895	0	7	900	40	64	35	3	40	800
119	10-Feb-25	3,895	0	7	900	40	64	35	3	40	800
120	11-Feb-25	3,895	0	7	900	40	64	35	3	40	800
121	12-Feb-25	3,895	0	7	900	40	64	35	3	40	800

Figure 11-19: 12 – 1/4" Hole Section Dewatering Analysis Table

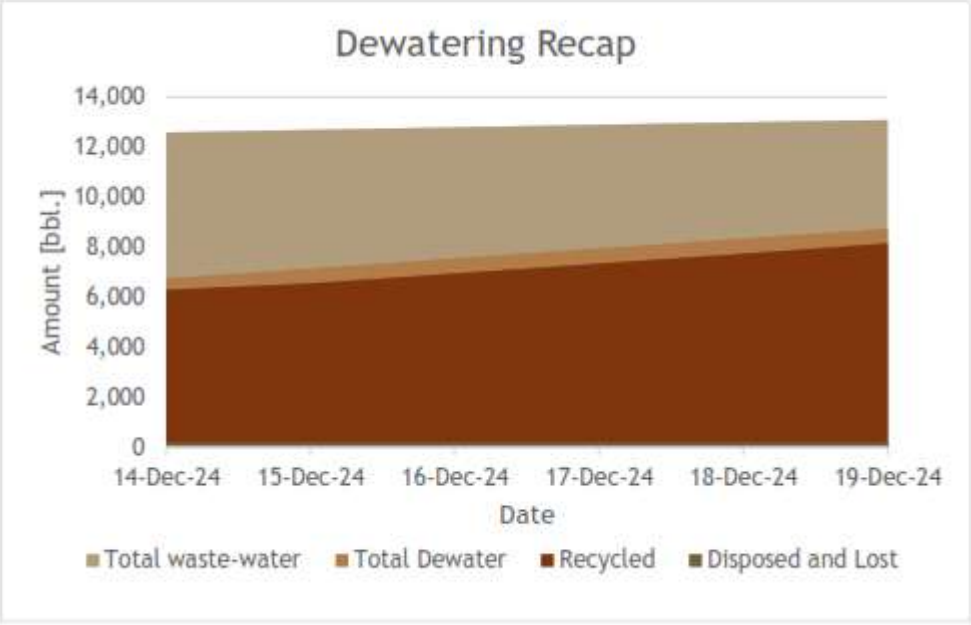


Figure 11-20: 12 – 1/4" Hole Section Dewatering Recap Graph

Chemical																	
No.	Date	Cement		Na2SiO3		Coagulant		Polymer		Lime		Soda ash		Citric acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
62	15-Dec-24	0	22,000	0	205	0	25	1	1	50	1,050	50	1,925	0	0	0	0
63	16-Dec-24	0	22,000	0	205	0	25	1	2	50	1,100	50	1,975	0	0	0	0
64	17-Dec-24	0	22,000	0	205	0	25	1	3	50	1,150	50	2,025	0	0	0	0
65	18-Dec-24	0	22,000	0	205	0	25	1	4	50	1,200	50	2,075	0	0	0	0
66	19-Dec-24	0	22,000	0	205	0	25	1	5	50	1,250	50	2,125	0	0	0	0
67	20-Dec-24	0	22,000	0	205	0	25	1	6	75	1,325	0	2,125	0	0	0	0
68	21-Dec-24	0	22,000	0	205	0	25	2	8	75	1,400	0	2,125	0	0	0	0
69	22-Dec-24	4,000	26,000	0	205	0	25	2	10	75	1,475	0	2,125	0	0	0	0
70	23-Dec-24	0	26,000	0	205	0	25	0	10	0	1,475	0	2,125	0	0	0	0
71	24-Dec-24	2,000	28,000	20	225	0	25	0	10	0	1,475	0	2,125	0	0	0	0
72	25-Dec-24	0	28,000	0	225	0	25	0	10	0	1,475	0	2,125	0	0	0	0
73	26-Dec-24	800	28,800	18	243	0	25	2	12	75	1,550	0	2,125	0	0	0	0
74	27-Dec-24	0	28,800	0	243	0	25	0	12	0	1,550	0	2,125	0	0	0	0
75	28-Dec-24	0	28,800	0	243	0	25	0	12	0	1,550	0	2,125	0	0	0	0
76	29-Dec-24	0	28,800	0	243	0	25	1	13	25	1,575	75	2,200	0	0	0	0
77	30-Dec-24	0	28,800	0	243	0	25	0	13	0	1,575	0	2,200	0	0	0	0
78	31-Dec-24	0	28,800	0	243	0	25	0	13	50	1,625	100	2,300	0	0	0	0
79	1-Jan-25	0	28,800	0	243	0	25	0	13	0	1,625	0	2,300	0	0	0	0
80	2-Jan-25	1,200	30,000	40	283	0	25	0	13	50	1,675	75	2,375	0	0	0	0
81	3-Jan-25	0	30,000	0	283	0	25	0	13	0	1,675	0	2,375	0	0	0	0
82	4-Jan-25	0	30,000	0	283	0	25	1	14	50	1,725	100	2,475	0	0	0	0
83	5-Jan-25	0	30,000	0	283	0	25	0	14	0	1,725	0	2,475	0	0	0	0
84	6-Jan-25	0	30,000	0	283	0	25	0	14	0	1,725	0	2,475	0	0	0	0
85	7-Jan-25	0	30,000	0	283	0	25	0	14	0	1,725	0	2,475	0	0	0	0
86	8-Jan-25	0	30,000	0	283	0	25	0	14	0	1,725	0	2,475	0	0	0	0
87	9-Jan-25	0	30,000	0	283	0	25	0	14	0	1,725	0	2,475	0	0	0	0
88	10-Jan-25	0	30,000	0	283	25	50	2	16	100	1,825	0	2,475	0	0	0	0
89	11-Jan-25	0	30,000	0	283	0	50	0	16	0	1,825	0	2,475	0	0	0	0
90	12-Jan-25	0	30,000	0	283	0	50	0	16	0	1,825	0	2,475	0	0	0	0
91	13-Jan-25	0	30,000	0	283	0	50	1	17	50	1,875	50	2,525	0	0	0	0
92	14-Jan-25	1,500	31,500	40	323	0	50	0	17	0	1,875	0	2,525	0	0	0	0
93	15-Jan-25	0	31,500	0	323	0	50	0	17	0	1,875	0	2,525	0	0	0	0
94	16-Jan-25	0	31,500	0	323	0	50	1	18	50	1,925	25	2,550	0	0	0	0
95	17-Jan-25	0	31,500	0	323	0	50	0	18	0	1,925	0	2,550	0	0	0	0
96	18-Jan-25	1,300	32,800	40	363	0	50	0	18	0	1,925	0	2,550	0	0	0	0
97	19-Jan-25	0	32,800	0	363	0	50	0	18	0	1,925	0	2,550	0	0	0	0
98	20-Jan-25	0	32,800	0	363	0	50	0	18	0	1,925	0	2,550	0	0	0	0
99	21-Jan-25	0	32,800	0	363	0	50	0	18	0	1,925	0	2,550	0	0	0	0
100	22-Jan-25	0	32,800	0	363	0	50	0	18	0	1,925	0	2,550	0	0	0	0
101	23-Jan-25	0	32,800	0	363	0	50	0	18	0	1,925	0	2,550	0	0	0	0
102	24-Jan-25	0	32,800	0	363	0	50	1	19	75	2,000	50	2,600	0	0	0	0
103	25-Jan-25	0	32,800	0	363	0	50	0	19	0	2,000	0	2,600	0	0	0	0
104	26-Jan-25	0	32,800	0	363	0	50	0	19	0	2,000	0	2,600	0	0	0	0
105	27-Jan-25	0	32,800	0	363	0	50	0	19	0	2,000	0	2,600	0	0	0	0
106	28-Jan-25	0	32,800	0	363	0	50	0	19	0	2,000	0	2,600	0	0	0	0
107	29-Jan-25	0	32,800	0	363	0	50	2	21	75	2,075	50	2,650	0	0	0	0
108	30-Jan-25	0	32,800	0	363	0	50	0	21	0	2,075	0	2,650	0	0	0	0
109	31-Jan-25	0	32,800	0	363	0	50	2	23	50	2,125	0	2,650	0	0	100	100
110	1-Feb-25	0	32,800	0	363	0	50	0	23	0	2,125	0	2,650	0	0	0	100

111	2-Feb-25	0	32,800	0	363	0	50	0	23	0	2,125	0	2,650	0	0	0	100
112	3-Feb-25	0	32,800	0	363	0	50	0	23	0	2,125	0	2,650	0	0	0	100
113	4-Feb-25	1,200	34,000	30	393	0	50	0	23	0	2,125	0	2,650	0	0	0	100
114	5-Feb-25	0	34,000	0	393	0	50	0	23	0	2,125	0	2,650	0	0	0	100
115	6-Feb-25	0	34,000	0	393	0	50	1	24	0	2,125	0	2,650	0	0	25	125
116	7-Feb-25	0	34,000	0	393	0	50	0	24	0	2,125	0	2,650	0	0	0	125
117	8-Feb-25	0	34,000	0	393	0	50	1	25	0	2,125	0	2,650	0	0	25	150
118	9-Feb-25	0	34,000	0	393	0	50	0	25	0	2,125	0	2,650	0	0	0	150
119	10-Feb-25	0	34,000	0	393	0	50	1	26	0	2,125	0	2,650	0	0	25	175
120	11-Feb-25	0	34,000	0	393	0	50	1	27	0	2,125	0	2,650	0	0	25	200
121	12-Feb-25	0	34,000	0	393	0	50	1	28	0	2,125	0	2,650	0	0	25	225

Figure 11-21: 12 – 1/4" Hole Section Chemical Table

8 - 3/8" Hole Section Information

Rig	208 OEOC
Start Date	Feb. 13th 2024
End Date	Feb. 23rd 2025
Start Depth (m)	3910
End Depth (m)	4180
Duration (day)	12

Table 11-3: AZNS-207 8-3/8" Hole Waste Management Information

8 - 3/8" Hole Section Operation's Recap

Solid Handling System									
Report No.	Date	Depth	Drilled	Total Cuttings		Fixed Waste		Sent to Disposal	
				Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
122	13-Feb-25	3,910	15	0	0	0	21,727	200	20,727
123	14-Feb-25	3,928	18	1,000	1,000	800	22,527	200	20,927
124	15-Feb-25	3,964	36	1,000	2,000	0	22,527	0	20,927
125	16-Feb-25	4,076	112	300	2,300	0	22,527	200	21,127
126	17-Feb-25	4,180	104	300	2,600	0	22,527	250	21,377
127	18-Feb-25	4,180	0	300	2,900	0	22,527	200	21,577
128	19-Feb-25	4,180	0	1,000	3,900	700	23,227	200	21,777
129	20-Feb-25	4,180	0	1,000	4,900	700	23,927	200	21,977
130	21-Feb-25	4,180	0	600	5,500	0	23,927	250	22,227
131	22-Feb-25	4,180	0	600	6,100	0	23,773	200	22,477
132	23-Feb-25	4,180	0	0	6,100	0	23,773	200	22,677

Figure 11-22: 8 – 3/8" Hole Section Solid Handling System Table

Solid Handling System analysis								
Report No.	Date	Depth	Drilled	Can test	Cement/Waste		SodSil/Waste	
				Daily	Daily	Average	Daily	Average
-	dd-M-yy	m	m	Pass/NA	kg/M3	kg/M3	kg/M3	kg/M3
122	13-Feb-25	3,910	15	NA	0.000	0.000	0.000	0.000
123	14-Feb-25	3,928	18	Pass	0.000	0.000	0.000	0.000
124	15-Feb-25	3,964	36	Pass	0.000	0.000	0.000	0.000
125	16-Feb-25	4,076	112	Pass	0.000	0.000	0.000	0.000
126	17-Feb-25	4,180	104	Pass	0.000	0.000	0.000	0.000
127	18-Feb-25	4,180	0	Pass	0.000	0.000	0.000	0.000
128	19-Feb-25	4,180	0	Pass	1.071	1.071	0.000	0.000
129	20-Feb-25	4,180	0	Pass	1.071	1.071	0.000	0.000
130	21-Feb-25	4,180	0	Pass	0.000	1.071	0.000	0.000
131	22-Feb-25	4,180	0	Pass	0.000	1.071	0.000	0.000
132	23-Feb-25	4,180	0	NA	0.000	1.071	0.000	0.000

Figure 11-23: 8 – 3/8" Hole Section Solid Handling System Analysis Table

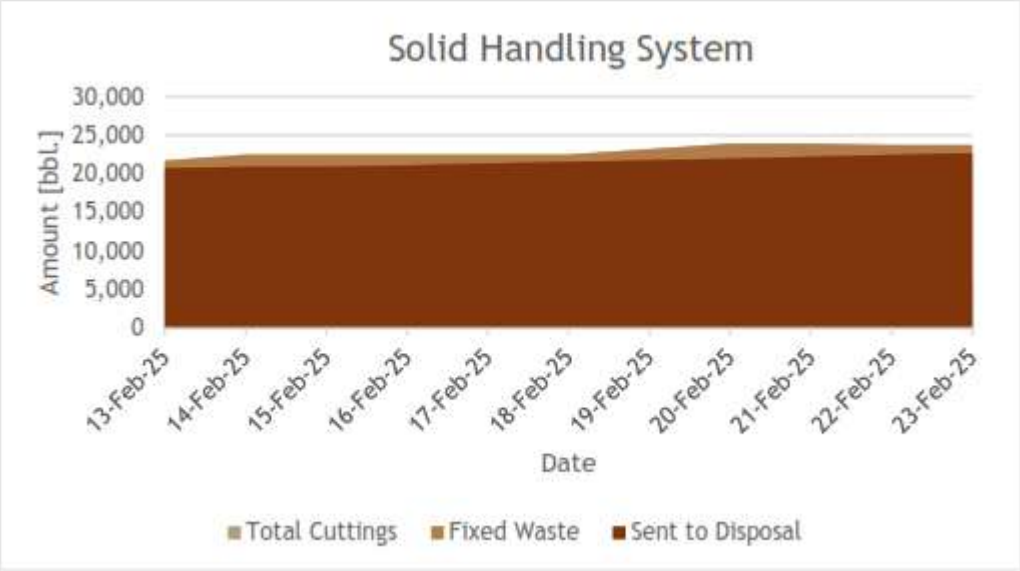


Figure 11-24: 8 – 3/8" Hole Section Solid Handling System Graph

Dewatering											
Report No.	Date	Depth	Drilled	Total waste-water		Total Dewater		Recycled		Disposed and Lost	
				Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	m	m	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.	bbl.
122	13-Feb-25	3,910	15	30	19,530	0	15,700	0	15,250	0	350
123	14-Feb-25	3,928	18	30	19,560	400	16,100	400	15,650	0	350
124	15-Feb-25	3,964	36	30	19,590	0	16,100	0	15,650	0	350
125	16-Feb-25	4,076	112	10	19,600	400	16,500	400	16,050	0	350
126	17-Feb-25	4,180	104	0	19,600	400	16,900	400	16,450	0	350
127	18-Feb-25	4,180	0	0	19,600	400	17,300	400	16,850	0	350
128	19-Feb-25	4,180	0	0	19,600	0	17,300	0	16,850	0	350
129	20-Feb-25	4,180	0	0	19,600	0	17,300	0	16,850	0	350
130	21-Feb-25	4,180	0	0	19,600	400	17,700	400	17,250	0	350
131	22-Feb-25	4,180	0	0	19,600	400	18,100	400	17,750	0	350
132	23-Feb-25	4,180	0	0	19,600	400	18,500	400	18,150	0	350
133	24-Feb-25	4,180	0	0	19,600	0	18,500	0	18,150	0	350

Figure 11-25: 8 – 3/8" Hole Section Dewatering Table

Dewatering Analysis											
Report No.	Date	Depth	Drilled	pH	Hardn.	Turb.	TSS	Nitrate	Al	Sulfate	Ca
				7-9	<800	<50	< 80	< 50	< 3	< 50	< 600
-	dd-M-yy	m	m	-	mg/L	NTU	mg/L	mg/L	mg/L	mg/L	mg/L
122	13-Feb-25	3,910	15	7	900	40	64	35	3	40	800
123	14-Feb-25	3,928	18	7	900	40	64	35	3	40	800
124	15-Feb-25	3,964	36	7	900	40	64	35	3	40	800
125	16-Feb-25	4,076	112	7	900	40	64	35	3	48	800
126	17-Feb-25	4,180	104	7	900	40	64	35	3	48	800
127	18-Feb-25	4,180	0	7	900	40	64	35	3	48	800
128	19-Feb-25	4,180	0	7	900	40	64	35	3	48	800
129	20-Feb-25	4,180	0	7	900	40	64	35	3	48	800
130	21-Feb-25	4,180	0	7	900	40	64	35	3	48	800
131	22-Feb-25	4,180	0	7	900	40	64	35	3	48	800
132	23-Feb-25	4,180	0	7	900	40	64	35	3	48	800
133	24-Feb-25	4,180	0	7	900	40	64	35	3	48	800

Figure 11-26: 8 – 3/8" Hole Section Dewatering Analysis Table

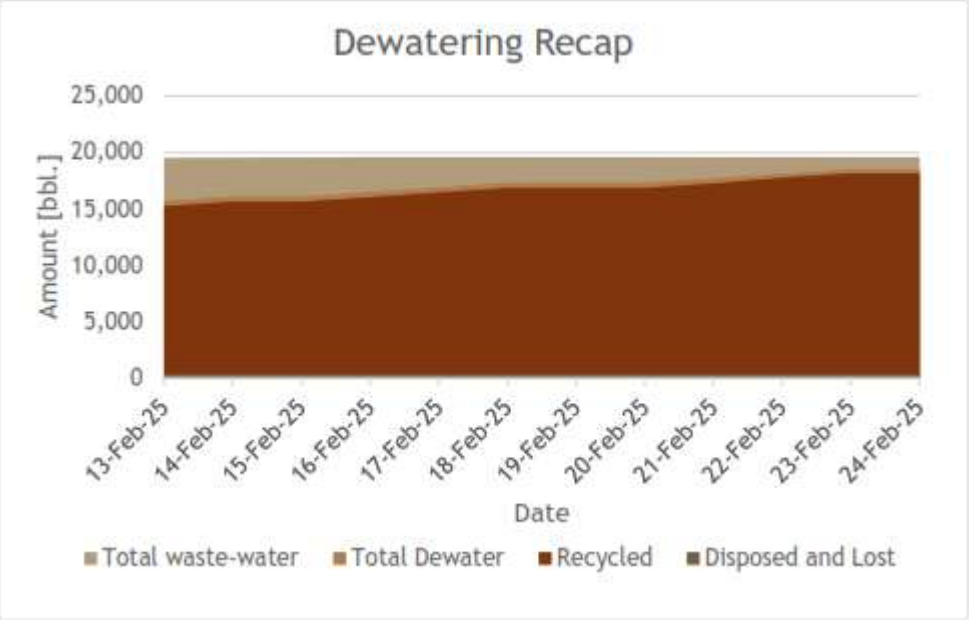


Figure 11-27: 8 – 3/8" Hole Section Dewatering Recap Graph

		Chemical															
No.	Date	Cement		Na_2SiO_3		Coagulant		Polymer		Lime		Soda ash		Citric acid		Caustic soda	
		Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.	Daily	Cum.
-	dd-M-yy	Kg		Lit.		Kg		Kg		Kg		Kg		Kg		Kg	
122	13-Feb-25	0	34,000	0	393	0	50	0	28	0	2,125	0	2,650	0	0	0	225
123	14-Feb-25	0	34,000	0	393	0	50	10	38	0	2,125	0	2,650	0	0	50	275
124	15-Feb-25	0	34,000	0	393	0	50	0	38	0	2,125	0	2,650	0	0	0	275
125	16-Feb-25	0	34,000	0	393	0	50	1	39	0	2,125	0	2,650	0	0	50	325
126	17-Feb-25	0	34,000	0	393	25	75	1	40	0	2,125	0	2,650	0	0	50	375
127	18-Feb-25	0	34,000	0	393	25	100	1	41	0	2,125	0	2,650	0	0	50	425
128	19-Feb-25	750	34,750	0	393	0	100	0	41	0	2,125	0	2,650	0	0	0	425
129	20-Feb-25	750	35,500	0	393	0	100	0	41	0	2,125	0	2,650	0	0	0	425
130	21-Feb-25	0	35,500	0	393	25	125	1	42	0	2,125	0	2,650	0	0	50	475
131	22-Feb-25	0	38,000	0	440	25	150	1	43	0	2,125	0	2,650	0	0	50	525
132	23-Feb-25	0	38,000	0	440	25	175	1	44	0	2,125	0	2,650	0	0	50	575

Figure 11-28: 8 – 3/8" Hole Section Chemical Table

12. List of Contractors

Item	Service Item	Contractor
1	Drilling Rig, Mobilization and Demobilization the Rig, Rig Move Between Well Pads	OEOC
2	Drilling Fluids and Completion Fluids	VIRA
3	Waste Management	Pars Haffaran Arvand
4	Electrical Logging and Perforation	SeaLand
5	Mud Logging	Geo Data Pars
6	Directional Drilling (MWD)	Hana Energy
7	H2S Monitoring and Control	BONYAN IMEN
8	Casing and Tubing Running	OEOC
9	Cementing	Dana Energy
10	Dry Test, DST and RTTS	OEOC
11	Slick Line	OEOC
12	Stimulation (Coiled Tubing and Acidizing and Nitrogen Lifting)	OEOC
13	Surface Well Testing	OEOC
14	Liner Hanger	PARS POOLAD
15	Well Head	OEOC

13. Appendix

13.1 DDR Summary

Hole Section 12-1/4"

Item	Date	Remark
1	15 – Oct.	Spud the rig @ 15-Oct-2024, 18:00. Started M/U stands and R/B in derrick.
2	16 – Oct.	Cont. M/U stands and R/B in derrick.
3	17 – Oct.	Perform Magnet trip, RIH w/ 26" M.T Bit to 14m, Commence 26" HS to 31m.
4	18 – Oct.	Cont. Drlg 26 HS to 151m while run totco @ 50, 108m. Perform Condition trip. Pump Circ. Out 60 bbl Hi-Vis Pill.
5	19 – Oct.	Spot Hi-Vis Pill, Drop Totco, POOH to surface, Run 20" CSG to 149m, Perform 20" CSG CMT Job as per program, Pull out stinger to surface, WOC.
6	20 – Oct.	Cut 20" CSG, Install Base Plate. Final Cut 20" CSG. Install CHH & Press test. N/U BOP Stack.
7	21 – Oct.	N/U BOP, Press test same as NIOC Policy, RIH w/ 17-1/2" MT Bit to BTM, D/O CMT & Float shoe, Drlg 17-1/2" HS to 155m.
8	22 – Oct.	Cont. Drlg 17-1/2" HS to 165m, POOH to surface, Obs. 2 No. of NZL Seat area washed out, RIH w/ 17-1/2" Drlg BHA to BTM, Commence Drlg 17-1/2" HS to 225m.
9	23 – Oct.	Cont. Drlg f/ 225 to 495m, While perform wiper trip to 150m, Run back to BTm, Run totco.
10	24 – Oct.	Cont. Drlg 17-1/2" HS f/ 495 to 730m, While displace the whole well @ 590m.
11	25 – Oct.	Cont. Drlg 17-1/2" HS to 793m, POOH to Surface, Run back w/ 17-1/2" PDC Bit to BTM, Commence Drlg 17-1/2" HS to 800m.

12	26 – Oct.	Cont. Drlg 17-1/2" HS to 1073m.
13	27 – Oct.	Cont. Drlg 17-1/2" HS to 1107m. Perform wiper trip to 792m, Run totco @ 1050m, Resume Drlg to 1227m.
14	28 – Oct.	Cont. Drlg 17-1/2" HS to 1356 m; NL.
15	29 – Oct.	Cont. Drlg 17-1/2" HS to 1373.8m, Work on TDS, POOH to surface. RIH w/ New PDC Bit to 30m.
16	30 – Oct.	Cont. RIH w/ 17-1/2" PDC Bit to 1373m (BTM), Drlg 17-1/2" HS to 1450 m
17	31 – Oct.	Cont. drlg 17-1/2" HS f/1450 to 1480m while pump LCM and cure formation loss. Obs drop in SPP and Hook Load. POOH to surf. Obs 17 1/2" PDC bit + Bit sub + 1 jt 9 1/2" DC left in hole. RIH w/ fishing BHA. Work on catch fish.
18	01 – Nov.	Cont. Work on chatch fish w/ 12-3/4" O.shot, No success. POOH to surface. P/U 11-3/4" fishing assembly. RIH to 1469m (TOF). Catch the fish. POOH with fish to 1220m till MN. 1 BPH Loss.
19	02 – Nov.	Cont. POOH with fish f/ 1220m to surf. Recover fish, L/D fishing assy. L/D all DC, XOS and B. Sub. M/U 17-1/2" PDC Bit and RIH to 110m till MN, 1 BPH Loss.
20	03 – Nov.	Cont. RIH w/ M/U 17-1/2" PDC Bit f/ 110m to 1480.3 (BTM). Pump Hi-Vis, Circ. Out bit, Resume drlg 17-1/2" HS to 1548 while pump LCM pill 20 lb/bbl several times. till MN, 6-60 BPH Loss.
21	04 – Nov.	Cont. drlg 17-1/2" HS f/ 1548 to 1562m. Due to low ROP stop drlg. POOH f/ 1562 to 550m till MN, 5-40 BPH Loss.
22	05 – Nov.	Cont. POOH f/ 550m to surf. P/U 17-1/2" R.Bit & J.Sub. RIH to 734m till MN, 5-15BPH Loss.
23	06 – Nov.	Cont. RIH f/734 to 1562m Work on junk sub, 5-20 BPH Loss.
24	07 – Nov.	Drlg 17-1/2" HS f/ 1562 to 1564.5m, pump & spot 100bbl LCM

		pill (40ppb). POOH to 1460m. Circ. btm's up while diluting active sys. with fresh mud. Spot 50 bbl LCM pill. POOH to 300m till MN. 5-25 BPH Loss.
25	08 – Nov.	Cont. POOH f/ 300m to surf. L/D 17-1/2" R.Bit & J.Sub. P/U & M/U 17-1/2" PDC Bit and RIH to 1200m till MN. 2-6 BPH Loss.
26	09 – Nov.	Cont. RIH w/ 17-1/2" PDC Bit f/ 1200 to 1515.5m while pumping hi-vis pill periodically, suddenly obs. 300psi drop in SPP & lost to 10-12klbs of strg weight. POOH to check string f/ 1515.5 to 600m till MN. 2-8 BPH Loss.
27	10 – Nov.	Cont. POOH to check string f/ 600m to surf. Obs 19.84m of BHA left in hole. P/U & M/U 11-3/4" O.Shot. & RIH to 1531m tag TOF. Work on fishing in progress till MN. 2-6 BPH Loss.
28	11 – Nov.	Cont. & Work on fishing WITH 11-3/4" O.Shot by applying different parameters, No success. POOH to 1400m till MN. 2-4 BPH Loss.
29	12 – Nov.	Cont. POOH f/ 1400m to surf. .L/D 11-3/4" O.Shot assembly. M/U 17-1/2" B.Bit (New, K.Dream, 415, 3 x 18/32" + CJ nzl) & RIH to 930m till MN. 3-8 BPH Loss.
30	13 – Nov.	Cont. RIH with 17-1/2" B.Bit (New, K.Dream, 415, 3 x 18/32" + CJ nzl) 1380m till MN. 3-8 BPH Loss.
31	14 – Nov.	Cont. RIH w/ 17-1/2" TCI Bit to 1542.4m (TOF), Tag TOF, Circ. Out Hi-Vis Pill, Over Circ. Meanwhile work on mud rheology.
32	15 – Nov.	POOH w/ 17-1/2" TCI Bit f/ 1542.4m to surface. M/U & Assemble 11-3/4" Overshot.
33	16 – Nov.	RIH w/ 11-3/4" Overshot BHA to 1539m, Circ. Out Hi-Vis Pill, Hard R/D to 1540.5m.
34	17 – Nov.	Cont. Hard wash & Ream Dn f/ 1540.5 to 1541.4m, POOH w/ 11-3/4" Overshot BHA to surface, P/U & M/U 17-1/2" Taper Mill + 1 Jt 5" HWDP to 10m.

35	18 – Nov.	RIH w/ 17-1/2" Taper Mill to 700m, POOH to 70m.
36	19 – Nov.	Cont. POOH w/ 17-1/2" Taper Mill to surface, RIH w/7-7/8" Center cut bit to 1536m, Perform CMT Plug Job as per program, POOH to 960m, WOC.
37	20 – Nov.	RIH w/ 7-7/8" Center Cut Bit f/ 960 to 1486m, While CBU @ 1330m, Perform CMT Plug job as per program, POOH w/ 7-7/8" Center Cut Bit to 130m, Work on TDS, Resume POOH to surface.
38	21 – Nov.	RIH w/ 17-1/2" TCI Bit to 1330.
39	22 – Nov.	Cont. RIH to 1407m, D/O CMT to 1429m, CBU, Circ. Mud & Work on mud properties, POOH to 1350m.
40	23 – Nov.	POOH 17-1/2" TCI Bit to surface, RIH w/ 17-1/2" MT Bit & Directional BHA to 142m; While perform shallow test of DHM & MWD tools. Meanwhile change MWD tools and Leakage f/ D.Jar & Wait on Rec. Another D.Jar.
41	24 – Nov.	Cont. RIH w/ 17-1/2" MT Bit & Directional BHA f/ 142 to 1419m.
42	25 – Nov.	Wash Dn w/ 17-1/2" MT Bit & Directional BHA f/ 1419 to 1429.4m, Commence Directional Drlg 17-1/2" HS well f/1429.4 to 1439.5m.
43	26 – Nov.	Cont. Directional Drlg 17-1/2" HS f/1439.5 to 1447m, CBU, POOH w/ 17-1/2" MT Bit to surface, RIH w/ 17-1/2" TCI Bit & Directional BHA (DHM AKO: 1.5 Deg) to 500m.
44	27 – Nov.	Cont. RIH w/ 17-1/2" TCI Bit & Directional BHA to 1447m, Resume Sidetrack the well to 1472m.
45	28 – Nov.	Cont. Directional Drlg f/ 1472 to 1507m.
46	29 – Nov.	Cont. Directional Drlg f/ 1507 to 1552m.
47	30 – Nov.	POOH directional BHA f/ 1552m to surf. P/U & M/U new DHM, MWD tools & 17-1/2" PDC Bit. RIH to 900m till MN.

		1-3BPHL.
48	01 – Dec.	Cont. RIH w/ 17-1/2" PDC Bit and directional BHA f/ 900m to 1552m (BTM). Resume drlg formation in slide and rotary mode to 1571m till MN. 1-4 BPHL.
49	02 – Dec.	Cont. drlg formation in slide and rotary mode f/ 1571 to 1592.9m. Due to low ROP stopped drlg. POOH to 1060m till MN. 1-3 BPHL.
50	03 – Dec.	Cont. POOH f/ 1060m to surf. L/D Directional BHA and 17-1/2" PDC Bit. P/U & M/U 17-1/2" Used Insert Bit and rotary BHA. RIH to 1592.9m(BTM). Resume drlg to 1594m. till MN. 1-2 BPHL.
51	04 – Dec.	Cont. drlg to 1616m. Due to obs gradually decrease in SPP stop drlg, Check mud pumps and surface lines; OK. Decided to POOH to surface. 1-2 BPHL.
52	05 – Dec.	Start POOH while check string for any wash out f/1616m to surface on elevator with good hole condition. RIH with same Bit & BHA to btm. Resume drlg formation to 1617.5m till MN, 1-2BPH Loss.
53	06 – Dec.	Cont. drlg formation f/ 1617.5 to 1636m till MN, 1-2BPH Loss.
54	07 – Dec.	Cont. drlg formation f/ 1636 to 1648.5m as section TD. Circ. Btm's up. POOH as wiper trip to 1420m while smooth KOP area till MN, 1-2BPH Loss.
55	08 – Dec.	wash down as wiper trip f/ 1420 to 1648.5m (BTM). CBU. Spot 300 bbl Hi-Vis at bottom. POOH on elevator to surf. RIH 13-3/8" casing as per program to 343m (totally 30 Jts) till MN, 1-2BPH Loss.
56	09 – Dec.	Cont. RIH 13-3/8" casing as per program f/343 to 1648m (totally 145 Jts) till MN, 1-2BPH Loss.
57	10 – Dec.	Cont. mix & prepare cement solution and spacer. L/up cmt line on csg strg & established circ. While P/up strg weight by spider elevator & L/D side door slips . Perform press test cmt line; OK.

		Pump ch. Wash & Spacer Till MN, 1-2 BPHL.
58	11 – Dec.	Perform 13-3/8" CSG CMT job as per program while obs. Bumping after 797bbl displaced. Perform CIT, ok. Hold pressure inside csg until the cmt get hard while H/U BOP & drop CSG HGR, slack off 50% off csg strg Wight. H/Off BOP & Cont. Weight on CMT to get 100% hard. Slack off 100%strg weight on csg HGR & press. Test to 1000psi, ok. R/D CMT head, Prepare to H/U BOP Stack H/U BOP Stack. Rough cut L.J & L/D same. N/D Hydrill, Double rams. Disconnect Kill line valves & Choke line valves. N/D Drilling spool in progress.
59	12 – Dec.	N/D 20-3/4" BOP Stack, Install 5K CHS & P/T, N/U 13-5/8" BOP Stack & P/T.
60	13 – Dec.	Cont. Perform BOP Press test as NIOC policy, perform injectivity test, L/D excess tubular, R/B 1 Std 8-1/2" DC and 1 Std 5" HWDP, Perform CMT Top job, RIH w/ pendulum BHA to 1590m. Meanwhile F/U Ann w/ 10 bbl 94 pcf CMT Slurry
61	14 – Dec.	Cont. RIH w/ 12-1/4" PDC Bit to 1648 m, while D/O Hard CMT, Plugs, F.Collar & Shoe, Run Totco survey @ 1623m (Inc: 6 Deg). Drlg 12-1/4" HS to 1654m, While displace the well @ 1653m.
62	15 – Dec.	Cont. Drlg 12-1/4" H.S to 1713m, while Perform FIT & Work on IBOP.
63	16 – Dec.	Cont. Drlg 12-1/4" HS to 1828m.
64	17 – Dec.	Cont. Drlg 12-1/4" HS to 1831m, POOH to surface, RIH w/ New Bit & Previous BHA to BTM & Resume Drlg to 1861m.
65	18 – Dec.	Cont. Drlg 12-1/4" HS to 1994m.
66	19 – Dec.	Cont. Drlg 12-1/4" HS to 2000m. POOH to surface. RIH w/ C.Cut Bit to 1890m. Spot 160 bbl LCM Pill. Pump & Inject LCM Pill w/ 80 bbl.
67	20 – Dec.	Pump & Inject LCM Pill, Perform CMT Plug Job, RIH to 1690m, CBU, POOH to Surface.

68	21 – Dec.	RIH w/ 12-1/4" TCI Bit to 1690m, D/O CMT to 1850m, Wash down to 2000m, pump Hi-vis pill & CBU, POOH to 13-3/8" Shoe, Prepare mud, Run back 2000m.
69	22 – Dec.	Cont. Drlg 12-1/4" HS to 2114m.
70	23 – Dec.	Cont. Drlg 12-1/4" HS to 2150m, CBU, POOH to 80m Meanwhile Run totco @ 2100m and R/B 8 Stds DP "S".
71	24 – Dec.	Cont. POOH f/ 80m to surf. L/D 12-1/4" TCI bit. P/U & M/U 12-1/4" PDC bit. RIH w/ 3 STD 8-1/2" DC (S.Stab) @ 20m, 3 STDs HWDP followed by 5" DPs Jt by Jt to 1716m. POOH & R/B DPs to 84m. M/U D.Jar. RIH back on 5" DPs to 25om Till MN, 0-1 BPH Losses.
72	25 – Dec.	Cont. RIH to 2150m (btm) Break cir. Resume drlg 12-1/4" HS. To 2151m. Obs Abnormal fluctuation in SPP stop drlg. POOH to 1620m. Change stand pipe manifold valve. RIH to btm. Resume drlg 12-1/4" HS to 2189m till MN. 0-3 BPHL.
73	26 – Dec.	Cont. drlg 12-1/4" HS f/ 2189 to 2339m while Pump Hi-Vis periodically till MN. 0-4 BPHL.
74	27 – Dec.	Cont. drlg 12-1/4" HS f/ 2339 to 2509m. Pump Hi-Vis pill and circ. while B/R and R/D last drilled stand prior to perform wiper trip. till MN. 0-5 BPHL.
75	28 – Dec.	Cont. POOH w/ soft B/R as wiper trip f/ 2509 to 2395m. Due to high wind speed stopped POOH. RIH on elevator to 2509m (btm), Resume drlg 12-1/4" HS f/ 2509 to 2686m till MN. 1-3 BPHL.
76	29 – Dec.	Cont. drlg 12-1/4" HS f/ 2686 to 2696.5m. Due to low progress stop drlg. POOH to 1620m w/ good hole condition. static Flow checked; 0.5 BPH formation loss. Resume POOH to surf. BOP test. M/U new 12-1/4" PDC Bit and RIH to 250m till MN. 0-3 BPHL.
77	30 – Dec.	Cont. RIH w/ new 12-1/4" PDC Bit and RIH to 2696.5m (btm) Fan the btm & profile the bit. Resume drlg 12-1/4" HS to 2738m

		till MN. 0-4 BPHL.
78	31 – Dec.	Cont. drlg 12-1/4" HS f/ 2738 to 2810m. Obs. Drop in SPP. Check surf. Equip. OK. POOH to 1550m till MN. 0-3 BPHL.
79	01 – Jan.	Cont. POOH While check drlg string f/ 1550m to surf. Obs string twist off. P/U & assembled 10-1/8" O.Shot and RIH to 2788.47m (TOF). Engaged with fish & catch same. POOH to 2100m till MN. 1 BPHL.
80	02 – Jan.	POOH f/ 2100m to surf. Released the fish & L/D Overshot. Check & B/out 12-1/4"PDC Bit, M/up the same bit with old BHA design (S.stab. @ 20mt) follow by 5"Dps to 2100m till MN, 1 BPH losses.
81	03 – Jan.	Cont. RIH w/ 12-1/4"PDC Bit f/ 2100 20 2810m (btm). Circ btm's up. Resumed drlg 12-1/4" HS f/2810 to 2868m. Break Circ. Prior to POOH till MN, 2-4 BPH Losses.
82	04 – Jan.	POOH on elevator f/2868m to surface with good hole condition. B/O & L/D PDC bit. P/U & M/U 12-1/4" PDC Bit (Best, New, M423, 5X13/32" + 4X14/32" NZL) & RIH to 2868m (btm). Pump 40 bbl Hi-Vis Pill & tag the btm while circ. out pill & fan the btm. Resume drlg 12-1/4" HS to 2870m till MN, 1-3 BPH losses.
83	05 – Jan.	Cont. drlg 12-1/4" HS f/ 2870 to 2941m till MN, 2-4 BPH losses.
84	06 – Jan.	Cont. drlg 12-1/4" H.S f/ 2441 to 3006.7m. Obs. Twist off string indications. POOH to surface, Obs string twist off from box of string stabilizer. Assemble 10-1/8" short catch O.Shot in progress. till MN, 1-4 BPH losses.
85	07 – Jan.	RIH w/ 10-1/8" O.Shot to TOF, Catch Fish, POOH to surface.
86	08 – Jan.	L/D Recovered Fish, RIH w/ Drlg BHA to 2480m.
87	09 – Jan.	Cont. RIH w/ Drlg BHA to 3006m. Resume Drlg 12-1/4" HS to 3017.5m.

88	10 – Jan.	Cont. Drlg 12-1/4" HS to 3019.5m, Stop Drlg due to leakage f/ Upper iBOP, POOH to 133/8" CSG Shoe, Change out iBOP Assy, Run Back to BTM, Resume Drlg 12-1/4" HS to 3023.5m.
89	11 – Jan.	Cont. Drlg 12-1/4" H.S f/ 3023.5 to 3027m, POOH w/ 12-1/4" PDC Bit to surface, meanwhile flow check @ Shoe and BHA Depth, RIH w/ New 12-1/4" PDC Bit and pendulum BHA to 900m.
90	12 – Jan.	Cont. RIH w/ 12-1/4" PDC Bit to 3027m, while run totco @ 2996m (0.5 Deg), Drill ahead 12-1/4" HS f/ 3027 to 3054m.
91	13 – Jan.	Cont. Drill ahead 12-1/4" HS f/ 3054 to 3140m.
92	14 – Jan.	Cont. Drill ahead 12-1/4" HS to 3236.m.
93	15 – Jan.	Cont. Drill ahead 12-1/4" HS to 3240m. String twist off. RIH w/ 10-1/8" Overshot to TOF, Catch fish, POOH to 2700m.
94	16 – Jan.	Cont. POOH to 1813m, Release overshot, Cont. POOH to surface, Perform BOP Test, Slip & Cut Drlg line, RIH w/ 12-1/4" New PDC Bit & Pendulum BHA to 560m.
95	17 – Jan.	Cont. RIH w/ 12-1/4" New PDC Bit & Pendulum BHA to 3240m, Commence drill ahead 12-1/4" HS to 3274m.
96	18 – Jan.	Cont. drill ahead 12-1/4" HS to 3275m. Due to low ROP. POOH w/ 12-1/4" PDC Bit to surface. RIH w/ 12-1/4" TCI Bit & Junk sub to 2100m.
97	19 – Jan.	Cont. RIH w/ 12-1/4" TCI Bit & J.Sub to 3275m, Circ. Out pill, Work on J.Sub, Resume Drlg to 3284.4m while change wash pipe.
98	20 – Jan.	Cont. drill ahead 12-1/4 HS f/3284 to 3284.4m, POOH w/ 12-1/4" TCI Bit & Junk Sub to surface, RIH w/ 10-1/8" RCJB to BTM, Circ. Mud.
99	21 – Jan.	Drop ball and chase same to seat. Work on RCJB f/ 3284.5 to 3284.9m. POOH RCJB to surf. B/O & L/D RCJB. Recovered 50cm formation core W/O any metal parts or junk.; 3-4 BPH

		losses.
100	22 – Jan.	P/U & M/U 12-1/4" PDC Bit (Beste, New, M1664, 9*13/32" Nozzle) and RIH to btm, Pump Hi-Vis pill. Resume drlg 12-1/4" HS to 3315m till MN, 3-5 BPH losses.
101	23 – Jan.	Cont. drlg 12-1/4" HS f/ 3315 to 3427m till MN, 3-5 BPH losses.
102	24 – Jan.	Cont. drlg 12-1/4" HS f/ 3427 to 3535m till MN, 3-5 BPH losses.
103	25 – Jan.	Cont. drlg 12-1/4" HS f/ 3535 to 3620m, B/R & R/D drilled stand, rack back same and start POOH w/ soft B/R as wiper trip to 3570m till MN, 3-5 BPH losses.
104	26 – Jan.	Cont. POOH w/ soft B/R as wiper trip f/ 3570 to 3250m, RIH back to 3600m on elevator. Perform totco survey. Resume drlg 12-1/4" HS to 3671m till MN, 2-5 BPH losses.
105	27 – Jan.	Cont. drlg 12-1/4" HS f/ 3671 to 3741m. Obs. Dec. in SPP. Take SCR, resume drlg with low parameters to 3741m and monitor the SPP; Constant. till MN, 3-5 BPH losses.
106	28 – Jan.	Cont. drlg 12-1/4" HS f/ 3741 to 3790m while increase MW to 84 pcf (due to get 82 pcf MW in return and obs. decrease in SPP.) till MN, 1-4 BPH losses.
107	29 – Jan.	Cont. drlg 12-1/4" HS f/ 3790 to 3814m. Change wash pipe. Resume drlg to 3820m while increase MW to 85 pcf till MN, 1-4 BPH losses.
108	30 – Jan.	Cont. drlg 12-1/4" HS f/ 3820 to 3842m. Change wash pipe. Resume drlg to 3846m while decrease MW to 84 pcf till MN, 4-12 BPH losses.
109	31 – Jan.	Cont. drlg 12-1/4" HS f/ 3846 to 3872m. Spot 60 bbl LCM pill. POOH on elevator to 3300m. till MN, 4-12 BPH losses.
110	01 – Feb.	Cont. POOH on elevator f/ 3300m to1700m with good hole condition, Pump & spot 140 bbl LCM pill. Resume POOH to

		surf. Change 12-1/4" PDC bit & D.Jar. RIH to 2900m with good hole condition. till MN, 10-15 BPH losses.
111	02 – Feb.	Cont. RIH f/ 2900 to 3872m (btm) Resume drlg 12-1/4" HS to 3891m while decrease MW to 82.5 and pump LCM pill. Obs. Leakage f/ upper IBOP. POOH to 3799m change same. RIH back to 3856m try to stablish circ. No success due to string plugged. till MN, 15-30 BPH losses.
112	03 – Feb.	Work on unplug string, no succ. POOH to 1623m. Slip & Cut drlg line. Try to unplug string; no succ. POOH to surf. obs. flapper of float valve is broken and drop down on bit also 4 nozzles were plugged. 25-35 BPH losses.
113	04 – Feb.	RIH w/ 12-1/4" PDC bit to 3891m, Resume Drlg 12-1/4" HS to 3895m. POOH w/ 12-1/4" PDC Bit f/ 3895 to 3750m
114	05 – Feb.	Cont. POOH w/ 12-1/4" PDC Bit to 1210m, Meanwhile spot LCM Pill @ 3595, 3500, 3385 & 1648m. Stop POOH Operation due to high wind speed
115	06 – Feb.	Cont. Stop POOH Operation due to high wind speed, POOH w/ 12-1/4" PDC Bit f/ 1210m to surface, RIH w/ C.Cut bit to 3100m, Pump 160 bbl LCM Pill.
116	07 – Feb.	POOH to surface while Spot 220 bbl 140 ppb Hi-Vis LCM Pill @ CSG Shoe, Change top rams, Run 9-5/8" CSG as per program to 400m.
117	08 – Feb.	Cont. Run 9-5/8" CSG to 1650m.
118	09 – Feb.	Cont. Run 9-5/8" CSG to 3440m.
119	10 – Feb.	Cont. Run 9-5/8" CSG to 3895m, Perform 9-5/8" CSG CMT Job as per program. (1108 bbl lead slurry, 116 bbl Tail Slurry). Displace is in progress till M.N.
120	11 – Feb.	Displace CMT, Set CSG Slips, S/O CSG Wt, L/D LND Jt, N/D BOP Stack, N/U THS, N/U BOP Stack is in progress.
121	12 – Feb.	N/U BOP Stack, P/T Same, L/D 9 Jts 8-1/2" DC, RIH w/ 8-3/8"

		PDC Bit to 1400m.
122	13 – Feb.	Cont. RIH w/ 8-3/8" PDC Bit to 3800 m, W/D to 3867m. D/O Med to Hard CMT, Plugs, F.C, F.Shoe. Drlg 8-3/8" HS to 3910m. Interrupted operation due to work on TDS & Change Saver sub.
123	14 – Feb.	Cont. Drlg 8-3/8" HS to 3928m, CBU, POOH to 3856m, Perform FIT to EMW 105pcf, Work on TDS, Run Back to BTM & Displace well w/ 100 pcf mud.
124	15 – Feb.	Cont. Drlg 8-3/8" HS to 3964m, Meanwhile Spot 20 bbl LCM Pill @ 3963m.
125	16 – Feb.	Cont. Drlg 8-3/8" HS to 4076m.
126	17 – Feb.	Cont. Drlg 8-3/8" HS to 4180m (Well TD). CBU. POOH to 3980m.
127	18 – Feb.	Cont. POOH as condition trip f/3980 to 3820m. RIH to 4180m (btm) Circ. Btm's up. Spot Hi-Vis pill @ btm. POOH to surf. Prepare to Run wireline logging equip.
128	19 – Feb	Cont. Prepare & R/U wireline logging equip. Perform logging run #1 (Resistivity/Sonic/CDR-GR) & run #2 (Nuclear Run) LDT/CNT/NGS. M/U logging assembly as run # 3 SBT/CCL/VDL-GR, Surface checked; OK. RIH to 700m till MN. 0-1 BPH Losses.
129	20 – Feb.	Cont. Perform run # 3 SBT/CCL/VDL-GR. R/D logging unit. Slip & Cut drlg line. P/U & M/U 8-3/8" PDC bit and RIH to 1250m till MN. 0-1 BPH Losses.
130	21 – Feb.	Cont. RIH with 8-3/8" PDC bit f/ 1250 to 4180m (btm), circ. & uniform mud. Spot 60 bbl Hi-Vis pill at btm. POOH on elevator with good hole condition f/ 4180m (btm) to 1000m till MN, 0-1 BPH Losses.
131	22 – Feb.	Cont. POOH f/ 1000m to surf. RIH 7' Liner and assembly as per program. Cont RIH with 5" DPs to 3500m till MN, 0-1 BPH Losses.

132	23 – Feb.	Cont. RIH 7" Liner on 5" DPs f/ 3500 to 4180m, tag btm. Set 7" liner hanger. Performed cement job as per plan. POOH to 3552m. Flushed string. Cont. POOH to surf. L/D Liner hanger setting tools till MN.
133	24 – Feb.	P/U & M/U 8-3/8" PDC Bit and RIH to 3650m. Took weight, Commence D/O cement to 3786m (7" L.Lap). Circ. Till shakers clean. POOH to 3300m till MN.
134	25 – Feb.	Cont. POOH f/ 3300m to surf. Change top rams. Perform 13-5/8" 10K BOP stack pressure tes; OK. M/U 5-7/8" R.Bit and RIH with clean out BHA Jt by Jt to 370m till MN.
135	26 – Feb.	Cont. RIH with 5-7/8" R.Bit and clean out BHAto3789m. D/O & Clean out inside 7" liner to 4141m (Top of LDC). Circ. Btm's up. POOH to 3780. Perform CIT; OK Resume POOH f/ 3780 to 3600m till MN.
136	27 – Feb.	Cont. POOH with clean out BHA f/ 3600m to surface. M/up & RIH By 5-7/8" Tri-Cone Bit with 7" & 9-5/8" scraper as Tandem BHA to 3800m till MN.
137	28 – Feb.	Cont. RIH by 5-7/8" Tri-Cone Bit with 7" & 9-5/8" scraper as Tandem BHA f/ 3800 to 4141.5m (LDC depth). Circ btm's up. Spot 30 bbl CaBr2 brine in 7" liner. POOH to 1000m. Slip & Cut drlg line. POOH to surf. M/U dry test assembly and RIH to 185m till MN.
138	01 – March	Cont. M/U dry test assembly and RIH f/ 185 to 1650m. Slip & cut drilling line. Resume RIH to 3224m till MN.
139	02 – March	Cont. M/U dry test assembly and RIH f/ 3224 to 3734m. Set PKR. Perform 7" L.Lap dry test (3Hrs open & 6 Hrs close position). Unset PKR. POOH f/ 3734 to 2300m till MN.
140	03 – March	Cont. POOH with dry test assembly f/ 2300 to suf. L/D Dry test tools. R/U WL tools. RIH with SBT/VDL/CCL/GR logging tools to 3772m. Try to pass, no succ. POOH WL to surf. 'RIH WL with 2jt 4.5" guns as dummy run to 2700m till MN

141	04 – March	Cont. Run Dummy to 3772m, Try to pass; No-Succ, POOH to surface, RIH w/ 5-7/8" MT Bit to 4141.5m, CBU & Work on mud, Spot CaBr2, POOH to 3450m.
142	05 – March	Cont. POOH w/ 5-7/8" MT Bit to surface, Run CMT quality Logging for 7" Liner, Wait on daylight.
143	06 – March	Wait on day light. Perform 2 run of perforation job as per program.
144	07 – March	RIH w/ 4-1/2" WCP HSD Gun Assy. as Run #3 as per program.
145	08 – March	Perform perforation as Run #4, #5 & #6 as per program.
146	09 – March	Wait on daylight, Perform 3 Runs of perforation, Change Top rams, Perform BOP test.
147	10 – March	L/D 5Stds 6-1/2" DC, RIH w/ 5-/8" M.M J.Mill to 4132m, CBU.
148	11 – March	CBU, Press test CMT Line, Displace well w/ Non-Solid Completion Fluid, POOH w/ 5-7/8" J.Mill to 2400m & L/D DPs.
149	12 – March	Cont. POOH to surface & L/D all tubulars.
150	13 – March	R/U Completion string running equipment, L/D all tools of De-Completed from AZNS-122, Run completion as per program to 790m. Meanwhile perform P/T @ 166m, Run gauge ring @ 29m & 166m.
151	14 – March	Cont. Run completion as per program to 3100m. Meanwhile perform P/T @ 1030, 2012m.
152	15 – March	Cont. Run completion as per program to 3877m. Meanwhile perform P/T @ 3100, 3780 & 3829m.
153	16 – March	P/T, Set P. Sleeve, Set Plug & Prong in No-Go, Run Shifting tools, Set PKR, P/T, Land TBG HGR & P/T, P/T PKR f/ Ann, L/D L/J, Install TWCV & P/T.

154	17 – March	N/D BOP Stack, Install XMT & P/T, Ret. Prong & Plug f/ No-Go, Ret. P. Sleeve, Install TWCV, Release the rig.
155	18 – March	Tear out Rig including L/D TDS, Disconnected Stand pipe & Choke Manifold, Flow Line & Divider.

Table 13-1: AZNS-207 Daily Drilling Report Summary
